

दलनह; {k= dh ifj;k t ukvk
CENTRAL SECTOR PROJECTS

₹150 djkM vkj vf/kd ykxr okyh
(₹ 150 Crore and above)

355oh ढYk'k fjikV@355th **Flash Report**
eb] 2015@May, 2015



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Hkkjr ljdkj / **Government of India**

lkf[; dh vkj dk; Øe dk; kUo; u e=ky ;

Ministry of Statistics and Programme Implementation

vk/kkjh ljpuk vkj ifj;k t uk i ck/ku iHkkx
Infrastructure and Project Monitoring Division

l jnkj iV;y Hkou] lln ekx]

Sardar Patel Bhavan, Sansad Marg,

ub] fnYyh / **New Delhi-110001**

oc lkbV / **Website- www.cspm.gov.in**

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministrial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents	
	Pages
Executive Summary Hindi	1-21
Executive Summary English	22-38
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2014-2015	39-39
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2014-2015	40-40
Summary of projects	41-54
Graphical Presentation of All Projects	55-66
Sector wise Analysis of Projects	67-102
Sector wise Graph	103-114
Annexures	115-115
Status of central sector projects costing Rs.150 Crore and above	116-117
List of projects in which expenditure is more than approved cost	118-123
Details of Projects Ahead of Schedule w.r.t. Original Schedule	124-124
Details of On Schedule Projects w.r.t. Original Schedule	125-131
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	132-142
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	143-147
List of Projects habving cost overruns with respect to Anticipated/Cumulative ecpenditure	148-156
Details of Delayed Projects w.r.t. Original and Revised Schedule	157-183
Details of projects without milestones w.r.t. original schedule	184-207
Details of Projects Without Date of Commissioning	208-222
Details of projects without original Date of Commissioning	223-224
List of Projects Ahead of Schedule w.r.t. Latest Schedule	225-225
List of ongoing projects having cost overrun w.r.t. to revised schedule	226-235
List of Projects on schedule w.r.t. Latest Schedule	236-244
List of Delayed Projects w.r.t. Latest Schedule	245-255
Details Of Central Sector Projects Showing Time Overruns Of 6 Months And More And Cost Overruns Of Rs.100 Crore And Above	256-266
Details of Central Sector Projects Showing Cost Overruns Of More Than Rs. 100 Crore	267-275
Details Of Central Sector Projects Showing Time Overruns Of 6 Months and More and cost overruns of Rs. 100 Crore and above	276-280
List of Road Sector projects Implemented by NHAI as on 31-05-15 for which cumulative expenditure has been reported zero	281-283
List of Road Sector projects Implemented by NHAI as on 31-05-15 for which date of commissioning has expired/lapsed.	284-286

कार्यकारी सारांश

1. मई, 2015 की फ्लैश रिपोर्ट में रु. 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 766 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। मई 2015 के दौरान, 6 परियोजनाओं (पेट्रोलियम में 3 परियोजनाएं, विद्युत में 2 परियोजनाएं तथा दूरसंचार क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 766 परियोजनाओं में से, 237 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 29 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 29 परियोजनाओं में से, 11 परियोजनाएं रु.1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	298	32	1	0
2.	सड़क परिवहन एवं राजमार्ग	132	16	0	0
3.	विद्युत	112	62	4	1
4.	पेट्रोलियम	65	41	7	4
5.	कोयला	76	44	5	1
6.	शहरी विकास	30	15	0	0
7.	इस्पात	28	16	7	3
8.	नागर विमानन	7	4	3	0
9.	पोत परिवहन एवं पत्तन	7	1	0	0
10.	परमाणु ऊर्जा	4	3	2	2
11.	दूरसंचार	3	1	0	0
12.	उर्वरक	1	0	0	0
13.	खदान	1	0	0	0
14.	पेट्रोरसायन	1	1	0	0
15.	भारी उद्योग	1	1	0	0
कुल		766	237	29	11

3. 766 परियोजनाओं के कार्यान्वयन की कुल मूल लागत रु. 10,68,206.97 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत रु. 12,73,650.02 करोड़ होने की संभावना है, जो रु. 2,05,443.05 करोड़ (मूल लागत का 19.23%) की समग्र लागत वृद्धि को दर्शाता है। मई, 2015 तक इन

परियोजनाओं पर किया गया व्यय रु. 4,85,680.02 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 38.13% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.05.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	लागत वृद्धि (%)
	परमाणु ऊर्जा				
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
2	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	31.12
	नागर विमानन				
3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	15.77
4	चंडीगढ़ अंतराष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	8.19
	कोयला				
5	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
6	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	76.47
7	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	50.37
8	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
9	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
	भारी उद्योग				
10	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
	पेट्रोरसायन				
11	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	80.08
	पेट्रोलियम				
12	जी1 और जी एस-15 का विकास	04/2003	429.82	3955.21	820.20

	(ओएनजीसीएल)				
13	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	75.35
14	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
15	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
16	कोरबा में विपणन टीओपी	01/2011	141.86	219.08	54.43
विद्युत					
17	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
18	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	159.38
19	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15
20	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी)	09/2003	6285.33	15300.00	143.42
21	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.68	139.35
रेलवे					
22	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
23	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
24	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
25	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
26	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
सड़क परिवहन एवं राजमार्ग					
27	पानीपत-जालंधर छ: लेन (96 किमी. से 387.1 किमी.)	05/2009	1108.00	2288.00	106.50
28	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
29	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
30	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	68.99
31	ब्रह्मपुत्र ब्रिज एनएच सं.-31	12/2003	217.61	309.56	42.25
पोत परिवहन एवं पत्तन					

32	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
33	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
34	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	51.92
35	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	18.89
इस्पात					
36	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
37	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	41.41
शहरी विकास					
38	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.05.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	4099.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
	नागर विमानन				

3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	52.92
4	चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	37.00
कोयला					
5	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
6	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	1552.99
7	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
8	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	236.62
9	मनुगुरु ओसी परियोजना का आरएफआर	11/2012	430.45	486.27	55.82
भारी उद्योग					
10	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
11	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	4372.91
पेट्रोलियम					
12	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
13	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	3525.39
14	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
16	बी-127 क्षेत्रों का एकीकृत विकास	12/2011	2059.63	2665.65	606.02
विद्युत					
17	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	15300.00	9014.67
18	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	3979.44

20	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7531.72	3612.13
21	कोल्डम एचईपी (एनटीपीसी)	10/2002	4527.15	7220.00	2692.85
रेलवे					
22	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
23	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19
24	लुमडिंग-सिलचर जिरिबाम, बदरपुर- बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
25	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
26	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52
सड़क परिवहन एवं राजमार्ग					
27	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
28	मैंबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
29	हरंगाजो से मैंबंग, एनएच-54	12/2003	196.00	331.23	135.23
30	मैंबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
31	ब्रह्मपुत्रा ब्रिज, एनएच सं. -31	12/2003	217.61	309.56	91.95
पोत परिवहन एवं पत्तन					
32	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
33	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
34	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	232.00
35	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	127.55
इस्पात					
36	तरल इस्पात क्षमता के विस्तार 3 एमटी से 6.3 एमटी तक (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00
37	सिंटर मंशीन -1 और 2 का सुधार	12/2009	343.00	488.40	145.40

शहरी विकास					
38	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 766 परियोजनाओं में से, 2 परियोजनाएं समय से पहले चल रही हैं, 127 समय पर तथा 237 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 211 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 29 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 371 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 237 विलंबित परियोजनाओं में से, 49 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 51 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 88 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 49 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.05.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	09/2015	81
2	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22
3	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	05/2018	17
नागर विमानन					
4	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	01/2011	06/2017	77
5	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	03/2014	05/2015	14
6	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर	10/2012	03/2015	09/2015	6

	निविदाओं की आपूर्ति				
7	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	03/2015	05/2015	2
	कोयला				
8	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
9	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	01/2005	03/2010	03/2017	84
10	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	06/2009	06/2015	72
11	झंझरा आर-VI सीम पीएसएलडब्ल्यू	11/2006	03/2011	03/2017	72
12	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
	भारी उद्योग				
13	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
	पेट्रोसायन				
14	असम गैस क्रैकर परियोजना	04/2006	04/2012	06/2015	38
	पेट्रोलियम				
15	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	04/2006	06/2015	110
16	जगदीशपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	12/2018	71
17	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
18	एक ईटीपी तथा तीन ईटीपी वाटर इंजेक्शन संयंत्र (डब्ल्यूआईपी) का निर्माण	06/2010	01/2014	06/2018	53
19	12 ऑफशोर आपूर्ति उपकरणों की निर्माण (ओएसवी)	06/2007	09/2011	12/2015	51
	विद्युत				
20	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123
21	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
22	बाढ़ एसटीपीपी (3X660 मेगावाट) एनटीपीसी	02/2005	12/2009	03/2018	99
23	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2015	96
24	टेहरी पंच भंडारण संयंत्र (1000 मेगावाट)	07/2006	07/2010	05/2018	94
	रेलवे				
25	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261

26	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193
27	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
28	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	03/1984	06/2005	12/2019	174
29	बेलापुर-सीवुड-उरान विद्युतीकृत दोहरी लाइन (एमटीपी)	03/1996	03/2004	03/2016	144
सड़क परिवहन एवं राजमार्ग					
30	आगरा-बाइपास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	09/2007	09/2017	120
31	धरमतुल से सोनापुर, 205 किमी.-183 किमी. (एस-20)	12/2003	05/2008	06/2015	85
32	धरमतुल से सोनापुर (एस-19)	12/2003	06/2008	05/2015	83
33	ब्रह्मपुत्र ब्रिज, एनएच सं. 31	12/2003	04/2010	01/2016	69
34	सूरत-दहिसर (छः लेन) 263 किमी. से 502 किमी.	02/2009	08/2011	12/2015	52
पोत परिवहन एवं पत्तन					
35	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	12/2010	01/2016	61
इस्पात					
36	आरएमएचपी में लौह अयस्क भंडारण की वृद्धि	07/2007	09/2009	06/2015	69
37	बोकारो इस्पात संयंत्र का विस्तार	05/2010	12/2011	08/2015	44
38	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	03/2016	36
39	दुर्गापुर इस्पात संयंत्र का विस्तार	08/2010	12/2012	06/2015	30
40	7.0 एमटीपीए कुमारस्वामी लौह अयस्क खनन परियोजना (एनएमडीसी)	02/2011	05/2013	08/2015	27
दूरसंचार					
41	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	09/2015	59
शहरी विकास					
42	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	06/2015	36
43	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	06/2017	34
44	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	11/2015	30
45	सार्वजनिक ट्रेनिंग (सीएपीटी) भोपाल के लिए सेंट्रल अकादमी का निर्माण	12/2012	12/2014	12/2016	24

46	प्लॉट नं. 4, सेक्टर- 10 द्वारिका नई दिल्ली पर पीएनबी के मुख्य कार्यालय भवन का निर्माण	05/2012	12/2014	04/2016	16
----	---	---------	---------	---------	----

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारु बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.05.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की	02/2010	344.28	344.28	58.50	03/2014	05/2015

	स्थापना						
3	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	गगन परियोजना	09/2008	626.00	626.00	514.70	06/2013	एन.ए.
कोयला							
6	मुराईदीह यूजी	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	उत्तरी तीसरा और दक्षिणी तीसरा विस्तार ओसीपी (6 एमटीवाई)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	अमेरा ओसी आरसीई	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	अमृतधारा ओसी परियोजना	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	बिजारी ओसी आरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020
उर्वरक							
11	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	197.79	13.09	11/2016	11/2016
भारी उद्योग							
12	राष्ट्रीय ऑटोमोटिव टेस्टिंग आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
खान							
13	मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
पेट्रोलियम							
14	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	1099.88	10/2011	10/2015

17	एक बहुदेशीय सहायता वेसेल्स का निर्माण	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	बी-173ए क्षेत्र की विकसित तेल वसूली	01/2012	352.49	352.49	115.81	03/2014	05/2016
विद्युत							
19	बीआरबीसीएल-नबीनगर-जेवी	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	एनपीजीसीपीएल-नबीनगर-जेवी	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	दक्षिणी क्षेत्र को सुदृढ़ बनाने की योजना-XXII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	किशनगंगा एचईपी के साथ जुड़ी पारेषण प्रणाली	01/2015	268.80	268.80	0.00	03/2018	03/2018
रेलवे							
24	जिंद-सोनीपत (एनएल), एनआर	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	लिव्ड फिंगर के साथ-साथ रंगिया-मूरकॉगस्लेक	01/2004	915.70	3700.00	3198.30	एन.ए.	03/2015
26	कालीकट-मैंगलोर (डीएल) (एसआर)	02/1996	240.00	579.37	599.40	एन.ए.	02/2012
27	अहमदनगर-पर्ली वैजनाथ (एनएल), सीआर	02/1997	514.68	2820.00	329.67	एन.ए.	एन.ए.
28	दौसा-गंगापुर सीटी (एनएल), एनडब्ल्यूआर	02/1997	410.08	410.08	294.70	एन.ए.	एन.ए.
सड़क परिवहन एवं राजमार्ग							
29	छपरा-हाजीपुर की चार लेनिंग	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	देवली-कोटा	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	जोरबट-बारापानी	01/2011	536.00	536.00	0.00	01/2014	एन.ए.
32	कांडला-मुंदरा पोर्ट	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	पीएस कानपुर कबरई	01/2013	373.47	373.47	0.00	07/2014	एन.ए.

	की दो लेनिंग						
	पोत परिवहन एवं पत्तन						
34	सिंगल प्वाइंट मूरिंग (एसपीएम) तथा एली की स्थापना करना	02/2011	830.00	621.53	0.00	05/2013	एन.ए.
35	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	373.22	373.22	04/2009	एन.ए.
36	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एन.ए.
37	मौजूदा बर्थ एन का संशोधन करना तथा सुदृढीकरण	06/2010	277.00	277.00	0.21	03/2012	एन.ए.
38	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	एन.ए.
	इस्पात						
39	गैस नेटवर्क बीएसएल	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	आरएसपी में नया एचएसएम	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	24.02	10/2016	10/2016
	दूरसंचार						
42	एनएफएस	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	रक्षा क्षेत्र के टेलीकॉम नेटवर्क आवश्यकता का निष्पादन	05/2006	1077.00	1077.00	0.00	03/2009	एन.ए.
44	असम टेलीकॉम सर्किल, चरण-V.I, 2 जी और 3 जी	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	384.00	384.00	55.22	10/2010	09/2015
	शहरी विकास						
46	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी में	01/2009	225.81	225.81	0.00	06/2012	06/2015

	शैक्षिक सहित आवासीय परिसर						
47	एनआईटी कालीकट केरल के लिए मेगा होस्टल II का निर्माण	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	आईआईटी हौज खास नई दिल्ली में लेक्चर थियेटर और लैब कॉम्प्लेक्स	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	प्लॉट संख्या सी-41-4 पर आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	बिहटा, पटना आईआईटी के कैम्पस के लिए आवासीय तथा अन्य परिसर	02/2012	171.10	171.10	0.00	09/2014	एन.ए.

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

8. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरूआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-05-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	0.00	18271.00
	नागर विमानन				
2	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में	01/2009	309.46	0.00	338.82

	नया हवाई अड्डा				
	कोयला				
3	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3207.92
	पेट्रोलियम				
4	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5925.40
	विद्युत				
5	बाढ़ एसटीपीपी फेज-II	02/2008	7341.04	0.00	8631.00
6	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7687.18
7	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5040.21
8	किशनगंगा एचईपी (3x110 मेवा)	01/2009	3642.04	0.00	3934.97
9	छत्तीसगढ़ में आईपीपीएस जेनरेशन परियोजनाओं के लिए डब्ल्यूआर के पश्चिमी भाग में पारेषण प्रणाली का सुदृढीकरण	11/2011	2127.51	0.00	2172.33
10	तीस्ता लो डैम एचईपी चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1742.55
	रेलवे				
11	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
12	लुमडिंग-सिलचर-जिरिबम बदरपुर-बराईग्राम-कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	0.00	4734.45
13	दमदम-नावपारा और नावपारा-एनएससीपी एयरपोर्ट तक विस्तार के साथ टॉलीगंज-गरिया (एमटीपी)	03/2000	1049.69	3385.14	3541.20
14	बोगीबिल तथा लिंक लाइनों पर ब्रह्मपुत्रा पुल, एनईएफआर	09/1997	1500.00	1000.00	3410.06
15	लिंकड फिंगर्स के साथ रंगिया-मुर्कोंगसलेक एनईएफआर	01/2004	915.70	915.70	3198.30
	सड़क परिवहन एवं राजमार्ग				
16	पानीपत-जालंधर छः लेनिंग (96 किमी. से 387.1 किमी.)	05/2009	1108.00	0.00	3466.00
17	नागपुर-बेतुल के चार लेनिंग	02/2011	2498.76	0.00	2786.00
18	सूरत-दहिसर (छः लेन) 263 किमी. से 502 किमी.	02/2009	1693.75	0.00	2762.00

19	गाजियाबाद-अलीगढ़ एनएच-91	02/2011	1141.00	0.00	2445.00
20	मुरादाबाद-बरेली	04/2010	1267.00	0.00	2425.00
पोत परिवहन एवं पत्तन					
21	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	0.00	373.22

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.05.2015 की स्थिति के अनुसार)

क्र. सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगन परियोजना	09/2008	06/2013	एन.आर.	06/2013
2	वीएसआई हवाई अड्डे, पोर्ट ब्लेयर में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	एन.आर.	एन.आर.	एन.आर.
कोयला					
1	शांतिखानी लौंगवॉल परियोजना-एससीसीएल	10/2006	03/2012	एन.आर.	एन.आर.
2	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.आर.	एन.आर.
3	रामागुंडम ओसी II विस्तार	12/2009	03/2012	एन.आर.	एन.आर.
4	मुराईडीह यूजी टर्नकी परियोजना	02/2011	04/2014	एन.आर.	04/2014
5	कृष्णाशिला (एनसीएल) (4एमटीवाई)	06/2011	03/2013	एन.आर.	03/2014
पेट्रोलसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एन.आर.	एन.आर.

	पेट्रोलियम				
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.आर.	एन.आर.	एन.आर.
2	बीपीसीआर/एचपीसीआर से उरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण के लिए पाइप लाइन	08/2009	08/2012	एन.आर.	एन.आर.
3	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	एन.आर.	एन.आर.	एन.आर.
	विद्युत				
1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एन.आर.
2	कुंदनकुलम एपीपी ट्रांस प्रणाली (पीजीसीआईएल)	05/2005	09/2008	एन.आर.	03/2013
3	एसआर -XII की व्यवस्था का सुदृढीकरण	02/2010	06/2012	एन.आर.	एन.आर.
4	आंध्र प्रदेश भाग-ए1 के वैमागिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी सामान्य प्रणाली	03/2012	06/2014	एन.आर.	एन.आर.
	रेलवे				
1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.आर.	एन.आर.
2	गजोली-ईटाहर(एनएल), एनईएफआर सहित एकलाखी-बालुरघाट से नई बीजी रेलवे लाइन	04/1983	एन.आर.	एन.आर.	एन.आर.
3	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एन.आर.
4	नामखाना चंद्रनगर काकदीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एन.आर.	एन.आर.	एन.आर.
5	विरमगम-भिल्डी (डब्ल्यू आर), जीसी	04/1990	एन.आर.	03/2010	एन.आर.
	सड़क परिवहन एवं राजमार्ग				
1	लखनऊ-रायबरेली	07/1999	07/2012	एन.आर.	09/2014
2	दीवापुर से यूपी/बिहार सीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एन.आर.	एन.आर.
3	सिलिगुडी से इस्लामपुर (पश्चिम बंगाल-7)	12/2003	07/2008	एन.आर.	एन.आर.
4	नलबाड़ी से बिजनी (एएस-8)	12/2003	06/2008	एन.आर.	एन.आर.
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपी चरण III)	03/2005	07/2012	एन.आर.	07/2012
	पोत परिवहन एवं पत्तन				
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एन.आर.	12/2012
2	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	11/2010	एन.आर.

3	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एन.आर.	एन.आर.
4	पारादीप बंदरगाह पर चैनल का सुदृढीकरण	12/2005	एन.आर.	01/2009	12/2010
5	कांडला में 13 और 14 कार्गो बर्थ का निर्माण	12/2005	03/2011	एन.आर.	03/2013
शहरी विकास					
1	सी/ओ सैन्य रक्षा मंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय	08/2005	08/2007	एन.आर.	एन.आर.
2	बंगलोर मेट्रो रेल परियोजना	05/2006	06/2011	एन.आर.	03/2013
3	सी/ओ बांद्रा कुर्ला कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन	11/2006	04/2009	एन.आर.	एन.आर.
4	सी/ओ एनआईटी कालीकट केरल के लिए मेगा हॉस्टल II	01/2010	10/2012	एन.आर.	एन.आर.
5	आईआईटी हॉजखास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	एन.आर.	07/2012

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और शुरू करने की संशोधित तारीख को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

i) रेलवे क्षेत्र में, 298 परियोजनाओं में से 32 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'डिडीगुल-पोलाची-पलघट-पोलाची तथा कोयंबटूर' में पोलाची-पोदनूर सेक्शन में भूमि अधिग्रहण में विलंब संबंधी समस्या के कारण 12 माह से विलंबित है ।

ii) परमाणु ऊर्जा क्षेत्र में, 4 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं 'राजस्थान परमाणु विद्युत परियोजना-7 तथा 8 (2X700 मेवा), एनपीसीआईएल' तथा 'कुडनकुलम एपीपी, एनपीसीआईएल' में उपस्करों की आपूर्ति में विलंब के कारण क्रमशः 1 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

iii) इस्पात क्षेत्र में, 28 परियोजनाओं में से 16 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 7 परियोजनाओं में से 3 मेगा परियोजनाएं हैं । परियोजना 'दुर्गापुर इस्पात संयंत्र का विस्तार, सेल' में अभिकल्प तथा अभियांत्रिकी में कमी और सिविल कार्यों के धीमे निष्पादन के कारण 1 माह के अतिरिक्त विलंब

की सूचना प्राप्त हुई है; परियोजनाएं 'बोकारो इस्पात संयंत्र का विस्तार, सेल' तथा 'अन्य जुड़ी हुई सुविधाओं के साथ 45 एमवीए सॉफ्ट की स्थापना, सेल' में क्रमशः संविदात्मक मामले तथा पर्यावरण संबंधी मंजूरी में विलंब के कारण क्रमशः 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'भिलाई इस्पात संयंत्र का विस्तार, सेल' में अभिकल्प तथा अभियांत्रिकी में कमी के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'राउरकेला इस्पात संयंत्र, राउरकेला, उड़ीसा में कोक ओवन बैट्री-3 का पुनर्निर्माण, सेल' तथा 'कैपटिव विद्युत संयंत्र-2, आरआईएनएल' प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा परियोजना 'बैट्री ब्लॉक 5 ए तथा बैट्री ब्लॉक 5 बी का पुनर्निर्माण, सेल' में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iv) नागर विमानन क्षेत्र में, 7 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । एक परियोजना 10 एयरपोर्टों पर एयरपोर्ट ऑपरेशन्स नियंत्रण केन्द्रों की स्थापना, एएआई' में उपस्करों की आपूर्ति में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा एक परियोजना 'पक्योंग (सिक्किम) एयरपोर्ट पर सी/ओ नया एयरपोर्ट, एएआई' में विपरीत मौसम की स्थिति के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डा (मोहाली) का विकास चरण-II, एएआई' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) कोयला क्षेत्र में, 76 परियोजनाओं में से 44 परियोजनाएं विलंबित हैं । माह के दौरान, 5 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । इन 5 परियोजनाओं में से 1 परियोजना मेगा परियोजना है । परियोजना 'तूतीकोरिन थर्मल पावर परियोजना-2X600 मेवा., एनएलसी' में सिविल तथा संरचनात्मक कार्यों में धीमी प्रगति के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'पूरनाडीह ओसीपी (3.0 एमटीवाई), सीसीएल' तथा 'आरजी ओसी-III विस्तार (चरण-II) परियोजना, एससीसीएल' में भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई; परियोजना 'मानिकपुर ओसी विस्तार (3.5 एमटीवाई), एसईसीएल' में पर्यावरण संबंधी मंजूरी तथा वन भूमि के अधिग्रहण में विलंब के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'आरकेपी ओसीपी चरण-I, एससीसीएल' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) पेट्रोलियम क्षेत्र में, 65 परियोजनाओं में से 41 परियोजनाएं विलंबित हैं। माह के दौरान, 7 परियोजनाओं के संबंध में 2-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 7 परियोजनाओं में से 4 परियोजनाएं मेगा परियोजनाएं हैं। परियोजनाएं '23 इमिडिएट सप्लाई वेसल्स (आईएसवी) का निर्माण, ओएनजीसी' तथा 'हीरा तथा दक्षिणी हीरा का पुनर्विकास चरण-II, ओएनजीसी' में क्रमशः ठेकेदार के द्वारा धीमी प्रगति तथा पाइपलाइन पैकेज में अम्बिलिकल लाइन की उपलब्धता न होने के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं "मुंबई रिफाइनरी में सीडीयू/वीडीयू का पुनर्स्थापन, बीपीसीएल' तथा 'कोच्ची एलपीजी टर्मिनल, आईओसीएल' में निर्माण कार्य में धीमी प्रगति तथा सांविधिक मंजूरी प्राप्त न होने के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; एक परियोजना 'एक ईटीपी तथा तीन ईटीपी सह वाटर इंजेक्शन संयंत्र (डब्ल्यूआईपी) का निर्माण, ओएनजीसी' में अभियांत्रिकी तथा इसकी शुरुआत में धीमी प्रगति के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'समूह क के लिए असम नवीकरण परियोजना, ओएनजीसी' तथा 'वशिष्ट तथा एस-1 क्षेत्रों का एकीकृत विकास, ओएनजीसी' में क्रमशः न्यायालय मामले तथा निविदा प्रक्रिया में विलंब के कारण प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

vii) विद्युत क्षेत्र में, 112 परियोजनाओं में से 62 परियोजनाएं विलंबित हैं। माह के दौरान, 4 परियोजनाओं के संबंध में 1-12 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 4 परियोजनाओं में से 1 परियोजना मेगा परियोजना है। एक परियोजना 'सिक्किम से एनआर/डब्ल्यूआर भाग-क में जनरेशन परियोजना से विद्युत के हस्तांतरण के लिए पारेषण प्रणाली, पीजीसीआईएल' में भूमि अधिग्रहण में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; एक परियोजना 'ईस्ट कोस्ट इनर्जी प्रा. लि. तथा एनसीसी विद्युत परियोजना लि. एनटीओए जेन. भाग-ख के साथ जुड़ी सामान्य प्रणाली, पीजीसीआईएल' में विभिन्न आरओडब्ल्यू समस्या तथा वन संबंधी मामलों की धीमी कार्यवाही के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'डब्ल्यूआर तथा एनआर (लाइन बे तथा रिएक्टर प्रावधान) के लिए सामान्य प्रणाली को सुदृढ़ करना, पीजीसीआईएल' तथा 'टेहरी पंप स्टोरेज संयंत्र (पीएसपी) के साथ जुड़ी सामान्य पारेषण प्रणाली, पीजीसीआईएल' प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

10. रेलवे मंत्रालय ने इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी चल रही परियोजनाओं संबंधी मासिक स्थिति रिपोर्टों को प्रस्तुत करने का अभ्यास बंद कर दिया है। अतः, उपलब्ध

सूचना/आंकड़े (जनवरी 2015 की स्थिति के अनुसार) का उपयोग रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में किया गया है।

11. सड़क क्षेत्रके 132 परियोजनाओं संबंधी सूचना/आंकड़े एनएचएआई द्वारा ऑनलाईन अद्यतन की गई है। इन 132 परियोजनाओं में से, 103 परियोजनाओं के लिए संचयी व्यय की सूचना शून्य के रूप में सूचित की गई है तथा 107 परियोजनाओं के संबंध में शुरू करने की तारीख पहले ही खत्म हो चुकी है और एनएचएआई के द्वारा इस संबंध में जानकारी अद्यतन/संशोधित नहीं की गई है।
12. दिनांक 31.05.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।
13. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for May 2015 contains information on the status of the 766 Central Sector Infrastructure Projects costing ₹150 crore and above. During May 2015, 6 projects (3 projects of Petroleum, 2 projects of Power and 1 project of Telecom sector) have reported completion.

2. During the reference month, out of 766 projects, 237 projects are delayed with respect to original schedule and 29 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 29 projects, 11 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	298	32	1	0
2	ROAD TRANSPORT AND HIGHWAYS	132	16	0	0
3	POWER	112	62	4	1
4	PETROLEUM	65	41	7	4
5	COAL	76	44	5	1
6	URBAN DEVELOPMENT	30	15	0	0
7	STEEL	28	16	7	3
8	CIVIL AVIATION	7	4	3	0
9	SHIPPING AND PORTS	7	1	0	0
10	ATOMIC ENERGY	4	3	2	2
11	TELECOMMUNICATIONS	3	1	0	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	1	0	0
15	HEAVY INDUSTRIES	1	1	0	0
Total		766	237	29	11

3. Total original cost of implementation of the 766 projects was ₹10,68,206.97 crore and their anticipated completion cost is likely to be ₹12,73,650.02 crore, which reflects overall cost overruns of ₹2,05,443.05 crore (19.23% of original cost). The expenditure incurred on these projects till May 2015 is ₹4,85,680.02 crore, which is 38.13% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-5-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	31.12
	CIVIL AVIATION				
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	15.77
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	8.19
	COAL				
5	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	76.47
7	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	50.37
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
	HEAVY INDUSTRY				
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
	PETROCHEMICALS				
11	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	80.08
	PETROLEUM				
12	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	820.20
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	75.35
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
16	MARKETING TOP AT KORBA	01/2011	141.86	219.08	54.43
	POWER				
17	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
18	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	159.38
19	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
20	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	143.42
21	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.68	139.35
	RAILWAYS				
22	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
23	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
24	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42

25	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
26	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
30	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	68.99
31	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	42.25
SHIPPING AND PORTS					
32	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
33	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
34	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	51.92
35	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	18.89
STEEL					
36	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
37	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	41.41
URBAN DEVELOPMENT					
38	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 31-5-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs. In crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	4099.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	52.92
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	37.00
COAL					
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20

6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	1552.99
7	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
8	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	236.62
9	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
HEAVY INDUSTRY					
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
11	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	4372.91
PETROLEUM					
12	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
13	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	3525.39
14	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
POWER					
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	9014.67
18	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	3979.44
20	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7531.72	3612.13
21	KOLDAM HEP (NTPC)	10/2002	4527.15	7220.00	2692.85
RAILWAYS					
22	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
23	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
24	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
25	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
26	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
ROAD TRANSPORT AND HIGHWAYS					
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
30	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
31	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	91.95
SHIPPING AND PORTS					
32	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
33	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
34	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	232.00

35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	127.55
STEEL					
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	3599.00
37	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
URBAN DEVELOPMENT					
38	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 766 projects, 2 projects are ahead of schedule, 127 are on schedule and 237 are delayed with respect to original schedule. However, the number of delayed projects decreases to 211 if delay is calculated on the basis of latest schedule of completion. Further, 29 projects have been sanctioned without original commissioning schedule date and for 371 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 237 delayed projects, 49 projects have overall delay in the range of 1 to 12 months, 51 projects have delay in the range of 13 to 24 months, 88 projects have delay in the range of 25 to 60 months and 49 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 31-5-2015)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	09/2015	81
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
CIVIL AVIATION					
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	01/2009	01/2011	06/2017	77
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	02/2010	03/2014	05/2015	14
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	09/2015	6
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	03/2015	05/2015	2
COAL					
8	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
9	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	06/2009	06/2015	72
11	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72

12	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
HEAVY INDUSTRY					
13	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75
PETROCHEMICALS					
14	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	06/2015	38
PETROLEUM					
15	DEV OF G1 AND GS-15 (ONGCL)	04/2003	04/2006	06/2015	110
16	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
17	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	06/2018	53
19	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2015	51
POWER					
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
21	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
22	BARH STPP(3X660MW) NTPC	02/2005	12/2009	03/2018	99
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2015	96
24	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	07/2010	05/2018	94
RAILWAYS					
25	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
26	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
27	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
28	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
29	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
ROAD TRANSPORT AND HIGHWAYS					
30	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	09/2017	120
31	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	06/2015	85
32	DHARAMTUL TO SONAPUR (AS-19)	12/2003	06/2008	05/2015	83
33	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	04/2010	01/2016	69
34	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	08/2011	12/2015	52
SHIPPING AND PORTS					
35	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
STEEL					
36	AUGMENTATION OF IRON ORE STORAGE IN RMHP	07/2007	09/2009	06/2015	69
37	EXPANSION OF BOKARO STEEL PLANT	05/2010	12/2011	08/2015	44
38	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	03/2016	36
39	EXPANSION OF DURGAPUR STEEL PLANT	08/2010	12/2012	06/2015	30
40	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	08/2015	27
TELECOMMUNICATIONS					
41	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	09/2015	59
URBAN DEVELOPMENT					
42	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	06/2015	36

43	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	06/2017	34
44	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	11/2015	30
45	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	12/2016	24
46	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	05/2012	12/2014	04/2016	16

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones is as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-5-2015)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT	02/2011	452.00	489.00	410.25	03/2015	04/2015

4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	GAGAN PROJECT	09/2008	626.00	626.00	514.70	06/2013	N.A.
COAL							
6	MURAI DIH UG	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	AMERA OC RCE	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	AMRITDHARA OC PROJECT	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020
FERTILISERS							
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	13.09	11/2016	11/2016
HEAVY INDUSTRY							
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
13	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
PETROLEUM							
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	352.49	115.81	03/2014	05/2016
POWER							
19	BRBCL-NABINAGAR - JV	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	NPGCPL-NABINAGAR - JV	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	URTD SM PHASE-I	01/2014	374.63	374.63	0.00	04/2016	04/2016

22	SYSTEM STRENGTHENING IN SOUTHERN REGION – XXIII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAG A HEP	01/2015	268.80	268.80	0.00	03/2018	03/2018
RAILWAYS							
24	JIND-SONEPAT (NL),NR	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	RANGIA-MURKONGSELE K, (GC) ALONG WITH LINKED FINGER	01/2004	915.70	3700.00	3198.30	N.A.	03/2015
26	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	579.37	599.40	N.A.	02/2012
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	514.68	2820.00	329.67	N.A.	N.A.
28	DAUSA-GANGAPUR CITY(NL),NWR	02/1997	410.08	410.08	294.70	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS							
29	4-LANNING OF CHAPRA-HAJIPUR	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	DEOLI-KOTA	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	JORBAT - BARAPANI	01/2011	536.00	536.00	0.00	01/2014	N.A.
32	KANDLA - MUNDRA PORT	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	2 LANING WITH PS KANPUR KABRAI	01/2013	373.47	373.47	0.00	07/2014	N.A.
SHIPPING AND PORTS							
34	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIE	02/2011	830.00	621.53	0.00	05/2013	N.A.
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	373.22	373.22	04/2009	N.A.
36	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	N.A.
37	MODIFICATION AND STRENGTHENING OF EXISTING BERTH N	06/2010	277.00	277.00	0.21	03/2012	N.A.
38	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE	10/2002	150.00	600.00	139.80	03/2006	N.A.

	STEEL						
39	GAS NETWORK BSL	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	NEW HSM AT RSP	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	24.02	10/2016	10/2016
	TELECOMMUNICATIONS						
42	NFS	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE	05/2006	1077.00	1077.00	0.00	03/2009	N.A.
44	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	55.22	10/2010	09/2015
	URBAN DEVELOPMENT						
46	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-4	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	171.10	0.00	09/2014	N.A.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-

reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-5-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	18271.00
CIVIL AVIATION					
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	338.82
COAL					
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3027.59	3207.92
PETROLEUM					
4	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5925.40
POWER					
5	BARH STPP STAGE -II	02/2008	7341.04	0.00	8631.00
6	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7687.18
7	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5040.21
8	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	3934.97
9	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	11/2011	2127.51	0.00	2172.33
10	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1742.55
RAILWAYS					
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
12	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	0.00	4734.45
13	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1049.69	3385.14	3541.20
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	1000.00	3410.06
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	915.70	3198.30
ROAD TRANSPORT AND HIGHWAYS					
16	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	0.00	3466.00
17	4 LANING OF NAGPUR-BETUL	02/2011	2498.76	0.00	2786.00
18	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2762.00
19	GHAZIABAD-ALIGARH NH-91	02/2011	1141.00	0.00	2445.00
20	MURADABAD-BAREILY	04/2010	1267.00	0.00	2425.00
SHIPPING AND PORTS					
21	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	0.00	373.22

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-5-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURAI DIH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING -XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014

2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.
4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

9. The Sector-wise details of additional delays are as under:-

- i) In the **Railways**, out of 298 projects, 32 projects are delayed. During the month 1 project 'Dindigul-Pollachi-Palghat-Pollachi and Coimbatore' is delayed by 12 months due to delay in land acquisition problem in Pollachi-Podanur section.
- ii) In the **Atomic Energy**, out of 4 projects, 3 projects are delayed. During the month 2 projects 'Rajasthan Atomic Power Project-7 and 8 (2X700 MW) NPCIL' and 'Kudankulam APP, NPCIL' have reported additional delay of 1 month and 3 months respectively due to delay in supply of equipments.

- iii) In the **Steel**, out of 28 projects, 16 projects are delayed. During the month 7 projects have reported additional delay in the range of 1-6 months. Out of 7 projects, 3 projects are mega projects. The project 'Expansion of Durgapur Steel Plant SAIL' has reported additional delay of 1 month due to shortcomings in design and engineering and poor performance of civil works; the projects 'Expansion of Bokaro Steel Plant, SAIL' and 'Installation of 45MVA SAFT With Other Associated Facilities, SAIL' have reported additional delay of 3 months and 4 months respectively due to contractual issues and delay in obtaining environmental clearances respectively; the project 'Expansion of Bhilai Steel Plant, SAIL' has reported additional delay of 6 months due to shortcomings in the design and engineering; two projects 'Rebuilding of Coke Oven Battery-3 AT Rourkela Steel Plant, Rourkela, Odisha, SAIL' and 'Captive Power Plant-2, RINL' have reported additional delay of 1 month each and the project 'Rebuilding of Battery Block 5A and Re-Construction of Battery Block 5B, SAIL' has reported additional delay of 6 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
- iv) In the **Civil Aviation**, out of 7 projects, 4 projects are delayed. During the month 3 projects have reported additional delay in the range of 1-12 months. 1 project 'Establishment of Airport Operations Control Centres at 10 Airports; AAI' is having additional delay of 1 month due to delay in supply of equipments and one project 'C/O New Airport at Pakyong (Sikkim) Airport, AAI' is delayed by 12 months due to adverse weather condition; the project 'Development of Chandigarh International Airport (Mohali) Ph – II, AAI' has reported additional delay of 1 month (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
- v) In the **Coal Sector**, out of 76 projects, 44 projects are delayed. During the month, 5 projects have reported additional delay in the range of 1-24 months. Out of 5 projects, 1 project is mega projects. The project 'Tuticorin Thermal Power Project- 2X500 MW, NLC' has reported additional delay of 1 month due to slow progress in civil and structural works; two projects 'Purnadih OCP (3.0 MTY) CCL' and 'RG OC-III Extension (Phase -II) project SCCL' have reported additional delay of 12 months each due to delay in land acquisition; the project 'Manikpur OC Expansion (3.5 MTY) SECL' has reported additional delay of 24 months due to delay in environment clearance and delay in possession of forest land; the project 'RKP OCP Phase-I SCCL' has reported additional delay of 1 month (however, no specific reasons have been

reported by the project implementing agencies for the delay in this project).

- vi) In the **Petroleum Sector**, out of 65 projects, 41 projects are delayed. During the month, 7 projects have reported additional delays in the range of 2-12 months. Out of 7 projects, 4 projects are mega projects. The projects 'Construction of 23 Immediate Supply Vessels (ISV), ONGC' and 'Heera and South Heera Redevelopment Ph-II, ONGC' have reported additional delay of 2 months each due to slow progress by contractor and due to Non availability of umbilical line in pipeline package respectively; the projects 'Replacement of CDU/VDU at Mumbai Refinery, BPCL' and 'LPG Terminal at KOCHI, IOCL' have reported additional delay of 3 months each due to slow progress in construction and non receiving of statutory clearances; one project 'Construction of One ETP and Three ETPs Cum Water Injection Plants (WIP), ONGC' has reported additional delay of 7 months due to slow progress in engineering and procurement; two projects 'Assam Renewal Project For Group A, ONGC' and 'Integrated Development of Vashista and S-1 Fields, ONGC' have reported additional delay of 12 months each due to court cases and delay in tendering process respectively.
- vii) In the **Power Sector**, out of 112 projects, 62 projects are delayed. During the month, 4 projects have reported additional delay in the range of 1-12 months. Out of 4 projects, 1 project is mega project. 1 project 'Transmission System for Transfer of Power From Generated Project in Sikkim to NR/WR Part-A, PGCIL' has reported additional delay of 3 months due to delay in land acquisition; 1 project 'Common System Associated With East Coast Energy Pvt Ltd and NCC Power Projects Ltd LTOA Gen Part- B, PGCIL' has reported additional delay of 12 months due to severe RoW problem and low processing of forest case; two projects 'System Strengthening Common For WR and NR (Line Bays and Reactor Provision), PGCIL' and 'Transmission System Associated With Tehri Pump Storage Plant (PSP), PGCIL' have reported additional delay of 1 month each (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
11. Ministry of Railway has discontinued the practice of furnishing monthly status reports on all on-going projects being implemented by Railways to this Ministry. Therefore, the available information/data (as on January 2015) has been used in respect of all projects of Railways sector.
12. The information/ data of 132 projects of Road Sector has been online updated by NHAI. Out of these 132 projects, the cumulative expenditure for 103 projects has been


reported as zero and 107 projects for which the date of commissioning has already been lapsed and the same has not been updated/ revised by NHAI.

13. The status as on 31.05.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.
14. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	298	1
2	ROAD TRANSPORT AND HIGHWAYS	132	0
3	POWER	112	4
4	COAL	76	5
5	PETROLEUM	65	7
6	URBAN DEVELOPMENT	30	0
7	STEEL	28	7
8	CIVIL AVIATION	7	3
9	SHIPPING AND PORTS	7	0
10	ATOMIC ENERGY	4	2
11	TELECOMMUNICATIONS	3	0
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	0
15	HEAVY INDUSTRY	1	0
	Total	766	29

Sectoral break up of on-going infrastructure projects.

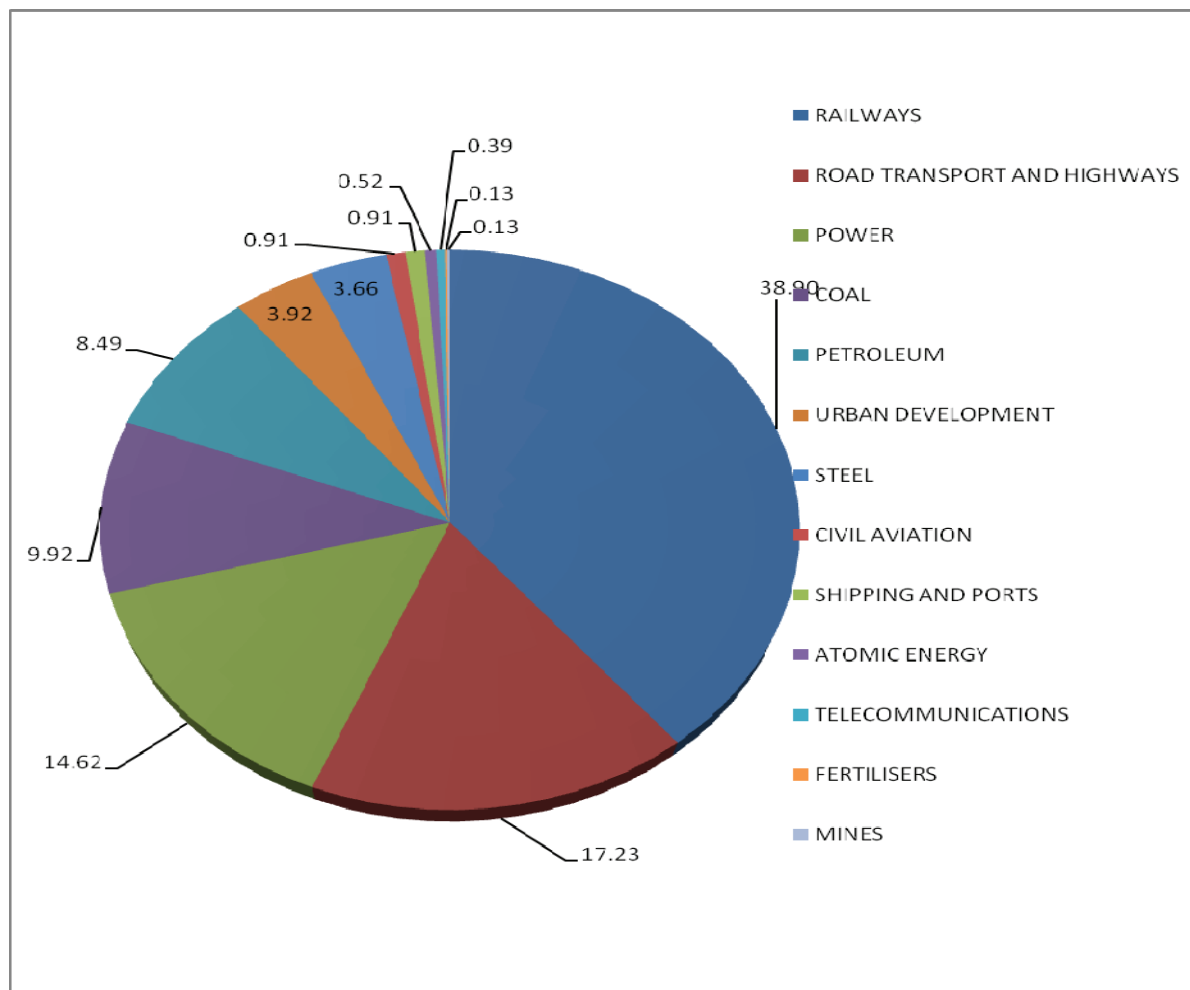

Month wise List of Completed Projects Costing Rs. 150 Crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May, 2015			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000170]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N24000127]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000127]	2,913.10	05/2016	13.86


Summary of projects in the Flash Report for the month of May, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	758
Number of Projects completed/dropped/frozen in Current Month	12
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	22
Number of Projects in Current Month	766

Brief Analysis


Project Status with respect to Original Schedule: Out of 766 projects, 2 projects are ahead of schedule, 127 projects are on schedule 237 projects are delayed. 371 projects do not have fixed dates of commissioning. 29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

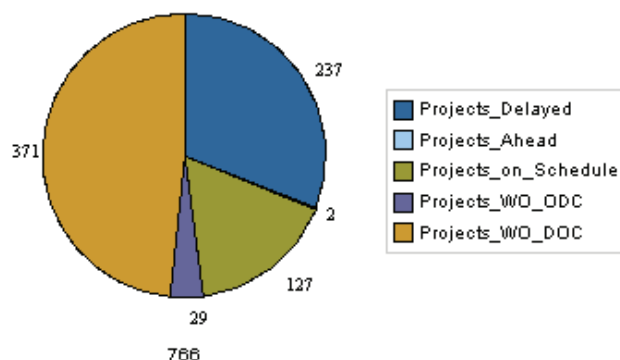

Investment Scenario

Total original cost of implementation of 766 projects when sanctioned, was of the order of Rs. 1068206.97 crore but this was subsequently revised to Rs. 1273650.02 crore implying a cost overrun of 19.2%. The expenditure incurred on these projects till May, 2015 is Rs. 485680.02 crore, which is 38.1% of the revised cost of the projects.

Figures are in Rs. Crore

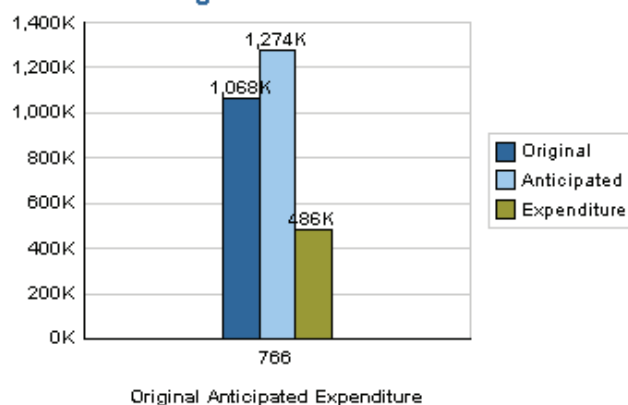

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	758
No of Projects Completed/Dropped/Frozen in Current Month	12
No of Projects added in Current Month	22
No of Projects in Current Month	766

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	237	2	127	29	371	766	30.94
Latest Approved (Date)	211	3	152	29	371	766	27.55

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	652	8,90,260.70	9,77,581.75	3,03,323.26	31.00	87,321.05	9.80
Project with Revision in Cost	114	2,37,821.51	2,96,068.27	1,82,356.76	61.60	58,246.76	24.50
Total	766	11,28,082.21	12,73,650.02	4,85,680.02	38.13	145567.81	12.90
Original Cost of All Projects							
Original Cost	766	10,68,206.97	12,73,650.02	4,85,680.02	38.13	2,05,443.05	19.23

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	237	482,575.22	590,529.85	338,372.93	57.30	107,954.63	22.40
Latest Approved (RCE)	213	471,452.57	530,889.88	314,100.63	59.20	59,437.31	12.60
Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	29	81,794.31	89,053.96	63,655.18	71.50	7,259.65	8.90

<u>Extent of cost overrun in projects with respect to original schedule (Sector Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	7	2,599.56	2,689.48	3.46	2	787.61	877.53	11.42
3	COAL	76	59,371.42	63,381.37	6.75	6	8,198.48	12,806.16	56.20
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	28	64,995.71	68,710.11	5.71	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	80.08
8	PETROLEUM	65	144,046.84	153,341.30	6.45	16	59,208.68	73,406.58	23.98
9	POWER	112	316,428.52	355,392.40	12.31	22	54,099.77	93,127.26	72.14
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS	298	173,660.34	302,322.34	74.09	163	87,416.65	217,200.13	148.47
12	ROAD TRANSPORT AND HIGHWAYS	132	98,429.90	100,253.98	1.85	9	2,934.62	4,786.21	63.09
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	4	1,990.06	3,102.68	55.91
14	TELECOMMUNICATIONS	3	14,795.00	14,795.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		766	1,068,206.97	1,273,650.02	19.23	229	253,907.48	466,302.77	83.65

Extent of cost overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	28	25,167.01	31,389.44	24.72	7	11,072.36	17,294.79	56.20
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	3	9,356.22	23,263.83	148.65
3	ASSAM	35	23,171.23	41,510.44	79.15	15	16,833.87	35,290.74	109.64
4	BIHAR	48	57,726.67	71,504.87	23.87	15	13,737.73	28,243.47	105.59
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	15.77
6	GUJARAT	26	28,108.61	28,687.78	2.06	4	1,202.26	2,117.22	76.10
7	HARYANA	9	4,659.81	6,630.43	42.29	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	11,681.24	19,906.33	70.41	3	9,493.62	17,718.71	86.64
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	34	66,982.20	81,944.97	22.34	17	13,700.79	28,669.59	109.26
11	KERALA	13	24,457.67	28,611.45	16.98	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	46	98,557.84	108,038.31	9.62	12	18,450.10	28,382.49	53.83
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	42	72,202.55	81,290.49	12.59	14	35,439.50	44,548.78	25.70
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	25	26,236.17	26,291.64	0.21	6	2,574.16	3,142.63	22.08
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	42	68,208.56	85,860.44	25.88	20	30,028.23	47,680.11	58.78
23	TRIPURA	6	2,966.26	6,629.97	123.51	5	2,678.22	6,376.31	138.08
24	UTTAR PRADESH	30	36,706.01	39,695.73	8.15	9	2,951.38	5,989.36	102.93
25	WEST BENGAL	39	42,838.90	52,831.80	23.33	13	8,447.62	18,669.36	121.00
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	8.19
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
28	DELHI	12	50,903.45	50,903.45	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	28	80,681.93	82,331.47	2.04	6	3,494.57	5,144.11	47.20
30	JHARKHAND	37	38,870.74	39,535.41	1.71	6	1,641.96	2,478.40	50.94
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
33	TELANGANA	21	9,410.62	12,235.26	30.02	6	1,903.46	4,728.10	148.40
34	MULTI STATE	187	212,378.07	237,630.89	11.89	41	24,378.87	53,480.92	119.37
Total		766	1,068,206.97	1,273,650.02	19.23	229	253,907.48	466,302.77	83.65

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	17 - 81
2	CIVIL AVIATION	7	2,599.56	2,689.48	3.46	4	1,323.34	1,360.34	2 - 77
3	COAL	76	59,371.42	63,381.37	6.75	44	31,052.51	35,167.14	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	28	64,995.71	68,710.11	5.71	16	47,384.59	47,354.59	6 - 69
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38 - 38
8	PETROLEUM	65	144,046.84	153,341.30	6.45	41	82,753.10	89,307.41	2 - 110
9	POWER	112	316,428.52	355,392.40	12.31	62	151,602.03	181,551.24	3 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS	298	173,660.34	302,322.34	74.09	32	28,013.16	84,366.38	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	132	98,429.90	100,253.98	1.85	16	13,301.24	13,393.22	11 - 120
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	1	366.39	669.46	61 - 61
14	TELECOMMUNICATIONS	3	14,795.00	14,795.00	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	15	82,266.25	82,266.25	2 - 36
	Total	766	1,068,206.97	1,273,650.02	19.23	237	482,575.22	590,529.85	

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	28	25,167.01	31,389.44	24.72	4	2,630.89	3,137.24	8 - 44
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	2	3,070.89	7,963.83	31 - 87
3	ASSAM	35	23,171.23	41,510.44	79.15	11	17,357.22	31,847.63	11 - 110
4	BIHAR	48	57,726.67	71,504.87	23.87	6	19,811.45	29,744.97	20 - 99
5	GOA	1	335.61	388.53	15.77	0	0.00	0.00	-
6	GUJARAT	26	28,108.61	28,687.78	2.06	3	12,329.08	12,252.39	19 - 39
7	HARYANA	9	4,659.81	6,630.43	42.29	0	0.00	0.00	-
8	HIMACHAL PRADESH	5	11,681.24	19,906.33	70.41	3	8,717.57	15,022.55	11 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	6	13,202.50	32,123.18	10 - 193
10	KARNATAKA	34	66,982.20	81,944.97	22.34	6	4,357.71	5,417.36	12 - 96
11	KERALA	13	24,457.67	28,611.45	16.98	3	2,217.06	2,917.06	18 - 45
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	6	2,304.29	2,206.15	12 - 69
13	MAHARASHTRA	46	98,557.84	108,038.31	9.62	18	56,487.30	61,257.93	2 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	0	0.00	0.00	-
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	42	72,202.55	81,290.49	12.59	16	38,298.46	43,470.05	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	-
20	RAJASTHAN	25	26,236.17	26,291.64	0.21	2	13,426.00	12,998.02	17 - 39
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 77
22	TAMIL NADU	42	68,208.56	85,860.44	25.88	11	48,419.68	56,149.65	3 - 90
23	TRIPURA	6	2,966.26	6,629.97	123.51	5	2,714.26	5,743.32	5 - 108
24	UTTAR PRADESH	30	36,706.01	39,695.73	8.15	8	11,808.45	13,553.85	9 - 120
25	WEST BENGAL	39	42,838.90	52,831.80	23.33	12	14,633.09	18,666.02	3 - 177
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	2 - 2
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	-
28	DELHI	12	50,903.45	50,903.45	0.00	5	42,630.16	42,630.16	8 - 34
29	CHHATTISGARH	28	80,681.93	82,331.47	2.04	14	55,685.34	56,167.39	9 - 72
30	JHARKHAND	37	38,870.74	39,535.41	1.71	21	13,241.54	13,780.92	2 - 138
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	3	7,127.06	10,570.24	52 - 94
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
33	TELANGANA	21	9,410.62	12,235.26	30.02	11	3,359.39	4,375.44	8 - 72
34	MULTI STATE	187	212,378.07	237,630.89	11.89	54	84,079.27	89,799.91	3 - 261
	Total	766	1,068,206.97	1,273,650.02	19.23	237	482,575.22	590,529.85	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	42,627.00	46,726.00	9.62	1	13,171.00	17,270.00	31.12
2	CIVIL AVIATION	7	2,636.56	2,689.48	2.01	1	335.61	388.53	15.77
3	COAL	76	63,008.27	63,381.37	0.59	3	3,647.96	4,488.76	23.05
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	28	68,594.71	68,710.11	0.17	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,833.52	10.24	1	8,920.00	9,833.52	10.24
8	PETROLEUM	65	154,813.12	153,341.30	-0.95	4	15,206.31	17,623.34	15.89
9	POWER	112	338,788.65	355,392.40	4.90	5	17,399.92	34,003.67	95.42
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS	298	187,075.37	302,322.34	61.60	157	92,775.91	209,360.19	125.66
12	ROAD TRANSPORT AND HIGHWAYS	132	98,543.85	100,253.98	1.74	8	2,717.01	4,476.65	64.76
13	SHIPPING AND PORTS	7	5,827.07	6,428.61	10.32	4	2,292.67	3,102.68	35.33
14	TELECOMMUNICATIONS	3	14,795.00	14,795.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		766	1,128,082.21	1,273,650.02	12.90	187	164,922.39	316,472.04	91.89

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	3,492.00	5,677.00	0- 0
2	CIVIL AVIATION	7	2,599.56	2,689.48	3.46	0	0.00	0.00	0- 0
3	COAL	76	59,371.42	63,381.37	6.75	2	6,935.32	10,186.51	39- 72
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	28	64,995.71	68,710.11	5.71	1	8,692.00	12,291.00	66- 66
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38- 38
8	PETROLEUM	65	144,046.84	153,341.30	6.45	7	34,975.40	44,635.28	11- 110
9	POWER	112	316,428.52	355,392.40	12.31	11	23,527.00	38,449.21	16- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	RAILWAYS	298	173,660.34	302,322.34	74.09	4	5,873.07	10,121.84	48- 174
12	ROAD TRANSPORT AND HIGHWAYS	132	98,429.90	100,253.98	1.85	2	425.61	517.56	69- 84
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	3	14,795.00	14,795.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		766	1068206.97	1273650.02	19.23	29	89381.01	131711.92	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	13,171.00	17,270.00	81- 81
2	CIVIL AVIATION	7	2,599.56	2,689.48	3.46	1	452.00	489.00	2- 2
3	COAL	76	59,371.42	63,381.37	6.75	4	7,617.44	12,121.30	30- 72
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	28	64,995.71	68,710.11	5.71	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38- 38
8	PETROLEUM	65	144,046.84	153,341.30	6.45	11	37,572.15	48,973.36	11- 110
9	POWER	112	316,428.52	355,392.40	12.31	21	47,814.44	77,827.26	5- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	RAILWAYS	298	173,660.34	302,322.34	74.09	28	22,395.40	78,977.44	3- 261
12	ROAD TRANSPORT AND HIGHWAYS	132	98,429.90	100,253.98	1.85	2	565.77	657.75	69- 120
13	SHIPPING AND PORTS	7	5,524.46	6,428.61	16.37	1	366.39	669.46	61- 61
14	TELECOMMUNICATIONS	3	14,795.00	14,795.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		766	1068206.97	1273650.02	19.23	71	137133.2	250646.39	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3,248.78	08/2010	5,933.42	05/2015	5,933.42
2	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	01/2010	723.64	03/2013	723.64	06/2016	.00
3	DEVELOPMENT OF CLUSTER-7 FIELDS	03/2010	4,550.40	03/2013	6,638.94	05/2015	2,583.55
4	AHMEDABAD REDEVELOPMENT PROJECT	11/2010	1,916.10	12/2014	1,916.10	12/2017	1,160.14
5	MEHESANA REDEVELOPMENT PROJECT	11/2010	3,823.00	04/2015	3,823.00	12/2017	1,076.57
6	ANKLESWAR REDEVELOPMENT	11/2010	2,189.63	12/2014	2,189.63	12/2018	1,034.30
7	PIPELINE REPLACEMENT PROJECT-3	04/2012	2,547.26	05/2014	1,417.00	05/2015	1,412.08
8	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	12/2012	3,513.07	02/2016	4,619.94	04/2017	.47
9	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS	03/2013	2,913.10	05/2016	2,913.10	04/2018	13.86
	<u>POWER</u>						
10	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	12/2011	901.77	08/2014	1,025.28	05/2015	945.20
11	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI	09/2012	803.34	03/2015	803.34	05/2015	593.19
	<u>TELECOMMUNICATIONS</u>						
12	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	01/2009	336.81	03/2015	199.37

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	MADHUBAND NLW WASHERY	11/2012	289.45	5/2014	289.45	4/2016
2	PATHERDIH NLW WASHERY	10/2012	269.82	4/2014	269.82	4/2016
3	NEW MAJRI UG TO OC	5/2015	295.56	3/2019	295.56	3/2019
	<u>PETROLEUM</u>					
4	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	6,068.80	4/2019	6,068.80	4/2019
5	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	5/2015	257.87	11/2016	257.87	11/2016
6	DAMAN DEVELOPMENT PROJECT	8/2014	6,086.08	5/2019	6,086.08	5/2019
	<u>POWER</u>					
7	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	436.68	12/2016	436.68	12/2016
8	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)	5/2015	780.33	7/2017	780.33	7/2017
9	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I)	5/2015	312.94	6/2016	312.94	6/2016
	<u>RAILWAYS</u>					
10	HUBLI- CHIKJAJUR	3/2015	1,900.00	/	1,900.00	-
11	PHULERA - DIGANA DOUBLING	5/2015	600.00	/	600.00	-
12	MIRAJ-LONDA	3/2015	1,830.00	/	1,830.00	-
13	SAMASTIPUR-DARBANGHA	5/2015	380.00	/	380.00	-
14	ROHTAK - BHIWANI DOUBLING	5/2015	400.00	/	400.00	-
15	HOTGI-KUDGI-GADAG	3/2015	1,618.00	/	1,618.00	-
16	HAJIPUR - BACHAWARA	5/2015	720.00	/	720.00	-
17	ARSIKERE-TUMKUR	3/2015	960.00	/	960.00	-
18	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	873.71	/	873.71	-
19	YELAHANKA-PENUKONDA	5/2015	860.43	/	860.43	-
	<u>SHIPPING AND PORTS</u>					
20	CONSTRUCTION OF OFFSHORE CONTAINER	1/2007	366.39	12/2010	669.46	1/2016

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB					
	<u>STEEL</u>					
21	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	1,034.01	10/2017	1,034.01	10/2017
22	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	1,154.18	12/2017	1,154.18	12/2017


Milestones (Cumulative due & achieved)

Total	3737
Achieved up to month	1572


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) NPCIL	12,320.00	12,320.00	12/2016	04/2018	05/2018	1
2	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	06/2015	09/2015	3
	<u>CIVIL AVIATION</u>						
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II AAI	452.00	489.00	03/2015	04/2015	05/2015	1
4	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS AAI	344.28	344.28	03/2014	04/2015	05/2015	1
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT AAI	309.46	309.46	01/2011	06/2016	06/2017	12
	<u>COAL</u>						
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	05/2015	06/2015	1
7	RKP OCP PHASE-I SCCL	209.78	209.78	03/2015	03/2016	04/2016	1
8	PURNADIH OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2016	03/2017	12
9	RG OC -III EXTENSION (PHASE -II) PROJECT SCCL	365.01	365.01	06/2015	03/2016	03/2017	12
10	MANIKPUR OC EXPANSION (3.5 MTY) SECL	321.50	321.50	03/2014	03/2016	03/2018	24
	<u>STEEL</u>						
11	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	05/2015	06/2015	1
12	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA SAIL	237.09	237.09	12/2014	08/2015	09/2015	1
13	CAPTIVE POWER PLANT - 2 RINL	677.00	677.00	09/2013	05/2015	06/2015	1
14	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	05/2015	08/2015	3
15	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	08/2015	12/2015	4

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	09/2015	03/2016	6
17	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B SAIL	313.05	313.05	06/2015	06/2015	12/2015	6
	<u>PETROLEUM</u>						
18	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) ONGC	331.20	269.10	08/2013	05/2015	07/2015	2
19	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II ONGC	5,608.40	5,608.40	05/2015	05/2015	07/2015	2
20	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY BPCL	1,419.00	1,419.00	12/2014	03/2015	06/2015	3
21	LPG TERMINAL AT KOCHI IOCL	607.06	607.06	01/2016	04/2017	07/2017	3
22	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) ONGC	202.94	188.89	01/2014	11/2017	06/2018	7
23	ASSAM RENEWAL PROJECT FOR GROUP A ONGC	2,465.15	2,378.89	03/2013	03/2016	03/2017	12
24	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS ONGC	4,124.35	4,124.35	04/2016	04/2016	04/2017	12
	<u>POWER</u>						
25	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	05/2015	06/2015	1
26	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) PGCIL	871.62	871.62	11/2017	10/2017	11/2017	1
27	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	250.03	250.03	01/2013	06/2015	09/2015	3
28	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL	2,514.88	2,514.88	12/2015	03/2015	03/2016	12
	<u>RAILWAYS</u>						
29	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE SR	343.17	914.98	N.A.	03/2015	03/2016	12

Graphical Presentation of All Projects w.r.t. Original Schedule

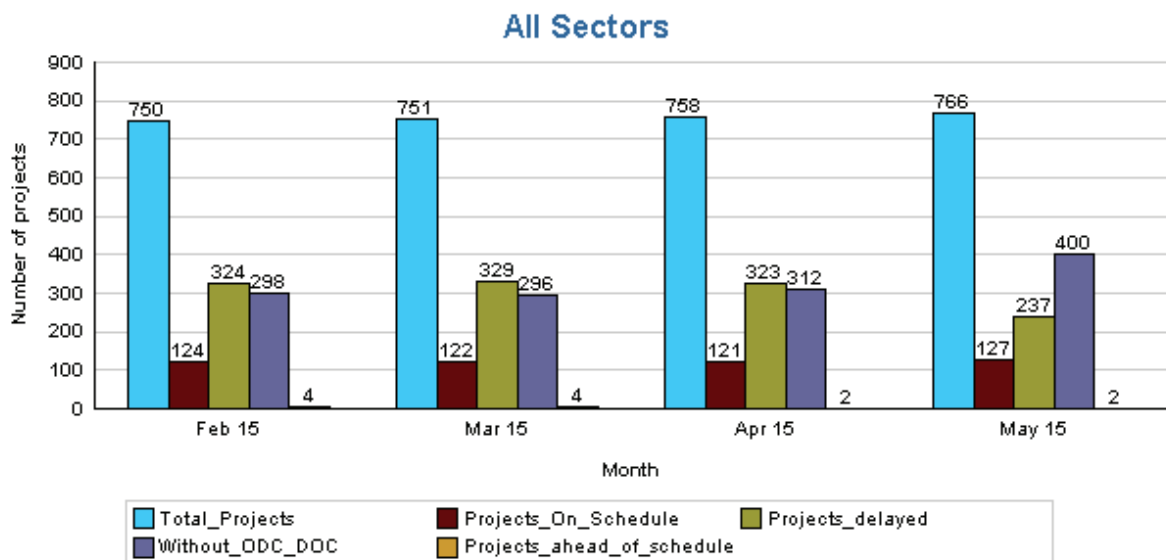


Break-up of 237 Delayed projects in May 2015

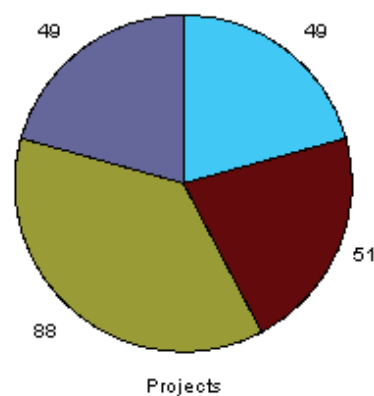


Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

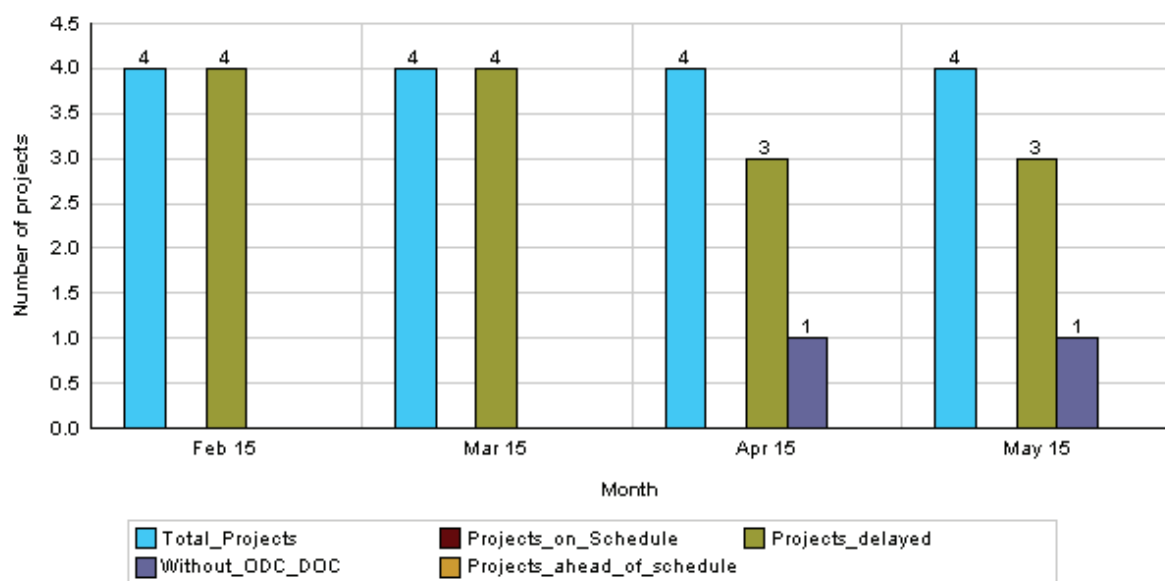


Break-up of 3 Delayed projects in May 2015

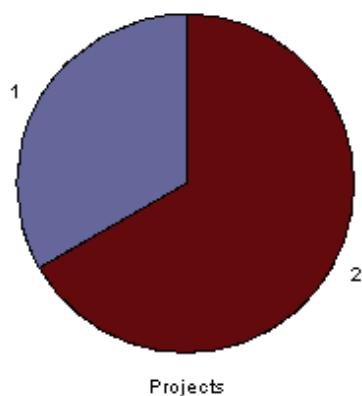


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

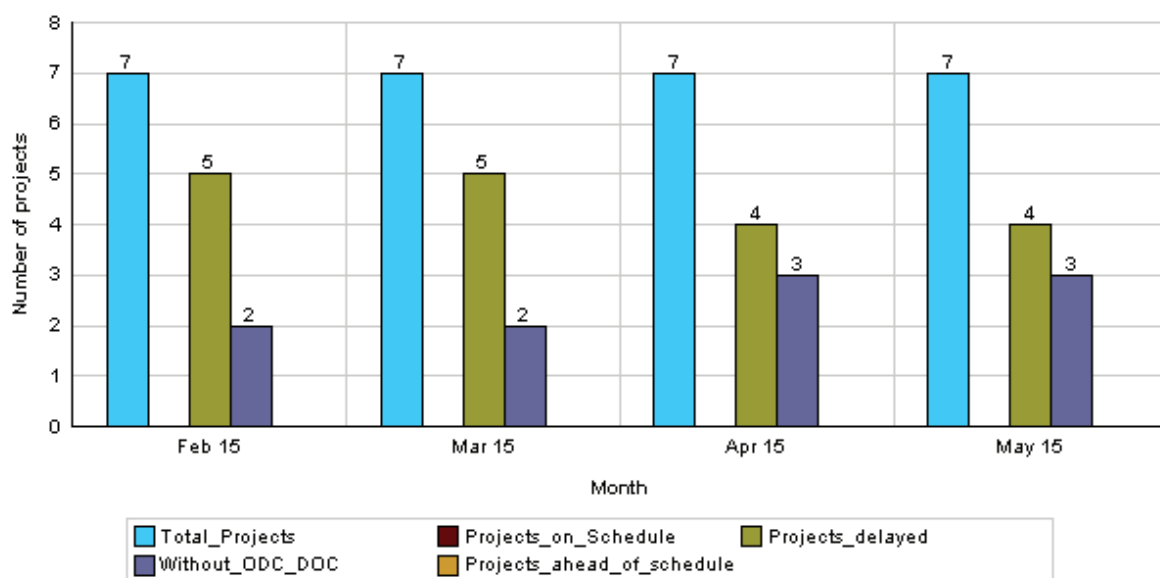


Break-up of 4 Delayed projects in May 2015

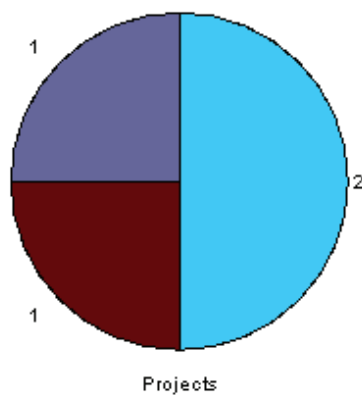


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of COAL Sector

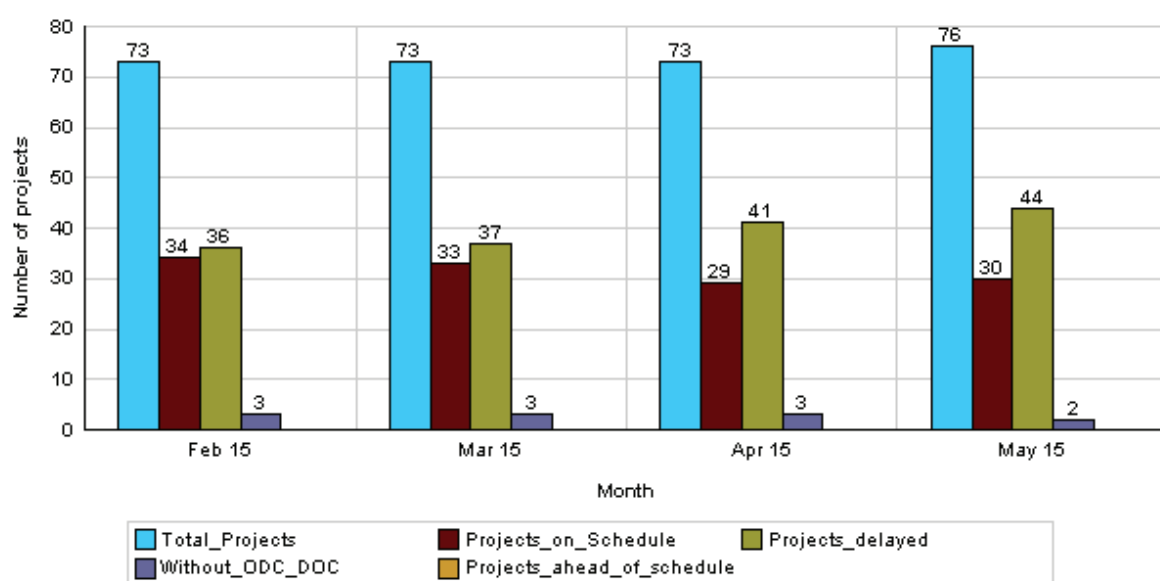


Break-up of 44 Delayed projects in May 2015

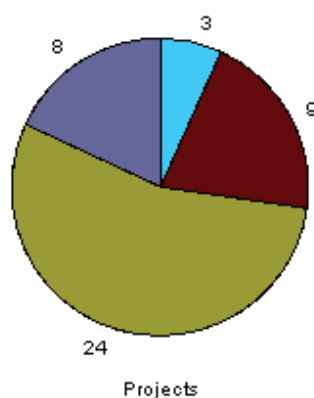


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

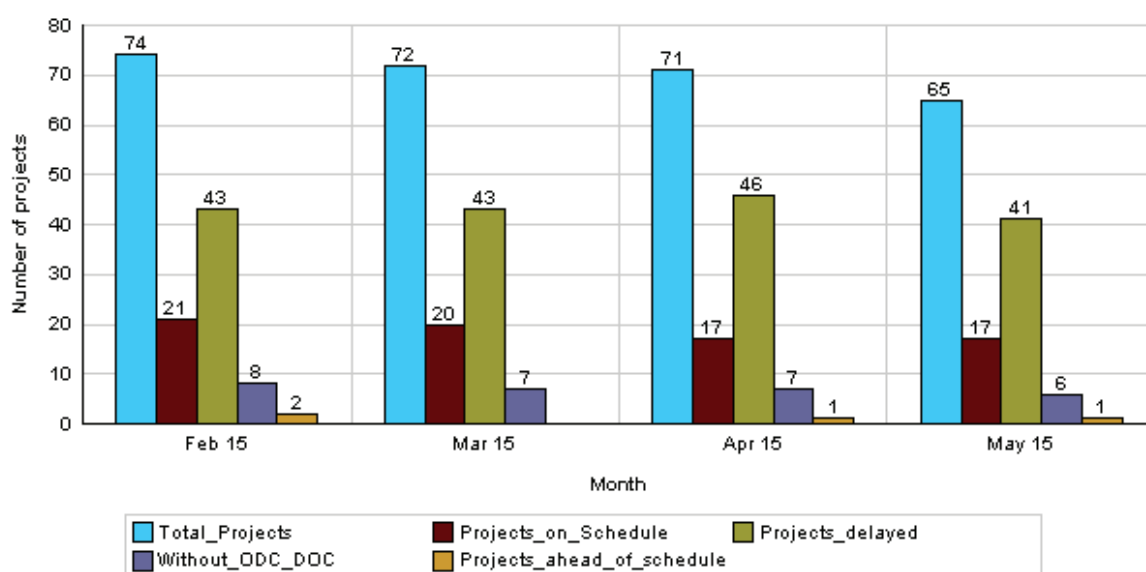


Break-up of 41 Delayed projects in May 2015

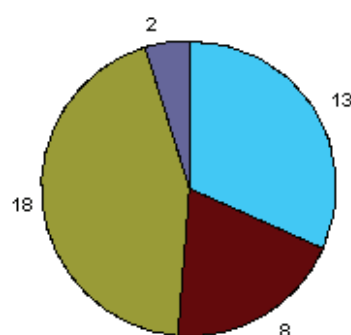


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

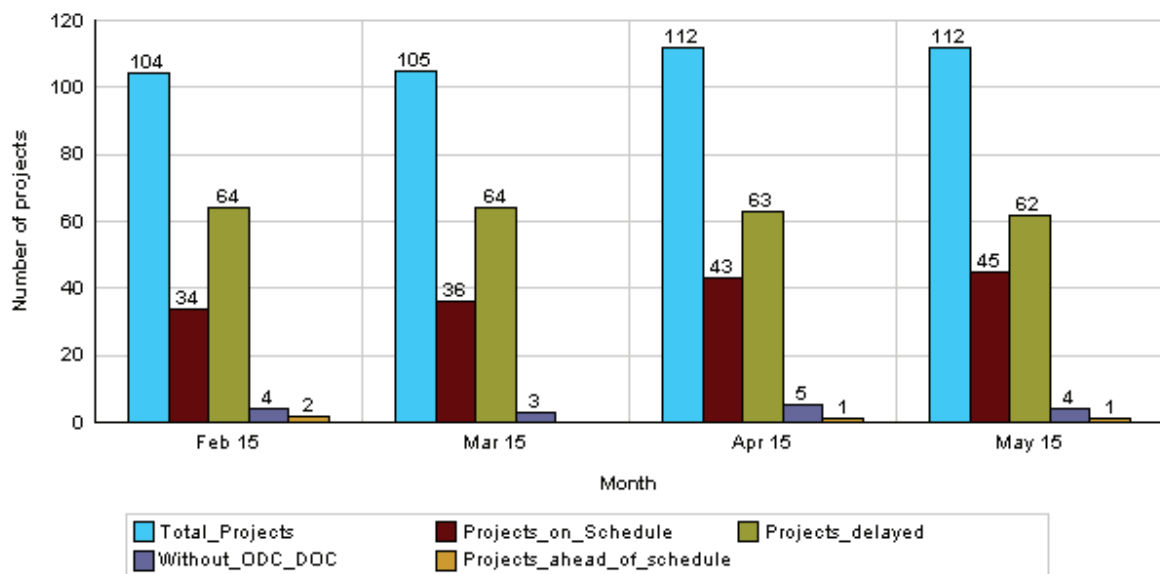


Break-up of 62 Delayed projects in May 2015

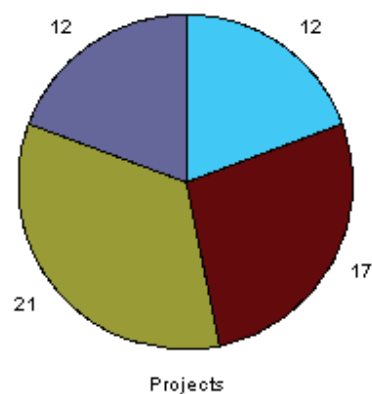


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

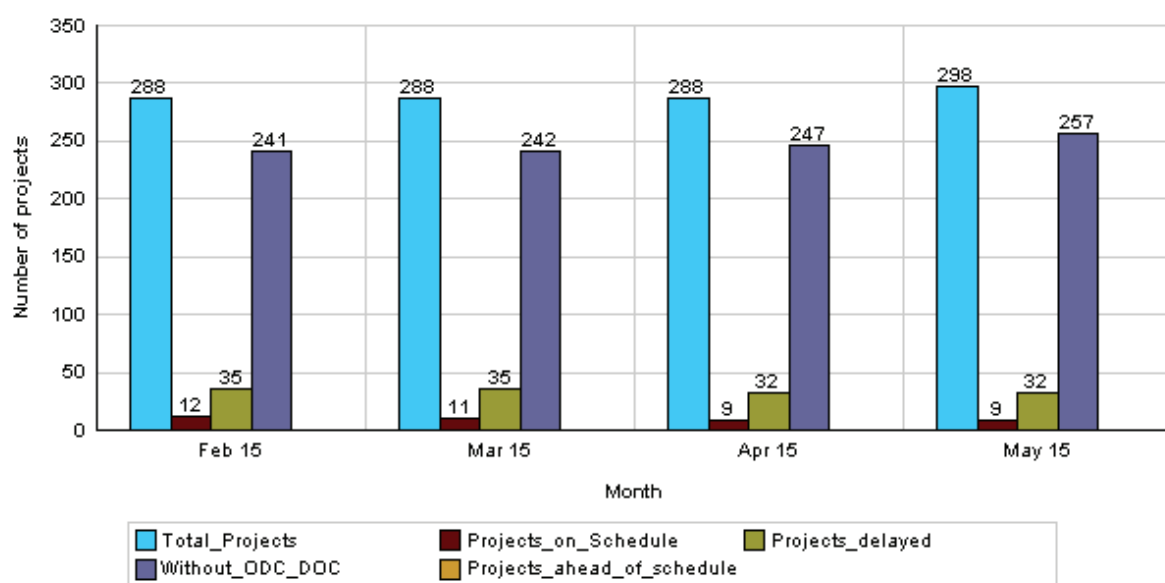


Break-up of 32 Delayed projects in May 2015

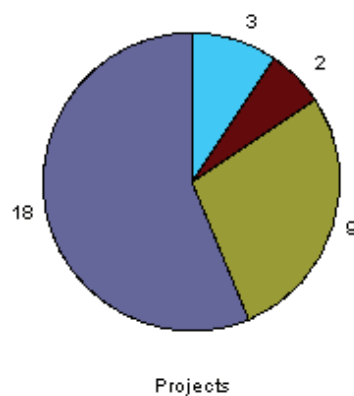


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60


Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

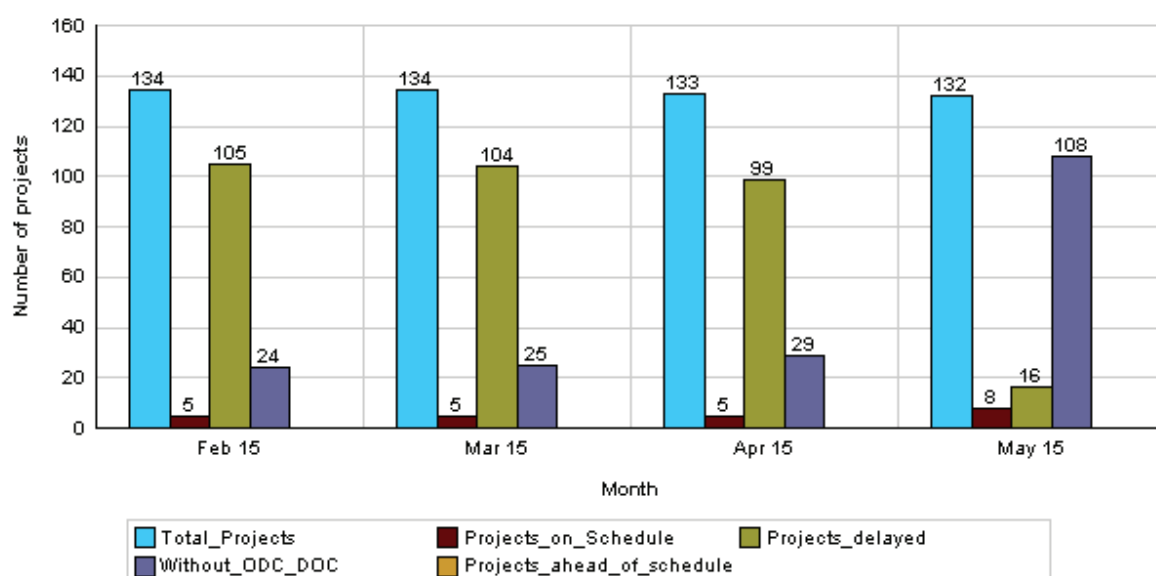


Break-up of 16 Delayed projects in May 2015

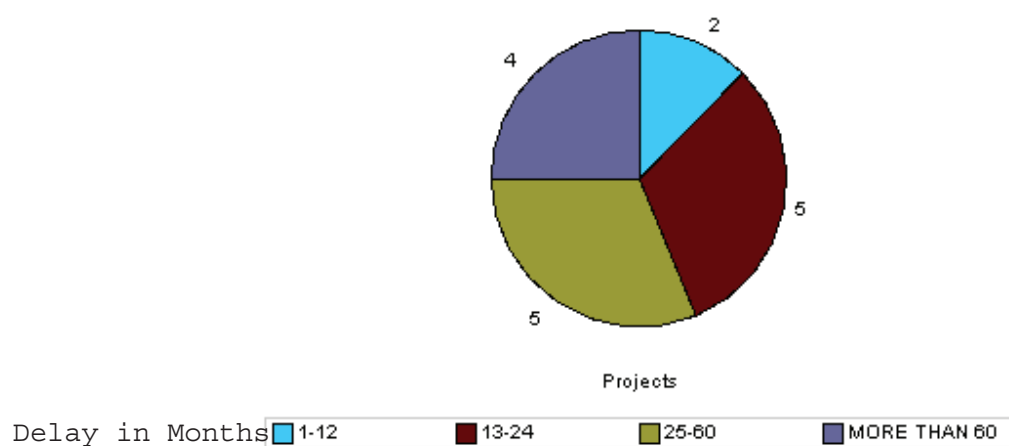


Graphical Presentation of SHIPPING AND PORTS Sector

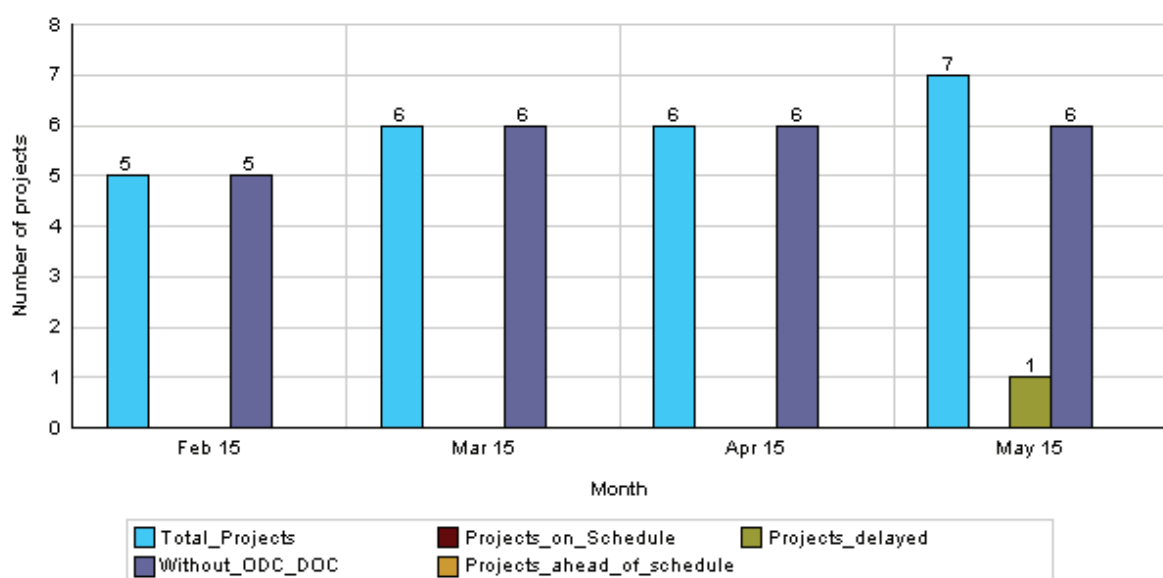


Break-up of 1 Delayed projects in May 2015



Graphical Presentation of STEEL Sector

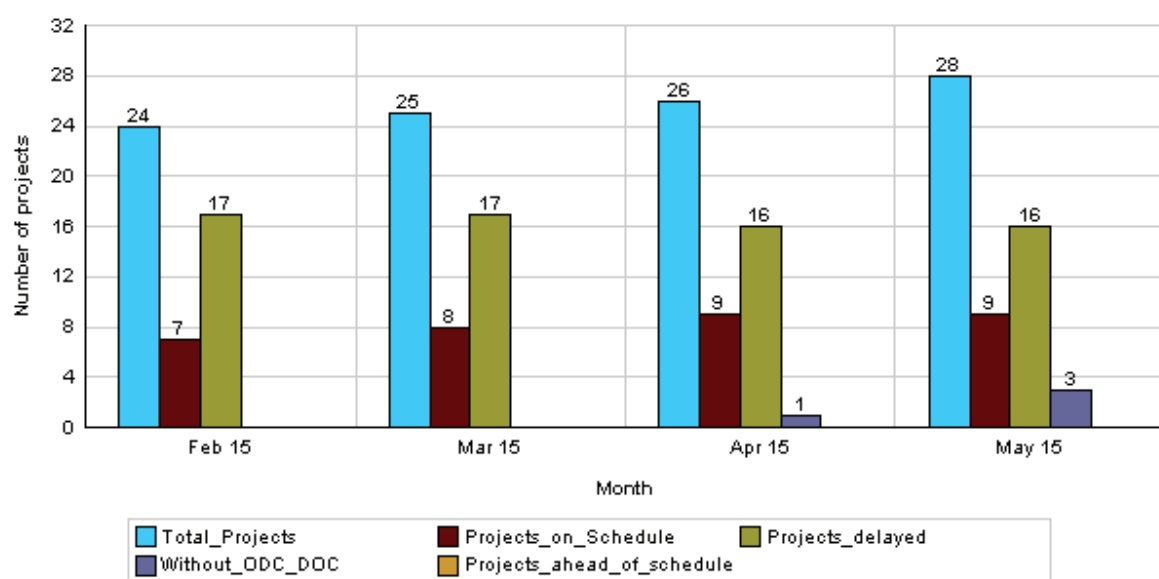


Break-up of 16 Delayed projects in May 2015

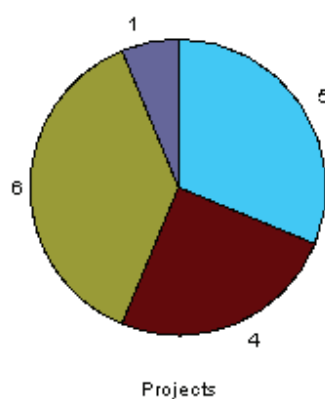


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of TELECOMMUNICATIONS Sector

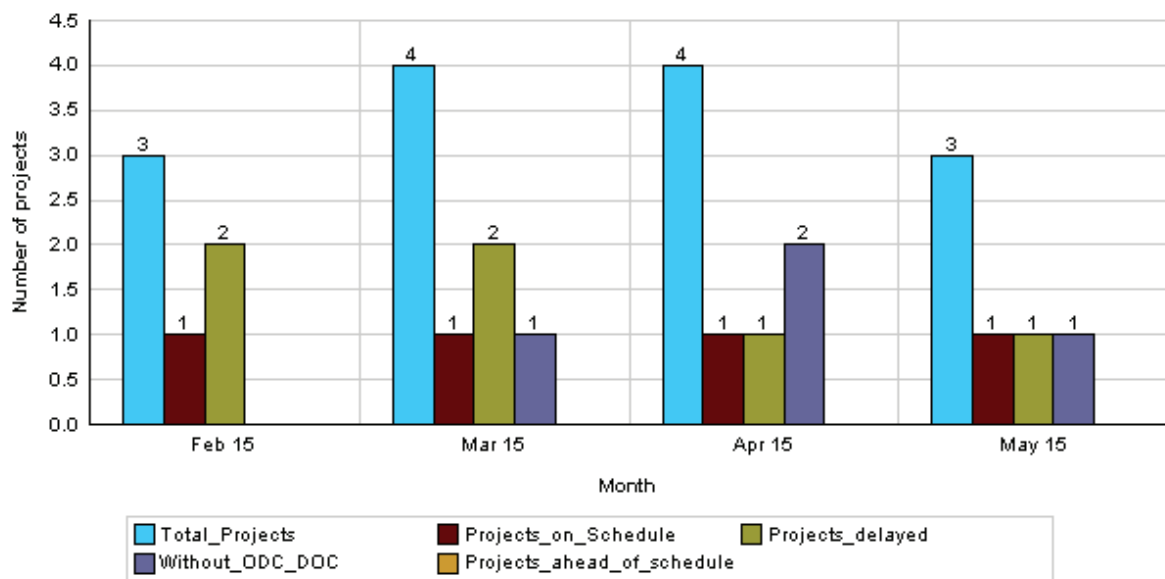


Break-up of 1 Delayed projects in May 2015

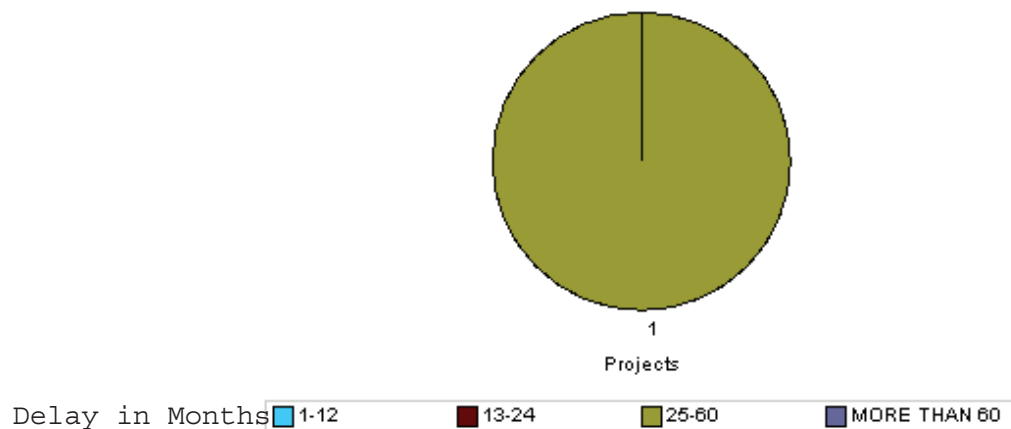

Graphical Presentation of URBAN DEVELOPMENT Sector

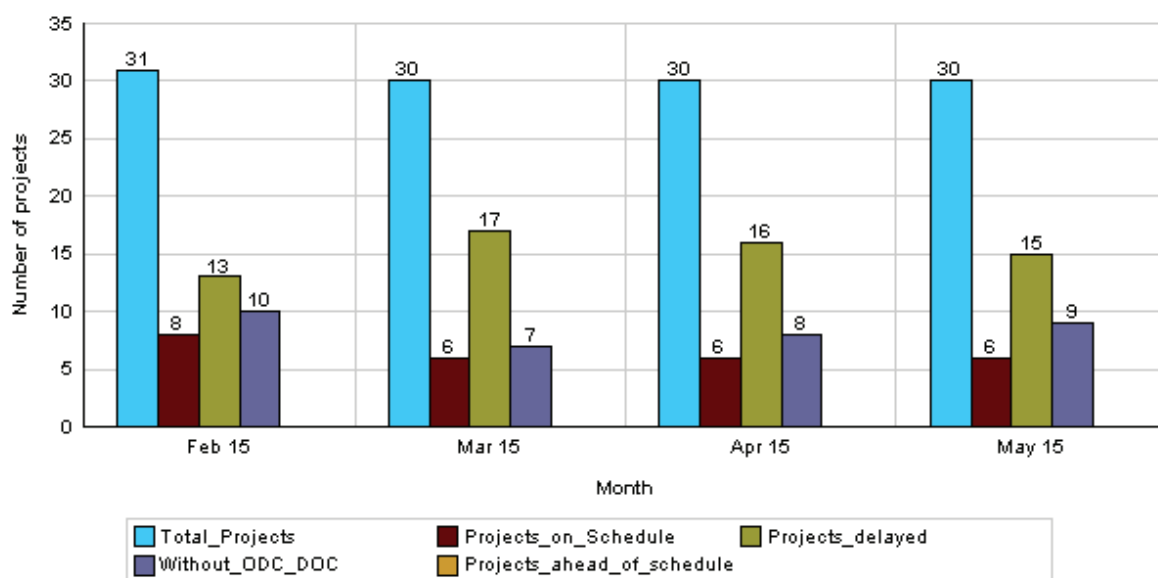

Break-up of 15 Delayed projects in May 2015

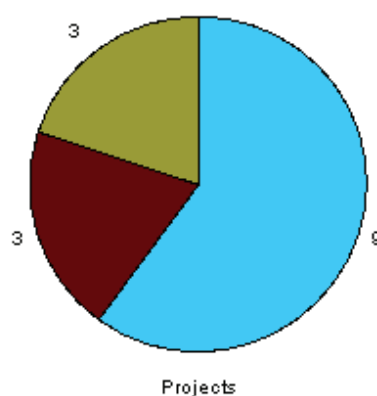

Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	42,627.00	46,726.00	34,774.77
CIVIL AVIATION	7	2,599.56	2,636.56	2,689.48	1,639.70
COAL	76	59,371.42	63,008.27	63,381.37	22,190.77
FERTILISERS	1	197.79	197.79	197.79	13.21
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	28	64,995.71	68,594.71	68,710.11	44,307.17
PETROCHEMICALS	1	5,460.61	8,920.00	9,833.52	8,648.40
PETROLEUM	65	144,046.84	154,813.12	153,341.30	65,243.75
POWER	112	316,428.52	338,788.65	355,392.40	174,461.16
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
RAILWAYS	298	173,660.34	187,075.37	302,322.34	94,357.19
ROAD TRANSPORT AND HIGHWAYS	132	98,429.90	98,543.85	100,253.98	15,546.19
SHIPPING AND PORTS	7	5,524.46	5,827.07	6,428.61	2,667.03
TELECOMMUNICATIONS	3	14,795.00	14,795.00	14,795.00	55.22
URBAN DEVELOPMENT	30	138,680.82	138,680.82	143,894.82	21,775.46
Grand total	766	1,068,206.97	1,128,082.21	1,273,650.02	485,680.02

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00	11,459.00	6,667.00	12/2015	10/2017	22(O)	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00	17,270.00	18,632.00	12/2008	09/2015	81(O)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00	5,677.00	4,967.77	09/2010	-	-	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00	12,320.00	4,508.00	12/2016	05/2018	17(O)	4/69
	Total		40,442.00	46,726.00	34,774.77				60/329
	<u>CIVIL AVIATION</u>								
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46	309.46	341.54	01/2011	06/2017	77(O)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	17.82	-	09/2018	0(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61	388.53	301.94	05/2012	03/2015	-	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00	489.00	433.99	03/2015	05/2015	2(O)	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28	344.28	60.84	03/2014	05/2015	14(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00	626.00	483.53	06/2013	-	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60	217.60	0.04	03/2015	09/2015	6(O)	0/0
	Total		2,599.56	2,689.48	1,639.70				0/0
	<u>COAL</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34	1,228.39	879.58	03/2013	09/2015	30(O)	21/22
13	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97	335.97	29.60	03/2018	03/2018	0(O)	0/0
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59	198.59	111.83	03/2016	03/2016	0(O)	3/7
15	AMLOHRI EPR (NCL) (6 MTY, INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04	1,143.54	799.08	03/2016	03/2016	0(O)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11	858.11	106.77	03/2020	03/2020	0(O)	3/4

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(0) -	0/0
18	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	191.16	03/2012 -	03/2017	60(0) -	4/5
19	ASHOK EXPN OCP CCL (10 MTY) - [060100096]JCL,JHARKHAND	12/2007	471.66 341.63	341.63	121.94	03/2011 -	03/2017	72(0) -	2/5
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	148.02	03/2010 -	03/2017	84(0) -	2/4
21	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	78.34	03/2016 -	03/2016	0(0) -	3/6
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	6.34	03/2019 -	03/2019	0(0) -	1/9
23	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	-	1/6
24	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 -	187.94	32.89	03/2023 -	03/2023	0(0) -	0/21
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	208.16	03/2017 -	03/2017	0(0) -	11/11
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	76.43	03/2020 -	03/2020	0(0) -	0/0
27	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]MCL,MADHYA PRADESH	06/2011	746.04 -	535.10	369.72	03/2015 -	03/2016	12(0) -	0/3
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.63	-	03/2022 -	03/2022	0(0) -	1/7
29	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.60	03/2014 -	03/2016	24(0) -	7/9
30	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND	08/2007	163.51 -	163.51	35.92	03/2011 -	03/2016	60(0) -	0/3
31	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020	0(0) -	0/15
32	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,663.41	03/2014 -	03/2016	24(0) -	10/13
33	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	12.57	03/2021 -	03/2021	0(0) -	1/9
34	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,817.84	03/2014 -	03/2016	24(0) -	11/16
35	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	267.67	148.56	03/2018 -	03/2018	0(0) -	0/18
36	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	77.18	03/2015 -	03/2021	72(0) -	2/13
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	173.03	03/2013 -	03/2017	48(0) -	4/8
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	-	03/2019 -	03/2019	0(0) -	2/6
39	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(0) -	1/7
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(0) -	4/13
41	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
42	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.18	144.92	03/2011 -	03/2017	72(0) -	7/15

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	99.05	12/2012 -	03/2017	51(O) -	11/44
44	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	11.44	07/2016 -	03/2017	8(O) -	6/28
45	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	26.13	03/2021 -	03/2021	0(O) -	0/0
46	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	172.18	03/2013 -	03/2017	48(O) -	8/9
47	KAPURIA UG(PSLV) - [N06000108]BCCL, JHARKHAND	08/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017	0(O) 0(R)	0/0
48	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	65.84	03/2014 -	03/2017	36(O) -	2/4
49	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
50	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]JNCL, UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	79.86	03/2018 -	03/2018	0(O) -	0/4
51	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/5
52	KRISHNASHILA (NCL) (4MTY) - [N06000007]JNCL, UTTAR PRADESH	06/2011	789.88 -	741.62	471.37	03/2013 -	03/2016	36(O) -	0/2
53	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
54	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	143.97	03/2010 -	03/2017	84(O) -	8/10
55	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH	08/2013	7,612.33 7,612.33	7,612.33	764.15	03/2023 03/2023	03/2023	0(O) 0(R)	1/16
56	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	11/2012	289.45 -	289.45	86.62	05/2014 -	04/2016	23(O) -	0/0
57	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	469.78 -	706.40	76.55	07/2012 -	03/2016	44(O) -	1/3
58	MAKARDHOKRA I OC - [N06000119]WCL, MAHARASHTRA	09/2014	266.23 -	266.23	79.31	03/2021 -	03/2021	0(O) -	0/23
59	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	206.52	03/2014 -	03/2018	48(O) -	3/6
60	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48(O) -	4/6
61	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	42.39	04/2015 04/2019	04/2019	48(O) 0(R)	0/0
62	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	10.00	04/2014 03/2016	03/2016	23(O) 0(R)	0/4
63	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	295.56	0.16	03/2019 -	03/2019	0(O) -	0/0
64	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	924.23	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
65	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]JNCL, MADHYA PRADESH	10/2007	259.40 -	259.40	15.49	03/2012 -	03/2016	48(O) -	0/2
66	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL, JHARKHAND	02/2014	555.52 -	555.52	3.52	03/2021 -	03/2021	0(O) -	0/2
67	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	80.29	03/2012 -	03/2017	60(O) -	1/3

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
68	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	30.35	04/2014 -	04/2016	24(O) -	0/0
69	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
70	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA	09/2014	441.82 -	441.82	112.65	03/2020 -	03/2020	0(O) -	0/27
71	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	144.43	03/2013 -	03/2017	48(O) -	2/4
72	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	55.60	03/2014 -	03/2016	24(O) -	3/9
73	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	108.43	03/2021 -	03/2021	0(O) -	0/0
74	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	221.78	03/2016 -	03/2016	0(O) -	2/4
75	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.28	03/2012 -	03/2016	48(O) -	0/2
76	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2019	48(O) -	4/29
77	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 486.27	486.27	69.97	03/2016 -	03/2016	0(O) -	6/39
78	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21(O) -	4/51
79	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	75.50	03/2015 -	04/2016	13(O) -	8/31
80	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	71.33	03/2012 -	03/2018	72(O) -	27/42
81	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026	0(O) -	3/15
82	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	156.45	03/2018 -	03/2018	0(O) -	1/10
83	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.58	03/2016 -	03/2020	48(O) -	2/11
84	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	143.74	03/2012 -	03/2016	48(O) -	2/4
85	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,583.77	3,212.02	06/2009 03/2013	06/2015	72(O) 27(R)	22/23
86	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,223.31	03/2012 05/2014	06/2015	39(O) 13(R)	28/39
87	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	136.88	10/2014 -	06/2015	8(O) -	8/11
	Total		59,371.42 -	63,381.37	22,190.77				288/921
	<u>FERTILISERS</u>								
88	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	197.79	13.21	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	197.79	13.21				0/0
	<u>MINES</u>								

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
89	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N1000007]JCL,MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(O) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0
	<u>STEEL</u>								
90	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	460.80	04/2013 09/2014	06/2015	26(O) 9(R)	17/18
91	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016	0(O) -	1/3
92	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	84.15	07/2016 -	07/2016	0(O) -	1/2
93	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	383.87	05/2013 01/2015	08/2015	27(O) 7(R)	16/20
94	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	255.19	-	03/2018 -	03/2018	0(O) -	0/0
95	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	381.47	09/2009 05/2012	06/2015	69(O) 37(R)	1/1
96	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	389.87	12/2011 01/2015	03/2015	-	20/20
97	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	201.36	07/2015 -	03/2016	8(O) -	0/2
98	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	515.80	09/2013 -	06/2015	21(O) -	0/1
99	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	178.95	08/2014 -	06/2015	10(O) -	3/4
100	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	16.95	04/2015 -	04/2015	-	1/3
101	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	126.73	11/2013 -	06/2015	19(O) -	2/4
102	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,462.86	03/2013 -	03/2016	36(O) -	31/35
103	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,133.16	12/2011 -	08/2015	44(O) -	20/24
104	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,615.92	12/2012 -	06/2015	30(O) -	18/20
105	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,325.64	10/2009 10/2012	04/2015	-	69/70
106	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	154.93	10/2013 -	12/2015	26(O) -	2/5
107	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	130.43	09/2014 -	06/2015	9(O) -	1/2
108	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018	0(O) -	0/0

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017	0(O) -	0/0
110	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(O) -	0/0
111	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,005.70	05/2015 12/2016	12/2016	19(O) 0(R)	16/79
112	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	240.95	06/2015 -	12/2015	6(O) -	2/3
113	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	176.42	12/2014 -	09/2015	9(O) -	1/2
114	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	25.02	10/2016 -	10/2016	0(O) -	0/0
115	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	151.54	07/2015 -	03/2017	20(O) -	0/1
116	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016	0(O) -	0/1
117	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	110.34	04/2016 -	04/2016	0(O) -	2/2
	Total		64,995.71 -	68,710.11	44,307.17				224/322
	<u>PETROCHEMICALS</u>								
118	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,648.40	04/2012 12/2013	06/2015	38(O) 18(R)	21/26
	Total		5,460.61 -	9,833.52	8,648.40				21/26
	<u>PETROLEUM</u>								
119	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39(O) 6(R)	0/1
120	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	59.21	12/2018 -	12/2018	0(O) -	0/9
121	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,777.84	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
122	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,MULTI STATE	08/2011	586.00 -	586.00	306.82	08/2015 -	12/2015	4(O) -	0/12
123	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]OCL,MULTI STATE	01/2015	1,823.00 -	1,823.00	-	- -	-	-	0/0
124	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	419.04	112.81	01/2017 -	01/2017	0(O) -	0/0
125	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015	51(O) 0(R)	0/0
126	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 07/2015	07/2015	23(O) 0(R)	0/0
127	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	114.88	09/2012 04/2015	12/2015	39(O) 8(R)	0/5

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 11/2017	06/2018	53(O) 7(R)	0/2
129	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 958.55	958.55	843.52	05/2013 06/2014	12/2015	31(O) 18(R)	1/5
130	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	-	05/2019 -	05/2019	0(O) -	0/0
131	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,220.38	08/2015 -	12/2015	4(O) -	0/12
132	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 04/2016	06/2015	110(O) -10(R)	1/5
133	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	539.15	05/2014 05/2016	05/2016	24(O) 0(R)	0/21
134	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
135	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
136	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,338.05	01/2014 12/2015	12/2015	23(O) 0(R)	0/13
137	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	-	10/2014 10/2015	10/2015	12(O) 0(R)	0/0
138	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	95.53	09/2017 -	09/2017	0(O) -	0/0
139	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	6.51	- -	-	-	0/0
140	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,720.30	05/2015 05/2015	07/2015	2(O) 2(R)	0/17
141	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	352.49	122.87	03/2014 -	05/2016	26(O) -	0/0
142	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	18.74	07/2016 -	07/2016	0(O) -	2/6
143	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,201.17	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
144	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2017	12(O) 12(R)	0/6
145	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 -	16,504.00	6,536.23	05/2016 -	05/2016	0(O) -	0/30
146	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	122.87	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
147	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	3,957.00	4.99	01/2013 -	12/2018	71(O) -	0/0
148	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	890.00	0.05	- -	-	-	0/0
149	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,343.65	12/2012 -	06/2015	30(O) -	0/14
150	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 607.06	607.06	57.83	01/2016 07/2017	07/2017	18(O) 0(R)	11/48

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	461.00	11/2015 11/2016	11/2016	12(O) 0(R)	24/29
152	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	184.18	07/2013 -	07/2015	24(O) -	0/1
153	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 219.08	219.08	137.25	09/2016 -	12/2015	-9(O) -	0/12
154	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	1,118.78	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
155	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	155.32	12/2014 -	07/2015	7(O) -	57/58
156	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	6,068.80	-	04/2019 -	04/2019	0(O) -	0/0
157	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	5.37	11/2016 -	11/2016	0(O) -	0/0
158	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
159	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	403.07	08/2015 -	06/2016	10(O) -	0/0
160	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	2,321.00	0.82	- -	-	-	0/0
161	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	07/2018	0(O) -	0/31
162	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,101.07	11/2012 11/2013	10/2015	35(O) 23(R)	87/100
163	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,123.79	09/2012 -	03/2016	42(O) -	6/7
164	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	57.16	07/2016 -	07/2016	0(O) -	5/12
165	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	98.95	09/2017 -	09/2017	0(O) -	0/0
166	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41(O) 0(R)	0/0
167	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	432.97	04/2015 04/2015	12/2015	8(O) 8(R)	0/0
168	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,151.94	12/2014 -	06/2015	6(O) -	0/20
169	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	33.61	02/2016 -	02/2016	0(O) -	2/6
170	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	625.93	11/2015 07/2016	07/2016	8(O) 0(R)	37/52
171	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	85.27	05/2015 -	12/2015	7(O) -	0/12
172	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016	0(O) 0(R)	0/0
173	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	1,049.32	11/2015 -	11/2015	0(O) -	18/25
174	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	951.70	10/2011 -	10/2015	48(O) -	0/0
176	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45(O) -	0/0
177	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,078.77	10/2011 -	06/2015	44(O) -	0/0
178	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.44	04/2015 -	-	-	0/0
179	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	123.67	12/2016 -	12/2016	0(O) -	0/0
180	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	225.72	08/2012 06/2015	06/2015	34(O) 0(R)	0/1
181	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	220.47	03/2015 11/2015	02/2016	11(O) 3(R)	0/5
182	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	222.98	10/2014 10/2016	10/2016	24(O) 0(R)	23/40
183	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	279.14	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
	Total		144,046.84 -	153,341.30	65,243.75				298/701
	POWER								
184	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	311.69	12/2014 -	05/2015	5(O) -	9/17
185	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	1.00	05/2016 -	05/2016	0(O) -	0/0
186	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,664.00	10/2013 -	03/2015	-	20/20
187	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,850.00	12/2009 10/2014	03/2018	99(O) 41(R)	26/46
188	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,243.00	09/2011 -	03/2017	66(O) -	12/36
189	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,678.00	05/2014 -	06/2017	37(O) -	0/0
190	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	680.95	12/2015 -	03/2016	3(O) -	9/19
191	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,804.46	09/2014 -	06/2016	21(O) -	12/19
192	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	718.73	06/2015 -	12/2015	6(O) -	1/7

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
193	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
194	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	121.50	06/2015 -	12/2015	6(O) -	5/7
195	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017	0(O) -	0/0
196	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	780.33	-	07/2017 -	07/2017	0(O) -	0/0
197	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	1,539.00	08/2018 -	08/2018	0(O) -	13/14
198	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	25.99	02/2014 -	09/2017	43(O) -	1/1
199	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	1.40	02/2016 -	02/2016	0(O) -	5/7
200	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,082.63	11/2012 -	12/2016	49(O) -	4/12
201	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	217.44	04/2016 -	04/2016	0(O) -	11/20
202	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	5.20	11/2016 -	11/2016	0(O) -	0/0
203	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	73.73	09/2014 -	06/2016	21(O) -	0/0
204	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	-	04/2018 -	04/2018	0(O) -	0/0
205	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,704.45	05/2014 -	03/2016	22(O) -	8/11
206	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	595.00	12/2016 -	12/2016	0(O) -	12/15
207	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	3,246.00	09/2017 -	09/2017	0(O) -	16/41
208	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	-	05/2017 -	05/2017	0(O) -	0/0
209	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	-	05/2018 -	05/2018	0(O) -	0/0
210	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	2.30	07/2016 -	07/2016	0(O) -	0/0
211	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017	0(O) -	0/0
212	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	444.97	10/2016 -	12/2015	-10(O) -	8/17

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
213	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	25.70	04/2018 -	04/2018	0(O) -	0/0
214	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	992.61	12/2007 12/2009	12/2015	96(O) 72(R)	5/10
215	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,899.87	12/2009 03/2017	03/2017	87(O) 0(R)	13/29
216	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,871.00	01/2013 -	03/2016	38(O) -	0/0
217	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,952.20	01/2016 -	11/2016	10(O) -	4/9
218	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,622.00	04/2009 -	06/2015	74(O) -	10/10
219	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	8,289.00	01/2017 -	01/2017	0(O) -	24/29
220	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,891.95	09/2008 03/2012	03/2016	90(O) 48(R)	19/23
221	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	4,174.00	06/2017 -	06/2017	0(O) -	18/39
222	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	144.00	08/2017 -	08/2017	0(O) -	0/9
223	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,086.00	09/2016 -	09/2016	0(O) -	21/27
224	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,400.00	12/2016 -	09/2017	9(O) -	0/1
225	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	2,086.00	02/2019 -	02/2019	0(O) -	4/4
226	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,590.30	08/2013 -	03/2016	31(O) -	6/17
227	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	30.70	06/2016 -	06/2016	0(O) -	10/20
228	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	482.22	07/2013 05/2015	11/2015	28(O) 6(R)	4/10
229	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	326.77	02/2012 -	03/2016	49(O) -	7/13
230	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	463.66	11/2011 -	03/2016	52(O) -	7/13
231	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	26.00	06/2016 -	06/2016	0(O) -	9/20
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,274.62	04/2013 -	03/2016	35(O) -	4/11
233	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	509.32	11/2014 -	12/2015	13(O) -	11/16
234	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	230.79	03/2016 -	03/2016	0(O) -	8/17
235	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	184.52	04/2015 -	09/2015	5(O) -	11/18
236	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	729.24	11/2012 -	03/2016	40(O) -	4/11

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
237	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60	12,964.60	3,569.00	01/2018	01/2018	0(O)	0/0
238	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC, JAMMU AND KASHMIR	10/2014	8,112.12	8,112.12	-	04/2020	04/2020	0(O)	0/0
239	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59	7,531.72	5,079.93	09/2009	12/2018	111(O)	7/14
240	PARE HYDRO ELECTRIC PROJECT - [N18000045]NPEPCO, ARUNACHAL PRADESH	12/2008	573.99	1,487.49	1,025.79	08/2013	03/2016	31(O)	28/38
241	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84	1,381.84	110.00	09/2019	09/2019	0(O)	3/3
242	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18	9,395.18	4,843.00	11/2016	08/2017	9(O)	20/23
243	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL, MULTI STATE	05/2014	829.98	829.98	2.00	08/2016	08/2016	0(O)	0/0
244	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL, KARNATAKA	02/2014	167.40	167.40	49.90	12/2015	12/2015	0(O)	6/7
245	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL, MULTI STATE	11/2014	972.42	972.42	-	11/2017	11/2017	0(O)	0/0
246	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33	15,300.00	7,705.13	09/2010	-	-	0/0
247	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL, ANDHRA PRADESH	03/2015	550.06	550.06	1.60	03/2018	03/2018	0(O)	0/0
248	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL, MULTI STATE	09/2012	1,508.74	1,508.74	750.88	03/2015	09/2015	6(O)	10/19
249	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL, MULTI STATE	08/2014	288.49	288.49	12.40	02/2017	02/2017	0(O)	0/0
250	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL, MULTI STATE	02/2010	232.34	232.34	197.19	06/2012	-	-	2/3
251	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL, MADHYA PRADESH	03/2012	213.78	213.78	196.14	03/2014	06/2015	15(O)	7/7
252	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL, CHHATTISGARH	12/2011	1,746.65	2,228.70	1,155.03	08/2014	03/2016	19(O)	10/17
253	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL, MULTI STATE	12/2009	1,216.83	1,216.83	1,051.79	08/2012	03/2016	43(O)	3/6
254	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL, MULTI STATE	02/2014	243.53	243.53	63.10	08/2016	08/2016	0(O)	10/20
255	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE	01/2015	203.28	203.28	0.20	07/2017	07/2017	0(O)	0/0
256	SYSTEM STRENGTHENING - XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL, MULTI STATE	06/2012	1,263.26	1,263.26	1,067.98	11/2014	09/2015	10(O)	8/15
257	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85	1,422.85	1,105.42	01/2015	03/2016	14(O)	12/20
258	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33	346.79	276.57	08/2014	12/2015	16(O)	13/19

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
259	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	360.52	06/2014 -	03/2016	21(O) -	17/19
260	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	709.00	03/2019 -	03/2019	0(O) -	5/7
261	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,460.00	03/2013 -	12/2018	69(O) -	1/15
262	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,762.59	09/2009 -	06/2016	81(O) -	2/6
263	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,235.17	07/2010 02/2016	05/2018	94(O) 27(R)	5/21
264	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,873.86	08/2014 -	09/2015	13(O) -	12/19
265	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,331.11	10/2014 -	03/2016	17(O) -	8/17
266	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,078.18	10/2012 -	03/2016	41(O) -	3/11
267	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	1.50	04/2017 -	04/2017	0(O) -	0/0
268	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,128.20	12/2012 -	03/2016	39(O) -	4/11
269	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	1.00	02/2017 -	02/2017	0(O) -	0/0
270	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	467.80	03/2018 -	03/2018	0(O) -	0/20
271	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,439.25	01/2015 -	03/2016	14(O) -	10/21
272	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	64.70	10/2016 -	10/2016	0(O) -	16/20
273	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	268.80	0.80	03/2018 -	03/2018	0(O) -	0/0
274	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,503.07	10/2014 -	09/2015	11(O) -	9/15
275	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	291.80	05/2016 -	05/2016	0(O) -	10/18
276	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	1.90	11/2017 -	11/2017	0(O) -	0/0
277	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	508.90	02/2014 -	09/2015	19(O) -	14/16
278	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,316.76	12/2013 04/2015	06/2015	18(O) 2(R)	9/12

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
279	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	445.41	11/2013 -	12/2015	25(O) -	12/20
280	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,834.94	03/2013 06/2015	09/2015	30(O) 3(R)	8/14
281	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,796.47	03/2014 06/2015	08/2015	17(O) 2(R)	12/14
282	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,718.80	12/2013 -	09/2015	21(O) -	9/12
283	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	127.70	01/2013 -	09/2015	32(O) -	12/21
284	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,467.86	11/2013 -	12/2015	25(O) -	12/15
285	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	312.94	-	06/2016 -	06/2016	0(O) -	0/0
286	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,703.27	11/2012 -	07/2015	32(O) -	4/10
287	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,182.93	07/2014 -	03/2016	20(O) -	8/13
288	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	912.03	07/2013 -	08/2015	25(O) -	25/26
289	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	822.11	07/2006 12/2015	10/2016	123(O) 10(R)	5/13
290	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
291	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	05/2012	3,180.40 -	3,180.40	1,816.00	08/2015 -	08/2015	0(O) -	22/24
292	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	641.42	07/2014 11/2018	11/2018	52(O) 0(R)	2/8
293	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	15.20	05/2018 -	05/2018	0(O) -	0/0
294	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	520.09	09/2010 06/2013	03/2016	66(O) 33(R)	2/7
295	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	4,319.89	06/2015 -	03/2016	9(O) -	15/28
	Total		316,428.52 -	355,392.40	174,461.16				794/1369
	HEAVY INDUSTRY								
296	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		1,718.00 -	3,827.30 -	.00				0/0
	<u>RAILWAYS</u>								
297	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	44.04	03/2016 -	03/2016	0(O) -	0/0
298	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
299	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
300	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
301	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66(O) 51(R)	0/0
302	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
303	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
304	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
305	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	873.71	-	- -	-	-	0/0
306	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	218.39	23.63	- -	-	-	0/0
307	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
308	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR, MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
309	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
310	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	242.09	0.02	- -	-	-	0/0
311	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR, MULTI STATE	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
312	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	- -	0/0
313	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
314	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
315	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
316	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
317	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
318	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
319	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00	960.00	-	-	-	-	0/0
320	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87	528.00	2.96	-	-	-	0/0
321	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75	199.75	76.08	-	-	-	0/0
322	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93	986.30	42.62	-	-	-	0/0
323	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	288.35	9.60	-	-	-	0/0
324	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33(O)	0/0
325	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00	1,382.78	0.72	-	-	-	0/0
326	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08	246.08	4.13	-	-	-	0/0
327	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
328	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62	1,106.62	244.99	12/2010	-	-	0/0
329	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	450.55	13.53	-	-	-	0/0
330	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	255.64	-	-	-	-	0/0
331	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	436.79	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
332	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49	337.50	0.21	-	-	-	0/0
333	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23	923.23	1.01	-	-	-	0/0
334	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67	837.33	1.15	-	-	-	0/0
335	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64	760.00	0.09	-	-	-	0/0
336	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
337	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88	2,966.99	40.80	-	-	-	0/0
338	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011	-	-	0/0
339	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64	195.64	94.11	-	-	-	0/0
340	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20	800.00	793.71	03/2010	12/2015	69(O)	0/0
341	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24	321.62	2.91	03/2012	-	-	0/0
342	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20	326.20	1.68	-	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
343	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.46	-	-	-	0/0
344	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	434.00	35.90	-	-	-	0/0
345	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
346	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	-	02/2012	-	0/0
347	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015	12/2016	21(O) -	0/0
348	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.30	-	-	-	0/0
349	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	61.36	-	-	-	0/0
350	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	619.87	-	03/2015	-	0/0
351	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	112.40	-	-	-	0/0
352	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	520.00	462.69	-	-	-	0/0
353	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.07	-	-	-	0/0
354	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.22	-	-	-	0/0
355	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	111.71	-	-	-	0/0
356	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	-	03/2017	-	0/0
357	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	30.05	-	-	-	0/0
358	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	-	-	-	0/0
359	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	-	-	-	0/0
360	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	-	-	-	0/0
361	CHOTTADEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	-	-	-	0/0
362	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
363	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007	03/2016	108(O) -	0/0
364	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	-	-	-	0/0
365	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	-	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
366	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
367	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
368	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
369	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
370	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
371	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	339.00	200.72	- -	-	-	0/0
372	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
373	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
374	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	410.08	296.12	- -	-	-	0/0
375	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	-	0/0
376	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
377	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91 -	336.91	144.05	- -	-	-	0/0
378	DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
379	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
380	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
381	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
382	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
383	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
384	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016	0(O) -	0/0
385	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
386	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
387	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
388	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82(O) -	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
389	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	495.74	311.52	06/2013 06/2013	06/2013	-	0/0
390	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
391	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	1,117.00 -	1,922.00	0.59	- -	-	-	0/0
392	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
393	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	415.67	13.99	- -	-	-	0/0
394	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
395	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
396	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
397	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]SER, JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	03/2016	121(O) -	0/0
398	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23 -	1,072.51	888.87	- -	06/2015	- -	0/0
399	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
400	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
401	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
402	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
403	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
404	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	179.32	35.18	- -	-	-	0/0
405	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
406	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER, MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
407	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	720.00 -	720.00	-	- -	-	-	0/0
408	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	367.17	13.02	- -	-	-	0/0
409	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	324.66	223.72	- -	-	-	0/0
410	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
411	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
412	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	266.35	- 09/2009	-	-	0/0
413	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
414	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	872.28	- -	- -	- -	0/0
415	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	- -	- -	- -	0/0
416	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	93.44	03/2015 -	03/2015	- -	0/0
417	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	- -	- -	0/0
418	HOSADURGA - CHICKKAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	29.81	- -	07/2015	- -	0/0
419	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	325.00	- -	- -	- -	0/0
420	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	1,618.00	-	- -	- -	- -	0/0
421	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	- -	- -	0/0
422	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	- -	0/0
423	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	- -	- -	0/0
424	HUBLI- CHIKKAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	1,900.00	-	- -	- -	- -	0/0
425	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	31.46	- -	- -	- -	0/0
426	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	- -	- -	0/0
427	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	255.52	03/2014 -	- -	- -	0/0
428	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	- -	- -	- -	0/0
429	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	- -	- -	0/0
430	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	815.43	03/2012 -	- -	- -	0/0
431	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	40.00	- -	- -	- -	0/0
432	JHARSUGUDA-RENGALI DOUBLING - [N22000317]JECOR,ODISHA	03/2006	201.00 -	230.00	218.67	- -	- -	- -	0/0
433	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	- -	0/0
434	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
435	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	- -	- -	- -	0/0
436	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	- -	- -	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
437	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
438	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
439	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2015	-	0/0
440	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
441	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	1/1
442	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.66	- -	-	-	0/0
443	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
444	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
445	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
446	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	7.96	- -	-	-	0/0
447	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	541.00	150.50	- -	-	-	0/0
448	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	277.33	03/2009 03/2009	08/2014	-	0/0
449	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
450	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
451	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
452	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	682.75	- 03/2010	03/2010	-	0/0
453	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,950.85	07/2005 -	-	-	0/0
454	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	255.38	- -	-	-	0/0
455	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
456	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	322.72	03/2012 -	-	-	0/0
457	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
458	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
459	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
460	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
461	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
462	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
463	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
464	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
465	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
466	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
467	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
468	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
469	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
470	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
471	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
472	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
473	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
474	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	108.93	- -	-	-	0/0
475	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	497.57	03/2012 -	-	-	0/0
476	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
477	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	0.17	01/1999 -	-	-	0/0
478	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.82	- -	-	-	0/0
479	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0
480	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
481	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	1,830.00	-	- -	-	-	0/0
482	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
483	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
484	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
485	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	-	-	-	0/0
486	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
487	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	-	-	-	0/0
488	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,431.72	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
489	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	-	03/2015	-	0/0
490	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	373.31	-	-	-	0/0
491	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	-	03/2018	-	0/0
492	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	-	-	-	0/0
493	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
494	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	-	-	-	0/0
495	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
496	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
497	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	-	-	-	0/0
498	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	-	-	-	0/0
499	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	-	03/2019	-	0/0
500	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	-	03/2017	-	0/0
501	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	-	03/2018	-	0/0
502	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	-	03/2020	-	0/0
503	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	-	03/2017	-	0/0
504	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.29	-	03/2019	-	0/0
505	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-JTAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	-	03/2019	-	0/0
506	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	-	03/2019	-	0/0

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
507	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
508	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0
509	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0
510	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
511	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
512	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.37	03/2014 -	03/2016	24(O) -	0/0
513	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.51	551.84	03/2016 -	03/2016	0(O) -	0/0
514	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	201.88	03/2016 -	06/2016	3(O) -	0/0
515	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	663.95	03/2016 -	03/2016	0(O) -	0/0
516	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	424.42	03/2008 06/2008	-	-	0/0
517	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
518	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
519	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	- -	01/2015	-	0/0
520	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,491.45	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
521	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	- -	02/2014	-	0/0
522	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
523	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	600.00	-	- -	-	-	0/0
524	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
525	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
526	PLASSEY-JAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
527	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
528	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00	323.00	-	-	-	-	0/0
529	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	205.22	1.54	-	-	-	0/0
530	QUILON-TIRUNELVELI- TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94	1,030.00	800.90	01/1999	-	-	0/0
531	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00	1,122.00	889.95	-	-	-	0/6
532	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62	289.93	277.09	12/2007	-	-	0/0
533	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00	2,363.00	1,667.30	03/2009	12/2014	-	0/0
534	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16	288.00	305.47	02/2009	08/2014	-	0/0
535	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77	209.00	2.64	12/2016	12/2016	0(O)	0/0
536	RAJKOT-VERAVAL, WANS,JALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]JWR,GUJARAT	04/1994	320.66	913.48	457.67	-	-	-	0/0
537	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00	874.57	606.08	03/2013	09/2015	30(O)	0/0
538	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92	1,225.90	257.59	-	03/2017	-	0/0
539	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07	335.00	230.67	06/2004	12/2015	138(O)	0/0
540	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]JNFR,ASSAM	01/2004	915.70	3,700.00	3,198.30	-	03/2015	-	0/0
541	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97	288.97	0.82	-	-	-	0/0
542	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65	872.22	793.42	-	-	-	0/0
543	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75	3,500.00	52.11	-	-	-	0/0
544	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04	1,421.25	420.33	03/2012	-	-	0/0
545	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34	1,743.00	293.38	-	-	-	0/0
546	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00	400.00	-	-	-	-	0/0
547	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00	576.18	3.40	-	-	-	0/0
548	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10	714.10	65.20	04/2016	03/2017	11(O)	0/0
549	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44	193.44	53.01	-	-	-	0/0
550	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69	325.00	255.17	-	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
551	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	288.69	- -	-	-	0/0
552	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	230.21	03/2010 -	-	-	0/0
553	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	380.00	-	- -	-	-	0/0
554	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
555	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
556	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
557	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,190.00	88.56	12/2015 -	03/2020	51(O)	0/0
558	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.58	- -	-	-	0/0
559	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
560	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
561	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
562	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	-	-	0/0
563	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
564	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	113.50	02/2015 -	-	-	0/0
565	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0
566	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	588.49	03/2014 -	-	-	0/0
567	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
568	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	1,428.00	466.36	06/2005 -	12/2019	174(O)	0/0
569	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
570	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
571	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- -	-	-	0/0
572	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	- -	-	-	0/0
573	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	0.41	- -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
574	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	-	-	-	0/0
575	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	-	-	-	0/0
576	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012	-	-	0/0
577	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	-	-	-	0/0
578	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,544.45	12/2006	-	-	0/0
579	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.07	-	-	-	0/0
580	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	0.76	-	-	-	0/0
581	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002	12/2018	193(O)	0/0
582	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014	-	-	0/0
583	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	-	-	-	0/0
584	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
585	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	-	-	-	0/0
586	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	-	-	-	0/0
587	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
588	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	-	-	-	0/0
589	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	-	-	-	0/0
590	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	-	-	-	0/0
591	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	-	-	-	0/0
592	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.32	-	-	-	0/0
593	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	-	-	-	0/0
594	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	-	-	-	-	0/0
	Total		173,660.34 -	302,322.34	94,357.19				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
595	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	-	08/2013	-	-	0/0

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
596	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014 -	-	-	0/0
597	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	-	07/2014 -	-	-	0/0
598	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	-	-	0/0
599	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	-	-	0/0
600	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,UTTAR PRADESH	04/2012	624.00 -	624.00	333.72	04/2014 -	07/2015	15(O) -	0/0
601	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	-	07/2014 -	-	-	0/0
602	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	-	01/2014 -	-	-	0/0
603	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
604	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20(O) -	0/0
605	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0
606	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014	-	0/0
607	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	-	-	0/3
608	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	-	-	0/0
609	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	-	06/2013 -	-	-	0/3
610	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	38.30	09/2013 -	-	-	0/0
611	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	-	08/2013 -	-	-	0/3
612	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
613	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19(O) -	0/0
614	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	-	08/2013 -	-	-	0/0
615	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	-	08/2013 -	-	-	0/0
616	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	-	08/2013 -	-	-	0/0
617	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	-	10/2015 -	10/2015	0(O) -	0/0
618	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	-	-	0/0
619	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	-	09/2014 -	-	-	0/0
620	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.19	269.40	09/2007 -	09/2017	120(O) -	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
621	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	-	12/2015 -	12/2015	0(O) -	0/3
622	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
623	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	-	09/2013 -	-	-	0/0
624	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	-	02/2015 -	-	-	0/0
625	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	-	06/2014 -	-	-	0/0
626	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	-	-	-	-	2/2
627	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35(O) -	0/0
628	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	-	-	0/0
629	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	-	06/2008 -	-	-	0/0
630	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	-	06/2008 -	-	-	0/0
631	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	-	-	0/0
632	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
633	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
634	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	-	03/2013 -	-	-	0/0
635	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	-	10/2011 -	-	-	0/0
636	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	-	10/2011 -	-	-	0/0
637	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	-	05/2013 -	-	-	0/0
638	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
639	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	-	04/2015 -	04/2015	-	0/0
640	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	-	05/2010 -	-	-	0/0
641	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	-	07/2013 -	-	-	0/0
642	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	-	06/2013 -	-	-	0/0
643	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	-	-	-	-	1/1
644	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	83(O) -	0/0
645	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 06/2015	06/2015	85(O) 0(R)	0/0

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
646	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	-	09/2010 -	-	-	0/0
647	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015	0(0) -	0/0
648	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	-	09/2008 -	-	-	0/0
649	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016	0(0) -	0/0
650	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	-	08/2015 -	08/2015	0(0) -	0/0
651	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	-	10/2013 -	-	-	0/0
652	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	-	09/2008 -	-	-	0/0
653	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	-	08/2013 -	-	-	0/0
654	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	-	09/2012 -	-	-	2/3
655	GUWHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	03/2015	-	0/0
656	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	-	04/2008 04/2015	04/2015	-	0/0
657	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
658	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	-	-	0/0
659	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	-	-	0/0
660	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	-	-	0/0
661	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	-	10/2013 -	-	-	0/0
662	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	28(0) -	0/0
663	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
664	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	-	-	0/0
665	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	-	04/2013 -	-	-	0/0
666	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	-	02/2013 -	-	-	0/0
667	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	-	12/2012 -	-	-	0/0
668	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29(0) -	0/0
669	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
670	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
671	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	-	05/2012 -	-	-	0/0
672	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	-	10/2008 -	-	-	0/0
673	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	-	07/2014 -	-	-	0/0
674	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	-	06/2015 -	-	2/3
675	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	-	07/2012 -	-	-	0/0
676	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	-	-	0/0
677	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	-	-	0/0
678	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	-	-	0/0
679	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	-	-	0/0
680	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	-	06/2013 -	-	-	0/0
681	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	-	03/2013 -	-	-	0/0
682	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	-	-	0/0
683	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17(O)	0/0
684	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	-	04/2008 04/2015	04/2015	-	0/0
685	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 04/2015	04/2015	-	0/0
686	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
687	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11(O)	0/0
688	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	-	09/2013 -	-	-	0/0
689	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	-	02/2010 -	-	-	0/0
690	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	-	01/2014 -	-	-	0/0
691	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	-	-	0/0
692	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	-	-	0/0
693	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	-	0/0
694	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	-	06/2014 -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
695	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	-	03/2014 -	-	-	0/0
696	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	-	-	0/0
697	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	-	07/2012 -	-	-	0/0
698	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	-	03/2013 -	-	-	0/0
699	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	-	01/2014 -	-	-	0/0
700	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11(O) -	0/0
701	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	326.30	10/2008 -	01/2015	-	0/0
702	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	-	06/2015 -	06/2015	0(O) -	0/0
703	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	-	09/2014 -	-	-	0/0
704	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	-	11/2013 -	-	-	0/0
705	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	-	03/2013 -	-	-	0/0
706	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	-	05/2014 -	-	-	0/0
707	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 - 157.47	154.57	228.30	09/2007 03/2014	03/2015	-	0/0
708	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
709	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	-	06/2014 -	-	-	0/0
710	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	-	12/2013 -	-	-	0/0
711	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	-	12/2013 -	-	-	0/0
712	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	-	05/2014 -	-	-	0/0
713	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43(O) -	0/0
714	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	-	03/2008 03/2015	03/2015	-	0/0
715	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18(O) -	0/0
716	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2015	52(O) -	2/2
717	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	-	11/2013 -	-	-	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
718	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	-	-	0/0
719	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	-	05/2013 -	-	-	0/0
720	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	188.40	-	07/2014	-	2/2
721	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	-	-	0/0
722	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
723	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	-	11/2012 -	-	-	0/0
724	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
725	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	02/2014 -	-	-	0/0
726	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		98,429.90 -	100,253.98	15,546.19				14/28
	<u>SHIPPING AND PORTS</u>								
727	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	1,460.00	937.28	12/2010 -	-	-	0/0
728	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.00	669.46	407.33	12/2010 -	01/2016	61(O) -	0/0
729	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
730	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	-	-	0/0
731	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	373.22	351.18	04/2009 -	-	-	0/0
732	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 -	-	-	0/0
733	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	-	-	0/0
	Total		5,524.46 -	6,428.61	2,667.03				0/0
	<u>TELECOMMUNICATIONS</u>								
734	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	55.22	10/2010 08/2015	09/2015	59(O) 1(R)	0/0

Sector Wise Details									
(May 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
735	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL,MULTI STATE	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
736	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015	0(O) -	0/0
	Total		14,795.00 -	14,795.00	55.22				0/0
	<u>URBAN DEVELOPMENT</u>								
737	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
738	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36(O) -	0/0
739	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	-	-	3/3
740	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
741	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	-	08/2007 -	03/2015	-	0/0
742	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	-	10/2012 -	09/2013	-	0/0
743	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	-	06/2015 -	08/2015	2(O) -	0/0
744	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,749.25	12/2015 -	08/2016	8(O) -	1/24
745	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34(O) -	0/0
746	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	-	12/2014 -	12/2016	24(O) -	0/0
747	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30(O) -	0/0
748	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
749	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
750	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15(O) -	0/0
751	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	-	03/2017 -	03/2017	0(O) -	0/0
752	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9(O) -	0/0

Sector Wise Details									
(May 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
753	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	-	03/2010 -	10/2014	-	0/0
754	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11(O) -	0/0
755	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
756	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	639.78	09/2014 -	05/2015	8(O) -	0/0
757	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017	0(O) -	0/0
758	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	-	07/2012 -	06/2014	-	0/0
759	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0
760	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(O) -	0/0
761	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	1.75	11/2014 -	12/2014	-	0/0
762	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019	0(O) -	0/7
763	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	-	-	-	-	0/0
764	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
765	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	12/2016	3(O) -	0/0
766	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	-	03/2012 -	04/2015	-	0/0
	Total		138,680.82 -	143,894.82	21,775.46				4/34
	Grand Total		1,068,206.97	1,273,650.02	485,680.02				1704/3737


Summary of projects in the Flash Report for the month of May, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	758
Number of Projects completed/dropped/frozen in Current Month	12
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	22
Number of Projects in Current Month	766


Brief Analysis

Project Status with respect to Original Schedule: Out of 766 projects, 2 projects are ahead of schedule, 127 projects are on schedule 237 projects are delayed. 371 projects do not have fixed dates of commissioning. 29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

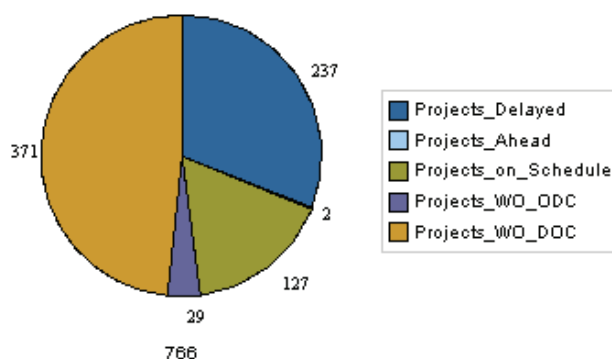

Investment Scenario

Total original cost of implementation of 766 projects when sanctioned, was of the order of Rs. 1068206.97 crore but this was subsequently revised to Rs. 1273650.02 crore implying a cost overrun of 19.2%. The expenditure incurred on these projects till May, 2015 is Rs. 485680.02 crore, which is 38.1% of the revised cost of the projects.

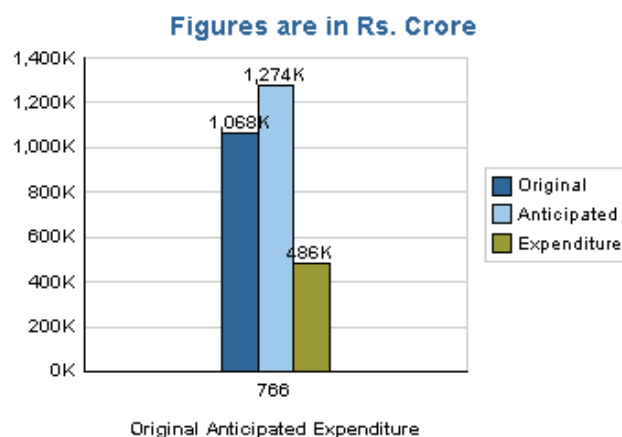

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed. 1 project does not have fixed dates of commissioning.

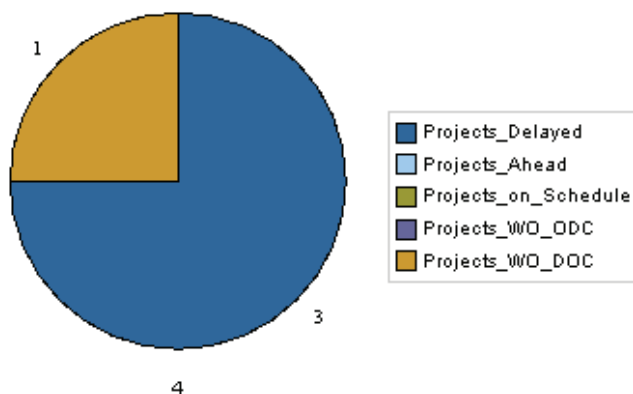

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till May, 2015 is Rs. 34774.77 crore, which is 74.4% of the revised cost of the projects.

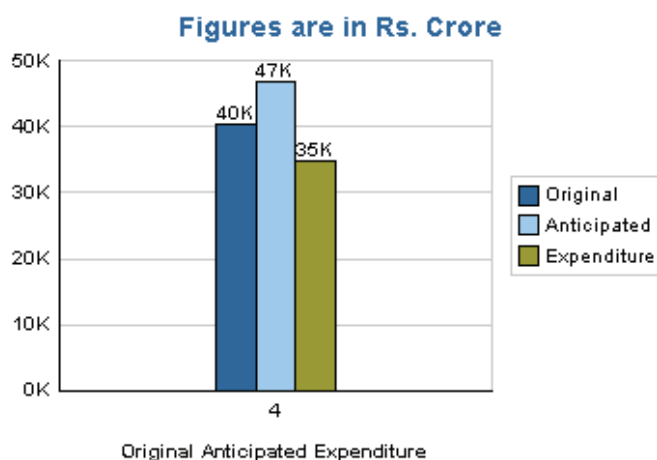

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	4
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 4 projects are delayed. 2 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

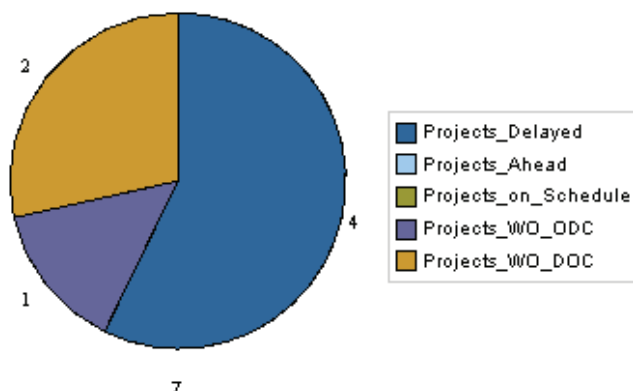

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently anticipated to Rs. 2689.48 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till May, 2015 is Rs. 1639.7 crore, which is 61% of the revised cost of the projects.

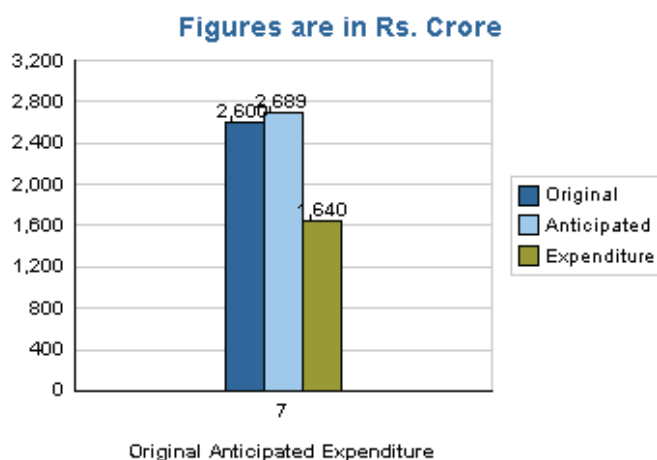

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	76
Number of Projects On Schedule	30
Number of Projects Delayed	44

Number of Projects Without Date Of Commissioning	2
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 76 projects, 30 projects are on schedule 44 projects are delayed. 2 projects do not have fixed dates of commissioning.

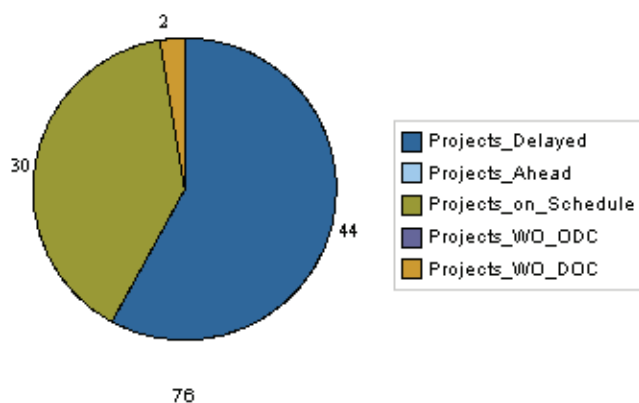

Investment Scenario

Total original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 59371.42 crore but this was subsequently anticipated to Rs. 63381.37 crore implying a cost overrun of 6.8%. The expenditure incurred on these projects till May, 2015 is Rs. 22190.77 crore, which is 35% of the revised cost of the projects.

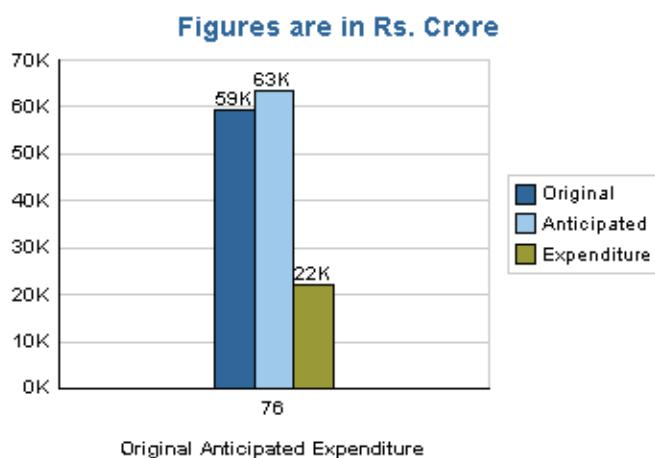

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	65
Number of Projects On Schedule	17
Number of Projects Delayed	41
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 65 projects, 1 project is ahead of schedule, 17 projects are on schedule 41 projects are delayed. 6 projects do not have fixed dates of commissioning.

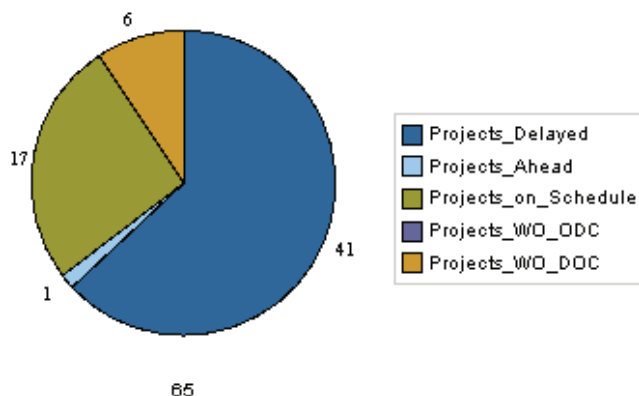

Investment Scenario

Total original cost of implementation of 65 projects when sanctioned, was of the order of Rs. 144046.84 crore but this was subsequently anticipated to Rs. 153341.3 crore implying a cost overrun of 6.5%. The expenditure incurred on these projects till May, 2015 is Rs. 65243.75 crore, which is 42.5% of the revised cost of the projects.

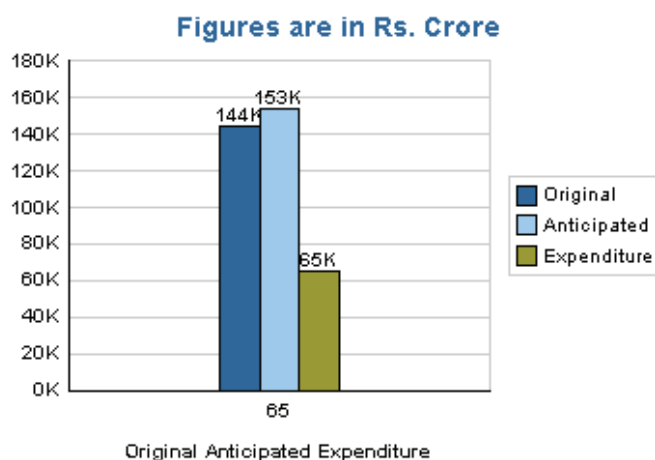

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	112
Number of Projects On Schedule	45
Number of Projects Delayed	62
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 112 projects, 1 project is ahead of schedule, 45 projects are on schedule 62 projects are delayed. 4 projects do not have fixed dates of commissioning.

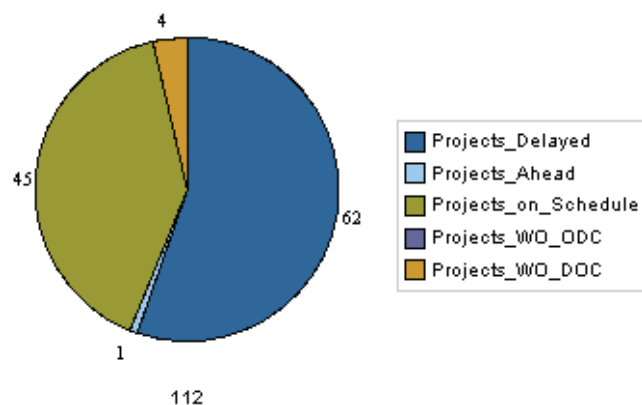

Investment Scenario

Total original cost of implementation of 112 projects when sanctioned, was of the order of Rs. 316428.52 crore but this was subsequently anticipated to Rs. 355392.4 crore implying a cost overrun of 12.3%. The expenditure incurred on these projects till May, 2015 is Rs. 174461.16 crore, which is 49.1% of the revised cost of the projects.

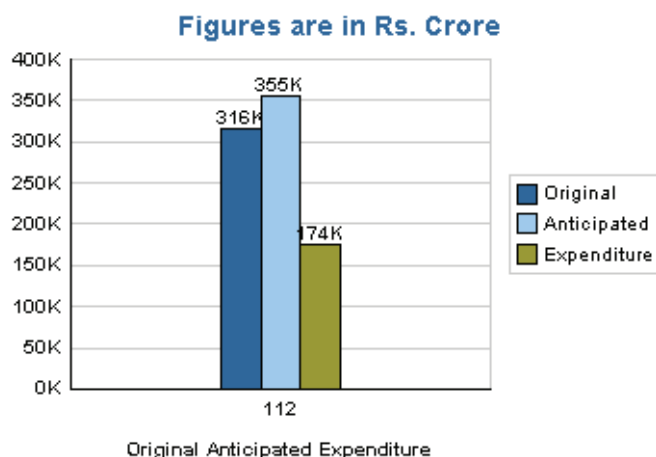

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	298
Number of Projects On Schedule	9
Number of Projects Delayed	32
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	230


Brief Analysis

Project Status with respect to Original Schedule: Out of 298 projects, 9 projects are on schedule 32 projects are delayed. 230 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

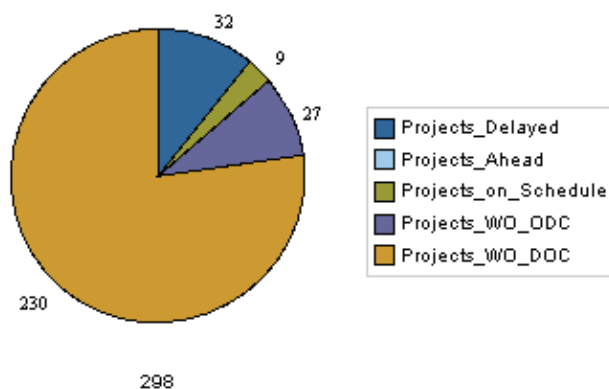

Investment Scenario

Total original cost of implementation of 298 projects when sanctioned, was of the order of Rs. 173660.34 crore but this was subsequently anticipated to Rs. 302322.34 crore implying a cost overrun of 74.1%. The expenditure incurred on these projects till May, 2015 is Rs. 94357.19 crore, which is 31.2% of the revised cost of the projects.

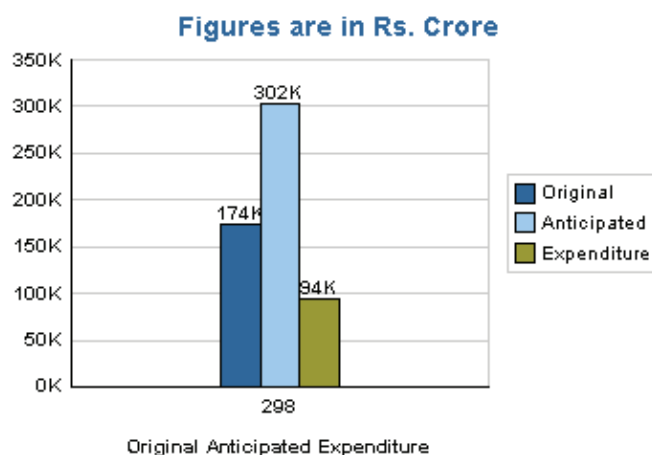

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHW

Current Status:

Number of Projects	132
Number of Projects On Schedule	8
Number of Projects Delayed	16
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	107


Brief Analysis

Project Status with respect to Original Schedule: Out of 132 projects, 8 projects are on schedule 16 projects are delayed. 107 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

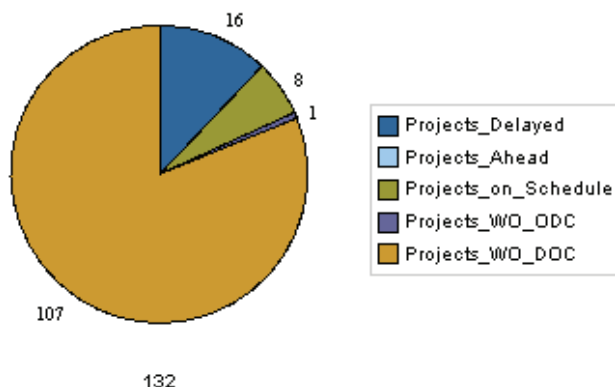

Investment Scenario

Total original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 98429.9 crore but this was subsequently anticipated to Rs. 100253.98 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till May, 2015 is Rs. 15546.19 crore, which is 15.5% of the revised cost of the projects.

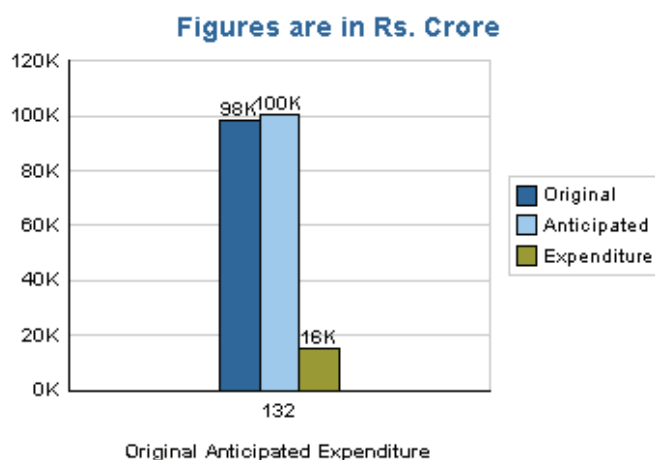

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	7
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 1 project is delayed. 6 projects do not have fixed dates of commissioning.

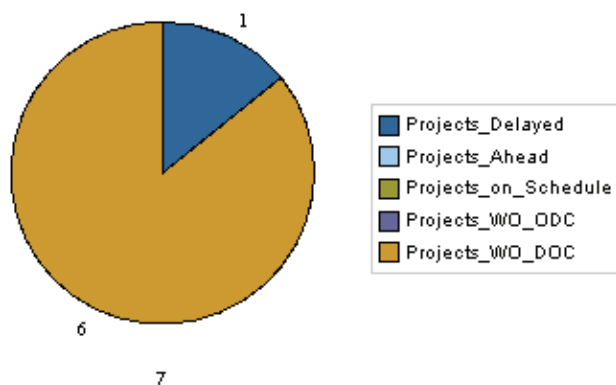

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 5524.46 crore but this was subsequently anticipated to Rs. 6428.61 crore implying a cost overrun of 16.4%. The expenditure incurred on these projects till May, 2015 is Rs. 2667.03 crore, which is 41.5% of the revised cost of the projects.

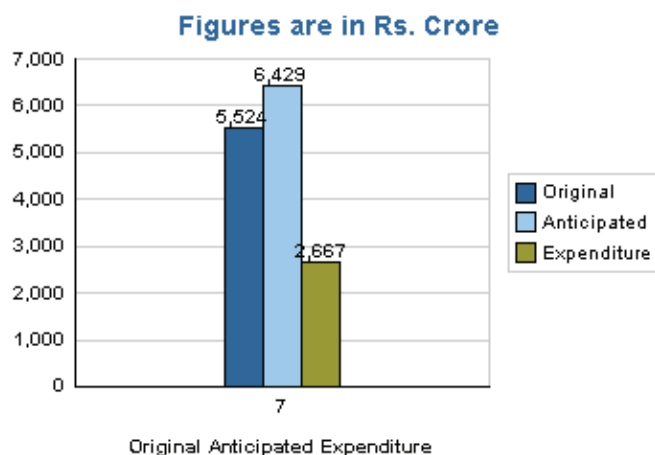

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	28
Number of Projects On Schedule	9
Number of Projects Delayed	16

Number of Projects Without Date Of Commissioning	3
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 9 projects are on schedule 16 projects are delayed. 3 projects do not have fixed dates of commissioning.

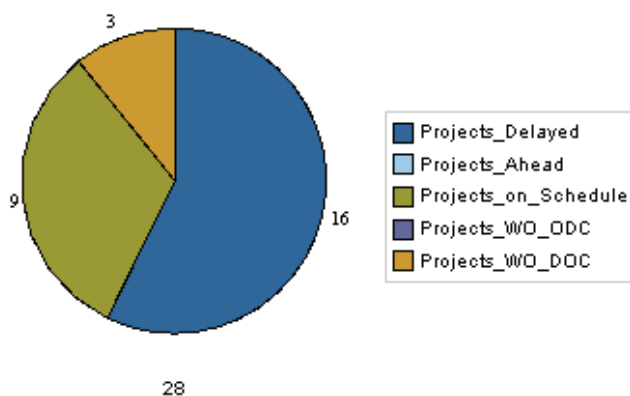

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 64995.71 crore but this was subsequently anticipated to Rs. 68710.11 crore implying a cost overrun of 5.7%. The expenditure incurred on these projects till May, 2015 is Rs. 44307.17 crore, which is 64.5% of the revised cost of the projects.

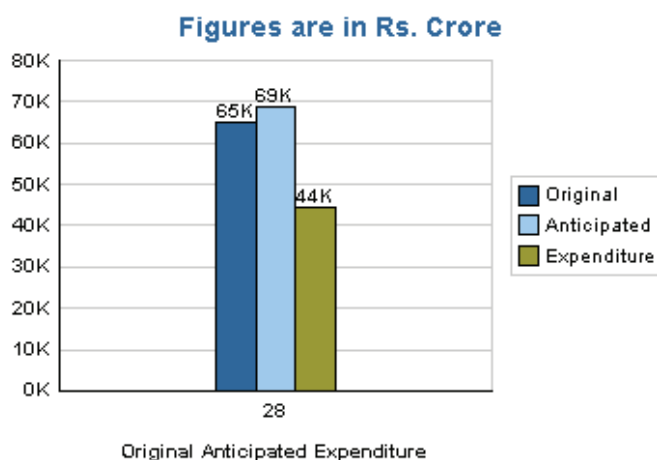

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	3
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 1 project is on schedule 1 project is delayed. 1 project does not have fixed dates of commissioning.

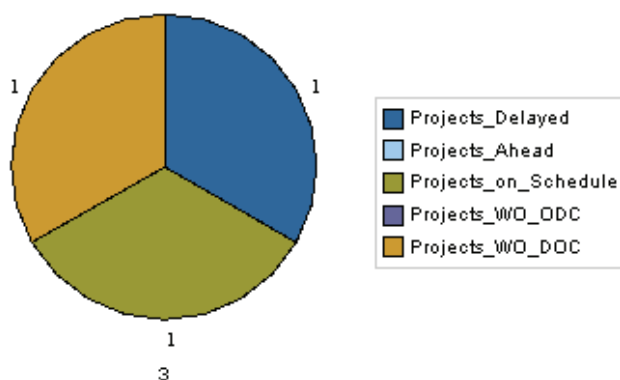

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14795 crore but this was subsequently anticipated to Rs. 14795 crore. The expenditure incurred on these projects till May, 2015 is Rs. 55.22 crore, which is .4% of the revised cost of the projects.

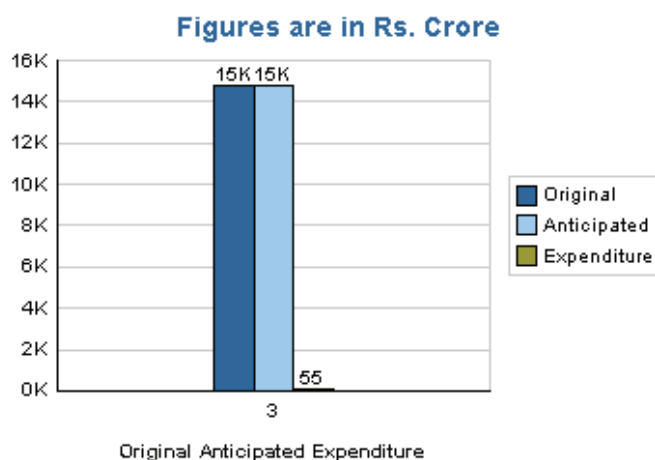

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	6
Number of Projects Delayed	15

Number of Projects Without Date Of Commissioning	9
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 30 projects, 6 projects are on schedule 15 projects are delayed. 9 projects do not have fixed dates of commissioning.

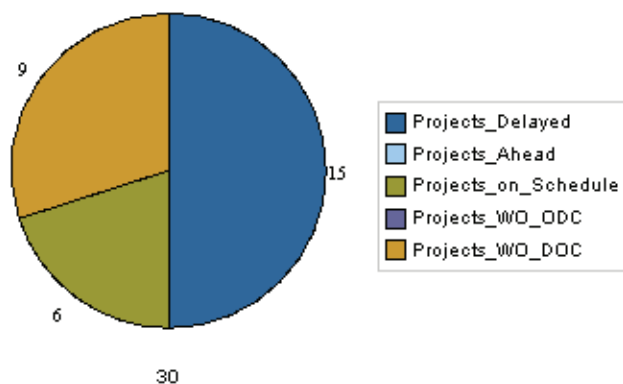

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 138680.82 crore but this was subsequently anticipated to Rs. 143894.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till May, 2015 is Rs. 21775.46 crore, which is 15.1% of the revised cost of the projects.

Figures are in Rs. Crore

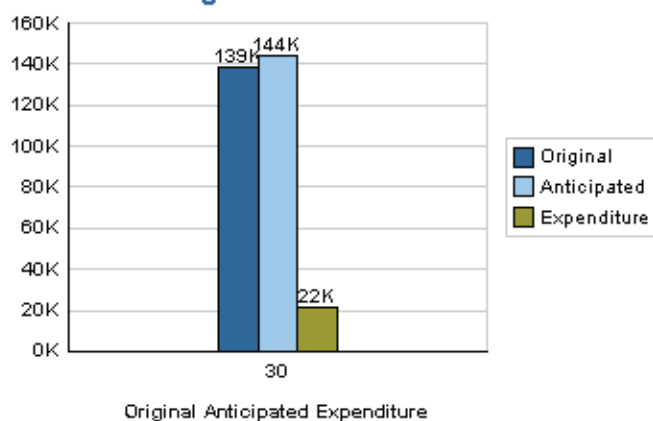

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	17.82
2	ANDHRA PRADESH	28	25,167.01	31,389.44	15,007.4
3	ARUNACHAL PRADESH	3	9,356.22	23,263.83	12,630.79
4	ASSAM	35	23,171.23	41,510.44	28,949.76
5	BIHAR	48	57,726.67	71,504.87	39,905.91
6	CHANDIGARH	1	452	489	433.99
7	CHHATISGARH	28	80,681.93	82,331.47	42,329.8
8	D & N HAVELI	1	6,086.08	6,086.08	0
9	DELHI	12	50,903.45	50,903.45	8,810.75
10	GOA	1	335.61	388.53	301.94
11	GUJARAT	26	28,108.61	28,687.78	9,706.99
12	HARYANA	9	4,659.81	6,630.43	1,852.6
13	HIMACHAL PRADESH	5	11,681.24	19,906.33	11,742.73
14	JAMMU AND KASHMIR	7	21,314.62	40,235.3	17,899.24
15	JHARKHAND	37	38,870.74	39,535.41	14,816.57
16	KARNATAKA	34	66,982.2	81,944.97	19,176.29
17	KERALA	13	24,457.67	28,611.45	8,753.44
18	MADHYA PRADESH	20	24,954.32	26,938.24	8,581.11
19	MAHARASHTRA	46	98,557.84	1,08,038.31	26,390.79
20	MANIPUR	1	727.56	6,570.75	2,787.99
21	MEGHALAYA	3	4,845.02	6,069.9	290.09
22	MIZORAM	2	988.06	4,201.96	1,021.42
23	MULTI STATE	187	2,12,378.07	2,37,630.89	73,110.82
24	NAGALAND	2	5,124	7,461.12	10.44
25	ODISHA	42	72,202.55	81,290.49	39,382.51
26	PUNJAB	3	792.5	765.46	110.47
27	RAJASTHAN	25	26,236.17	26,291.64	7,562
28	SIKKIM	2	1,648.94	4,499.46	430.1
29	TAMIL NADU	42	68,208.56	85,860.44	55,787.9
30	TELANGANA	21	9,410.62	12,235.26	3,007.38
31	TRIPURA	6	2,966.26	6,629.97	3,279.08
32	UTTAR PRADESH	30	36,706.01	39,695.73	9,553.66
33	UTTARAKHAND	6	9,351.89	12,905.21	4,482.97
34	WEST BENGAL	39	42,838.9	52,831.8	17,555.27

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

TOTAL	766	10,68,206.97	12,73,650.02	4,85,680.02
--------------	------------	---------------------	---------------------	--------------------

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	18,632
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,212.02
3	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,079.93
4	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,705.13
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,762.59
6	VIRAMGAM-BHILDI (WR) , GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	RAILWAYS	03/1995	2,500	3000	10,658.34
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	RAILWAYS	02/1997	295	-	872.28
12	KARUR-SALEM (NL) , SR	RAILWAYS	02/1997	155.55	-	800.66
13	NANDYAL-YERRAGUNTALA (NL) , SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR-KASGANJ-MATHURA (GC) , NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06
16	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
17	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
18	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	815.43
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
21	KATI HAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
22	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
23	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	RAILWAYS	04/1997	863.23	-	888.87
24	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
25	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
26	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,544.45

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84
30	JIND-SONEPAT (NL) ,NR	RAILWAYS	01/2004	238.56	-	639.77
31	RAJATGARH-BARANG (LD) , ECR	RAILWAYS	04/1999	166.16	-	305.47
32	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	RAILWAYS	04/2002	921	-	1,667.3
34	PATNA GANGA BRIDGE (NL) , ECR	RAILWAYS	04/2001	624.47	-	2,491.45
35	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	3,198.3
36	ETAHWAH-MAINPURI (NL) ,NCR	RAILWAYS	04/1997	120	245.39	249.33
37	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
38	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	277.33
39	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	277.09
40	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	228.3
41	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	326.3
42	C/O NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	341.54

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	3,952.2
44	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	8,664
45	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,182.93
46	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	497.57
47	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	793.71
48	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
49	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
50	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
51	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
52	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
53	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
54	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	606.08
55	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
56	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45
58	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
59	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	793.42
60	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	255.17
61	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
62	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
63	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
64	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
65	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
66	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
67	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
68	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
69	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	373.31
70	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	800.9

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
72	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
73	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
74	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
75	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
76	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
77	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
78	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273
79	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
80	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
81	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	776.4
82	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	-	351.18

Details of Projects Ahead of Schedule w.r.t. Original Schedule

							(May 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 219.08	219.08	137.25	09/2016 -	12/2015
	Total		141.86 -	219.08	137.25		
	<u>POWER</u>						
2	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	444.97	10/2016 -	12/2015
	Total		1,315.90 -	1,315.90	444.97		
	Grand Total		1,457.76	1,534.98	582.22		

Details of On Schedule Projects w.r.t. Original Schedule

							(May 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	764.15	03/2023 03/2023	03/2023
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	799.08	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	208.16	03/2017 -	03/2017
4	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
5	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	112.65	03/2020 -	03/2020
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	111.83	03/2016 -	03/2016
7	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	221.78	03/2016 -	03/2016
8	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	79.86	03/2018 -	03/2018
9	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	78.34	03/2016 -	03/2016
10	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	486.27	69.97	03/2016 -	03/2016
11	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	106.77	03/2020 -	03/2020
12	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
13	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2021
14	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	156.45	03/2018 -	03/2018
16	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
17	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	6.34	03/2019 -	03/2019
18	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
19	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
20	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
21	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	12.57	03/2021 -	03/2021
22	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020

							(May 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	MAKARDHOKRA I OC - [N06000119	9/2014	266.23 -	266.23	79.31	03/2021 -	03/2021
24	GOKUL - [N06000120	11/2014	267.67 -	267.67	148.56	03/2018 -	03/2018
25	BHANEAGAON OC - [N06000121	2/2015	187.94 -	187.94	32.89	03/2023 -	03/2023
26	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
27	AMERA OC RCE - [N06000123	2/2015	335.97 -	335.97	29.60	03/2018 -	03/2018
28	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	108.43	03/2021 -	03/2021
29	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	26.13	03/2021 -	03/2021
30	NEW MAJRI UG TO OC - [N06000128	5/2015	295.56 -	295.56	0.16	03/2019 -	03/2019
	Total		27,647.31 -	27,542.63	3,288.92		
	<u>FERTILISERS</u>						
31	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	197.79	13.21	11/2016 -	11/2016
	Total		197.79 -	197.79	13.21		
	<u>MINES</u>						
32	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
33	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	3/2012	14,225.00 -	16,504.00	6,536.23	05/2016 -	05/2016
34	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199	5/2015	257.87 -	257.87	5.37	11/2016 -	11/2016
35	DAMAN DEVELOPMENT PROJECT - [N16000198	8/2014	6,086.08 -	6,086.08	-	05/2019 -	05/2019
36	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	6,068.80	-	04/2019 -	04/2019
37	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
38	TWENTY NOS. FEEDER GAS LINES - [N16000192	3/2009	228.64 -	214.19	123.67	12/2016 -	12/2016
39	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
40	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190	7/2014	419.04 -	419.04	112.81	01/2017 -	01/2017

							(May 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,118.78	05/2017 05/2017	05/2017
42	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	59.21	12/2018 -	12/2018
43	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
44	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	95.53	09/2017 -	09/2017
45	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	33.61	02/2016 -	02/2016
46	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	18.74	07/2016 -	07/2016
47	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	98.95	09/2017 -	09/2017
48	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	57.16	07/2016 -	07/2016
49	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,049.32	11/2015 -	11/2015
	Total		44,954.05 -	47,616.98	9,322.45		
	<u>POWER</u>						
50	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,289.00	01/2017 -	01/2017
51	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
52	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	3,569.00	01/2018 -	01/2018
53	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
54	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
55	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
56	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
57	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	15.20	05/2018 -	05/2018
58	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
59	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	1.90	11/2017 -	11/2017
60	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	-	06/2016 -	06/2016
61	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	-	05/2017 -	05/2017

(May 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	-	05/2018 -	05/2018
63	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
64	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	25.70	04/2018 -	04/2018
65	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	110.00	09/2019 -	09/2019
66	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,086.00	02/2019 -	02/2019
67	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,539.00	08/2018 -	08/2018
68	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	709.00	03/2019 -	03/2019
69	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	595.00	12/2016 -	12/2016
70	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	5.20	11/2016 -	11/2016
71	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
72	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
73	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	49.90	12/2015 -	12/2015
74	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	63.10	08/2016 -	08/2016
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	30.70	06/2016 -	06/2016
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	26.00	06/2016 -	06/2016
77	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
78	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	217.44	04/2016 -	04/2016
79	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
80	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
81	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	1.40	02/2016 -	02/2016
82	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	1.00	02/2017 -	02/2017
83	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	12.40	02/2017 -	02/2017
84	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	467.80	03/2018 -	03/2018
85	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	1.50	04/2017 -	04/2017

							(May 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	64.70	10/2016 -	10/2016
87	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	1.00	05/2016 -	05/2016
88	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,174.00	06/2017 -	06/2017
89	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	144.00	08/2017 -	08/2017
90	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,246.00	09/2017 -	09/2017
91	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	291.80	05/2016 -	05/2016
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	230.79	03/2016 -	03/2016
93	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,816.00	08/2015 -	08/2015
94	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,086.00	09/2016 -	09/2016
	Total		149,445.44 -	149,445.44	31,877.43		
	<u>RAILWAYS</u>						
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	663.95	03/2016 -	03/2016
96	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
97	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
98	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
99	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	44.04	03/2016 -	03/2016
100	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
101	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
102	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	551.84	03/2016 -	03/2016
	Total		15,043.28 -	19,672.48	3,804.10		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
104	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	-	06/2015 -	06/2015

							(May 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	-	12/2015 -	12/2015
106	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
107	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
108	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
109	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
110	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	-	08/2015 -	08/2015
111	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015
	Total		11,163.83 -	11,163.83	.00		
	<u>STEEL</u>						
112	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016
113	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	110.34	04/2016 -	04/2016
114	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	84.15	07/2016 -	07/2016
115	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	25.02	10/2016 -	10/2016
116	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016
117	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
118	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018
119	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
120	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017
	Total		8,123.02 -	8,268.42	253.82		
	<u>TELECOMMUNICATIONS</u>						
121	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
122	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019

(May 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
123	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
124	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
125	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019
126	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
127	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		45,907.98 -	45,907.98	.00		
	Grand Total		317,672.70	325,005.55	48,559.93		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2015)

S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year)		Cost Overruns (%)
					Original/ Revised	Anticipated	
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	09/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	-	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	05/2015	8.19
	Total		787.61 -	877.53			
	<u>COAL</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	06/2015	76.47
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	06/2015	34.63
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2016	12.97
	Total		8,198.48 -	12,806.16			
	<u>HEAVY INDUSTRY</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
12	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	06/2015	80.08

(May 2015)

(May 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		5,460.61	9,833.52			
	<u>PETROLEUM</u>						
13	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82	3,955.21	04/2006	06/2015	820.20
14	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00	34,555.00	11/2012	10/2015	16.05
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128	03/2011	861.79	958.55	05/2013	12/2015	11.23
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63	2,665.65	03/2015	05/2016	29.42
17	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00	16,504.00	05/2016	05/2016	16.02
18	REWARI KANPUR PIPELINE PROJECT - [N16000145	02/2012	1,210.64	1,446.34	11/2015	11/2015	19.47
19	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	02/2012	666.00	838.08	11/2015	11/2016	25.84
20	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81	462.79	10/2014	10/2016	49.38
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00	1,178.35	10/2011	06/2015	75.35
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00	1,227.00	10/2011	10/2015	67.62
23	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56	450.55	03/2017	03/2017	27.79
24	MARKETING TERMINAL AT PARADEEP - [N16000168	07/2009	199.75	239.73	07/2013	07/2015	20.02
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00	1,693.00	01/2012	10/2015	70.49
26	MARKETING TOP AT KORBA - [N16000186	01/2011	141.86	219.08	09/2016	12/2015	54.43
27	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47	5,813.25	05/2017	05/2017	1.87
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35	1,200.00	03/2015	02/2016	37.72
	Total		59,208.68	73,406.58			
	<u>POWER</u>						
29	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59	7,531.72	09/2009	12/2018	92.16
30	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15	7,220.00	04/2009	06/2015	59.48
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33	15,300.00	09/2010	-	143.42

(May 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38
33	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65
34	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
35	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34
36	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
37	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
38	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
39	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10
40	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
41	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
42	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15
43	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35
44	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	09/2015	13.18
45	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87
46	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH [N18000105]	09/2011	1,366.34 -	1,606.38	12/2013 -	06/2015	17.57
47	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63
48	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH [N18000116]	12/2011	1,746.65 -	2,228.70	08/2014 -	03/2016	27.60
49	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
50	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52
	Total		54,099.77 -	93,127.26			
	<u>RAILWAYS</u>						
51	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
52	VIRAMGAM-BHILD(I(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06

(May 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
53	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
54	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
55	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
56	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
57	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
58	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
59	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
60	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
61	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
62	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
63	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
64	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
65	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
66	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
67	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
68	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
69	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
70	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
71	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
72	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
73	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
74	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
75	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
76	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37

(May 2015)

(May 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
77	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
78	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
79	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
80	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
81	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
82	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
83	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
84	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
86	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
87	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
88	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
89	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
90	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
91	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
92	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
93	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
94	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
95	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
96	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
97	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
98	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
99	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,700.00	- -	03/2015	304.06

(May 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
100	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
101	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
102	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
103	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
104	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
105	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
106	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
107	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
108	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
109	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
110	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	261.70 -	280.00	02/2006 -	03/2016	6.99
111	OBULAVARIIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
112	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
113	BHOPAL BINA 3D LINE DOUBLING - [N220000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
114	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N220000079	09/2007	404.19 -	1,383.45	- -	-	242.28
115	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080	09/2006	343.17 -	914.98	- -	03/2016	166.63
116	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
117	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084	09/2006	125.00 -	490.00	- -	-	292.00
118	TIDIVANAM-NAGARI (NL) - [N220000085	09/2006	456.00 -	1,080.00	- -	-	136.84
119	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
120	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087	09/2006	300.00 -	827.73	- -	03/2019	175.91
121	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
122	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
123	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77

(May 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
124	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
125	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
126	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
127	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
128	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
129	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
130	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
131	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
132	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
133	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
134	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
135	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
136	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
137	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
138	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
139	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
140	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
141	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
142	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
143	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
144	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
145	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92

(May 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
146	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
147	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
148	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
149	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
150	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
151	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
152	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
153	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
154	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
155	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
156	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
157	HAJIPUR-RAMDALYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
158	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
159	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
160	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
161	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
162	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
163	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
164	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
165	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
166	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
167	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
168	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85

(May 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
169	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
170	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
171	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
172	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
173	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
174	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
175	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
176	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
177	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
178	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
179	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
180	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
181	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
182	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
183	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
184	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
185	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
186	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
187	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
188	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
189	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
190	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
191	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
192	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42

(May 2015)

(May 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
194	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
195	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
196	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
197	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
198	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
199	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
200	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
201	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
202	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
203	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
204	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
205	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
206	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
207	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
208	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
209	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
210	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
211	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
212	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
213	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		87,416.65 -	217,200.13			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
214	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10

(May 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
215	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
216	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
217	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
218	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
219	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
220	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
221	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	348.19	09/2007 -	09/2017	0.01
222	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		2,934.62 -	4,786.21			
	<u>SHIPPING AND PORTS</u>						
223	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
224	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
225	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	-	51.92
226	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,990.06 -	3,102.68			
	<u>STEEL</u>						
227	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	04/2015	41.41
228	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		9,035.00 -	12,779.40			
	<u>URBAN DEVELOPMENT</u>						
229	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		253,907.48	466,302.77			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2015)

(May 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	09/2015	31.12	81
	Total		13,171.00 -	17,270.00				
	<u>CIVIL AVIATION</u>							
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	05/2015	8.19	2
	Total		452.00 -	489.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
4	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	06/2015	76.47	72
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	06/2015	34.63	39
	Total		7,617.44 -	12,121.30				
	<u>HEAVY INDUSTRY</u>							
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROCHEMICALS</u>							
8	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	06/2015	80.08	38
	Total		5,460.61 -	9,833.52				
	<u>PETROLEUM</u>							
9	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	07/2015	20.02	24
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24

(May 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
11	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110
12	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) [N16000146	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,178.35	10/2011 -	06/2015	75.35	44
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	958.55	05/2013 -	12/2015	11.23	31
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	02/2016	37.72	11
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
19	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05	35
	Total		37,572.15 -	48,973.36				
	<u>POWER</u>							
20	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) [N18000156	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52	5
21	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63	16
22	TUJIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
23	TRIPURA GAS BASED POWER PROJECT [N18000071	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35	25
24	WESTERN REGION STRENGTHENING SCHEME-V [N18000035	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10	66
25	PARE HYDRO ELECTRIC PROJECT [N18000045	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15	31
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
27	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH [N18000105	09/2011	1,366.34 -	1,606.38	12/2013 -	06/2015	17.57	18
28	TEHRI PUMPED STORAGE PLANT(1000MW) [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
29	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH [N18000116	12/2011	1,746.65 -	2,228.70	08/2014 -	03/2016	27.60	19

(May 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34	90
31	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	09/2010	2,074.86 -	2,348.37	03/2013 -	09/2015	13.18	30
32	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31	52
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38	87
34	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C [N18000096	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87	17
35	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69
36	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
37	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16	111
38	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
39	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	7,220.00	04/2009 -	06/2015	59.48	74
40	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65	99
	Total		47,814.44 -	77,827.26				
	<u>RAILWAYS</u>							
41	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67	66
42	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
43	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49	82
44	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
45	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
46	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
47	KATAKHAL TO BHAIKABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
48	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	03/2016	6.99	121
49	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174

(May 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
50	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
51	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
52	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
53	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45	30
54	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
56	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
57	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
58	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
59	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
60	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
61	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
62	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
63	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
64	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
65	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
67	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
68	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		22,395.40 -	78,977.44				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
69	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69

(May 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
70	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	348.19	09/2007 -	09/2017	0.01	120
	Total		565.77 -	657.75				
	<u>SHIPPING AND PORTS</u>							
71	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72	61
	Total		366.39 -	669.46				
	Grand Total		137,133.20	250,646.39				

List of Projects having cost overrun with respect to Anticipated/Cumulative Expenditure

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
1	ATOMIC ENERGY	NPCIL	KUDANKULAM APP (NPCIL)	13,171.00	17,270.00	18,632.00	5,461.00
2	ATOMIC ENERGY	BHAVNI	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	3,492.00	5,677.00	4,967.77	2,185.00
3	CIVIL AVIATION	AAI	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	309.46	309.46	341.54	32.00
4	CIVIL AVIATION	AAI	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	452.00	489.00	433.99	37.00
5	CIVIL AVIATION	AAI	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	335.61	388.53	301.94	53.00
6	COAL	NLC	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	3,583.77	3,212.02	1,553.00
7	COAL	CCL	MAGADH OC 20 MTY (CCL)	469.78	706.40	76.55	237.00
8	COAL	NLC	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	4,904.54	6,602.74	6,223.31	1,698.00
9	COAL	SCCL	RFR OF MANUGURU OC PROJECT	430.45	486.27	69.97	56.00
10	COAL	SECL	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	150.59	198.59	111.83	48.00
11	COAL	SCCL	ADRIYALA SHAFT PROJECT	212.34	1,228.39	879.58	1,016.00
12	HEAVY INDUSTRY	HIPE	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	1,718.00	3,827.30	0.00	2,109.00
13	PETROCHEMICALS	BCPL	ASSAM GAS CRACKER PROJECT	5,460.61	9,833.52	8,648.40	4,373.00
14	PETROLEUM	ONGC	DEV OF G1 AND GS-15 (ONGCL)	429.82	3,955.21	3,439.38	3,525.00
15	PETROLEUM	IOCL	PARADIP REFINERY PROJECT	29,777.00	34,555.00	29,101.07	4,778.00
16	PETROLEUM	ONGC	INTEGRATED DEVELOPMENT OF B-127 FIELDS	2,059.63	2,665.65	1,201.17	606.00
17	PETROLEUM	HPCL	REWARI KANPUR PIPELINE PROJECT	1,210.64	1,446.34	1,049.32	236.00
18	PETROLEUM	HPCL	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	309.81	462.79	222.98	153.00
19	PETROLEUM	OIL	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	871.35	1,200.00	220.47	329.00
20	PETROLEUM	ONGC	MH NORTH REDEVELOPMENT PHASE III	5,706.47	5,813.25	1,118.78	107.00
21	PETROLEUM	IOCL	MARKETING TOP AT KORBA	141.86	219.08	137.25	77.00
22	PETROLEUM	ISPRL	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	993.00	1,693.00	1,398.50	700.00
23	PETROLEUM	IOCL	MARKETING TERMINAL AT PARADEEP	199.75	239.73	184.18	40.00
24	PETROLEUM	OIL	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	352.56	450.55	10.60	98.00
25	PETROLEUM	ISPRL	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	732.00	1,227.00	951.70	495.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
26	PETROLEUM	ISPR	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	672.00	1,178.35	1,078.77	506.00
27	PETROLEUM	HPCL	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	666.00	838.08	461.00	172.00
28	PETROLEUM	BPCL	INTEGRATED REFINERY EXPANSION PROJECT	14,225.00	16,504.00	6,536.23	2,279.00
29	PETROLEUM	ONGC	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	861.79	958.55	843.52	97.00
30	POWER	NHPC	PARBATI HEP (4X200 MW) (NHPC) II	3,919.59	7,531.72	5,079.93	3,612.00
31	POWER	NTPC	BARH STPP(3X660MW) NTPC	8,692.97	15,095.67	10,850.00	6,403.00
32	POWER	PGCIL	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	1,779.29	2,159.07	1,891.95	380.00
33	POWER	NHPC	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	1,061.38	1,929.15	1,762.59	868.00
34	POWER	NEEPC O	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	2,496.90	6,476.34	3,899.87	3,979.00
35	POWER	NEEPC O	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW)	296.87	363.73	311.69	67.00
36	POWER	NEEPC O	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	368.72	1,381.71	822.11	1,013.00
37	POWER	PGCIL	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	1,746.65	2,228.70	1,155.03	482.00
38	POWER	PGCIL	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	297.33	346.79	276.57	49.00
39	POWER	PGCIL	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	2,127.51	2,127.51	2,182.93	55.00
40	POWER	PGCIL	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	1,366.34	1,606.38	1,316.76	240.00
41	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	2,569.25	3,105.51	2,796.47	536.00
42	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	2,074.86	2,348.37	1,834.94	274.00
43	POWER	NEEPC O	TRIPURA GAS BASED POWER PROJECT	421.01	1,007.68	912.03	587.00
44	POWER	NTPC	BARH STPP STAGE -II	7,341.04	7,341.04	8,664.00	1,323.00
45	POWER	NEEPC O	PARE HYDRO ELECTRIC PROJECT	573.99	1,487.49	1,025.79	914.00
46	POWER	THDCIL	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	3,745.08	641.42	1,254.00
47	POWER	NTPC	BONGAIGAON THERMAL POWER PROJECT	4,375.35	6,749.18	5,243.00	2,374.00
48	POWER	PGCIL	WESTERN REGION STRENGTHENING SCHEME-V	477.69	721.81	520.09	244.00
49	POWER	NHPC	KISHANGANGA HEP (3X110 MW)	3,642.04	5,497.72	3,952.20	1,856.00
50	POWER	NTPC	TAPOVAN-VISHNUGAD HEP (4X130MW)	2,978.48	3,846.30	2,460.00	868.00
51	POWER	THDCIL	TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	2,978.86	1,235.17	1,322.00
52	POWER	NTPC	KOLDAM HEP (NTPC)	4,527.15	7,220.00	6,622.00	2,693.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
53	POWER	NHPC	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	6,285.33	15,300.00	7,705.13	9,015.00
54	RAILWAYS	NCR	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	158.77	608.02	602.10	449.00
55	RAILWAYS	CR	AMRAVATI-NARKHER NL(CR)	663.01	725.00	586.75	62.00
56	RAILWAYS	NFR	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	36.80	1,336.57	255.55	1,300.00
57	RAILWAYS	SR	CALICUT-MANGALORE (DL) (SR)	240.00	579.37	599.40	359.00
58	RAILWAYS	CR	AHMEDNAGAR-PARLI VAJNATH(NL) CR	514.68	2,820.00	329.67	2,305.00
59	RAILWAYS	SECR	GONDIA-JABALPUR(GC),(SECR)	386.30	1,544.40	590.26	1,158.00
60	RAILWAYS	SR	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	343.17	914.98	846.18	572.00
61	RAILWAYS	SR	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-AGASTIYAMPALLI	404.19	1,383.45	457.88	979.00
62	RAILWAYS	RVNL	BHOPAL BINA 3D LINE DOUBLING	687.20	800.00	793.71	113.00
63	RAILWAYS	RVNL	SALKA ROAD -ANUPNAGAR LINE DOUBLING	324.90	385.54	230.21	61.00
64	RAILWAYS	RVNL	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	743.00	1,117.11	424.42	374.00
65	RAILWAYS	SER	GOELKERA-MANOHARPUR,(LD)(SER)	261.70	280.00	177.01	18.00
66	RAILWAYS	SCR	MANOHARABAD-KOTHPALL NEW LINE(SCR)	378.56	791.59	5.41	413.00
67	RAILWAYS	ECR	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	332.92	477.88	497.57	165.00
68	RAILWAYS	NER	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	863.23	1,072.51	888.87	209.00
69	RAILWAYS	ER	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	207.52	207.52	223.44	16.00
70	RAILWAYS	NWR	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	516.23	516.23	588.49	72.00
71	RAILWAYS	RVNL	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	3,951.98	4,259.48	663.95	308.00
72	RAILWAYS	SWR	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	482.00	874.57	606.08	393.00
73	RAILWAYS	NFR	SEVOK RANGPO, NEFR	1,339.48	4,190.00	88.56	2,851.00
74	RAILWAYS	NFR	KISHANGANJ JALALGARH, NL, NEFR	282.92	565.13	2.80	282.00
75	RAILWAYS	NFR	BHAIRABI SAIRONG, NL, NEFR	619.34	2,820.25	199.31	2,201.00
76	RAILWAYS	NFR	AGARTALA SABROOM, NL, NEFR	813.34	2,876.00	823.83	2,063.00
77	RAILWAYS	SER	TAMLUK DIGHA,LINE DOUBLING (SER)	293.97	1,428.00	466.36	1,134.00
78	RAILWAYS	SER	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	148.77	209.00	2.64	60.00
79	RAILWAYS	NER	GHAZIPUR - AUNRIHAR (40 KM)	182.92	197.73	0.00	15.00
80	RAILWAYS	ECOR	DELANG-PURI DOUBLING	165.16	234.71	137.01	70.00
81	RAILWAYS	ECOR	KIRANDUL - JAGDALPUR DOUBLING	826.57	1,143.60	189.12	317.00
82	RAILWAYS	ECOR	JHARSUGUDA-RENGALI DOUBLING	201.00	230.00	218.67	29.00
83	RAILWAYS	ECOR	SAMBALPUR-TALCHER DOUBLING	679.27	1,111.99	60.31	433.00
84	RAILWAYS	SER	MM FROM PANSKURA-GHATAL NL	276.69	426.00	0.00	149.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
85	RAILWAYS	SER	MM FROM BURAMARA-CHAKULIA	466.48	800.00	0.83	334.00
86	RAILWAYS	SR	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	460.94	1,030.00	800.90	569.00
87	RAILWAYS	SWR	CHIKBALLA-PUR-GOWRIBIDANUR NL	327.25	367.77	0.00	41.00
88	RAILWAYS	SWR	GADAG-WADI NL	1,117.00	1,922.00	0.59	805.00
89	RAILWAYS	SWR	TORANAGALLU-RANJITPURA DL	146.75	167.50	0.07	21.00
90	RAILWAYS	NR	HARIDWAR-LAKSAR	219.83	329.97	2.38	110.00
91	RAILWAYS	SWR	WHITE FIELD-KOLAR NL	341.05	348.85	0.32	8.00
92	RAILWAYS	SWR	RAYADURGA-TUMKUR NL	970.34	1,743.00	293.38	773.00
93	RAILWAYS	SWR	SHIMOGA-HARIHAR NL	562.74	832.47	0.58	270.00
94	RAILWAYS	SWR	SRINIVASA-PURA-MADANAPALLI NL	296.00	466.65	0.00	171.00
95	RAILWAYS	SWR	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	558.00	692.43	0.00	134.00
96	RAILWAYS	NR	BHANUPALI-BILASPUR BERI NL	1,046.88	2,966.99	40.80	1,920.00
97	RAILWAYS	NR	ROHTAK-MEHAM HANSI	287.00	576.18	3.40	289.00
98	RAILWAYS	SCR	AKOLA-KHANDWA GC AKOLA-AKOT	184.26	2,000.00	17.32	1,816.00
99	RAILWAYS	SWR	BAGALKOT-KUDACHI NL	377.93	986.30	42.62	608.00
100	RAILWAYS	SWR	MUNIRABAD (GINGERA) -RAICHUR NL	179.65	1,350.91	373.31	1,171.00
101	RAILWAYS	SWR	TUMKUR-CHITRADURGA-DAVENGERE NL	913.00	1,801.01	0.76	888.00
102	RAILWAYS	CR	PANVEL PEN DOUBLING	96.16	260.16	240.21	164.00
103	RAILWAYS	CR	PEN ROHA DOUBLING	98.74	203.00	227.84	129.00
104	RAILWAYS	CR	KALYAN-KASARA 3RD LINE	277.70	279.70	4.73	2.00
105	RAILWAYS	CR	WARDHA-NANDED MAHARASHTRA	499.30	2,501.05	84.11	2,002.00
106	RAILWAYS	SR	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	601.43	800.00	0.69	199.00
107	RAILWAYS	M RTP	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	632.68	816.55	44.04	184.00
108	RAILWAYS	NFR	LUMDING-HOJAI PATCH DOUBLING PROJECT	246.07	364.06	0.30	118.00
109	RAILWAYS	NFR	AMBARI FALAKATA TO NEW MAYNAGURI	312.12	453.10	134.79	141.00
110	RAILWAYS	NFR	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	523.17	1,653.55	1,040.11	1,130.00
111	RAILWAYS	NFR	MURKONGSELEK-PASIGHAT NL	165.82	435.58	0.56	270.00
112	RAILWAYS	NFR	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	241.52	394.28	233.46	153.00
113	RAILWAYS	NFR	NEW BG LINE FROM BALURGHAT TO HILLY NFR	242.22	679.57	40.41	437.00
114	RAILWAYS	NFR	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4,083.02	5,307.90	7.79	1,225.00
115	RAILWAYS	SR	CHENGANNUR-CHINGAVANAM	191.72	222.95	112.40	31.00
116	RAILWAYS	SR	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	247.00	951.24	619.87	704.00
117	RAILWAYS	SR	MADURAI-BODINAYAKKANUR	164.41	450.00	16.97	286.00
118	RAILWAYS	SR	ERODE-PALANI	288.57	603.22	1.64	315.00
119	RAILWAYS	NFR	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	283.55	288.81	11.74	5.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
120	RAILWAYS	NFR	NEW COOCHBEHAR TO SAMUKTALA	209.77	441.45	85.78	232.00
121	RAILWAYS	NFR	DIMAPUR-TIZIT NL	4,274.00	4,487.70	0.00	214.00
122	RAILWAYS	NFR	AGARTALA-AKHAURA NL	252.00	886.65	0.00	635.00
123	RAILWAYS	NFR	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	895.00	1,242.25	1,005.81	347.00
124	RAILWAYS	NFR	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	221.42	563.13	22.29	342.00
125	RAILWAYS	SR	KURUPPANTHARA-CHINGAVANAM	270.14	346.15	14.61	76.00
126	RAILWAYS	SR	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	822.39	1,280.83	1,031.83	458.00
127	RAILWAYS	SR	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	271.24	520.00	462.69	249.00
128	RAILWAYS	SR	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	198.68	556.64	268.56	358.00
129	RAILWAYS	SR	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	839.00	1,500.00	0.01	661.00
130	RAILWAYS	SR	CHENNAI-CUDDALORE VIA MAMALLAPURAM	523.52	1,200.00	2.07	676.00
131	RAILWAYS	SR	ATTIPPATTU-PUTTUR	446.87	528.00	2.96	81.00
132	RAILWAYS	NFR	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	1,798.00	1,887.90	0.00	90.00
133	RAILWAYS	ECR	HAJIPUR-RAMDAYALUNAGAR DOUBLING	213.01	367.17	13.02	154.00
134	RAILWAYS	ECR	MOTIHARI-SITAMARHI (NL)	211.00	926.09	4.41	715.00
135	RAILWAYS	ECOR	CHHAPRA-MUZAFFARPUR (NL)	285.07	378.56	111.71	93.00
136	RAILWAYS	ECOR	SAKRI-HASANPUR ROAD (NL)	175.69	325.00	255.17	149.00
137	RAILWAYS	SER	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	258.20	365.00	2.52	107.00
138	RAILWAYS	SER	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	309.44	583.00	144.66	274.00
139	RAILWAYS	SER	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	149.90	230.00	68.67	80.00
140	RAILWAYS	SER	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	289.64	760.00	0.09	470.00
141	RAILWAYS	SER	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	553.63	1,009.00	7.50	455.00
142	RAILWAYS	SER	BOWAICHANDI-ARAMBAGH	267.37	434.00	35.90	167.00
143	RAILWAYS	NCR	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	622.41	2,030.50	3.61	1,408.00
144	RAILWAYS	NWR	AJMER-BANGURGRAM	213.39	218.39	23.63	5.00
145	RAILWAYS	NWR	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	739.65	872.22	793.42	133.00
146	RAILWAYS	NWR	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	456.00	855.16	557.82	399.00
147	RAILWAYS	NWR	THIYAT HAMIRA-SANU	236.93	262.00	0.41	25.00
148	RAILWAYS	NCR	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	1,176.09	3,845.60	2.33	2,670.00
149	RAILWAYS	NWR	RATLAM-DUNGARPUR VIA BANSWARA (NL)	2,082.75	3,500.00	52.11	1,417.00
150	RAILWAYS	WR	VIRAMGAM-SAMAKHIALI (DL)	446.00	685.17	206.59	239.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
151	RAILWAYS	WR	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	320.66	913.48	457.67	593.00
152	RAILWAYS	NER	CHHAPRA-BALLIA UP	295.00	494.92	4.22	200.00
153	RAILWAYS	NFR	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	1,676.31	5,500.00	4,734.45	3,824.00
154	RAILWAYS	NFR	KATAKHAL TO BHAIRABI	227.90	331.40	182.22	104.00
155	RAILWAYS	WR	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	117.36	196.95	198.83	81.00
156	RAILWAYS	NFR	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	850.00	2,973.42	10.44	2,123.00
157	RAILWAYS	WR	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	318.24	321.62	2.91	3.00
158	RAILWAYS	WR	RATLAM-MHOW-KHANDWA-AKOLA (GC)	603.04	1,421.25	420.33	818.00
159	RAILWAYS	RE	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	171.10	275.08	141.55	104.00
160	RAILWAYS	M RTP	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	5,300.00	7,986.04	2,431.72	2,686.00
161	RAILWAYS	NR	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	325.00	1,564.54	420.71	1,240.00
162	RAILWAYS	NFR	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	300.00	827.73	53.52	528.00
163	RAILWAYS	NFR	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	200.00	496.24	213.72	296.00
164	RAILWAYS	SR	TIDIVANAM-NAGARI (NL)	456.00	1,080.00	194.61	624.00
165	RAILWAYS	SR	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	125.00	490.00	67.57	365.00
166	RAILWAYS	NFR	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	170.00	485.00	417.70	315.00
167	RAILWAYS	SCR	GULBARGA-BIDAR,SCR(NL)	242.42	844.00	798.87	602.00
168	RAILWAYS	SR	ANGAMALI-SABARIMALA (N.L.)(SR)	550.00	1,566.00	137.40	1,016.00
169	RAILWAYS	NFR	KATI HAR - JOGBANI (GC)(NEFR)	492.98	1,727.27	743.74	1,234.00
170	RAILWAYS	NCR	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	108.00	432.72	436.85	329.00
171	RAILWAYS	ECR	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	501.69	1,043.56	815.43	542.00
172	RAILWAYS	WCR	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	247.66	1,630.97	488.76	1,383.00
173	RAILWAYS	SCR	MACHERLA-NALGONDA(NL)(SCR)	125.00	480.00	3.51	355.00
174	RAILWAYS	SER	RANCHI-LOHARDAGA(GC),SER	194.07	335.00	230.67	141.00
175	RAILWAYS	ECR	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	921.00	2,363.00	1,667.30	1,442.00
176	RAILWAYS	ECR	KOSI BRIDGE (NL), ECR	322.95	341.41	322.72	18.00
177	RAILWAYS	NFR	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	727.56	6,570.75	2,787.99	5,843.00
178	RAILWAYS	RVNL	RAJATGARH-BARANG(LD),ECOR	166.16	288.00	305.47	139.00
179	RAILWAYS	RVNL	HARIDASPUR-PARADEEP(NL)	301.64	1,185.64	266.35	884.00
180	RAILWAYS	ECOR	KHURDA ROAD-BOLANGIR(NL)ECOR	470.21	1,995.25	355.02	1,525.00
181	RAILWAYS	NR	JIND-SONEPAT (NL),NR	238.56	740.00	639.77	501.00
182	RAILWAYS	SER	BANKURA - DAMODAR (GC) (SER)	111.90	2,371.85	486.25	2,260.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
183	RAILWAYS	SWR	BANGLORE - SATYAMANGALAM (NL)(SWR)	138.00	1,382.78	0.72	1,245.00
184	RAILWAYS	RVNL	RAICHUR-GUNTAKAL(DL)(SCR)	136.62	289.93	277.09	153.00
185	RAILWAYS	RVNL	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	133.41	276.00	277.33	144.00
186	RAILWAYS	RVNL	CUTTACK - BARANG (LD)	127.13	225.00	193.37	98.00
187	RAILWAYS	RVNL	SUKINDA ROAD - ANGUL (NL)(ECOR)	183.23	818.29	113.50	635.00
188	RAILWAYS	SECR	CHHINDWARA - NAGPUR (GC)(SECR)	383.79	1,101.16	194.91	717.00
189	RAILWAYS	NCR	ETAWAH-MAINPURI (NL),NCR	120.00	245.39	249.33	129.00
190	RAILWAYS	NER	MAHARAJGANJ-MASRAKH (NL) - NER	218.19	343.00	216.17	125.00
191	RAILWAYS	NFR	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	915.70	3,700.00	3,198.30	2,784.00
192	RAILWAYS	WCR	RAMGANJMUNDI-BHOPAL (NL),WCR	470.92	1,225.90	257.59	755.00
193	RAILWAYS	ECR	PATNA GANGA BRIDGE (NL), ECR	624.47	2,921.00	2,491.45	2,297.00
194	RAILWAYS	SCR	GADWAL - RAICHUR (NL), SCR	92.63	270.00	301.84	209.00
195	RAILWAYS	M RTP	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	1,049.69	3,404.92	3,544.45	2,495.00
196	RAILWAYS	NFR	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	733.00	2,531.34	1,732.43	1,798.00
197	RAILWAYS	SCR	KOTLPALLI-NARASAPUR (NL) (SCR)	330.00	1,047.00	1.29	717.00
198	RAILWAYS	SR	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	280.00	1,122.00	889.95	842.00
199	RAILWAYS	SR	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	100.00	980.00	596.66	880.00
200	RAILWAYS	NR	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	625.30	847.75	835.14	222.00
201	RAILWAYS	ECR	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	162.87	541.00	150.50	378.00
202	RAILWAYS	SER	HOWRAH-AMTA-CHAMPADANGA NL (SER)	393.46	1,026.00	181.48	633.00
203	RAILWAYS	SCR	MUNEERABAD-MAHABOBNAGAR(NL),SCR	218.24	645.00	309.19	427.00
204	RAILWAYS	NFR	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	1,500.00	4,996.19	3,410.06	3,496.00
205	RAILWAYS	NER	KANPUR-KASGANJ-MATHURA(GC),NER	677.97	1,651.54	1,621.40	974.00
206	RAILWAYS	SWR	HUBLI-ANKOLA(NL),SWR	227.00	2,135.00	31.46	1,908.00
207	RAILWAYS	SCR	NANDYAL-YERRAGUNTALA(NL),SCR	155.74	883.00	755.50	727.00
208	RAILWAYS	SR	KARUR-SALEM(NL),SR	155.55	800.00	800.66	645.00
209	RAILWAYS	NR	NANGALDAM-TALWARA(NL),NR	450.00	2,100.00	391.95	1,650.00
210	RAILWAYS	SWR	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	295.00	1,289.92	872.28	995.00
211	RAILWAYS	M RTP	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	495.44	1,781.98	436.79	1,287.00
212	RAILWAYS	RVNL	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	304.00	968.60	0.00	665.00
213	RAILWAYS	NR	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	2,500.00	19,565.00	10,658.34	17,065.00
214	RAILWAYS	SCR	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	124.43	925.30	712.02	801.00
215	RAILWAYS	WR	VIRAMGAM-BHILDI(WR),GC	155.66	548.01	201.26	392.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
216	ROAD TRANSPORT AND HIGHWAYS	NHAI	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	157.47	154.57	228.30	71.00
217	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI TO BIJNI (AS-8)	200.00	200.00	281.60	82.00
218	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING WITH PS KHAGARIA-PURNEA	664.00	664.00	776.40	112.00
219	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING OF SHILONG BYPASS	226.00	226.00	282.30	56.00
220	ROAD TRANSPORT AND HIGHWAYS	NHAI	PANIPAT-ROHTAK	807.00	807.00	1,209.43	402.00
221	ROAD TRANSPORT AND HIGHWAYS	NHAI	KUNDUPUR-SURATHKAL & MANGLORE	671.00	671.00	1,273.00	602.00
222	ROAD TRANSPORT AND HIGHWAYS	NHAI	ARMUR TO KADLOOR YELLAREDDY	390.56	390.56	631.70	241.00
223	ROAD TRANSPORT AND HIGHWAYS	NHAI	HAZARIBAGH-RANCHI	625.07	625.07	995.90	371.00
224	ROAD TRANSPORT AND HIGHWAYS	NHAI	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	1,108.00	2,288.00	0.00	1,180.00
225	ROAD TRANSPORT AND HIGHWAYS	NHAI	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	1,693.75	1,693.75	2,762.00	1,068.00
226	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHAMBAL BRIDGE, NH-76 (RJ-5)	275.00	281.31	0.00	6.00
227	ROAD TRANSPORT AND HIGHWAYS	NHAI	BRAHMPUTRA BRIDGE,NH NO-31	217.61	309.56	0.00	92.00
228	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG, NH-54	196.00	331.23	0.00	135.00

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
229	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHARAMTUL TO SONAPUR (AS-19)	200.00	200.00	289.50	90.00
230	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUWAHATI TO NALBARI (AS-5)	198.16	198.16	242.40	44.00
231	ROAD TRANSPORT AND HIGHWAYS	NHAI	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	155.00	201.66	0.00	47.00
232	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	199.81	385.13	0.00	185.00
233	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	155.04	280.13	0.00	125.00
234	ROAD TRANSPORT AND HIGHWAYS	NHAI	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	251.03	251.03	326.30	75.00
235	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	280.00	361.00	0.00	81.00
236	SHIPPING AND PORTS	MUMBAI PORT TRU	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	1,228.00	1,460.00	937.28	232.00
237	SHIPPING AND PORTS	PORT TRUST	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	150.00	600.00	139.80	450.00
238	SHIPPING AND PORTS	RVNL	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	245.67	373.22	351.18	128.00
239	SHIPPING AND PORTS	MUMBAI PORT TRU	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	366.39	669.46	407.33	303.00
240	STEEL	RINL	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	8,692.00	12,291.00	11,325.64	3,599.00
241	STEEL	RINL	REVAMPING OF SINTER MACHINES - 1 AND 2	343.00	488.40	25.02	145.00
242	URBAN DEVELOPMENT	M RTP	BANGALORE METRO RAIL PROJECT	6,395.00	11,609.00	2,267.57	5,214.00
			TOTAL	268,343.66	480,735.63	267,245.48	218,738.00

Details of Delayed Projects w.r.t. Original and Revised Schedule

(May 2015)

						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	18,632.00	12/2008 -	09/2015	81	31.12	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	6,667.00	12/2015 -	10/2017	22	0	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,508.00	12/2016 -	05/2018	17	0	
	Total		36,950.00 -	41,049.00	29,807.00					
	<u>CIVIL AVIATION</u>									
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	489.00	433.99	03/2015 -	05/2015	2	8.19	
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	60.84	03/2014 -	05/2015	14	0	
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	0	
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	341.54	01/2011 06/2016	06/2017	77	0	
	Total		1,323.34 -	1,360.34	836.41					
	<u>COAL</u>									

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,583.77	3,212.02	06/2009 03/2013	06/2015	72	76.47	Unit I -The unit was under shutdown from 13.03.2015 due to the fire in the area of SUB 3 & 4 suspecting refractory failure and economizer puncture. The refractory work rectification completed. Load rising activity could not be carried out due to suction pressure in the ID Fan duct. Modification proposals are finalized in the ID fan duct. Modification of Duct involves erection of 140 Tons of ducts and structural materials. The materials required for erection are being received.
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,223.31	03/2012 05/2014	06/2015	39	34.63	The delay in late finalisation of sub-contractor by M/s BHEL, inadequate mobilization of resources by the contractor and slow progress of civil & structural fabrication & erection and TG erection in unit I & unit II.
10	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	136.88	10/2014 -	06/2015	8	0	Delay in acquisition of private land Delay in supply of equipment Delay in civil works Delay in equipment erection.
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.58	03/2013 09/2012	09/2015	30	478.5	Delay in drivage of gate roadways due to adverse geomining conditions.
12	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,817.84	03/2014 -	03/2016	24	0	
13	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,663.41	03/2014 -	03/2016	24	0	
14	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 -	741.62	471.37	03/2013 -	03/2016	36	-6.11	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
15	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	369.72	03/2015 -	03/2016	12	-28.27	
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	76.55	07/2012 -	03/2016	44	50.37	
17	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	15.49	03/2012 -	03/2016	48	0	
18	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.60	03/2014 -	03/2016	24	0	
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	55.60	03/2014 -	03/2016	24	0	(1)Delay in finalization of Global tender. (2) Delay in rehabilitation and Resettlement activity due to resistance by villagers.
20	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.28	03/2012 -	03/2016	48	0	
21	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48	0	-
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.92	03/2011 -	03/2016	60	0	
23	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	143.74	03/2012 -	03/2016	48	0	
24	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	10.00	04/2014 03/2016	03/2016	23	0	
25	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	75.50	03/2015 -	04/2016	13	0	-
26	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	11/2012	289.45 -	289.45	86.62	05/2014 -	04/2016	23	0	
27	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	30.35	04/2014 -	04/2016	24	0	
28	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	143.97	03/2010 -	03/2017	84	0	Coal Evacuation problem
29	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	121.94	03/2011 -	03/2017	72	-27.57	i)Law & Order ii) Coal evacuation problems
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	144.92	03/2011 -	03/2017	72	0	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	172.18	03/2013 -	03/2017	48	0	i) Environmental Clearance ii) Coal evacuation Problems ii) Rehabilitations & Resettlement Problems
32	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.02	03/2010 -	03/2017	84	0	Rehabilitations & Resettlement Issues
33	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	99.05	12/2012 -	03/2017	51	0	-
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	191.16	03/2012 -	03/2017	60	0	i) Environmental Clearance ii) Delay in forest land Diversion
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	173.03	03/2013 -	03/2017	48	0	Environmental Clearance
36	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCCL, JHARKHAND	12/2007	179.87 -	179.87	80.29	03/2012 -	03/2017	60	0	i) Rehabilitations & Resettlement Problems ii) Law & order iii) Coal evacuation problems
37	PURNADIH OCP (3.0 MTY) - [N06000085]JCCL, JHARKHAND	07/2008	210.98 -	210.98	144.43	03/2013 -	03/2017	48	0	
38	KARMA OCP (1.0 MTY) - [N06000088]JCCL, JHARKHAND	06/2009	162.46 -	162.46	65.84	03/2014 -	03/2017	36	0	
39	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	0	-
40	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	11.44	07/2016 -	03/2017	8	0	-
41	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	71.33	03/2012 -	03/2018	72	0	Inconsistent seam thickness of seam envisaged in the Project.
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	206.52	03/2014 -	03/2018	48	0	
43	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	
44	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	
45	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	924.23	12/2015 04/2018	04/2018	28	0	Re-tendering of Steam Generator & Auxiliaries package incorporating changes in specification.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
46	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2019	48	0	
47	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	42.39	04/2015 04/2019	04/2019	48	0	
48	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.58	03/2016 -	03/2020	48	0	Delay in Environment and forestry Clearance.
49	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	
51	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	77.18	03/2015 -	03/2021	72	0	i) Rehabilitation & resettlement problems. ii) Environmental clearance
	Total		31,052.51 -	35,167.14	18,899.00					
	STEEL									
52	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	381.47	09/2009 05/2012	06/2015	69	-6.25	
53	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	460.80	04/2013 09/2014	06/2015	26	0	
54	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,615.92	12/2012 -	06/2015	30	0	
55	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	126.73	11/2013 -	06/2015	19	0	
56	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	178.95	08/2014 -	06/2015	10	0	
57	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	130.43	09/2014 -	06/2015	9	0	
58	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00 -	677.00	515.80	09/2013 -	06/2015	21	0	
59	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,133.16	12/2011 -	08/2015	44	0	
60	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	383.87	05/2013 01/2015	08/2015	27	0	

(May 2015)

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
61	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	176.42	12/2014 -	09/2015	9	0	
62	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	154.93	10/2013 -	12/2015	26	0	
63	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	240.95	06/2015 -	12/2015	6	0	
64	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,462.86	03/2013 -	03/2016	36	0	
65	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	201.36	07/2015 -	03/2016	8	0	
66	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,005.70	05/2015 12/2016	12/2016	19	0	
67	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	151.54	07/2015 -	03/2017	20	0	
	Total		47,384.59 -	47,354.59	32,320.89					
	<u>PETROCHEMICALS</u>									
68	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,648.40	04/2012 12/2013	06/2015	38	80.08	•
	Total		5,460.61 -	9,833.52	8,648.40					
	<u>PETROLEUM</u>									

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
69	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 04/2016	06/2015	110	820.2	LSTK contract was terminated on 04.06.07 due to non performance by the contractor M/s CEL, Australia . Prolonged legal battle between ONGC, CEL and delay in Arbitration proceedings. Complication in well G-1-9 and well control activities.
70	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	225.72	08/2012 06/2015	06/2015	34	-11.94	Reasons for delay: -Construction of activities hampered due to ROU related issues. -Marshy and highly undulating terrain resulting in poor progress in pipeline laying work. -Some additional work included (up gradation of fire fighting system).
71	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,343.65	12/2012 -	06/2015	30	0	
72	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,151.94	12/2014 -	06/2015	6	0	
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,078.77	10/2011 -	06/2015	44	75.35	Completion delayed primarily because the rectification of rock wedge failure in cavern A1 took more time.Zones of poor geology encountered during excavation of balance bench.Slow construction progress of AG facility Works as it was dependent on completion of UG works.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
74	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 07/2015	07/2015	23	-18.75	- Delay in award of work. - Slow progress by the contractors. -Custom bond issue with M/S SHM Shipcare and some vessels of M/s Abu Dhabi waiting for customs and DGFT clearances.
75	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,720.30	05/2015 05/2015	07/2015	2	0	1- Delay due to Non availability of umbilical line in pipeline package.
76	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	155.32	12/2014 -	07/2015	7	0	Pre-commissioning activities are in progress. Hook up shutdown for Mounded bullet pipelines are to be done during existing refinery-III S/d which is planned in July 2015
77	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	184.18	07/2013 -	07/2015	24	20.02	
78	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	-38.7	-Commissioning is pending as NOC is awaited from the MOD (air force)
79	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,101.07	11/2012 11/2013	10/2015	35	16.05	
80	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRIL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	951.70	10/2011 -	10/2015	48	67.62	Delay in finalization of crude filling and evacuation philosophy for Mangalore project. Delayed land acquisition for Mangalore.Delay in award.Slow construction progress of AG works

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
81	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45	70.49	Delay in getting Order for Mangalore-Padur pipeline.Delay in preparation/approval of DFR.Delay in land acquisition. Delay in site surveys. Delay in finalization of Basic Engg and Detailed Engg.Delay in finalization of crude filling and evacuation philosophy
82	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	-	10/2014 10/2015	10/2015	12	0	-
83	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13	Delay in placement of order for 2 nos drilling rigs. One of the bidder went to court in anticipation of disqualification of their bid
84	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015	51	0	-Delay in preparation of drawing and additional model testing of Hull form in Austria . - Shortage of skilled manpower at contractors end. - Inadequate ancillary/sub-contractors at the location -Lack of planning to match resources to work targets. - Change in delivery location. -Delay in procurement of steel by PSL.
85	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,220.38	08/2015 -	12/2015	4	0	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
86	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,338.05	01/2014 12/2015	12/2015	23	0	Slow progress by contractor. - Slow progress by the contractor in laying of pipelines. - Delay in conversion work of Sagar Samrat to MOPU. - Delay in drilling of some wells due to non-availability of light rig.
87	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	114.88	09/2012 04/2015	12/2015	39	-24.14	-Slow progress in civil work and fabrication work due to less resource mobilization. -Unresolved commercial issues between M/s UEM and NSF Vendor. -Delay in finalization of Process package leading to delay in engg and procurement services. -Delay in delivery of Nut Shell filters and internal of IGF units.
88	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 958.55	958.55	843.52	05/2013 06/2014	12/2015	31	11.23	-Increase in scope of work -Delay in procurement of steel and fabrication of legs by the contractor.
89	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	306.82	08/2015 -	12/2015	4	0	
90	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	432.97	04/2015 04/2015	12/2015	8	-39.69	
91	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	85.27	05/2015 -	12/2015	7	0	
92	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	220.47	03/2015 11/2015	02/2016	11	37.72	Heavy rain in Assam.Refloating of tender will have impact on timeline
93	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,123.79	09/2012 -	03/2016	42	0	

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
94	VKPL UPGADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32	463.32	279.14	06/2011 03/2012	03/2016	57	0	
95	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,201.17	03/2015 05/2016	05/2016	14	29.42	Pipeline package: Non-performance by the contractor: : The contractor of pipeline package has served notice of termination of the contract on 11.01.2014 and again on 07.03.2014 in view of contractors inability to execute the work on time. -Delay in conversion of Rig Sagar Laxmi to MOPU due to financial issues and non-performance of the contractor.
96	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	539.15	05/2014 05/2016	05/2016	24	0	Package-1 delayed due to representation by M/s Essar in IEM. -Slow progress by contractor.
97	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	progress is held up due to Non-performance by the contractor. Arbitration case is already filed by contractor.
98	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49	352.49	122.87	03/2014 05/2016	05/2016	26	0	-Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. - Clubbing of project facilities alongwith C-26 Cluster development project. - slow progress by the contractor.
99	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49	352.49	122.87	03/2014	05/2016	26	0	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
100	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]OCL,MULTI STATE	02/2011	913.00 -	913.00	403.07	08/2015 -	06/2016	10	0	
101	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	625.93	11/2015 07/2016	07/2016	8	0	Restricted working environment due to nearby operating plants, availability of limited space for storage & fabrication, Restricted timings for radiography activities etc.. were affecting the progress of the work.
102	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	222.98	10/2014 10/2016	10/2016	24	49.38	
103	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	461.00	11/2015 11/2016	11/2016	12	25.84	
104	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,777.84	03/2013 03/2016	03/2017	48	-3.5	-Substantial time taken for mobilization by survey and other agency. -ROU acquisition and issue related to payment -Delay in forest clearance. -Inadequate manpower at working sites affected the construction progress. -Local problem and court cases by tea gardener. -Slow progress in engineering and procurement.
105	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2017	12	0	RETENDERING
106	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	Delay due to re tendering.
107	LPG TERMINAL AT KOCHI - [N16000171]OCL,KERALA	12/2012	607.06 607.06	607.06	57.83	01/2016 07/2017	07/2017	18	0	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
108	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 11/2017	06/2018	53	-6.92	- Retendering (2times). -Slow progress in engineering and procurement resulting in termination of contract. -Bid was not Techno-Commercially acceptable.
109	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	3,957.00	4.99	01/2013 -	12/2018	71	-47.91	
	Total		82,753.10 -	89,307.41	55,775.23					
	<u>POWER</u>									
110	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	311.69	12/2014 -	05/2015	5	22.52	
111	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,622.00	04/2009 -	06/2015	74	59.48	Geological surprises leading to huge change in scope. Contractual issues with M/s ITD leading to slow down of work & intermittent stoppage of work.
112	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,316.76	12/2013 04/2015	06/2015	18	17.57	Delayed due to delay in land acquisition.
113	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	196.14	03/2014 -	06/2015	15	0	
114	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,703.27	11/2012 -	07/2015	32	0	Delayed in forest clearance & land acquisition for Vindhyachal S/stn.
115	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	912.03	07/2013 -	08/2015	25	139.35	
116	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,796.47	03/2014 06/2015	08/2015	17	20.87	Forest clearance (wildlife sanctuary) delayed & severe ROW problem faced at Bhiwani end.

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
117	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	750.88	03/2015 -	09/2015	6	0	Delayed due to delay in land acquisition of Kudgi s/stn. (land acquired in Feb 14).
118	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,834.94	03/2013 06/2015	09/2015	30	13.18	Forest clearance delayed & severe ROW problem at Angul end in Odisha.
119	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,718.80	12/2013 -	09/2015	21	0	Forest clearance delayed (received in Feb'15).
120	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	127.70	01/2013 -	09/2015	32	0	Delayed land acquisition of Kishanganj S/stn. (acquired in Aug 13).
121	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,873.86	08/2014 -	09/2015	13	0	Delayed due to delay in forest clearance.
122	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	508.90	02/2014 -	09/2015	19	0	Severe ROW problem.
123	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,503.07	10/2014 -	09/2015	11	0	Severe ROW problem faced.
124	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,067.98	11/2014 -	09/2015	10	0	Severe ROW problem in Andhra Pradesh.
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	184.52	04/2015 -	09/2015	5	0	Delayed land acquisition of Varansai S/stn.
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	482.22	07/2013 05/2015	11/2015	28	-8.45	Forest clearance delayed (awaited) & Limited working period due to snow-bound area & flood.
127	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	992.61	12/2007 12/2009	12/2015	96	0	Severe ROW problem in Karnataka.
128	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,467.86	11/2013 -	12/2015	25	0	Forest clearance awaited, ROW problem & delay in land acquisition for Kishanganj S/stn.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
129	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	445.41	11/2013 -	12/2015	25	0	Delayed due to forest clearance & delay in S/stn. land acquisition.
130	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	276.57	08/2014 06/2015	12/2015	16	16.63	Severe ROW problem in Karnataka.
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	509.32	11/2014 -	12/2015	13	0	Forest clearance delayed & severe ROW problem.
132	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	121.50	06/2015 -	12/2015	6	0	
133	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	718.73	06/2015 -	12/2015	6	0	Forest clearance awaited & contractual issue in 01 package.
134	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,891.95	09/2008 03/2012	03/2016	90	21.34	Severe ROW problem faced in Kerala. Work to start after assessment of compensation & payment by state govt./KSEB.
135	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	520.09	09/2010 06/2013	03/2016	66	51.1	Forest clearance awaited & severe ROW problem in almost all locations. Balance portion of LIL0 at Navi Mumbai line is being completed using underground cable. However ROW problem for laying of cable continue. Critical.
136	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,025.79	08/2013 -	03/2016	31	159.15	Law & order problem from time to time and change in geotechnical parameters necessitating revision of side slopes.

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
137	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	463.66	11/2011 -	03/2016	52	0	Severe ROW problem in Western U.P. (near Bagpat etc.) due to farmers agitations & high compensation demand. Land acquisition of Dehradun S/stn. was also delayed.
138	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	326.77	02/2012 -	03/2016	49	0	Severe ROW problem in western UP.
139	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,078.18	10/2012 -	03/2016	41	0	Forest clearance awaited & contractual issues.
140	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,590.30	08/2013 -	03/2016	31	0	Law & order problem & Gen. project also delayed.
141	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,439.25	01/2015 -	03/2016	14	0	Involved wildlife Sanctuary. Delay in land acquisition (patly land acquired) and Gen. project also delayed.
142	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,128.20	12/2012 -	03/2016	39	0	Forest clearance delayed, compensation issue by land owners & Poor performance by contractor.
143	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,051.79	08/2012 -	03/2016	43	0	Delayed due to contractual/ legal issues arising out of change of ownership due to poor performance of the executing contractor.
144	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	729.24	11/2012 -	03/2016	40	0	Severe ROW problem in western UP (farmers agitation) & high compensation demand.
145	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,274.62	04/2013 -	03/2016	35	0	Severe ROW problem in Roorkee-Saharanpur line in western UP due to farmer agitation & high compensation demand.
146	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,704.45	05/2014 -	03/2016	22	0	Delayed due to delay in land acquisition of Champa Sub station.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
147	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,182.93	07/2014 -	03/2016	20	0	Forest clearance awaited and severe ROW problem (routing of line through Grape garden)
148	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL, CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,155.03	08/2014 12/2015	03/2016	19	27.6	Forest clearance awaited.
149	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,105.42	01/2015 -	03/2016	14	0	Forest clearance awaited.
150	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,319.89	06/2015 -	03/2016	9	0	Delay in land acquisition for Champa HVDC station & forest clearance awaited.
151	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44 -	3,201.44	2,331.11	10/2014 -	03/2016	17	0	Delay in land acquisition for Kanpur Sub station. Completion matching with Sub station.
152	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL, MULTI STATE	03/2013	2,514.88 -	2,514.88	680.95	12/2015 -	03/2016	3	0	Severe ROW Problem and huge forest involvement. Processing of forest case very slow
153	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	3,984.03	2,871.00	01/2013 -	03/2016	38	0	
154	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,762.59	09/2009 -	06/2016	81	81.76	Financial crunch with M/s HCC affected work progress
155	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,804.46	09/2014 -	06/2016	21	0	Severe ROW problem & contractual issue in 01 line.
156	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	73.73	09/2014 -	06/2016	21	0	Severe ROW problem are being encountered across the TL.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
157	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	822.11	07/2006 12/2015	10/2016	123	274.73	Lack of sufficient labourers available to the Package Contractor.
158	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,952.20	01/2016 -	11/2016	10	50.95	Work stopped at all front from 14.03.2015 consequent to retrenchment notice of manpower issued by M/s HCC. Work resumed at Dam site on 11.04.2015 and at Power House on 15.04.2015 after continuous meeting through District Administration with PAFs.
159	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,082.63	11/2012 -	12/2016	49	0	Land acquisition for sub stations delayed (Daltonganj s/stn. land yet to be acquired).
160	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,899.87	12/2009 03/2017	03/2017	87	159.38	Permission for Quarry operation yet to be received from Govt. of Arunachal Pradesh.
161	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,243.00	09/2011 -	03/2017	66	54.25	Inadequate deployment of manpower & resources by M/s BHEL and its sub-agencies have affected the erection/commissioning progress of U#1. •Frequent Bandh calls by local outfits (Total Bandh-262 days) leading to stoppage of work at site for more than 500 days. •Eruption of ethnic violence in Jul-12, May-14 & Dec-14 (41 days) leading to stoppage of work for 171 days. •Poor performance of BOP/Civil contractors due to geo-political situation in the region.
162	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,678.00	05/2014 -	06/2017	37	0	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
163	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,843.00	11/2016 -	08/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
164	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	25.99	02/2014 -	09/2017	43	0	
165	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,400.00	12/2016 -	09/2017	9	0	
166	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,850.00	12/2009 10/2014	03/2018	99	73.65	Non performance of Russian agency M/s TPE & M/s PM. TPE stopped work from Oct-2013 and the contract of M/s TPE was terminated on 14.01.15.
167	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,235.17	07/2010 02/2016	05/2018	94	79.77	1. Non availability of Asena Quarry 2.Regular hindrances in Chopra dumping area 3.Fund crises with HCC civil contractor.
168	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	641.42	07/2014 11/2018	11/2018	52	50.31	
169	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,531.72	5,079.93	09/2009 -	12/2018	111	92.16	Three major slides in PH area and subsequent stabilization of back hill slope. Cash crunch with M/s Coastal Project Ltd. resulting in complete stoppage of work in Sainj Valley from 6th Jan' 14 to 9th Oct. 14.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
170	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,460.00	03/2013 -	12/2018	69	29.14	-Flash Flood in Jun-12 in Uttarakhand leading to damage of coffer dam & approach road. -TBM stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. -HRT Package is under retender & expected to be awarded shortly. The completion schedule is 3 years after award of HRT Package.
171	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	360.52	06/2014 -	03/2016	21	0	Severe ROW problem. Critical
	Total		151,602.03 -	181,551.24	125,528.47					
	<u>HEAVY INDUSTRY</u>									
172	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	
	Total		1,718.00 -	3,827.30	.00					
	<u>RAILWAYS</u>									
173	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	300.67	
174	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MYSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	606.08	03/2013 -	09/2015	30	81.45	
175	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	0	
176	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	104.49	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
177	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
178	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,491.45	10/2007 12/2012	12/2015	98	367.76	Not Reported
179	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	16.41	
180	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	436.79	03/2004 12/2010	03/2016	144	259.68	Fund & land constraint (to be given by CIDCO) affecting the progress of projects.
181	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	03/2016	121	6.99	Work has been affected frequently due to local disturbances. Progress is slow due to explosive stocking is not allowed by SP
182	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defrozen and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut - Saharanpur).

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.37	03/2014 -	03/2016	24	-9.96	Works may be suffered due to land availability constraints and shifting of services by State Govt.
184	KATAKHAL TO BHAIKABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	
185	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	State Govt. is yet to form guidelines for land acquisition as per new Act in Karimganj District, Assam for Karimganj-Maishashan section and Baraigram-Dullabchera section.
186	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	Work delayed due to foundation problem.
187	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
188	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	201.88	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
189	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
190	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	
191	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	0	Not Reported
192	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	
193	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
194	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
195	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
196	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
197	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	
198	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
199	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,431.72	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
200	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Progress is undergoing as per the allotment of budget grant.
201	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
202	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
203	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected the work progress in Rangchong and Kalimpong (West Bengal).
204	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		28,013.16 -	84,366.38	37,075.14					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
205	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	83	0	
206	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	28	0	

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
207	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	-	05/2008 06/2015	06/2015	85	0	
208	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	07/2015	15	0	
209	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	0	Project abandoned by contractor
210	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	0	
211	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2015	52	0	
212	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29	0	
213	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	0	
214	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	0	Land acquisition Forest clearance Poor progress by the contractor
215	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 01/2016	01/2016	69	42.25	
216	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	0	Funds constraint of contractor
217	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	0	
218	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0	
219	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0	
220	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.19	269.40	09/2007 -	09/2017	120	.01	
	Total		13,301.24 -	13,393.22	9,513.70					
	SHIPPING AND PORTS									

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
221	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.00	669.46	407.33	12/2010 -	01/2016	61	82.72	
	Total		366.39 -	669.46	407.33					
	<u>TELECOMMUNICATIONS</u>									
222	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	55.22	10/2010 08/2015	09/2015	59	0	
	Total		384.00 -	384.00	55.22					
	<u>URBAN DEVELOPMENT</u>									
223	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	639.78	09/2014 -	05/2015	8	0	
224	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36	0	Progress of balance work was hampered due to heavy rains and consequent water logging of site and change in decision by the Client department. Scheme of Electrical Services particularly HVAC work was changed after detailed elaboration and award of work was delayed due to General Election in May 2014.
225	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	Finalization of flooring work in 1st year lab building and approval of sample flat for Grade- A qtr from client awaited.
226	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	-	06/2015 -	08/2015	2	0	Initial Delay due to time taken in finalisation of Drawings by Architect/ Client
227	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	0	

(May 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
228	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	0	Initial delay of 1 year in availability of site, subsequent delay due to non-uniform flow of funds during 2012-13 & 2013-14, delay in finalization of interior scheme, non-availability of full site till date, non-performance of Interior Agency
229	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
230	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	Extra time involved in finalization of tender for addressing certain issues of client department.
231	2000 BOYS HOSTEL(1000 DOWNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
232	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,749.25	12/2015 -	08/2016	8	0	
233	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9	0	
234	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	-	12/2014 -	12/2016	24	0	
235	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	12/2016	3	0	NR
236	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0	
237	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	0	The work was terminated on 24-07-2014 because of the non performance of the contractor for the first package. However, the tender for balance items of the package I along with package III has been awarded and work started at site.

(May 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		82,266.25	82,266.25	19,506.14					
	Grand Total		482,575.22	590,529.85	338,372.93					

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	03/2015 -	05/2015	0/0
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	05/2015	0/0
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	06/2017	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- 09/2018	09/2018	0/0
7	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-	0/0
	Total		2,599.56 -			0/0
	<u>COAL</u>					
8	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	11/2012	289.45 -	05/2014 -	04/2016	0/0
9	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2016	0/0
10	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 04/2017	04/2017	0/0
11	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	03/2018 -	03/2018	0/0
12	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	03/2019 -	03/2019	0/0
13	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 04/2019	04/2019	0/0
14	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	03/2020 -	03/2020	0/0
15	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	03/2021 -	03/2021	0/0
16	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	03/2021 -	03/2021	0/0
17	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	03/2023 -	03/2023	0/0
	Total		4,784.35 -			0/0
	<u>FERTILISERS</u>					

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
19	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		1,856.00 -			0/0
	<u>STEEL</u>					
20	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	10/2016	0/0
21	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
22	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
23	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
24	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0
	Total		5,913.68 -			0/0
	<u>PETROLEUM</u>					
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	10/2011 -	06/2015	0/0
26	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	08/2013 07/2015	07/2015	0/0
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
29	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	10/2014 10/2015	10/2015	0/0
30	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 11/2015	11/2015	0/0
31	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 12/2015	12/2015	0/0
32	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 04/2015	12/2015	0/0
33	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	02/2016	0/0
34	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	03/2014 -	05/2016	0/0

			(May 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	06/2016	0/0
36	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	11/2016 -	11/2016	0/0
37	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
38	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	01/2017 -	01/2017	0/0
39	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
40	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	09/2017 -	09/2017	0/0
41	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
42	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2018	0/0
43	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	04/2019	0/0
44	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 -	05/2019	0/0
45	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
46	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	04/2015 -	-	0/0
47	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
48	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
49	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
50	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		50,160.90 -			0/0
	<u>POWER</u>					
51	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	01/2013 -	03/2016	0/0
52	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
53	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	05/2016 -	05/2016	0/0
54	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
55	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	06/2016 -	06/2016	0/0
56	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0

				(May 2015)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
57	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	08/2016 -	08/2016	0/0
58	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
59	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	02/2017 -	02/2017	0/0
60	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	02/2017 -	02/2017	0/0
61	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	04/2017 -	04/2017	0/0
62	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	05/2017 -	05/2017	0/0
63	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	05/2017 -	05/2017	0/0
64	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	05/2014 -	06/2017	0/0
65	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	07/2017	0/0
66	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
67	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	10/2017 -	10/2017	0/0
68	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	11/2017 -	11/2017	0/0
69	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	11/2017 -	11/2017	0/0
70	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	01/2018 -	01/2018	0/0
71	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	03/2018 -	03/2018	0/0
72	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	03/2018 -	03/2018	0/0
73	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	04/2018 -	04/2018	0/0
74	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	04/2018 -	04/2018	0/0
75	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	05/2018 -	05/2018	0/0
76	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	05/2018 -	05/2018	0/0
77	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
78	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		61,947.86 -			0/0
	HEAVY INDUSTRY					

			(May 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
79	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00	09/2011	12/2017	0/0
	Total		1,718.00			0/0
	<u>RAILWAYS</u>					
80	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00	07/2008	07/2008	0/0
81	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87	-	03/2010	0/0
82	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00	-	02/2012	0/0
83	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01	06/1999	07/2012	0/0
84	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56	03/2012	12/2012	0/0
85	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT,TAMIL NADU	04/2006	495.74	06/2013	06/2013	0/0
86	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03	12/2011	11/2013	0/0
87	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43	-	02/2014	0/0
88	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42	03/2014	03/2014	0/0
89	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16	02/2009	08/2014	0/0
90	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41	03/2009	08/2014	0/0
91	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13	-	10/2014	0/0
92	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00	03/2009	12/2014	0/0
93	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02	06/2013	01/2015	0/0
94	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16	-	01/2015	0/0
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77	03/1994	03/2015	0/0
96	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74	02/2009	03/2015	0/0
97	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97	-	03/2015	0/0
98	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24	-	03/2015	0/0
99	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46	03/2007	03/2015	0/0
100	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42	-	03/2015	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
101	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	- -	03/2015	0/0
102	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
103	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONG WITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
104	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
105	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
106	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
107	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
108	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	04/1997	863.23 -	- -	06/2015	0/0
109	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	07/2015	0/0
110	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESHI-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
111	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
112	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
113	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
114	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
115	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
116	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	03/2004 12/2010	03/2016	0/0
117	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	03/2016	0/0
118	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
119	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
120	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
121	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
122	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
123	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
124	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
125	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
126	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
127	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
128	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	03/2016 -	03/2016	0/0
129	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
130	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
131	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	12/2016	0/0
132	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
133	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
134	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
135	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
136	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
137	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
138	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
139	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
140	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
141	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	04/2008 03/2014	06/2017	0/0
142	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
143	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
144	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
145	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
146	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
147	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
148	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	- -	03/2018	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
149	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
150	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
151	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0
152	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
153	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
154	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
155	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
156	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
157	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
158	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
159	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
160	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
162	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
163	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
164	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
165	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
166	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
167	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
168	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
169	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
170	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
171	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
172	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0

				(May 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
173	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
174	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
175	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
176	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
177	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
178	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
179	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
180	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
181	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
182	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
183	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
184	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
185	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
186	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
187	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
188	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
189	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
190	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
191	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
192	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
193	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
194	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
195	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
196	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
197	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
198	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	- -	-	0/0
199	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
200	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-	0/0
201	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-	0/0
202	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	- -	-	0/0
203	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	- -	-	0/0
204	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
205	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 -	- -	-	0/0
206	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
207	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
208	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	378.56 -	- -	-	0/0
209	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
210	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
211	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	404.19 -	- -	-	0/0
212	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
213	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 -	- -	-	0/0
214	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU	09/2006	456.00 -	- -	-	0/0
215	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
216	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
217	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
218	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
219	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
220	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0

				(May 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
221	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
222	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
223	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
224	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
225	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
226	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
227	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
228	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
229	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
230	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
231	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
232	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
233	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
234	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
235	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
236	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
237	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
238	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
239	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
240	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
241	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
242	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
243	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
244	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
245	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
246	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
247	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
248	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
249	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
250	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
251	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
252	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
253	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
254	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
255	NAWADA-LAXMIPUR (NL) - [N22000167]JECR,BIHAR	04/2008	620.57 -	- -	-	0/0
256	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]JECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
257	GAYA-CHATRA (NL) - [N22000169]JECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
258	BIHTA-AURANGABAD (NL) - [N22000170]JECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
259	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
260	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
261	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]JECR,BIHAR	04/2005	205.00 -	- -	-	0/0
262	MOTIHARI-SITAMARHI (NL) - [N22000174]JECR,BIHAR	04/2006	211.00 -	- -	-	0/0
263	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]JECR,BIHAR	04/2008	678.62 -	- -	-	0/0
264	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]JECR,BIHAR	04/2008	228.05 -	- -	-	0/0
265	ARARIA-SUPAUL (NL) - [N22000177]JECR,BIHAR	04/2008	304.41 -	- -	-	0/0
266	KURSELA-BIHARIGANJ (NL) - [N22000178]JECR,BIHAR	04/2008	192.56 -	- -	-	0/0
267	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]JECR,BIHAR	04/2008	281.30 -	- -	-	0/0
268	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]JECR,BIHAR	04/2004	372.14 -	- -	-	0/0

			(May 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
269	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
270	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
271	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
272	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
273	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
274	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
275	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
276	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
277	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
278	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
279	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
280	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
281	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
282	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
283	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
284	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
285	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
286	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
287	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
288	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
289	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
290	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
291	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
292	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
293	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
294	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
295	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
296	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
297	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
298	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
299	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
300	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
301	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
302	HANSIDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
303	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
304	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
305	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
306	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
307	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
308	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
309	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
310	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
311	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
312	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
313	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
314	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
315	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
316	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
317	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
318	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
319	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
320	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
321	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
322	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
323	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
324	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
325	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
326	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
327	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
328	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
329	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
330	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
331	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
332	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
333	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
334	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
335	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
336	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
337	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
338	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
339	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
340	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
341	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83	-	-	0/0
342	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54	-	-	0/0
343	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96	-	-	0/0
344	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00	-	-	0/0
345	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00	-	-	0/0
346	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00	-	-	0/0
347	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	-	-	0/0
348	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14	-	-	0/0
349	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00	-	-	0/0
350	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	-	-	0/0
351	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00	-	-	0/0
352	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	-	-	0/0
353	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93	-	-	0/0
354	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	-	-	0/0
355	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94	01/1999	-	0/0
356	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24	01/1999	-	0/0
357	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48	01/1999	-	0/0
358	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57	01/1999	-	0/0
359	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69	01/1999	-	0/0
360	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71	-	-	0/0
361	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27	-	-	0/0
362	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67	-	-	0/0
363	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00	-	-	0/0
364	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92	-	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
365	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
366	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
367	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
368	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
369	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
370	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
371	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
372	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
373	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
374	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0
375	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		172,635.63 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
376	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
377	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
378	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
379	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
380	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015	0/0
381	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015	0/0
382	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 03/2015	03/2015	0/0
383	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	03/2015	0/0
384	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 04/2015	04/2015	0/0
385	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2015	04/2015	0/0
386	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 04/2015	04/2015	0/0

				(May 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
387	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22	04/2015	04/2015	0/0
388	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00	06/2008	05/2015	0/0
389	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07	01/2013	05/2015	0/0
390	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00	05/2008	06/2015	0/0
391	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00	06/2015	06/2015	0/0
392	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00	04/2014	07/2015	0/0
393	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00	08/2015	08/2015	0/0
394	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00	02/2014	09/2015	0/0
395	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00	09/2015	09/2015	0/0
396	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00	02/2014	10/2015	0/0
397	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25	10/2015	10/2015	0/0
398	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95	11/2015	11/2015	0/0
399	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76	07/2013	12/2015	0/0
400	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70	06/2014	12/2015	0/0
401	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00	01/2013	12/2015	0/0
402	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61	04/2010	01/2016	0/0
403	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00	08/2012	03/2016	0/0
404	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	10/2014	03/2016	0/0
405	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00	06/2015	05/2016	0/0
406	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00	07/2015	06/2016	0/0
407	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60	09/2016	09/2016	0/0
408	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79	11/2016	11/2016	0/0
409	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16	09/2007	09/2017	0/0
410	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [N240106221]NHAI,UTTAR PRADESH	12/2003	155.00	09/2008	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
411	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-	0/0
412	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
413	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
414	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
415	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
416	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
417	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-	0/0
418	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0
419	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
420	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-	0/0
421	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-	0/0
422	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
423	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
424	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-	0/0
425	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-	0/0
426	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
427	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
428	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
429	NH CONNECTIVITY TO ICTT VALLARPADAU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
430	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-	0/0
431	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
432	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-	0/0
433	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-	0/0
434	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
435	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
436	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
437	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
438	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
439	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
440	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
441	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0
442	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
443	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
444	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-	0/0
445	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	-	0/0
446	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-	0/0
447	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
448	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
449	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
450	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
451	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
452	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
453	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
454	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-	0/0
455	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
456	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
457	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
458	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0

			(May 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
459	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
460	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
461	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-	0/0
462	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-	0/0
463	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	-	0/0
464	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
465	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
466	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
467	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
468	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
469	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	-	0/0
470	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	-	0/0
471	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-	0/0
472	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-	0/0
473	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
474	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0
475	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	-	0/0
476	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
477	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
478	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-	0/0
479	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-	0/0
480	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-	0/0
481	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	-	0/0
482	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0

			(May 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
483	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
484	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
485	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-	0/0
486	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	-	0/0
487	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	-	0/0
488	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	10/2013 -	-	0/0
489	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	06/2014 -	-	0/0
490	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
491	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-	0/0
492	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	09/2014 -	-	0/0
493	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	-	0/0
494	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-	0/0
495	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT (TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
496	YADGIRI-WARANGAL OF NH 202 (NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		87,249.81 -			0/0
	<u>SHIPPING AND PORTS</u>					
497	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.00	12/2010 -	01/2016	0/0
498	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
499	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-	0/0
500	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
501	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST, GUJARAT	06/2010	277.00 -	03/2012 -	-	0/0
502	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-	0/0
503	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST, GUJARAT	02/2011	830.00 -	05/2013 -	-	0/0
	Total		5,524.46 -			0/0

			(May 2015)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>TELECOMMUNICATIONS</u>					
504	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	07/2015	0/0
505	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 08/2015	09/2015	0/0
506	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-	0/0
	Total		14,795.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
507	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013	0/0
508	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014	0/0
509	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014	0/0
510	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014	0/0
511	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015	0/0
512	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015	0/0
513	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
514	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	06/2012 -	06/2015	0/0
515	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	08/2015	0/0
516	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	08/2015	0/0
517	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	10/2015	0/0
518	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 -	11/2015	0/0
519	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
520	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
521	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	05/2016	0/0
522	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
523	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
524	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	12/2016	0/0

				(May 2015)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
525	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	09/2015 -	12/2016	0/0
526	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
527	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	08/2014 -	06/2017	0/0
528	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
529	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	07/2017	0/0
530	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
531	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
532	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD, BIHAR	02/2012	171.10 -	09/2014 -	-	0/0
533	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI (IN ZONE 2 IN - [N28000082]JnNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		113,421.82 -			0/0
	Grand Total		522,804.86			0/0

Details of Projects Without Date of Commissioning

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ATOMIC ENERGY</u>				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	09/2010 09/2016	-
	Total		3,492.00 -		
	<u>CIVIL AVIATION</u>				
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-
	Total		961.61 -		
	<u>COAL</u>				
4	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	03/2015 -	03/2015
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		671.60 -		
	<u>STEEL</u>				
6	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	12/2011 01/2015	03/2015
7	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	10/2009 10/2012	04/2015
8	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	04/2015
	Total		9,488.10 -		
	<u>PETROLEUM</u>				
9	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
10	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	04/2015 -	-
11	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
12	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
13	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
14	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		16,197.83		
			-		
	<u>POWER</u>				
15	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04	10/2013	03/2015
			-	-	
16	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33	09/2010	-
			-	-	
17	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34	06/2012	-
			-	-	
18	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44	06/2014	-
			-	-	
	Total		14,065.15		
			-		
	<u>RAILWAYS</u>				
19	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00	07/2008	07/2008
			-	-	
20	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87	-	03/2010
			-	03/2010	
21	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00	-	02/2012
			-	-	
22	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01	06/1999	07/2012
			663.01	-	
23	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56	03/2012	12/2012
			-	03/2012	
24	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74	06/2013	06/2013
			-	06/2013	
25	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03	12/2011	11/2013
			-	11/2013	
26	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43	-	02/2014
			-	-	
27	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42	03/2014	03/2014
			-	-	
28	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16	02/2009	08/2014
			-	02/2009	
29	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41	03/2009	08/2014
			207.00	03/2009	
30	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13	-	10/2014
			-	10/2014	
31	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00	03/2009	12/2014
			-	12/2012	
32	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02	06/2013	01/2015
			-	-	
33	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16	-	01/2015
			-	-	
34	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77	03/1994	03/2015
			608.02	-	
35	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74	02/2009	03/2015
			164.36	-	

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
36	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2015
37	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015
38	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
39	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
40	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	- -	03/2015
41	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
42	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015
43	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
44	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015
45	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015
46	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
47	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
48	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
49	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
50	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
51	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
52	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
53	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
54	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
55	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
56	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
57	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
58	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
59	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
60	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
61	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
62	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
63	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
64	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
65	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
66	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
68	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
69	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
70	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
71	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
72	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
73	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
74	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
75	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
76	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
77	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
78	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
79	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
80	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
81	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
82	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
83	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
84	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N220000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
85	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
87	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
88	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
89	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	03/2014 -	-
90	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
91	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-
92	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
93	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
94	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
95	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	-
96	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	-
97	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	-
98	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-
99	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
100	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-
101	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-
102	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-
103	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-
104	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
105	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-
106	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-
107	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-
108	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-
109	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	- -	-
110	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
136	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
137	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
138	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
139	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
140	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
141	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
142	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
143	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
144	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
145	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
146	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
147	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
148	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
149	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
150	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
151	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
152	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
153	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
154	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
155	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
156	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHAPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
157	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
158	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
159	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
160	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
161	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
162	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
163	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
164	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
165	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
166	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
167	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
168	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
169	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
170	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
171	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
172	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
173	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
174	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
175	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
176	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
177	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
178	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
179	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
180	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
181	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
182	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
183	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
185	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
186	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
187	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
188	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
189	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
190	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
191	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
192	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
193	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
194	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
195	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
196	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
197	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
198	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
199	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
200	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
201	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
202	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
203	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
204	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
205	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
206	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
207	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
208	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
209	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
210	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
211	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
212	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
213	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
214	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
215	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
216	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
217	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
218	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
219	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
220	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
221	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
222	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
223	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
224	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
225	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
226	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
227	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
228	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
229	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
230	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
231	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
232	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
233	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
234	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
235	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
236	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
237	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
238	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
239	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
240	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
241	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
242	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
243	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
244	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUT KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
245	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
246	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
247	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
248	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-
	Total		112,128.07 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
249	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
250	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
251	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
252	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
253	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
254	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015
255	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015
256	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 03/2015	03/2015
257	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	03/2015
258	GUWHAATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 04/2015	04/2015

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
259	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2015	04/2015
260	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 04/2015	04/2015
261	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015
262	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-
263	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-
264	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
265	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
266	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
267	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
268	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
269	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-
270	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
271	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
272	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
273	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
274	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
275	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
276	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-
277	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-
278	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
279	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
280	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
281	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
282	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-
283	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
284	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
285	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
286	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	05/2012 -	-
287	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	10/2011 -	-
288	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
289	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	-
290	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	-
291	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
292	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	- -	-
293	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
294	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
295	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	03/2013 -	-
296	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
297	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	07/2013 -	-
298	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	11/2012 -	-
299	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	- -	-
300	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	09/2013 -	-
301	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
302	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
303	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
304	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	- -	-
305	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
306	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	-
307	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-
308	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	06/2013 -	-
309	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	-
310	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
311	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
312	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-
313	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
314	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
315	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
316	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
317	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
318	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
319	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-
320	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-
321	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	-
322	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
323	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
324	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
325	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
326	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
327	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	-
328	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	-
329	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-
330	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-
331	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
332	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-
333	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	-
334	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
335	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
336	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
337	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-
338	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-
339	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	-
340	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
341	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
342	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
343	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-
344	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	-
345	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	-
346	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
347	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	-
348	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
349	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-
350	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	09/2014 -	-
351	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	-
352	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	-
353	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
354	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
355	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		73,293.83 -		
	<u>SHIPPING AND PORTS</u>				
356	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
357	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-
358	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
359	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-
360	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
361	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	-
	Total		5,158.07 -		
	<u>TELECOMMUNICATIONS</u>				
362	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-
	Total		1,077.00 -		
	<u>URBAN DEVELOPMENT</u>				
363	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013
364	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014
365	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
366	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
367	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015
368	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015
369	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
370	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
371	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		10,506.59 -		
	Grand Total		247,039.85		

Details of Projects Without Original Date of Commissioning

(May 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved / Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	17.82	- 09/2018	09/2018	0(R3)	0/0
	Total		314.61 -	314.61	17.82				0/0
	<u>RAILWAYS</u>								
2	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23 -	1,072.51	888.87	- -	06/2015	-	0/0
3	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	203.40	29.81	- -	07/2015	-	0/0
4	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	0/1
5	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
6	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECON, ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
7	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
8	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
9	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
10	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N220000207]NFR, MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
11	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
12	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
13	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
14	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
15	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
16	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N220000206]NFR, MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0

(May 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved / Total
1	2	3	4	5	6	7	8	9	10
17	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
18	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL & RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
19	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
20	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
22	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
23	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
24	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.29	- -	03/2019	-	0/0
25	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
26	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
27	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
28	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		18,475.83 -	29,005.42	5,114.43				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
29	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	06/2015	-	2/3
	Total		671.00 -	671.00	1,273.00				2/3
	Grand Total		19,461.44	29,991.03	6,405.25				2/4

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(May 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	DEV OF G1 AND GS-15 (ONGCL) - [160100231	4/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 04/2016	06/2015
2	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 219.08	219.08	137.25	09/2016 -	12/2015
	Total		571.68 -	4,174.29	3,576.63		
	<u>POWER</u>						
3	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) [N18000154	10/2013	1,315.90 -	1,315.90	444.97	10/2016 -	12/2015
	Total		1,315.90 -	1,315.90	444.97		
	Grand Total		1,887.58	5,490.19	4,021.60		

List of ongoing projects having cost overrun w.r.t. to revised schedule

(May 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	09/2015	31.12
	Total		13,171.00 -	17,270.00			
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	06/2015	76.47
4	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		2,651.15 -	4,488.76			
	<u>HEAVY INDUSTRY</u>						
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
7	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	06/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
8	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
9	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	07/2015	20.02
11	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	10/2014 -	10/2015	0.00
	Total		15,206.37 -	17,623.34			
	<u>POWER</u>						
12	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
14	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
15	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
16	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
	Total		17,399.92 -	34,003.67			
	<u>RAILWAYS</u>						
17	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
18	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
19	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
20	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
22	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
23	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
24	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
25	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
26	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
27	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
28	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
29	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
30	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
31	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
32	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
33	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
34	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
35	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
36	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
37	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
38	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
39	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
40	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
41	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
42	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
43	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
44	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
45	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
46	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
47	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
48	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
49	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
50	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
51	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69	3,404.92	12/2006	-	224.37
52	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63	270.00	02/2011	-	191.48
53	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00	1,382.78	-	-	902.01
54	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90	2,371.85	03/2005 12/2008	12/2019	2,019.62
55	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56	740.00	03/2012	12/2012	210.19
56	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21	1,995.25	-	-	324.33
57	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64	1,185.64	- 09/2009	-	293.06
58	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16	288.00	02/2009 02/2009	08/2014	73.33
59	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56	6,570.75	03/2011	03/2019	803.12
60	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95	341.41	03/2012	-	5.72
61	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00	2,363.00	03/2009	12/2014	156.57
62	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47	2,921.00	10/2007	12/2015	367.76
63	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
64	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70	3,700.00	- -	03/2015	304.06
65	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19	343.00	- -	-	57.20
66	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79	1,101.16	- -	03/2017	186.92
67	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23	818.29	02/2015	-	346.59
68	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13	225.00	- -	10/2014	76.98
69	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
70	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78	810.80	- -	-	0.00
71	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62	289.93	12/2007 03/2010	-	112.22
72	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012	-	43.54
73	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56	791.59	- -	-	109.11

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	280.00	02/2006 -	03/2016	6.99
75	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
76	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
77	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
78	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
79	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
80	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
81	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
82	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
83	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
84	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
85	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
86	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
87	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
88	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
89	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
90	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
91	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
92	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
93	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
95	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06

(May 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
96	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
97	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
98	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
99	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
100	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
101	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
102	VIRAMGAM-SAMAKHALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
103	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
104	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
105	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH- UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
106	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
107	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
108	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
109	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
110	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
111	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
112	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
113	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
114	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
115	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
116	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
117	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
118	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00

(May 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
120	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
121	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
122	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
123	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
124	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
125	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
126	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
127	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
128	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
129	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
130	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
131	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
132	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
133	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
134	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
135	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
136	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
137	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
138	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
139	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
140	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
141	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
142	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
143	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
144	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
145	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
146	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
147	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
148	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
149	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
150	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
151	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
152	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
153	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
154	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
155	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
156	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
157	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
158	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
159	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
160	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
161	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
162	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
163	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
164	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
166	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
167	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
168	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
169	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
170	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
171	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
172	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
173	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		84,901.36 -	209,360.19			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
174	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10
175	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
176	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
177	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
178	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
179	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
180	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	348.19	09/2007 -	09/2017	0.01
181	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		2,717.01 -	4,476.65			
	<u>SHIPPING AND PORTS</u>						
182	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
183	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00

(May 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
184	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	-	51.92
185	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,990.06 -	3,102.68			
	<u>STEEL</u>						
186	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
187	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		152,289.09	316,472.04			

List of Projects on schedule w.r.t. Latest Schedule

(May 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	764.15	03/2023 03/2023	03/2023
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	799.08	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	208.16	03/2017 -	03/2017
4	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	112.65	03/2020 -	03/2020
5	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	221.78	03/2016 -	03/2016
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095	6/2011	5,907.11 -	5,907.11	924.23	12/2015 04/2018	04/2018
7	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	42.39	04/2015 04/2019	04/2019
8	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	486.27	69.97	03/2016 -	03/2016
9	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
10	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	12.57	03/2021 -	03/2021
11	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
12	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
13	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
14	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	6.34	03/2019 -	03/2019
15	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	156.45	03/2018 -	03/2018
17	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017
18	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2021
19	NEW MAJRI UG TO OC - [N06000128	5/2015	295.56 -	295.56	0.16	03/2019 -	03/2019
20	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	26.13	03/2021 -	03/2021
21	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	108.43	03/2021 -	03/2021

(May 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
22	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.60	03/2018 -	03/2018
23	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
24	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	32.89	03/2023 -	03/2023
25	GOKUL - [N06000120]	11/2014	267.67 -	267.67	148.56	03/2018 -	03/2018
26	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	79.31	03/2021 -	03/2021
27	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020
28	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	106.77	03/2020 -	03/2020
29	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	78.34	03/2016 -	03/2016
30	MURAI DIH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	10.00	04/2014 03/2016	03/2016
31	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	79.86	03/2018 -	03/2018
32	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.83	03/2016 -	03/2016
33	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
	Total		35,124.57 -	35,019.89	4,265.54		
	<u>FERTILISERS</u>						
34	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	13.21	11/2016 -	11/2016
	Total		197.79 -	197.79	13.21		
	<u>MINES</u>						
35	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
36	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015
37	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA [N16000098]	7/2008	288.04 288.04	253.66	225.72	08/2012 06/2015	06/2015

(May 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
38	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]	11/2010	331.20 -	269.10	190.04	08/2013 07/2015	07/2015
39	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	122.87	03/2014 05/2016	05/2016
40	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	539.15	05/2014 05/2016	05/2016
41	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,201.17	03/2015 05/2016	05/2016
42	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]	6/2010	2,523.00 -	2,523.00	1,338.05	01/2014 12/2015	12/2015
43	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	6,536.23	05/2016 -	05/2016
44	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	5.37	11/2016 -	11/2016
45	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	-	05/2019 -	05/2019
46	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	-	04/2019 -	04/2019
47	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
48	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	123.67	12/2016 -	12/2016
49	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	95.53	09/2017 -	09/2017
50	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
51	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	57.83	01/2016 07/2017	07/2017
52	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
53	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015
54	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	57.16	07/2016 -	07/2016
55	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	222.98	10/2014 10/2016	10/2016
56	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	461.00	11/2015 11/2016	11/2016
57	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,049.32	11/2015 -	11/2015
58	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
59	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	112.81	01/2017 -	01/2017
60	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,118.78	05/2017 05/2017	05/2017

(May 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	625.93	11/2015 07/2016	07/2016
62	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	59.21	12/2018 -	12/2018
63	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 10/2015	10/2015
64	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	18.74	07/2016 -	07/2016
65	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	98.95	09/2017 -	09/2017
66	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	33.61	02/2016 -	02/2016
	Total		59,514.34 -	62,957.53	14,779.48		
	<u>POWER</u>						
67	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	3,899.87	12/2009 03/2017	03/2017
68	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,745.08	641.42	07/2014 11/2018	11/2018
69	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,816.00	08/2015 -	08/2015
70	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,174.00	06/2017 -	06/2017
71	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,086.00	09/2016 -	09/2016
72	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,289.00	01/2017 -	01/2017
73	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	144.00	08/2017 -	08/2017
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	230.79	03/2016 -	03/2016
75	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
76	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
77	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	49.90	12/2015 -	12/2015
78	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	63.10	08/2016 -	08/2016
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	30.70	06/2016 -	06/2016

(May 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	26.00	06/2016 -	06/2016
81	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
82	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	217.44	04/2016 -	04/2016
83	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	291.80	05/2016 -	05/2016
84	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
85	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	25.70	04/2018 -	04/2018
86	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	110.00	09/2019 -	09/2019
87	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,086.00	02/2019 -	02/2019
88	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,539.00	08/2018 -	08/2018
89	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	709.00	03/2019 -	03/2019
90	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	595.00	12/2016 -	12/2016
91	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
92	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
93	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
94	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	3,569.00	01/2018 -	01/2018
95	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
96	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
97	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
98	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
99	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	15.20	05/2018 -	05/2018
100	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017

(May 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
101	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62	871.62	1.90	11/2017	11/2017
102	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94	312.94	-	06/2016	06/2016
103	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30	1,479.30	-	05/2017	05/2017
104	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61	3,705.61	-	05/2018	05/2018
105	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58	196.58	1.40	02/2016	02/2016
106	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75	188.75	1.00	02/2017	02/2017
107	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49	288.49	12.40	02/2017	02/2017
108	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37	5,151.37	467.80	03/2018	03/2018
109	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47	400.47	1.50	04/2017	04/2017
110	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71	378.71	64.70	10/2016	10/2016
111	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57	155.57	1.00	05/2016	05/2016
112	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29	522.29	5.20	11/2016	11/2016
113	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55	11,638.55	3,246.00	09/2017	09/2017
	Total		154,433.92	159,666.86	36,418.72		
	RAILWAYS						
114	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00	1,564.54	420.71	03/2010 03/2017	03/2017
115	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51	2,913.51	551.84	03/2016	03/2016
116	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00	2,973.42	10.44	03/2015 03/2020	03/2020
117	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98	4,259.48	663.95	03/2016	03/2016

(May 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,431.72	03/2014 03/2019	03/2019
119	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016
120	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
121	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
122	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
123	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
124	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	44.04	03/2016 -	03/2016
125	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
	Total		21,518.28 -	32,196.48	6,666.97		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
126	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	-	05/2008 06/2015	06/2015
127	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	-	04/2010 01/2016	01/2016
128	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	-	08/2015 -	08/2015
129	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
130	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
131	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
132	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
133	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	-	12/2015 -	12/2015
134	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015
135	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	-	06/2015 -	06/2015
	Total		11,541.44 -	11,633.39	.00		
	<u>STEEL</u>						

(May 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016
137	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	110.34	04/2016 -	04/2016
138	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	7,005.70	05/2015 12/2016	12/2016
139	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	84.15	07/2016 -	07/2016
140	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	25.02	10/2016 -	10/2016
141	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016
142	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
143	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018
144	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
145	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017
	Total		23,648.02 -	23,793.42	7,259.52		
	<u>TELECOMMUNICATIONS</u>						
146	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
147	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
148	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
149	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
150	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019
151	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
152	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		45,907.98 -	45,907.98	.00		

(May 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		367,076.34	386,563.34	69,403.44		

List of Delayed Projects w.r.t. Latest Schedule

(May 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00	17,270.00	18,632.00	12/2008	09/2015	81	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	11,459.00	6,667.00	12/2015	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00	12,320.00	4,508.00	12/2016	05/2018	17	-
	Total		36,950.00	41,049.00	29,807.00				
	<u>CIVIL AVIATION</u>								
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00 489.00	489.00	433.99	03/2015	05/2015	2	-
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28	344.28	60.84	03/2014	05/2015	14	-
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60	217.60	0.04	03/2015	09/2015	6	-
7	C/O NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46	309.46	341.54	01/2011 06/2016	06/2017	77	12
	Total		1,323.34	1,360.34	836.41				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,583.77	3,212.02	06/2009 03/2013	06/2015	72	27
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,223.31	03/2012 05/2014	06/2015	39	13
10	WIND POWER PROJECT, KAZHUNEERKULAM, TAMIL NADU - [N060000110]NLC, TAMIL NADU	04/2012	364.75	364.75	136.88	10/2014	06/2015	8	-
11	ADRIYALA SHAFT PROJECT - [N060000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.58	03/2013 09/2012	09/2015	30	36
12	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67	2,675.67	1,817.84	03/2014	03/2016	24	-
13	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66	1,943.66	1,663.41	03/2014	03/2016	24	-
14	KRISHNASHILA (NCL) (4MTY) - [N060000007]NCL, UTTAR PRADESH	06/2011	789.88	741.62	471.37	03/2013	03/2016	36	-
15	BLOCK-B OCP NCL (3.5 MTY) - [N060000009]NCL, MADHYA PRADESH	06/2011	746.04	535.10	369.72	03/2015	03/2016	12	-
16	MAGADH OC 20 MTY (CCL) - [N060000015]JCL, JHARKHAND	08/2008	469.78	706.40	76.55	07/2012	03/2016	44	-
17	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N060000033]NCL, MADHYA PRADESH	10/2007	259.40	259.40	15.49	03/2012	03/2016	48	-

(May 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35	462.35	298.60	03/2014	03/2016	24	-
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82	153.82	55.60	03/2014	03/2016	24	-
20	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97	418.97	326.28	03/2012	03/2016	48	-
21	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48	-
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	35.92	03/2011	03/2016	60	-
23	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	143.74	03/2012	03/2016	48	-
24	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78	209.78	75.50	03/2015	04/2016	13	-
25	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	11/2012	289.45	289.45	86.62	05/2014	04/2016	23	-
26	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	30.35	04/2014	04/2016	24	-
27	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96	302.96	143.97	03/2010	03/2017	84	-
28	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	121.94	03/2011	03/2017	72	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18	287.18	144.92	03/2011	03/2017	72	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	172.18	03/2013	03/2017	48	-
31	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	148.02	03/2010	03/2017	84	-
32	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63	453.63	99.05	12/2012	03/2017	51	-
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	191.16	03/2012	03/2017	60	-
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.53	173.03	03/2013	03/2017	48	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	80.29	03/2012	03/2017	60	-
36	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	144.43	03/2013	03/2017	48	-
37	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	65.84	03/2014	03/2017	36	-
38	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	-
39	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33	417.33	11.44	07/2016	03/2017	8	-
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03	249.03	71.33	03/2012	03/2018	72	-
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50	321.50	206.52	03/2014	03/2018	48	-
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29	242.29	0.03	03/2015	03/2018	36	-
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36	-

(May 2015)

(May 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
44	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76	162.76	2.48	03/2015	03/2019	48	-
45	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.58	03/2016	03/2020	48	-
46	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	-
47	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	-
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87	395.87	77.18	03/2015	03/2021	72	-
	Total		23,575.25	27,689.88	17,922.38				
	STEEL								
49	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00	450.00	381.47	09/2009 05/2012	06/2015	69	37
50	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00	572.00	460.80	04/2013 09/2014	06/2015	26	9
51	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00	2,875.00	2,615.92	12/2012	06/2015	30	-
52	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55	254.55	126.73	11/2013	06/2015	19	-
53	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65	332.65	178.95	08/2014	06/2015	10	-
54	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48	160.48	130.43	09/2014	06/2015	9	-
55	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00	677.00	515.80	09/2013	06/2015	21	-
56	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00	6,325.00	5,133.16	12/2011	08/2015	44	-
57	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55	898.55	383.87	05/2013 01/2015	08/2015	27	7
58	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09	237.09	176.42	12/2014	09/2015	9	-
59	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33	187.33	154.93	10/2013	12/2015	26	-
60	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05	313.05	240.95	06/2015	12/2015	6	-
61	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00	17,265.00	14,462.86	03/2013	03/2016	36	-
62	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73	877.73	201.36	07/2015	03/2016	8	-
63	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16	404.16	151.54	07/2015	03/2017	20	-
	Total		31,859.59	31,829.59	25,315.19				

(May 2015)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>PETROCHEMICALS</u>								
64	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,648.40	04/2012 12/2013	06/2015	38	18
	Total		5,460.61 -	9,833.52	8,648.40				
	<u>PETROLEUM</u>								
65	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,915.00	1,343.65	12/2012 -	06/2015	30	-
66	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,151.94	12/2014 -	06/2015	6	-
67	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPL, ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,078.77	10/2011 -	06/2015	44	-
68	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,720.30	05/2015 05/2015	07/2015	2	2
69	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	155.32	12/2014 -	07/2015	7	-
70	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 -	239.73	184.18	07/2013 -	07/2015	24	-
71	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	6
72	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,101.07	11/2012 11/2013	10/2015	35	23
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	951.70	10/2011 -	10/2015	48	-
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45	-
75	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,220.38	08/2015 -	12/2015	4	-
76	CONSTRUCTION OF 6 ETSPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	114.88	09/2012 04/2015	12/2015	39	8
77	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 958.55	958.55	843.52	05/2013 06/2014	12/2015	31	18
78	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	306.82	08/2015 -	12/2015	4	-
79	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	432.97	04/2015 04/2015	12/2015	8	8
80	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	85.27	05/2015 -	12/2015	7	-
81	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 1,200.00	1,200.00	220.47	03/2015 11/2015	02/2016	11	3
82	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,123.79	09/2012 -	03/2016	42	-

(May 2015)

(May 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
83	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32	463.32	279.14	06/2011 03/2012	03/2016	57	48
84	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12
85	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49	352.49	122.87	03/2014	05/2016	26	-
86	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]OCL,MULTI STATE	02/2011	913.00	913.00	403.07	08/2015	06/2016	10	-
87	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,777.84	03/2013 03/2016	03/2017	48	12
88	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35	4,124.35	75.24	04/2016 04/2016	04/2017	12	12
89	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 11/2017	06/2018	53	7
90	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18	3,957.00	4.99	01/2013	12/2018	71	-
	Total		67,762.99	70,011.65	46,878.82				
	POWER								
91	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NNEPCO,TRIPURA	07/2012	296.87 363.73	363.73	311.69	12/2014	05/2015	5	-
92	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,622.00	04/2009	06/2015	74	-
93	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,316.76	12/2013 04/2015	06/2015	18	2
94	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78	213.78	196.14	03/2014	06/2015	15	-
95	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99	4,672.99	3,703.27	11/2012	07/2015	32	-
96	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	912.03	07/2013	08/2015	25	-
97	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,796.47	03/2014 06/2015	08/2015	17	2
98	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74	1,508.74	750.88	03/2015	09/2015	6	-
99	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,834.94	03/2013 06/2015	09/2015	30	3
100	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19	2,743.19	2,718.80	12/2013	09/2015	21	-

(May 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
101	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	127.70	01/2013 -	09/2015	32	-
102	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,873.86	08/2014 -	09/2015	13	-
103	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	508.90	02/2014 -	09/2015	19	-
104	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,503.07	10/2014 -	09/2015	11	-
105	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,067.98	11/2014 -	09/2015	10	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	184.52	04/2015 -	09/2015	5	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	482.22	07/2013 05/2015	11/2015	28	6
108	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	992.61	12/2007 12/2009	12/2015	96	72
109	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,467.86	11/2013 -	12/2015	25	-
110	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	445.41	11/2013 -	12/2015	25	-
111	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	276.57	08/2014 06/2015	12/2015	16	6
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	509.32	11/2014 -	12/2015	13	-
113	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	121.50	06/2015 -	12/2015	6	-
114	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	718.73	06/2015 -	12/2015	6	-
115	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,891.95	09/2008 03/2012	03/2016	90	48
116	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	520.09	09/2010 06/2013	03/2016	66	33
117	PARE HYDRO ELECTRIC PROJECT - [N18000045]NPEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,025.79	08/2013 -	03/2016	31	-
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	463.66	11/2011 -	03/2016	52	-
119	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	326.77	02/2012 -	03/2016	49	-

(May 2015)

(May 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,078.18	10/2012 -	03/2016	41	-
121	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,590.30	08/2013 -	03/2016	31	-
122	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,439.25	01/2015 -	03/2016	14	-
123	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,128.20	12/2012 -	03/2016	39	-
124	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,051.79	08/2012 -	03/2016	43	-
125	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	729.24	11/2012 -	03/2016	40	-
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,274.62	04/2013 -	03/2016	35	-
127	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,704.45	05/2014 -	03/2016	22	-
128	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,182.93	07/2014 -	03/2016	20	-
129	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	1,155.03	08/2014 12/2015	03/2016	19	3
130	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,105.42	01/2015 -	03/2016	14	-
131	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,319.89	06/2015 -	03/2016	9	-
132	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,331.11	10/2014 -	03/2016	17	-
133	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	680.95	12/2015 -	03/2016	3	-
134	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,871.00	01/2013 -	03/2016	38	-
135	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,762.59	09/2009 -	06/2016	81	-

(May 2015)

(May 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
136	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,804.46	09/2014 -	06/2016	21	-
137	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	73.73	09/2014 -	06/2016	21	-
138	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	822.11	07/2006 12/2015	10/2016	123	10
139	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,952.20	01/2016 -	11/2016	10	-
140	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,082.63	11/2012 -	12/2016	49	-
141	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,243.00	09/2011 -	03/2017	66	-
142	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,678.00	05/2014 -	06/2017	37	-
143	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,843.00	11/2016 -	08/2017	9	-
144	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	25.99	02/2014 -	09/2017	43	-
145	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,400.00	12/2016 -	09/2017	9	-
146	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,850.00	12/2009 10/2014	03/2018	99	41
147	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,235.17	07/2010 02/2016	05/2018	94	27
148	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,531.72	5,079.93	09/2009 -	12/2018	111	-
149	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,460.00	03/2013 -	12/2018	69	-
150	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	360.52	06/2014 -	03/2016	21	-
	Total		146,613.55 -	171,329.82	120,987.18				
	HEAVY INDUSTRY								
151	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	RAILWAYS								
152	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	51
153	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	606.08	03/2013 -	09/2015	30	-
154	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	-

(May 2015)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
155	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	-
156	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	-
157	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,491.45	10/2007 12/2012	12/2015	98	36
158	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	-
159	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	436.79	03/2004 12/2010	03/2016	144	63
160	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	03/2016	121	-
161	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
162	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.37	03/2014 -	03/2016	24	-
163	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
164	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
165	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
166	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
167	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	201.88	03/2016 -	06/2016	3	-
168	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
169	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	-
170	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
171	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
172	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
173	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
174	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
175	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
176	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
177	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-

(May 2015)

(May 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
178	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
179	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
180	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
	Total		21,538.16 -	71,842.38	34,212.27				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
181	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	83	-
182	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	28	-
183	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	07/2015	15	-
184	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	-
185	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	-
186	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2015	52	-
187	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29	-
188	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	-
189	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	-
190	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	-
191	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	-
192	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	-
193	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	-
194	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.19	269.40	09/2007 -	09/2017	120	-
	Total		12,923.63 -	12,923.66	9,513.70				
	<u>SHIPPING AND PORTS</u>								
195	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.00	669.46	407.33	12/2010 -	01/2016	61	-
	Total		366.39 -	669.46	407.33				

(May 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>TELECOMMUNICATIONS</u>								
196	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	55.22	10/2010 08/2015	09/2015	59	1
	Total		384.00 -	384.00	55.22				
	<u>URBAN DEVELOPMENT</u>								
197	FARIDABAD EXTENSION - [N28000057]DMRCL, DELHI	09/2011	2,494.00 -	2,494.00	639.78	09/2014 -	05/2015	8	-
198	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36	-
199	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
200	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	-	06/2015 -	08/2015	2	-
201	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	-
202	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	-
203	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	-
204	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
205	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
206	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,749.25	12/2015 -	08/2016	8	-
207	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9	-
208	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	-	12/2014 -	12/2016	24	-
209	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	12/2016	3	-
210	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-
211	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	-
	Total		82,266.25 -	82,266.25	19,506.14				
	Grand Total		432,741.76	525,016.85	314,090.04				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	09/2015	13171	81
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	C/O NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	06/2017	309.46	77
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	AAI	02/2010	03/2014	05/2015	344.28	14
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	AAI	10/2012	03/2015	09/2015	217.6	6

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	06/2015	2030.78	72
8	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
9	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	44
10	CHURCHA ROUG (1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
11	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
12	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
13	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
14	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
15	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2016	259.4	48
16	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
17	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
18	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	30
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	04/2016	209.78	13
20	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
21	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
22	JAGANNATHPOR OC	SECL	09/2008	03/2015	03/2020	152.43	60
23	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
24	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
25	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
26	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
27	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	06/2015	4904.54	39
28	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2019	162.76	48
29	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
30	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
31	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
32	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
33	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
34	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
35	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
36	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
37	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2016	269.82	24
38	MADHUBAND NLW WASHERY	BCCL	11/2012	05/2014	04/2016	289.45	23
39	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	06/2015	364.75	8
40	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
41	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
42	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
43	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
45	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
46	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
47	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
48	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
49	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
50	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	471.66	72

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	06/2015	5460.61	38

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	110
54	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
55	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23
56	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	10/2015	429.06	12
57	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
58	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	04/2017	4124.35	12
59	LPG TERMINAL AT KOCHI	IOCL	12/2012	01/2016	07/2017	607.06	18
60	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	10/2015	993	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
61	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	07/2013	07/2015	199.75	24
62	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	11/2015	270	41
63	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	12/2015	1138.5	8
64	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	10/2015	732	48
65	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
66	IMPROVED OIL RECOVERY OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
67	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	06/2015	672	44
69	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	24
70	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	07/2015	279	7
71	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	06/2016	913	10
72	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
73	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	BPCL	03/2012	12/2014	06/2015	1419	6
74	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
75	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
76	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	02/2016	871.35	11
77	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24
78	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
79	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	06/2015	2915	30
80	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	31
81	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	06/2018	202.94	53
82	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV)	ONGC	11/2010	08/2013	07/2015	331.2	23
83	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	09/2015	1106	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
84	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	12/2015	317.64	39
85	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA	ONGC	07/2008	08/2012	06/2015	288.04	34
86	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
87	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	29777	35
88	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
89	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	12/2015	736.65	51
90	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	7596.18	71

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
91	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
92	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	06/2015	4527.15	74
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	03/2016	509.66	52
94	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	31
95	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	11/2018	2491.58	52
96	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
97	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	66
98	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
99	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
100	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657	94
101	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	PGCIL	09/2012	03/2015	09/2015	1508.74	6
102	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	03/2016	965.58	40
103	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
104	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	03/2016	2144	39
105	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST	PGCIL	04/2010	01/2015	03/2016	4404.57	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	BENGAL AND TRANSFER OF POWER FROM B						
106	TRANSMISSION SYSTEM OF VINDHUACHAL - IV AND RIHAND -III GEN. PROJ.	PGCIL	03/2010	11/2012	07/2015	4672.99	32
107	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	25
108	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2016	11130.19	31
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2016	4824.12	41
110	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
111	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2015	297.33	16
112	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	09/2015	552.44	19
113	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	09/2015	2422.66	13
114	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	03/2016	2127.51	20
115	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2016	487.49	21
116	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	06/2015	1366.34	18
117	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	12/2015	558.26	25
118	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
119	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	03/2016	1961.87	22
120	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
121	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
122	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	06/2017	5353	37
123	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	09/2017	195.42	43
124	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	12/2015	1909.24	6
125	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2015	514.2	6
126	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
127	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	PGCIL	06/2012	11/2014	09/2015	1263.26	10
128	TR. SYS. FOR PHASE-I PROJ. IN	PGCIL	02/2012	10/2014	03/2016	3201.44	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	JHARKHAN AND WEST BENGAL PART-B						
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2015	723.63	13
130	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	03/2016	9569.76	9
131	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	PGCIL	03/2012	03/2014	06/2015	213.78	15
132	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
133	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	09/2015	1927.16	11
134	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
135	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	03/2016	1422.85	14
136	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	19
137	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
138	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	12/2015	1585.12	25
139	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	09/2015	250.03	32
140	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ. IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	17
141	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	03/2016	1677.57	35
142	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	11/2015	752.64	28
143	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	09/2015	2743.19	21
144	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	09/2015	2074.86	30
145	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.9	87
146	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	03/2018	8692.97	99
147	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
148	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	12/2015	1007.16	96
149	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	90

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
151	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144
152	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
153	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
154	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
155	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
156	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
157	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
158	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2019	5300	60
159	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
160	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
161	GOELKERA-MANOHARPUR, (LD) (SER)	SER	03/1997	02/2006	03/2016	261.7	121
162	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
163	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
164	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
165	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
166	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
167	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
168	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	09/2015	207.52	33
169	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	03/2016	2298.42	24
170	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482	30
171	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
172	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	138

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
173	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108	66
174	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
175	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2018	733	111
176	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
177	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
178	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	98
179	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	10/2015	120	82

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
180	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	06/2015	160	85
181	AGRA-BYPASS (NS-1/UP-1), NH-2, 3	NHAI	12/2003	09/2007	09/2017	348.16	120
182	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	12/2015	1693.75	52
183	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	01/2016	217.61	69
184	DHARAMTUL TO SONAPUR (AS-19)	NHAI	12/2003	06/2008	05/2015	200	83
185	HAZARIBAGH-RANCHI	NHAI	08/2010	01/2013	05/2015	625.07	28
186	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
187	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	07/2015	624	15
188	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
189	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209	35
190	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398	19
191	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2015	1100.7	18
192	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	10/2015	664	20
193	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	12/2015	1813.76	29
194	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
195	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION (KM 240-270KM)	NHAI	02/2010	08/2012	03/2016	617	43

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
196	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	01/2016	366.39	61

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
197	AUGMENTATION OF IRON ORE STORAGE IN RMHP	RINL	07/2007	09/2009	06/2015	480	69
198	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	08/2015	6325	44
199	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	03/2016	17265	36
200	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	NMDC	04/2011	04/2013	06/2015	572	26
201	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	08/2015	898.55	27
202	EXPANSION OF DURGAPUR STEEL PLANT	SAIL	08/2010	12/2012	06/2015	2875	30
203	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES	SAIL	11/2011	11/2013	06/2015	254.55	19
204	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	12/2015	187.33	26
205	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	06/2015	332.65	10
206	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	09/2015	237.09	9
207	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	SAIL	11/2012	06/2015	12/2015	313.05	6
208	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	06/2015	160.48	9
209	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
210	CAPTIVE POWER PLANT - 2	RINL	02/2011	09/2013	06/2015	677	21
211	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	03/2016	877.73	8
212	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
213	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	09/2015	384	59

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
214	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
215	FARIDABAD EXTENSION	DMRCL	09/2011	09/2014	05/2015	2494	8
216	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
217	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	06/2015	225.81	36
218	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	12/2016	156.57	15
219	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2015	270.83	11
220	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	CPWD	11/2012	02/2015	08/2015	238.43	6
221	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	11/2015	261.85	30
222	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
223	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	06/2017	884.3	34
224	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8
225	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	17270	4099

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	4904.54	6602.74	1698.2
4	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	469.78	706.4	236.62
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	2030.78	3583.77	1552.99

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9833.52	4372.91

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	672	1178.35	506.35
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
11	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
12	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
14	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
15	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	429.82	3955.21	3525.39
16	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7
17	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
20	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6476.34	3979.44
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	15300	9014.67
24	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	8692.97	15095.67	6402.7
25	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7531.72	3612.13
26	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.7	482.05
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	2569.25	3105.51	536.26
28	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	1366.34	1606.38	240.04
29	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
30	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.68	586.67
31	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	1779.29	2159.07	379.78
32	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
33	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
34	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
35	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	1657	2978.86	1321.86
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	2491.58	3745.08	1253.5
38	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	4527.15	7220	2692.85
40	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11
42	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
43	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
44	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
45	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
46	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
47	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
48	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
49	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
50	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
51	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
52	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NFR	01/2004	N.A.	915.7	3700	2784.3
53	KATAKHAL TO BHAIIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
54	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
55	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
56	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8
57	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
58	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
59	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
60	HUBLI-ANKOLA (NL), SWR	SWR	04/1997	N.A.	227	2135	1908

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
62	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
63	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
64	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
65	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
66	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
67	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	288	121.84
68	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
69	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
70	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
71	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
72	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
73	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
74	KANPUR-KASGANJ-MATHURA (GC) , NER	NER	03/1997	N.A.	677.97	1651.54	973.57
75	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
76	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER)	NER	04/1997	N.A.	863.23	1072.51	209.28
77	ETAWAH-MAINPURI (NL) , NCR	NCR	04/1997	12/2008	120	245.39	125.39
78	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
79	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
80	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
81	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
82	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
83	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
85	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
86	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
87	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
88	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
89	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
90	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
91	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
92	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
93	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
94	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
95	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
96	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
97	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
98	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
99	DALLI-RAJHARA - RAOGHAT (PART OF DALLI- RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
100	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
101	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
102	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
103	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
104	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
105	NANGALDAM-TALWARA (NL) ,NR	NR	03/1981	07/2012	450	2100	1650
106	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	645	426.76

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
108	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	847.75	222.45
109	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
111	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	270	177.37
112	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
113	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
114	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
115	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
116	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
117	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
118	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
119	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
120	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
121	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
122	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
123	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
124	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
125	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
126	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
127	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
128	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
129	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
131	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
132	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
133	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	800	644.45
134	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
135	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
136	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
137	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
138	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
139	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
140	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
141	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
142	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
143	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
144	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
145	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
146	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
147	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
148	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
149	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
150	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
151	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
152	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
154	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
155	RAMGANJ MUNDI-BHOPAL (NL), WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
156	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
157	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
158	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
159	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	19565	17065
160	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
161	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
162	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
163	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
164	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
165	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
166	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
167	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
168	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
169	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
170	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
171	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	921	2363	1442
172	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
173	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
174	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
175	NANDYAL-YERRAGUNTALA (NL), SCR	SCR	03/1996	02/2009	155.74	883	727.26

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
177	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
178	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
179	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
180	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
181	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	373.22	127.55
182	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
183	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
184	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
185	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
186	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	8692	12291	3599
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
187	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	09/2015	1,3171.00	1,7270.00	4099	81

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	06/2015	2030.78	3583.77	1552.99	72
3	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	706.40	236.62	44
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	06/2015	4904.54	6602.74	1698.2	39
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	1228.39	1016.05	30

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	06/2015	5460.61	9833.52	4372.91	38

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	3955.21	3525.39	110
9	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	462.79	152.98	24
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	02/2016	871.35	1200.00	328.65	11
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	10/2015	993.00	1693.00	700	45

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	10/2015	732.00	1227.00	495	48
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	06/2015	672.00	1178.35	506.35	44
15	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
16	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	2,9777.00	3,4555.00	4778	35

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
17	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7531.72	3612.13	111
18	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	06/2015	4527.15	7220.00	2692.85	74
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	6476.34	3979.44	87
20	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	03/2018	8692.97	1,5095.67	6402.7	99
21	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
22	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	2159.07	379.78	90
23	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	09/2015	2074.86	2348.37	273.51	30
24	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	1007.68	586.67	25
25	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	1487.49	913.5	31
26	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	11/2018	2491.58	3745.08	1253.5	52
27	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	721.81	244.12	66

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
29	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
30	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
31	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	07/2010	05/2018	1657.00	2978.86	1321.86	94
32	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
33	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	2228.70	482.05	19
34	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	06/2015	1366.34	1606.38	240.04	18
35	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	3105.51	536.26	17

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
37	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
38	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
39	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
40	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
41	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108.00	432.72	324.72	66
42	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
43	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
44	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
45	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
46	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
47	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482.00	874.57	392.57	30
48	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
49	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
50	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
51	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174
52	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
53	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
54	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
55	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
56	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
57	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
58	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
59	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
60	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	10/2015	120.00	245.39	125.39	82

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
61	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

LIST OF ROAD SECTOR PROJECTS IMPLEMENTED BY NHAI AS ON 31.05.2015 FOR WHICH CUMULATIVE EXPENDITURE HAS BEEN REPORTED ZERO									
S.NO.	PROJECT NAME	DOA	ORIGINAL DOC	REVISED /LATEST DOC	ANTICIPATED DOC	ORIGINAL COST	REVISED/LATEST COST	ALL COST IN RS. CRORE	
								ANTICIPATED COST	CUMULATIVE EXPENDITURE
1	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III	09/2013	N.A.	N.A.	N.A.	606	0	606	0
2	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	05/2014	N.A.	N.A.	1,535	0	1,535	0
3	TIRUPATI - TIRUTHANI - CHENNAI	04/2011	10/2013	N.A.	N.A.	571	0	571	0
4	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	05/2013	N.A.	N.A.	1,585	0	1,585	0
5	CHILKALURIPET-VIJAYAWADA 6 LANE (KM 355 TO KM 434.15)	05/2009	10/2011	N.A.	N.A.	572	0	572	0
6	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	04/2010	01/2016	01/2016	218	310	310	0
7	HARANGAJO TO MAIBANG, NH-54	12/2003	07/2009	N.A.	N.A.	196	0	331	0
8	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	N.A.	N.A.	212	0	212	0
9	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	06/2015	06/2015	160	0	160	0
10	NALBARI T BIJNI (AS-7)	12/2003	04/2008	04/2015	04/2015	208	230	208	0
11	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	04/2015	04/2015	225	0	225	0
12	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	03/2015	03/2015	245	0	245	0
13	NAGAON TO DHARAMTUL (AS-2)	12/2003	06/2008	N.A.	N.A.	265	0	265	0
14	GUWAHTI TO NALBARI (AS-4)	12/2003	04/2008	04/2015	04/2015	176	0	176	0
15	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	12/2003	06/2008	N.A.	N.A.	238	0	238	0
16	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12/2003	06/2008	N.A.	N.A.	195	0	195	0
17	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	04/2009	N.A.	N.A.	200	0	200	0
18	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	N.A.	N.A.	155	0	280	0
19	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	N.A.	N.A.	168	0	168	0
20	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	04/2009	N.A.	N.A.	200	0	385	0
21	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	02/2009	N.A.	N.A.	280	0	361	0
22	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	N.A.	N.A.	230	0	230	0
23	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	07/2012	07/2014	N.A.	N.A.	356	0	356	0
24	2 LANNING OF MUZAFFARPUR - SONBARSA	05/2011	11/2013	N.A.	N.A.	512	0	512	0
25	4-LANNING OF CHAPRA-HAJIPUR	01/2011	07/2013	N.A.	N.A.	575	0	575	0
26	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	04/2014	N.A.	N.A.	375	0	375	0
27	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	09/2011	03/2014	N.A.	N.A.	574	0	574	0
28	2 LANNING OF MOKAMA-MUNGER	05/2011	05/2013	N.A.	N.A.	352	0	352	0
29	PATNA-MUZAFFARPUR	08/2010	02/2013	N.A.	N.A.	671	0	671	0
30	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	12/2003	09/2008	N.A.	N.A.	333	0	333	0
31	4 LANNING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	03/2012	09/2014	N.A.	N.A.	828	0	828	0
32	AHMEDABAD TO VADODARA SECTION	01/2013	12/2015	N.A.	12/2015	2,125	0	2,125	0
33	SAMAIKHALI - GANDHIDHAM	09/2010	03/2013	N.A.	N.A.	805	0	805	0
34	KANDLA - MUNDRA PORT	01/2011	07/2013	N.A.	N.A.	954	0	954	0

35	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	03/2011	08/2013	N.A.	N.A.	786	0	786	0
36	4 LANNING OF AHMEDABAD TO GODHARA	12/2010	06/2013	N.A.	N.A.	1,009	0	1,009	0
37	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	09/2012	N.A.	N.A.	1,509	0	1,509	0
38	4-LANING OF ROHATAK JIND(LENGTH 45 KM)	10/2013	10/2015	N.A.	10/2015	283	0	283	0
39	ROHTAK-BAWAL	05/2011	11/2013	N.A.	N.A.	650	0	650	0
40	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	11/2011	N.A.	N.A.	1,108	0	2,288	0
41	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	N.A.	N.A.	486	0	486	0
42	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016	N.A.	11/2016	1,917	0	1,917	0
43	BELGAUM-DHARWAD(NH-4)	12/2010	N.A.	N.A.	N.A.	480	0	480	0
44	DEVIHALLI-HASSAN	12/2010	N.A.	N.A.	N.A.	453	0	453	0
45	FOUR LANNING OF WALAYAR-VADAKANCHERRY SECTION	04/2011	10/2013	N.A.	N.A.	682	0	682	0
46	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	03/2005	02/2010	N.A.	N.A.	557	0	557	0
47	INDORE-DEWAS(NH-3)	11/2010	05/2013	N.A.	N.A.	325	0	325	0
48	INDORE-JHABUA-GUJARAT/MP	10/2010	04/2013	N.A.	N.A.	1,175	0	1,175	0
49	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	05/2013	02/2014	N.A.	N.A.	1,348	0	1,348	0
50	PUNE-SHOLAPUR,PKG-II	09/2011	01/2014	N.A.	N.A.	835	0	835	0
51	PUNE-SATARA(NH-4)	10/2010	03/2013	N.A.	N.A.	1,725	0	1,725	0
52	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	02/2011	11/2012	N.A.	N.A.	193	0	193	0
53	TALEGAON-AMRAVATI	11/2009	11/2013	N.A.	N.A.	567	0	567	0
54	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.A.	N.A.	940	0	940	0
55	JORBAT - BARAPANI	01/2011	01/2014	N.A.	N.A.	536	0	536	0
56	PANIKHOLI-RIMOLI	03/2012	09/2014	N.A.	N.A.	1,410	0	1,410	0
57	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	11/2011	05/2014	N.A.	N.A.	909	0	909	0
58	BHUBANESWAR TO PURI	03/2011	08/2013	N.A.	N.A.	500	0	500	0
59	NIROLI-ROXY-RAJAMUNDA	07/2011	01/2014	N.A.	N.A.	586	0	586	0
60	REENGUS SIKAR	03/2012	09/2014	N.A.	N.A.	334	0	334	0
61	BEAWAR-PALI-PINDWARA	12/2011	06/2014	N.A.	N.A.	2,388	0	2,388	0
62	JAIPUR-REENGUS	08/2010	02/2013	N.A.	N.A.	268	0	268	0
63	DEOLI-KOTA	01/2011	07/2013	N.A.	N.A.	593	0	593	0
64	JAIPUR-TONK-DEOLI	06/2010	12/2012	N.A.	N.A.	792	0	792	0
65	KISHANGARH-AJMER-BEAWER	11/2009	05/2012	N.A.	N.A.	795	0	795	0
66	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	02/2010	N.A.	N.A.	275	0	281	0
67	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12/2003	10/2008	N.A.	N.A.	275	0	250	0
68	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	06/2013	11/2015	N.A.	11/2015	1,288	0	1,288	0
69	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	09/2011	08/2013	N.A.	N.A.	485	0	485	0
70	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	05/2010	05/2013	N.A.	N.A.	374	0	374	0
71	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	06/2011	06/2013	N.A.	N.A.	600	0	600	0
72	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	09/2011	12/2013	N.A.	N.A.	1,250	0	1,250	0
73	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	06/2011	12/2013	N.A.	N.A.	535	0	535	0
74	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	09/2010	03/2013	N.A.	N.A.	852	0	852	0
75	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4	09/2010	09/2013	N.A.	N.A.	1,655	0	1,655	0
76	CHENNAI-TADA(SIX LANE)	04/2009	10/2011	N.A.	N.A.	353	0	353	0
77	2 LANING WITH PS KANPUR KABRAI	01/2013	07/2014	N.A.	N.A.	373	0	373	0
78	ETAWAH CHAKERI	03/2013	09/2015	N.A.	09/2015	1,573	0	1,573	0

79	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	07/2012	01/2014	N.A.	N.A.	291	0	291	0
80	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.A.	N.A.	636	0	636	0
81	BAREILY-SITAPUR (NH-24)	03/2011	09/2013	N.A.	N.A.	1,046	0	1,046	0
82	GHAZIABAD-ALIGARH NH-91	02/2011	08/2013	N.A.	N.A.	1,141	0	1,141	0
83	MURADABAD-BAREILY	04/2010	06/2013	N.A.	N.A.	1,267	0	1,267	0
84	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	12/2003	09/2008	N.A.	N.A.	155	0	202	0
85	BARSAT-KRISHNANAGAR	08/2012	02/2015	N.A.	N.A.	867	0	867	0
86	KRISHNANAGAR-BERHAMPUR	02/2012	07/2014	N.A.	N.A.	702	0	702	0
87	6-LANING OF DHANKUNI-KHARAGPUR SECTION	04/2012	09/2014	N.A.	N.A.	1,396	0	1,396	0
88	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	04/2015	N.A.	04/2015	1,928	0	1,928	0
89	FOUR LANING OF ORISSA CHATTISHGARH BORDER	02/2013	08/2015	N.A.	08/2015	1,232	0	1,232	0
90	PANVEL-INDAPUR	12/2011	06/2014	N.A.	N.A.	943	0	943	0
91	RANCHI-RARGA-JAMSETHPUR	12/2012	06/2015	N.A.	06/2015	1,479	0	1,479	0
92	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	06/2014	N.A.	N.A.	1,047	0	1,047	0
93	4-LANING OF RAIGANJ-DALKOLA	02/2011	08/2013	N.A.	N.A.	580	0	580	0
94	4-LANING OF BRAHAMPUR-FARAKA	02/2011	08/2013	N.A.	N.A.	999	0	999	0
95	4-LANING OF FARAKA-RAIGANJ	02/2011	08/2013	N.A.	N.A.	1,079	0	1,079	0
96	MUZAFFARNAGAR-HARIDWAR	09/2011	03/2013	N.A.	N.A.	754	0	754	0
97	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	N.A.	N.A.	2,848	0	2,848	0
98	4 LANING OF NAGPUR-BETUL	02/2011	08/2014	N.A.	N.A.	2,499	0	2,499	0
99	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	12/2003	09/2010	N.A.	N.A.	232	0	232	0
100	GWALIOR-JHANSI, NH-75	12/2003	12/2009	N.A.	N.A.	604	0	604	0
101	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	11/2011	10/2013	N.A.	N.A.	478	0	478	0
102	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV	04/2014	N.A.	N.A.	N.A.	1,123	0	1,123	0
103	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	04/2014	09/2016	N.A.	09/2016	1,267	0	1,267	0

LIST OF ROAD SECTOR PROJECTS IMPLEMENTED BY NHAI AS ON 31.05.2015 FOR WHICH DATE OF COMMISSIONING HAS EXPIRED/LAPSED

ALL COST IN RS. CRORE

S.NO.	PROJECT NAME	DOA	ORIGINAL DOC	REVISED /LATEST DOC	ANTICIPATED DOC	ORIGINAL COST	REVISED/LATEST COST	ANTICIPATED COST	CUMULATIVE EXPENDITURE
1	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III	09/2013	N.A.	N.A.	N.A.	606	0	606	0
2	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	05/2014	N.A.	N.A.	1,535	0	1,535	0
3	TIRUPATI - TIRUTHANI - CHENNAI	04/2011	10/2013	N.A.	N.A.	571	0	571	0
4	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	05/2013	N.A.	N.A.	1,585	0	1,585	0
5	CHILKALURIPET-VIJAYAWADA 6 LANE (KM 355 TO KM 434.15)	05/2009	10/2011	N.A.	N.A.	572	0	572	0
6	HARANGAJO TO MAIBANG, NH-54	12/2003	07/2009	N.A.	N.A.	196	0	331	0
7	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	12/2003	09/2007	N.A.	N.A.	212	0	212	0
8	NALBARI T BIJNI (AS-7)	12/2003	04/2008	04/2015	04/2015	208	230	208	0
9	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	04/2015	04/2015	225	0	225	0
10	GUWAHATI TO NALBARI (AS-5)	12/2003	04/2008	01/2015	03/2015	198	0	198	242
11	SONAPUR TO GUWAHATI (AS-3)	12/2003	03/2008	03/2015	03/2015	245	0	245	0
12	NAGAON TO DHARAMTUL (AS-2)	12/2003	06/2008	N.A.	N.A.	265	0	265	0
13	GUWHATI TO NALBARI (AS-4)	12/2003	04/2008	04/2015	04/2015	176	0	176	0
14	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.A.	N.A.	200	0	200	282
15	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	12/2003	06/2008	N.A.	N.A.	238	0	238	0
16	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12/2003	06/2008	N.A.	N.A.	195	0	195	0
17	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	04/2009	N.A.	N.A.	200	0	200	0
18	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	N.A.	N.A.	155	0	280	0
19	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	N.A.	N.A.	168	0	168	0
20	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	04/2009	N.A.	N.A.	200	0	385	0
21	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	02/2009	N.A.	N.A.	280	0	361	0
22	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00. NH-31 C	12/2003	06/2005	N.A.	N.A.	230	0	230	0
23	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	12/2003	09/2007	03/2014	03/2015	157	157	155	228
24	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	07/2012	07/2014	N.A.	N.A.	356	0	356	0
25	2LANING WITH PS GOPALGANJ-CHAPPRA	12/2011	05/2014	N.A.	05/2014	325	0	325	160
26	2 LANNING OF MUZAFFARPUR - SONBARSA	05/2011	11/2013	N.A.	N.A.	512	0	512	0
27	4-LANNING OF CHAPRA-HAJIPUR	01/2011	07/2013	N.A.	N.A.	575	0	575	0
28	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	04/2014	N.A.	N.A.	375	0	375	0
29	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	09/2011	03/2014	N.A.	N.A.	574	0	574	0
30	2 LANNING OF MOKAMA-MUNGER	05/2011	05/2013	N.A.	N.A.	352	0	352	0
31	PATNA-MUZZAFFARPUR	08/2010	02/2013	N.A.	N.A.	671	0	671	0
32	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	12/2003	09/2008	N.A.	N.A.	333	0	333	0
33	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402.360.915	12/2003	10/2008	N.A.	N.A.	300	0	300	177
34	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	03/2012	09/2014	N.A.	N.A.	828	0	828	0
35	SAMAIKHIALI - GANDHIDHAM	09/2010	03/2013	N.A.	N.A.	805	0	805	0
36	KANDLA - MUNDRA PORT	01/2011	07/2013	N.A.	N.A.	954	0	954	0
37	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	03/2011	08/2013	N.A.	N.A.	786	0	786	0
38	4 LANNING OF AHMEDABAD TO GODHARA	12/2010	06/2013	N.A.	N.A.	1,009	0	1,009	0
39	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	09/2012	N.A.	N.A.	1,509	0	1,509	0
40	ROHTAK-BAWAL	05/2011	11/2013	N.A.	N.A.	650	0	650	0
41	PANIPAT-ROHTAK	04/2011	10/2014	N.A.	10/2014	807	0	807	1,209

42	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	11/2011	N.A.	N.A.	1,108	0	2,288	0
43	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	N.A.	N.A.	486	0	486	0
44	UGRADATION OF HYDERABAD-BANGALORE SECTION	11/2010	N.A.	N.A.	07/2014	680	0	680	188
45	BELGAUM-DHARWAD(NH-4)	12/2010	N.A.	N.A.	N.A.	480	0	480	0
46	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	03/2011	09/2013	N.A.	N.A.	359	0	359	38
47	DEVIHALLI-HASSAN	12/2010	N.A.	N.A.	N.A.	453	0	453	0
48	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	09/2010	N.A.	N.A.	N.A.	946	0	946	738
49	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	04/2011	10/2013	N.A.	N.A.	682	0	682	0
50	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH	03/2005	02/2010	N.A.	N.A.	557	0	557	0
51	INDORE-DEWAS(NH-3)	11/2010	05/2013	N.A.	N.A.	325	0	325	0
52	INDORE-JHABUA-GUJRAT/MP	10/2010	04/2013	N.A.	N.A.	1,175	0	1,175	0
53	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	12/2003	10/2008	N.A.	01/2015	251	0	251	326
54	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	05/2013	02/2014	N.A.	N.A.	1,348	0	1,348	0
55	PUNE-SHOLAPUR,PKG-II	09/2011	01/2014	N.A.	N.A.	835	0	835	0
56	PUNE-SATARA(NH-4)	10/2010	03/2013	N.A.	N.A.	1,725	0	1,725	0
57	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	02/2011	11/2012	N.A.	N.A.	193	0	193	0
58	TALEGAON-AMRAVATI	11/2009	11/2013	N.A.	N.A.	567	0	567	0
59	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.A.	N.A.	940	0	940	0
60	2-LANNING OF SHILONG BYPASS	02/2011	02/2014	N.A.	02/2014	226	0	226	282
61	JORBAT - BARAPANI	01/2011	01/2014	N.A.	N.A.	536	0	536	0
62	PANIKHOLI-RIMOLI	03/2012	09/2014	N.A.	N.A.	1,410	0	1,410	0
63	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	11/2011	05/2014	N.A.	N.A.	909	0	909	0
64	BHUBANESWAR TO PURI	03/2011	08/2013	N.A.	N.A.	500	0	500	0
65	NIROLI-ROXY-RAJAMUNDA	07/2011	01/2014	N.A.	N.A.	586	0	586	0
66	REENGUS SIKAR	03/2012	09/2014	N.A.	N.A.	334	0	334	0
67	BEAWAR-PALI-PINDWARA	12/2011	06/2014	N.A.	N.A.	2,388	0	2,388	0
68	JAIPUR-REENGUS	08/2010	02/2013	N.A.	N.A.	268	0	268	0
69	DEOLI-KOTA	01/2011	07/2013	N.A.	N.A.	593	0	593	0
70	JAIPUR-TONK-DEOLI	06/2010	12/2012	N.A.	N.A.	792	0	792	0
71	KISHANGARH-AJMER-BEAWER	11/2009	05/2012	N.A.	N.A.	795	0	795	0
72	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	02/2010	N.A.	N.A.	275	0	281	0
73	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12/2003	10/2008	N.A.	N.A.	275	0	250	0
74	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	09/2011	08/2013	N.A.	N.A.	485	0	485	0
75	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	05/2010	05/2013	N.A.	N.A.	374	0	374	0
76	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	06/2011	06/2013	N.A.	N.A.	600	0	600	0
77	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	09/2011	12/2013	N.A.	N.A.	1,250	0	1,250	0
78	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	06/2011	12/2013	N.A.	N.A.	535	0	535	0
79	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	09/2010	03/2013	N.A.	N.A.	852	0	852	0
80	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT- MADURAVOYAL NH NO.4	09/2010	09/2013	N.A.	N.A.	1,655	0	1,655	0
81	CHENNAI-TADA(SIX LANE)	04/2009	10/2011	N.A.	N.A.	353	0	353	0
82	2 LANING WITH PS KANPUR KABRAI	01/2013	07/2014	N.A.	N.A.	373	0	373	0
83	2 LANING WITH PS AGRA ALIGARH	10/2012	10/2014	N.A.	N.A.	251	0	251	65
84	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	07/2012	01/2014	N.A.	N.A.	291	0	291	0
85	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.A.	N.A.	636	0	636	0
86	BAREILY-SITAPUR (NH-24)	03/2011	09/2013	N.A.	N.A.	1,046	0	1,046	0
87	GHAZIABAD-ALIGARH NH-91	02/2011	08/2013	N.A.	N.A.	1,141	0	1,141	0
88	MURADABAD-BAREILY	04/2010	06/2013	N.A.	N.A.	1,267	0	1,267	0

89	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	12/2003	09/2008	N.A.	N.A.	155	0	202	0
90	BARSAT-KRISHNANAGAR	08/2012	02/2015	N.A.	N.A.	867	0	867	0
91	KRISHNANAGAR-BERHAMPUR	02/2012	07/2014	N.A.	N.A.	702	0	702	0
92	6-LANING OF DHANKUNI-KHARAGPUR SECTION	04/2012	09/2014	N.A.	N.A.	1,396	0	1,396	0
93	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.A.	N.A.	225	0	225	191
94	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	04/2015	N.A.	04/2015	1,928	0	1,928	0
95	PANVEL-INDAPUR	12/2011	06/2014	N.A.	N.A.	943	0	943	0
96	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	06/2014	N.A.	N.A.	1,047	0	1,047	0
97	4-LANING OF RAIGANJ-DALKOLA	02/2011	08/2013	N.A.	N.A.	580	0	580	0
98	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	N.A.	N.A.	999	0	999	0
99	4-LANING OF FARAKA-RAIGANJ	02/2011	08/2013	N.A.	N.A.	1,079	0	1,079	0
100	MUZAFFARNAGAR-HARIDWAR	09/2011	03/2013	N.A.	N.A.	754	0	754	0
101	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	N.A.	N.A.	2,848	0	2,848	0
102	4 LANING OF NAGPUR-BETUL	02/2011	08/2014	N.A.	N.A.	2,499	0	2,499	0
103	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	12/2003	09/2010	N.A.	N.A.	232	0	232	0
104	GWALIOR-JHANSI, NH-75	12/2003	12/2009	N.A.	N.A.	604	0	604	0
105	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	11/2011	10/2013	N.A.	N.A.	478	0	478	0
106	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV	04/2014	N.A.	N.A.	N.A.	1,123	0	1,123	0
107	ARMUR TO KADLOOR YELLAREDDY	02/2010	02/2012	N.A.	06/2013	391	0	391	632
