

379th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
May 2017



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
East Block-6, R. K. Puram,
New Delhi-110066
Website: www.cspm.gov.in

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for May 2017 contains information on the status of the 1252 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 26 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 26 projects, 11 are **Mega** Projects costing ₹1000 crore and above.

(ii). Total original cost of implementation of the 1252 projects was Rs. 15,64,786.27 crore and their anticipated completion cost is likely to be Rs. 17,34,083.56 crore, which reflects overall cost overruns of Rs. 1,69,297.29 crore (10.82% of original cost). The expenditure incurred on these projects till May 2017 is Rs. 6,69,895.38 crore, which is 38.63% of the anticipated cost of the projects.

(iii). Out of a total of 1252 projects, 1 project has reported completion and 4 new projects have been initiated on the monitor of this ministry during the current month. Of these, 10 projects are ahead of schedule, 313 are on schedule and 314 are delayed, 330 projects are showing cost overrun and 100 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 227 if delay is calculated with reference to latest revised schedules of completion. For 615 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 314 delayed projects, 56 projects have overall delay in the range of 1 to 12 months, 69 projects have delay in the range of 13 to 24 months, 119 projects have delay in the range of 25 to 60 months and 70 projects have delay of 61 months and above.

(v). Further, out of the 314 delayed projects, 100 projects have cost overruns. Out of these, the cost for 63 projects has been revised and for 37 projects the cost has not yet been revised. Of the 63 projects where cost has been revised, the anticipated cost of 13 projects has again exceeded the revised cost. Out of 314 delayed projects, 168 projects have not provided any milestones and in 74 cases the dates of completion of the milestones have already lapsed.

(vi). In addition to above there are 230 projects which though on schedule but are having cost overruns. Of these, the cost for 95 projects has since been revised. Of the 95 projects where cost has been revised, the anticipated cost of 38 projects has exceeded even the revised costs. Out of these 230 projects, 149 projects have not provided any milestones and for 4 projects the completion date of milestone(s) has already lapsed.

(vii). In the current month, there are 299 projects showing time overrun of more than 6 months; 235 projects showing cost overruns of more than Rs.100 crore and 77 projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore. Further, expenditure has exceeded the approved cost in 140 projects and in 899 projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimates.

3. The implementation status of **Central Sector Mega Projects** (costing Rs.1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1252 projects 367 are mega projects. Total original cost of implementation of these 367 projects was Rs. 12,04,310.30 crore and their anticipated completion cost is likely to be Rs. 13,43,873.47 crore, which reflects overall cost overruns of Rs. 1,39,563.17 crore (11.59% of original cost). The expenditure incurred on these projects till May 2017 is Rs. 5,55,873.10 crore, which is 41.36% of the anticipated cost of the projects. Out of the 367 mega projects, 131 projects have cost overruns with respect to original cost and the number of such projects decreases to 88 when cost overrun is calculated on the basis of revised cost.

(ii) Further, out of the 125 delayed mega projects, 51 projects have cost overruns. Out of these, the cost for 32 projects has been revised and for 19 projects the cost has not yet been revised. Of the 32 projects where cost has been revised, the anticipated cost of 8 projects has again exceeded the revised cost. Out of 125 delayed projects, 65 projects have not provided any milestones and in 40 cases the dates of completion of the milestones have already lapsed

iii). In addition to above there are 80 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 34 projects has since been revised. Of the 34 projects where cost has been revised, the anticipated cost of 15 projects has exceeded even the revised costs. Out of these 80 projects, 45 projects have not provided any milestones and for 3 projects the completion date of milestone(s) has already lapsed.

(iv). In the current month, there are 121 mega projects showing time overruns of more than 6 months; 122 mega projects showing cost overruns of more than Rs.100 crore and 48 mega projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore.

Further, expenditure has exceeded the approved cost in 56 mega projects and in 247 mega projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimate.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.

7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.

8. The status as on 30.04.2017 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at [www.cspm.gov.in /publication](http://www.cspm.gov.in/publication).

9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-01
SECTOR WISE DETAIL OF ADDITIONALLY DELAYED PROJECTS

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	484	0
2	RAILWAYS	348	1
3	POWER	128	6
4	PETROLEUM	95	5
5	COAL	89	3
6	STEEL	35	1
7	URBAN DEVELOPMENT	33	6
8	HEALTH AND FAMILY WELFARE	13	4
9	SHIPPING AND PORTS	8	0
10	ATOMIC ENERGY	4	0
11	MINES	4	0
12	CIVIL AVIATION	3	0
13	TELECOMMUNICATIONS	3	0
14	FERTILISERS	2	0
15	DEFENCE PRODUCTION	2	0
16	HEAVY INDUSTRY	1	0
	Total	1252	26

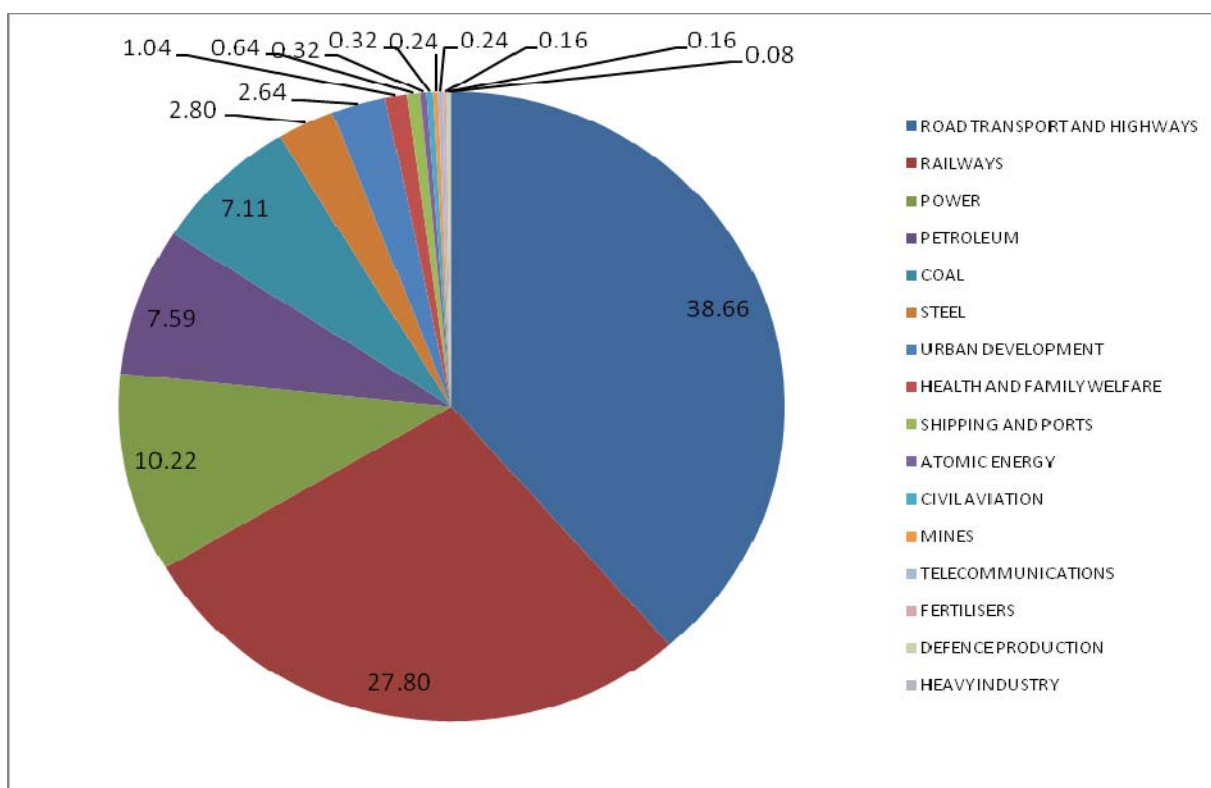


Table-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2017			
	<u>PETROCHEMICALS</u>			
1	ASSAM GAS CRACKER PROJECT (BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]	5,460.61	04/2012	9,895.05
	<u>POWER</u>			
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]	509.66	11/2011	566.26
3	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]	1,216.83	08/2012	1,074.89
4	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000101]	1,961.87	05/2014	1,817.05
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000117]	1,422.85	01/2015	1,490.42
6	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000145]	1,909.24	06/2015	1,093.03
7	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]	303.07	07/2016	48.50
8	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000173]	972.42	11/2017	92.20
	May,2017			
	<u>CIVIL AVIATION</u>			
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]	217.60	03/2015	196.94

Table-3

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)


Summary of projects in the Flash Report for the month of May, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1247
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	4
Number of Projects in Current Month	1252

Brief Analysis


Project Status with respect to Original Schedule: Out of 1252 projects, 12 projects are ahead of schedule, 311 projects are on schedule 314 projects are delayed. 484 projects do not have fixed dates of commissioning. 131 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

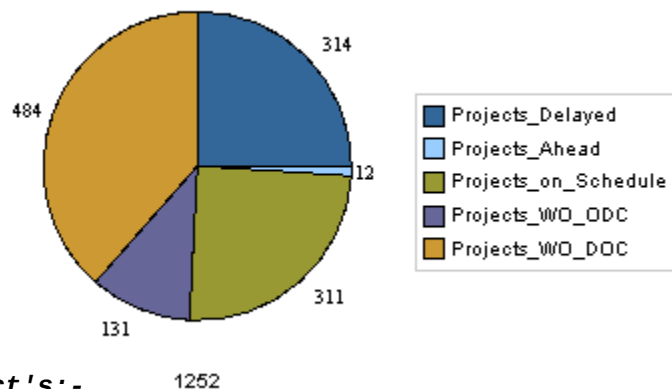

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1252 projects when sanctioned, was of the order of Rs. 1564786.27 crore but this was subsequently revised to Rs. 1734083.56 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till May, 2017 is Rs. 669895.38 crore, which is 38.6% of the anticipated cost of the projects.

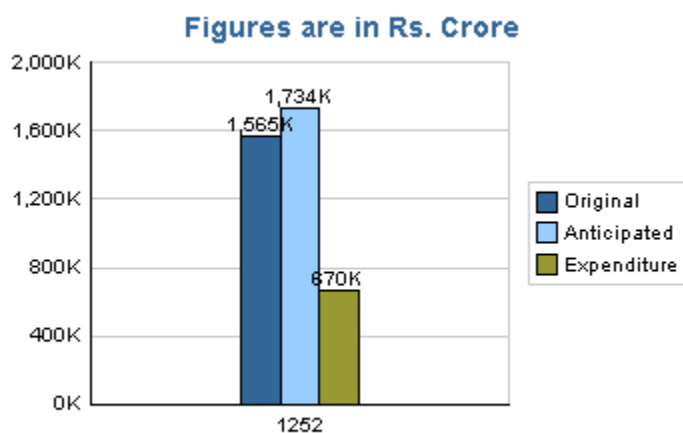

Summary of Projects (costing Rs 150 crore and above) during May 2017

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1247
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	4
No. of Projects upgraded to the status of Major Projects	2
No of Projects in Current Month	1252

Project status						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	314 (25.08%)	10 (.80%)	313(25.00%)	131 (10.46%)	484(38.66%)	1252
Latest Approved (Date)	227 (18.13%)	9 (.72%)	419(33.47%)	98 (7.83%)	499(39.86%)	1252

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1014	13,04,422.42	13,59,212.23	4,32,045.02	31.80	54,789.81	4.20
Project with Revision in Cost	238	3,51,265.63	3,74,871.33	2,37,850.36	63.45	23,605.70	6.70
Total	1,252	16,55,688.05	17,34,083.56	6,69,895.38	38.63	78,395.51	4.73
Original Cost of All Projects							
Original Cost	1,252	15,64,786.27	17,34,083.56	6,69,895.38	38.63	1,69,297.29	10.82

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	314	5,42,127.36	6,45,233.47	4,07,427.12	63.14	1,03,106.11	19.00
Latest Approved (RCE)	227	3,75,267.59	4,25,977.19	2,59,369.47	60.88	50,709.60	13.50
Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	26	66,157.07	69,309.47	39,815.71	57.40	3,152.40	4.80

Table-4

<u>Extent of cost overrun in projects (costing Rs 150 crore and above) with respect to original schedule(Sector Wise)</u>									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	59.41
3	COAL	89	86,482.99	86,697.92	0.25	6	18,670.33	19,677.89	5.40
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	3.35
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	35	57,753.65	57,967.33	0.37	5	1,639.71	2,211.39	34.86
7	PETROLEUM	95	1,88,746.90	1,89,467.02	0.38	19	23,673.73	29,116.08	22.99
8	POWER	128	3,43,460.25	3,93,759.12	14.64	42	99,180.91	1,49,758.51	51.00
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	1	196.70	209.00	6.25
11	RAILWAYS	348	3,52,470.03	4,41,335.56	25.21	200	1,04,781.62	2,54,477.80	142.86
12	ROAD TRANSPORT AND HIGHWAYS	484	3,15,935.94	3,22,248.77	2.00	42	25,210.69	32,209.56	27.76
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	5	1,205.50	2,172.77	80.24
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	33	1,45,290.66	1,52,798.14	5.17	3	6,986.35	14,674.21	110.04
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0.00
Total		1252	15,64,786.27	17,34,083.56	10.82	330	3,01,231.25	5,38,494.81	78.76

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Table-5

Extent of cost overrun in projects (costing Rs 150 crore and above) with respect to original schedule (State Wise)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	59	97,206.37	1,02,378.99	5.32	9	3,738.30	9,937.07	165.82
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	6	9,755.78	25,584.87	162.25
3	ASSAM	49	33,519.75	47,046.96	40.36	16	15,110.50	28,814.28	90.69
4	BIHAR	78	68,807.61	82,225.55	19.50	17	14,312.60	28,026.49	95.82
5	GOA	10	4,379.12	4,361.51	-0.40	0	0.00	0.00	0.00
6	GUJARAT	43	37,987.30	41,775.68	9.97	11	6,598.07	10,510.61	59.30
7	HARYANA	21	14,081.22	15,967.45	13.40	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	12	12,531.81	18,931.08	51.06	2	4,966.47	11,365.74	128.85
9	JAMMU AND KASHMIR	10	27,408.66	47,178.95	72.13	3	7,930.45	27,700.74	249.30
10	KARNATAKA	47	79,506.59	97,832.65	23.05	23	17,879.22	37,369.06	109.01
11	KERALA	21	37,154.14	38,770.19	4.35	6	2,117.36	3,733.41	76.32
12	MADHYA PRADESH	52	53,756.78	58,203.32	8.27	8	16,272.90	20,727.98	27.38
13	MAHARASHTRA	112	1,67,460.76	1,76,862.47	5.61	27	33,696.88	47,110.55	39.81
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	500.11
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	252.94
18	ODISHA	64	70,292.05	78,295.70	11.39	20	6,813.46	14,834.36	117.72
19	PUNJAB	27	15,261.77	15,267.50	0.04	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	62	43,839.05	46,128.14	5.22	15	6,007.10	8,296.19	38.11
21	SIKKIM	5	2,149.08	5,138.08	139.08	2	1,648.94	4,638.22	181.28
22	TAMIL NADU	51	74,509.10	89,961.89	20.74	15	23,236.47	39,438.37	69.73
23	TRIPURA	11	4,400.64	9,067.42	106.05	7	2,909.18	7,575.96	160.42
24	UTTAR PRADESH	83	1,09,253.66	1,12,709.08	3.16	14	25,132.50	29,042.50	15.56
25	WEST BENGAL	53	54,854.77	66,160.14	20.61	19	16,018.91	29,421.60	83.67
26	D & N HAVELI	1	6,086.08	4,701.44	-22.75	0	0.00	0.00	0.00
27	DELHI	17	50,925.07	50,831.89	-0.18	2	353.35	406.17	14.95
28	CHHATISGARH	40	93,631.97	95,569.00	2.07	7	5,623.92	7,839.68	39.40
29	JHARKHAND	48	46,724.53	49,958.75	6.92	9	8,788.69	12,026.69	36.84
30	UTTARAKHAND	10	14,901.99	15,982.05	7.25	3	3,340.76	4,421.33	32.35
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	40.28
32	TELANGANA	35	24,832.84	27,174.20	9.43	8	2,623.87	5,096.00	94.22
33	MULTI STATE	179	2,84,226.28	2,66,611.60	-6.20	70	56,430.26	94,533.91	67.52
Total		1252	15,64,786.27	17,34,083.56	10.82	330	3,01,231.25	5,38,494.81	78.76

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Table-6

<u>Extent of time overrun in projects (costing Rs 150 crore and above) with respect to original schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	3	27,271.00	29,779.00	47 - 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	21 - 80
3	COAL	89	86,482.99	86,697.92	0.25	36	19,328.36	19,543.45	6 - 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	10 - 10
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	35	57,753.65	57,967.33	0.37	19	41,293.75	41,520.97	5 - 72
7	PETROLEUM	95	1,88,746.90	1,89,467.02	0.38	37	58,728.99	58,111.86	1 - 71
8	POWER	128	3,43,460.25	3,93,759.12	14.64	55	1,97,490.96	2,28,408.62	4 - 134
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	4	1,030.98	1,030.98	5 - 15
11	RAILWAYS	348	3,52,470.03	4,41,335.56	25.21	34	38,524.68	1,00,896.37	12 - 261
12	ROAD TRANSPORT AND HIGHWAYS	484	3,15,935.94	3,22,248.77	2.00	99	82,263.28	86,298.58	1 - 110
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	516.39	1,269.46	96 - 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	1	13,334.00	13,334.00	26 - 26
15	URBAN DEVELOPMENT	33	1,45,290.66	1,52,798.14	5.17	20	59,805.11	60,008.58	3 - 69
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1252	15,64,786.27	17,34,083.56	10.82	314	5,42,127.36	6,45,233.47	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Table-7

**Extent of time overrun in projects (costing Rs 150 crore and above) with respect to original schedule
(State Wise)**

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	59	97,206.37	1,02,378.99	5.32	14	8,432.52	10,471.16	3 - 144
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	3	3,209.82	7,672.72	36 - 97
3	ASSAM	49	33,519.75	47,046.96	40.36	15	11,444.92	18,197.51	15 - 122
4	BIHAR	78	68,807.61	82,225.55	19.50	13	32,707.56	39,276.02	1 - 88
5	GOA	10	4,379.12	4,361.51	-0.40	0	0.00	0.00	-
6	GUJARAT	43	37,987.30	41,775.68	9.97	12	21,113.63	22,730.15	3 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	3	2,360.95	3,540.95	24 - 69
8	HIMACHAL PRADESH	12	12,531.81	18,931.08	51.06	3	6,107.21	10,586.37	15 - 111
9	JAMMU AND KASHMIR	10	27,408.66	47,178.95	72.13	8	23,103.03	42,873.32	12 - 193
10	KARNATAKA	47	79,506.59	97,832.65	23.05	7	44,869.00	45,569.00	6 - 65
11	KERALA	21	37,154.14	38,770.19	4.35	4	6,108.08	6,215.27	17 - 65
12	MADHYA PRADESH	52	53,756.78	58,203.32	8.27	10	16,827.98	17,888.53	6 - 87
13	MAHARASHTRA	112	1,67,460.76	1,76,862.47	5.61	25	55,917.14	60,381.90	6 - 258
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	39 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 41
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	71 - 134
17	NAGALAND	7	8,126.79	10,276.79	26.46	4	2,049.11	4,199.11	36 - 60
18	ODISHA	64	70,292.05	78,295.70	11.39	13	8,552.66	9,918.24	5 - 108
19	PUNJAB	27	15,261.77	15,267.50	0.04	3	1,359.14	1,359.14	3 - 23
20	RAJASTHAN	62	43,839.05	46,128.14	5.22	11	18,435.91	19,191.82	6 - 87
21	SIKKIM	5	2,149.08	5,138.08	139.08	2	1,648.94	4,638.22	51 - 80
22	TAMIL NADU	51	74,509.10	89,961.89	20.74	21	39,135.72	42,515.16	1 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	5	1,556.55	4,276.03	4 - 72
24	UTTAR PRADESH	83	1,09,253.66	1,12,709.08	3.16	12	17,620.74	17,620.74	12 - 48
25	WEST BENGAL	53	54,854.77	66,160.14	20.61	15	26,415.01	26,060.54	5 - 57
26	D & N HAVELI	1	6,086.08	4,701.44	-22.75	1	6,086.08	4,701.44	5 - 5
27	DELHI	17	50,925.07	50,831.89	-0.18	5	3,516.83	3,516.83	5 - 30
28	CHHATISGARH	40	93,631.97	95,569.00	2.07	12	59,514.34	60,708.38	10 - 93
29	JHARKHAND	48	46,724.53	49,958.75	6.92	23	25,328.21	25,610.35	5 - 166
30	UTTARAKHAND	10	14,901.99	15,982.05	7.25	3	5,948.57	6,815.88	50 - 78
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	35	24,832.84	27,174.20	9.43	13	5,449.94	5,717.72	10 - 132
33	MULTI STATE	179	2,84,226.28	2,66,611.60	-6.20	46	84,009.53	1,05,684.20	4 - 261
Total		1252	15,64,786.27	17,34,083.56	10.82	314	5,42,127.36	6,45,233.47	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Table-8

Extent of time overrun in projects (costing Rs 150 crore and above) with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	3	29,456.00	29,779.00	47 - 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	1	314.61	441.33	21 - 21
3	COAL	89	86,563.98	86,697.92	0.15	26	9,576.36	9,576.36	6 - 108
4	FERTILISERS	2	703.44	703.44	0.00	0	0.00	0.00	-
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	35	58,134.62	57,967.33	-0.29	17	25,640.92	25,789.26	5 - 72
7	PETROLEUM	95	1,91,363.71	1,89,467.02	-0.99	13	20,150.15	18,265.47	1 - 65
8	POWER	128	3,77,333.57	3,93,759.12	4.35	18	1,05,410.51	1,10,128.38	5 - 111
9	HEAVY INDUSTRY	1	3,727.30	3,827.30	2.68	1	3,727.30	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	3	666.99	666.99	5 - 7
11	RAILWAYS	348	3,88,171.98	4,41,335.56	13.70	30	40,687.97	85,148.01	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	484	3,17,897.35	3,22,248.77	1.37	98	80,792.40	83,060.71	1 - 110
13	SHIPPING AND PORTS	8	4,434.32	5,085.02	14.67	1	150.00	600.00	141 - 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	-
15	URBAN DEVELOPMENT	33	1,52,943.96	1,52,798.14	-0.10	16	58,694.38	58,694.38	3 - 69
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	-
Total		1252	16,55,688.05	17,34,083.56	4.73	227	3,75,267.59	4,25,977.19	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

Table-9

Extent of cost overrun in projects (costing Rs 150 crore and above) with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	2	22,947.00	28,462.00	24.03
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	59.41
3	COAL	89	86,563.98	86,697.92	0.15	3	17,831.46	17,966.36	0.76
4	FERTILISERS	2	703.44	703.44	0.00	0	0.00	0.00	0.00
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	35	58,134.62	57,967.33	-0.29	3	1,586.97	1,777.68	12.02
7	PETROLEUM	95	1,91,363.71	1,89,467.02	-0.99	6	6,699.82	8,853.69	32.15
8	POWER	128	3,77,333.57	3,93,759.12	4.35	11	41,511.44	60,694.08	46.21
9	HEAVY INDUSTRY	1	3,727.30	3,827.30	2.68	1	3,727.30	3,827.30	2.68
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	1	196.70	209.00	6.25
11	RAILWAYS	348	3,88,171.98	4,41,335.56	13.70	166	1,09,734.54	2,19,383.45	99.92
12	ROAD TRANSPORT AND HIGHWAYS	484	3,17,897.35	3,22,248.77	1.37	31	23,849.54	29,097.60	22.00
13	SHIPPING AND PORTS	8	4,434.32	5,085.02	14.67	4	852.61	1,503.31	76.32
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	33	1,52,943.96	1,52,798.14	-0.10	1	496.00	496.18	0.04
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0.00
Total		1252	16,55,688.05	17,34,083.56	4.73	231	2,30,057.45	3,73,265.51	62.25

[^] - Cost Overrun = Anticipated Cost minus latest Cost.

Table-10

Extent of time & cost overrun in projects (costing Rs 150 crore and above) with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	1	5,677.00	6,000.00	85- 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	1	314.61	441.33	21- 21
3	COAL	89	86,563.98	86,697.92	0.15	0	0.00	0.00	0- 0
4	FERTILISERS	2	703.44	703.44	0.00	0	0.00	0.00	0- 0
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	35	58,134.62	57,967.33	-0.29	2	516.00	664.34	17- 18
7	PETROLEUM	95	1,91,363.71	1,89,467.02	-0.99	1	871.35	1,200.00	26- 26
8	POWER	128	3,77,333.57	3,93,759.12	4.35	5	10,019.06	17,381.93	12- 111
9	HEAVY INDUSTRY	1	3,727.30	3,827.30	2.68	1	3,727.30	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	0	0.00	0.00	0- 0
11	RAILWAYS	348	3,88,171.98	4,41,335.56	13.70	18	20,900.80	65,103.01	21- 261
12	ROAD TRANSPORT AND HIGHWAYS	484	3,17,897.35	3,22,248.77	1.37	8	4,443.85	6,734.67	22- 102
13	SHIPPING AND PORTS	8	4,434.32	5,085.02	14.67	1	150.00	600.00	141- 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	33	1,52,943.96	1,52,798.14	-0.10	0	0.00	0.00	0- 0
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0- 0
Total		1252	16,55,688.05	17,34,083.56	4.73	38	46,619.97	1,01,952.58	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

Table-11

Extent of time & cost overrun in projects (costing Rs 150 crore and above) with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	1	3,492.00	6,000.00	85- 85
2	CIVIL AVIATION	3	959.68	1,312.86	36.80	2	624.07	994.86	21- 80
3	COAL	89	86,482.99	86,697.92	0.25	5	1,433.33	2,440.09	24- 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	10- 10
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	35	57,753.65	57,967.33	0.37	4	870.83	1,098.05	7- 18
7	PETROLEUM	95	1,88,746.90	1,89,467.02	0.38	11	16,238.96	19,246.91	12- 70
8	POWER	128	3,43,460.25	3,93,759.12	14.64	34	80,777.09	1,11,973.48	4- 134
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	0	0.00	0.00	0- 0
11	RAILWAYS	348	3,52,470.03	4,41,335.56	25.21	26	23,663.30	86,886.98	21- 261
12	ROAD TRANSPORT AND HIGHWAYS	484	3,15,935.94	3,22,248.77	2.00	11	6,283.38	10,319.54	13- 102
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	33	1,45,290.66	1,52,798.14	5.17	2	591.35	829.20	21- 30
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1252	15,64,786.27	17,34,083.56	10.82	100	1,36,406.49	2,45,095.31	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Table-12


State-Wise Position of Central Sector Projects costing Rs. 150 crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$ and cost overruns^			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	59	97,206.37	1,02,378.99	5.32	3	1,241.74	3,280.38	17 - 144
2	ARUNACHAL PRADESH	31	16,602.41	32,431.50	95.34	3	3,209.82	7,672.72	36 - 97
3	ASSAM	49	33,519.75	47,046.96	40.36	9	7,930.49	14,788.79	26 - 122
4	BIHAR	78	68,807.61	82,225.55	19.50	2	9,129.65	15,698.11	12 - 88
5	GOA	10	4,379.12	4,361.51	-0.40	0	0.00	0.00	-
6	GUJARAT	43	37,987.30	41,775.68	9.97	2	1,827.34	3,559.49	63 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	1	1,108.00	2,288.00	69 - 69
8	HIMACHAL PRADESH	12	12,531.81	18,931.08	51.06	1	3,919.59	8,398.75	111 - 111
9	JAMMU AND KASHMIR	10	27,408.66	47,178.95	72.13	3	7,930.45	27,700.74	12 - 193
10	KARNATAKA	47	79,506.59	97,832.65	23.05	1	993.00	1,693.00	65 - 65
11	KERALA	21	37,154.14	38,770.19	4.35	1	607.06	714.25	17 - 17
12	MADHYA PRADESH	52	53,756.78	58,203.32	8.27	5	14,815.15	15,883.44	6 - 87
13	MAHARASHTRA	112	1,67,460.76	1,76,862.47	5.61	10	16,369.54	22,328.58	10 - 258
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	71 - 134
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	60 - 60
18	ODISHA	64	70,292.05	78,295.70	11.39	3	546.81	1,912.74	13 - 108
19	PUNJAB	27	15,261.77	15,267.50	0.04	0	0.00	0.00	-
20	RAJASTHAN	62	43,839.05	46,128.14	5.22	4	2,107.95	2,863.86	30 - 87
21	SIKKIM	5	2,149.08	5,138.08	139.08	2	1,648.94	4,638.22	51 - 80
22	TAMIL NADU	51	74,509.10	89,961.89	20.74	4	7,361.42	11,489.97	33 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	4	1,341.17	4,060.65	7 - 72
24	UTTAR PRADESH	83	1,09,253.66	1,12,709.08	3.16	0	0.00	0.00	-
25	WEST BENGAL	53	54,854.77	66,160.14	20.61	1	4,404.57	5,135.01	38 - 38
26	D & N HAVELI	1	6,086.08	4,701.44	-22.75	0	0.00	0.00	-
27	DELHI	17	50,925.07	50,831.89	-0.18	0	0.00	0.00	-
28	CHHATISGARH	40	93,631.97	95,569.00	2.07	4	4,351.49	5,824.26	38 - 93
29	JHARKHAND	48	46,724.53	49,958.75	6.92	2	1,161.75	1,443.89	99 - 166
30	UTTARAKHAND	10	14,901.99	15,982.05	7.25	1	2,978.48	3,846.30	75 - 75
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	35	24,832.84	27,174.20	9.43	3	1,482.10	1,792.44	21 - 132
33	MULTI STATE	179	2,84,226.28	2,66,611.60	-6.20	26	37,059.75	59,052.96	4 - 261
Total		1252	15,64,786.27	17,34,083.56	10.82	100	1,36,406.49	2,45,095.31	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

SECTOR-WISE SUMMARY OF MEGA PROJECTS (Rs 1000 crore and above)
Table-13

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	125	1
2	ROAD TRANSPORT AND HIGHWAYS	100	0
3	POWER	62	6
4	PETROLEUM	39	3
5	COAL	12	0
6	URBAN DEVELOPMENT	11	1
7	STEEL	9	0
8	ATOMIC ENERGY	4	0
9	TELECOMMUNICATIONS	2	0
10	MINES	1	0
11	HEAVY INDUSTRY	1	0
12	SHIPPING AND PORTS	1	0
	Total	367	11

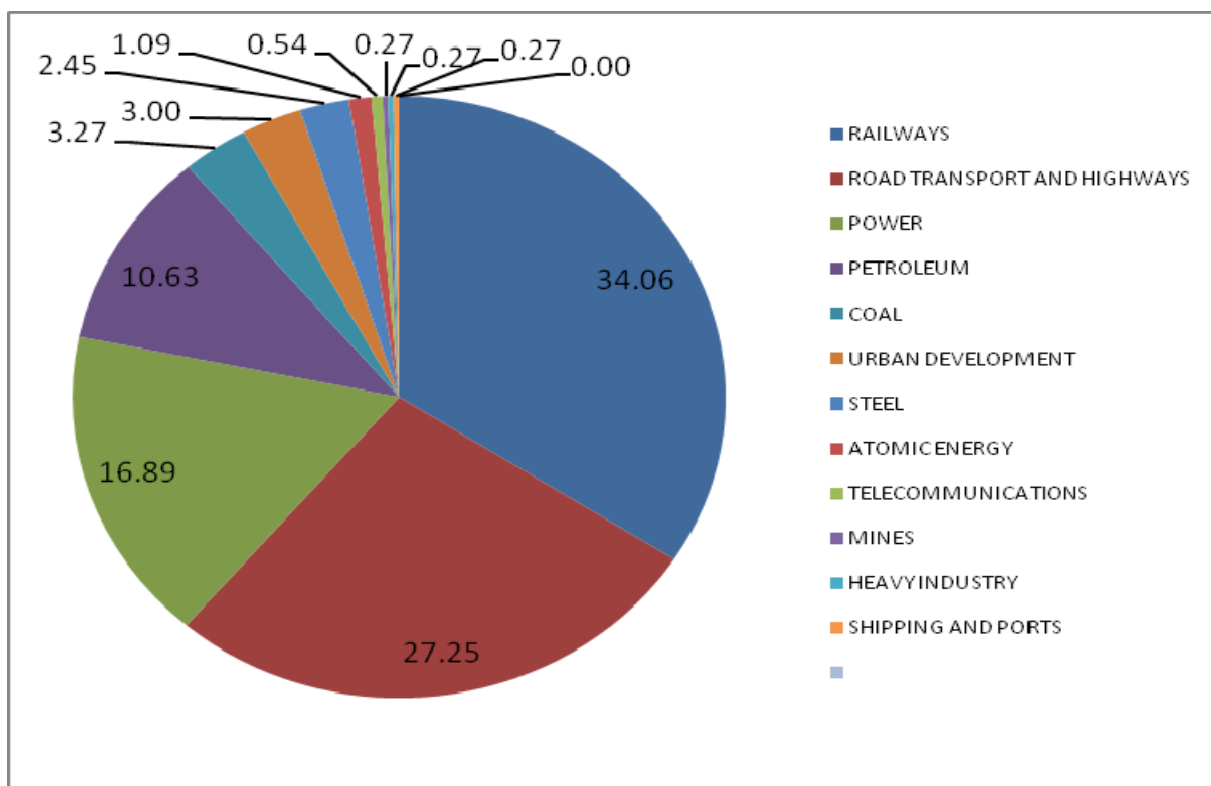

Summary of Projects (costing Rs 1000 crore and above) during May 2017

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	365
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	0
No. of Projects upgraded to the status of Mega Projects	2
No of Projects in Current Month	367

Project status						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	125 (34.06%)	3 (.82%)	89 (24.25%)	47 (12.81%)	103 (28.07%)	367
Latest Approved (Date)	89 (24.25%)	2 (.54%)	135 (36.78%)	28 (7.63%)	113 (30.79%)	367

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	282	9,94,258.55	10,31,691.54	3,51,069.59	34.00	37,432.99	3.80
Project with Revision in Cost	85	2,91,034.25	3,12,181.93	2,04,803.51	65.60	21,147.68	7.30
Total	367	12,85,292.80	13,43,873.47	5,55,873.10	41.36	58,580.67	4.56
Original Cost of All Projects							
Original Cost	367	12,04,310.30	13,43,873.47	5,55,873.10	41.36	1,39,563.17	11.59

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	125	4,65,493.44	5,62,093.22	3,53,985.90	62.98	96,599.78	20.80
Latest Approved (RCE)	89	3,19,599.15	3,68,232.71	2,20,817.75	60.00	48,633.56	15.20
Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	11	62,244.83	65,275.12	37,774.87	57.90	3,030.29	4.90

Table-14

Extent of cost overrun in Mega projects (costing Rs 1000 crore and above) with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	COAL	12	55,807.73	55,808.53	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROLEUM	39	1,66,416.41	1,66,283.76	-0.08	10	20,798.50	25,225.52	21.29
6	POWER	62	3,16,950.13	3,65,714.02	15.39	26	92,163.38	1,41,206.00	53.21
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	125	2,68,073.85	3,32,470.15	24.02	74	67,227.73	1,89,897.28	182.47
9	ROAD TRANSPORT AND HIGHWAYS	100	1,44,161.25	1,49,597.31	3.77	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
12	URBAN DEVELOPMENT	11	1,39,164.14	1,46,468.15	5.25	1	6,395.00	13,845.01	116.50
Total		367	12,04,310.30	13,43,873.47	11.59	131	2,40,384.70	4,43,663.52	84.56

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Table-15

Extent of cost overrun in Mega projects (costing Rs 1000 crore and above) with respect to original schedule (State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	17	82,694.82	86,462.48	4.56	4	2,521.62	7,016.28	178.24
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	3	9,356.22	24,952.87	166.70
3	ASSAM	9	21,033.85	32,693.76	55.43	5	12,723.01	24,469.18	92.32
4	BIHAR	14	41,018.97	52,350.17	27.62	5	10,666.26	21,997.46	106.23
5	GUJARAT	9	22,120.57	24,650.49	11.44	3	3,626.32	6,156.24	69.77
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	5	9,740.15	16,139.42	65.70	2	4,966.47	11,365.74	128.85
8	JAMMU AND KASHMIR	10	27,408.66	47,178.95	72.13	3	7,930.45	27,700.74	249.30
9	KARNATAKA	22	67,362.06	84,410.34	25.31	13	14,079.10	31,886.38	126.48
10	KERALA	6	31,137.08	32,153.08	3.26	1	550.00	1,566.00	184.73
11	MADHYA PRADESH	13	34,706.96	38,672.07	11.42	6	15,326.30	19,291.41	25.87
12	MAHARASHTRA	44	1,39,135.61	1,47,078.32	5.71	17	29,763.57	41,277.58	38.68
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	500.11
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	23	54,160.98	60,748.36	12.16	6	3,733.20	10,320.58	176.45
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	1	829.74	1,161.64	40.00
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	13	58,170.40	71,800.95	23.43	5	21,221.42	34,851.97	64.23
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	33	86,307.66	88,855.13	2.95	6	22,325.93	25,327.98	13.45
24	WEST BENGAL	21	42,248.95	51,400.93	21.66	7	12,949.21	23,828.84	84.02
25	D & N HAVELI	1	6,086.08	4,701.44	-22.75	0	0.00	0.00	0.00
26	DELHI	4	45,462.73	45,316.73	-0.32	0	0.00	0.00	0.00
27	CHHATISGARH	12	83,067.13	84,096.77	1.24	3	4,700.73	6,009.10	27.83
28	JHARKHAND	10	33,188.25	35,781.77	7.81	3	7,451.01	10,044.53	34.81
29	UTTARAKHAND	5	12,735.36	13,603.18	6.81	1	2,978.48	3,846.30	29.14
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	61	2,36,011.11	2,11,549.22	-10.36	25	40,957.20	71,075.80	73.54
Total		367	12,04,310.30	13,43,873.47	11.59	131	2,40,384.70	4,43,663.52	84.56

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Table-16

Extent of time overrun in Mega projects (costing Rs 1000 crore and above) with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	3	27,271.00	29,779.00	47 - 85
2	COAL	12	55,807.73	55,808.53	0.00	3	8,192.43	8,192.43	6 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	4	34,978.19	34,978.19	5 - 51
5	PETROLEUM	39	1,66,416.41	1,66,283.76	-0.08	17	51,185.10	49,965.82	5 - 71
6	POWER	62	3,16,950.13	3,65,714.02	15.39	36	1,89,054.43	2,18,622.94	5 - 134
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	125	2,68,073.85	3,32,470.15	24.02	22	33,096.33	93,242.94	27 - 261
9	ROAD TRANSPORT AND HIGHWAYS	100	1,44,161.25	1,49,597.31	3.77	33	50,577.82	54,064.46	10 - 74
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	13,334.00	13,334.00	26 - 26
12	URBAN DEVELOPMENT	11	1,39,164.14	1,46,468.15	5.25	5	56,086.14	56,086.14	5 - 29
Total		367	12,04,310.30	13,43,873.47	11.59	125	4,65,493.44	5,62,093.22	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Table-17

Extent of time overrun in Mega projects (costing Rs 1000 crore and above) with respect to original schedule (State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	82,694.82	86,462.48	4.56	3	3,863.00	4,945.00	37 - 144
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	2	3,070.89	7,517.72	52 - 97
3	ASSAM	9	21,033.85	32,693.76	55.43	4	9,211.85	15,328.07	26 - 122
4	BIHAR	14	41,018.97	52,350.17	27.62	3	27,010.57	33,413.27	5 - 88
5	GUJARAT	9	22,120.57	24,650.49	11.44	4	16,482.96	18,211.73	19 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	69 - 69
7	HIMACHAL PRADESH	5	9,740.15	16,139.42	65.70	2	5,836.38	10,315.54	15 - 111
8	JAMMU AND KASHMIR	10	27,408.66	47,178.95	72.13	8	23,103.03	42,873.32	12 - 193
9	KARNATAKA	22	67,362.06	84,410.34	25.31	4	44,219.34	44,919.34	6 - 65
10	KERALA	6	31,137.08	32,153.08	3.26	1	5,181.79	5,181.79	29 - 29
11	MADHYA PRADESH	13	34,706.96	38,672.07	11.42	4	14,881.45	15,459.77	6 - 53
12	MAHARASHTRA	44	1,39,135.61	1,47,078.32	5.71	14	49,672.70	53,293.11	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	71 - 134
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	23	54,160.98	60,748.36	12.16	4	5,790.23	6,809.70	15 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	3	14,823.44	15,155.34	48 - 74
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	13	58,170.40	71,800.95	23.43	7	32,078.89	35,757.44	18 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	33	86,307.66	88,855.13	2.95	5	14,777.89	14,777.89	15 - 48
24	WEST BENGAL	21	42,248.95	51,400.93	21.66	8	22,750.71	22,396.24	6 - 57
25	D & N HAVELI	1	6,086.08	4,701.44	-22.75	1	6,086.08	4,701.44	5 - 5
26	DELHI	4	45,462.73	45,316.73	-0.32	2	2,613.73	2,613.73	5 - 25
27	CHHATISGARH	12	83,067.13	84,096.77	1.24	6	58,079.92	58,775.30	10 - 51
28	JHARKHAND	10	33,188.25	35,781.77	7.81	6	20,164.09	20,389.93	5 - 99
29	UTTARAKHAND	5	12,735.36	13,603.18	6.81	2	5,470.06	6,337.88	75 - 78
30	TELANGANA	6	14,904.53	16,572.01	11.19	1	1,266.60	1,266.60	10 - 10
31	MULTI STATE	61	2,36,011.11	2,11,549.22	-10.36	24	73,231.40	93,241.95	6 - 261
Total		367	12,04,310.30	13,43,873.47	11.59	125	4,65,493.44	5,62,093.22	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Table-18

Extent of time overrun in projects Mega projects (costing Rs 1000 crore and above) with respect to latest schedule									
						(All Cost/ Expenditure in Rs. crore)			
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	3	29,456.00	29,779.00	47 - 85
2	COAL	12	55,807.73	55,808.53	0.00	2	2,285.32	2,285.32	6 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,466.31	48,150.68	-0.65	3	19,453.19	19,453.19	5 - 51
5	PETROLEUM	39	1,67,997.02	1,66,283.76	-1.02	7	18,509.61	16,652.12	5 - 65
6	POWER	62	3,49,546.88	3,65,714.02	4.63	15	1,04,546.07	1,09,085.52	5 - 111
7	HEAVY INDUSTRY	1	3,727.30	3,827.30	2.68	1	3,727.30	3,827.30	75 - 75
8	RAILWAYS	125	2,97,560.15	3,32,470.15	11.73	21	36,466.80	80,237.53	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	100	1,45,434.69	1,49,597.31	2.86	32	49,068.72	50,826.59	10 - 74
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	-
12	URBAN DEVELOPMENT	11	1,46,614.15	1,46,468.15	-0.10	5	56,086.14	56,086.14	5 - 29
Total		367	12,85,292.80	13,43,873.47	4.56	89	3,19,599.15	3,68,232.71	

\$- Time overrun = Anticipated Date of Commissioning minus latest Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus latest Cost.

Table-19

Extent of cost overrun in projects Mega projects (costing Rs 1000 crore and above) with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	2	22,947.00	28,462.00	24.03
2	COAL	12	55,807.73	55,808.53	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROLEUM	39	1,67,997.02	1,66,283.76	-1.02	4	6,140.26	8,207.41	33.67
6	POWER	62	3,49,546.88	3,65,714.02	4.63	7	40,193.63	59,117.86	47.08
7	HEAVY INDUSTRY	1	3,727.30	3,827.30	2.68	1	3,727.30	3,827.30	2.68
8	RAILWAYS	125	2,97,560.15	3,32,470.15	11.73	57	73,970.33	1,64,340.56	122.17
9	ROAD TRANSPORT AND HIGHWAYS	100	1,45,434.69	1,49,597.31	2.86	15	18,686.65	22,849.27	22.28
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
12	URBAN DEVELOPMENT	11	1,46,614.15	1,46,468.15	-0.10	0	0.00	0.00	0.00
Total		367	12,85,292.80	13,43,873.47	4.56	88	1,83,973.14	3,05,155.54	65.87

[^] - Cost Overrun = Anticipated Cost minus latest Cost.

Table-20

Extent of time & cost overrun in projects Mega projects (costing Rs 1000 crore and above) with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	1	5,677.00	6,000.00	85- 85
2	COAL	12	55,807.73	55,808.53	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,466.31	48,150.68	-0.65	0	0.00	0.00	0- 0
5	PETROLEUM	39	1,67,997.02	1,66,283.76	-1.02	1	871.35	1,200.00	26- 26
6	POWER	62	3,49,546.88	3,65,714.02	4.63	3	9,350.04	16,534.49	12- 111
7	HEAVY INDUSTRY	1	3,727.30	3,827.30	2.68	1	3,727.30	3,827.30	75- 75
8	RAILWAYS	125	2,97,560.15	3,32,470.15	11.73	13	18,676.08	62,180.44	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	100	1,45,434.69	1,49,597.31	2.86	3	3,338.00	5,095.87	22- 69
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,46,614.15	1,46,468.15	-0.10	0	0.00	0.00	0- 0
Total		367	12,85,292.80	13,43,873.47	4.56	22	41,639.77	94,838.10	

\$- Time overrun = Anticipated Date of Commissioning minus latest Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest Cost.

Table-21

Extent of time & cost overrun in Mega projects (costing Rs 1000 crore and above) with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	1	3,492.00	6,000.00	85- 85
2	COAL	12	55,807.73	55,808.53	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROLEUM	39	1,66,416.41	1,66,283.76	-0.08	6	14,616.59	16,888.11	12- 65
6	POWER	62	3,16,950.13	3,65,714.02	15.39	21	74,784.08	1,04,631.32	6- 134
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	125	2,68,073.85	3,32,470.15	24.02	18	19,966.64	81,198.16	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	100	1,44,161.25	1,49,597.31	3.77	4	4,847.10	8,333.74	22- 69
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,39,164.14	1,46,468.15	5.25	0	0.00	0.00	0- 0
Total		367	12,04,310.30	13,43,873.47	11.59	51	1,19,424.41	2,20,878.63	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Table-22

State-Wise Position of Central Sector Projects costing Rs. 1000 crore and above showing Both Time and Cost Overruns									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	82,694.82	86,462.48	4.56	1	743.00	1,825.00	144 - 144
2	ARUNACHAL PRADESH	4	10,609.32	26,205.97	147.01	2	3,070.89	7,517.72	52 - 97
3	ASSAM	9	21,033.85	32,693.76	55.43	3	6,746.70	12,949.18	26 - 122
4	BIHAR	14	41,018.97	52,350.17	27.62	1	8,692.97	15,095.67	88 - 88
5	GUJARAT	9	22,120.57	24,650.49	11.44	1	1,509.10	3,237.87	63 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	69 - 69
7	HIMACHAL PRADESH	5	9,740.15	16,139.42	65.70	1	3,919.59	8,398.75	111 - 111
8	JAMMU AND KASHMIR	10	27,408.66	47,178.95	72.13	3	7,930.45	27,700.74	12 - 193
9	KARNATAKA	22	67,362.06	84,410.34	25.31	1	993.00	1,693.00	65 - 65
10	KERALA	6	31,137.08	32,153.08	3.26	0	0.00	0.00	-
11	MADHYA PRADESH	13	34,706.96	38,672.07	11.42	3	13,868.55	14,446.87	6 - 53
12	MAHARASHTRA	44	1,39,135.61	1,47,078.32	5.71	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	71 - 134
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	23	54,160.98	60,748.36	12.16	1	183.23	1,202.70	58 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	1	829.74	1,161.64	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	13	58,170.40	71,800.95	23.43	3	7,211.42	10,889.97	33 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	33	86,307.66	88,855.13	2.95	0	0.00	0.00	-
24	WEST BENGAL	21	42,248.95	51,400.93	21.66	1	4,404.57	5,135.01	38 - 38
25	D & N HAVELI	1	6,086.08	4,701.44	-22.75	0	0.00	0.00	-
26	DELHI	4	45,462.73	45,316.73	-0.32	0	0.00	0.00	-
27	CHHATISGARH	12	83,067.13	84,096.77	1.24	2	3,874.16	4,848.27	38 - 40
28	JHARKHAND	10	33,188.25	35,781.77	7.81	1	900.05	1,125.89	99 - 99
29	UTTARAKHAND	5	12,735.36	13,603.18	6.81	1	2,978.48	3,846.30	75 - 75
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	61	2,36,011.11	2,11,549.22	-10.36	13	31,318.74	51,889.29	13 - 261
Total		367	12,04,310.30	13,43,873.47	11.59	51	1,19,424.41	2,20,878.63	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

[^] - Cost Overrun = Anticipated Cost minus Original Cost.

Table-23

<u>List of projects (costing Rs 150 crore and above) completed/dropped/Frozen during current month</u>							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>CIVIL AVIATION</u>						
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	03/2015	215.00	09/2017	196.94

Table-24

(All Cost in Rs. Crore)

List of projects <u>(costing Rs 150 crore and above)</u> added					(May 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	409.87	3/2022	409.87	3/2022
2	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	319.76	3/2022	319.76	3/2022
3	DHANKASA UG (1.00 MTY)	9/2016	458.07	3/2022	458.07	3/2022
4	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	328.00	3/2021	328.00	3/2021

Table-25

Milestones (Cumulative due & achieved)

Total	3930
Achieved up to month	2104


Table-26

List of projects (costing Rs 150 crore and above) reporting additional delays (May 2017)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	MADHUBAND NLW WASHERY BCCL	289.45	289.45	05/2014	09/2017	10/2017	1
2	PATHERDIH NLW WASHERY BCCL	269.82	269.82	04/2014	08/2017	10/2017	2
3	KISTARAM OCP SCCL	242.29	242.29	03/2015	03/2018	03/2020	24
	<u>STEEL</u>						
4	TURBO BLOWER - 5 RINL	280.00	280.00	09/2016	05/2017	06/2017	1
	<u>PETROLEUM</u>						
5	SIX PIPELINE REPLACEMENT PROJECT ONGC Central Sector Projects	181.02	173.28	01/2017	12/2017	03/2018	3
6	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A ONGC	215.38	215.38	06/2017	06/2017	10/2017	4
7	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,256.72	05/2013	05/2017	10/2017	5
8	DEVELOPMENT OF C-26 CLUSTER FIELDS ONGC	2,592.17	2,592.17	05/2014	12/2017	05/2018	5
9	DAMAN DEVELOPMENT PROJECT ONGC	6,086.08	4,701.44	05/2019	05/2019	10/2019	5
	<u>POWER</u>						
10	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II PGCIL	1,575.30	1,656.15	05/2016	05/2017	06/2017	1
11	SOLAPUR STPP NTPC	9,395.18	9,395.18	11/2016	12/2017	04/2018	4
12	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) NTPC	11,846.00	11,846.00	06/2017	12/2017	04/2018	4
13	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	6,749.18	09/2011	06/2017	12/2017	6
14	NORTH KARANPURA STPP (3X660 MW) NTPC	14,366.58	14,366.58	02/2019	02/2020	02/2021	12
15	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT PGCIL	1,788.41	2,352.57	09/2017	09/2017	09/2018	12


**List of projects (costing Rs 150 crore and above) reporting additional delays
(May 2017)**

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>HEALTH AND FAMILY WELFARE</u>						
16	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR HSCC	168.90	168.90	05/2017	07/2017	10/2017	3
17	NEIGRIHMS SHILLONG MEGHALYA HSCC	363.99	363.99	05/2018	05/2019	08/2019	3
18	AIIMS - MOTHER AND CHILD BLOCK HSCC	204.44	204.44	05/2017	06/2017	12/2017	6
19	AIIMS - OPD(NEW) HSCC	293.65	293.65	05/2017	06/2017	12/2017	6
	<u>RAILWAYS</u>						
20	KANPUR KASGANJ MATHURA(GC) NER NER	677.97	1,679.13	N.A.	04/2017	05/2017	1
	<u>URBAN DEVELOPMENT</u>						
21	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	332.72	09/2016	07/2017	08/2017	1
22	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN CPWD Central Sector Projects	350.02	479.87	03/2015	07/2017	09/2017	2
23	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL CPWD	188.87	188.87	12/2015	06/2017	09/2017	3
24	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR CPWD Central Sector Projects	216.69	216.69	03/2015	03/2018	06/2018	3
25	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA CPWD	315.00	315.00	06/2015	04/2017	08/2017	4
26	NAGPUR METRO RAIL NMRCL	8,680.00	8,680.00	03/2018	03/2018	12/2019	21

Graphical Presentation of All Projects w.r.t. Original Schedule

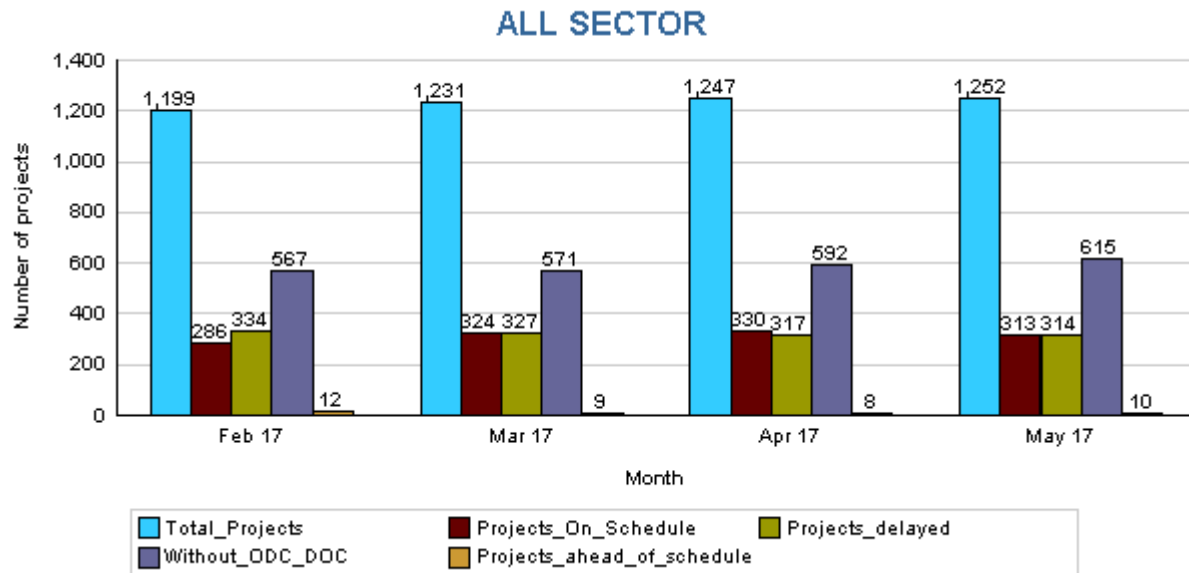


Break-up of 314 Delayed projects in May 2017

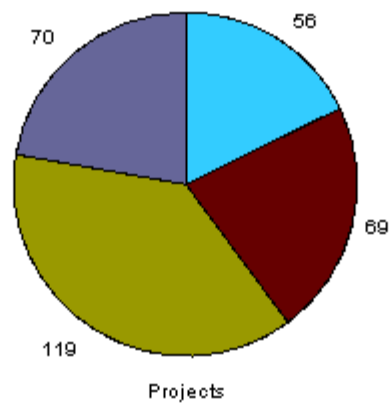


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

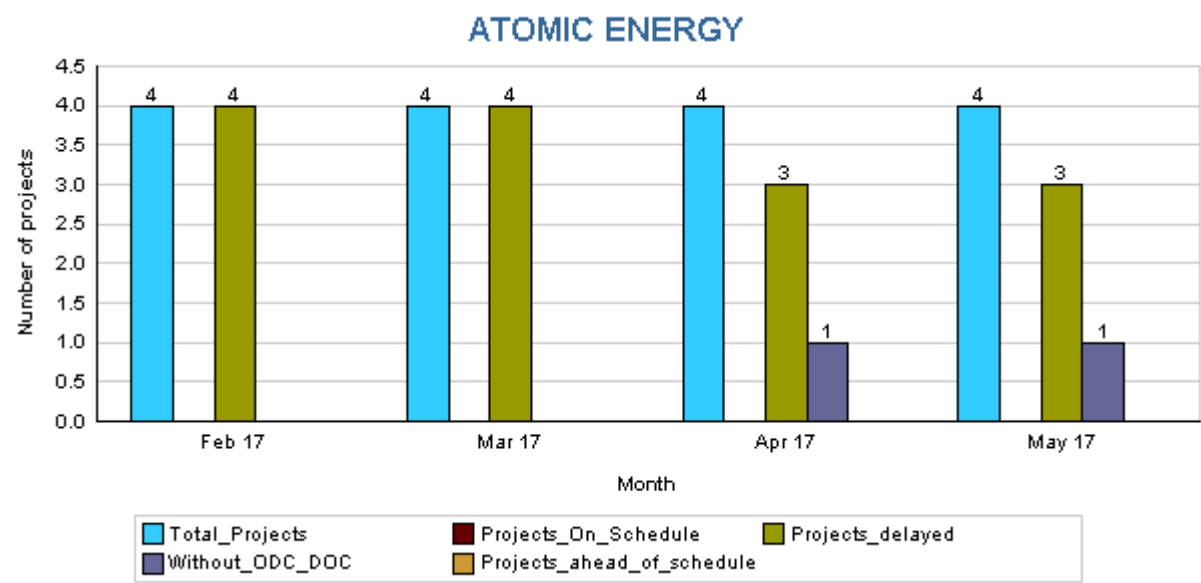


Break-up of 3 Delayed projects in May 2017

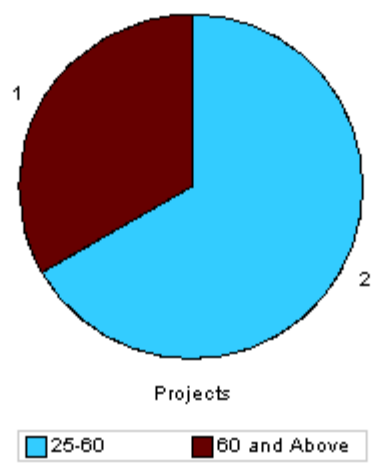


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

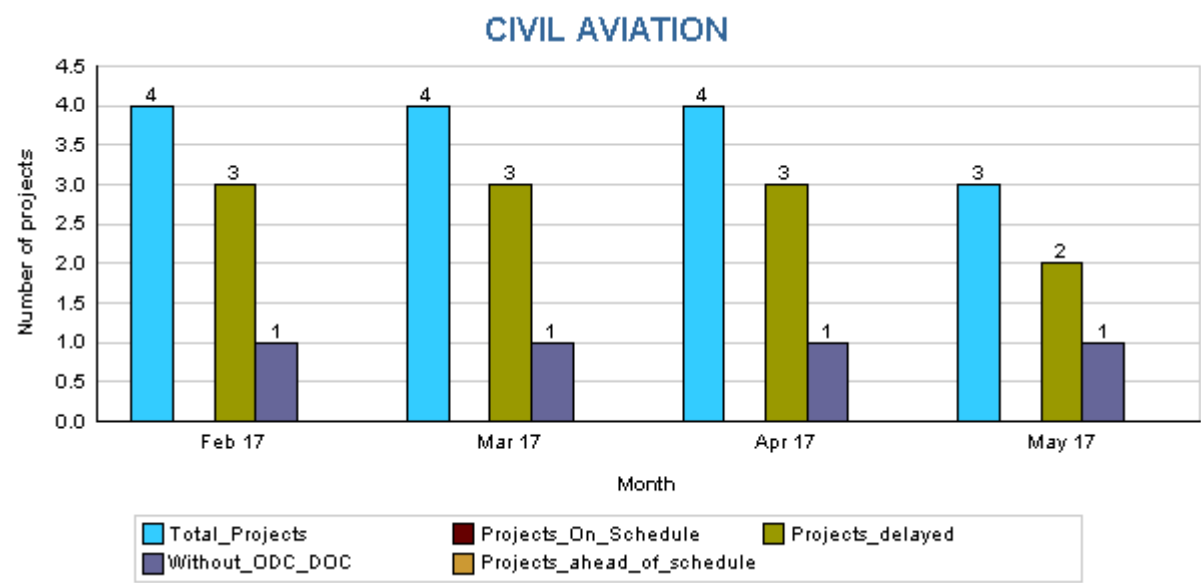


Break-up of 2 Delayed projects in May 2017

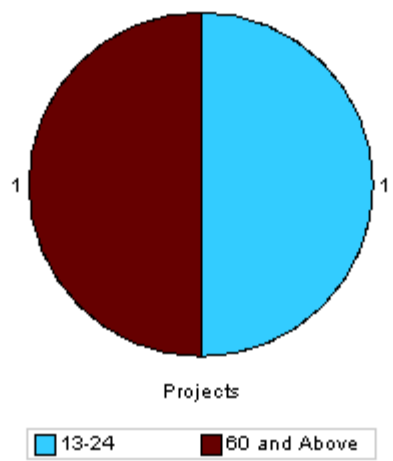


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

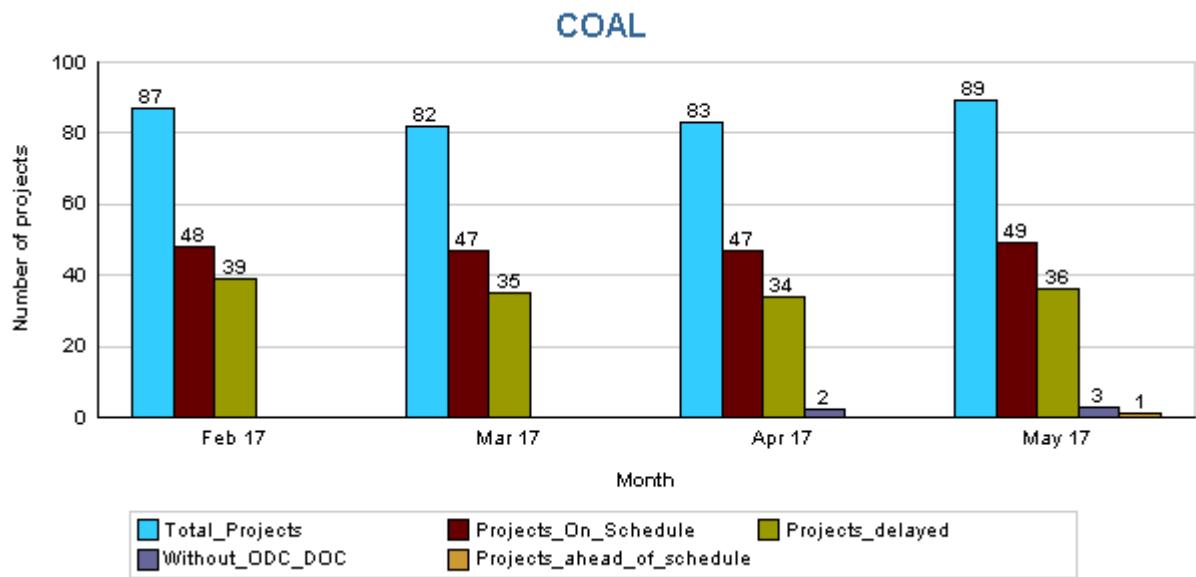


Break-up of 36 Delayed projects in May 2017

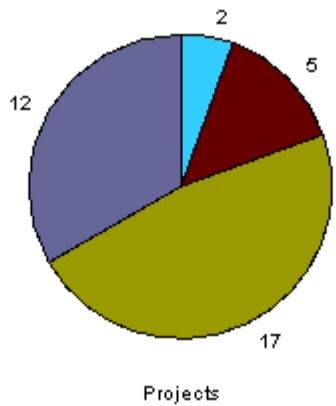


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

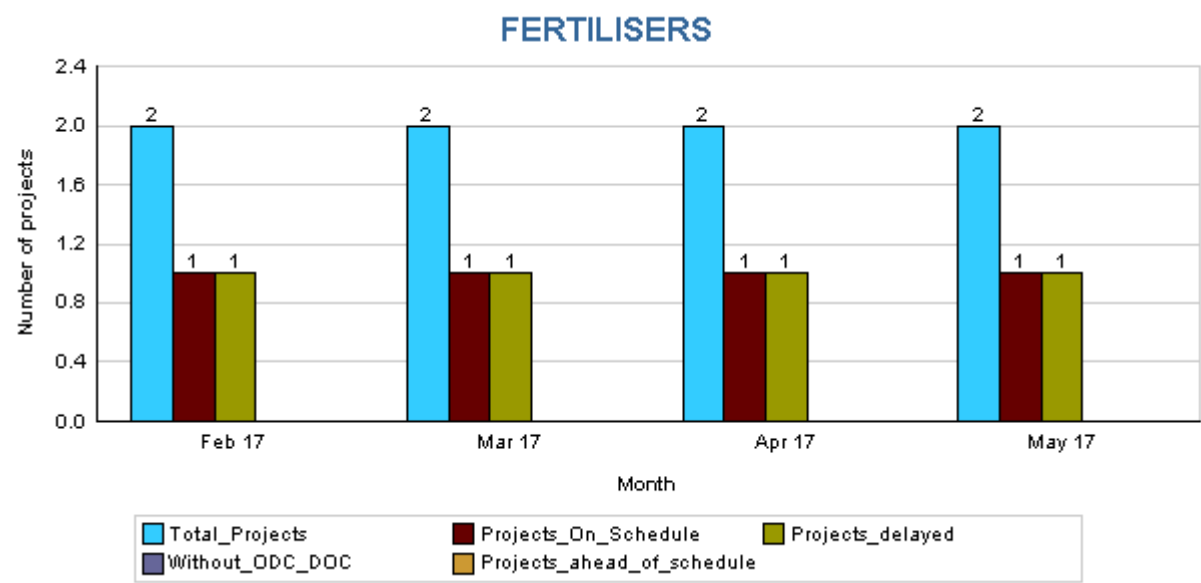


Break-up of 1 Delayed projects in May 2017

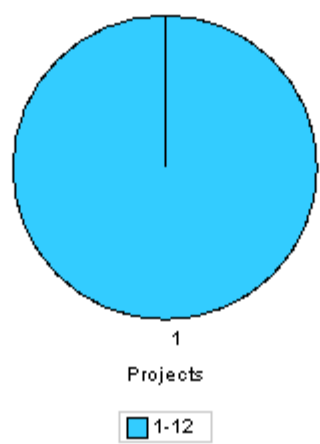


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

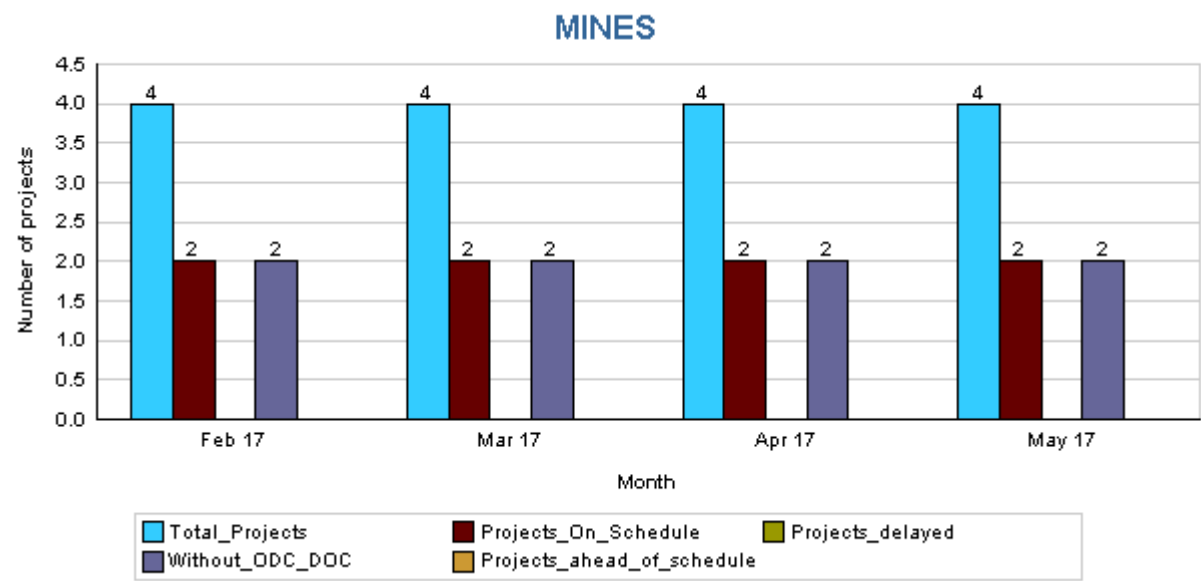


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

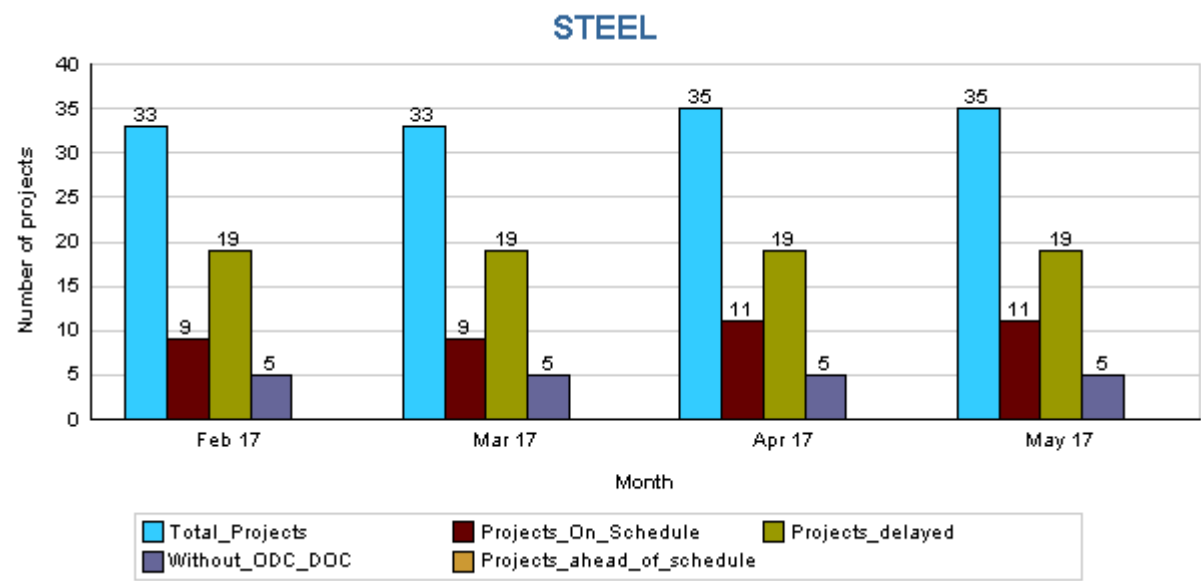


Break-up of 19 Delayed projects in May 2017

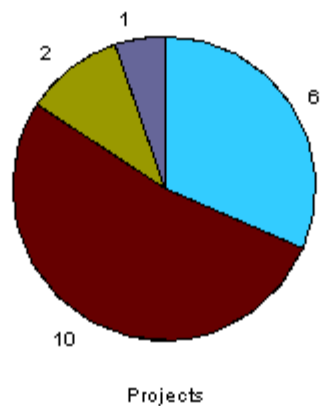

Delay in Months


1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

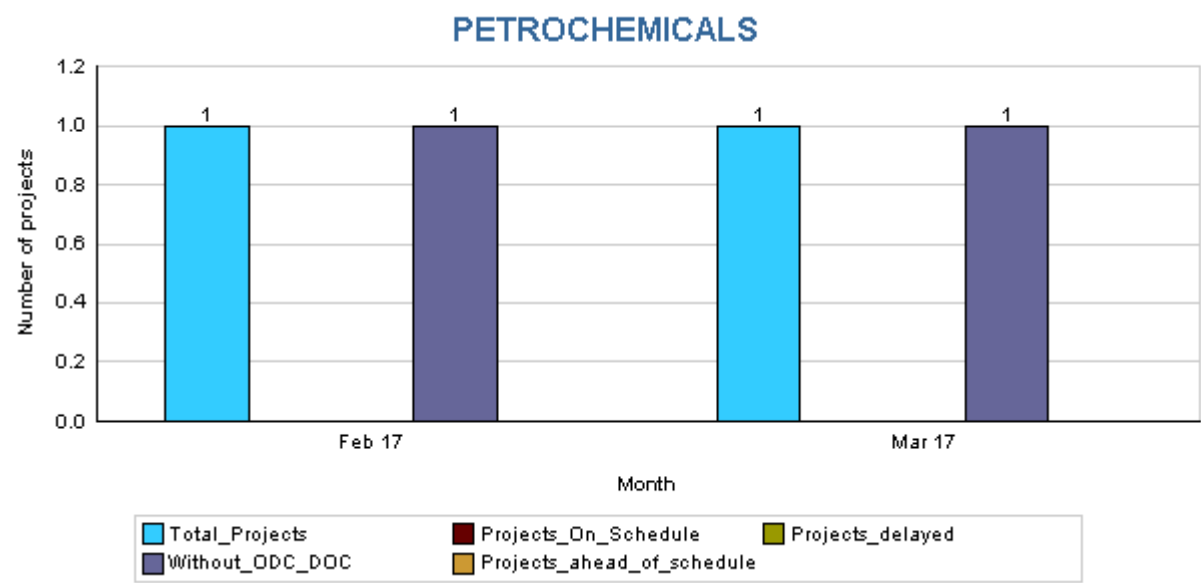


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

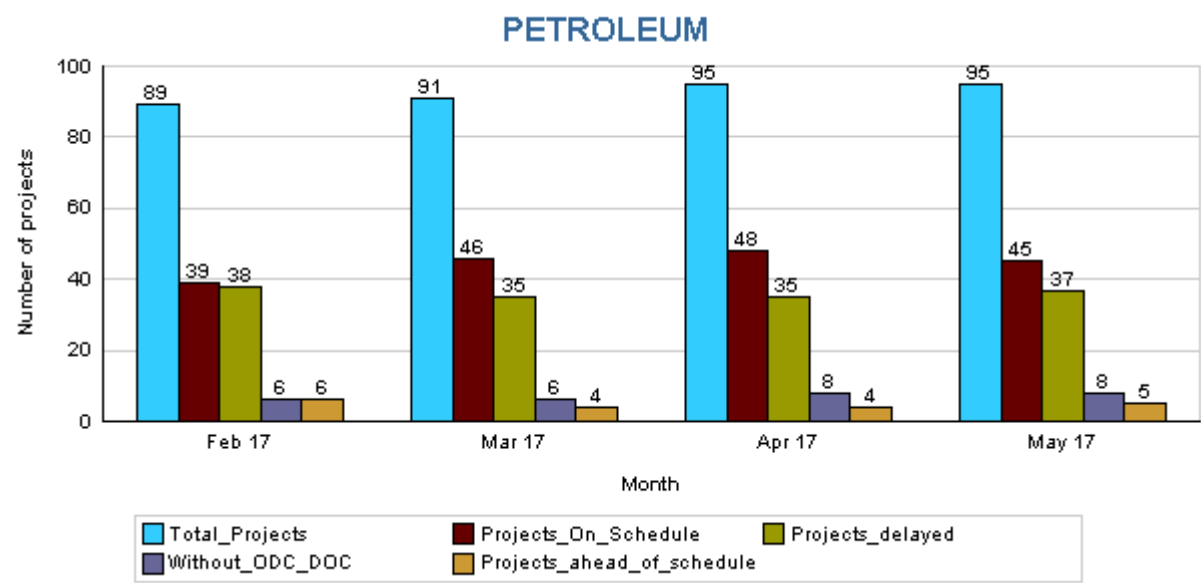


Break-up of 37 Delayed projects in May 2017

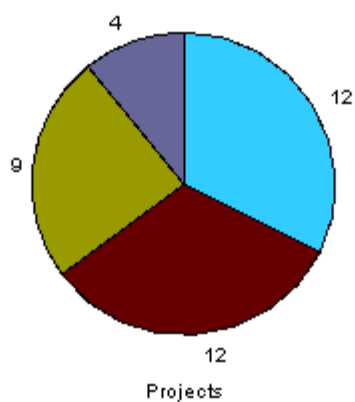


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------

Graphical Presentation of All Projects w.r.t. Original Schedule

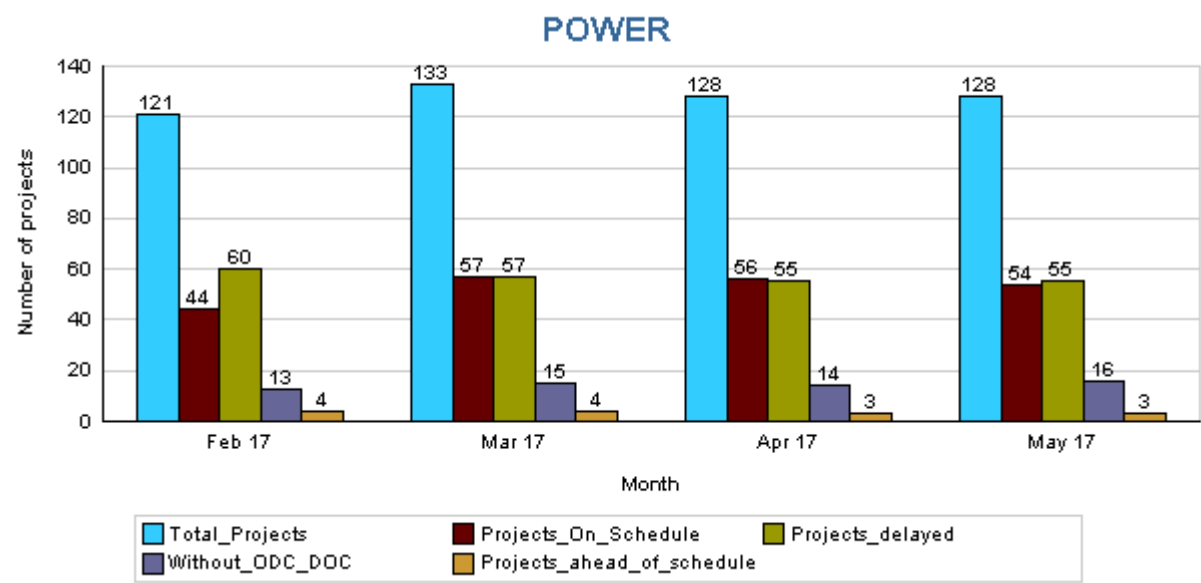

Break-up of 55 Delayed projects in May 2017

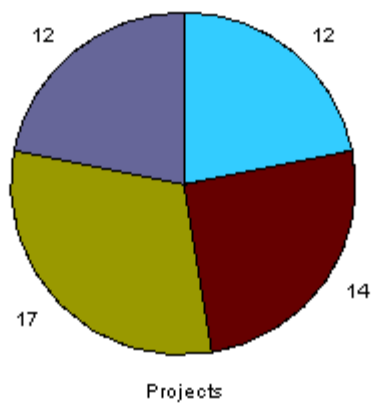

Delay in Months


1-12

13-24


25-60

60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

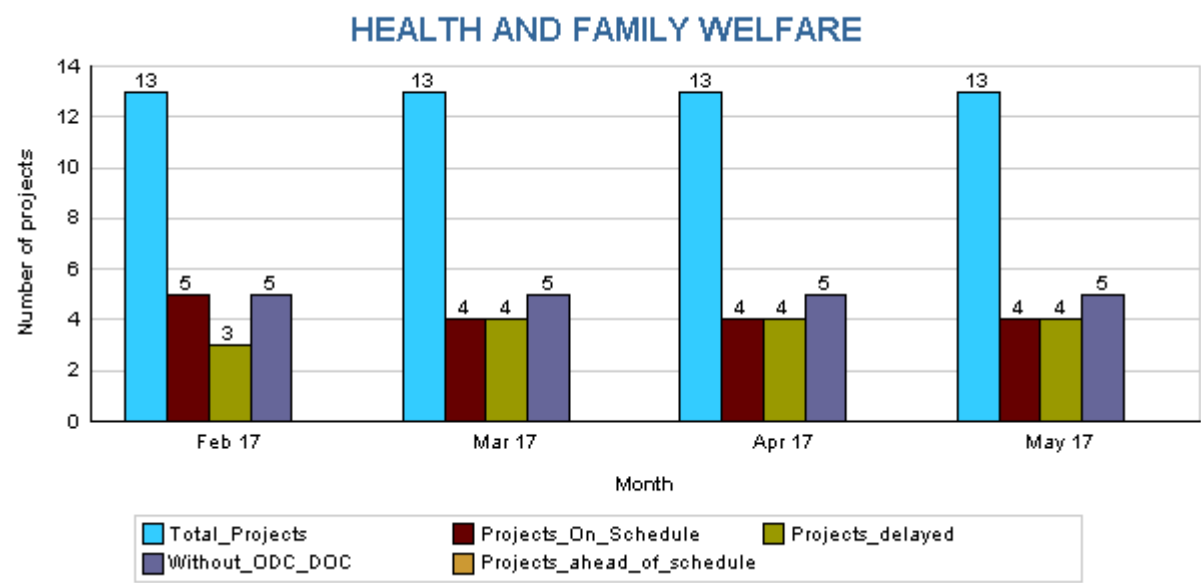


Break-up of 4 Delayed projects in May 2017

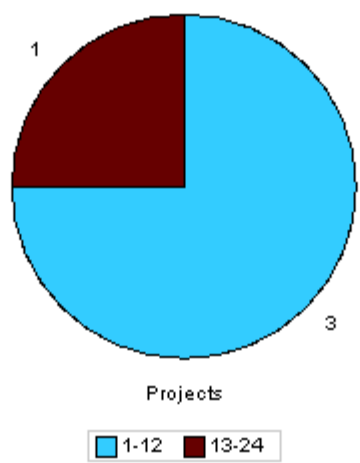


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

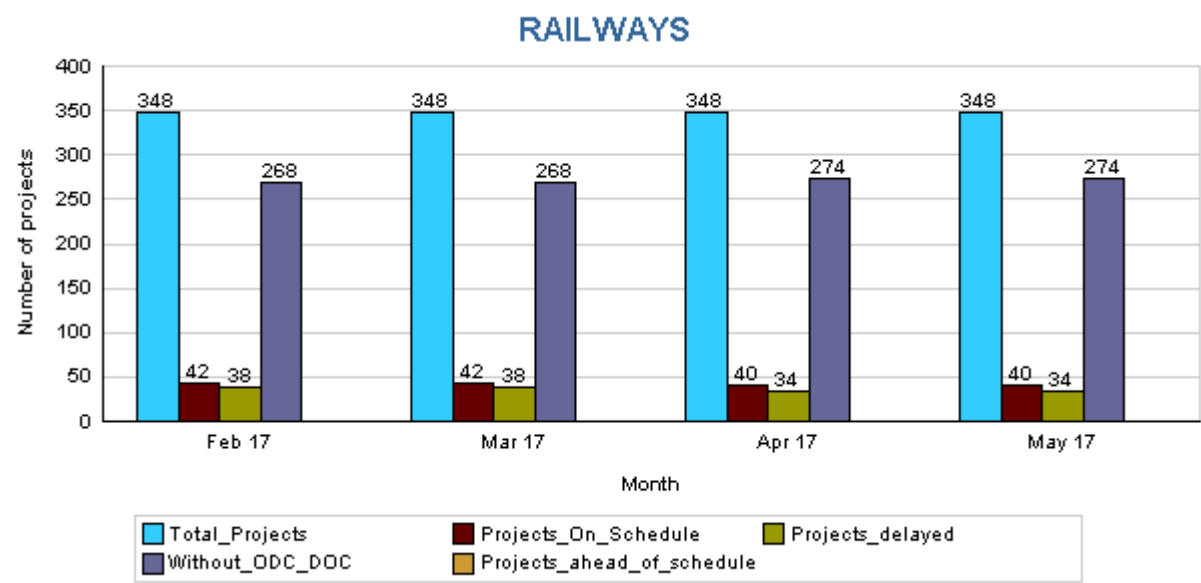


Break-up of 34 Delayed projects in May 2017

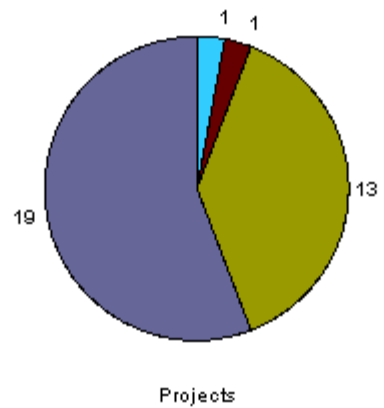


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Count	1	1	13	19

Graphical Presentation of All Projects w.r.t. Original Schedule

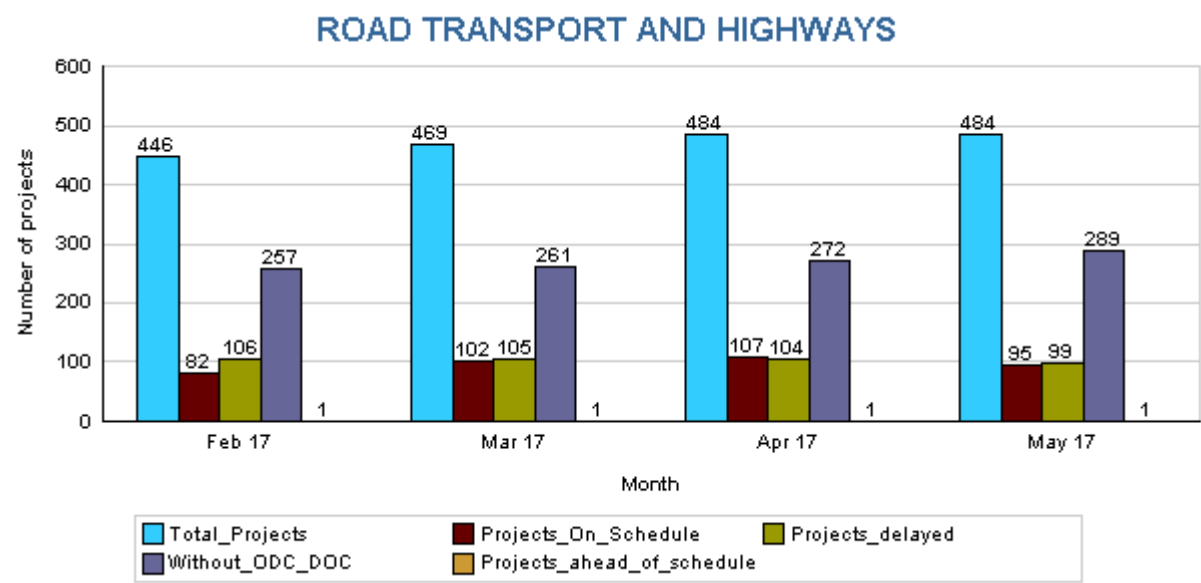

Break-up of 99 Delayed projects in May 2017

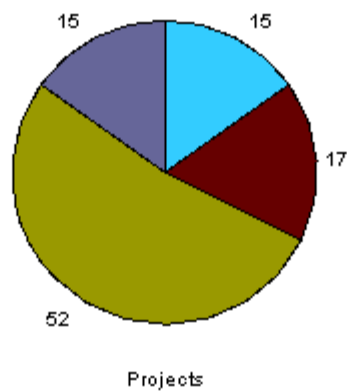


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- 60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

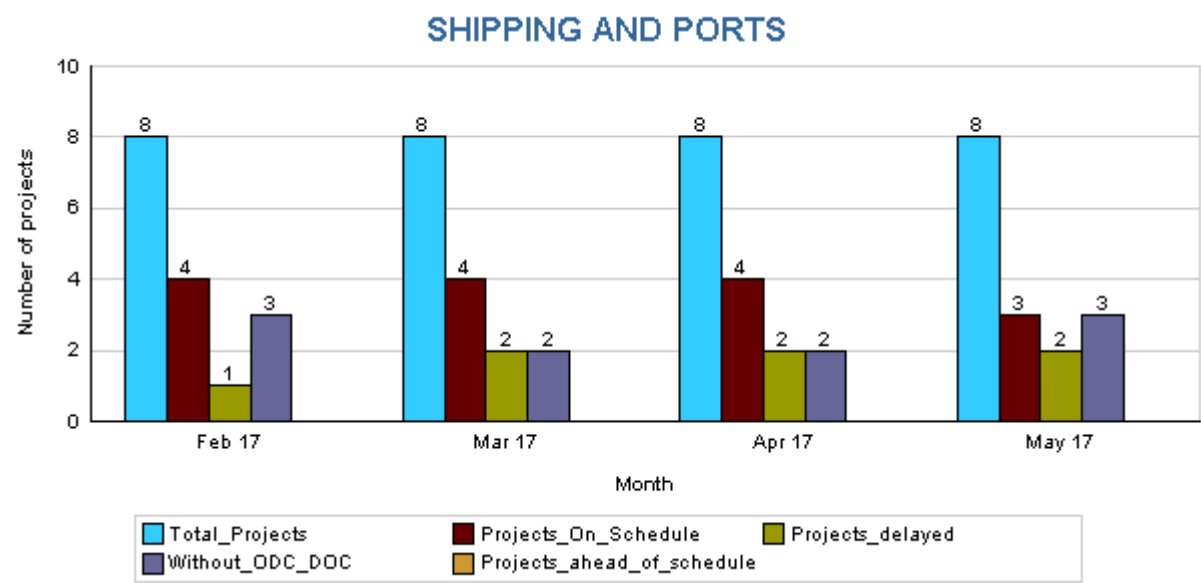


Break-up of 2 Delayed projects in May 2017

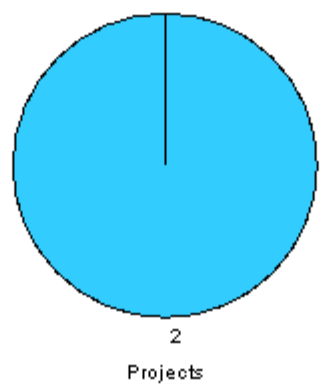


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

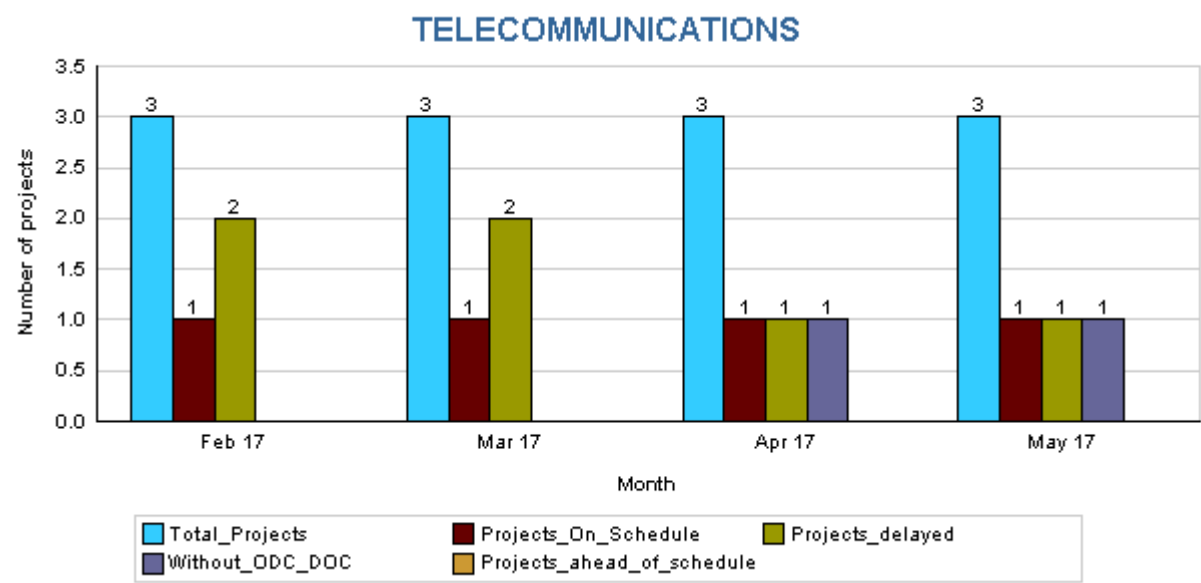


Break-up of 1 Delayed projects in May 2017

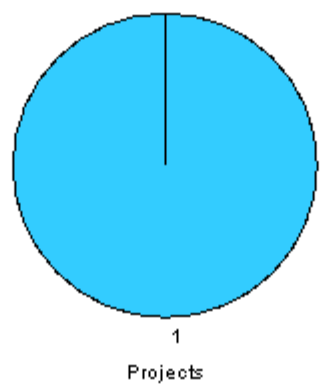


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

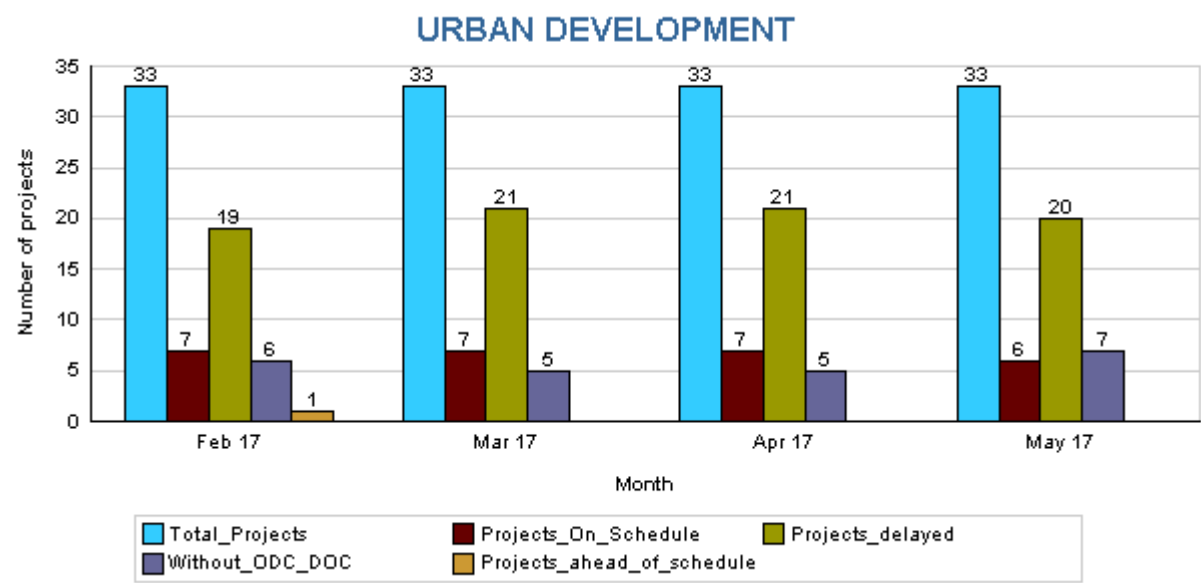


Break-up of 20 Delayed projects in May 2017

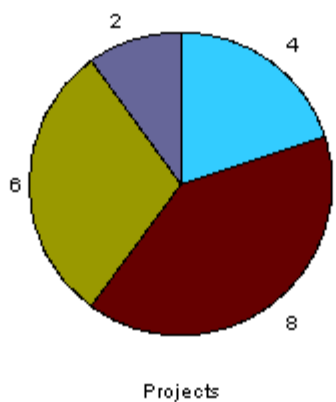

Delay in Months

Delay in Months	Number of Projects
1-12	4
13-24	8
25-60	6
60 and Above	2

Graphical Presentation of All Projects w.r.t. Original Schedule

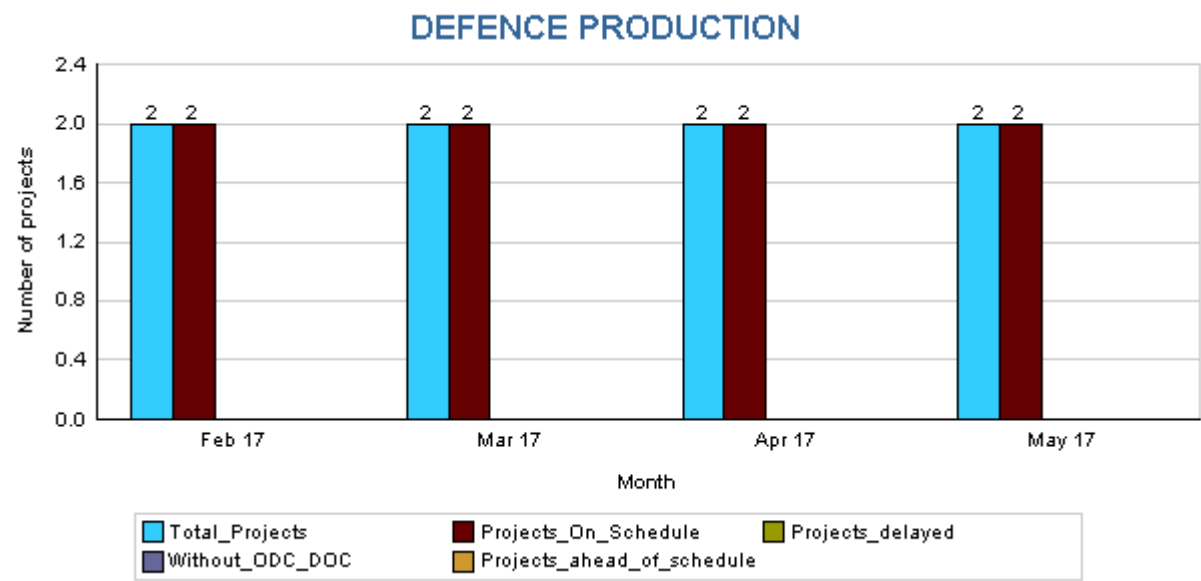

Delay in Months

Table-27

Sector-wise analysis of projects (costing Rs 150 crore and above)					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	467,26.00	52,241.00	44,697.43
CIVIL AVIATION	3	959.68	9,59.68	1,312.86	814.48
COAL	89	86,482.99	865,63.98	86,697.92	15,684.54
FERTILISERS	2	680.64	7,03.44	703.44	233.17
MINES	4	6,773.63	67,73.63	6,773.63	372.63
STEEL	35	57,753.65	581,34.62	57,967.33	34,533.61
PETROLEUM	95	1,88,746.90	1,913,63.71	1,89,467.02	58,375.08
POWER	128	3,43,460.25	3,773,33.57	3,93,759.12	2,15,028.58
HEAVY INDUSTRY	1	1,718.00	37,27.30	3,827.30	2289.00
HEALTH AND FAMILY WELFARE	13	3,637.08	36,37.08	3,649.38	1,598.30
RAILWAYS	348	3,52,470.03	3,881,71.98	4,41,335.56	1,19,196.86
ROAD TRANSPORT AND HIGHWAYS	484	3,15,935.94	3,178,97.35	3,22,248.77	1,04,899.30
SHIPPING AND PORTS	8	4,117.75	44,34.32	5,085.02	1,875.38
TELECOMMUNICATIONS	3	15,863.43	158,63.43	15,763.43	2,313.90
URBAN DEVELOPMENT	33	1,45,290.66	1,529,43.96	1,52,798.14	67,935.21
DEFENCE PRODUCTION	2	453.64	4,54.00	453.64	47.91
Grand total	1252	15,64,786.27	16,55,688.05	17,34,083.56	6,69,895.38

Table-28

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	11,459.00	9,980.00	12/2015 11/2016	11/2019	47(O) 36(R)	43/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	7,688.00	12/2016 03/2017	12/2020	48(O) 45(R)	32/68
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU ,	12/2001	13,171.00 17,270.00	22,462.00	21,600.00	12/2008 10/2013	03/2017	-	102/102
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,000.00	5,429.43	09/2010 09/2016	10/2017	85(O) 13(R)	81/87
	Total		40,442.00 -	52,241.00	44,697.43				258/327
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS ,	10/2013	314.61 -	441.33	24.13	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA ,	05/2010	335.61 -	318.00	305.59	05/2012 -	-	-	0/0
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017	80(O) 0(R)	0/0
	Total		959.68 -	1,312.86	814.48				0/0
	<u>COAL</u>								
8	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,326.67	03/2023 -	03/2023	0(O) -	11/16
9	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 7,612.33	7,612.33	1,251.27	03/2023 03/2023	03/2023	0(O) 0(R)	2/18
10	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 1,624.59	1,624.59	5.73	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.59	459.59	72.61	03/2015 03/2020	03/2020	60(O) 0(R)	2/7
12	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.00	03/2014 -	03/2020	72(O) -	1/7
13	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	199.20	03/2014 -	03/2018	48(O) -	0/2
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	199.20	03/2016 -	03/2018	24(O) -	4/7
15	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	143.44	03/2016 -	03/2018	24(O) -	3/6
16	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	.15	03/2022 -	03/2022	0(O) -	1/7
17	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	104.02	03/2020 -	03/2020	0(O) -	3/6
18	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	47.90	03/2018 -	03/2018	0(O) -	1/5

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
19	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	24.78	03/2020 -	03/2020	0(O) -	0/5
20	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	1/9
21	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/2
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	116.58	07/2012 03/2017	03/2021	104(O) 48(R)	2/3
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	119.45	03/2014 -	12/2017	45(O) -	4/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	92.97	03/2011 -	03/2020	108(O) -	2/2
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84(O) -	2/2
26	PUKNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND ,	07/2008	210.98 -	210.98	204.04	03/2013 -	03/2018	60(O) -	3/3
27	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	153.14	03/2012 -	03/2019	84(O) -	2/3
28	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	334.92	03/2016 -	03/2018	24(O) -	2/3
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	80.62	03/2014 -	03/2019	60(O) -	2/2
30	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
31	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	166.63	04/2015 -	04/2019	48(O) -	1/6
32	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	174.68	03/2020 -	03/2020	0(O) -	4/4
33	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.58	03/2021 -	03/2021	0(O) -	0/2
34	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	04/2017	-	1/3
35	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	145.88	05/2014 -	10/2017	41(O) -	0/8
36	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	134.69	04/2014 -	10/2017	42(O) -	0/10
37	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	7.06	03/2022 -	03/2022	0(O) -	0/21
38	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 486.57	486.57	268.54	03/2012 03/2018	03/2018	72(O) 0(R)	1/3
39	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	1,186.64	43.65	03/2023 -	03/2023	0(O) -	3/10
40	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
41	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	113.15	03/2021 -	03/2021	0(O) -	1/7
42	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	31.62	03/2021 -	03/2021	0(O) -	1/6
43	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	-	03/2022 -	03/2020	-24(O) -	0/6

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	.25	03/2023 -	03/2023	0(O) -	0/3
45	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	107.86	03/2021 -	03/2021	0(O) -	1/2
46	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	9.72	03/2022 -	03/2022	0(O) -	0/0
47	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	172.13	03/2020 -	03/2020	0(O) -	5/11
48	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	346.77	03/2020 -	03/2020	0(O) -	2/8
49	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	135.99	03/2021 -	03/2021	0(O) -	6/12
50	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	197.50	03/2018 -	03/2018	0(O) -	5/7
51	BHANEAGON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	187.94	71.92	03/2023 -	03/2023	0(O) -	6/11
52	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	83.66	03/2019 -	03/2019	0(O) -	10/13
53	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	58.98	03/2020 -	03/2020	0(O) -	3/10
54	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	70.75	03/2021 -	03/2021	0(O) -	2/6
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	222.50	03/2025 -	03/2025	0(O) -	3/13
56	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
57	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	-	03/2021 -	03/2021	0(O) -	2/6
58	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020	0(O) -	2/6
59	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	30.32	03/2019 -	03/2019	0(O) -	2/9
60	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	122.07	03/2019 -	03/2019	0(O) -	1/8
61	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	-	03/2022 -	03/2022	0(O) -	0/0
62	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	-	03/2022 -	03/2022	0(O) -	0/0
63	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	37.55	03/2021 -	03/2021	0(O) -	0/0
64	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.00	341.37	03/2010 -	03/2017	-	9/10
65	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	223.57	03/2017 -	05/2018	14(O) -	11/11
66	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 518.04	518.04	190.31	03/2010 -	03/2019	108(O) -	3/4
67	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	203.73	03/2013 -	03/2019	72(O) -	5/8
68	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	20.35	03/2019 -	03/2019	0(O) -	2/9
69	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	661.64	03/2026 -	03/2026	0(O) -	3/15

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
70	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	.78	03/2019 -	03/2019	0(O) -	3/6
71	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	341.27	03/2018 -	03/2018	0(O) -	2/5
72	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	351.47	03/2021 -	03/2021	0(O) -	1/9
73	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	2.56	09/2019 -	09/2019	0(O) -	0/0
74	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	67.25	12/2019 -	12/2019	0(O) -	0/0
75	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	1,813.37	12/2015 04/2018	04/2018	28(O) 0(R)	14/35
76	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU ,	04/2012	364.75 -	364.75	197.05	10/2014 06/2017	06/2017	32(O) 0(R)	8/10
77	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	188.63	06/2015 09/2019	09/2019	51(O) 0(R)	3/7
78	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU ,	05/2016	687.28 -	687.28	.06	06/2017 -	06/2017	0(O) -	0/0
79	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	249.03	126.88	03/2012 -	03/2019	84(O) -	32/42
80	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	03/2017	-	11/44
81	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 489.62	489.62	617.39	03/2012 03/2023	03/2023	132(O) 0(R)	0/2
82	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	96.89	03/2015 -	03/2018	36(O) -	29/31
83	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72(O) -	5/6
84	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 164.01	242.29	10.27	03/2015 03/2020	03/2020	60(O) 0(R)	0/5
85	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2020	60(O) -	4/29
86	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 437.51	437.51	224.01	03/2015 03/2021	03/2021	72(O) 0(R)	5/13
87	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	57.64	06/2015 -	03/2018	33(O) -	27/36
88	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 384.32	384.32	35.60	07/2016 03/2020	03/2020	44(O) 0(R)	19/28
89	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	486.27	92.33	03/2016 03/2018	03/2018	24(O) 0(R)	33/39
90	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	397.09	16.34	03/2019 03/2019	03/2019	0(O) 0(R)	6/18
91	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12(O) -	0/9
92	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17
93	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 1,131.28	1,131.28	404.31	03/2018 -	03/2018	0(O) -	6/10

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
94	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	190.44	11/2021 -	11/2021	0(O) -	0/0
95	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	209.13	03/2022 -	03/2022	0(O) -	6/12
96	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	297.66	03/2018 -	09/2018	6(O) -	7/15
	Total		86,482.99 -	86,697.92	15,684.54				372/851
	<u>FERTILISERS</u>								
97	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	72.73	11/2016 09/2017	09/2017	10(O) 0(R)	0/0
98	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 494.00	494.00	160.44	12/2017 -	12/2017	0(O) -	0/1
	Total		680.64 -	703.44	233.17				0/1
	<u>MINES</u>								
99	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 355.13	355.13	94.63	11/2016 12/2016	12/2016	-	1/1
100	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 -	5,540.00	.31	04/2021 04/2021	04/2021	0(O) 0(R)	1/1
101	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	157.34	01/2020 -	01/2020	0(O) -	1/1
102	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 344.50	344.50	120.35	11/2016 12/2016	09/2016	-	1/1
	Total		6,773.63 -	6,773.63	372.63				4/4
	<u>STEEL</u>								
103	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH ,	07/2011	974.76 -	974.76	478.53	07/2016 -	07/2017	12(O) -	1/1
104	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH ,	07/2011	877.73 -	877.73	728.59	07/2015 -	06/2017	23(O) -	2/2
105	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH ,	05/2012	404.16 -	404.16	394.74	07/2015 -	05/2017	22(O) -	0/1
106	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	190.50	10/2016 -	03/2018	17(O) -	0/0
107	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH ,	12/2009	280.00 -	280.00	140.55	09/2016 -	06/2017	9(O) -	1/1
108	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
109	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	427.35	12/2017 -	12/2017	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
110	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	-	08/2018 -	08/2018	0(O) -	0/0
111	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	-	07/2018 -	07/2018	0(O) -	0/0
112	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
113	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH ,	08/2010	17,265.00 -	17,265.00	15,905.00	03/2013 -	06/2017	51(O) -	35/37
114	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	61.26	04/2015 -	-	-	3/4
115	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	12,136.78	05/2015 12/2017	12/2017	31(O) 0(R)	53/85
116	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	25.34	06/2020 -	06/2020	0(O) -	4/12
117	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	12/2017	- -	0/0
118	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND ,	10/2013	245.67 -	245.67	115.64	05/2016 -	10/2017	17(O) -	1/3
119	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND ,	03/2015	255.19 -	255.19	27.42	03/2018 -	03/2018	0(O) -	0/1
120	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	53.68	10/2017 -	07/2018	9(O) -	0/2
121	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	78.00	12/2017 -	05/2018	5(O) -	1/2
122	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	13.64	09/2017 -	09/2017	0(O) -	0/0
123	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21(O) -	0/0
124	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
125	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
126	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
127	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	-	06/2019 -	06/2019	0(O) -	0/0
128	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 03/2016	03/2016	-	0/0
129	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	06/2017	18(O) -	0/0
130	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA ,	04/2015	3,127.30 -	3,127.30	309.85	04/2018 -	04/2018	0(O) -	1/2
132	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN ,	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17(O) -	0/0
133	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	06/2017	18(O) -	0/0
134	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12(O) -	0/0
135	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 07/2017	07/2017	7(O) 0(R)	0/0
136	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	40.47	09/2018 -	09/2018	0(O) -	0/0
137	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES (ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	03/2016	-	0/0
	Total		57,753.65 -	57,967.33	34,533.61				102/153
	<u>PETROLEUM</u>								
138	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020	0(O) -	0/0
139	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL, ANDHRA PRADESH ,	09/2016	407.00 -	1,879.00	16.42	09/2019 -	09/2019	0(O) -	3/27
140	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	-	06/2020 -	06/2020	0(O) -	0/0
141	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH ,	01/2015	342.00 -	342.00	-	03/2021 -	03/2021	0(O) -	0/0
142	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH ,	07/2014	247.00 -	247.00	-	03/2021 -	03/2021	0(O) -	0/0
143	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL, ARUNACHAL PRADESH ,	01/2016	247.52 247.52	247.52	.18	02/2019 -	12/2018	-2(O) -	2/10
144	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM ,	03/2009	2,465.15 2,378.89	2,378.89	1,931.23	03/2013 03/2018	03/2018	60(O) 0(R)	5/15
145	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS (WIP) - [N16000127]ONGC, ASSAM ,	06/2010	202.94 341.70	222.19	2.00	01/2014 11/2019	11/2019	70(O) 0(R)	0/2
146	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM ,	02/2014	163.88 -	163.88	144.38	07/2016 02/2017	01/2017	-	6/6
147	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM ,	03/2009	228.64 -	209.19	144.01	12/2016 -	03/2018	15(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
148	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	312.92	01/2018 -	01/2018	0(O) -	46/61
149	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM ,	06/2012	150.00 259.93	259.93	141.18	07/2014 09/2017	09/2017	38(O) 0(R)	4/12
150	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	-	08/2019 -	12/2018	-8(O) -	1/13
151	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	58.14	11/2019 -	11/2019	0(O) -	0/0
152	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	887.00	03/2015 -	05/2017	26(O) -	0/5
153	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	156.97	11/2018 -	11/2018	0(O) -	0/0
154	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	14.82	12/2020 -	12/2020	0(O) -	0/0
155	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	-	06/2020 -	06/2020	0(O) -	0/0
156	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH ,	01/2011	141.86 222.81	222.81	174.37	09/2016 02/2017	02/2017	-	12/12
157	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 -	4,701.44	1,960.89	05/2019 05/2019	10/2019	5(O) 5(R)	0/0
158	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT ,	09/2011	202.25 -	160.16	104.65	07/2016 06/2018	06/2018	23(O) 0(R)	5/12
159	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
160	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT , Central Sector Projects	11/2015	500.00 435.00	435.00	304.20	03/2017 06/2017	06/2017	3(O) 0(R)	0/1
161	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	123.00	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
162	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	107.72	03/2018 -	03/2018	0(O) -	14/22
163	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	327.78	6.97	04/2018 -	04/2018	0(O) -	12/20
164	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT ,	02/2016	931.00 -	931.00	237.72	07/2017 02/2018	02/2018	7(O) 0(R)	0/0
165	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	1.12	05/2019 -	12/2018	-5(O) -	1/13
166	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	-	09/2019 -	09/2019	0(O) -	0/0
167	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	112.86	05/2015 06/2017	06/2017	25(O) 0(R)	8/12
168	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 -	658.62	-	03/2023 -	03/2023	0(O) -	0/0
169	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA ,	02/2012	666.00 838.08	768.25	606.13	11/2015 11/2016	10/2016	-	29/29

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
170	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL, KARNATAKA ,	01/2006	993.00 1,693.00	1,693.00	1,537.45	01/2012 -	06/2017	65(O) -	0/0
171	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	136.00	02/2020 -	02/2020	0(O) -	0/0
172	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN, KARNATAKA ,	05/2015	224.00 207.00	207.25	24.96	04/2019 -	04/2019	0(O) -	2/8
173	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN, KARNATAKA ,	10/2015	135.00 170.70	170.70	33.30	03/2019 -	03/2019	0(O) -	3/11
174	BSVI UPGRADATION - [N16000257]MANGALORE REFIN, KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	-	12/2019 -	12/2019	0(O) -	3/9
175	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA ,	03/2012	16,504.00 -	16,504.00	11,257.06	03/2017 -	03/2017	-	15/16
176	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA ,	10/2015	607.06 714.25	714.25	99.05	10/2017 03/2019	03/2019	17(O) 0(R)	32/52
177	PALAKKAD LPG PLANT - [N16000225]BPCL, KERALA ,	02/2015	184.00 -	184.00	73.87	12/2017 -	12/2017	0(O) -	0/10
178	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA ,	11/2014	4,588.29 -	4,588.29	760.33	08/2018 -	08/2018	0(O) -	0/20
179	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA ,	02/2016	3,313.00 -	3,313.00	40.40	02/2020 -	01/2020	-1(O) -	0/0
180	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL, KERALA ,	05/2015	337.06 -	337.06	10.92	08/2018 -	08/2018	0(O) -	0/0
181	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	119.72	01/2017 06/2017	03/2018	14(O) 9(R)	0/0
182	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA ,	12/2009	1,584.00 -	1,584.00	1,355.45	03/2017 -	03/2017	-	12/12
183	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,079.94	05/2013 05/2017	10/2017	53(O) 5(R)	1/5
184	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,348.25	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
185	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA ,	03/2012	2,592.17 2,592.17	2,592.17	1,890.18	05/2014 12/2017	05/2018	48(O) 5(R)	0/21
186	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA ,	06/2014	5,706.47 5,813.25	5,813.25	5,359.34	05/2017 05/2018	05/2018	12(O) 0(R)	7/16
187	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	3,466.38	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
188	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA ,	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2017	05/2018	12(O) 12(R)	0/0
189	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	-	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
190	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL, MAHARASHTRA ,	05/2015	1,714.00 1,417.00	1,417.00	981.91	06/2017 06/2017	06/2017	0(O) 0(R)	0/21

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
191	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	3,961.54	3,019.16	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
192	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	442.98	04/2018 04/2018	04/2018	0(O) 0(R)	0/0
193	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	2.39	08/2021 -	08/2021	0(O) -	0/0
194	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	11.34	02/2020 -	02/2020	0(O) -	0/0
195	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	91.05	12/2019 -	12/2019	0(O) -	0/0
196	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA ,	05/2015	193.40 -	193.40	3.36	01/2019 -	01/2019	0(O) -	0/0
197	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	-	01/2021 -	01/2021	0(O) -	0/0
198	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	-	01/2021 -	01/2021	0(O) -	0/0
199	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	07/2009	3,957.00 3,561.00	3,397.00	911.00	01/2013 12/2018	12/2018	71(O) 0(R)	21/39
200	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	736.65	534.50	09/2011 06/2017	06/2017	69(O) 0(R)	0/0
201	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,387.47	12/2016 06/2017	06/2017	6(O) 0(R)	7/7
202	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE ,	04/2012	600.17 600.17	600.17	3,466.38	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
203	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	523.10	06/2018 -	06/2018	0(O) -	0/0
204	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE ,	08/2011	586.00 -	586.00	440.20	08/2015 03/2017	03/2017	-	11/11
205	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	333.57	10/2014 03/2018	03/2018	41(O) 0(R)	28/40
206	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	439.03	85.59	03/2017 11/2018	11/2018	20(O) 0(R)	0/0
207	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE ,	05/2013	4,124.35 4,259.49	4,259.49	3,201.25	04/2016 12/2017	12/2017	20(O) 0(R)	0/3
208	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	2.19	12/2020 -	12/2020	0(O) -	0/0
209	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	2.55	12/2020 -	12/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
210	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	3.62	10/2019 -	10/2019	0(O) -	0/0
211	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	-	07/2018 11/2019	11/2019	16(O) 0(R)	6/36
212	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	114.51	03/2020 -	03/2020	0(O) -	5/24
213	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	5.73	01/2019 -	01/2019	0(O) -	2/13
214	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	-	10/2020 -	10/2020	0(O) -	0/0
215	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	-	12/2019 -	12/2019	0(O) -	0/0
216	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	950.69	09/2017 12/2018	12/2018	15(O) 0(R)	2/6
217	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA ,	03/2014	238.50 -	238.50	153.97	03/2017 10/2017	10/2017	7(O) 0(R)	4/6
218	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 370.00	370.00	17.84	03/2013 01/2017	01/2017	-	0/24
219	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	7.98	06/2020 -	06/2020	0(O) -	0/0
220	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	1,687.77	11/2015 01/2017	05/2017	18(O) 4(R)	50/52
221	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU ,	05/2015	257.87 -	257.87	35.76	11/2016 -	02/2018	15(O) -	17/22
222	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11	4.16	04/2017 -	05/2017	1(O) -	20/22
223	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU ,	08/2014	393.00 -	393.00	165.80	04/2018 -	04/2018	0(O) -	0/10
224	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.06	02/2017 -	-	-	0/0
225	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 -	390.52	213.51	03/2019 -	04/2019	1(O) -	0/0
226	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	-	12/2018 -	12/2018	0(O) -	0/0
227	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA ,	05/2016	215.38 -	215.38	128.25	06/2017 06/2017	10/2017	4(O) 4(R)	0/0
228	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	1,427.94	273.08	12/2018 -	12/2018	0(O) -	9/20
229	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,	03/2014	3,076.00 -	3,076.00	1,565.57	09/2017 06/2018	06/2018	9(O) 0(R)	5/7
230	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL ,	08/2014	190.45 190.45	190.45	104.95	09/2017 03/2018	03/2018	6(O) 0(R)	0/0
231	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 -	694.00	117.93	10/2018 -	10/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
232	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]OCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	-	12/2020 -	12/2020	0(O) -	0/0
	Total		1,88,746.90 -	1,89,467.02	58,375.08				410/840
	<u>POWER</u>								
233	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH ,	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	-	2/2
234	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH ,	03/2015	550.06 -	550.06	406.10	03/2018 -	12/2017	-3(O) -	0/3
235	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH ,	01/2016	207.88 -	207.88	28.80	07/2018 -	07/2018	0(O) -	0/0
236	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	17,435.15	9,315.46	09/2010 -	-	-	0/0
237	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	5,649.46	12/2009 01/2018	01/2018	97(O) 0(R)	16/30
238	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH ,	12/2008	573.99 1,337.76	1,337.76	1,399.06	08/2013 12/2017	12/2017	52(O) 0(R)	31/38
239	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 6,749.18	6,749.18	6,580.00	09/2011 06/2017	12/2017	75(O) 6(R)	30/37
240	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	13,201.00	01/2011 05/2018	05/2018	88(O) 0(R)	26/47
241	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 7,998.00	5,353.00	5,472.83	05/2014 03/2017	03/2018	46(O) 12(R)	1/18
242	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR ,	03/2010	3,984.03 -	3,984.03	3,290.44	01/2013 -	03/2016	-	1/1
243	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	12,964.60	6,002.44	01/2018 -	06/2018	5(O) -	27/31
244	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	465.36	12/2016 -	12/2017	12(O) -	7/7
245	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.13	164.50	06/2019 -	06/2019	0(O) -	0/0
246	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH ,	11/2011	2,127.51 2,619.56	2,619.56	2,563.73	07/2014 09/2017	09/2017	38(O) 0(R)	6/8
247	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH ,	12/2011	1,746.65 2,228.71	2,228.71	1,882.93	08/2014 12/2017	12/2017	40(O) 0(R)	7/11
248	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH ,	03/2012	9,569.76 9,291.03	9,291.03	7,148.89	06/2015 06/2017	06/2017	24(O) 0(R)	27/30
249	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	11,846.00	8,103.00	06/2017 12/2017	04/2018	10(O) 4(R)	29/40
250	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	10.50	05/2017 06/2019	06/2019	25(O) 0(R)	4/9

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
251	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	8.20	10/2018 10/2018	10/2018	0(O) 0(R)	0/0
252	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT ,	12/2011	552.44 609.44	609.44	501.60	02/2014 03/2016	03/2016	-	10/10
253	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT ,	02/2014	378.71 -	378.71	257.90	10/2016 04/2017	04/2017	-	10/11
254	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT ,	10/2015	315.00 -	315.00	14.61	10/2016 -	10/2016	-	2/2
255	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT ,	01/2016	244.19 -	244.19	71.90	07/2018 -	07/2018	0(O) -	0/0
256	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	7.50	12/2018 -	12/2018	0(O) -	0/0
257	KANDORNA AND BHANWAD WIND FARM - [N18000234]THDCIL,GUJARAT ,	11/2016	415.49 -	415.49	-	03/2017 -	03/2017	-	1/2
258	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	110.40	11/2017 -	11/2017	0(O) -	1/4
259	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	6,275.55	09/2009 -	12/2018	111(O) -	2/3
260	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,HIMACHAL PRADESH ,	12/2005	358.42 -	358.42	-	12/2008 09/2010	-	-	0/15
261	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR ,	01/2009	3,642.04 -	5,783.17	4,892.47	01/2016 -	01/2018	24(O) -	5/6
262	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	139.96	04/2020 -	01/2023	33(O) -	0/0
263	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,352.57	945.96	09/2017 -	09/2018	12(O) -	0/0
264	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	14,366.58	4,911.00	02/2019 02/2020	02/2021	24(O) 12(R)	14/18
265	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND ,	08/2006	2,313.00 4,138.41	4,366.64	3,484.00	12/2011 03/2016	02/2017	-	14/14
266	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	1,681.43	10/2017 -	10/2017	0(O) -	0/0
267	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	15,166.19	13,390.00	01/2017 07/2017	07/2017	6(O) 0(R)	46/46
268	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	11,639.00	7,508.00	09/2017 03/2018	03/2018	6(O) 0(R)	23/41
269	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	9,870.51	2,703.00	09/2019 -	09/2019	0(O) -	17/19
270	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	102.60	03/2017 10/2017	10/2017	7(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
271	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	-	06/2018 -	06/2018	0(O) -	0/0
272	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	641.09	09/2010 12/2017	12/2017	87(O) 0(R)	4/8
273	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 03/2017	03/2017	-	41/41
274	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	7,620.00	11/2016 12/2017	04/2018	17(O) 4(R)	32/36
275	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM ,	07/1998	368.72 1,441.52	1,329.43	1,212.66	07/2006 09/2017	09/2017	134(O) 0(R)	6/13
276	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,466.58	10/2012 02/2018	02/2018	64(O) 0(R)	8/11
277	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,547.20	08/2013 12/2017	12/2017	52(O) 0(R)	22/26
278	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,517.90	12/2012 02/2018	02/2018	62(O) 0(R)	12/23
279	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE ,	02/2010	232.34 -	245.00	237.49	06/2012 -	06/2017	60(O) -	1/4
280	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE ,	07/2010	752.64 757.94	757.94	616.22	07/2013 06/2017	06/2017	47(O) 0(R)	7/9
281	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE ,	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	03/2016	-	11/12
282	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,391.53	11/2012 12/2017	12/2017	61(O) 0(R)	10/13
283	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	481.82	06/2014 03/2018	03/2018	45(O) 0(R)	10/12
284	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 346.79	426.29	353.47	08/2014 12/2017	12/2017	40(O) 0(R)	8/10
285	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE ,	03/2012	198.63 -	198.63	129.33	09/2014 09/2017	09/2017	36(O) 0(R)	0/0
286	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE ,	11/2011	723.63 882.13	882.13	704.52	11/2014 06/2017	06/2017	31(O) 0(R)	7/10
287	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 703.10	703.10	549.20	06/2015 12/2017	12/2017	30(O) 0(R)	7/10
288	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	2,514.88	1,878.35	12/2015 12/2017	12/2017	24(O) 0(R)	15/18
289	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE ,	09/2013	1,575.30 1,656.15	1,656.15	1,296.40	05/2016 05/2017	06/2017	13(O) 1(R)	10/13
290	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,119.84	04/2016 09/2017	09/2017	17(O) 0(R)	8/12
291	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	67.00	04/2016 12/2017	12/2017	20(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
292	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	378.30	06/2016 02/2018	02/2018	20(O) 0(R)	8/11
293	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE ,	02/2014	908.08 969.97	969.97	648.20	06/2016 02/2018	02/2018	20(O) 0(R)	13/18
294	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE ,	05/2014	829.98 -	829.98	396.40	08/2016 10/2017	10/2017	14(O) 0(R)	2/4
295	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 550.18	550.18	347.20	11/2016 11/2017	11/2017	12(O) 0(R)	7/12
296	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	121.70	03/2016 07/2017	07/2017	16(O) 0(R)	3/6
297	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE ,	06/2014	400.47 -	400.47	265.20	04/2017 -	04/2017	-	1/3
298	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	1,168.60	03/2018 -	03/2018	0(O) -	8/12
299	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE ,	08/2014	288.49 376.09	376.09	195.40	02/2017 06/2017	06/2017	4(O) 0(R)	6/12
300	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 244.66	244.66	100.10	02/2016 06/2017	06/2017	16(O) 0(R)	8/17
301	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE ,	12/2014	6,517.36 -	6,517.36	2,983.30	04/2018 -	04/2018	0(O) -	3/12
302	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	122.30	03/2018 -	03/2018	0(O) -	0/3
303	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	115.10	10/2017 -	10/2017	0(O) -	0/5
304	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	145.40	07/2017 07/2017	07/2017	0(O) 0(R)	3/5
305	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE ,	01/2015	3,662.02 -	3,662.02	2,210.30	05/2018 -	12/2017	-5(O) -	2/5
306	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	40.10	03/2018 -	03/2018	0(O) -	0/0
307	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	300.00	09/2017 -	09/2017	0(O) -	0/0
308	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	1,653.40	04/2018 -	04/2018	0(O) -	4/9
309	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE ,	04/2015	1,479.30 -	1,479.30	551.80	04/2017 03/2018	03/2018	11(O) 0(R)	2/8
310	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	317.00	07/2018 -	07/2018	0(O) -	0/0
311	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	224.50	07/2018 -	07/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
312	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	116.50	01/2018 -	01/2018	0(O) -	0/0
313	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	.60	11/2018 -	11/2018	0(O) -	0/0
314	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	248.90	05/2019 -	05/2019	0(O) -	0/0
315	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	499.30	11/2019 -	11/2019	0(O) -	0/0
316	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE ,	04/2016	810.48 -	810.48	170.10	12/2018 -	12/2018	0(O) -	0/0
317	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	21.70	11/2018 -	11/2018	0(O) -	0/0
318	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	1.10	07/2018 -	07/2018	0(O) -	0/0
319	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	14.60	03/2019 -	03/2019	0(O) -	0/0
320	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	.40	02/2019 -	02/2019	0(O) -	0/0
321	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	10.80	02/2019 -	02/2019	0(O) -	0/0
322	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	-	03/2019 -	03/2019	0(O) -	0/0
323	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	-	06/2019 -	06/2019	0(O) -	0/0
324	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE ,	10/2016	167.75 -	167.75	-	04/2019 -	04/2019	0(O) -	0/0
325	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	2.40	11/2019 -	11/2019	0(O) -	0/0
326	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	21.80	01/2019 -	01/2019	0(O) -	0/0
327	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	-	04/2019 -	04/2019	0(O) -	0/0
328	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	-	02/2020 -	02/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	.20	02/2019 -	02/2019	0(O) -	0/0
330	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	-	03/2019 -	03/2019	0(O) -	0/0
331	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	-	06/2019 -	06/2019	0(O) -	0/0
332	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	19.60	12/2019 -	12/2019	0(O) -	0/0
333	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	-	09/2019 -	09/2019	0(O) -	0/0
334	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	-	04/2020 -	04/2020	0(O) -	0/0
335	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	-	06/2019 -	06/2019	0(O) -	0/0
336	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	4,754.42	260.20	12/2018 -	12/2019	12(O) -	0/0
337	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	5,111.33	246.00	12/2018 -	12/2019	12(O) -	0/0
338	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	12,532.44	5,571.00	08/2018 -	08/2018	0(O) -	23/27
339	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA ,	01/2016	187.04 -	187.04	54.60	06/2018 -	05/2017	-13(O) -	0/0
340	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	51.70	04/2019 -	04/2019	0(O) -	0/0
341	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	117.50	11/2017 -	11/2017	0(O) -	0/0
342	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN ,	02/2015	302.49 302.00	302.49	270.77	02/2016 -	-	-	1/1
343	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	76.50	01/2019 -	01/2019	0(O) -	0/0
344	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	1,939.45	11/2008 09/2018	09/2018	118(O) 0(R)	20/22
345	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 2,702.65	2,702.65	2,312.86	09/2014 06/2017	06/2017	33(O) 0(R)	11/13
346	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU ,	01/2016	162.11 -	162.11	93.20	05/2018 -	05/2018	0(O) -	0/0
347	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	837.00	07/2020 -	07/2020	0(O) -	11/18

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
348	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 1,078.31	1,078.31	963.23	07/2013 -	-	-	26/26
349	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA ,	05/2016	409.19 -	409.19	28.90	05/2018 -	05/2018	0(O) -	0/0
350	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	1,259.00	12/2016 03/2017	03/2017	-	28/28
351	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	2,697.00	03/2019 -	03/2019	0(O) -	19/25
352	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	195.42	116.41	02/2014 -	02/2018	48(O) -	2/3
353	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	5,079.75	12/2016 -	03/2018	15(O) -	28/34
354	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 3,846.30	3,846.30	3,156.00	03/2013 06/2019	06/2019	75(O) 0(R)	3/15
355	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	2,491.58	1,182.02	06/2013 -	12/2019	78(O) -	7/11
356	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,527.00	146.00	08/2017 -	08/2017	0(O) -	0/9
357	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL ,	04/2010	4,404.57 5,135.01	5,135.01	3,289.85	01/2015 03/2018	03/2018	38(O) 0(R)	12/16
358	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	262.00	09/2019 -	09/2019	0(O) -	5/6
359	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL ,	04/2007	4,122.00 8,781.30	9,142.58	8,300.00	02/2011 -	03/2016	-	26/26
360	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	29.70	04/2018 -	04/2018	0(O) -	0/0
	Total		3,43,460.25 -	3,93,759.12	2,15,028.58				870/1206
	<u>HEAVY INDUSTRY</u>								
361	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 3,727.30	3,827.30	2289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
362	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
363	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
364	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI ,	09/2013	444.70 -	444.70	326.30	12/2015 -	07/2016	-	0/0
365	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI ,	11/2013	196.70 -	209.00	170.00	01/2016 -	01/2016	-	0/0
366	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	127.00	05/2017 -	12/2017	7(O) -	0/2

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
367	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	184.70	05/2017 -	12/2017	7(O) -	0/5
368	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	505.58	174.00	03/2018 -	03/2018	0(O) -	0/2
369	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	312.99	80.00	08/2018 -	08/2018	0(O) -	0/1
370	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	-	05/2018 08/2019	08/2019	15(O) 0(R)	0/0
371	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	28.00	02/2018 -	02/2018	0(O) -	0/1
372	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH ,	10/2013	159.50 -	159.50	144.80	11/2013 -	10/2016	-	0/8
373	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	168.90	68.00	05/2017 07/2017	10/2017	5(O) 3(R)	0/3
374	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	41.00	09/2018 -	09/2018	0(O) -	0/0
	Total		3,637.08 -	3,649.38	1,598.30				0/22
	<u>RAILWAYS</u>								
375	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	155.74 843.45	966.98	874.72	02/2009 12/2017	12/2017	106(O) 0(R)	0/0
376	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	330.00 1,045.20	2,125.18	14.17	- -	03/2021	- -	0/0
377	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH ,	04/2003	136.62 -	376.00	367.85	12/2007 03/2010	-	-	0/0
378	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	743.00 -	1,825.00	831.39	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
379	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	283.54 -	759.41	.51	- -	-	-	0/0
380	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.48	- -	-	-	0/1
381	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	1,313.48 -	1,313.48	8.06	- -	-	-	0/1
382	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	193.46	- -	03/2020	- -	0/0
383	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	-	- -	-	-	0/0
384	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	4,000.00 3,631.00	3,631.00	-	- -	-	-	0/0
385	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,246.26	-	- -	-	-	0/0
386	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	-	03/2021 -	03/2021	0(O) -	0/0
387	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]JCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	03/2018	0(O) -	0/0
388	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM ,	09/1997	1,500.00 -	5,000.00	4,090.26	04/2008 12/2011	06/2018	122(O) 78(R)	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
389	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM ,	09/2006	200.00 -	780.00	285.64	- -	03/2019	- -	0/0
390	KATAKHAL TO BHAIKABI - [N22000126]NFR,ASSAM ,	04/1998	227.90 -	509.00	286.07	12/2012 -	03/2016	-	0/0
391	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM ,	04/1996	1,676.31 -	7,000.00	6,068.59	03/2009 -	03/2017	-	0/0
392	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12 -	508.00	285.31	- -	03/2019	- -	0/0
393	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	.57	- -	03/2019	- -	0/0
394	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM ,	04/2003	971.22 -	966.27	834.11	- -	12/2009	-	0/0
395	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM ,	04/2003	4,300.00 -	4,520.00	4,043.90	- -	05/2015	-	0/0
396	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM ,	04/2007	180.09 -	180.00	153.11	- -	05/2011	-	0/0
397	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.32	-	- -	03/2021	- -	0/0
398	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	870.96	-	- -	03/2021	- -	0/0
399	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR ,	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0
400	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	492.98 -	1,320.00	758.76	12/2010 -	-	-	0/0
401	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	541.00	183.72	- -	-	-	0/0
402	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	324.66	330.82	- -	-	-	0/0
403	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR ,	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
404	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
405	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	413.56	343.54	- -	10/2017	- -	0/0
406	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	332.92 332.92	477.88	495.40	03/2012 -	-	-	0/0
407	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR ,	09/2006	300.00 -	2,145.00	361.21	- -	03/2020	- -	0/0
408	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR ,	04/2008	282.92 -	360.00	3.13	- -	-	-	0/0
409	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	490.80 633.87	490.80	.39	- -	-	-	0/0
410	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	-	- -	-	-	0/0
411	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	445.25	-	- -	-	-	0/0
412	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
413	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
414	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
415	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
416	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
417	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
418	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
419	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	304.41 -	304.41	.19	- -	-	-	0/0
420	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
421	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
422	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
423	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
424	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
425	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	-	- -	-	-	0/0
426	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(O) -	0/1
427	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(O) -	1/1
428	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
429	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	304.00 -	631.78	252.28	12/2012 -	-	-	0/0
430	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	516.40	370.69	03/2010 -	12/2017	93(O) -	0/3
431	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	268.41	- 03/2020	03/2020	- 0(R)	0/1
432	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	432.25	03/2020 -	03/2020	0(O) -	0/0
433	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	135.51	03/2018 -	03/2018	0(O) -	0/0
434	GRADE SEPERATOR AT DAYABASTI - [N22000269]JNR,DELHI ,	04/1999	156.65 197.17	197.17	56.10	- -	-	-	0/0
435	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]JNR,DELHI ,	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
436	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]JWR,GUJARAT ,	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
437	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45(O) -	0/0
438	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84(O) -	0/0
439	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
440	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	21.53	- -	03/2020	- -	0/0
441	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	376.59 -	644.38	.11	- -	12/2020	- -	0/0
442	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	439.88 -	845.68	.78	- -	-	-	0/0
443	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	399.63	-	- -	03/2019	- -	0/0
444	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,266.89	55.00	- -	12/2020	- -	0/0
445	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	- -	0/0
446	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 -	355.00	323.64	- -	-	-	0/0
447	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	- -	0/0
448	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	03/2019	0(O) -	0/0
449	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA ,	01/2004	238.56 717.15	740.00	745.02	03/2012 01/2016	01/2016	-	0/0
450	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	- -	-	-	0/0
451	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	-	- -	-	-	0/0
452	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA ,	05/2015	400.00 -	400.00	-	- -	-	-	0/0
453	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	186.13	03/2019 -	03/2019	0(O) -	0/0
454	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	2,966.99	3.56	- -	-	-	0/0
455	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018	193(O) -	0/0
456	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 1,125.89	1,125.89	980.99	12/2011 03/2020	03/2020	99(O) 0(R)	0/0
457	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND ,	04/1997	194.07 -	335.00	226.39	06/2004 -	-	-	0/0
458	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
459	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	318.00	258.17	02/2006 -	12/2019	166(O) -	0/1
460	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 167.73	167.73	207.11	03/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
461	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	583.00	279.37	12/2015 -	-	-	0/0
462	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	32.81	-	12/2017	-	0/0
463	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	209.00	38.98	12/2016 -	-	-	0/0
464	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	100.00	03/2021 -	03/2021	0(O)	0/0
465	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA ,	02/1997	295.00 1,289.92	1,289.92	1,439.40	-	01/2017	-	0/1
466	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	135.11	-	-	-	0/0
467	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA ,	02/1998	242.42 369.70	1,542.41	927.68	-	-	-	0/1
468	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	5.59	-	-	-	0/0
469	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA ,	04/2007	482.00 874.57	874.57	968.06	03/2013 -	-	-	0/0
470	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 -	1,801.01	2.55	-	-	-	0/0
471	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	718.02	-	-	-	0/1
472	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	260.40	-	-	-	0/1
473	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	-	-	-	-	0/0
474	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 -	832.47	.94	-	-	-	0/0
475	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 -	348.85	.35	-	-	-	0/0
476	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	598.29	-	03/2019	-	0/1
477	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.32	-	-	-	0/0
478	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 1,922.00	1,922.00	2.88	-	-	-	0/0
479	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	-	-	-	-	0/0
480	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	1.51	01/1999 -	-	-	0/0
481	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA ,	04/2010	203.40 203.40	273.84	276.15	-	-	-	0/0
482	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	341.86	-	-	-	0/5
483	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	266.97	-	03/2020	-	0/2
484	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 -	1,566.00	235.68	-	-	-	0/0
485	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	7.16	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
486	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	342.85	360.22	- -	-	-	0/0
487	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.17	- -	-	-	0/0
488	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	900.00	-	- -	-	-	0/0
489	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,000.00	-	- -	-	-	0/0
490	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 1,849.60	2,713.09	632.05	- 03/2021	03/2021	- 0(R)	0/0
491	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	03/2017	-	0/0
492	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH ,	09/2007	687.20 -	950.00	913.84	03/2010 -	06/2017	87(O) -	0/0
493	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 1,030.29	1,030.29	628.11	03/2012 -	12/2016	-	0/0
494	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
495	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.65	329.46	12/2020 -	12/2020	0(O) -	0/0
496	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 2,478.23	2,478.23	-	03/2022 03/2022	03/2022	0(O) 0(R)	0/1
497	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 582.13	582.13	-	03/2020 03/2020	03/2020	0(O) 0(R)	0/1
498	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	74.22	03/2019 -	03/2019	0(O) -	0/0
499	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.23	688.04	06/1999 12/2020	12/2020	258(O) 0(R)	0/0
500	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	514.44	03/2004 03/2020	03/2020	192(O) 0(R)	0/0
501	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	812.01	- 12/2020	-	-	0/0
502	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
503	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	-	0/0
504	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 2,491.43	3,168.29	532.82	- 03/2023	-	-	0/0
505	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	52.35	- 03/2021	-	-	0/0
506	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	142.22	- 03/2019	-	-	0/0
507	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	98.02	- 03/2022	-	-	0/0
508	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	-	- 03/2024	-	-	0/0
509	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	2,425.00	-	- 03/2024	-	-	0/0
510	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	2,750.00	-	- -	-	-	0/0
511	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	19.48	- 03/2022	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 2,449.91	2,449.91	.63	- 03/2023	-	-	0/0
513	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.47	3,627.47	-	- 03/2023	-	-	0/0
514	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	-	- 03/2023	-	-	0/0
515	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 -	1,035.16	-	- 03/2022	-	-	0/0
516	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 -	637.95	.35	- 03/2022	-	-	0/0
517	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,514.45	839.11	03/2020 -	03/2020	0(O) -	0/0
518	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.14	12/2025 -	12/2025	0(O) -	0/0
519	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021	0(O) -	0/0
520	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	212.71	03/2019 -	03/2019	0(O) -	0/0
521	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 4,454.18	9,658.00	4,927.46	03/2011 -	03/2020	108(O) -	0/0
522	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02 -	6,000.00	14.80	- -	03/2021	- -	0/0
523	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 2,393.48	4,600.00	549.89	04/2014 -	03/2020	71(O) -	0/0
524	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 608.02	634.48	629.43	03/1994 02/2016	02/2016	-	0/0
525	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.02	- -	-	-	0/0
526	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 1,160.54	1,776.81	967.96	03/1998 -	12/2019	261(O) -	0/0
527	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
528	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 372.09	525.00	544.20	- 03/2019	03/2019	- 0(R)	0/0
529	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 4,327.28	6,093.31	972.82	05/2008 03/2023	03/2023	178(O) 0(R)	0/4
530	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 744.71	1,126.79	751.05	- -	-	-	1/1
531	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 781.02	876.10	841.57	06/2007 -	-	-	0/0
532	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
533	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019	123(O) -	0/0
534	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE ,	04/1998	92.63 228.08	350.00	316.64	02/2011 -	-	-	0/0
535	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 724.89	973.33	613.71	12/2012 12/2012	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
536	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	718.54	265.71	- -	05/2019	- -	0/0
537	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE ,	12/2006	170.00 -	436.00	435.57	03/2011 -	10/2011	-	0/0
538	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	268.78	87.86	- -	08/2017	- -	0/0
539	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	66.66	- -	05/2018	- -	0/0
540	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	270.58	- -	-	-	0/0
541	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	331.91	- 03/2022	03/2022	- 0(R)	0/0
542	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,562.27	177.84	- -	-	-	0/1
543	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
544	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	10.34	02/2019 12/2022	12/2022	46(O) 0(R)	0/0
545	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	553.63 -	1,009.00	7.88	- -	-	-	0/0
546	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 549.75	549.75	14.62	- -	-	-	0/0
547	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0
548	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	523.52	2.26	- -	-	-	0/0
549	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE ,	04/2008	822.39 -	1,480.83	1,421.19	- -	03/2018	- -	0/1
550	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	346.15	253.87	- -	-	-	0/0
551	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	45.36	- -	-	-	0/0
552	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 210.00	394.28	148.33	- -	03/2017	-	0/0
553	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82 -	450.00	.79	- -	03/2019	- -	0/0
554	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17 -	1,871.00	1,081.00	- -	03/2018	- -	0/0
555	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 -	800.00	56.77	- -	-	-	0/0
556	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 319.58	319.58	141.88	- -	-	-	0/0
557	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 290.85	290.85	9.31	- -	-	-	0/0
558	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 260.60	260.60	6.42	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
559	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 1,130.13	1,130.13	.30	- -	-	-	0/0
560	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 234.41	234.41	161.17	03/2015 -	-	-	0/0
561	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 238.36	238.36	51.31	- -	-	-	0/0
562	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 332.14	332.14	87.22	- 03/2019	-	-	0/0
563	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	227.50	- -	-	-	0/0
564	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 595.91	595.91	103.62	- -	-	-	0/0
565	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 104.80	160.97	56.25	- -	-	-	0/0
566	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 266.00	266.00	92.93	- -	12/2012	-	0/0
567	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 198.88	198.88	15.83	- -	-	-	0/0
568	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 157.94	157.94	47.63	- -	11/2018	- -	0/0
569	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	251.05	15.66	- -	-	-	0/0
570	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
571	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	350.78	98.15	- -	-	-	0/0
572	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 186.64	186.64	150.28	- -	-	-	0/0
573	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 173.91	173.91	18.54	- -	-	-	0/0
574	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.11	03/2017 -	03/2017	-	0/0
575	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 370.81	369.69	31.99	- -	-	-	0/0
576	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 131.47	153.02	52.01	- -	-	-	0/0
577	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 79.39	186.89	62.73	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
578	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 681.68	681.68	135.79	- -	-	-	0/0
579	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66 579.03	720.59	456.58	03/2017 -	03/2017	-	0/0
580	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
581	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
582	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE ,	04/2007	98.74 203.00	381.39	312.12	- 03/2017	-	-	0/0
583	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE ,	04/2006	96.16 260.16	280.00	268.37	- -	-	-	0/0
584	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 -	2,200.00	85.33	- -	-	-	0/0
585	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	1.11	- -	-	-	0/1
586	DELHI-SOHNALAH-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
587	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
588	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	-	- -	-	-	0/0
589	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 -	1,714.49	581.72	- -	-	-	0/2
590	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 -	792.01	1.13	- -	-	-	0/1
591	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,050.00	200.35	- -	-	-	0/1
592	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
593	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
594	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	-	- -	-	-	0/0
595	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
596	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 259.23	259.23	8.43	- -	-	-	0/0
597	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE ,	04/2007	313.24 -	554.70	342.00	01/1999 06/2017	06/2017	221(O) 0(R)	0/0
598	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
599	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	648.00	-	- -	02/2019	-	0/0
600	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	34.03	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
601	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	237.57	- -	03/2020	- -	0/0
602	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	355.19	- -	-	-	0/0
603	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 678.54	678.54	-	- 12/2018	12/2018	- 0(R)	0/38
604	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	- -	-	-	0/0
605	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	.14	- 03/2021	03/2021	- 0(R)	0/0
606	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	-	- -	-	-	0/0
607	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE ,	04/1992	315.64 -	315.00	307.28	-	08/2014	-	0/0
608	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE ,	04/2006	614.54 -	613.00	511.74	- -	04/2014	-	0/0
609	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	147.52	03/2015 -	03/2020	60(O) -	0/0
610	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	- -	0/0
611	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	470.21 -	3,004.90	572.56	- 06/2021	06/2021	- 0(R)	0/0
612	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,185.64	620.08	- 09/2009	03/2019	- 114(R)	0/0
613	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA ,	04/1999	166.16 -	370.00	353.00	02/2009 02/2009	02/2017	-	0/1
614	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.70	199.98	02/2015 -	12/2019	58(O) -	0/0
615	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	340.00	327.59	03/2009 03/2009	02/2017	-	1/1
616	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	247.50	- 03/2021	06/2022	- 15(R)	0/0
617	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	-	0/0
618	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27 1,111.99	1,579.27	168.29	- 03/2020	03/2021	- 12(R)	0/0
619	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67 843.04	843.04	4.30	- 03/2021	03/2021	- 0(R)	0/0
620	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA ,	03/2006	201.00 230.00	230.00	244.18	- 10/2015	10/2015	-	0/0
621	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	94.33	- -	03/2020	- -	0/0
622	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA ,	03/2011	165.16 -	234.71	224.99	03/2015 -	07/2015	-	0/0
623	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021	0(O) -	0/0
624	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	-	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
625	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	701.61	-	03/2021 -	03/2021	0(O) -	0/0
626	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	-	03/2021 03/2021	03/2021	0(O) 0(R)	0/0
627	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	12.00	03/2020 -	03/2020	0(O) -	0/0
628	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	183.93	12/2021 -	12/2021	0(O) -	0/0
629	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.67	-	- -	-	-	0/0
630	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	960.18	410.44	03/2020 -	03/2020	0(O) -	0/0
631	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	621.66	03/2019 -	03/2019	0(O) -	0/0
632	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
633	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
634	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
635	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	780.98	346.97	- -	-	-	0/0
636	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,161.64	353.32	03/2015 -	03/2019	48(O) -	0/0
637	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 658.07	941.04	575.19	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
638	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN ,	04/2008	516.23 732.06	735.00	694.13	03/2014 -	-	-	0/0
639	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 348.55	348.55	14.66	- -	02/2019	-	0/0
640	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	276.89	74.21	- -	-	-	0/0
641	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	822.00	-	- -	-	-	0/1
642	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	323.00	-	- -	-	-	0/0
643	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 855.16	855.16	585.06	- -	05/2018	-	0/0
644	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN ,	04/2010	739.65 -	872.22	796.25	- -	03/2017	-	0/1
645	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN ,	04/2011	239.73 -	257.78	30.33	- -	-	-	0/0
646	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 218.39	272.99	63.54	- -	02/2019	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
647	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN ,	04/2012	288.97 335.53	369.08	144.27	- -	-	-	0/0
648	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN ,	04/2013	242.09 -	293.68	76.86	- -	03/2019	- -	0/0
649	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN ,	05/2015	873.71 -	873.71	-	- -	-	-	0/0
650	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN ,	01/2011	493.17 -	493.17	376.00	03/2018 -	03/2018	0(O) -	0/0
651	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI, RAJASTHAN ,	04/2012	471.82 -	471.82	19.91	03/2019 -	03/2019	0(O) -	0/0
652	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
653	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU ,	02/1997	155.55 774.90	870.00	830.45	- -	-	-	0/0
654	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU ,	09/1995	100.00 -	712.82	632.04	- -	-	-	0/0
655	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU ,	04/2006	495.74 -	495.74	386.03	06/2013 -	03/2018	57(O) -	1/4
656	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
657	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU ,	04/1998	271.24 -	520.00	464.30	- -	-	-	0/0
658	ERODE-PALANI - [N22000199]SR, TAMIL NADU ,	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
659	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU ,	04/2011	190.10 -	355.96	149.07	- -	03/2019	- -	0/0
660	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA ,	12/1994	124.43 926.23	1,010.00	919.06	- 03/2017	03/2017	-	0/0
661	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA ,	07/1998	125.00 458.26	480.00	3.48	07/2008 -	-	-	0/0
662	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA ,	04/2006	378.56 1,160.47	1,160.47	1.74	- -	03/2022	- -	0/1
663	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA ,	04/2012	632.68 -	816.55	150.22	03/2016 -	12/2017	21(O) -	0/0
664	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA ,	04/2013	1,112.00 -	1,112.00	.36	- -	-	-	0/1
665	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR, TELANGANA ,	04/2013	616.08 -	616.08	.36	- -	-	-	0/1
666	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES, TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
667	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA ,	04/2015	728.10 -	728.10	-	12/2024 -	12/2024	0(O) -	0/0
668	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA ,	04/2008	813.34 -	3,451.00	1,569.30	03/2014 -	03/2020	72(O) -	0/0
669	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA ,	04/1999	895.00 -	1,857.00	1,194.68	03/2007 -	03/2016	-	0/0
670	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA ,	04/2012	252.00 580.00	580.00	-	- 07/2019	07/2019	- 0(R)	2/3

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
671	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH ,	03/1997	677.97 1,595.40	1,679.13	1,698.69	- -	05/2017	- -	0/0
672	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
673	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 245.39	245.39	210.67	12/2008 -	10/2015	-	0/0
674	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	618.19	03/2010 -	03/2017	-	0/0
675	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	-	0/0
676	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	308.00	-	- -	-	-	0/0
677	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	195.64	351.04	- -	06/2017	-	0/0
678	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	199.75	199.41	- -	12/2017	-	0/0
679	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	-	- -	-	-	0/0
680	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
681	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	-	- -	-	-	0/0
682	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
683	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	-	- -	-	-	0/0
684	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH ,	04/1997	836.26 1,072.52	1,072.52	1,024.07	- -	-	-	0/0
685	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,295.42	16.40	03/2022 -	03/2022	0(O) -	0/0
686	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(O) -	0/6
687	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	943.60	-	12/2024 -	12/2024	0(O) -	0/0
688	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	927.01	289.76	03/2019 -	03/2019	0(O) -	0/0
689	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025	0(O) -	0/0
690	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	357.50	12/2020 -	12/2020	0(O) -	0/0
691	RAMNA - SINGRAULI DOUBLING - [N22000417]EJCR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	22.62	03/2020 -	03/2020	0(O) -	0/0
692	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]EJCR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12(O) -	0/0
693	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
694	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
695	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	4,295.30	46.32	12/2026 -	12/2026	0(O) -	0/0
696	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	36.80 274.41	614.00	258.39	- -	-	-	0/0
697	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	181.88	03/2007 03/2007	-	-	0/0
698	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 3,385.14	3,404.92	3,544.30	12/2006 -	-	-	0/0
699	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 1,319.33	1,319.33	757.23	- 12/2009	03/2019	- 111(R)	0/0
700	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	355.85	12/2010 -	-	-	3/7
701	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 -	749.69	-	06/2005 -	-	-	0/0
702	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	06/2016	-	0/0
703	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	1,655.68	38.29	03/2014 -	-	-	0/0
704	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	3,161.58	933.09	03/2016 -	12/2020	57(O) -	0/0
705	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,619.00	631.67	03/2016 -	12/2018	33(O) -	0/0
706	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL ,	04/2009	533.38 -	533.38	127.10	12/2011 -	-	-	0/0
707	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL ,	04/2009	611.03 -	611.03	146.31	12/2011 -	-	-	0/0
708	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL ,	04/2004	293.74 155.56	229.33	140.60	12/2010 03/2017	-	-	0/0
709	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL ,	04/1999	207.52 334.87	334.87	293.47	12/2012 06/2016	-	-	0/0
710	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
711	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	434.00	37.56	- -	-	-	0/0
712	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
713	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL ,	04/2010	171.02 -	235.00	219.89	06/2013 -	12/2016	-	0/0
714	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	27.17	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
715	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL ,	04/2011	209.77 -	445.00	319.06	- -	03/2018	- -	0/0
716	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL ,	04/2012	283.55 -	330.00	87.65	- -	03/2018	- -	0/0
717	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 268.52	268.52	.67	- -	-	-	0/0
718	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 272.20	272.20	.64	- -	-	-	0/0
719	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL ,	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
720	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	556.31 -	612.00	-	- -	-	-	0/0
721	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL ,	01/1991	763.18 -	1,428.00	478.32	12/2021 -	12/2021	0(O) -	0/0
722	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	481.30	03/2003 -	-	-	0/0
	Total		3,52,470.03 -	4,41,335.56	1,19,196.86				13/110
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
723	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	06/2017	49(O) -	0/0
724	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50(O) -	0/0
725	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,620.72	05/2014 -	06/2017	37(O) -	0/0
726	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH, ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
727	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD, ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	02/2017	-	0/1
728	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	-	0/0
729	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD, ANDHRA PRADESH ,	01/2014	361.30 200.69	207.40	44.08	07/2014 -	-	-	0/1
730	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
731	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/1
732	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	- -	-	-	0/1
733	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	- -	-	-	0/4
734	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	- -	-	-	0/0
735	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
736	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
737	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
738	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
739	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	2/4
740	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23(O) -	0/4
741	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
742	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0
743	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
744	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
745	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	-	- -	11/2018	- -	0/0
747	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	51.12	02/2017 -	02/2017	-	0/0
748	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	-	03/2020 -	03/2020	0(O) -	0/0
749	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020	0(O) -	0/0
750	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
751	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
752	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
753	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	05/2018	0(O) -	1/4
754	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
755	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
756	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/3
757	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
758	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
759	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
760	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	05/2018	0(O) -	1/4
761	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
762	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	-	06/2016 -	06/2016	-	0/4
763	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	-	-	-	-	0/0
764	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	-	10/2016 -	10/2016	-	0/4
765	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	-	-	-	-	0/0
766	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36(O) -	0/0
767	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	-	03/2017 -	-	-	0/0
768	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	-	04/2017 -	-	-	0/0
769	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	-	04/2017 -	-	-	0/0
770	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	-	04/2017 -	-	-	0/0
771	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	-	04/2017 -	-	-	0/0
772	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	-	04/2017 -	-	-	0/0
773	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	-	04/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
774	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	-	04/2017 -	-	-	0/0
775	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	-	04/2017 -	-	-	0/0
776	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	-	04/2017 -	-	-	0/0
777	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	410.32	02/2009 -	05/2017	99(O) -	0/0
778	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	209.80	04/2009 -	05/2017	97(O) -	0/0
779	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	05/2017	102(O) -	0/0
780	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	05/2017	102(O) -	0/0
781	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	245.83	04/2009 -	05/2017	97(O) -	0/0
782	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	05/2017	110(O) 7(R)	0/0
783	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	312.79	06/2008 06/2016	04/2017	-	0/0
784	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 230.00	208.00	297.81	04/2008 01/2017	06/2017	110(O) 5(R)	0/0
785	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	198.82	05/2008 12/2016	04/2017	-	0/0
786	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	05/2017	94(O) -	0/0
787	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 309.56	309.56	389.08	04/2010 09/2016	03/2017	-	0/0
788	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	05/2018	0(O) -	0/4
789	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4
790	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
791	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
792	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
793	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
794	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	0(O) -	0/0
795	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
796	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
797	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
798	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4
799	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
800	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	-	-	-	0/0
801	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
802	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4
803	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/4
804	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	880.29	02/2013 -	06/2018	64(O) -	0/0
805	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	10/2017	53(O) -	0/0
806	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	654.59	02/2014 -	05/2017	39(O) -	0/0
807	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2017	42(O) -	0/0
808	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	06/2017	38(O) -	0/0
809	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	604.61	07/2013 -	03/2018	56(O) -	0/0
810	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	545.27	11/2013 -	12/2017	49(O) -	0/0
811	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	-	-	-	0/0
812	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	08/2016	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
813	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	10/2016	-	0/0
814	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	-	- -	-	-	0/0
815	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	-	0/0
816	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	-	- -	-	-	0/0
817	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
818	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	-	- -	-	-	0/0
819	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	-	- -	-	-	0/0
820	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
821	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	-	- -	-	-	0/0
822	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
823	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	18.48	- -	04/2018	-	0/0
824	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	- -	-	-	0/0
825	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	- -	-	-	0/0
826	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	-	03/2014 -	-	-	0/0
827	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	-	08/2014 -	08/2014	-	0/0
828	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	-	08/2014 -	-	-	0/0
829	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	-	07/2016 -	-	-	0/0
830	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	-	07/2016 -	-	-	0/0
831	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	-	05/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
832	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	-	06/2016 -	06/2016	-	0/0
833	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	-	05/2016 -	-	-	0/0
834	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	-	10/2016 -	-	-	0/0
835	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	-	07/2016 -	10/2016	-	0/0
836	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	-	11/2015 -	-	-	0/0
837	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2017	1(O) -	0/0
838	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	-	0/0
839	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	0(O) -	0/0
840	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	-	03/2020 -	03/2020	0(O) -	0/0
841	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
842	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0
843	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	03/2015	-	0/0
844	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
845	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
846	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
847	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
848	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
849	FOUR LANING OF ORISSA/CHHATISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00	1,090.17	08/2015 -	04/2017	-	0/0
850	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	-	- 05/2018	05/2018	- 0(R)	0/0
851	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	-	- 04/2018	04/2018	- 0(R)	0/0
852	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	-	- 04/2018	04/2018	- 0(R)	0/0
853	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) , NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	-	- -	03/2018	- -	0/0
854	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	- -	04/2018	- -	0/1
855	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
856	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
857	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
858	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	- -	-	-	0/0
859	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	- -	-	-	0/0
860	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	- -	-	-	0/0
861	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 2,782.54	3,237.87	2,948.41	09/2012 12/2017	12/2017	63(O) 0(R)	2/3
862	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	964.46	07/2013 -	06/2017	47(O) -	0/0
863	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,508.05	12/2015 -	07/2017	19(O) -	0/3
864	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	870.15	09/2014 -	10/2017	37(O) -	0/3
865	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	211.03	08/2016 -	05/2017	9(O) -	0/0
866	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
867	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	-	-	-	-	0/0
868	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	-	-	-	-	0/0
869	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	-	-	-	-	0/0
870	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	-	-	-	-	0/0
871	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56	-	-	-	-	0/0
872	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	-	-	-	-	0/0
873	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	-	-	-	-	0/0
874	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	-	-	-	-	0/0
875	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	469.41	05/2010 -	04/2017	-	0/0
876	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	08/2017	69(O) -	0/0
877	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	05/2017	42(O) -	0/0
878	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 -	723.54	235.85	02/2018 -	02/2018	0(O) -	0/0
879	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA ,	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
880	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
881	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
882	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	-	04/2019	-	0/0
883	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	1,060.85	-	01/2018	-	0/0
884	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	154.48	-	05/2018	-	0/0
885	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA ,	05/2015	600.85 -	600.85	-	-	05/2018	-	0/0
886	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	-	-	05/2019	-	0/0
887	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	1,004.67	-	-	05/2019	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
888	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	-	03/2020 -	03/2020	0(O) -	0/0
889	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,288.43	11/2016 -	02/2018	15(O) -	0/0
890	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	57.43	03/2018 -	03/2018	0(O) -	0/0
891	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	-	- -	-	-	0/0
892	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	-	- -	-	-	0/0
893	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	-	- -	-	-	0/0
894	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	-	- -	-	-	0/0
895	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,566.61	07/2015 -	07/2017	24(O) -	0/0
896	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	05/2017	23(O) -	0/0
897	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	05/2017	46(O) -	0/0
898	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,216.15	06/2014 -	12/2017	42(O) -	0/0
899	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
900	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
901	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	498.11	06/2015 -	12/2017	30(O) -	0/0
902	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND ,	09/2015	341.61 -	341.61	114.87	09/2017 -	09/2017	0(O) -	0/0
903	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	-	- -	03/2019	-	0/0
904	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	-	- -	-	-	0/0
905	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	-	- -	08/2018	-	0/0
906	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	-	03/2020 -	03/2020	0(O) -	0/0
907	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	-	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
908	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	- -	06/2017	- -	3/3
909	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	-	0/0
910	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24(O) -	0/0
911	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24(O) -	0/0
912	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	19.24	09/2017 -	09/2017	0(O) -	0/0
913	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
914	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	785.00	08/2016 -	08/2017	12(O) -	0/0
915	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	20.60	- -	08/2018	- -	0/0
916	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	-	- -	-	-	0/0
917	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	-	- -	-	-	0/0
918	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	34.62	- -	-	-	0/0
919	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	-	- -	-	-	0/0
920	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	-	- -	-	-	0/0
921	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	-	- -	-	-	0/0
922	SIX LANING & STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) S - [N24000673]NHAI,KARNATAKA ,	03/2017	985.41 -	1,200.00	-	03/2020 -	03/2020	0(O) -	0/0
923	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	-	03/2020 -	03/2020	0(O) -	0/0
924	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	-	03/2020 -	03/2020	0(O) -	0/0
925	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2017	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
926	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	0(O) -	0/0
927	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017	0(O) -	0/0
928	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	47.56	- -	11/2017	- -	0/0
929	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	-	- -	06/2018	- -	0/0
930	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,206.00	04/2013 -	09/2017	53(O) -	0/0
931	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	07/2017	50(O) -	0/0
932	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	07/2017	0(O) -	0/0
933	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	09/2016	- -	0/0
934	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	- -	0/0
935	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	05/2015	- -	0/0
936	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	02/2016	- -	0/0
937	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	0(O) -	0/0
938	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	05/2017	0(O) -	0/0
939	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	- -	0/0
940	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	08/2016	- -	0/0
941	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
942	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	- -	0/0
943	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	- -	0/0
944	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	-	- -	06/2017	- -	0/0
945	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	-	- -	06/2017	- -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
946	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	05/2017	0(O) -	0/0
947	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
948	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018	0(O) -	0/0
949	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	-	- -	12/2017	- -	0/0
950	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	09/2017	22(O) -	0/0
951	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36(O) -	0/0
952	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	26.00	07/2018 -	07/2018	0(O) -	0/0
953	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	-	- -	06/2017	- -	0/0
954	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	- -	0/0
955	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	0(O) -	0/0
956	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	-	- -	01/2019	- -	0/0
957	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58(O) -	3/3
958	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
959	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2017	57(O) -	0/0
960	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	345.22	06/2014 -	09/2017	39(O) -	0/0
961	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,328.50	02/2014 -	09/2017	43(O) -	2/2
962	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	11/2016	-	0/2
963	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	10/2017	- -	0/4
964	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	07/2016	-	0/12

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
965	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	06/2017	- -	0/4
966	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	11/2016	-	0/4
967	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	- -	-	-	0/0
968	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	65.16	- 03/2013	-	-	0/0
969	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	205.97	- 11/2014	11/2014	-	0/0
970	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
971	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	- -	0/0
972	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	-	- -	05/2018	- -	0/0
973	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	-	- -	05/2018	- -	0/0
974	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	- -	0/0
975	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	-	- -	05/2018	- -	0/0
976	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	-	- -	03/2019	- -	0/0
977	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	-	- -	05/2018	- -	0/0
978	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	957.02	07/2017 -	01/2018	6(O) -	0/0
979	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	297.35	11/2016 -	11/2017	12(O) -	0/0
980	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
981	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	1,200.90	01/2018 -	01/2018	0(O) -	0/0
982	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
983	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0
984	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
985	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	-	- -	07/2019	- -	0/0
986	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	-	- -	07/2019	- -	0/0
987	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
988	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	-	- -	-	-	0/0
989	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	-	- -	-	-	0/0
990	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	-	- -	-	-	0/0
991	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	-	- -	-	-	0/0
992	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	-	- -	-	-	0/0
993	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	-	- -	03/2019	-	0/0
994	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	-	- -	-	-	0/0
995	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	-	- -	-	-	0/0
996	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	-	02/2020 -	02/2020	0(O) -	0/0
997	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	-	03/2020 -	03/2020	0(O) -	0/0
998	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	0(O) -	0/0
999	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020	0(O) -	0/0
1000	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	-	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1001	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	-	03/2017 -	-	-	0/0
1002	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	-	03/2020 -	03/2020	0(O) -	0/0
1003	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020	0(O) -	0/0
1004	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	671.62	01/2014 -	06/2017	41(O) -	0/0
1005	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
1006	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	6.14	- -	05/2018	- -	0/0
1007	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
1008	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
1009	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1010	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	-	-	0/0
1011	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	09/2017	73(O) -	2/2
1012	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,486.59	08/2014 -	12/2017	40(O) -	0/0
1013	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	574.74	03/2014 -	04/2018	49(O) -	0/0
1014	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,077.66	03/2013 -	11/2017	56(O) -	0/0
1015	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	1,607.34	04/2015 -	12/2017	32(O) -	0/0
1016	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	- -	-	-	0/0
1017	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
1018	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1019	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
1020	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36(O) -	0/0
1021	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36(O) -	0/0
1022	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36(O) -	0/0
1023	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	-	04/2017 -	-	-	0/0
1024	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	869.91	08/2013 -	06/2017	46(O) -	0/0
1025	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	06/2017	33(O) -	0/0
1026	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	06/2017	36(O) -	0/0
1027	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA ,	06/2015	996.37 -	996.37	-	12/2017 -	12/2017	0(O) -	0/0
1028	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 251.92	218.63	29.27	10/2017 -	10/2017	0(O) -	0/0
1029	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1030	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 265.35	229.41	6.65	05/2018 -	05/2018	0(O) -	0/0
1031	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	-	0/0
1032	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
1033	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	-	- -	-	-	0/0
1034	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	0(O) -	0/0
1035	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
1036	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1037	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	-	- -	-	-	0/0
1038	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	-	- -	-	-	0/0
1039	WIDENING AND STRENTFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	13(O) -	0/0
1040	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	-	04/2018 -	04/2018	0(O) -	0/0
1041	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	-	10/2017 -	10/2017	0(O) -	0/0
1042	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	-	10/2017 -	10/2017	0(O) -	0/0
1043	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	-	05/2016 -	03/2017	-	0/0
1044	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	7(O) -	0/0
1045	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	-	06/2016 -	03/2017	-	0/0
1046	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1047	WIDENING AND STRENTFTHENING OF EXISITNG SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	-	05/2016 -	03/2017	-	0/0
1048	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020	0(O) -	0/0
1049	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1050	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1051	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1052	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1053	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	77.49	01/2016 -	12/2017	23(O) -	0/0
1054	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1055	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1056	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1057	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1058	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1059	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1060	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1061	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1062	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1063	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	-	- -	11/2017	- -	0/0
1064	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	349.60	- -	05/2017	- -	0/0
1065	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	0(O) -	0/0
1066	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16(O) -	0/0
1067	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1068	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1069	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1070	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	-	-	-	-	0/0
1071	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	-	03/2020 -	03/2020	0(O) -	0/0
1072	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	168.31	02/2010 -	05/2017	87(O) -	0/0
1073	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,036.26	07/2013 -	10/2017	51(O) -	0/0
1074	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	151.72	03/2016 -	04/2017	-	0/0
1075	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1076	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1077	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
1078	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
1079	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1080	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
1081	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BORDER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08	30.08	02/2018 -	02/2018	0(O) -	0/0
1082	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	217.87	09/2016 -	09/2017	12(O) -	0/0
1083	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27	40.75	02/2018 -	02/2018	0(O) -	0/0
1084	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60	54.50	07/2017 -	07/2017	0(O) -	0/0
1085	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	62.77	05/2017 -	05/2017	0(O) -	0/0
1086	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	98.18	04/2017 -	04/2017	-	0/0
1087	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	42.79	03/2018 -	03/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1088	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	10/2016	-	0/0
1089	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	206.78	05/2016 -	05/2016	-	0/0
1090	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6(O) -	0/0
1091	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	234.21	08/2016 -	06/2017	10(O) -	0/0
1092	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	55.00	04/2018 -	04/2018	0(O) -	0/0
1093	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1094	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1095	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	12/2017	74(O) -	0/0
1096	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	-	- -	02/2018	- -	0/0
1097	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	06/2019	0(O) -	0/0
1098	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(O) -	0/0
1099	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN , PPP (BOT)	06/2016	725.95 -	725.95	-	06/2019 -	06/2019	0(O) -	0/0
1100	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
1101	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	-	- -	-	-	0/0
1102	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	-	- -	10/2018	-	0/0
1103	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1104	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	-	-	-	-	0/0
1105	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	-	-	-	-	0/0
1106	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	-	-	-	-	0/0
1107	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
1108	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
1109	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1110	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	885.43	03/2013 -	06/2017	51(O) -	0/0
1111	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,328.34	12/2013 -	12/2017	48(O) -	0/0
1112	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	312.80	06/2013 -	-	-	0/0
1113	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	236.00	05/2013 -	12/2017	55(O) -	0/0
1114	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	303.07	08/2013 -	12/2017	52(O) -	0/0
1115	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	338.40	04/2014 -	-	-	0/0
1116	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
1117	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
1118	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0
1119	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	114.38	11/2017 -	11/2017	0(O) -	0/0
1120	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	11.37	12/2017 -	06/2018	6(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1121	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	200.96	01/2017 -	05/2017	4(O) -	0/0
1122	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	103.08	11/2016 -	05/2017	6(O) -	0/0
1123	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
1124	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	-	-	08/2018	-	0/0
1125	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	-	-	07/2018	-	0/0
1126	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	-	03/2020 -	03/2020	0(O) -	0/0
1127	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	834.00	09/2016 -	07/2017	10(O) -	0/0
1128	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1129	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1130	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1131	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
1132	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1133	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4
1134	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	-	0/1
1135	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	-	0/0
1136	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1137	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	-	-	11/2018	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1138	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
1139	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	04/2017	-	0/4
1140	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	06/2017	48(O) -	0/0
1141	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017	48(O) -	0/0
1142	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	541.42	09/2013 -	05/2017	44(O) -	0/0
1143	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	320.46	01/2014 -	06/2017	41(O) -	0/0
1144	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25(O) -	0/0
1145	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH, UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
1146	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH, UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
1147	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH, UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1148	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH ,	05/2015	261.09 -	261.09	31.17	05/2017 -	05/2017	0(O) -	0/0
1149	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH ,	04/2014	351.34 -	351.34	160.49	01/2016 -	06/2017	17(O) -	0/0
1150	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH ,	09/2015	368.73 -	368.73	70.23	09/2016 -	09/2017	12(O) -	0/0
1151	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH ,	06/2014	301.04 -	301.04	39.38	01/2016 -	12/2016	-	0/0
1152	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH ,	04/2014	495.78 -	495.78	239.48	01/2016 -	06/2017	17(O) -	0/0
1153	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	-	0/0
1154	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD, UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	-	0/0
1155	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP, UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	-	0/0
1156	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1157	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	03/2017	-	0/0
1158	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	-	0/0
1159	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	-	0/0
1160	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
1161	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(O) -	0/0
1162	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
1163	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
1164	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	-	- -	01/2019	- -	0/0
1165	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24(O) -	0/0
1166	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	-	06/2018 -	06/2018	0(O) -	0/0
1167	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018	0(O) -	0/0
1168	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	-	07/2018 -	06/2018	-1(O) -	0/0
1169	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	-	06/2018 -	06/2018	0(O) -	0/0
1170	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1171	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1172	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1173	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	.45	- -	-	-	0/0
1174	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
1175	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
1176	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	-	- -	06/2018	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1177	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	-	-	-	-	0/0
1178	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	-	-	-	-	0/0
1179	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	-	-	-	-	0/0
1180	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	-	-	-	-	0/0
1181	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	-	-	-	-	0/0
1182	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	-	-	-	-	0/0
1183	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	-	-	-	-	0/0
1184	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	-	-	-	-	0/0
1185	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	-	-	-	-	0/0
1186	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	-	-	-	-	0/0
1187	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020	0(O) -	0/0
1188	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020	0(O) -	0/0
1189	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020	0(O) -	0/0
1190	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020	0(O) -	0/0
1191	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	277.41	10/2013 -	12/2017	50(O) -	0/0
1192	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1193	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	-	-	-	-	0/0
1194	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175,000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	546.24	-	06/2017	-	0/0
1195	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,004.42	08/2013 -	06/2017	46(O) -	0/0
1196	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,674.82	08/2013 -	03/2018	55(O) -	0/0
1197	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL , PPP (BOT)	02/2011	580.43 -	580.43	226.67	08/2013 -	12/2017	52(O) -	0/0
1198	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,354.75	09/2014 -	05/2017	32(O) -	0/0
1199	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	391.77	07/2014 -	09/2017	38(O) -	0/0
1200	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1201	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	03/2018	0(O) -	0/0
1202	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL ,	10/2015	361.15 -	361.15	-	-	01/2018	-	0/0
1203	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
1204	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,185.55	-	12/2017	-	0/0
1205	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL ,	03/2016	229.37 -	229.37	-	-	11/2018	-	0/0
1206	FOUR LANNING OF CHICHA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL ,	09/2016	767.03 -	767.03	-	-	-	-	0/0
	Total		3,15,935.94 -	3,22,248.77	1,04,899.30				26/188
	SHIPPING AND PORTS								
1207	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA ,	03/2007	245.67 -	409.83	350.68	04/2009 -	-	-	0/0
1208	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 669.46	669.46	411.12	12/2010 12/2018	12/2018	96(O) 0(R)	0/0
1209	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1210	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 03/2016	12/2017	141(O) 21(R)	0/0

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1211	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	235.15	98.60	06/2017 -	06/2017	0(O) -	0/1
1212	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017	0(O) -	0/1
1213	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU ,	12/2014	274.85 -	274.85	43.83	04/2017 -	04/2017	-	0/1
1214	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU ,	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
	Total		4,117.75 -	5,085.02	1,875.38				0/3
	<u>TELECOMMUNICATIONS</u>								
1215	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	-	06/2017 -	06/2017	0(O) -	0/0
1216	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	13,334.00	2,060.00	07/2015 09/2017	09/2017	26(O) 0(R)	0/0
1217	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	03/2017	-	0/70
	Total		15,863.43 -	15,763.43	2,313.90				0/70
	<u>URBAN DEVELOPMENT</u>								
1218	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	72.96	03/2017 -	06/2017	3(O) -	0/5
1219	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	-	-	-	-	0/0
1220	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	496.18	-	06/2017 -	06/2017	0(O) -	0/0
1221	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI ,	09/2011	38,585.00 -	38,585.00	29,618.49	03/2016 -	12/2016	-	0/0
1222	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,219.21	10.53	10/2019 -	03/2020	5(O) -	0/0
1223	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI ,	05/2012	405.01 405.01	405.01	219.34	12/2014 06/2017	06/2017	30(O) 0(R)	2/3
1224	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	445.50	08/2014 -	-	-	0/0
1225	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,118.00	2,479.76	11/2019 -	11/2019	0(O) -	1/7

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1226	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	-	- 04/2019	04/2019	- 0(R)	0/2
1227	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 270.83	270.83	75.52	11/2014 05/2017	12/2017	37(O) 7(R)	0/0
1228	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	1.31	03/2016 02/2018	02/2018	23(O) 0(R)	1/6
1229	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA ,	05/2006	6,395.00 13,845.01	13,845.01	14,200.11	06/2011 12/2015	04/2017	-	3/3
1230	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1231	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65(O) 11(R)	0/1
1232	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29(O) -	0/0
1233	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA ,	07/2015	154.00 -	154.00	49.82	11/2015 -	11/2017	24(O) -	0/0
1234	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH ,	12/2012	188.87 -	188.87	153.40	12/2015 12/2016	09/2017	21(O) 9(R)	0/0
1235	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	12/2016	164.00 -	164.00	24.22	01/2018 -	01/2018	0(O) -	0/10
1236	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 349.33	349.33	196.00	03/2016 12/2017	12/2017	21(O) 0(R)	0/13
1237	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 170.62	170.62	127.15	03/2012 08/2016	12/2017	69(O) 16(R)	9/20
1238	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA ,	12/2012	315.00 315.00	315.00	277.92	06/2015 08/2016	08/2017	26(O) 12(R)	7/8
1239	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21(O) -	0/0
1240	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0
1241	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 06/2017	06/2018	39(O) 12(R)	0/10
1242	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	219.38	05/2017 08/2017	08/2017	3(O) 0(R)	6/12
1243	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	479.87	281.57	03/2015 03/2017	09/2017	30(O) 6(R)	0/0
1244	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	332.72	216.89	09/2016 01/2017	08/2017	11(O) 7(R)	0/0
1245	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 14,600.00	14,600.00	12,472.32	12/2015 -	12/2017	24(O) -	11/24

Detail of ongoing Projects Costing Rs.150Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(May 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1246	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	-	- -	-	-	0/6
1247	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018	0(O) -	0/0
1248	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	-	03/2020 -	03/2020	0(O) -	0/5
1249	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 03/2019	03/2019	0(O) 0(R)	0/0
1250	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	98.07	08/2016 03/2017	03/2018	19(O) 12(R)	7/12
	Total		1,45,290.66 -	1,52,798.14	67,935.21				47/147
	DEFENCE PRODUCTION								
1251	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	167.69	19.24	05/2018 -	05/2018	0(O) -	1/5
1252	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	285.95	28.67	08/2020 -	08/2020	0(O) -	1/3
	Total		453.64 -	453.64	47.91				2/8
	Grand Total		15,64,786.27	17,34,083.56	6,69,895.38				2104/3930


Summary of projects in the Flash Report for the month of May, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1247
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	4
Number of Projects in Current Month	1252

Brief Analysis


Project Status with respect to Original Schedule: Out of 1252 projects, 12 projects are ahead of schedule, 311 projects are on schedule 314 projects are delayed. 484 projects do not have fixed dates of commissioning. 131 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

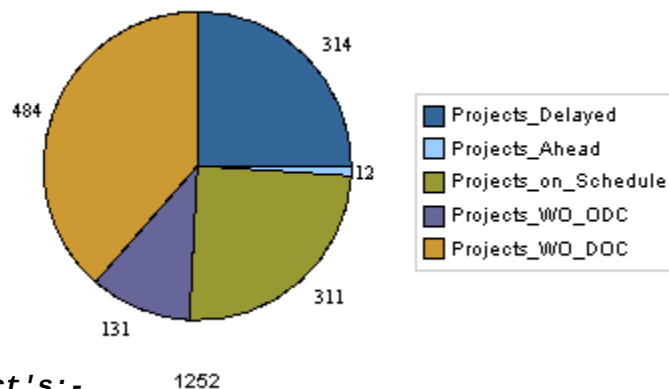

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1252 projects when sanctioned, was of the order of Rs. 1564786.27 crore but this was subsequently revised to Rs. 1734083.56 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till May, 2017 is Rs. 669895.38 crore, which is 38.6% of the anticipated cost of the projects.

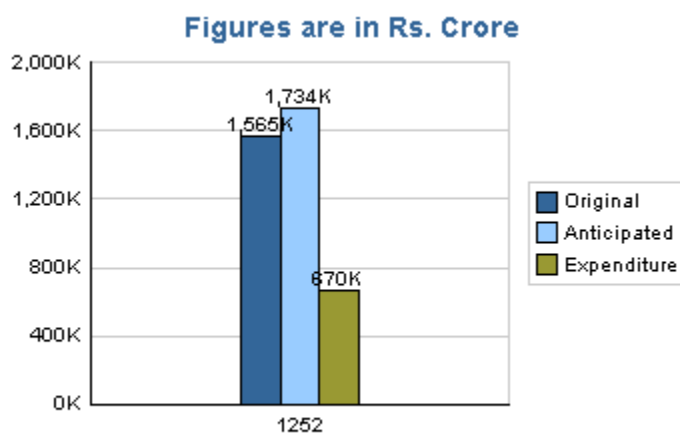

Sector wise current status of projects on the Flash Report

ATOMIC ENERGY

Current Status:


Number of Projects 4

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed. 1 project does not have fixed dates of commissioning.

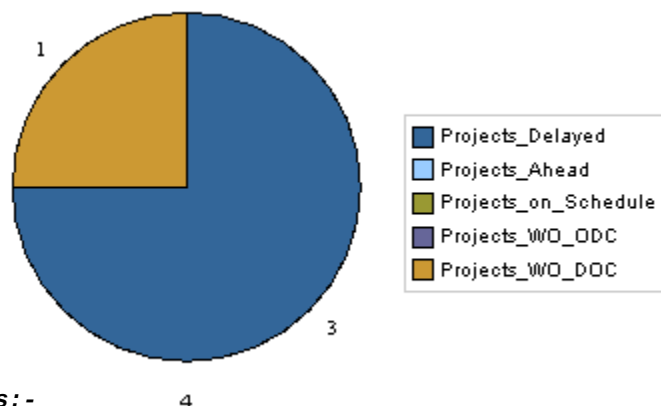


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 52241 crore implying a cost overrun of 29.2%. The expenditure incurred on these projects till May, 2017 is Rs. 44697.43 crore, which is 85.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

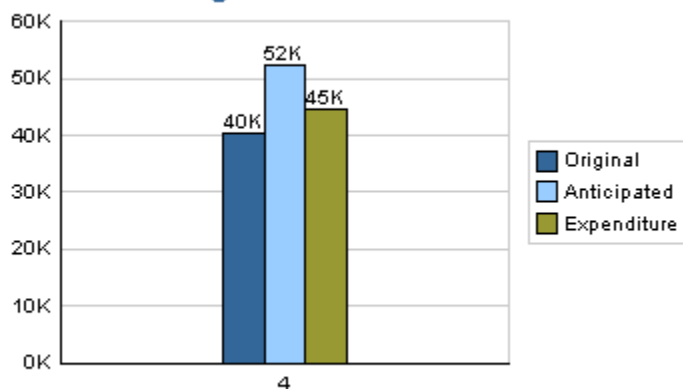

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects **3**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **1**

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed. 1 project does not have fixed dates of commissioning.

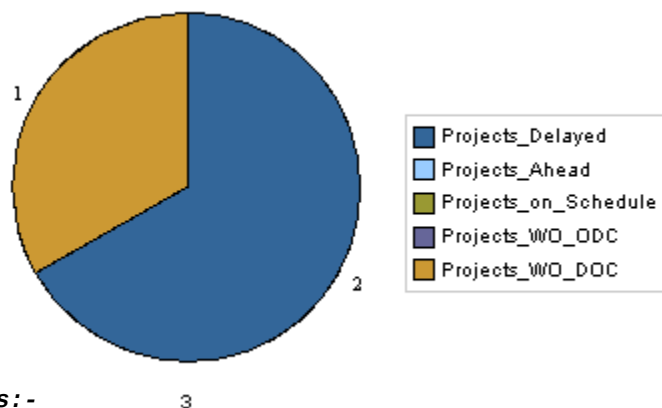


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 959.68 crore but this was subsequently anticipated to Rs. 1312.86 crore implying a cost overrun of 36.8%. The expenditure incurred on these projects till May, 2017 is Rs. 814.48 crore, which is 62% of the anticipated cost of the projects.

Figures are in Rs. Crore

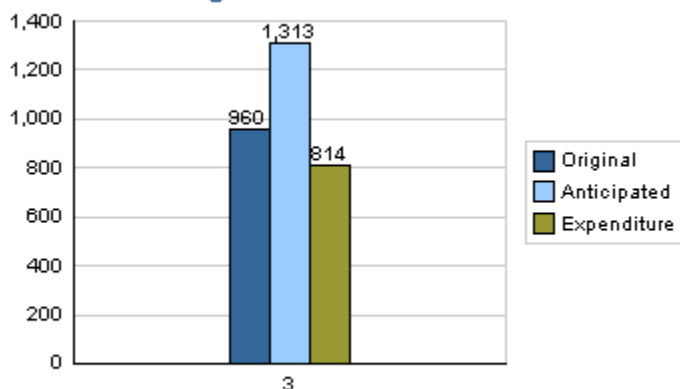

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	89
Number of Projects On Schedule	49
Number of Projects Delayed	36
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 89 projects, 1 project is ahead of schedule, 49 projects are on schedule 36 projects are delayed. 3 projects do not have fixed dates of commissioning.

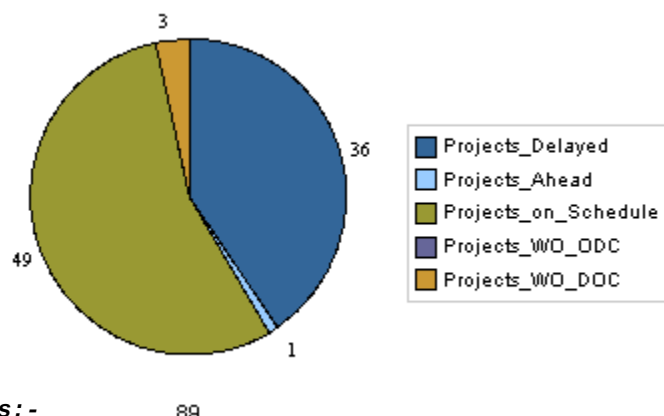


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 89 projects when sanctioned, was of the order of Rs. 86482.99 crore but this was subsequently anticipated to Rs. 86697.92 crore implying a cost overrun of .2%. The expenditure incurred on these projects till May, 2017 is Rs. 15684.54 crore, which is 18.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

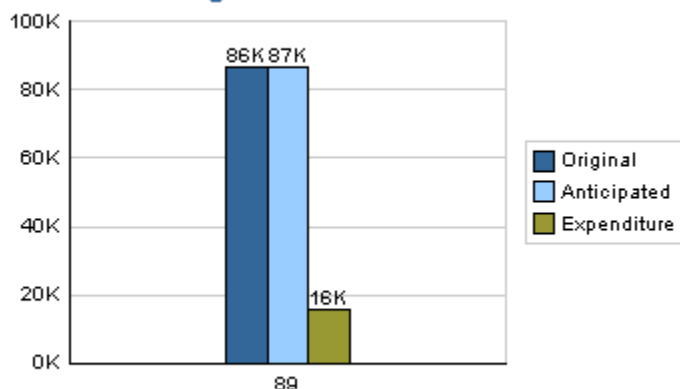

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

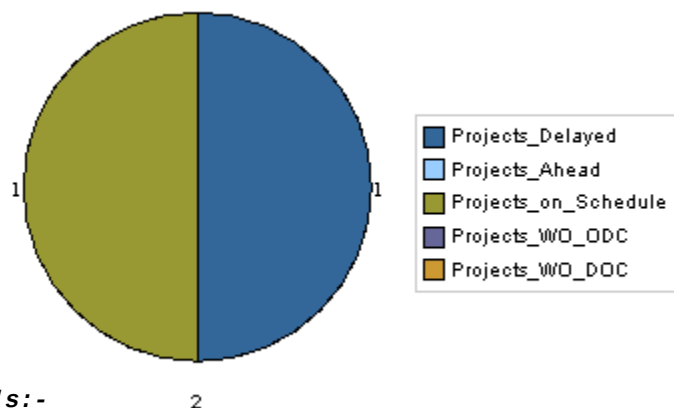


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 703.44 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till May, 2017 is Rs. 233.17 crore, which is 33.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

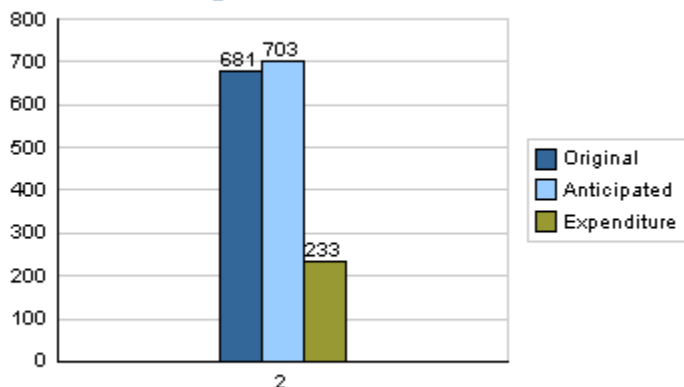

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	4
Number of Projects On Schedule	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule 2 projects do not have fixed dates of commissioning.

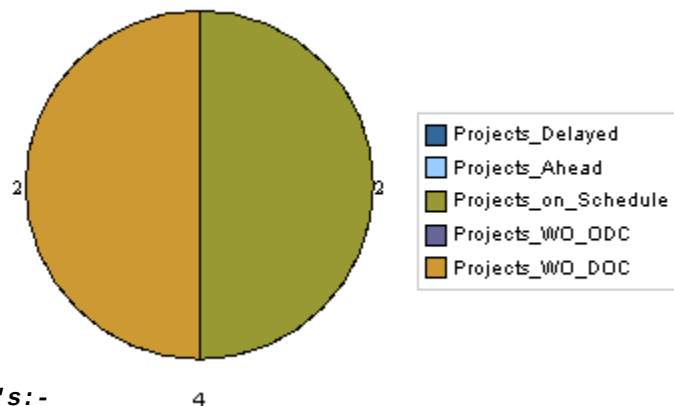


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6773.63 crore but this was subsequently anticipated to Rs. 6773.63 crore The expenditure incurred on these projects till May, 2017 is Rs. 372.63 crore, which is 5.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

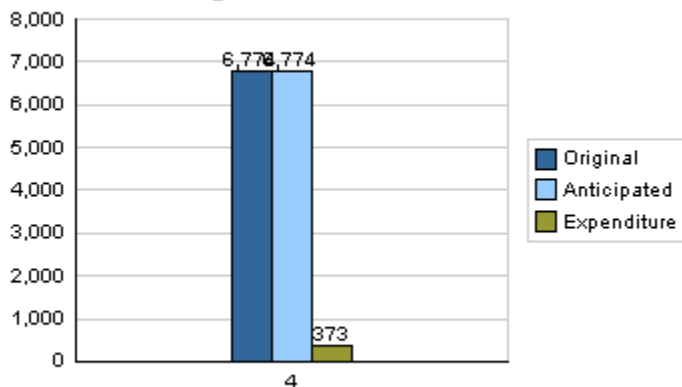

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	35
Number of Projects On Schedule	11
Number of Projects Delayed	19

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 35 projects, 11 projects are on schedule 19 projects are delayed. 4 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

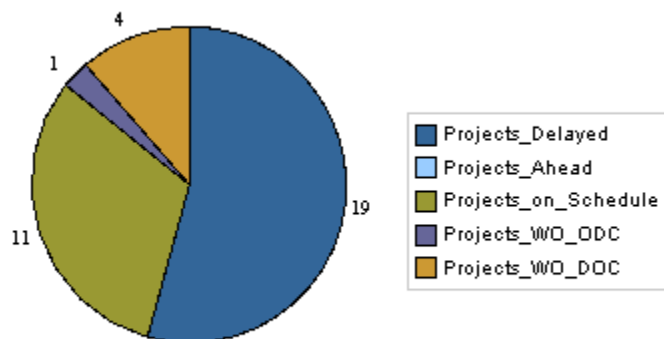


Total No Of Project's:-

35

Investment Scenario

Total original cost of implementation of 35 projects when sanctioned, was of the order of Rs. 57753.65 crore but this was subsequently anticipated to Rs. 57967.33 crore implying a cost overrun of .4%. The expenditure incurred on these projects till May, 2017 is Rs. 34533.61 crore, which is 59.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

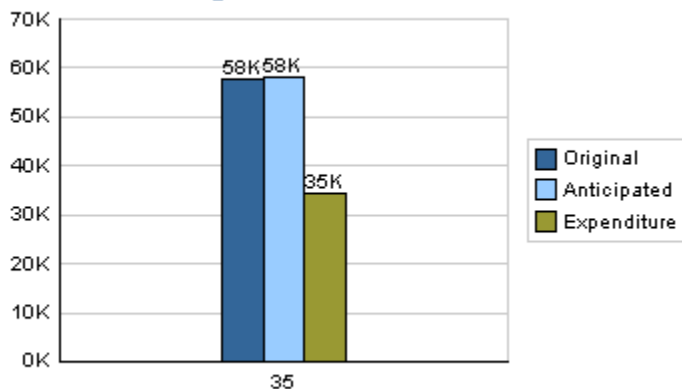

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	95
Number of Projects On Schedule	45
Number of Projects Delayed	37
Number of Projects Ahead	5
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 95 projects, 5 projects are ahead of schedule, 45 projects are on schedule 37 projects are delayed. 8 projects do not have fixed dates of commissioning.

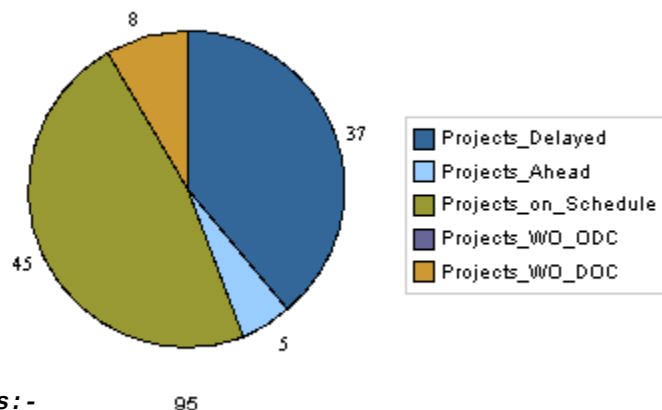

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 95 projects when sanctioned, was of the order of Rs. 188746.9 crore but this was subsequently anticipated to Rs. 189467.02 crore implying a cost overrun of .4%. The expenditure incurred on these projects till May, 2017 is Rs. 58375.08 crore, which is 30.8% of the anticipated cost of the projects.

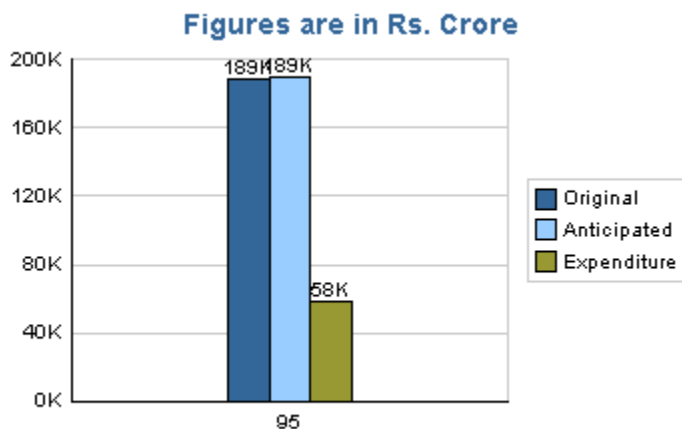

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	128
Number of Projects On Schedule	54
Number of Projects Delayed	55
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	16

Brief Analysis

Project Status with respect to Original Schedule: Out of 128 projects, 3 projects are ahead of schedule, 54 projects are on schedule 55 projects are delayed. 16 projects do not have fixed dates of commissioning.

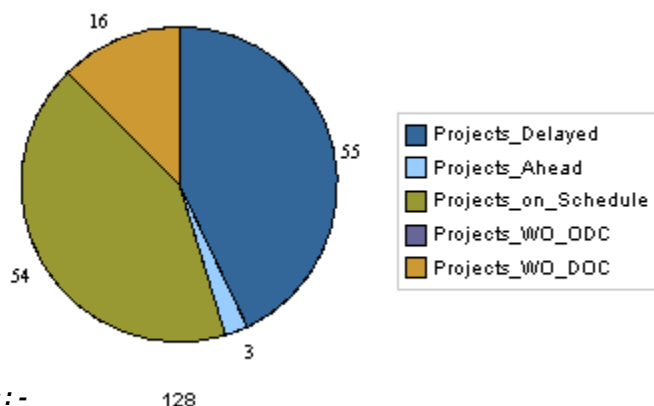


Total No Of Project's:-

128

Investment Scenario

Total original cost of implementation of 128 projects when sanctioned, was of the order of Rs. 343460.25 crore but this was subsequently anticipated to Rs. 393759.12 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till May, 2017 is Rs. 215028.58 crore, which is 54.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

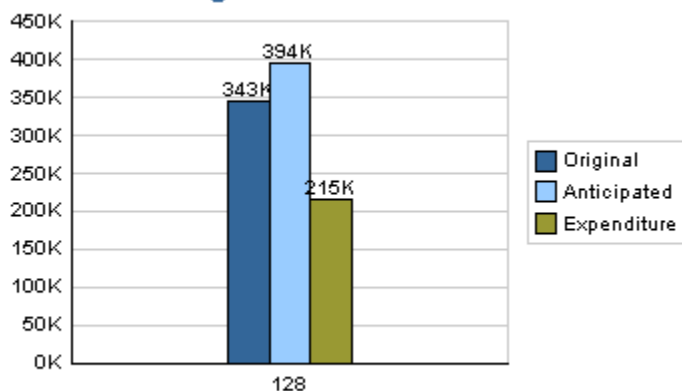

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

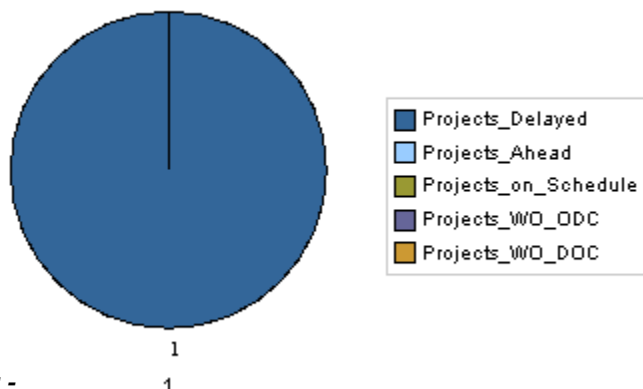

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till May, 2017 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

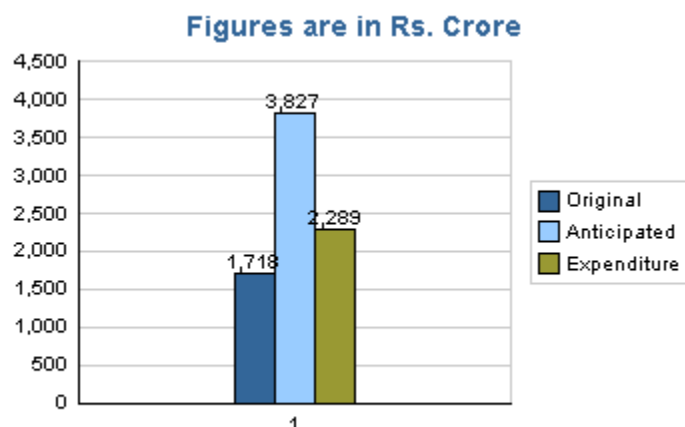

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	13
Number of Projects On Schedule	4
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 4 projects are on schedule 4 projects are delayed. 5 projects do not have fixed dates of commissioning.

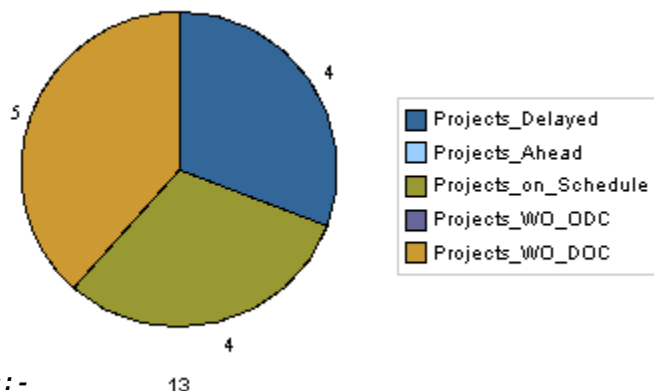


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 3637.08 crore but this was subsequently anticipated to Rs. 3649.38 crore implying a cost overrun of .3%. The expenditure incurred on these projects till May, 2017 is Rs. 1598.3 crore, which is 43.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

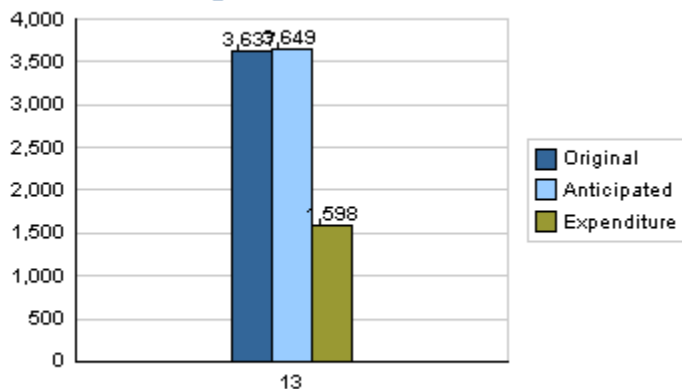

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	348
Number of Projects On Schedule	40
Number of Projects Delayed	34

Number of Projects Without Original Date of Commissioning	70
Number of Projects Without Date Of Commissioning	204

Brief Analysis

Project Status with respect to Original Schedule: Out of 348 projects, 40 projects are on schedule 34 projects are delayed. 204 projects do not have fixed dates of commissioning. 70 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

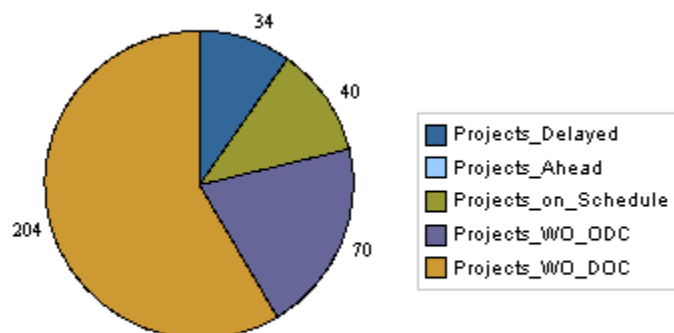


Total No Of Project's:-

348

Investment Scenario

Total original cost of implementation of 348 projects when sanctioned, was of the order of Rs. 352470.03 crore but this was subsequently anticipated to Rs. 441335.56 crore implying a cost overrun of 25.2%. The expenditure incurred on these projects till May, 2017 is Rs. 119196.86 crore, which is 27% of the anticipated cost of the projects.

Figures are in Rs. Crore

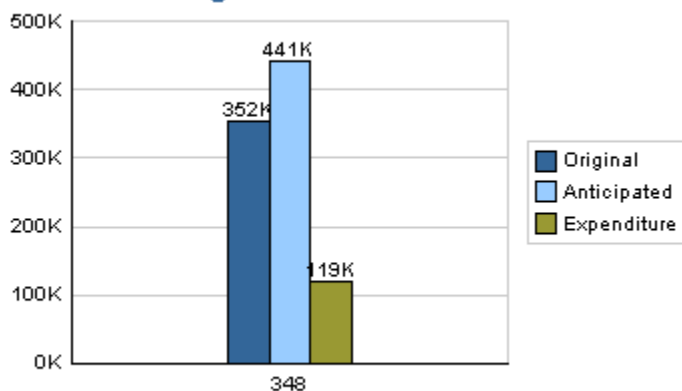

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	484
Number of Projects On Schedule	95
Number of Projects Delayed	99
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	59
Number of Projects Without Date Of Commissioning	230

Brief Analysis

Project Status with respect to Original Schedule: Out of 484 projects, 1 project is ahead of schedule, 95 projects are on schedule 99 projects are delayed. 230 projects do not have fixed dates of commissioning. 59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

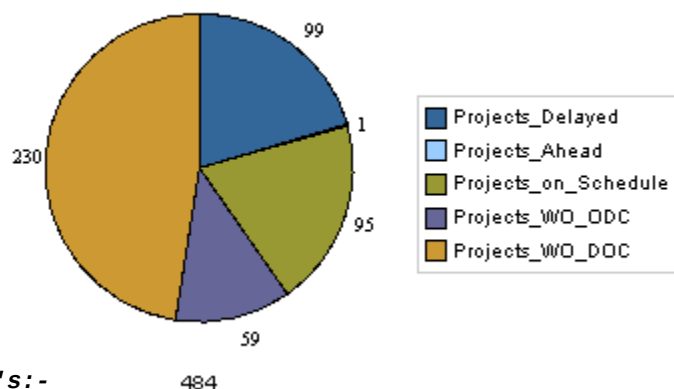

Investment Scenario

Total original cost of implementation of 484 projects when sanctioned, was of the order of Rs. 315935.94 crore but this was subsequently anticipated to Rs. 322248.77 crore implying a cost overrun of 2%. The expenditure incurred on these projects till May, 2017 is Rs. 104899.3 crore, which is 32.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

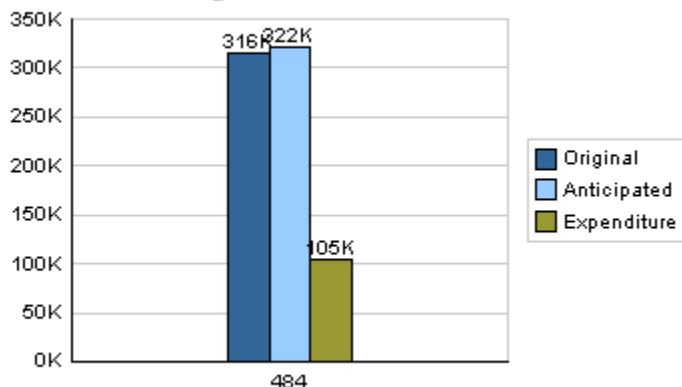

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	3
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

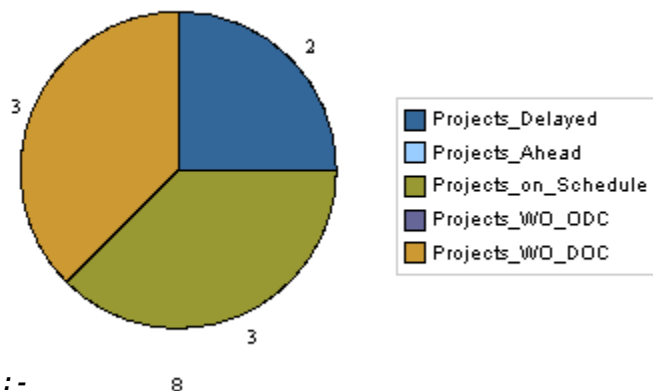


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5085.02 crore implying a cost overrun of 23.5%. The expenditure incurred on these projects till May, 2017 is Rs. 1875.38 crore, which is 36.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

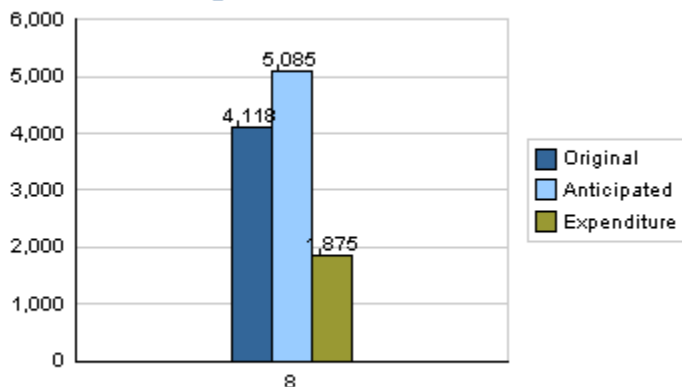

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	3
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 1 project is on schedule 1 project is delayed. 1 project does not have fixed dates of commissioning.

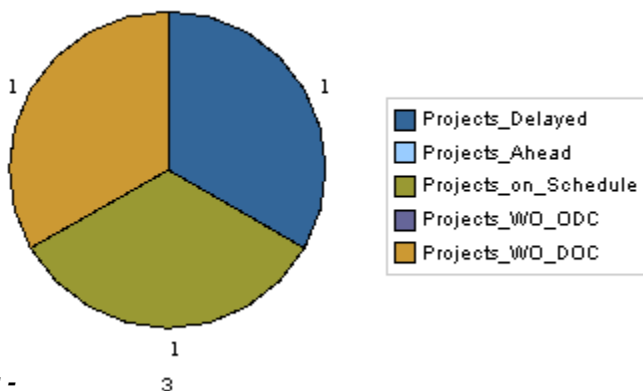


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15863.43 crore but this was subsequently anticipated to Rs. 15763.43 cr The expenditure incurred on these projects till May, 2017 is Rs. 2313.9 crore, which is 14.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

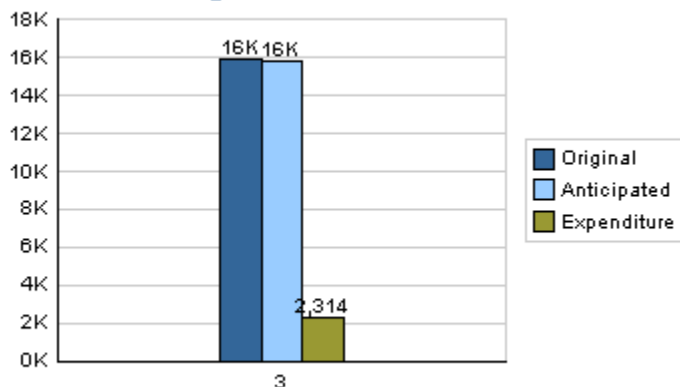

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	33
Number of Projects On Schedule	6
Number of Projects Delayed	20

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 33 projects, 6 projects are on schedule 20 projects are delayed. 6 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

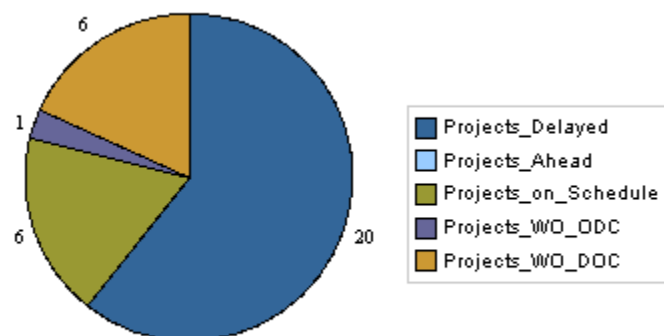


Total No Of Project's:-

33

Investment Scenario

Total original cost of implementation of 33 projects when sanctioned, was of the order of Rs. 145290.66 crore but this was subsequently anticipated to Rs. 152798.14 crore implying a cost overrun of 5.2%. The expenditure incurred on these projects till May, 2017 is Rs. 67935.21 crore, which is 44.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

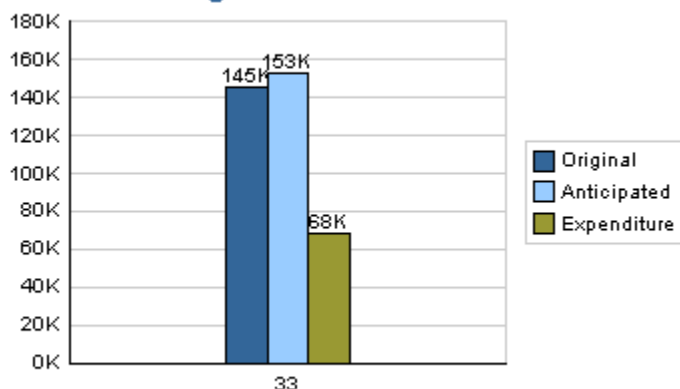

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule

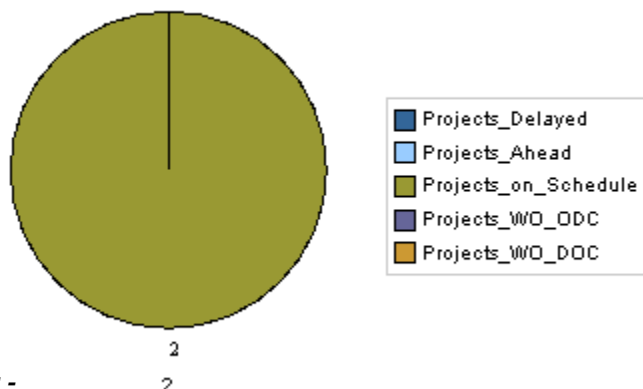


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 453.64 crore. The expenditure incurred on these projects till May, 2017 is Rs. 47.91 crore, which is 10.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

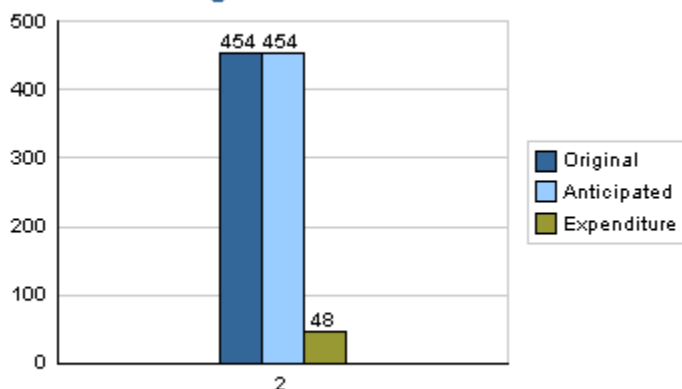

**Annexure
of Projects
costing Rs 150 crore
and
above**

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (MAY 2017)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	24.13
2	ANDHRA PRADESH	59	97,206.37	1,02,378.99	10,583.89
3	ARUNACHAL PRADESH	31	16,602.41	32,431.5	16,622.21
4	ASSAM	49	33,519.75	47,046.96	29,656.21
5	BIHAR	78	68,807.61	82,225.55	39,345.47
6	CHHATISGARH	40	93,631.97	95,569	54,952.83
7	D & N HAVELI	1	6,086.08	4,701.44	1,960.89
8	DELHI	17	50,925.07	50,831.89	33,798.62
9	GOA	10	4,379.12	4,361.51	434.71
10	GUJARAT	43	37,987.3	41,775.68	24,327.5
11	HARYANA	21	14,081.22	15,967.45	7,650.8
12	HIMACHAL PRADESH	12	12,531.81	18,931.08	7,701.61
13	JAMMU AND KASHMIR	10	27,408.66	47,178.95	28,678.93
14	JHARKHAND	48	46,724.53	49,958.75	16,026.26
15	KARNATAKA	47	79,506.59	97,832.65	41,294.79
16	KERALA	21	37,154.14	38,770.19	13,570.76
17	MADHYA PRADESH	52	53,756.78	58,203.32	18,985.3
18	MAHARASHTRA	112	1,67,460.76	1,76,862.47	56,226.25
19	MANIPUR	2	944.25	9,874.69	4,979.46
20	MEGHALAYA	6	7,108.02	9,025	699.71
21	MIZORAM	5	2,001.2	6,942.57	1,893.37
22	MULTI STATE	179	2,84,226.28	2,66,611.6	86,350.71
23	NAGALAND	7	8,126.79	10,276.79	147.52
24	ODISHA	64	70,292.05	78,295.7	17,999.15
25	PUNJAB	27	15,261.77	15,267.5	2,822.22
26	RAJASTHAN	62	43,839.05	46,128.14	18,494.44
27	SIKKIM	5	2,149.08	5,138.08	893.04
28	TAMIL NADU	51	74,509.1	89,961.89	56,556.04
29	TELANGANA	35	24,832.84	27,174.2	4,903.19
30	TRIPURA	11	4,400.64	9,067.42	4,511.61
31	UTTAR PRADESH	83	1,09,253.66	1,12,709.08	26,248.15
32	UTTARAKHAND	10	14,901.99	15,982.05	5,392.47
33	WEST BENGAL	53	54,854.77	66,160.14	33,874.14
TOTAL		1,252	15,64,786.27	17,34,083.56	6,67,606.38

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

(May 2017)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	21,600.00	12/2008 10/2013	03/2017
	Total		13,171.00 -	22,462.00	21,600.00		
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	1/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017
	Total		309.46 -	553.53	484.76		
	<u>COAL</u>						
3	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	617.39	03/2012 03/2023	03/2023
4	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	199.20	03/2016 -	03/2018
5	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	341.27	03/2018 -	03/2018
6	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]	1/2005	302.96 -	302.00	341.37	03/2010 -	03/2017
	Total		1,209.55 -	1,279.24	1,499.23		
	<u>PETROLEUM</u>						
7	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	3,466.38	12/2014 03/2018	03/2018
8	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	1,200.00	887.00	03/2015 -	05/2017
	Total		1,471.52 -	1,800.17	4,353.38		
	<u>POWER</u>						
9	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	8,398.75	6,275.55	09/2009 -	12/2018
10	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	17,435.15	9,315.46	09/2010 -	-
11	SYSTEM STRENGTHENING XII OF SR - [N18000085]	2/2010	232.34 -	245.00	237.49	06/2012 -	06/2017
12	KISHANGANGA HEP (3X110 MW) - [N18000031]	1/2009	3,642.04 -	5,783.17	4,892.47	01/2016 -	01/2018
13	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	353.47	08/2014 12/2017	12/2017

List of Projects in which Expenditure is More than Approved Cost

						(May 2017)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
14	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,399.06	08/2013 12/2017	12/2017
15	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	602.44	465.36	12/2016 -	12/2017
	Total		15,387.30 -	34,228.56	22,938.86		
	<u>RAILWAYS</u>						
16	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	4/1986	158.77 274.56	634.48	629.43	03/1994 02/2016	02/2016
17	CALICUT-MANGALORE (DL) (SR) - [220100151]	2/1996	240.00 -	579.37	537.02	- -	-
18	KARUR-SALEM(NL),SR - [220100191]	2/1997	155.55 -	870.00	830.45	- -	-
19	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	9/2001	492.98 -	1,320.00	758.76	12/2010 -	-
20	GULBARGA-BIDAR,SCR(NL) - [220100254]	2/1998	242.42 369.70	1,542.41	927.68	- 05/2009	-
21	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	3/1998	280.00 -	1,122.00	834.61	- -	-
22	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-
23	TINPAHAR - SAHIBGANJ (ER) - [N22000115]	4/2008	167.73 -	167.73	207.11	03/2012 -	-
24	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	7/2006	743.00 -	1,825.00	831.39	03/2008 06/2008	03/2020
25	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	332.92 283.95	477.88	495.40	03/2012 -	-
26	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	9/2007	687.20 -	950.00	913.84	03/2010 -	06/2017
27	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	4/2003	136.62 -	376.00	367.85	12/2007 03/2010	-
28	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	340.00	327.59	03/2009 03/2009	02/2017
29	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	1,202.70	199.98	02/2015 -	12/2019
30	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	718.54	265.71	- -	05/2019
31	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	4/2003	218.19 -	413.56	343.54	- -	10/2017
32	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	541.00	183.72	- -	-
33	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	4/1999	108.00 -	432.72	446.52	12/2009 -	-
34	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-
35	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	9/1997	1,500.00 -	5,000.00	4,090.26	04/2008 12/2011	06/2018

List of Projects in which Expenditure is More than Approved Cost

						(May 2017)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
36	JAGGAYAPET - MELLACHERUVU - [N22000304]	4/2007	313.24 -	554.70	342.00	01/1999 06/2017	06/2017
37	PANVEL PEN DOUBLING - [N22000255]	4/2006	96.16 -	280.00	268.37	- -	-
38	PEN ROHA DOUBLING - [N22000254]	4/2007	98.74 -	381.39	312.12	- 03/2017	-
39	KATAKHAL TO BHAIRABI - [N22000126]	4/1998	227.90 -	509.00	286.07	12/2012 -	03/2016
40	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	4/2006	117.36 196.95	203.00	202.29	03/2011 -	-
41	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	155.74 164.36	966.98	874.72	02/2009 12/2017	12/2017
42	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	9/2006	324.90 -	516.40	370.69	03/2010 -	12/2017
43	RAJATGARH-BARANG(LD),ECOR - [220100286]	4/1999	166.16 -	370.00	353.00	02/2009 02/2009	02/2017
44	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,581.53	618.19	03/2010 -	03/2017
45	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	3/2002	625.30 408.76	876.10	841.57	06/2007 -	-
46	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018
47	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,100.00	484.14	07/2012 -	-
48	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	4/1999	744.71 -	1,126.79	751.05	- -	-
49	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	3/1997	677.97 1,062.36	1,679.13	1,698.69	- -	05/2017
50	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]	4/2010	203.40 -	273.84	276.15	- -	-
51	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	224.99	03/2015 -	07/2015
52	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	3/2006	201.00 -	230.00	244.18	- 10/2015	10/2015
53	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017
54	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	100.00 -	712.82	632.04	- -	-
55	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	4/2007	482.00 -	874.57	968.06	03/2013 -	-
56	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	2/1997	295.00 -	1,289.92	1,439.40	- -	01/2017
57	RANCHI-LOHARDAGA(GC),SER - [220100214]	4/1997	194.07 -	335.00	226.39	06/2004 -	-
58	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	4/1997	218.24 236.41	525.00	544.20	- 03/2019	03/2019
59	AMRAVATI-NARKHER NL(CR) - [220100118]	6/1994	663.01 175.30	858.23	688.04	06/1999 12/2020	12/2020

List of Projects in which Expenditure is More than Approved Cost

						(May 2017)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
60	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	813.34 -	3,451.00	1,569.30	03/2014 -	03/2020
61	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	4/1996	1,676.31 -	7,000.00	6,068.59	03/2009 -	03/2017
62	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	300.00 -	2,145.00	361.21	- -	03/2020
63	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	200.00 -	780.00	285.64	- -	03/2019
64	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	436.00	435.57	03/2011 -	10/2011
65	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	727.56 -	9,658.00	4,927.46	03/2011 -	03/2020
66	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	470.21 -	3,004.90	572.56	- 06/2021	06/2021
67	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019
68	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	523.17 -	1,871.00	1,081.00	- -	03/2018
69	CHENGANNUR-CHINGAVANAM - [N22000203]	4/2006	191.72 -	342.85	360.22	- -	-
70	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	4/2011	209.77 -	445.00	319.06	- -	03/2018
71	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	4/1999	895.00 -	1,857.00	1,194.68	03/2007 -	03/2016
72	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	4/2008	822.39 -	1,480.83	1,421.19	- -	03/2018
73	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	4/1998	271.24 -	520.00	464.30	- -	-
74	SAKRI-HASANPUR ROAD (NL) - [N22000171]	4/1999	175.69 -	325.00	253.10	- -	-
75	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	4/2010	171.02 -	235.00	219.89	06/2013 -	12/2016
76	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	4/2010	739.65 -	872.22	796.25	- -	03/2017
77	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	4/2010	279.40 -	355.00	323.64	- -	-
78	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	446.00 -	1,037.15	590.60	- -	03/2019
79	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	3/2008	195.64 -	195.64	351.04	- -	06/2017
80	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	559.91	538.21	07/2014 -	-
81	GADWAL - RAICHUR (NL), SCR - [220100270]	4/1998	92.63 -	350.00	316.64	02/2011 -	-
82	JIND-SONEPAT (NL),NR - [220100280]	1/2004	238.56 -	740.00	745.02	03/2012 01/2016	01/2016

List of Projects in which Expenditure is More than Approved Cost

						(May 2017)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
83	HARIDASPUR-PARADEEP(NL) - [220100285	4/1996	301.64 -	1,185.64	620.08	- 09/2009	03/2019
	Total		29,435.07 -	1,02,252.74	71,349.72		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
84	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	410.32	02/2009 -	05/2017
85	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	209.80	04/2009 -	05/2017
86	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	167.64	268.94	11/2008 -	05/2017
87	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	195.35	11/2008 -	05/2017
88	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281	12/2003	200.00 -	200.00	245.83	04/2009 -	05/2017
89	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	880.29	02/2013 -	06/2018
90	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	05/2017
91	NASHRI- CHANANI - [N24000162	5/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	05/2017
92	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131	2/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	09/2017
93	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123	3/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017
94	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	1,206.00	04/2013 -	09/2017
95	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	3/2010	1,509.10 -	3,237.87	2,948.41	09/2012 12/2017	12/2017
96	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	06/2017
97	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144	9/2010	852.00 -	852.00	885.43	03/2013 -	06/2017
98	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	1,674.82	08/2013 -	03/2018
99	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,004.42	08/2013 -	06/2017
100	MUZZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	1,077.66	03/2013 -	11/2017
101	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	06/2017
102	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	869.91	08/2013 -	06/2017
103	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	1,216.15	06/2014 -	12/2017
104	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	545.27	11/2013 -	12/2017

List of Projects in which Expenditure is More than Approved Cost

						(May 2017)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	604.61	07/2013 -	03/2018
106	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	494.33	04/2014 -	06/2017
107	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018
108	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	09/2017
109	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	12/2017
110	NAGPUR - KONDHALI - [N24000472	9/2005	168.00 -	168.00	279.92	06/2006 -	-
111	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	4,508.05	12/2015 -	07/2017
112	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017
113	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	320.46	01/2014 -	06/2017
114	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	2,354.75	09/2014 -	05/2017
115	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	06/2017
116	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	761.19	07/2008 -	-
117	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	898.99	03/2014 -	09/2017
118	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	2,620.72	05/2014 -	06/2017
119	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	671.62	01/2014 -	06/2017
120	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	622.89	10/2013 -	12/2017
121	KANDLA - MUNDRA PORT - [N24000175	1/2011	953.88 -	953.88	964.46	07/2013 -	06/2017
122	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,328.34	12/2013 -	12/2017
123	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017
124	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	832.39	11/2013 -	05/2017
125	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	312.79	06/2008 06/2016	04/2017
126	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	208.00	297.81	04/2008 01/2017	06/2017
127	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	389.08	04/2010 09/2016	03/2017
128	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	325.00	469.54	05/2013 -	07/2017

List of Projects in which Expenditure is More than Approved Cost

						(May 2017)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
129	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2017
130	MURADABAD-BAREILY - [N24000154]	4/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	06/2017
131	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	870.15	09/2014 -	10/2017
132	DEOLI-KOTA - [N24000148]	1/2011	593.00 -	593.00	1,036.26	07/2013 -	10/2017
133	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	08/2017
134	TALEGAON-AMRAVATI - [N24000140]	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-
135	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	198.82	05/2008 12/2016	04/2017
136	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	340.12	07/2009 -	05/2017
	Total		46,351.69 -	50,456.92	70,367.11		
	<u>SHIPPING AND PORTS</u>						
137	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	3/2007	245.67 -	409.83	350.68	04/2009 -	-
	Total		245.67 -	409.83	350.68		
	<u>STEEL</u>						
138	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 03/2016	03/2016
139	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	178.65	12/2015 -	06/2017
	Total		918.61 -	1,289.28	1,264.29		
	<u>URBAN DEVELOPMENT</u>						
140	BANGALORE METRO RAIL PROJECT - [N28000008]	5/2006	6,395.00 -	13,845.01	14,200.11	06/2011 12/2015	04/2017
	Total		6,395.00 -	13,845.01	14,200.11		
	Grand Total		1,14,894.87	2,28,577.28	2,08,408.14		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

							(May 2017)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	2,210.30	05/2018 -	12/2017
2	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	406.10	03/2018 -	12/2017
	Total		4,212.08 -	4,212.08	2,616.40		
	<u>PETROLEUM</u>						
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	3,466.38	04/2019 03/2019	03/2019
	Total		6,068.80 -	5,296.93	3,466.38		
	<u>COAL</u>						
4	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2020
	Total		231.92 -	231.92	.00		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	-	07/2018 -	06/2018
	Total		667.00 -	667.00	.00		
	<u>POWER</u>						
6	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	54.60	06/2018 -	05/2017
	Total		187.04 -	187.04	54.60		
	<u>PETROLEUM</u>						
7	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 247.52	247.52	.18	02/2019 -	12/2018
8	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	1.12	05/2019 -	12/2018
9	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	-	08/2019 -	12/2018
10	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	40.40	02/2020 -	01/2020
	Total		4,339.52 -	4,339.52	41.70		
	Grand Total		15,706.36	14,934.49	6,179.08		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

(May 2017)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	107.86	03/2021 -	03/2021
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	0.25	03/2023 -	03/2023
4	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	351.47	03/2021 -	03/2021
5	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	47.90	03/2018 -	03/2018
6	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	222.50	03/2025 -	03/2025
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	404.31	03/2018 -	03/2018
8	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	31.62	03/2021 -	03/2021
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	661.64	03/2026 -	03/2026
10	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	-	03/2022 -	03/2022
11	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	7.06	03/2022 -	03/2022
12	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
13	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	58.98	03/2020 -	03/2020
14	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	209.13	03/2022 -	03/2022
15	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	172.13	03/2020 -	03/2020
16	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
17	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,251.27	03/2023 03/2023	03/2023
18	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.15	03/2021 -	03/2021
19	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	104.02	03/2020 -	03/2020
20	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	0.15	03/2022 -	03/2022
21	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	71.92	03/2023 -	03/2023
22	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	174.68	03/2020 -	03/2020
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	197.50	03/2018 -	03/2018
25	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	43.65	03/2023 -	03/2023
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	20.35	03/2019 -	03/2019
27	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	16.34	03/2019 03/2019	03/2019
28	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	67.25	12/2019 -	12/2019
29	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
30	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	37.55	03/2021 -	03/2021
31	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	346.77	03/2020 -	03/2020
32	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	190.44	11/2021 -	11/2021
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
34	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	341.27	03/2018 -	03/2018
35	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.58	03/2021 -	03/2021
36	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	83.66	03/2019 -	03/2019
37	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	30.32	03/2019 -	03/2019
38	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	9.72	03/2022 -	03/2022
39	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,326.67	03/2023 -	03/2023
40	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
41	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 03/2023	03/2023
42	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.78	03/2019 -	03/2019
43	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
44	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	5/2016	687.28 -	687.28	0.06	06/2017 -	06/2017
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	70.75	03/2021 -	03/2021
46	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	24.78	03/2020 -	03/2020
47	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	135.99	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
48	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
49	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	122.07	03/2019 -	03/2019
	Total		65,177.77 -	65,178.57	8,076.55		
	<u>DEFENCE PRODUCTION</u>						
50	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	28.67	08/2020 -	08/2020
51	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	167.69	19.24	05/2018 -	05/2018
	Total		453.64 -	453.64	47.91		
	<u>FERTILISERS</u>						
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	160.44	12/2017 -	12/2017
	Total		482.85 -	494.00	160.44		
	<u>HEALTH AND FAMILY WELFARE</u>						
53	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	174.00	03/2018 -	03/2018
54	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	80.00	08/2018 -	08/2018
55	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	41.00	09/2018 -	09/2018
56	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	152.95	28.00	02/2018 -	02/2018
	Total		1,215.52 -	1,215.52	323.00		
	<u>MINES</u>						
57	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	157.34	01/2020 -	01/2020
58	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	0.31	04/2021 04/2021	04/2021
	Total		6,074.00 -	6,074.00	157.65		
	<u>PETROLEUM</u>						
59	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	3.62	10/2019 -	10/2019

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
60	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	5.73	01/2019 -	01/2019
61	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	33.30	03/2019 -	03/2019
62	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	312.92	01/2018 -	01/2018
63	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	442.98	04/2018 04/2018	04/2018
64	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	123.00	09/2018 09/2018	09/2018
65	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	136.00	02/2020 -	02/2020
66	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
67	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	-	06/2020 -	06/2020
68	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	760.33	08/2018 -	08/2018
69	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	-	01/2021 -	01/2021
70	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	-	12/2020 -	12/2020
71	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	523.10	06/2018 -	06/2018
72	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	58.14	11/2019 -	11/2019
73	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	-	06/2020 -	06/2020
74	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
75	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	2.19	12/2020 -	12/2020
76	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	11.34	02/2020 -	02/2020
77	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	2.39	08/2021 -	08/2021
78	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	-	12/2019 -	12/2019
79	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	24.96	04/2019 -	04/2019
80	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	91.05	12/2019 -	12/2019
81	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	-	01/2021 -	01/2021

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
82	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	10.92	08/2018 -	08/2018
83	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	-	12/2018 -	12/2018
84	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	114.51	03/2020 -	03/2020
85	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
86	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	-	10/2020 -	10/2020
87	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	1,714.00 -	1,417.00	981.91	06/2017 06/2017	06/2017
88	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	-	09/2019 -	09/2019
89	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	165.80	04/2018 -	04/2018
90	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
91	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	3.36	01/2019 -	01/2019
92	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	273.08	12/2018 -	12/2018
93	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	73.87	12/2017 -	12/2017
94	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	7.98	06/2020 -	06/2020
95	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	107.72	03/2018 -	03/2018
96	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	2.55	12/2020 -	12/2020
97	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	156.97	11/2018 -	11/2018
98	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	117.93	10/2018 -	10/2018
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	1,879.00	16.42	09/2019 -	09/2019
100	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	14.82	12/2020 -	12/2020
101	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	-	12/2019 -	12/2019
102	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	658.62	-	03/2023 -	03/2023
103	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	6.97	04/2018 -	04/2018
	Total		98,975.85 -	1,00,841.77	4,585.86		

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
104	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	146.00	08/2017 -	08/2017
105	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	145.40	07/2017 07/2017	07/2017
106	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	1,168.60	03/2018 -	03/2018
107	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
108	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	-	06/2019 -	06/2019
109	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	21.70	11/2018 -	11/2018
110	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	-	04/2019 -	04/2019
111	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	1,681.43	10/2017 -	10/2017
112	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	-	04/2020 -	04/2020
113	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	51.70	04/2019 -	04/2019
114	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	1.10	07/2018 -	07/2018
115	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	2,983.30	04/2018 -	04/2018
116	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	499.30	11/2019 -	11/2019
117	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	248.90	05/2019 -	05/2019
118	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	7.50	12/2018 -	12/2018
119	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH-II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	-	03/2019 -	03/2019
120	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	93.20	05/2018 -	05/2018
121	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	21.80	01/2019 -	01/2019
122	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	317.00	07/2018 -	07/2018
123	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	-	04/2019 -	04/2019
124	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.60	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
125	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	0.20	02/2019 -	02/2019
126	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	28.90	05/2018 -	05/2018
127	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	0.40	02/2019 -	02/2019
128	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]	11/2016	330.00 -	330.00	110.40	11/2017 -	11/2017
129	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	2,697.00	03/2019 -	03/2019
130	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	28.80	07/2018 -	07/2018
131	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	340.88	122.30	03/2018 -	03/2018
132	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	262.00	09/2019 -	09/2019
133	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	115.10	10/2017 -	10/2017
134	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
135	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	837.00	07/2020 -	07/2020
136	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.80	02/2019 -	02/2019
137	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	-	03/2019 -	03/2019
138	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	76.50	01/2019 -	01/2019
139	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	29.70	04/2018 -	04/2018
140	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	-	06/2018 -	06/2018
141	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	-	09/2019 -	09/2019
142	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	2,703.00	09/2019 -	09/2019
143	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	116.50	01/2018 -	01/2018
144	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.13	164.50	06/2019 -	06/2019
145	TRANSMISSION SYSTEM STRENTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	71.90	07/2018 -	07/2018
146	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	0.60	11/2018 -	11/2018

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
147	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	-	06/2019 -	06/2019
148	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	8.20	10/2018 10/2018	10/2018
149	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	40.10	03/2018 -	03/2018
150	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	5,571.00	08/2018 -	08/2018
151	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	300.00	09/2017 -	09/2017
152	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	170.10	12/2018 -	12/2018
153	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	2.40	11/2019 -	11/2019
154	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	14.60	03/2019 -	03/2019
155	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	1,653.40	04/2018 -	04/2018
156	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	224.50	07/2018 -	07/2018
157	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	117.50	11/2017 -	11/2017
	Total		1,08,663.32 -	1,09,106.19	22,883.93		
	<u>RAILWAYS</u>						
158	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
159	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	-	03/2021 03/2021	03/2021
160	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	376.00	03/2018 -	03/2018
161	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
162	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	74.22	03/2019 -	03/2019
163	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 03/2022	03/2022
164	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	357.50	12/2020 -	12/2020
165	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
166	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	135.51	03/2018 -	03/2018
167	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	432.25	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
169	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
170	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	212.71	03/2019 -	03/2019
171	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	-	03/2021 -	03/2021
172	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	16.40	03/2022 -	03/2022
173	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	-	03/2021 -	03/2021
174	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	289.76	03/2019 -	03/2019
175	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	19.91	03/2019 -	03/2019
176	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	-	12/2024 -	12/2024
177	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	329.46	12/2020 -	12/2020
178	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	12.00	03/2020 -	03/2020
179	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.14	12/2025 -	12/2025
180	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
181	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	100.00	03/2021 -	03/2021
182	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	222.83	03/2019 -	03/2019
183	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	22.62	03/2020 -	03/2020
184	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	410.44	03/2020 -	03/2020
185	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021
186	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 03/2020	03/2020
187	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	186.13	03/2019 -	03/2019
188	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	839.11	03/2020 -	03/2020
189	BANASPAHI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	621.66	03/2019 -	03/2019
190	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	323.91	03/2018 -	03/2018
191	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	-	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
192	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	1/1991	763.18 -	1,428.00	478.32	12/2021 -	12/2021
193	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
194	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	4/1995	524.43 -	939.00	183.93	12/2021 -	12/2021
195	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
196	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
197	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	4/2011	4,295.30 -	4,295.30	46.32	12/2026 -	12/2026
	Total		50,362.78 -	51,913.32	5,860.29		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
198	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
199	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
200	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
201	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
202	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
203	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
204	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
205	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
206	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
207	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
208	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
209	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
210	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
211	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
212	4 LANING FROM KALIABHOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
213	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
214	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
215	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]	6/2015	532.49 -	532.49	137.08	05/2017 -	05/2017
216	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
217	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
218	UMARIYA TO SHAHOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
219	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
220	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
221	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
222	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
223	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	57.42	07/2017 -	07/2017
224	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
225	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
226	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	29.27	10/2017 -	10/2017

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
228	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
229	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
230	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
231	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
232	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
233	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
234	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,200.90	01/2018 -	01/2018
235	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
236	TWO LANNING WITH PAVED SHOULDER OF SALASAR- NAGAU - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
237	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
238	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	26.00	07/2018 -	07/2018
239	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	55.00	04/2018 -	04/2018
240	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
241	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
242	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
243	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]	3/2015	226.31 226.00	226.00	-	10/2017 -	10/2017
244	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
245	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32 -	327.32	142.73	05/2017 -	05/2017
246	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
247	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	30.08	02/2018 -	02/2018
248	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
249	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
250	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
252	SIX LANING & STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) S - [N24000673	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
253	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
254	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09 -	261.09	31.17	05/2017 -	05/2017
255	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
256	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
257	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
258	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020
259	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
260	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
261	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
262	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
263	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
264	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347	8/2015	723.54 -	723.54	235.85	02/2018 -	02/2018
265	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
266	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
267	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349	5/2015	1,387.11 -	1,387.11	114.38	11/2017 -	11/2017

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
268	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342	5/2015	709.00 -	709.00	19.24	09/2017 -	09/2017
269	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
270	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	40.75	02/2018 -	02/2018
271	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
272	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
273	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
274	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
275	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
276	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	62.77	05/2017 -	05/2017
277	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
278	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61 -	341.61	114.87	09/2017 -	09/2017
279	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
280	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	57.43	03/2018 -	03/2018
281	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
282	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
283	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
284	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	-	03/2020 -	03/2020
285	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
286	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
287	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
288	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
289	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
290	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
291	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60 -	455.60	54.50	07/2017 -	07/2017
292	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	-	10/2017 -	10/2017
	Total		62,528.36 -	64,511.96	3,069.28		
	<u>SHIPPING AND PORTS</u>						
293	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
294	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	98.60	06/2017 -	06/2017
295	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	0.14	12/2017 -	12/2017
	Total		653.44 -	703.48	98.74		
	<u>STEEL</u>						
296	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	13.64	09/2017 -	09/2017
297	COKE OVEN BATTERY-5 - [N12000117	12/2011	2,858.00 -	2,500.00	427.35	12/2017 -	12/2017
298	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	40.47	09/2018 -	09/2018
299	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	-	06/2019 -	06/2019
300	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	27.42	03/2018 -	03/2018
301	CENTRAL DISPATCH YARD - [N12000119	8/2015	320.66 -	320.66	-	08/2018 -	08/2018
302	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120	7/2015	465.85 -	465.85	-	07/2018 -	07/2018
303	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	309.85	04/2018 -	04/2018
304	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	25.34	06/2020 -	06/2020
305	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
306	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
	Total		14,909.72 -	14,551.72	1,064.13		

Details of On Schedule Projects w.r.t. Original Schedule

(May 2017)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
307	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]	6/2016	418.26 -	418.26	-	06/2017 -	06/2017
	Total		418.26 -	418.26	.00		
	<u>URBAN DEVELOPMENT</u>						
308	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	2/2016	496.18 496.00	496.18	-	06/2017 -	06/2017
309	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 03/2019	03/2019
310	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	12/2016	164.00 -	164.00	24.22	01/2018 -	01/2018
311	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,479.76	11/2019 -	11/2019
312	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
313	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	-	03/2020 -	03/2020
	Total		15,832.02 -	15,686.02	5,040.75		
	Grand Total		4,25,747.53	4,31,148.45	51,368.53		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	03/2017	70.54
	Total		16,663.00 -	28,462.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2017	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
5	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59	03/2015 -	03/2020	201.51
6	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
8	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	518.04	03/2010 -	03/2019	201.05
9	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
10	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		18,670.33 -	19,677.89			
	<u>FERTILISERS</u>						
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010]	02/2016	482.85 -	494.00	12/2017 -	12/2017	2.31
	Total		680.64 -	703.44			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
13	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK [N21000005]	11/2013	196.70 -	209.00	01/2016 -	01/2016	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
15	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	06/2017	70.49
17	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
18	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,259.49	04/2016 -	12/2017	3.28
19	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	222.81	09/2016 -	02/2017	57.06
20	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87
21	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
22	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	222.19	01/2014 -	11/2019	9.49
23	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	10/2017	45.83
24	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
25	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	768.25	11/2015 -	10/2016	15.35
26	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	06/2018	45.67
27	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	05/2017	37.72
29	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	01/2017	19.35
30	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
31	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]	06/2012	150.00 -	259.93	07/2014 -	09/2017	73.29
32	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	09/2016	407.00 -	1,879.00	09/2019 -	09/2019	361.67
33	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	Total		23,673.73 -	29,116.08			
	POWER						
34	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
35	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
36	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2017	54.59
37	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14
38	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58
39	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	11,639.00	09/2017 -	03/2018	.00
40	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
41	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79
42	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	09/2013	1,575.30 -	1,656.15	05/2016 -	06/2017	5.13
43	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	09/2017	38.61
44	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	02/2018	6.82
45	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	11/2017	5.34
46	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	07/2017	32.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
47	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
48	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	12/2017	54.25
49	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2017	30.37
50	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	244.66	02/2016 -	06/2017	24.46
51	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88	03/2018 -	03/2018	26.82
52	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	07/2017	27.92
53	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]	07/2010	752.64 -	757.94	07/2013 -	06/2017	.70
54	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01
55	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	06/2017	5.45
56	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96
57	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79
58	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	121.80
59	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	01/2018	147.51
60	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	06/2017	39.30
61	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	03/2018	31.17
62	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	09/2017	23.13
63	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	12/2017	133.06
64	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
65	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37
66	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
67	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	01/2018	58.79
68	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
69	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
70	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,329.43	07/2006 02/2015	09/2017	260.55
71	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	11/2014 -	06/2017	21.90
73	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	12/2017	36.74
74	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,352.57	09/2017 -	09/2018	31.55
75	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	10/2017	7.41
	Total		99,180.91 -	1,49,758.51			
	<u>RAILWAYS</u>						
76	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	299.62
77	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	-	1,568.48
78	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
79	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31
80	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
81	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	536.26
82	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
83	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
84	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
85	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
86	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
87	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
88	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	01/2016	210.19
89	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
90	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	- -	03/2021	476.13
91	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56	- -	10/2017	89.54
92	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
93	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
94	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	- -	05/2019	212.37
95	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
96	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
97	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	02/2017	154.85
98	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	- -	06/2022	137.80
99	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
100	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51
101	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
102	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
103	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
104	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
105	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
106	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
107	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	03/2019	44.07
108	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	12/2016	70.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
109	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
110	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	03/2016	123.34
111	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	-	534.55
112	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	-	185.52
113	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
114	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
115	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
116	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	03/2017	70.09
117	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	-	8.18
118	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	-	81.31
119	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	-	286.26
120	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
121	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
122	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
123	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
124	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
125	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
126	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
127	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
128	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
129	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
130	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
131	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
132	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
133	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
134	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
135	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
136	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
137	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
138	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
139	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
140	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
141	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
142	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
143	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
144	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
145	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	-	341.34
146	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
147	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
148	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
150	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
151	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
152	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
153	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
154	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
155	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
156	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
157	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
158	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	780.00	- -	03/2019	290.00
159	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
160	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
162	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119	04/1999	207.52 -	334.87	12/2012 -	-	61.37
163	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58
164	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
165	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	360.00	- -	-	27.24
166	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
167	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,679.13	- -	05/2017	147.67
168	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	744.71 -	1,126.79	- -	-	51.31
169	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	780.98	- -	-	90.45
170	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
171	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
172	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
173	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
174	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
175	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
176	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	02/2017	122.68
177	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
178	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89
179	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
180	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
181	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
182	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
183	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
184	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	-	72.62
185	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
186	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.52	- -	-	28.25
187	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	01/2017	337.26
188	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
189	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
190	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	712.82	- -	-	612.82
191	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
192	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
193	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	10/2015	14.43
194	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
195	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	- -	03/2020	52.77
196	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
197	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
198	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	355.96	- -	03/2019	87.25
199	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
200	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]	04/2010	203.40 -	273.84	- -	-	34.63
201	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	648.00	- -	02/2019	8.00
202	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,161.64	03/2015 -	03/2019	40.00
203	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	03/2017	711.70
204	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.23	06/1999 -	12/2020	29.44
205	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
206	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
207	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	- -	08/2017	10.26
208	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	- -	05/2018	61.80
209	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
210	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	02/2019	41.64
211	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
212	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
213	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
214	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
215	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
216	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
217	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
218	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
219	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	- -	-	16.87
220	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	05/2018	87.54
221	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	03/2017	17.92
222	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]	04/2011	239.73 -	257.78	- -	-	7.53
223	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	- -	02/2019	27.93
224	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	- -	-	27.72
225	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	- -	03/2019	21.31
226	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
227	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
228	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
229	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
230	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
231	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
232	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
233	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
234	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
235	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
236	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
237	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
238	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
239	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
240	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
241	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
242	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
243	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
244	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
245	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	03/2016	107.49
246	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
247	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	445.00	- -	03/2018	112.14
248	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	330.00	- -	03/2018	16.38
249	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
250	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
251	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
252	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
253	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
254	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2019	171.38
255	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
256	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	508.00	- -	03/2019	62.76
257	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
258	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
259	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
260	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
261	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
262	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
263	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	- -	-	101.93
264	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	-	5.33
265	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	-	10.94
266	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	-	21.21
267	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
268	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
269	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	05/2015	5.12
270	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01
271	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
272	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
273	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60	12/2024 -	12/2024	25.72
274	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
275	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
	Total		1,04,781.62 -	2,54,477.80			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
276	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2017	28.93
277	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	05/2017	92.75
278	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	05/2017	80.68
279	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	05/2017	68.99
280	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50
281	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]	11/2014	573.96 605.00	605.00	- -	-	5.41

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
282	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
283	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
284	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
285	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	03/2017	42.25
286	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
287	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
288	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
289	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
290	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
291	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
292	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
293	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
294	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
295	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
296	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26
297	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	04/2018	.11
298	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	10/2017	.04
299	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
300	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	06/2016 -	03/2017	.02
301	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30
302	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
303	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
304	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
305	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
306	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
307	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
308	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
309	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
310	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
311	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
312	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
313	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
314	SIX LANING & STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) S - [N24000673	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
315	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
316	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
317	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(May 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		25,210.69 -	32,209.56			
	<u>SHIPPING AND PORTS</u>						
318	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
319	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20
320	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
321	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
322	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
323	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04
324	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79
325	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	03/2016	44.80
326	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39
327	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	06/2017	17.50
	Total		1,639.71 -	2,211.39			
	<u>URBAN DEVELOPMENT</u>						
328	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	13,845.01	06/2011 -	04/2017	116.50
329	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	349.33	03/2016 -	12/2017	44.75
330	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091	08/2014	350.02 -	479.87	03/2015 -	09/2017	37.10
	Total		6,986.35 -	14,674.21			
	Grand Total		3,01,231.25	5,38,494.81			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

(May 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,000.00	5,429.43	09/2010 09/2016	10/2017	85	71.82	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	9,980.00	12/2015 11/2016	11/2019	47	0	Equipment supply/erection delays by various vendors and contractors.
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	7,688.00	12/2016 03/2017	12/2020	48	0	Equipment supply/erection delays by various vendors and contractors.
	Total		27,271.00 -	29,779.00	23,097.43					
	<u>CIVIL AVIATION</u>									
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017	80	78.87	long rainy season
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	24.13	09/2018 -	06/2020	21	40.28	
	Total		624.07 -	994.86	508.89					
	<u>COAL</u>									
6	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	197.05	10/2014 06/2017	06/2017	32	0	
7	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	145.88	05/2014 -	10/2017	41	0	late of Issue of 'Consent to Establish'
8	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	134.69	04/2014 -	10/2017	42	0	
9	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	119.45	03/2014 -	12/2017	45	0	
10	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 486.57	486.57	268.54	03/2012 03/2018	03/2018	72	87.58	
11	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	96.89	03/2015 -	03/2018	36	0	forest land diversion

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
12	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72	0	due to Forest land diversion
13	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	199.20	03/2014 -	03/2018	48	0	
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	199.20	03/2016 -	03/2018	24	0	
15	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	204.04	03/2013 -	03/2018	60	0	
16	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	334.92	03/2016 -	03/2018	24	0	
17	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	143.44	03/2016 -	03/2018	24	0	
18	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	57.64	06/2015 -	03/2018	33	0	due to diversion of Jallaram vagu
19	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	486.27	92.33	03/2016 03/2018	03/2018	24	12.97	
20	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,813.37	12/2015 04/2018	04/2018	28	0	
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	223.57	03/2017 -	05/2018	14	0	
22	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	297.66	03/2018 -	09/2018	6	0	
23	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
24	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	126.88	03/2012 -	03/2019	84	0	
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 518.04	518.04	190.31	03/2010 -	03/2019	108	201.05	
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	203.73	03/2013 -	03/2019	72	0	Delay in Forest diversion and EMP clearance
27	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84	0	
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.14	03/2012 -	03/2019	84	0	
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	80.62	03/2014 -	03/2019	60	0	

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
43	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	394.74	07/2015 -	05/2017	22	0	
44	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,905.00	03/2013 -	06/2017	51	0	
45	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	728.59	07/2015 -	06/2017	23	0	
46	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	140.55	09/2016 -	06/2017	9	0	
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	178.65	12/2015 -	06/2017	18	17.5	
48	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	324.87	262.93	12/2015 -	06/2017	18	0	
49	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	478.53	07/2016 -	07/2017	12	0	
50	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	206.71	141.28	12/2016 07/2017	07/2017	7	17.79	
51	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	115.64	05/2016 -	10/2017	17	0	
52	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	12,136.78	05/2015 12/2017	12/2017	31	0	forest clearance, RoU, RoW
53	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	12.04	
54	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	190.50	10/2016 -	03/2018	17	42.39	
55	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
56	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	78.00	12/2017 -	05/2018	5	0	
57	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	53.68	10/2017 -	07/2018	9	0	
58	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	Delay in clearances by the Central Government
59	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
60	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
61	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	Total		41,293.75 -	41,520.97	32,142.45					
	<u>PETROLEUM</u>									
62	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	1,687.77	11/2015 01/2017	05/2017	18	0	
63	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	4.16	04/2017 -	05/2017	1	0	
64	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	887.00	03/2015 -	05/2017	26	37.72	
65	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	534.50	09/2011 06/2017	06/2017	69	0	
66	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,387.47	12/2016 06/2017	06/2017	6	0	
67	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA	01/2006	993.00 1,693.00	1,693.00	1,537.45	01/2012 -	06/2017	65	70.49	Court Cases and RoU

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
68	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	112.86	05/2015 06/2017	06/2017	25	0	
69	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT	11/2015	500.00 435.00	435.00	304.20	03/2017 06/2017	06/2017	3	-13	
70	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 259.93	259.93	141.18	07/2014 09/2017	09/2017	38	73.29	
71	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,079.94	05/2013 05/2017	10/2017	53	45.83	
72	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	153.97	03/2017 10/2017	10/2017	7	0	
73	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	215.38	128.25	06/2017 06/2017	10/2017	4	0	heavy monsoon
74	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,259.49	4,259.49	3,201.25	04/2016 12/2017	12/2017	20	3.28	
75	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	35.76	11/2016 -	02/2018	15	0	
76	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	237.72	07/2017 02/2018	02/2018	7	0	
77	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,931.23	03/2013 03/2018	03/2018	60	-3.5	
78	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,348.25	03/2015 03/2018	03/2018	36	29.42	procurement
79	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	3,466.38	12/2014 03/2018	03/2018	39	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
80	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	333.57	10/2014 03/2018	03/2018	41	133.5	severe resistance from villagers
81	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	144.01	12/2016 -	03/2018	15	-8.51	
82	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	173.28	119.72	01/2017 06/2017	03/2018	14	-4.28	RoU
83	NEW 250 TMTPA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 190.45	190.45	104.95	09/2017 03/2018	03/2018	6	0	
84	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,890.18	05/2014 12/2017	05/2018	48	0	-Pipeline package tender was cancelled 4 times due to various reasons viz. legal issues, change in scope in view of taking over of JV facilities, high quoted price etc. Pipeline Project progress affected due to inability of M/s. Swiber due to financial problems.
85	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,359.34	05/2017 05/2018	05/2018	12	1.87	
86	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2017	05/2018	12	-27.64	
87	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	104.65	07/2016 06/2018	06/2018	23	-20.81	
88	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	1,565.57	09/2017 06/2018	06/2018	9	0	
89	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	85.59	03/2017 11/2018	11/2018	20	24.53	
90	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,397.00	911.00	01/2013 12/2018	12/2018	71	-14.15	
91	POLYPROPYLENE PLANT AT PARADIPI REFINERY - [N16000179]IOCL, ODISHA	03/2014	3,150.00 -	3,150.00	950.69	09/2017 12/2018	12/2018	15	0	
92	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	99.05	10/2017 03/2019	03/2019	17	17.66	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
93	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	3,961.54	3,019.16	12/2017 03/2019	03/2019	15	-14.25	
94	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	213.51	03/2019 -	04/2019	1	0	
95	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	4,701.44	1,960.89	05/2019 05/2019	10/2019	5	-22.75	
96	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	222.19	2.00	01/2014 11/2019	11/2019	70	9.49	
97	PARADIP LPG IMPORT FACILITY - [N16000196]OCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 11/2019	11/2019	16	0	
98	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	-	03/2019 05/2020	05/2020	14	0	
	Total		58,728.99 -	58,111.86	36,280.65					
	<u>POWER</u>									
99	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	245.00	237.49	06/2012 -	06/2017	60	5.45	
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 757.94	757.94	616.22	07/2013 06/2017	06/2017	47	.7	Balance Kishenpur – New Wanpoo line affected due to ROW problem & disturbance in Jammu & Kashmir.
101	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,312.86	09/2014 06/2017	06/2017	33	39.3	Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS – Madhugiri line. Matter resolved progressively with the help of Police protection.
102	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 9,291.03	9,291.03	7,148.89	06/2015 06/2017	06/2017	24	-2.91	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	704.52	11/2014 06/2017	06/2017	31	21.9	Implementation affected due to severe ROW problem in Uttarakhand in Dehradun-Abdullapur line. Progress of Dulhasti-Kishenpur line, site work affected due to severe ROW at 02 locs. in Doda distt. and disturbance in J&K
104	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 1,656.15	1,656.15	1,296.40	05/2016 05/2017	06/2017	13	5.13	
105	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 376.09	376.09	195.40	02/2017 06/2017	06/2017	4	30.37	
106	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 244.66	244.66	100.10	02/2016 06/2017	06/2017	16	24.46	
107	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	13,390.00	01/2017 07/2017	07/2017	6	0	
108	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	121.70	03/2016 07/2017	07/2017	16	32.69	
109	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 2,619.56	2,619.56	2,563.73	07/2014 09/2017	09/2017	38	23.13	Balance Aurangabad-Boisor line affected due to severe ROW in routing of line through grape garden area being resolved progressively with support for State Govt.
110	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,441.52	1,329.43	1,212.66	07/2006 09/2017	09/2017	134	260.55	Local agitation, Poor condition of roads
111	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	129.33	09/2014 09/2017	09/2017	36	0	
112	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,119.84	04/2016 09/2017	09/2017	17	38.61	
113	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	396.40	08/2016 10/2017	10/2017	14	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04	305.04	102.60	03/2017 10/2017	10/2017	7	0	
115	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	347.20	11/2016 11/2017	11/2017	12	5.34	
116	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	641.09	09/2010 12/2017	12/2017	87	54.59	Severe ROW problem in balance 02 lines, (400KV D/C Vapi-Navi Mumbai line & LILO at Navi Mumbai). LILO line is being completed using underground cable, however, ROW problem for laying of cable continue. Cable burnt/ damaged by miscreants. Critical. Vapi-Navi Mumbai line now decided to be terminated at Kudus S/stn. Further, its commissioning is linked to readiness of Kudus S/s of MSETCL. Critical.
117	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,580.00	09/2011 06/2017	12/2017	75	54.25	
118	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,399.06	08/2013 12/2017	12/2017	52	133.06	
119	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,547.20	08/2013 12/2017	12/2017	52	23.65	Implementation affected due to agitation against Big Dam proj. affecting the construction works in Assam and adverse law & order situation in NER. Lower Subhansiri-B'Chariyali line in almost standstill since Dec'11 due to agitation. Gen. Proj. are also getting delayed. Kameng HEP is anticipated in Dec'17 & Lower Subhansiri HEP is uncertain.

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
120	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,391.53	11/2012 12/2017	12/2017	61	36.01	Implementation of balance work affected due to delay in land acquisition of Daltonganj (land acquired in May'15). Down stream 220KV line of state at Daltonganj required matching with readiness of Sasaram - Daltonganj line.
121	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	353.47	08/2014 12/2017	12/2017	40	43.37	Implementation affected due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Compensation order issued by State in line with Govt. guidance. Villages-wise compensation rate is to be decided by Distt. Admn. (awaited) for which corridor survey is under progress.
122	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,882.93	08/2014 12/2017	12/2017	40	27.6	Implementation of balance works affected due to ROW problem & delay in completion Kudus (Padghe) S/stn. being executed by MSETCL.
123	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	549.20	06/2015 12/2017	12/2017	30	36.74	Completion matching with Srikakulam – Garividi line being executed under TBCB rout (ant. by Dec'17).
124	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,878.35	12/2015 12/2017	12/2017	24	0	Implementation affected due to severe ROW problem in Odisha & huge forest involvement in Chattisgarh Stg.-I forest clearance awaited. Critical
125	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	67.00	04/2016 12/2017	12/2017	20	0	
126	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	465.36	12/2016 -	12/2017	12	37.96	
127	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	5,649.46	12/2009 01/2018	01/2018	97	147.51	Geological issues, Flash flood in 2008

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
128	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,783.17	4,892.47	01/2016 -	01/2018	24	58.79	
129	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,466.58	10/2012 02/2018	02/2018	64	5.14	
130	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,517.90	12/2012 02/2018	02/2018	62	36.79	Implementing of balance lines affected due to local disturbances & geographical constraints. 03 lines in Arunachal Pradesh affected due to compensation issues & land ownership disputes and further their commissioning linked to readiness of up stream/ down stream system being implemented by Govt. of Arunachal Pradesh. Issue getting resolved with support of state/Distt. Admn.
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	378.30	06/2016 02/2018	02/2018	20	0	Implementation affected due to severe ROW problem.
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 969.97	969.97	648.20	06/2016 02/2018	02/2018	20	6.82	Implementation affected due to severe ROW problem / Court case demanding high compensation. Work recommenced after Hon'ble High Court order.
133	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	116.41	02/2014 -	02/2018	48	0	
134	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 5,135.01	5,135.01	3,289.85	01/2015 03/2018	03/2018	38	16.58	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
135	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	481.82	06/2014 03/2018	03/2018	45	31.17	Balance 400KV Madugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Re-NIT done & award under progress of balance work.
136	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,639.00	7,508.00	09/2017 03/2018	03/2018	6	0	
137	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	5,353.00	5,472.83	05/2014 03/2017	03/2018	46	0	
138	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,079.75	12/2016 -	03/2018	15	0	
139	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	551.80	04/2017 03/2018	03/2018	11	0	
140	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	7,620.00	11/2016 12/2017	04/2018	17	0	
141	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,103.00	06/2017 12/2017	04/2018	10	0	
142	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,201.00	01/2011 05/2018	05/2018	88	73.65	
143	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	6,002.44	01/2018 -	06/2018	5	0	
144	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,939.45	11/2008 09/2018	09/2018	118	22.93	Implementation of balance 01 line (Edamon-Muvattupuzha line) is affected due to severe ROW problem (long pending). Problem being addressed progressively as per latest Revised G.O. of 30.07.15 (compensation to be done on land value, to be finalised by concerned DC with the support of State Govt.). Works resumed after re-award.

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
145	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,352.57	945.96	09/2017 -	09/2018	12	31.55	
146	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,275.55	09/2009 -	12/2018	111	114.28	
147	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	3,156.00	03/2013 06/2019	06/2019	75	29.14	
148	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	10.50	05/2017 06/2019	06/2019	25	0	
149	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,182.02	06/2013 -	12/2019	78	0	
150	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	260.20	12/2018 -	12/2019	12	0	
151	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	246.00	12/2018 -	12/2019	12	0	
152	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	4,911.00	02/2019 02/2020	02/2021	24	0	
153	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	139.96	04/2020 -	01/2023	33	0	
	Total		1,97,490.96 -	2,28,408.62	1,54,796.98					
	HEAVY INDUSTRY									
154	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	3,827.30	2289.00	09/2011 -	12/2017	75	122.78	train manpower was not available in the country

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		1,718.00 -	3,827.30	2289.00					
	HEALTH AND FAMILY WELFARE									
155	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	168.90	68.00	05/2017 07/2017	10/2017	5	0	local protest
156	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	127.00	05/2017 -	12/2017	7	0	delay in release of fund + stoppage of work by NGT
157	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	184.70	05/2017 -	12/2017	7	0	Fund Release in intermittent interval
158	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	-	05/2018 08/2019	08/2019	15	0	
	Total		1,030.98 -	1,030.98	379.70					
	RAILWAYS									
159	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	913.84	03/2010 -	06/2017	87	38.24	
160	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	554.70	342.00	01/1999 06/2017	06/2017	221	77.08	
161	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 843.45	966.98	874.72	02/2009 12/2017	12/2017	106	520.89	
162	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	516.40	370.69	03/2010 -	12/2017	93	58.94	
163	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	0	
164	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	150.22	03/2016 -	12/2017	21	29.06	
165	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	495.74	386.03	06/2013 -	03/2018	57	0	
166	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	5,000.00	4,090.26	04/2008 12/2011	06/2018	122	233.33	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
167	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	
168	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018	193	682.6	
169	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	631.67	03/2016 -	12/2018	33	-10.11	
170	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019	123	310.64	
171	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
172	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,161.64	353.32	03/2015 -	03/2019	48	40	
173	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 658.07	941.04	575.19	03/2014 03/2019	03/2019	60	44.07	
174	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	1.06	
175	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	0	
176	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,160.54	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
177	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.70	199.98	02/2015 -	12/2019	58	556.39	
178	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	318.00	258.17	02/2006 -	12/2019	166	21.51	
179	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	514.44	03/2004 03/2020	03/2020	192	259.68	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
193	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	410.32	02/2009 -	05/2017	99	28.93	
194	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	209.80	04/2009 -	05/2017	97	92.75	
195	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	268.94	11/2008 -	05/2017	102	0	
196	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	195.35	11/2008 -	05/2017	102	80.68	
197	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	245.83	04/2009 -	05/2017	97	0	
198	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	05/2017	110	0	
199	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	340.12	07/2009 -	05/2017	94	68.99	
200	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	168.31	02/2010 -	05/2017	87	2.29	
201	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	0	
202	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	05/2017	23	0	
203	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	05/2017	46	0	
204	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	05/2017	42	0	
205	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	05/2017	39	0	
206	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	541.42	09/2013 -	05/2017	44	0	
207	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,354.75	09/2014 -	05/2017	32	0	
208	REHABILITATION AND UPGRADEATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
209	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	401.11	200.96	01/2017 -	05/2017	4	0	
210	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	503.16	211.03	08/2016 -	05/2017	9	0	
211	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	103.08	11/2016 -	05/2017	6	0	
212	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	297.81	04/2008 01/2017	06/2017	110	0	
213	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	885.43	03/2013 -	06/2017	51	0	
214	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	06/2017	49	0	
215	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	06/2017	48	0	
216	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	964.46	07/2013 -	06/2017	47	0	
217	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	671.62	01/2014 -	06/2017	41	0	
218	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,620.72	05/2014 -	06/2017	37	0	
219	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	494.33	04/2014 -	06/2017	38	0	
220	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	869.91	08/2013 -	06/2017	46	0	
221	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	06/2017	33	0	
222	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,004.42	08/2013 -	06/2017	46	0	
223	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	06/2017	36	0	
224	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	06/2017	41	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
225	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	351.34	160.49	01/2016 -	06/2017	17	0	
226	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	495.78	239.48	01/2016 -	06/2017	17	0	
227	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	530.07	234.21	08/2016 -	06/2017	10	0	
228	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2017	1	0	
229	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH, ODISHA	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	13	.26	
230	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	469.54	05/2013 -	07/2017	50	0	
231	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,566.61	07/2015 -	07/2017	24	0	
232	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	4,508.05	12/2015 -	07/2017	19	0	
233	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	834.00	09/2016 -	07/2017	10	0	
234	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	08/2017	69	106.5	
235	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017	48	0	
236	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
237	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	785.00	08/2016 -	08/2017	12	0	
238	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	7	-01	
239	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	09/2017	73	0	
240	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,206.00	04/2013 -	09/2017	53	2.65	
241	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2017	42	0	
242	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	09/2017	38	0	
243	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	345.22	06/2014 -	09/2017	39	0	
244	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,328.50	02/2014 -	09/2017	43	0	
245	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	217.87	09/2016 -	09/2017	12	0	
246	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	70.23	09/2016 -	09/2017	12	0	
247	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	09/2017	22	51.83	
248	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,036.26	07/2013 -	10/2017	51	0	
249	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	10/2017	53	0	
250	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
251	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	870.15	09/2014 -	10/2017	37	0	
252	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	
253	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	1,077.66	03/2013 -	11/2017	56	0	
254	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	0	
255	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	0	
256	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	297.35	11/2016 -	11/2017	12	0	
257	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 2,782.54	3,237.87	2,948.41	09/2012 12/2017	12/2017	63	114.56	
258	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,486.59	08/2014 -	12/2017	40	0	
259	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2017	57	0	
260	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.34	12/2013 -	12/2017	48	0	
261	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	236.00	05/2013 -	12/2017	55	0	
262	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	303.07	08/2013 -	12/2017	52	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
263	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	0	
264	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	545.27	11/2013 -	12/2017	49	0	
265	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,216.15	06/2014 -	12/2017	42	0	
266	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	580.43	226.67	08/2013 -	12/2017	52	0	
267	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	277.41	10/2013 -	12/2017	50	-11	
268	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00	498.11	06/2015 -	12/2017	30	0	
269	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,607.34	04/2015 -	12/2017	32	0	
270	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
271	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	77.49	01/2016 -	12/2017	23	0	
272	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	12/2017	74	0	
273	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	957.02	07/2017 -	01/2018	6	0	
274	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,288.43	11/2016 -	02/2018	15	0	
275	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.61	07/2013 -	03/2018	56	0	
276	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,674.82	08/2013 -	03/2018	55	0	
277	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
278	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
279	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	574.74	03/2014 -	04/2018	49	0	
280	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	0	
281	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.29	02/2013 -	06/2018	64	0	
282	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	11.37	12/2017 -	06/2018	6	0	
283	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
284	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	0	
285	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	
286	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	0	
287	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	0	
288	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
289	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
290	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
291	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	Total		82,263.28 -	86,298.58	85,185.44					
	SHIPPING AND PORTS									
292	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 03/2016	12/2017	141	300	slow progress by contractor
293	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	411.12	12/2010 12/2018	12/2018	96	82.72	
	Total		516.39 -	1,269.46	550.92					
	TELECOMMUNICATIONS									
294	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	2,060.00	07/2015 09/2017	09/2017	26	0	
	Total		13,334.00 -	13,334.00	2,060.00					
	URBAN DEVELOPMENT									
295	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	72.96	03/2017 -	06/2017	3	0	
296	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 405.01	405.01	219.34	12/2014 06/2017	06/2017	30	0	
297	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	216.89	09/2016 01/2017	08/2017	11	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
298	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	277.92	06/2015 08/2016	08/2017	26	0	
299	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	219.38	05/2017 08/2017	08/2017	3	0	
300	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	153.40	12/2015 12/2016	09/2017	21	0	
301	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	281.57	03/2015 03/2017	09/2017	30	37.1	
302	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	49.82	11/2015 -	11/2017	24	0	
303	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	270.83	75.52	11/2014 05/2017	12/2017	37	0	
304	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	196.00	03/2016 12/2017	12/2017	21	44.75	
305	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 170.62	170.62	127.15	03/2012 08/2016	12/2017	69	-16.77	
306	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	12,472.32	12/2015 -	12/2017	24	0	
307	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	1.31	03/2016 02/2018	02/2018	23	0	

Details of Delayed Projects w.r.t. Original Schedule

(May 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
308	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	98.07	08/2016 03/2017	03/2018	19	0	
309	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	0	
310	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 06/2017	06/2018	39	0	fund constraint
311	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
312	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21	0	
313	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	land acquisition
314	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	10.53	10/2019 -	03/2020	5	0	
	Total		59,805.11 -	60,008.58	18,630.36					
	Grand Total		5,42,127.36	6,45,233.47	4,07,427.12					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(May 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82	85
	Total		3,492.00 -	6,000.00				
	<u>CIVIL AVIATION</u>							
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2017	78.87	80
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		624.07 -	994.86				
	<u>COAL</u>							
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59	03/2015 -	03/2020	201.51	60
5	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	518.04	03/2010 -	03/2019	201.05	108
6	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58	72
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97	24
	Total		1,433.33 -	2,440.09				
	<u>FERTILISERS</u>							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89	10
	Total		197.79 -	209.44				
	<u>HEAVY INDUSTRY</u>							
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>PETROLEUM</u>							
11	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217	06/2012	150.00 -	259.93	07/2014 -	09/2017	73.29	38
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	222.19	01/2014 -	11/2019	9.49	70
13	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50	41
14	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53	20
15	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	10/2017	45.83	53
17	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	05/2017	37.72	26
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	06/2017	70.49	65
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42	36
20	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	05/2013	4,124.35 -	4,259.49	04/2016 -	12/2017	3.28	20
21	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87	12
	Total		16,238.96 -	19,246.91				
	<u>POWER</u>							
22	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	03/2014	155.57 -	206.42	03/2016 -	07/2017	32.69	16
23	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	02/2014	196.58 -	244.66	02/2016 -	06/2017	24.46	16
24	SYSTEM STRENGTHENING XII OF SR - [N18000085	02/2010	232.34 -	245.00	06/2012 -	06/2017	5.45	60
25	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169	08/2014	288.49 -	376.09	02/2017 -	06/2017	30.37	4
26	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37	40
27	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,329.43	07/2006 02/2015	09/2017	260.55	134

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
28	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96	12
29	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2017	54.59	87
30	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	03/2018	31.17	45
31	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	12/2017	36.74	30
32	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	11/2017	5.34	12
33	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	12/2017	133.06	52
34	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	11/2014 -	06/2017	21.90	31
35	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]	07/2010	752.64 -	757.94	07/2013 -	06/2017	.70	47
36	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	02/2018	6.82	20
37	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01	61
38	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	09/2017	38.61	17
39	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	09/2013	1,575.30 -	1,656.15	05/2016 -	06/2017	5.13	13
40	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60	40
41	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
42	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALISTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,352.57	09/2017 -	09/2018	31.55	12
43	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	06/2017	39.30	33
44	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	09/2017	23.13	38
45	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79	62
46	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	01/2018	147.51	97

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
47	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14	75
48	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,783.17	01/2016 -	01/2018	58.79	24
49	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111
50	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	12/2017	54.25	75
51	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58	38
52	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14	64
53	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
54	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
55	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I [N18000151	03/2013	11,638.55 -	11,639.00	09/2017 -	03/2018	.00	6
	Total		80,777.09 -	1,11,973.48				
	<u>RAILWAYS</u>							
56	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
57	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39	58
58	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
59	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51	166
60	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
61	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94	93
62	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
63	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
64	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
65	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
66	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21
67	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) [N22000113]	04/2008	653.19 -	941.04	03/2014 -	03/2019	44.07	60
68	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.23	06/1999 -	12/2020	29.44	258
69	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87
70	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
71	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64	123
72	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144
73	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
74	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,161.64	03/2015 -	03/2019	40.00	48
75	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
76	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
77	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
78	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
79	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33	122
80	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
81	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		23,663.30 -	86,886.98				
	ROAD TRANSPORT AND HIGHWAYS							
82	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
83	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	05/2017	80.68	102
84	WIDENING AND STRENGTHENING OF EXISTING SLIL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26	13

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
85	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	05/2017	68.99	94
86	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	05/2017	92.75	97
87	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29	87
88	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2017	28.93	99
89	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83	22
90	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50	69
91	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65	53
92	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63
	Total		6,283.38 -	10,319.54				
	<u>SHIPPING AND PORTS</u>							
93	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00	141
94	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		516.39 -	1,269.46				
	<u>STEEL</u>							
95	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	06/2017	17.50	18
96	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79	7
97	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04	12
98	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39	17
	Total		870.83 -	1,098.05				
	<u>URBAN DEVELOPMENT</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
99	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	349.33	03/2016 -	12/2017	44.75	21
100	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091	08/2014	350.02 -	479.87	03/2015 -	09/2017	37.10	30
	Total		591.35 -	829.20				
	Grand Total		1,36,406.49	2,45,095.31				

Details of Projects Without Date of Commissioning

Annexure - VIII

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ATOMIC ENERGY</u>				
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	12/2008 10/2013	03/2017
	Total		13,171.00 -		
	<u>CIVIL AVIATION</u>				
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-
	Total		335.61 -		
	<u>COAL</u>				
3	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	03/2010 -	03/2017
4	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	03/2017
5	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	04/2017
	Total		1,744.94 -		
	<u>MINES</u>				
6	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 344.50	11/2016 12/2016	09/2016
7	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 355.13	11/2016 12/2016	12/2016
	Total		699.63 -		
	<u>STEEL</u>				
8	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 03/2016	03/2016
9	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016
10	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
11	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
	Total		1,375.18 -		
	<u>PETROLEUM</u>				

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
12	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	11/2015 11/2016	10/2016
13	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	07/2016 02/2017	01/2017
14	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	03/2013 01/2017	01/2017
15	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 222.81	09/2016 02/2017	02/2017
16	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	03/2017 -	03/2017
17	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	08/2015 03/2017	03/2017
18	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	16,504.00 -	03/2017 -	03/2017
19	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	Total		20,633.74 -		
	<u>POWER</u>				
20	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	01/2013 -	03/2016
21	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	11/2013 -	03/2016
22	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 609.44	02/2014 03/2016	03/2016
23	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
24	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT	10/2015	315.00 -	10/2016 -	10/2016
25	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	02/2017 -	02/2017
26	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	12/2011 03/2016	02/2017
27	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 03/2017	03/2017
28	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 03/2017	03/2017
29	KANDORNA AND BHANWAD WIND FARM - [N18000234]THDCIL,GUJARAT	11/2016	415.49 -	03/2017 -	03/2017
30	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	10/2016 04/2017	04/2017
31	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	04/2017 -	04/2017
32	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,HIMACHAL PRADESH	12/2005	358.42 -	12/2008 09/2010	-
33	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,078.31	07/2013 -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
35	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC, RAJASTHAN	02/2015	302.49 302.00	02/2016 -	-
	Total		32,906.85 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
36	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI	11/2013	196.70 -	01/2016 -	01/2016
37	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI	09/2013	444.70 -	12/2015 -	07/2016
38	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	11/2013 -	10/2016
39	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	-
40	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		1,390.58 -		
	<u>RAILWAYS</u>				
41	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM	04/2003	971.22 -	- -	12/2009
42	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM	04/2007	180.09 -	- -	05/2011
43	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011
44	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 266.00	- -	12/2012
45	HARMUTI-NAHARLAGUN - [N22000382]NFR, MULTI STATE	04/2006	614.54 -	- -	04/2014
46	DUDHNOI-MENDHIPATHAR - [N22000378]NFR, MULTI STATE	04/1992	315.64 -	- -	08/2014
47	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR, ASSAM	04/2003	4,300.00 -	- -	05/2015
48	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	07/2015
49	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
50	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 230.00	- 10/2015	10/2015
51	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	238.56 717.15	03/2012 01/2016	01/2016
52	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016
53	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016
54	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 -	12/2012 -	03/2016

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
55	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016
56	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016
57	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	03/2012 -	12/2016
58	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016
59	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016
60	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 1,289.92	- -	01/2017
61	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	02/2017
62	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	02/2017
63	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017
64	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	03/2017
65	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	03/2017
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2017
67	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	03/2017
68	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017
69	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]JMRT,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017
70	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017
71	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 579.03	03/2017 -	03/2017
72	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
73	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
74	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
75	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
76	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 774.90	- -	-
77	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
78	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
79	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
80	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 458.26	07/2008 -	-
81	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
82	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
83	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	-
84	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
85	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
86	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 781.02	06/2007 -	-
87	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
88	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.08	02/2011 -	-
89	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 724.89	12/2012 12/2012	-
90	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
91	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
92	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
93	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
94	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
95	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
96	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
97	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	-
98	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
99	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
100	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	03/2012 -	-
101	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
102	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 -	-
103	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 155.56	12/2010 03/2017	-
104	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 334.87	12/2012 06/2016	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
105	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
106	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
107	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
108	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
109	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
110	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
111	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
112	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
113	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
114	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
115	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
116	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 335.53	- -	-
117	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
118	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
119	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
120	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-
121	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 633.87	- -	-
122	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
123	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
124	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 549.75	- -	-
125	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
126	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
127	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
128	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
129	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
130	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
131	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
132	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
133	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
134	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
135	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
136	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
137	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 268.52	- -	-
138	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
139	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 319.58	- -	-
140	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 290.85	- -	-
141	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 260.60	- -	-
142	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-
143	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 234.41	03/2015 -	-
144	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 238.36	- -	-
145	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
146	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-
147	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 104.80	- -	-
148	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 198.88	- -	-
149	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
150	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
151	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
152	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 186.64	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
153	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 173.91	- -	-
154	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 370.81	- -	-
155	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 131.47	- -	-
156	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 79.39	- -	-
157	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 681.68	- -	-
158	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
159	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-
160	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
161	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	- -	-
162	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
163	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
164	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
165	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
166	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
167	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
168	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
169	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 197.17	- -	-
170	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
171	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
172	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
173	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
174	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
175	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
176	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	- -	-
177	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
178	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
179	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
180	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
181	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
182	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
183	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
184	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
185	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
186	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
187	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
188	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
189	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
190	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
191	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
192	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
193	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 259.23	- -	-
194	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 272.20	- -	-
195	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
196	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
197	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
198	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-
199	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 203.40	- -	-
200	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
201	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
202	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
203	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 1,072.52	- -	-
204	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
205	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-
206	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
207	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
208	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 3,631.00	- -	-
209	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
210	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
211	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
212	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-
213	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
214	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
215	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
216	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	-
217	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	-
218	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	-
219	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
220	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
221	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
222	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
223	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
224	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
225	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
226	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
227	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
228	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
229	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
230	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
231	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
232	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
233	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
234	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
235	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
236	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	- -	-
237	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER, MULTI STATE	04/2010	268.52 -	- -	-
238	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 203.00	- 03/2017	-
239	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	- -	-
240	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE	04/2013	1,239.00 -	- -	-
241	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	- -	-
242	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
243	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR	05/2015	380.00 -	- -	-
244	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR, HARYANA	05/2015	400.00 -	- -	-
	Total		1,94,445.75 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
245	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD, ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
246	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD, ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
247	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD, MIZORAM	08/2010	195.04 -	10/2010 -	10/2010

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
248	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
249	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
250	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
251	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
252	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014
253	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014
254	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
255	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
256	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
257	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
258	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
259	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015
260	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015
261	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
262	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015
263	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015
264	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
265	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
266	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
267	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
268	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
269	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
270	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
271	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016
272	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
273	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
274	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
275	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
276	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
277	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
278	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
279	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016
280	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
281	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016
282	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016
283	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
284	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
285	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016

Details of Projects Without Date of Commissioning

					(May 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
286	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
287	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
288	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
289	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016
290	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016
291	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016
292	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
293	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
294	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
295	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016
296	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
297	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017
298	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017
299	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017
300	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017
301	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017
302	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017
303	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017
304	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	03/2017
305	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2017

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
306	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017
307	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017
308	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017
309	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017
310	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017
311	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017
312	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017
313	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 06/2016	04/2017
314	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 12/2016	04/2017
315	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	04/2017
316	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	04/2017
317	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	04/2017
318	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017
319	FOUR LANING OF ORISSA/CHHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATTISGARH	02/2013	1,232.00 -	08/2015 -	04/2017
320	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
321	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
322	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI-ENMORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
323	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
324	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
325	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
326	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
327	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
328	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
329	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
330	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
331	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
332	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
333	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
334	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
335	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
336	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
337	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
338	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
339	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
340	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
341	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
342	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-

Details of Projects Without Date of Commissioning

					(May 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
343	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
344	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
345	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
346	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
347	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
348	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
349	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
350	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
351	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
352	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
353	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
354	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
355	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
356	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
357	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
358	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
359	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
360	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
361	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
362	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
363	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
364	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
365	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
366	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
367	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
368	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
369	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
370	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
371	CONST. OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
372	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
373	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
374	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
375	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
376	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
377	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
378	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
379	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
380	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
381	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
382	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
383	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
384	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
385	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
386	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
387	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
388	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
389	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
390	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
391	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
392	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
393	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
394	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
395	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
396	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
397	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
398	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
399	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
400	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-
401	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
402	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
403	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
404	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	-
405	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-
406	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-
407	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	-
408	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
409	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
410	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
411	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
412	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
413	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
414	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
415	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
416	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
417	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
418	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
419	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
420	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
421	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
422	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
423	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
424	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
425	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
426	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
427	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
428	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
429	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
430	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
431	4-LANING OF HOSKOTE-DOBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
432	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	-
433	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	-
434	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
435	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	-
436	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	-
437	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-
438	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
439	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
440	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
441	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
442	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	-
443	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	- -	-
444	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN	09/2016	1,239.82 -	- -	-
445	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	- -	-
446	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	-
447	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	- -	-
448	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- -	-
449	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- -	-
450	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	- -	-
451	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-
452	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-
453	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-
454	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
455	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	-
456	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-
457	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
458	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	- -	-
459	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	- -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
460	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
461	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
462	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
463	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
464	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
465	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
466	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
467	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
468	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
469	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
470	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
471	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
472	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
473	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
474	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
	Total		1,25,521.22 -		
	<u>SHIPPING AND PORTS</u>				
475	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU	12/2014	274.85 -	04/2017 -	04/2017
476	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
477	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-

Details of Projects Without Date of Commissioning

(May 2017)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		2,947.92 -		
	<u>TELECOMMUNICATIONS</u>				
478	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	03/2017
	Total		2,111.17 -		
	<u>URBAN DEVELOPMENT</u>				
479	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015
480	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016
481	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 13,845.01	06/2011 12/2015	04/2017
482	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-
483	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
484	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		69,456.20 -		
	Grand Total		4,66,739.79		

Details of Projects Without Original Date of Commissioning

Annexure - IX

(May 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	175.00	1.83	- -	12/2017	-	0/0
	Total		175.00 -	175.00	1.83				0/0
	<u>RAILWAYS</u>								
2	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,595.40	1,679.13	1,698.69	- -	05/2017	-	0/0
3	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	195.64	351.04	- -	06/2017	-	0/0
4	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	268.78	87.86	- -	08/2017	-	0/0
5	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	413.56	343.54	- -	10/2017	-	0/0
6	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	199.75	199.41	- -	12/2017	-	0/0
7	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 -	365.00	32.81	- -	12/2017	-	0/0
8	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL, MULTI STATE	04/2008	822.39 -	1,480.83	1,421.19	- -	03/2018	-	0/1
9	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 -	445.00	319.06	- -	03/2018	-	0/0
10	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	330.00	87.65	- -	03/2018	-	0/0
11	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	1,871.00	1,081.00	- -	03/2018	-	0/0
12	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	66.66	- -	05/2018	-	0/0
13	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 855.16	855.16	585.06	- -	05/2018	-	0/0
14	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 157.94	157.94	47.63	- -	11/2018	-	0/0
15	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	720.00 678.54	678.54	-	- 12/2018	12/2018	0(R3)	0/38

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 348.55	348.55	14.66	- -	02/2019	-	0/0
17	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 218.39	272.99	63.54	- -	02/2019	-	0/0
18	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	648.00	-	- -	02/2019	-	0/0
19	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 372.09	525.00	544.20	- 03/2019	03/2019	0(R3)	0/0
20	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 1,319.33	1,319.33	757.23	- 12/2009	03/2019	111(R1)	0/0
21	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	620.08	- 09/2009	03/2019	114(R1)	0/0
22	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	780.00	285.64	- -	03/2019	-	0/0
23	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	399.63	-	- -	03/2019	-	0/0
24	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	-	0/0
25	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	293.68	76.86	- -	03/2019	-	0/0
26	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
27	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	450.00	.79	- -	03/2019	-	0/0
28	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	508.00	285.31	- -	03/2019	-	0/0
29	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	398.93	.57	- -	03/2019	-	0/0
30	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,127.00	598.29	- -	03/2019	-	0/1
31	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	355.96	149.07	- -	03/2019	-	0/0
32	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	718.54	265.71	- -	05/2019	-	0/0
33	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 580.00	580.00	-	- 07/2019	07/2019	0(R3)	2/3
34	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	2,145.00	361.21	- -	03/2020	-	0/0
35	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	975.62	21.53	- -	03/2020	-	0/0
36	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
37	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	193.46	- -	03/2020	-	0/0
38	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 1,160.83	1,160.83	268.41	- 03/2020	03/2020	0(R3)	1/1
39	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	94.33	- -	03/2020	-	0/0
40	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	237.57	- -	03/2020	-	0/0
41	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	266.97	- 11/2015	03/2020	52(R3)	0/2
42	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	644.38	.11	- -	12/2020	-	0/0
43	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	1,266.89	55.00	- -	12/2020	-	0/0
44	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,045.20	2,125.18	14.17	- -	03/2021	-	0/0
45	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 1,849.60	2,713.09	632.05	- 03/2021	03/2021	0(R3)	0/0
46	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	6,000.00	14.80	- -	03/2021	-	0/0
47	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	1,579.27	168.29	- 03/2020	03/2021	12(R3)	0/0
48	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 843.04	843.04	4.30	- 03/2021	03/2021	0(R3)	0/0
49	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	.14	- 03/2021	03/2021	0(R3)	0/0
50	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,232.32	-	- -	03/2021	-	0/0
51	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	870.96	-	- -	03/2021	-	0/0
52	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	-	0/0
53	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	3,004.90	572.56	- 06/2021	06/2021	0(R3)	0/0
54	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 1,160.47	1,160.47	1.74	- -	03/2022	-	0/1
55	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	331.91	- 03/2022	03/2022	0(R3)	0/0
56	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	247.50	- 03/2021	06/2022	15(R3)	0/0
57	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	2,271.50	812.01	- 12/2020	-	-	0/0
58	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 332.14	332.14	87.22	- 03/2019	-	-	0/0

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
59	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	3,168.29	532.82	- 03/2023	-	-	0/0
60	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	540.02	98.02	- 03/2022	-	-	0/0
61	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 1,141.00	1,141.00	341.86	- 03/2020	-	-	0/5
62	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	9,968.00	-	- 03/2024	-	-	0/0
63	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	2,425.00	-	- 03/2024	-	-	0/0
64	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	1,272.19	19.48	- 03/2022	-	-	0/0
65	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	2,449.91	.63	- 03/2023	-	-	0/0
66	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	3,627.47	-	- 03/2023	-	-	0/0
67	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	2,081.27	-	- 03/2023	-	-	0/0
68	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	1,035.16	-	- 03/2022	-	-	0/0
69	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	637.95	.35	- 03/2022	-	-	0/0
70	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	792.89	52.35	- 03/2021	-	-	0/0
71	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	199.12	142.22	- 03/2019	-	-	0/0
	Total		69,136.82 -	95,915.60	16,147.16				3/52
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
72	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	349.60	- -	05/2017	-	0/0
73	HUNGUND-SURATHKAL AND MANGALORE- KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	06/2017	-	3/3
74	REHABILITATION AND UPGRADATION OF NH- 222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	446.77	87.62	- -	06/2017	-	0/4
75	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	795.76	-	- -	06/2017	-	0/0
76	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	794.30	-	- -	06/2017	-	0/0
77	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	-	- -	06/2017	-	0/0

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
78	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	546.24	- -	06/2017	-	0/0
79	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	13.43	- -	10/2017	-	0/4
80	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	47.56	- -	11/2017	-	0/0
81	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	-	- -	11/2017	-	0/0
82	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
83	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	1,665.00	1,185.55	- -	12/2017	-	0/0
84	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
85	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0
86	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	1,060.85	- -	01/2018	-	0/0
87	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
88	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	771.18	-	- -	03/2018	-	0/0
89	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	38.33	- -	04/2018	-	0/1
90	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
91	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	509.13	-	- 04/2018	04/2018	0(R3)	0/0
92	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	-	- 04/2018	04/2018	0(R3)	0/0
93	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	18.48	- -	04/2018	-	0/0
94	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	-	- -	05/2018	-	0/0

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
95	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	-	- -	05/2018	-	0/0
96	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	-	- -	05/2018	-	0/0
97	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	-	- -	05/2018	-	0/0
98	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	154.48	- -	05/2018	-	0/0
99	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	-	- 05/2018	05/2018	0(R3)	0/0
100	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	6.14	- -	05/2018	-	0/0
101	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	600.85	-	- -	05/2018	-	0/0
102	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	676.73	-	- -	06/2018	-	0/0
103	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
104	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	- -	07/2018	-	0/0
105	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	-	- -	07/2018	-	0/0
106	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	244.00	-	- -	07/2018	-	0/0
107	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	20.60	- -	08/2018	-	0/0
108	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	-	- -	08/2018	-	0/0
109	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	-	- -	08/2018	-	0/0

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
110	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	-	- -	10/2018	-	0/0
111	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	-	- -	11/2018	-	0/0
112	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	-	- -	11/2018	-	0/0
113	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	-	- -	11/2018	-	0/0
114	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	1,657.20	-	- -	01/2019	-	0/0
115	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	-	0/0
116	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	-	- -	01/2019	-	0/0
117	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	-	- -	03/2019	-	0/0
118	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	-	- -	03/2019	-	0/0
119	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	-	- -	03/2019	-	0/0
120	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	-	- -	04/2019	-	0/0
121	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	-	0/0
122	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
123	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
124	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	-	0/0
125	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
126	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	-	- -	05/2019	-	0/0

Details of Projects Without Original Date of Commissioning

(May 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
127	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	1,004.67	-	- -	05/2019	-	0/0
128	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
129	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	-	- -	07/2019	-	0/0
130	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	-	- -	07/2019	-	0/0
	Total		44,956.08 -	44,955.57	4,347.41				3/12
	<u>URBAN DEVELOPMENT</u>								
131	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	-	- 04/2019	04/2019	0(R3)	0/2
	Total		197.33 -	197.33	.00				0/2
	Grand Total		1,14,465.23	1,41,243.50	20,496.40				6/66

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 09/2017	09/2017	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-	0/0
	Total		959.68 -			0/0
	<u>COAL</u>					
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	06/2017 -	06/2017	0/0
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
7	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	03/2021 -	03/2021	0/0
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
9	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
10	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE	08/2016	319.76 -	03/2022 -	03/2022	0/0
11	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	458.07 -	03/2022 -	03/2022	0/0
	Total		20,476.06 -			0/0
	<u>FERTILISERS</u>					
12	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 09/2017	09/2017	0/0
	Total		197.79 -			0/0
	<u>STEEL</u>					
13	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 03/2016	03/2016	0/0
14	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	06/2017	0/0
16	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	06/2017	0/0
17	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 07/2017	07/2017	0/0
18	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
19	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2017	0/0
20	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
21	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 -	12/2017	0/0
22	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	03/2018	0/0
23	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	03/2018	0/0
24	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
25	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
26	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	07/2018 -	07/2018	0/0
27	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0
28	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	08/2018 -	08/2018	0/0
29	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 -	09/2018	0/0
30	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
31	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
32	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	06/2019 -	06/2019	0/0
33	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
34	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
	Total		15,603.72 -			0/0
	<u>PETROLEUM</u>					
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 06/2017	06/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
36	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KARNATAKA	01/2006	993.00 1,693.00	01/2012 -	06/2017	0/0
37	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	06/2017 06/2017	10/2017	0/0
38	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	07/2017 02/2018	02/2018	0/0
39	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	03/2018	0/0
40	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	01/2017 06/2017	03/2018	0/0
41	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 190.45	09/2017 03/2018	03/2018	0/0
42	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
43	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 05/2017	05/2018	0/0
44	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	06/2018 -	06/2018	0/0
45	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA	05/2015	337.06 -	08/2018 -	08/2018	0/0
46	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
47	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
48	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 11/2018	11/2018	0/0
49	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	11/2018 -	11/2018	0/0
50	ENNORE THIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	12/2018 -	12/2018	0/0
51	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA	05/2015	193.40 -	01/2019 -	01/2019	0/0
52	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 03/2019	03/2019	0/0
53	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	12/2017 03/2019	03/2019	0/0
54	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	03/2019 -	04/2019	0/0
55	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH	02/2016	151.00 -	09/2019 -	09/2019	0/0
56	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	10/2019 -	10/2019	0/0
57	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 05/2019	10/2019	0/0
58	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
59	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	11/2019 -	11/2019	0/0
60	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
61	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
62	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	02/2020 -	01/2020	0/0
63	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
64	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA	02/2016	554.00 -	02/2020 -	02/2020	0/0
65	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
66	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
67	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 -	06/2020	0/0
68	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR	09/2015	324.00 -	06/2020 -	06/2020	0/0
69	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	07/2020 -	07/2020	0/0
70	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	10/2020 -	10/2020	0/0
71	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
72	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	12/2020 -	12/2020	0/0
73	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
74	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR	05/2016	664.00 -	12/2020 -	12/2020	0/0
75	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
76	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
77	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
78	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
79	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	08/2021 -	08/2021	0/0
80	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND	12/2015	658.62 -	03/2023 -	03/2023	0/0
81	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
	Total		1,15,128.37 -			0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>POWER</u>					
82	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL, ODISHA	01/2016	187.04 -	06/2018 -	05/2017	0/0
83	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	09/2014 09/2017	09/2017	0/0
84	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
85	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 -	03/2017 10/2017	10/2017	0/0
86	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	10/2017	0/0
87	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
88	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 12/2017	12/2017	0/0
89	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 -	01/2018	0/0
90	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
91	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0
92	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL, TAMIL NADU	01/2016	162.11 -	05/2018 -	05/2018	0/0
93	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL, TRIPURA	05/2016	409.19 -	05/2018 -	05/2018	0/0
94	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL, MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
95	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
96	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL, GUJARAT	01/2016	244.19 -	07/2018 -	07/2018	0/0
97	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
98	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL, ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
99	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
100	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
101	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	10/2018 10/2018	10/2018	0/0
102	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
103	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
104	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
105	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
106	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
107	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
108	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
109	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
110	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
111	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
112	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
113	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
114	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
115	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE	10/2016	167.75 -	04/2019 -	04/2019	0/0
116	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
117	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
118	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
119	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
120	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
121	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
122	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
123	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
124	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
125	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
126	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
127	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
128	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
129	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
130	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	01/2023	0/0
131	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		73,632.48 -			0/0
	<u>HEAVY INDUSTRY</u>					
132	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
133	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	01/2016	0/0
134	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	07/2016	0/0
135	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
136	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 08/2019	08/2019	0/0
137	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0
138	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	Total		1,839.07 -			0/0
	<u>RAILWAYS</u>					
139	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2003	971.22 -	- -	12/2009	0/0
140	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011	0/0
141	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011	0/0
142	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 266.00	- -	12/2012	0/0
143	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	04/2014	0/0
144	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	08/2014	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
145	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	05/2015	0/0
146	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015	0/0
147	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
148	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 230.00	- 10/2015	10/2015	0/0
149	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 717.15	03/2012 01/2016	01/2016	0/0
150	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016	0/0
151	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
152	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	03/2016	0/0
153	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
155	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	03/2012 -	12/2016	0/0
156	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
157	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
158	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017	0/0
159	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	03/2017	0/0
160	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	03/2017	0/0
161	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2017	0/0
162	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
163	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
164	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
165	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 579.03	03/2017 -	03/2017	0/0
166	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,595.40	- -	05/2017	0/0
167	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
168	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	06/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
169	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 06/2017	06/2017	0/0
170	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2017	0/0
171	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	10/2017	0/0
172	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 843.45	02/2009 12/2017	12/2017	0/0
173	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	12/2017	0/0
174	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	12/2017	0/0
175	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
176	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
177	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
178	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2018	0/0
179	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
180	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
181	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
182	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
183	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	05/2018	0/0
184	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 855.16	- -	05/2018	0/0
185	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0
186	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
187	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 157.94	- -	11/2018	0/0
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2018	0/0
189	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
190	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 348.55	- -	02/2019	0/0
191	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 218.39	- -	02/2019	0/0
192	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	02/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
193	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 372.09	- 03/2019	03/2019	0/0
194	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
195	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,319.33	- 12/2009	03/2019	0/0
196	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
197	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	- -	03/2019	0/0
198	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
199	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2019	0/0
200	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 658.07	03/2014 03/2019	03/2019	0/0
201	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
202	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
203	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
204	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	03/2019	0/0
205	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
206	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 -	- -	03/2019	0/0
207	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 -	- -	03/2019	0/0
208	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	- -	03/2019	0/0
209	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
210	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
211	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
212	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
213	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
214	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI, RAJASTHAN	04/2012	471.82 -	03/2019 -	03/2019	0/0
215	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
216	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
217	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
218	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	- -	05/2019	0/0
219	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,160.54	03/1998 -	12/2019	0/0
220	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23	02/2015 -	12/2019	0/0
221	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 03/2020	03/2020	0/0
222	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER, JHARKHAND	04/1995	900.05 1,125.89	12/2011 03/2020	03/2020	0/0
223	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 4,454.18	03/2011 -	03/2020	0/0
224	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
225	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	- -	03/2020	0/0
226	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
227	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 2,393.48	04/2014 -	03/2020	0/0
228	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
229	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	03/2020	0/0
230	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
231	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
232	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
233	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
234	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	03/2020	0/0
235	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 -	- -	03/2020	0/0
236	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
237	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL, MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
238	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
239	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
240	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
241	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
242	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 12/2020	12/2020	0/0
243	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
244	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
245	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
246	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0
247	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
248	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 1,045.20	- -	03/2021	0/0
249	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 1,849.60	- 03/2021	03/2021	0/0
250	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
251	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 1,111.99	- 03/2020	03/2021	0/0
252	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 843.04	- 03/2021	03/2021	0/0
253	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	- 03/2021	03/2021	0/0
254	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR, ODISHA	04/2015	1,547.38 -	03/2021 -	03/2021	0/0
255	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 -	03/2021 -	03/2021	0/0
256	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 -	03/2021 -	03/2021	0/0
257	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR, ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
258	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR, ODISHA	04/2015	1,172.92 1,172.92	03/2021 03/2021	03/2021	0/0
259	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	- -	03/2021	0/0
260	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	- -	03/2021	0/0
261	SURENDRA NAGAR RAJKOT - [N22000392]WR, GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0
262	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER, JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
263	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	470.21 -	- 06/2021	06/2021	0/0
264	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL	01/1991	763.18 -	12/2021 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
265	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
266	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
267	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- 03/2022	03/2022	0/0
268	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
269	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	- 03/2021	06/2022	0/0
270	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
271	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 12/2022	12/2022	0/0
272	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
273	SECUNDERABAD-MAHABUNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
274	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
275	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
276	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
277	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
278	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
279	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- 12/2020	-	0/0
280	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
281	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
282	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 774.90	- -	-	0/0
283	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
284	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
285	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
286	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 458.26	07/2008 -	-	0/0
287	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
288	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
289	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	-	0/0
290	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
291	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 781.02	06/2007 -	-	0/0
292	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
293	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.08	02/2011 -	-	0/0
294	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 724.89	12/2012 12/2012	-	0/0
295	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
296	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
297	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
298	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
299	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
300	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
301	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	-	0/0
302	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
303	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
304	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	03/2012 -	-	0/0
305	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
306	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
307	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 155.56	12/2010 03/2017	-	0/0
308	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 334.87	12/2012 06/2016	-	0/0
309	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
310	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
311	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
312	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
313	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
314	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
315	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
316	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
317	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
318	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 335.53	- -	-	0/0
319	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
320	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0
321	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
322	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
323	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 633.87	- -	-	0/0
324	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
325	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
326	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 549.75	- -	-	0/0
327	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
328	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
329	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
330	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
331	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
332	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
333	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
334	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
335	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
336	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
337	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
338	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
339	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 268.52	- -	-	0/0
340	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
341	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 319.58	- -	-	0/0
342	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 290.85	- -	-	0/0
343	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 260.60	- -	-	0/0
344	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-	0/0
345	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 234.41	03/2015 -	-	0/0
346	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 238.36	- -	-	0/0
347	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 332.14	- 03/2019	-	0/0
348	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
349	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-	0/0
350	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 104.80	- -	-	0/0
351	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 198.88	- -	-	0/0
352	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- 03/2023	-	0/0
353	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
354	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
355	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
356	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 186.64	- -	-	0/0
357	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 173.91	- -	-	0/0
358	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 370.81	- -	-	0/0
359	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 131.47	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
360	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 79.39	- -	-	0/0
361	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 681.68	- -	-	0/0
362	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
363	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- 03/2022	-	0/0
364	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-	0/0
365	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
366	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
367	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
368	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
369	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
370	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 197.17	- -	-	0/0
371	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
372	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
373	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
374	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
375	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
376	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
377	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
378	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
379	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
380	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
381	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
382	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
383	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
384	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
385	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
386	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
387	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
388	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
389	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 259.23	- -	-	0/0
390	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 272.20	- -	-	0/0
391	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
392	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
393	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
394	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-	0/0
395	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 203.40	- -	-	0/0
396	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
397	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
398	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
399	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 1,072.52	- -	-	0/0
400	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
401	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- 03/2024	-	0/0
402	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- 03/2024	-	0/0
403	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-	0/0
404	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- 03/2022	-	0/0
405	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	- 03/2023	-	0/0
406	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	- 03/2023	-	0/0
407	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- 03/2023	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
408	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- 03/2022	-	0/0
409	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- 03/2022	-	0/0
410	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
411	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 3,631.00	- -	-	0/0
412	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
413	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
414	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
415	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	- -	-	0/0
416	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
417	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
418	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
419	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	-	0/0
420	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	- -	-	0/0
421	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
422	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
423	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
424	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
425	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
426	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-	0/0
427	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
428	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
429	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
430	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
431	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
432	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
433	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
434	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
435	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
436	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
437	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
438	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- 03/2021	-	0/0
439	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- 03/2019	-	0/0
440	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
441	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- 03/2017	-	0/0
442	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
443	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
444	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
445	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
446	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
447	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
	Total		3,19,156.24 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
448	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0
449	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
450	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
451	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
452	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
453	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
454	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
455	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
456	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014	0/0
457	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
458	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0
459	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
460	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
461	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015	0/0
462	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
463	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015	0/0
464	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
465	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0
466	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
467	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
468	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
469	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
470	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
471	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
472	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
473	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
474	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
475	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
476	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
477	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]NHDP, UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
478	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH, BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
479	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP, UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
480	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD, ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
481	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH, BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
482	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
483	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
484	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
485	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016	0/0
486	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH, BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0
487	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
488	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD, ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
489	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
490	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017	0/0
491	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	04/2010 09/2016	03/2017	0/0
492	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION KM 240 270 KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0
493	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
494	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD (NH-52B) (NEW NH NO.215) FROM KM 0.00 TO KM 68.30 IN THE STATE - [N24000373]PWD, UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
495	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
496	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
497	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH, ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
498	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH, ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017	0/0
499	WIDENING AND STRENGTHENING OF EXISTING SL. IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH, ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
500	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 06/2016	04/2017	0/0
501	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 12/2016	04/2017	0/0
502	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	04/2017	0/0
503	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	04/2017	0/0
504	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
505	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	04/2017	0/0
506	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	05/2017	0/0
507	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	05/2017	0/0
508	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	05/2017	0/0
509	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	05/2017	0/0
510	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	05/2017	0/0
511	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 10/2016	05/2017	0/0
512	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	05/2017	0/0
513	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
514	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	05/2017	0/0
515	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	05/2017	0/0
516	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	05/2017	0/0
517	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	05/2017	0/0
518	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	05/2017	0/0
519	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2017	0/0
520	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
521	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
522	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	05/2017	0/0
523	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	05/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
524	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	05/2017	0/0
525	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
526	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
527	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
528	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
529	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	05/2017	0/0
530	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	06/2017	0/0
531	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2017	0/0
532	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	06/2017	0/0
533	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	06/2017	0/0
534	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2017	0/0
535	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2017	0/0
536	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017	0/0
537	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	06/2017	0/0
538	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	06/2017	0/0
539	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	06/2017	0/0
540	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	06/2017	0/0
541	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	06/2017	0/0
542	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	06/2017	0/0
543	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	06/2017	0/0
544	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	06/2017	0/0
545	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2017	0/0
546	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	06/2017	0/0
547	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	06/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
548	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	06/2017	0/0
549	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2017	0/0
550	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	- -	06/2017	0/0
551	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
552	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017	0/0
553	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2017	0/0
554	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	07/2017	0/0
555	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
556	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
557	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	08/2017	0/0
558	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017	0/0
559	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2017	0/0
560	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
561	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	08/2017	0/0
562	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017	0/0
563	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017	0/0
564	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	09/2017	0/0
565	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	09/2017	0/0
566	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
567	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
568	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
569	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017	0/0
570	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
571	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
572	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
573	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017	0/0
574	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017	0/0
575	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
576	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017	0/0
577	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
578	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
579	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
580	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
581	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
582	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
583	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
584	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
585	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017	0/0
586	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
587	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
588	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017	0/0
589	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017	0/0
590	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2017	0/0
591	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
592	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
593	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
594	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017	0/0
595	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
596	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	08/2013 -	12/2017	0/0
597	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
598	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
599	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017	0/0
600	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
601	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	12/2017	0/0
602	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI, ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
603	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP, MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
604	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017	0/0
605	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI, PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
606	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
607	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017	0/0
608	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	12/2017	0/0
609	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH, KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
610	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
611	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
612	FOUR LANING OF KATHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
613	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
614	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0
615	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
616	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
617	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
618	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD, ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
619	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
620	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
621	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2018	0/0
622	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	03/2018	0/0
623	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
624	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
625	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
626	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
627	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
628	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
629	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
630	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
631	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
632	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
633	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
634	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
635	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	03/2018	0/0
636	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2018	0/0
637	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
638	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2018	0/0
639	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
640	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	04/2018	0/0
641	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- 04/2018	04/2018	0/0
642	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- 04/2018	04/2018	0/0
643	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	04/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
644	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
645	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 265.35	05/2018 -	05/2018	0/0
646	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	05/2018	0/0
647	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	- -	05/2018	0/0
648	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	05/2018	0/0
649	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	05/2018	0/0
650	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	- -	05/2018	0/0
651	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- 05/2018	05/2018	0/0
652	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
653	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	05/2018	0/0
654	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2018	0/0
655	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
656	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2018	0/0
657	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHAI,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
658	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
659	4-LANING OF GHAGHRA BRIDGE TO VARANASI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
660	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
661	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHAI,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
662	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
663	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
664	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
665	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
666	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	06/2018	0/0
667	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	- -	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
668	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
669	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
670	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
671	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
672	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
673	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0
674	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0
675	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
676	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
677	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
678	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
679	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
680	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
681	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
682	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
683	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
684	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
685	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0
686	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0
687	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
688	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
689	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	- -	03/2019	0/0
690	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
691	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
692	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
693	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	04/2019	0/0
694	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
695	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	05/2019	0/0
696	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
697	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	05/2019	0/0
698	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	05/2019	0/0
699	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
700	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
701	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
702	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
703	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN	06/2016	725.95 -	06/2019 -	06/2019	0/0
704	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
705	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	- -	07/2019	0/0
706	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	- -	07/2019	0/0
707	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
708	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
709	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
710	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
711	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	02/2020	0/0
712	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
713	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
714	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
715	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
716	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
717	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	03/2020	0/0
718	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	03/2020	0/0
719	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	03/2020	0/0
720	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
721	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
722	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
723	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
724	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
725	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
726	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
727	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2020	0/0
728	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
729	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
730	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
731	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
732	SIX LANING & STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) S - [N24000673]NHAI,KARNATAKA	03/2017	985.41 -	03/2020 -	03/2020	0/0
733	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	03/2020	0/0
734	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	03/2020	0/0
735	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
736	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
737	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
738	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	-	-	0/0
739	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
740	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
741	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
742	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
743	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
744	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
745	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
746	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
747	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
748	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
749	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
750	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
751	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
752	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
753	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
754	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
755	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
756	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
757	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
758	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
759	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
760	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
761	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
762	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
763	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
764	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
765	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
766	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
767	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
768	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
769	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
770	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
771	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
772	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
773	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
774	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
775	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
776	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
777	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
778	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
779	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
780	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
781	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
782	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
783	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
784	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
785	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
786	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
787	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
788	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
789	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
790	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
791	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
792	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
793	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
794	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
795	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
796	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
797	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
798	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
799	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
800	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
801	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
802	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-	0/0
803	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
804	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
805	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
806	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	-	0/0
807	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-	0/0
808	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-	0/0
809	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
810	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
811	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
812	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
813	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
814	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
815	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
816	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
817	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
818	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
819	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
820	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
821	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
822	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
823	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
824	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
825	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
826	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
827	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
828	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
829	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
830	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
831	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
832	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
833	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
834	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	-	0/0
835	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	-	0/0
836	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
837	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	-	0/0
838	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	-	0/0
839	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-	0/0
840	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
841	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
842	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHAI,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
843	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL - [N24000618]NHAI,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
844	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	-	0/0
845	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	- -	-	0/0
846	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
847	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	-	0/0
848	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
849	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
850	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
851	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
852	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	- -	-	0/0
853	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
854	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
855	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
856	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
857	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
858	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
859	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
860	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
861	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	- -	-	0/0
862	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
863	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
864	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
865	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
866	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
867	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
868	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
869	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
870	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
871	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
872	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
873	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
874	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
875	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
876	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
	Total		2,92,535.65 -			0/0
	<u>SHIPPING AND PORTS</u>					
877	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 03/2016	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
878	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL, TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
879	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	12/2010 12/2018	12/2018	0/0
880	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
881	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-	0/0
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
882	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI	06/2016	418.26 -	06/2017 -	06/2017	0/0
883	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 09/2017	09/2017	0/0
	Total		13,752.26 -			0/0
	<u>URBAN DEVELOPMENT</u>					
884	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
885	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
886	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	06/2017 -	06/2017	0/0
887	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	08/2017	0/0
888	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	12/2015 12/2016	09/2017	0/0
889	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 479.87	03/2015 03/2017	09/2017	0/0
890	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD, KERALA	07/2015	154.00 -	11/2015 -	11/2017	0/0
891	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 270.83	11/2014 05/2017	12/2017	0/0
892	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2018	0/0
893	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 03/2019	03/2019	0/0
894	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
895	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
896	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

			(May 2017)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
897	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	10/2019 -	03/2020	0/0
898	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-	0/0
899	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		1,16,828.96 -			0/0
	Grand Total		9,75,227.74			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(May 2017)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	WARDHA-HYDERABAD 765 KV LINK - [N18000183	1/2015	3,662.02 -	3,662.02	2,210.30	05/2018 -	12/2017
2	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186	3/2015	550.06 -	550.06	406.10	03/2018 -	12/2017
	Total		4,212.08 -	4,212.08	2,616.40		
	<u>COAL</u>						
3	BATURA HIGHWALL PROJECT - [N06000134	7/2015	231.92 -	231.92	-	03/2022 -	03/2020
	Total		231.92 -	231.92	.00		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	06/2018
	Total		667.00 -	667.00	.00		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS [N18000211	1/2016	187.04 -	187.04	54.60	06/2018 -	05/2017
	Total		187.04 -	187.04	54.60		
	<u>PETROLEUM</u>						
6	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216	1/2016	247.52 247.52	247.52	0.18	02/2019 -	12/2018
7	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226	2/2016	356.00 -	356.00	1.12	05/2019 -	12/2018
8	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	6/2016	423.00 -	423.00	-	08/2019 -	12/2018
9	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY [N16000263	2/2016	3,313.00 -	3,313.00	40.40	02/2020 -	01/2020
	Total		4,339.52 -	4,339.52	41.70		
	Grand Total		9,637.56	9,637.56	2,712.70		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	1/2009	309.46 -	553.53	484.76	01/2011 09/2017	09/2017
	Total		309.46 -	553.53	484.76		
	<u>COAL</u>						
2	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.59	72.61	03/2015 03/2020	03/2020
3	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	617.39	03/2012 03/2023	03/2023
4	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	43.65	03/2023 -	03/2023
5	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	209.13	03/2022 -	03/2022
6	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	188.63	06/2015 09/2019	09/2019
7	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
8	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.58	03/2021 -	03/2021
10	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	346.77	03/2020 -	03/2020
11	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	351.47	03/2021 -	03/2021
12	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	341.27	03/2018 -	03/2018
13	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	.78	03/2019 -	03/2019
14	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	661.64	03/2026 -	03/2026
15	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	20.35	03/2019 -	03/2019
16	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	104.02	03/2020 -	03/2020
17	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]	4/2012	364.75 -	364.75	197.05	10/2014 06/2017	06/2017
18	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	7.06	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	404.31	03/2018 -	03/2018
20	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,251.27	03/2023 03/2023	03/2023
21	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
22	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	24.78	03/2020 -	03/2020
23	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
24	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	222.50	03/2025 -	03/2025
25	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	70.75	03/2021 -	03/2021
26	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	58.98	03/2020 -	03/2020
27	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	16.34	03/2019 03/2019	03/2019
28	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	122.07	03/2019 -	03/2019
29	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	30.32	03/2019 -	03/2019
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	107.86	03/2021 -	03/2021
31	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
32	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	67.25	12/2019 -	12/2019
33	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
34	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	83.66	03/2019 -	03/2019
35	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	31.62	03/2021 -	03/2021
36	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.15	03/2021 -	03/2021
37	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	47.90	03/2018 -	03/2018
38	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
39	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	71.92	03/2023 -	03/2023
40	GOKUL - [N06000120]	11/2014	267.67 -	267.67	197.50	03/2018 -	03/2018
41	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	135.99	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
42	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	37.55	03/2021 -	03/2021
43	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
44	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	-	03/2022 -	03/2022
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	9.72	03/2022 -	03/2022
46	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	190.44	11/2021 -	11/2021
47	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	5/2016	687.28 -	687.28	.06	06/2017 -	06/2017
48	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	174.68	03/2020 -	03/2020
49	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	92.33	03/2016 03/2018	03/2018
50	KALYANIKHANI OPENCASE PROJECT - [N06000101]	7/2012	417.33 -	384.32	35.60	07/2016 03/2020	03/2020
51	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	437.51	224.01	03/2015 03/2021	03/2021
52	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,813.37	12/2015 04/2018	04/2018
53	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,326.67	03/2023 -	03/2023
54	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	172.13	03/2020 -	03/2020
55	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
56	MALACHUA OPENCASE PROJECT - [N06000139]	10/2015	488.33 -	488.33	.25	03/2023 -	03/2023
57	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	.15	03/2022 -	03/2022
58	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	268.54	03/2012 03/2018	03/2018
59	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	10.27	03/2015 03/2020	03/2020
60	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 03/2023	03/2023
	Total		75,275.73 -	75,145.66	11,596.35		
	DEFENCE PRODUCTION						
61	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	167.69	19.24	05/2018 -	05/2018
62	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	28.67	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		453.64 -	453.64	47.91		
	<u>FERTILISERS</u>						
63	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	72.73	11/2016 09/2017	09/2017
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	160.44	12/2017 -	12/2017
	Total		680.64 -	703.44	233.17		
	<u>HEALTH AND FAMILY WELFARE</u>						
65	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	174.00	03/2018 -	03/2018
66	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	80.00	08/2018 -	08/2018
67	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	41.00	09/2018 -	09/2018
68	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	-	05/2018 08/2019	08/2019
69	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	152.95	28.00	02/2018 -	02/2018
	Total		1,579.51 -	1,579.51	323.00		
	<u>MINES</u>						
70	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	.31	04/2021 04/2021	04/2021
71	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	157.34	01/2020 -	01/2020
	Total		6,074.00 -	6,074.00	157.65		
	<u>PETROLEUM</u>						
72	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	1,931.23	03/2013 03/2018	03/2018
73	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	24.96	04/2019 -	04/2019
74	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	-	06/2020 -	06/2020
75	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	-	12/2018 -	12/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	14.82	12/2020 -	12/2020
77	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	-	12/2020 -	12/2020
78	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	-	09/2019 -	09/2019
79	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	2.39	08/2021 -	08/2021
80	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	156.97	11/2018 -	11/2018
81	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	5.73	01/2019 -	01/2019
82	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
83	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
84	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	-	01/2021 -	01/2021
85	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	-	01/2021 -	01/2021
86	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	10.92	08/2018 -	08/2018
87	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	3.36	01/2019 -	01/2019
88	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	91.05	12/2019 -	12/2019
89	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	11.34	02/2020 -	02/2020
90	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	-	12/2019 -	12/2019
91	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	-	10/2020 -	10/2020
92	BSVI UPGRADEATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	-	12/2019 -	12/2019
93	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	33.30	03/2019 -	03/2019
94	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	658.62	-	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	114.51	03/2020 -	03/2020
96	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	1,879.00	16.42	09/2019 -	09/2019
97	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
98	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	6.97	04/2018 -	04/2018
99	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	107.72	03/2018 -	03/2018
100	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	273.08	12/2018 -	12/2018
101	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	760.33	08/2018 -	08/2018
102	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	-	06/2020 -	06/2020
103	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]	2/2016	931.00 -	931.00	237.72	07/2017 02/2018	02/2018
104	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	58.14	11/2019 -	11/2019
105	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	73.87	12/2017 -	12/2017
106	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	165.80	04/2018 -	04/2018
107	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	117.93	10/2018 -	10/2018
108	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	104.95	09/2017 03/2018	03/2018
109	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) [N16000217]	6/2012	150.00 -	259.93	141.18	07/2014 09/2017	09/2017
110	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	442.98	04/2018 04/2018	04/2018
111	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	3,961.54	3,019.16	12/2017 03/2019	03/2019
112	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	123.00	09/2018 09/2018	09/2018
113	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	136.00	02/2020 -	02/2020
114	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	435.00	304.20	03/2017 06/2017	06/2017
115	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 05/2020	05/2020

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
116	GAMJI REDEVELOPMENT PROJECT - [N16000202	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
117	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	5,296.93	3,466.38	04/2019 03/2019	03/2019
118	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00 -	690.00	-	07/2018 11/2019	11/2019
119	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195	2/2015	890.00 -	887.00	3.62	10/2019 -	10/2019
120	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 -	2,321.00	2.55	12/2020 -	12/2020
121	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	1,823.00	2.19	12/2020 -	12/2020
122	MH NORTH REDEVELOPMENT PHASE III - [N16000188	6/2014	5,706.47 -	5,813.25	5,359.34	05/2017 05/2018	05/2018
123	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187	4/2011	191.96 -	191.96	112.86	05/2015 06/2017	06/2017
124	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205	5/2015	1,714.00 -	1,417.00	981.91	06/2017 06/2017	06/2017
125	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179	3/2014	3,150.00 -	3,150.00	950.69	09/2017 12/2018	12/2018
126	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	3/2014	3,076.00 -	3,076.00	1,565.57	09/2017 06/2018	06/2018
127	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	5/2013	4,124.35 -	4,259.49	3,201.25	04/2016 12/2017	12/2017
128	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	99.05	10/2017 03/2019	03/2019
129	DIESEL HYDROTREATOR - [N16000207	7/2015	1,031.37 -	1,031.37	312.92	01/2018 -	01/2018
130	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	333.57	10/2014 03/2018	03/2018
131	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	1,330.00	523.10	06/2018 -	06/2018
132	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136	4/2012	600.17 -	600.17	3,466.38	12/2014 03/2018	03/2018
133	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	1,348.25	03/2015 03/2018	03/2018
134	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088	8/2009	1,793.00 -	1,793.00	1,387.47	12/2016 06/2017	06/2017
135	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	6/2010	202.94 -	222.19	2.00	01/2014 11/2019	11/2019
136	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072	7/2009	3,957.00 -	3,397.00	911.00	01/2013 12/2018	12/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
137	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	153.97	03/2017 10/2017	10/2017
138	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	439.03	85.59	03/2017 11/2018	11/2018
139	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	7.98	06/2020 -	06/2020
140	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	736.65	534.50	09/2011 06/2017	06/2017
141	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	104.65	07/2016 06/2018	06/2018
	Total		1,44,718.42 -	1,45,985.09	33,406.82		
	<u>POWER</u>						
142	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	641.09	09/2010 12/2017	12/2017
143	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	4,466.58	10/2012 02/2018	02/2018
144	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,119.84	04/2016 09/2017	09/2017
145	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	67.00	04/2016 12/2017	12/2017
146	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	551.80	04/2017 03/2018	03/2018
147	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	1,653.40	04/2018 -	04/2018
148	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	8.20	10/2018 10/2018	10/2018
149	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	10.50	05/2017 06/2019	06/2019
150	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	300.00	09/2017 -	09/2017
151	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	40.10	03/2018 -	03/2018
152	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	7/2010	1,272.80 -	1,731.10	1,391.53	11/2012 12/2017	12/2017
153	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI [N18000094]	7/2010	752.64 -	757.94	616.22	07/2013 06/2017	06/2017
154	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	262.00	09/2019 -	09/2019

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	-	06/2019 -	06/2019
156	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	-	04/2020 -	04/2020
157	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	-	09/2019 -	09/2019
158	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.60	12/2019 -	12/2019
159	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	-	06/2019 -	06/2019
160	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	-	03/2019 -	03/2019
161	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]	2/2017	322.30 -	322.30	.20	02/2019 -	02/2019
162	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
163	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	-	04/2019 -	04/2019
164	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	21.80	01/2019 -	01/2019
165	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	2.40	11/2019 -	11/2019
166	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	-	04/2019 -	04/2019
167	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
168	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]	11/2016	330.00 -	330.00	110.40	11/2017 -	11/2017
169	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	-	03/2019 -	03/2019
170	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.80	02/2019 -	02/2019
171	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	.40	02/2019 -	02/2019
172	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	14.60	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
173	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	1.10	07/2018 -	07/2018
174	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	7.50	12/2018 -	12/2018
175	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	76.50	01/2019 -	01/2019
176	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	1,681.43	10/2017 -	10/2017
177	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	21.70	11/2018 -	11/2018
178	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	51.70	04/2019 -	04/2019
179	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS [N18000222]	4/2016	790.13 -	790.13	164.50	06/2019 -	06/2019
180	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	-	06/2018 -	06/2018
181	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	170.10	12/2018 -	12/2018
182	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	499.30	11/2019 -	11/2019
183	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	248.90	05/2019 -	05/2019
184	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	.60	11/2018 -	11/2018
185	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	28.90	05/2018 -	05/2018
186	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	29.70	04/2018 -	04/2018
187	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	116.50	01/2018 -	01/2018
188	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	837.00	07/2020 -	07/2020
189	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	28.80	07/2018 -	07/2018
190	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	93.20	05/2018 -	05/2018
191	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	224.50	07/2018 -	07/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
192	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	71.90	07/2018 -	07/2018
193	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	102.60	03/2017 10/2017	10/2017
194	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	2,703.00	09/2019 -	09/2019
195	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	1,878.35	12/2015 12/2017	12/2017
196	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	703.10	549.20	06/2015 12/2017	12/2017
197	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	146.00	08/2017 -	08/2017
198	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	13,390.00	01/2017 07/2017	07/2017
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	704.52	11/2014 06/2017	06/2017
200	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,291.03	7,148.89	06/2015 06/2017	06/2017
201	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	129.33	09/2014 09/2017	09/2017
202	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,329.43	1,212.66	07/2006 09/2017	09/2017
203	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	13,201.00	01/2011 05/2018	05/2018
204	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,187.32	1,939.45	11/2008 09/2018	09/2018
205	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	1,882.93	08/2014 12/2017	12/2017
206	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	353.47	08/2014 12/2017	12/2017
207	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,399.06	08/2013 12/2017	12/2017
208	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	2,563.73	07/2014 09/2017	09/2017
209	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	481.82	06/2014 03/2018	03/2018
210	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	9/2011	1,940.13 -	2,702.65	2,312.86	09/2014 06/2017	06/2017
211	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	5,649.46	12/2009 01/2018	01/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
212	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	117.50	11/2017 -	11/2017
213	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	317.00	07/2018 -	07/2018
214	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	5,571.00	08/2018 -	08/2018
215	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	2,697.00	03/2019 -	03/2019
216	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	244.66	100.10	02/2016 06/2017	06/2017
217	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	376.09	195.40	02/2017 06/2017	06/2017
218	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	1,168.60	03/2018 -	03/2018
219	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,156.00	03/2013 06/2019	06/2019
220	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	206.42	121.70	03/2016 07/2017	07/2017
221	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	550.18	347.20	11/2016 11/2017	11/2017
222	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	145.40	07/2017 07/2017	07/2017
223	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	115.10	10/2017 -	10/2017
224	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	340.88	122.30	03/2018 -	03/2018
225	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	2,983.30	04/2018 -	04/2018
226	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	396.40	08/2016 10/2017	10/2017
227	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	969.97	648.20	06/2016 02/2018	02/2018
228	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	378.30	06/2016 02/2018	02/2018
229	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,547.20	08/2013 12/2017	12/2017
230	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	2/2010	2,144.00 -	2,932.88	2,517.90	12/2012 02/2018	02/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
231	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,639.00	7,508.00	09/2017 03/2018	03/2018
232	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	4/2010	4,404.57 -	5,135.01	3,289.85	01/2015 03/2018	03/2018
	Total		2,05,843.45 -	2,27,386.43	1,17,854.07		
	<u>RAILWAYS</u>						
233	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	470.92 727.13	2,713.09	632.05	- 03/2021	03/2021
234	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	74.22	03/2019 -	03/2019
235	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	186.13	03/2019 -	03/2019
236	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	135.51	03/2018 -	03/2018
237	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	323.91	03/2018 -	03/2018
238	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	19.91	03/2019 -	03/2019
239	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	212.71	03/2019 -	03/2019
240	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	376.00	03/2018 -	03/2018
241	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
242	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	289.76	03/2019 -	03/2019
243	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	222.83	03/2019 -	03/2019
244	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	-	12/2024 -	12/2024
245	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
246	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.93	12/2021 -	12/2021
247	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	478.32	12/2021 -	12/2021
248	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	100.00	03/2021 -	03/2021
249	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	12.00	03/2020 -	03/2020
250	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	.14	- 03/2021	03/2021

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
251	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
252	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
253	RAMNA - SINGRAULI DOUBLING - [N22000417	8/2015	2,436.21 -	2,436.21	22.62	03/2020 -	03/2020
254	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	8/2016	582.13 -	582.13	-	03/2020 03/2020	03/2020
255	KATNI-BINA 3RD LINE (263 KM) - [N22000415	6/2016	2,478.23 -	2,478.23	-	03/2022 03/2022	03/2022
256	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.65 -	1,485.65	329.46	12/2020 -	12/2020
257	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,183.25	357.50	12/2020 -	12/2020
258	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	942.95	621.66	03/2019 -	03/2019
259	RAIPUR - TITLAGARH - DOUBLING - [N22000411	3/2007	758.09 -	758.09	432.25	03/2020 -	03/2020
260	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	960.18 -	960.18	410.44	03/2020 -	03/2020
261	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	1,514.45 -	1,514.45	839.11	03/2020 -	03/2020
262	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	.14	12/2025 -	12/2025
263	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	4/2011	4,295.30 -	4,295.30	46.32	12/2026 -	12/2026
264	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
265	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	-	03/2021 03/2021	03/2021
266	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61 -	701.61	-	03/2021 -	03/2021
267	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379	4/2015	2,361.74 -	2,361.74	-	03/2021 -	03/2021
268	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	2,499.71	-	03/2021 -	03/2021
269	JAGDALPUR-KORAPUT DOUBLING - [N22000376	4/2015	1,547.38 -	1,547.38	-	03/2021 -	03/2021
270	AMRAVATI-NARKHER NL(CR) - [220100118	6/1994	663.01 175.30	858.23	688.04	06/1999 12/2020	12/2020
271	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,160.83	268.41	- 03/2020	03/2020
272	BHADRAK - NERGUNDI 3RD LINE - [N22000316	3/2013	858.67 -	843.04	4.30	- 03/2021	03/2021

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
273	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	4/1997	218.24 236.41	525.00	544.20	- 03/2019	03/2019
274	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	3/1996	155.74 164.36	966.98	874.72	02/2009 12/2017	12/2017
275	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	3/1996	495.44 -	1,781.98	514.44	03/2004 03/2020	03/2020
276	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	4/1995	900.05 -	1,125.89	980.99	12/2011 03/2020	03/2020
277	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	9/1998	247.66 -	6,093.31	972.82	05/2008 03/2023	03/2023
278	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00 -	7,986.04	2,423.55	03/2014 03/2019	03/2019
279	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	4/1994	470.21 -	3,004.90	572.56	- 06/2021	06/2021
280	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) [N22000113	4/2008	653.19 -	941.04	575.19	03/2014 03/2019	03/2019
281	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
282	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
283	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
284	KIUL - GAYA DOUBLING PROJECT - [N22000349	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
285	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,750.00 -	1,295.42	16.40	03/2022 -	03/2022
286	AGARTALA-AKHAURA NL - [N22000195	4/2012	252.00 -	580.00	-	- 07/2019	07/2019
287	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	10.34	02/2019 12/2022	12/2022
288	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04 -	1,640.04	331.91	- 03/2022	03/2022
289	HAJIPUR - BACHAWARA - [N22000334	5/2015	720.00 -	678.54	-	- 12/2018	12/2018
290	JAGGAYYAPET - MELLACHERUVU - [N22000304	4/2007	313.24 -	554.70	342.00	01/1999 06/2017	06/2017
	Total		67,233.20 -	87,460.46	15,595.95		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
291	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
292	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	57.42	07/2017 -	07/2017
293	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
294	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
295	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
296	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
297	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	3,237.87	2,948.41	09/2012 12/2017	12/2017
298	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
299	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	55.00	04/2018 -	04/2018
300	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
301	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
302	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
303	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
304	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
305	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
306	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
307	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
308	SIX LANEING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
309	SIX LANEING & STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) S - [N24000673	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
310	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
311	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
312	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
313	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
314	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
315	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
316	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
317	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
318	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
319	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
320	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
321	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
322	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	-	03/2020 -	03/2020
323	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
324	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
325	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
326	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
327	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
328	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
329	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
330	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
331	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642	3/2015	226.31 226.00	226.00	-	10/2017 -	10/2017
332	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	-	10/2017 -	10/2017
333	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
334	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
335	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
336	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
337	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
338	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	1,200.90	01/2018 -	01/2018
339	FOUR LANING OF SARAGAON - BILASPUR - [N24000502	12/2015	509.13 -	509.13	-	- 04/2018	04/2018
340	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	26.00	07/2018 -	07/2018
341	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
342	FOUR LANING OF SIMGA - SARAGAON - [N24000495	12/2015	596.67 -	596.67	-	- 05/2018	05/2018
343	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
344	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
345	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
346	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
347	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
348	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
349	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510	12/2015	726.67 -	726.67	-	- 04/2018	04/2018
350	FOUR LANING OF PARWANOO - SOLAN - [N24000479	9/2015	934.46 -	934.46	57.43	03/2018 -	03/2018
351	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
352	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
353	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	142.73	05/2017 -	05/2017
354	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
355	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
356	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
357	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
358	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
359	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
360	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
361	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
362	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
363	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
364	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]	6/2015	532.49 -	532.49	137.08	05/2017 -	05/2017
365	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	54.50	07/2017 -	07/2017
366	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	40.75	02/2018 -	02/2018
367	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	114.38	11/2017 -	11/2017
368	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	235.85	02/2018 -	02/2018
369	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	114.87	09/2017 -	09/2017
370	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	19.24	09/2017 -	09/2017
371	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	30.08	02/2018 -	02/2018
372	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017
373	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017
374	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
375	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
376	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	29.27	10/2017 -	10/2017
377	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
378	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	-	12/2017 -	12/2017

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
379	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
380	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
381	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	31.17	05/2017 -	05/2017
382	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	62.77	05/2017 -	05/2017
383	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
384	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
385	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
386	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
387	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
388	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
389	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
	Total		65,869.93 -	69,582.30	6,017.69		
	<u>SHIPPING AND PORTS</u>						
390	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	235.15	98.60	06/2017 -	06/2017
391	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	1/2007	366.39 -	669.46	411.12	12/2010 12/2018	12/2018
392	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
393	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017
	Total		1,019.83 -	1,372.94	509.86		

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
394	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	141.28	12/2016 07/2017	07/2017
395	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	27.42	03/2018 -	03/2018
396	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
397	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
398	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	12,136.78	05/2015 12/2017	12/2017
399	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	309.85	04/2018 -	04/2018
400	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]	7/2015	465.85 -	465.85	-	07/2018 -	07/2018
401	CENTRAL DISPATCH YARD - [N12000119]	8/2015	320.66 -	320.66	-	08/2018 -	08/2018
402	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	-	06/2019 -	06/2019
403	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,500.00	427.35	12/2017 -	12/2017
404	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	40.47	09/2018 -	09/2018
405	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	25.34	06/2020 -	06/2020
406	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	13.64	09/2017 -	09/2017
	Total		30,610.21 -	30,283.43	13,342.19		
	<u>TELECOMMUNICATIONS</u>						
407	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	2,060.00	07/2015 09/2017	09/2017
408	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]	6/2016	418.26 -	418.26	-	06/2017 -	06/2017
	Total		13,752.26 -	13,752.26	2,060.00		
	<u>URBAN DEVELOPMENT</u>						
409	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	197.33	-	- 04/2019	04/2019

List of Projects on schedule w.r.t. Latest Schedule

(May 2017)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
410	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	2/2016	496.18 496.00	496.18	-	06/2017 -	06/2017
411	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	-	03/2020 -	03/2020
412	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
413	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	12/2016	164.00 -	164.00	24.22	01/2018 -	01/2018
414	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]	9/2012	171.86 -	171.86	1.31	03/2016 02/2018	02/2018
415	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	2/2011	241.33 -	349.33	196.00	03/2016 12/2017	12/2017
416	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,479.76	11/2019 -	11/2019
417	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 03/2019	03/2019
418	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]	5/2012	405.01 -	405.01	219.34	12/2014 06/2017	06/2017
419	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	219.38	05/2017 08/2017	08/2017
	Total		17,235.55 -	17,197.55	5,676.78		
	Grand Total		6,30,655.83	6,77,530.24	2,07,306.20		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	03/2017	70.54
	Total		16,663.00 -	28,462.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2017	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
5	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	03/2015 -	03/2020	.00
6	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		17,909.74 -	17,966.36			
	<u>HEALTH AND FAMILY WELFARE</u>						
8	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK [N21000005]	11/2013	196.70 -	209.00	01/2016 -	01/2016	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53
11	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
12	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	05/2017	37.72
13	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
14	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	09/2016	407.00 -	1,879.00	09/2019 -	09/2019	361.67
15	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	Total		6,716.82 -	8,853.69			
	<u>POWER</u>						
16	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
18	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	11,639.00	09/2017 -	03/2018	.00
19	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49	02/2016 -	-	.16
20	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	06/2017	5.45
21	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96
22	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	5.50
23	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	4.12
24	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37
25	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	01/2018	58.79
26	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,352.57	09/2017 -	09/2018	31.55

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		34,977.76	60,694.08			
			-				
	<u>RAILWAYS</u>						
27	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	131.09
28	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	614.00	- -	-	123.75
29	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	-	141.40
30	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	870.00	- -	-	459.31
31	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
32	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	1,542.41	- 05/2009	-	317.21
33	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
34	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
35	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
36	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	350.00	02/2011 -	-	277.85
37	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
38	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	01/2016	210.19
39	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
40	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	2,713.09	- -	03/2021	273.12
41	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	413.56	- -	10/2017	89.54
42	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34
43	HATHUA-BHATNI (N L) (NER) - [220100319	04/2005	230.03 -	718.54	- -	05/2019	212.37
44	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
45	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
46	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	02/2017	64.25

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
47	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
48	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51
49	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
50	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
51	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
53	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
54	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	03/2019	44.07
55	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
56	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	03/2016	123.34
57	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	-	534.55
58	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
59	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
60	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR- MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	153.02	- -	-	-48.56
61	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON- PORAMAHESHTALA AND CHA - [N22000242]	04/2003	337.96 -	186.89	- -	-	-44.70
62	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	03/2017	70.09
63	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	-	286.26
64	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
65	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
66	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
67	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
68	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	-	-	117.77
69	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	-	-	183.41
70	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	-	57.65
71	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	-	-	47.93
72	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	-	-	76.69
73	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	-	-	2.29
74	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	-	-	134.68
75	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	-	-	57.68
76	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	-	-	369.31
77	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	-	-	14.14
78	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
79	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
80	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
81	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33
82	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
83	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
84	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
85	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
86	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64
87	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
88	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
89	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
90	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
91	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	-	03/2019	290.00
92	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,145.00	-	03/2020	615.00
93	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	293.74 -	229.33	12/2010 -	-	-21.93
94	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
95	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
96	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58
97	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
98	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	-	27.24
99	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
100	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,679.13	- -	05/2017	58.06
101	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
102	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	780.98	- -	-	90.45
103	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114]	04/2008	516.23 -	735.00	03/2014 -	-	42.38
104	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
105	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
106	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
107	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62
108	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78	12/2012 -	-	107.82
109	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	370.00	02/2009 02/2009	02/2017	122.68
110	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
111	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
112	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	-	03/2019	122.07
113	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
114	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
115	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
116	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
117	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	-	72.62
118	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
119	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	712.82	- -	-	612.82
120	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
121	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
122	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	- -	03/2020	52.77
123	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
124	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
125	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322	04/2011	190.10 -	355.96	- -	03/2019	87.25
126	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	-	40.49
127	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324	04/2010	203.40 -	273.84	- -	-	34.63
128	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	648.00	- -	02/2019	8.00
129	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	04/2008	829.74 -	1,161.64	03/2015 -	03/2019	40.00
130	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	1,010.00	- -	03/2017	711.70
131	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	858.23	06/1999 -	12/2020	389.58
132	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
133	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	308.00	- -	-	.33
134	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	268.78	- -	08/2017	10.26

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
135	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	-	05/2018	61.80
136	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
137	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	-	03/2020	72.01
138	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	-	12/2020	71.11
139	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	-	-	92.25
140	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	-	03/2019	24.63
141	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	-	03/2019	132.54
142	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	-	-	27.06
143	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	-	-	23.02
144	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020	12/2022	226.98
145	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	-	-	16.87
146	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	-	03/2017	17.92
147	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]	04/2011	239.73 -	257.78	-	-	7.53
148	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	-	02/2019	27.93
149	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	-	-	27.72
150	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	-	03/2019	21.31
151	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019	12/2022	226.23
152	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	-	-	62.32
153	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	-	-	82.25
154	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	-	-	162.39
155	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015	12/2016	53.44
156	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013	12/2016	37.41

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
157	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
158	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
159	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
160	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
161	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
162	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
163	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
164	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
165	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
166	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
167	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
168	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
169	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	03/2016	107.49
170	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	445.00	- -	03/2018	112.14
171	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	330.00	- -	03/2018	16.38
172	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
173	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
174	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
175	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
176	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
177	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2019	171.38
178	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
179	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	508.00	-	03/2019	62.76
180	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	-	03/2019	62.12
181	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
182	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
183	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]	04/2010	174.56 -	160.97	- -	-	-7.79
184	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	-	10.94
185	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	-	21.21
186	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
187	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	05/2015	5.12
188	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01
189	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
190	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
191	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60	12/2024 -	12/2024	25.72
192	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	Total		85,938.78 -	2,19,383.45			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
193	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2017	28.93
194	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	05/2017	92.75
195	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	05/2017	80.68
196	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	05/2017	68.99
197	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
198	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
199	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
200	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
201	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
202	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
203	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
204	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	.12
205	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	.01
206	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
207	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
208	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
209	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
210	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
211	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
212	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
213	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
214	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
215	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
216	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
217	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
218	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
219	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
220	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
221	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
222	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
223	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
	Total		22,559.74 -	29,097.60			
	<u>SHIPPING AND PORTS</u>						
224	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
225	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20
226	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	.13
227	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
	Total		839.11 -	1,503.31			
	<u>STEEL</u>						
228	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	03/2016	3.96
229	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39
230	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	06/2017	1.70
	Total		1,261.61 -	1,777.68			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(May 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	URBAN DEVELOPMENT						
231	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	496.18	06/2017 -	06/2017	.04
	Total		496.18 -	496.18			
	Grand Total		1,89,901.51	3,73,265.51			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

(May 2017)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,000.00	5,429.43	09/2010 09/2016	10/2017	85	13
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	9,980.00	12/2015 11/2016	11/2019	47	36
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	7,688.00	12/2016 03/2017	12/2020	48	45
	Total		27,271.00 -	29,779.00	23,097.43				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	24.13	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	24.13				
	<u>COAL</u>								
5	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	145.88	05/2014 -	10/2017	41	-
6	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	134.69	04/2014 -	10/2017	42	-
7	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	119.45	03/2014 -	12/2017	45	-
8	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	96.89	03/2015 -	03/2018	36	-
9	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72	-
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	199.20	03/2014 -	03/2018	48	-
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	199.20	03/2016 -	03/2018	24	-
12	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	204.04	03/2013 -	03/2018	60	-
13	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	334.92	03/2016 -	03/2018	24	-
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	143.44	03/2016 -	03/2018	24	-
15	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	57.64	06/2015 -	03/2018	33	-
16	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	223.57	03/2017 -	05/2018	14	-
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	297.66	03/2018 -	09/2018	6	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
19	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	126.88	03/2012 -	03/2019	84	-
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 518.04	518.04	190.31	03/2010 -	03/2019	108	-
21	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	203.73	03/2013 -	03/2019	72	-
22	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84	-
23	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.14	03/2012 -	03/2019	84	-
24	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	80.62	03/2014 -	03/2019	60	-
25	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
26	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	166.63	04/2015 -	04/2019	48	-
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.00	03/2014 -	03/2020	72	-
28	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	92.97	03/2011 -	03/2020	108	-
29	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2020	60	-
30	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	116.58	07/2012 03/2017	03/2021	104	48
	Total		9,230.40 -	9,576.36	3,579.65				
	<u>STEEL</u>								
31	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	394.74	07/2015 -	05/2017	22	-
32	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,905.00	03/2013 -	06/2017	51	-
33	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	728.59	07/2015 -	06/2017	23	-
34	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	140.55	09/2016 -	06/2017	9	-
35	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	178.65	12/2015 -	06/2017	18	-
36	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	324.87	262.93	12/2015 -	06/2017	18	-
37	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	478.53	07/2016 -	07/2017	12	-
38	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	115.64	05/2016 -	10/2017	17	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
39	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	-
40	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	190.50	10/2016 -	03/2018	17	-
41	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	-
42	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	78.00	12/2017 -	05/2018	5	-
43	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	53.68	10/2017 -	07/2018	9	-
44	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-
45	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
46	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
47	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	Total		25,593.26 -	25,789.26	19,864.39				
	PETROLEUM								
48	RESID UPGRADE PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	1,687.77	11/2015 01/2017	05/2017	18	4
49	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	4.16	04/2017 -	05/2017	1	-
50	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	887.00	03/2015 -	05/2017	26	-
51	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 1,693.00	1,693.00	1,537.45	01/2012 -	06/2017	65	-
52	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,079.94	05/2013 05/2017	10/2017	53	5
53	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	215.38	128.25	06/2017 06/2017	10/2017	4	4
54	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	35.76	11/2016 -	02/2018	15	-
55	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	144.01	12/2016 -	03/2018	15	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
56	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02 -	173.28	119.72	01/2017 06/2017	03/2018	14	9
57	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,890.18	05/2014 12/2017	05/2018	48	5
58	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2017	05/2018	12	12
59	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 -	390.52	213.51	03/2019 -	04/2019	1	-
60	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	4,701.44	1,960.89	05/2019 05/2019	10/2019	5	5
	Total		19,055.22 -	18,265.47	10,926.07				
	<u>POWER</u>								
61	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL, MULTI STATE	02/2010	232.34 -	245.00	237.49	06/2012 -	06/2017	60	-
62	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL, MULTI STATE	09/2013	1,575.30 1,656.15	1,656.15	1,296.40	05/2016 05/2017	06/2017	13	1
63	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,580.00	09/2011 06/2017	12/2017	75	6
64	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR	05/2015	436.68 -	602.44	465.36	12/2016 -	12/2017	12	-
65	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04 -	5,783.17	4,892.47	01/2016 -	01/2018	24	-
66	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 -	195.42	116.41	02/2014 -	02/2018	48	-
67	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 7,998.00	5,353.00	5,472.83	05/2014 03/2017	03/2018	46	12
68	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	5,079.75	12/2016 -	03/2018	15	-
69	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18 -	9,395.18	7,620.00	11/2016 12/2017	04/2018	17	4
70	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,103.00	06/2017 12/2017	04/2018	10	4
71	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 -	12,964.60	6,002.44	01/2018 -	06/2018	5	-
72	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	2,352.57	945.96	09/2017 -	09/2018	12	-
73	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,275.55	09/2009 -	12/2018	111	-
74	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,182.02	06/2013 -	12/2019	78	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
75	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	260.20	12/2018 -	12/2019	12	-
76	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	246.00	12/2018 -	12/2019	12	-
77	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	4,911.00	02/2019 02/2020	02/2021	24	12
78	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	139.96	04/2020 -	01/2023	33	-
	Total		1,00,310.83 -	1,10,128.38	59,826.84				
	<u>HEAVY INDUSTRY</u>								
79	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	3,827.30	2289.00	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	2289.00				
	<u>HEALTH AND FAMILY WELFARE</u>								
80	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	168.90	68.00	05/2017 07/2017	10/2017	5	3
81	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	127.00	05/2017 -	12/2017	7	-
82	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	184.70	05/2017 -	12/2017	7	-
	Total		666.99 -	666.99	379.70				
	<u>RAILWAYS</u>								
83	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	913.84	03/2010 -	06/2017	87	-
84	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	370.69	03/2010 -	12/2017	93	-
85	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	-
86	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	150.22	03/2016 -	12/2017	21	-
87	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	386.03	06/2013 -	03/2018	57	-
88	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,000.00	4,090.26	04/2008 12/2011	06/2018	122	78

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
89	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
90	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	13,536.97	11/2002 -	12/2018	193	-
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	631.67	03/2016 -	12/2018	33	-
92	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,010.00	2,225.72	12/2008 -	03/2019	123	-
93	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,319.33	1,319.33	757.23	- 12/2009	03/2019	-	111
94	HARIDASPUR-PARADEEP (NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	620.08	- 09/2009	03/2019	-	114
95	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,161.64	353.32	03/2015 -	03/2019	48	-
96	BHUJ-NALIYA (GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	-
97	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	-
98	GONDIA-JABALPUR (GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,160.54	1,776.81	967.96	03/1998 -	12/2019	261	-
99	SUKINDA ROAD - ANGUL (NL) (ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.70	199.98	02/2015 -	12/2019	58	-
100	GOELKERA-MANOHARPUR, (LD) (SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	318.00	258.17	02/2006 -	12/2019	166	-
101	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 4,454.18	9,658.00	4,927.46	03/2011 -	03/2020	108	-
102	OBULAVARIPALLE-KRISHNAPATNAM (RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,825.00	831.39	03/2008 06/2008	03/2020	144	141
103	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	3,451.00	1,569.30	03/2014 -	03/2020	72	-
104	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 2,393.48	4,600.00	549.89	04/2014 -	03/2020	71	-
105	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
106	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-
107	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	3,000.00	147.52	03/2015 -	03/2020	60	-
108	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	266.97	- 11/2015	03/2020	-	52
109	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	933.09	03/2016 -	12/2020	57	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
110	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	1,579.27	168.29	- 03/2020	03/2021	-	12
111	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	247.50	- 03/2021	06/2022	-	15
112	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
	Total		33,114.54 -	85,148.01	39,011.10				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
113	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	410.32	02/2009 -	05/2017	99	-
114	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	209.80	04/2009 -	05/2017	97	-
115	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	268.94	11/2008 -	05/2017	102	-
116	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	195.35	11/2008 -	05/2017	102	-
117	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	245.83	04/2009 -	05/2017	97	-
118	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	05/2017	110	7
119	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	340.12	07/2009 -	05/2017	94	-
120	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	168.31	02/2010 -	05/2017	87	-
121	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	-
122	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	05/2017	23	-
123	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	05/2017	46	-
124	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	05/2017	42	-
125	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	05/2017	39	-
126	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	541.42	09/2013 -	05/2017	44	-
127	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,354.75	09/2014 -	05/2017	32	-
128	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
129	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	401.11	200.96	01/2017 -	05/2017	4	-
130	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	503.16	211.03	08/2016 -	05/2017	9	-
131	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	103.08	11/2016 -	05/2017	6	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
132	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	297.81	04/2008 01/2017	06/2017	110	5
133	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	885.43	03/2013 -	06/2017	51	-
134	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,708.35	05/2013 -	06/2017	49	-
135	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	06/2017	48	-
136	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	964.46	07/2013 -	06/2017	47	-
137	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	671.62	01/2014 -	06/2017	41	-
138	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,620.72	05/2014 -	06/2017	37	-
139	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	494.33	04/2014 -	06/2017	38	-
140	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	869.91	08/2013 -	06/2017	46	-
141	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	06/2017	33	-
142	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,004.42	08/2013 -	06/2017	46	-
143	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	06/2017	36	-
144	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	06/2017	41	-
145	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	160.49	01/2016 -	06/2017	17	-
146	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	239.48	01/2016 -	06/2017	17	-
147	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	234.21	08/2016 -	06/2017	10	-
148	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2017	1	-
149	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	13	-
150	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	469.54	05/2013 -	07/2017	50	-
151	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,566.61	07/2015 -	07/2017	24	-
152	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,508.05	12/2015 -	07/2017	19	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
153	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	834.00	09/2016 -	07/2017	10	-
154	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,708.29	11/2011 -	08/2017	69	-
155	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	08/2017	48	-
156	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 TO 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	-
157	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	785.00	08/2016 -	08/2017	12	-
158	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	7	-
159	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	09/2017	73	-
160	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,206.00	04/2013 -	09/2017	53	-
161	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2017	42	-
162	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	09/2017	38	-
163	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	345.22	06/2014 -	09/2017	39	-
164	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,328.50	02/2014 -	09/2017	43	-
165	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	217.87	09/2016 -	09/2017	12	-
166	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	70.23	09/2016 -	09/2017	12	-
167	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	09/2017	22	-
168	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,036.26	07/2013 -	10/2017	51	-
169	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	10/2017	53	-
170	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25	-
171	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	870.15	09/2014 -	10/2017	37	-
172	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
173	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,077.66	03/2013 -	11/2017	56	-
174	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	-
175	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	-
176	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	297.35	11/2016 -	11/2017	12	-
177	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,486.59	08/2014 -	12/2017	40	-
178	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,788.25	03/2013 -	12/2017	57	-
179	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.34	12/2013 -	12/2017	48	-
180	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	236.00	05/2013 -	12/2017	55	-
181	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	303.07	08/2013 -	12/2017	52	-
182	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	-
183	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	545.27	11/2013 -	12/2017	49	-
184	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,216.15	06/2014 -	12/2017	42	-
185	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	580.43	226.67	08/2013 -	12/2017	52	-
186	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	277.41	10/2013 -	12/2017	50	-
187	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00	498.11	06/2015 -	12/2017	30	-
188	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	1,607.34	04/2015 -	12/2017	32	-
189	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
190	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	77.49	01/2016 -	12/2017	23	-
191	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	2,816.74	10/2011 -	12/2017	74	-
192	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	957.02	07/2017 -	01/2018	6	-
193	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,288.43	11/2016 -	02/2018	15	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
194	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	604.61	07/2013 -	03/2018	56	-
195	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,674.82	08/2013 -	03/2018	55	-
196	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,041.03	06/2012 -	03/2018	69	-
197	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
198	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	574.74	03/2014 -	04/2018	49	-
199	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	-
200	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	880.29	02/2013 -	06/2018	64	-
201	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	11.37	12/2017 -	06/2018	6	-
202	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
203	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
204	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
205	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	-
206	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	-
207	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
208	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
209	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
210	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	Total		80,754.18 -	83,060.71	82,237.03				

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>SHIPPING AND PORTS</u>								
211	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 03/2016	12/2017	141	21
	Total		150.00 -	600.00	139.80				
	<u>URBAN DEVELOPMENT</u>								
212	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	72.96	03/2017 -	06/2017	3	-
213	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	216.89	09/2016 01/2017	08/2017	11	7
214	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	277.92	06/2015 08/2016	08/2017	26	12
215	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	153.40	12/2015 12/2016	09/2017	21	9
216	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	281.57	03/2015 03/2017	09/2017	30	6
217	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	49.82	11/2015 -	11/2017	24	-
218	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	270.83	75.52	11/2014 05/2017	12/2017	37	7
219	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 170.62	170.62	127.15	03/2012 08/2016	12/2017	69	16
220	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	12,472.32	12/2015 -	12/2017	24	-
221	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	98.07	08/2016 03/2017	03/2018	19	12
222	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	11
223	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 06/2017	06/2018	39	12
224	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
225	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21	-
226	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-

List of Delayed Projects w.r.t. Latest Schedule

(May 2017)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
227	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	10.53	10/2019 -	03/2020	5	-
	Total		58,598.91 -	58,694.38	17,994.33				
	Grand Total		3,56,777.94	4,25,977.19	2,59,369.47				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2019	11459	47
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	33
9	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	60
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
11	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
12	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
13	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	10/2017	269.82	42
14	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24
15	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
16	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
17	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72
18	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	36
19	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
20	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
22	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
23	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2018	210.98	60
24	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
25	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
26	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
27	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	84
28	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	12/2017	153.82	45
29	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	60
30	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.4	72
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
37	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	72
38	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
39	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	09/2018	1055.05	6
40	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	06/2017	364.75	32
41	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2017	289.45	41

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
42	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2017	197.79	10

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
44	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	12/2017	293.65	7
45	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	12/2017	204.44	7

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931	7
48	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	09/2017	150	38
49	NEW 250 TMTPL LPG PLANT AT PANAGARH	HPCL	08/2014	09/2017	03/2018	190.45	6
50	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	41
51	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	05/2017	871.35	26
52	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
53	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2017	736.65	69
54	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	11/2018	352.56	20
55	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	03/2018	228.64	15
56	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	11/2019	690	16
57	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	02/2018	257.87	15
58	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	IOCL	03/2014	03/2017	10/2017	238.5	7
59	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
61	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
62	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
63	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	10/2017	861.79	53
64	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	12/2016	06/2017	1793	6
65	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
66	SIX PIPELINE REPLACEMENT PROJECT	ONGC	03/2009	01/2017	03/2018	181.02	14
67	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2018	2465.15	60
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRIL	01/2006	01/2012	06/2017	993	65
69	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
70	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
71	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
72	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
73	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	05/2017	3110.36	18
74	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	06/2017	191.96	25
75	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12
76	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
77	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2018	2592.17	48
78	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
80	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
81	COMMON SYS. ASSOCIATED WITH EAST	PGCIL	03/2013	12/2015	12/2017	2514.88	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B						
82	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	04/2018	11846	10
83	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	09/2017	198.63	36
84	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	38
85	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	03/2018	11638.55	6
86	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
87	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144	62
88	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II	PGCIL	09/2013	05/2016	06/2017	1575.3	13
89	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2018	487.49	45
90	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	09/2017	2127.51	38
91	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	12/2017	573.99	52
92	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	40
93	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	40
94	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	01/2018	3642.04	24
95	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118
96	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
97	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	09/2017	368.72	134
98	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	03/2018	9750.89	15
99	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
100	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	09/2017	1364.52	17
101	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2017	374.63	20
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	02/2018	539.82	20
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	02/2018	908.08	20
104	STATIC VAR COMPENSATORS (SVCS) IN	PGCIL	05/2014	08/2016	10/2017	829.98	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NORTHERN REGION						
105	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	02/2021	14366.58	24
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2017	752.64	47
107	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.8	61
108	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	06/2017	232.34	60
109	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2017	477.69	87
110	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	64
111	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
112	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
113	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	03/2018	5353	46
114	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2017	436.68	12
115	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	03/2018	1479.3	11
116	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
117	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	01/2018	2496.9	97
118	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2017	1940.13	33
119	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	11/2017	522.29	12
120	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	07/2017	155.57	16
121	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	75
122	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	12/2017	4375.35	75
123	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	06/2017	196.58	16
124	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	01/2023	8112.12	33
125	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2017	9569.76	24
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2017	723.63	31
127	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	07/2017	15166.19	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
128	SOLAPUR STPP	NTPC	03/2012	11/2016	04/2018	9395.18	17
129	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2017	514.2	30
130	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	10/2017	305.04	7
131	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
132	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
133	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
134	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
135	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
136	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
137	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
139	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
140	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	221
141	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
142	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	99
143	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
144	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
145	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733	123
146	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
147	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2018	495.74	57
148	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	12/2017	1389.62	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
149	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
150	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
151	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2019	829.74	48
152	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	12/2020	663.01	258
153	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTTP	03/2013	03/2016	06/2018	4874.58	27
154	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
155	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
156	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	21
157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
158	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTTP	04/2008	03/2014	03/2019	5300	60
159	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
160	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
161	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2018	2500	193
162	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
163	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
164	NANDYAL-YERRAGUNTLA(NL),SCR	SCR	03/1996	02/2009	12/2017	155.74	106
165	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
166	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
167	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
168	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
169	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
170	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
171	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
172	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597	6
173	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	06/2017	495.78	17
174	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	06/2017	375.09	38
175	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2017	478.51	50
176	PANVEL-INDAPUR	NHAI	12/2011	06/2014	09/2017	942.69	39
177	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	09/2017	425.19	12
178	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	12/2017	523.85	23
179	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2018	563.92	6
180	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	06/2017	351.34	17
181	VADODARA-SURAT SECTION	NHAI	03/2014	08/2016	05/2017	503.16	9
182	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH- 125	NHAI	09/2015	09/2016	09/2017	368.73	12
183	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	07/2017	2125.24	19
184	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2017	1928.22	32
185	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	06/2017	530.07	10
186	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.5	6
187	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	11/2017	923.04	12
188	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION	NHAI	05/2014	08/2016	08/2017	1655.01	12
189	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	12/2017	1673.7	74
190	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	09/2017	1055	22
191	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	05/2017	280	99
192	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO	NHAI	09/2011	12/2013	12/2017	1250	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM.148.3 NH-46						
193	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2017	953.88	47
194	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
195	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848	49
196	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2017	1535	37
197	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	09/2017	574	42
198	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	06/2017	500.29	46
199	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2017	1410	33
200	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	05/2017	1046	44
201	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	08/2017	1108	69
202	DEOLI-KOTA	NHAI	01/2011	07/2013	10/2017	593	51
203	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	10/2017	828	37
204	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	09/2017	1348.2	43
205	MURADABAD-BAREILY	NHAI	04/2010	06/2013	06/2017	1267	48
206	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2017	1724.55	57
207	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	07/2017	325	50
208	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM	NHAI	09/2010	03/2013	06/2017	852	51
209	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM	NHAI	11/2010	05/2013	06/2017	1585	49
210	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
211	REHABILITATION AND UPGRADATION OF NH- 42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDQU	PWD	03/2015	09/2015	08/2017	309.01	23
212	REHABILITATION AND UPGRADATION OF NH- 219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
213	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
214	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
215	WIDENING TO 2 LANE AND IMPROVEMENT	PWD	12/2011	08/2015	03/2018	191.08	31

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA)						
216	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
217	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2017	2498.76	40
218	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	07/2017	1987	24
219	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2017	2159	23
220	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	05/2017	1813.76	46
221	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.3	64
222	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	10/2017	351.54	53
223	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
224	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52
225	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2017	536	41
226	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	05/2017	664	39
227	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575	56
228	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2017	511.54	49
229	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2017	1100.7	42
230	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	09/2017	702.16	38
231	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2017	1479	30
232	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	15
233	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	07/2017	1266.6	10
234	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.1	63
235	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	09/2017	1175	53
236	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	05/2017	940	58
237	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	09/2017	1693.75	73
238	ROHTAK-BAWAL	NHAI	05/2011	11/2013	05/2017	650	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
239	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	08/2017	1141	48
240	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	11/2017	754	56
241	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	06/2017	1078.84	46
242	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55
243	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	12/2017	580.43	52
244	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	06/2017	1047	36
245	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2017	1396.18	32
246	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	06/2017	291.36	41
247	ETAWAH CHAKERI	NHAI	03/2013	09/2015	10/2017	1573	25
248	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	05/2017	199.81	97
249	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	05/2017	167.64	102
250	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	05/2017	155.04	102
251	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	05/2017	200	97
252	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	05/2017	196	94
253	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	05/2017	245	110
254	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	06/2017	208	110
255	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
256	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	05/2017	563.92	6
257	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
258	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
259	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
260	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	MORTH	07/2014	01/2017	08/2017	342.05	7
261	WIDENING AND STRENGTHENING OF	MORTH	03/2014	05/2016	06/2017	191.5	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO						

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
262	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96
263	ENORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150	141

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
264	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSC	03/2007	12/2015	06/2017	149.73	18
265	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2018	343	17
266	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSC	12/2007	12/2016	12/2017	202.61	12
267	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSC	10/2011	12/2016	07/2017	175.49	7
268	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	HSC	07/2011	12/2015	06/2017	324.87	18
269	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP	HSC	04/2014	09/2017	12/2018	151.33	15
270	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSC	05/2015	03/2017	08/2018	189	17
271	IRRIGATION WORK OF BAGMATI	HSC	10/2005	03/2015	03/2021	956	72
272	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	HSC	12/2007	06/2016	03/2018	253.92	21
273	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSC	02/2014	12/2016	12/2018	787.29	24
274	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	06/2017	17265	51
275	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	10/2017	245.67	17
276	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2017	15525	31
277	3RD CONVERTER AND 4TH CASTER	RINL	07/2011	07/2016	07/2017	974.76	12
278	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	06/2017	877.73	23
279	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	05/2017	404.16	22

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
280	TURBO BLOWER - 5	RINL	12/2009	09/2016	06/2017	280	9
281	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	07/2018	1034.01	9

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
282	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	09/2017	13334	26

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
283	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER	CPWD	07/2015	11/2015	11/2017	154	24
284	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	09/2017	350.02	30
285	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	06/2018	216.69	39
286	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
287	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2015	09/2017	188.87	21
288	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	08/2017	332.72	11
289	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	03/2018	156.57	19
290	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	12/2017	270.83	37
291	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	02/2018	171.86	23
292	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	12/2017	241.33	21
293	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
294	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	06/2017	405.01	30
295	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	65
296	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	12/2017	205	69
297	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	08/2017	315	26
298	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
299	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	14600	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

ATOMIC ENERGY

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6000	2508
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291

CIVIL AVIATION

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.59	307.16
6	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
7	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	172.08	518.04	345.96

HEAVY INDUSTRY

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPR	01/2006	01/2012	993	1693	700
10	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
11	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	4259.49	135.14
12	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	HPCL	09/2016	09/2019	407	1879	1472
13	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	150	259.93	109.93
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	768.25	102.25

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
20	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
21	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
23	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	17435.15	11149.82
25	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
26	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	4404.57	5135.01	730.44
27	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
28	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
30	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5783.17	2141.13
31	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
32	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	426.29	128.96
33	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
34	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	2127.51	2619.56	492.05
35	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
36	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
37	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
38	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2352.57	564.16

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
40	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	723.63	882.13	158.5
41	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
42	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1329.43	960.71
43	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
44	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
45	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
46	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
47	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
48	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
49	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
50	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
51	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
52	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
53	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	N.A.	36.8	614	577.2
54	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
55	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	870	714.45
56	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
57	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	1542.41	1299.99
58	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
59	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	376	239.38
60	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	340	206.59
62	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
63	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
64	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	230.03	718.54	488.51
65	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
66	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	413.56	195.37
67	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	2713.09	2242.17
68	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	509	281.1
69	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
70	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	941.04	287.85
71	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
72	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
74	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
75	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
76	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
77	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
78	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5000	3500
79	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	900.05	1125.89	225.84
80	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
81	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
82	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
84	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
85	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
86	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
87	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	N.A.	677.97	1679.13	1001.16
88	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
89	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
90	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	7000	5323.69
91	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
92	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
93	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
94	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2145	1845
95	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
96	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
97	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	12/2024	750.55	943.6	193.05
98	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
99	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
100	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	N.A.	4300	4520	220
101	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
102	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
103	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16
104	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
105	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
107	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
108	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
109	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
110	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
111	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	508	195.88
112	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
113	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
114	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
115	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
116	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
117	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
118	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
119	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	445	235.23
120	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	580	328
121	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962
122	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
123	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1480.83	658.44
124	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
125	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
126	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
127	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
128	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
130	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
131	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
132	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
133	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
134	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
135	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
136	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
137	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
138	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
139	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
140	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2562.27	479.52
141	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
142	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8
143	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
144	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
145	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	348.55	102.47
146	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	477.31	182.31
147	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	227	2135	1908
148	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	06/2004	194.07	335	140.93
149	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
150	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
151	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
153	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
154	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
155	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	516.4	191.5
156	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	1566	1016
157	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.23	195.22
158	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
159	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1161.64	331.9
160	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	355.96	165.86
161	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
162	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
163	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	N.A.	100	712.82	612.82
164	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
165	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
166	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
167	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.52	236.26
168	RAJATGARH-BARANG(LD), Ecor	RVNL	04/1999	02/2009	166.16	370	203.84
169	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
170	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
171	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
172	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	19565	17065
173	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
174	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	N.A.	410.08	780.98	370.9
176	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
177	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	436	266
178	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
179	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
180	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	733	3010	2277
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
182	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
183	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
184	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
185	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
186	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	2966.99	1920.11
187	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
188	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
189	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
190	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
191	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
192	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
193	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
194	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
195	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
196	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
197	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	280	183.84
199	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	381.39	282.65
200	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
201	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
202	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
203	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
204	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	3168.29	2668.99
205	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
206	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
207	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
208	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
209	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
210	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
211	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
212	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
213	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
214	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
215	SIX LANING & STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) S	NHAI	03/2017	03/2020	985.41	1200	214.59
216	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
217	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
218	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
219	4-LANNING OF BODHRE-DHULE SECTION(KM	NHAI	03/2017	03/2020	744.64	982	237.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	390.000 TO 452.800)						
220	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
221	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
222	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
223	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
224	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
225	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
226	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
227	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
228	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
229	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
230	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
231	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
232	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
233	BANGALORE METRO RAIL PROJECT	MRTD	05/2006	06/2011	6395	13845.01	7450.01
234	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	350.02	479.87	129.85
235	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MAY 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492.00	6000.00	2508	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	553.53	244.07	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	518.04	345.96	108
5	NIGAH OCP EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	227.17	72
6	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.59	307.16	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	09/2017	150.00	259.93	109.93	38
9	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	05/2017	871.35	1200.00	328.65	26
10	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	723.40	413.59	41
11	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12
12	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	06/2017	993.00	1693.00	700	65
14	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	4259.49	135.14	20
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	10/2017	861.79	1256.72	394.93	53
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
17	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2352.57	564.16	12
18	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2017	514.20	703.10	188.9	30
19	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88
20	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	01/2018	3642.04	5783.17	2141.13	24
21	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	426.29	128.96	40
22	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.80	1731.10	458.3	61
23	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2017	436.68	602.44	165.76	12
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	01/2018	2496.90	6179.96	3683.06	97
25	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2017	1940.13	2702.65	762.52	33
26	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2018	487.49	639.46	151.97	45
27	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	09/2017	2127.51	2619.56	492.05	38
28	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	12/2017	573.99	1337.76	763.77	52

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	2228.71	482.06	40
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
31	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
32	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2017	477.69	738.48	260.79	87
33	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	5071.94	247.82	64
34	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	5135.01	730.44	38
35	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
36	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144.00	2932.88	788.88	62
37	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	09/2017	1364.52	1891.41	526.89	17
38	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	3846.30	867.82	75
39	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	12/2017	4375.35	6749.18	2373.83	75
40	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	09/2017	368.72	1329.43	960.71	134
41	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2017	723.63	882.13	158.5	31

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
42	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
43	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	12/2020	663.01	858.23	195.22	258
44	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
46	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	554.70	241.46	221
47	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
48	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
49	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5000.00	3500	122
50	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
51	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733.00	3010.00	2277	123
52	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
53	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
54	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
55	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
56	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
57	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.70	1019.47	58
58	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
59	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
60	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
61	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	941.04	287.85	60
62	SALKA ROAD -ANUPNAGAR LINE	RVNL	09/2006	03/2010	12/2017	324.90	516.40	191.5	93

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	DOUBLING								
63	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
64	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2019	829.74	1161.64	331.9	48
65	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
66	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
67	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	05/2017	196.00	331.23	135.23	94
68	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	05/2017	199.81	385.13	185.32	97
69	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	09/2017	1055.00	1601.77	546.77	22
70	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	08/2017	1108.00	2288.00	1180	69
71	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.10	3237.87	1728.77	63
72	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	05/2017	155.04	280.13	125.09	102

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
73	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96
74	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150.00	600.00	450	141

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
75	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2018	343.00	488.40	145.4	17

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(MAY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
76	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	12/2017	241.33	349.33	108	21
77	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	09/2017	350.02	479.87	129.85	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

(May 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - PPP (ANNUITY) - [N10000009]	12/2015	344.50 -	344.50	11/2016 -	09/2016	.00	-2
	Total		344.50 -	344.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	06/2017	.00	41
3	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	07/2017	.00	50
4	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	10/2017	.00	53
5	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - PPP (BOT) - [N24000153]	03/2011	359.00 -	359.00	09/2013 -	12/2016	.00	39
6	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2017	.00	55
7	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2017	.00	52
8	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	04/2017	.00	83
9	BHUBANESWAR TO PURI - PPP (BOT) - [N24000195]	03/2011	500.29 -	500.29	08/2013 -	06/2017	.00	46
10	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2017	.00	49
11	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
12	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	06/2017	.00	10
13	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	06/2017	.00	41
14	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	.00	0
15	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2017	.00	50
16	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2017	.00	42
17	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2018	.00	56

Details of Ongoing Projects Under -Public Private Partnership Mode

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	4-LANING OF RAIGANJ-DALKOLA - PPP (BOT) - [N24000204]	02/2011	580.43 -	580.43	08/2013 -	12/2017	.00	52
19	DEOLI-KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	10/2017	.00	51
20	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
21	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	03/2017	.00	55
22	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
23	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	06/2019	.00	0
24	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	05/2017	.00	42
25	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00 -	664.00	02/2014 -	05/2017	.00	39
26	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	06/2018	.00	64
27	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	09/2017	.00	38
28	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - PPP (BOT) - [N24000588]	06/2016	725.95 -	725.95	06/2019 -	06/2019	.00	0
29	MUZZAFFARNAGAR-HARDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	11/2017	.00	56
30	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	06/2019	.00	0
31	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	04/2018	.00	0
32	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - PPP (BOT) - [N24000225]	03/2012	828.00 -	828.00	09/2014 -	10/2017	.00	37
33	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	.00	0
34	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - PPP (BOT) - [N24000144]	09/2010	852.00 -	852.00	03/2013 -	06/2017	.00	51
35	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00 -	867.00	02/2015 -	12/2017	.00	34
36	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	11/2017	.00	12
37	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - PPP (BOT) - [N24000123]	03/2005	940.00 -	940.00	07/2012 -	05/2017	.00	58

Details of Ongoing Projects Under -Public Private Partnership Mode

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	06/2017	.00	47
39	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	01/2018	.00	6
40	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2018	.00	55
41	BAREILY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	05/2017	.00	44
42	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	06/2017	.00	36
43	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83	22
44	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	06/2017	.00	46
45	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	12/2017	.00	42
46	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50	69
47	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	08/2017	.00	48
48	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65	53
49	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2017	.00	48
50	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,266.60	09/2016 -	07/2017	.00	10
51	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00 -	1,267.00	06/2013 -	06/2017	.00	48
52	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	09/2017	.00	43
53	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	- -	08/2018	.00	0
54	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00 -	1,393.00	- -	01/2018	.00	0
55	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	05/2017	.00	32
56	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	06/2017	.00	33
57	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	12/2017	.00	30
58	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63

Details of Ongoing Projects Under -Public Private Partnership Mode

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	06/2017	.00	37
60	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	10/2017	.00	25
61	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79 -	1,583.79	- -	01/2019	.00	0
62	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00 -	1,585.00	05/2013 -	06/2017	.00	49
63	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	08/2017	.00	12
64	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	- -	01/2019	.00	0
65	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	12/2017	.00	0
66	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	12/2017	.00	74
67	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	09/2017	.00	73
68	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	12/2017	.00	57
69	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	05/2017	.00	46
70	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	01/2018	.00	0
71	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	02/2018	.00	15
72	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	1,928.22	04/2015 -	12/2017	.00	32
73	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	07/2017	.00	24
74	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	07/2017	.00	19
75	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	- -	04/2019	.00	0
76	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	05/2017	.00	23
77	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	- -	05/2019	.00	0
78	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	12/2017	.00	40
79	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2018	.00	49
	Total		87,497.15 -	90,983.79				

Details of Ongoing Projects Under -Public Private Partnership Mode

(May 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>SHIPPING AND PORTS</u>							
80	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20	0
81	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66	0
82	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		809.83 -	1,162.94				
	Grand Total		88,651.48	92,491.23				
