

**349th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(` 150 crore and above)
November 2014**



ONGC - DEVELOPMENT OF C-SERIES FIELDS



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

EXECUTIVE SUMMARY

1. The Flash Report for November 2014 contains information on the status of the 731 Central Sector Infrastructure Projects costing ₹150 crore and above. During November 2014, 15 projects (1 project is in Petroleum, 2 projects are in Power and 1 project is in Telecommunication and 11 projects in Shipping and Ports) have reported completion.

2. During the reference month, out of 731 projects, 324 projects are delayed with respect to original schedule and 54 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 54 projects, 31 are Mega Projects costing ₹ 1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	290	34	6	3
2.	ROAD TRANSPORT AND HIGHWAYS	136	94	4	0
3.	POWER	99	68	22	19
4.	PETROLEUM	75	49	9	5
5.	COAL	64	37	4	1
6.	URBAN DEVELOPMENT	25	13	0	0
7.	STEEL	21	17	5	1
8.	SHIPPING AND PORTS	6	2	0	0
9.	CIVIL AVIATION	7	4	1	0
10.	ATOMIC ENERGY	4	4	2	2
11.	TELECOMMUNICATIONS	2	2	1	0
12.	PETROCHEMICALS	1	0	0	0
13.	FERTILISERS	1	0	0	0
Total		731	324	54	31

3. Total original cost of implementation of the 731 projects was ₹9,39,753.89 crore and their anticipated completion cost is likely to be ₹1,149,063.01 crore, which reflects overall cost overruns of ₹2,09,309.12 crore (22.30 % of original cost). The expenditure incurred on these projects till November 2014 is ₹5,57,015.12 crore, which is 48.50 % of the anticipated cost of the projects. Sector wise projects with the maximum percentage cost overruns are as follows:-

Sector wise List of Projects having Maximum Percentage Cost Overruns(as on 30-11-2014)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL COST (Rs; crore)	ANTICIPATED COST (Rs; crore)	COST OVERRUN(%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	15.77
COAL					
4	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.02
5	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.00	490.10	0.02
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
8	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	50.37
PETROCHEMICALS					
9	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	63.35
PETROLEUM					
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	02/2012	666.00	701.00	5.26
11	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	16.02
12	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	16.05
13	WAX PROJECT	06/2010	576.60	676.05	17.25
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	29.42
POWER					
15	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC	08/2008	2360.95	2580.90	9.32
16	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	2159.07	21.34
17	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	3846.30	29.14
18	PARBATI HEP (NHPC) II	09/2002	3919.59	5366.00	36.90
19	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	2491.58	3745.08	50.31
RAILWAYS					
20	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	04/2008	653.19	653.55	0.06
21	KALYAN-KASARA 3RD LINE	04/2011	277.70	279.70	0.72
22	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	04/2008	318.24	321.62	1.06
23	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	04/2012	283.55	288.81	1.86
24	WHITE FIELD-KOLAR NL	04/2011	341.05	348.85	2.29
ROAD TRANSPORT AND HIGHWAYS					
25	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	275.00	281.31	2.29
26	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	12/2003	155.00	201.66	30.10
27	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	348.16	465.50	33.70
28	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	42.25
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
SHIPPING AND PORTS					

30	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	11/2007	1228.00	2098.56	70.89
31	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
STEEL					
32	EXPANSION OF IISCO STEEL PLANT	06/2008	14443.00	16408.00	13.61
33	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	41.41
34	COKE OVEN BATTERY NO. 4 PHASE-II	06/2006	108.00	216.68	100.63
35	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC)	01/2007	295.89	607.17	105.20
URBAN DEVELOPMENT					
36	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	114.18	173.08	51.59
37	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Sector wise projects with maximum cost overruns in absolute terms are as below:-

Sector wise List of Projects having Maximum Cost Overruns in absolute terms(as on 30-11-2014)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL COST (Rs; crore)	ANTICIPATED COST (Rs; crore)	COST OVERRUN (Rs; crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	4099.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	52.92
COAL					
4	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	06/2008	1188.31	7612.33	6424.02
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3388.61	1357.83
7	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
8	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	236.62
PETROCHEMICALS					
9	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	3459.39
PETROLEUM					
10	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
11	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	3525.39
12	DEVELOPMENT OF CLUSTER-7 FIELDS	03/2010	3241.03	6638.94	3397.91
13	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	2384.66
14	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
POWER					
15	SUBANSIRI LOWER H.E.P (NHPC)	09/2003	6285.33	15300.00	9014.67

16	BARH STPP(3X660MW) NTPC	09/2010	8692.97	15095.67	6402.70
17	KOLDAM HEP (NTPC)	01/2011	4527.15	7220.00	2692.85
18	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	4653.95	2157.05
19	KISHANGANGA HEP	01/2009	3642.04	5497.72	1855.68
RAILWAYS					
20	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
21	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
22	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
23	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	09/1997	1500.00	4996.19	3496.19
24	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
ROAD TRANSPORT AND HIGHWAYS					
25	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
26	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
27	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	212.00	386.10	174.10
28	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	363.74	167.74
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
SHIPPING AND PORTS					
30	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	11/2007	1228.00	2098.56	870.56
31	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
STEEL					
32	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	3599.00
33	EXPANSION OF IISCO STEEL PLANT	06/2008	14443.00	16408.00	1965.00
34	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC)	01/2007	295.89	607.17	311.28
35	COKE OVEN BATTERY NO. 4 PHASE-II	06/2006	108.00	216.68	108.68
URBAN DEVELOPMENT					
36	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00
37	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	114.18	173.08	58.90

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 731 projects, 6 projects are ahead of schedule, 101 are on schedule and 324 are delayed with respect to original schedule. However, the number of delayed projects decreases to 306 if delay is calculated on the basis of latest schedule of completion. Further, 32 projects have

been sanctioned without any commissioning schedule/date and for 268 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 324 delayed projects, 78 projects have overall delay in the range of 1 to 12 months, 72 projects have delay in the range of 13 to 24 months, 101 projects have delay in the range of 25 to 60 months and 73 projects have delay of 61 months and above. Sector wise projects with the maximum delay are as below:-

Sector wise List of Projects having Maximum Time Overruns(as on 30-11-2014)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL DTE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING	TIME OVERRUNS (in months)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	04/2015	76
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	03/2015	54
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
CIVIL AVIATION					
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	06/2016	65
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	12/2014	31
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	03/2016	12
8	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	02/2010	03/2014	01/2015	10
COAL					
9	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	06/2008	03/2013	03/2023	120
10	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
11	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
12	ASHOK EXPN.OCP - CCL (10 MTY)	12/2007	03/2011	03/2017	72
13	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72
PETROLEUM					
14	DEV OF G1 AND GS-15 (ONGCL)	04/2003	04/2006	06/2015	110
15	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	08/2010	05/2015	57

16	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2015	51
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	10/2015	48
18	ANKLESWAR REDEVELOPMENT	11/2010	12/2014	12/2018	48
	POWER				
19	PARBATI HEP (NHPC) II	09/2002	09/2009	03/2019	114
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	12/2015	113
21	SUBANSIRI LOWER H.E.P (NHPC)	09/2003	09/2010	12/2018	99
22	BARH STPP(3X660MW) NTPC	09/2010	12/2009	03/2018	99
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	03/2016	99
	RAILWAYS				
24	GONDIA- JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
25	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	10/2014	247
26	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
27	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2017	153
28	BELAPUR-SEAWOOD- URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
	ROAD TRANSPORT AND HIGHWAYS				
29	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH- 31 C	12/2003	06/2005	06/2015	120
30	AGRA-BYPASS(NS- 1/UP-1), NH-2,3	12/2003	09/2007	06/2015	93
31	HARANGAJO TO MAIBANG,KM 164.08- 190.587 NH-54	12/2003	09/2007	03/2015	90
32	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	12/2003	09/2007	12/2014	87
33	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12/2003	10/2008	11/2015	85
	SHIPPING AND PORTS				
34	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	11/2014	104
35	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	11/2007	12/2010	01/2016	61
	STEEL				
36	COKE OVEN BATTERY NO. 4 PHASE-II	06/2006	09/2008	12/2014	75

37	AUGMENTATION OF IRON ORE STORAGE IN RMHP	07/2007	09/2009	06/2015	69
38	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	10/2009	03/2015	65
39	EXPANSION OF BOKARO STEEL PLANT	05/2010	12/2011	06/2015	42
40	BAILADILA IRON ORE PROJECT DEPOSIT-11B (NMDC)	01/2007	12/2011	03/2015	39
TELECOMMUNICATIONS					
41	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	01/2009	12/2014	71
42	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	09/2015	59
URBAN DEVELOPMENT					
43	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	03/2010	10/2014	55
44	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	05/2015	35
45	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	01/2015	34
46	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	10/2015	29
47	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL	12/2012	12/2014	12/2016	24

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2014, out of 727 projects on the monitor of this Ministry, 235 projects reported cost overruns and 282 projects reported time overruns; while during November 2014, out of 731 projects, 227 projects reported cost overruns and 324 projects reported time overruns. In comparison to April 2014, number of projects reporting cost overruns has gone down from 32% to 31% whereas projects reporting time overruns have increased to 39% from 44% (Annexure 6 (a) & 6 (b)).

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, Maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. Sector wise earliest initiated projects in which project agencies are not providing milestones are as follows:-

Sector wise List of Earliest Projects without Milestones(as on 30-11-2014)

[illegible]

1	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	08/2010	8140.00	8140.00	7117.42	02/2014	12/2014	0
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	246.81	276.83	262.21	08/2012	10/2014	0
3	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	08/2008	144.02	204.29	155.22	06/2012	12/2014	0
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	470.27	09/2011	12/2015	0
5	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	270.00	270.00	NR	12/2014	03/2016	0
POWER								
1	SUBANSIRI LOWER H.E.P (NHPC)	09/2003	6285.33	15300.00	7019.81	09/2010	12/2018	0
2	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION	06/2012	1909.24	1909.24	639.63	06/2015	06/2015	0
3	EASTERN REGION STRENGTHENING SCHEME-XII	05/2014	522.29	522.29	NR	11/2016	11/2016	0
4	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	03/2014	155.57	155.57	NR	03/2016	05/2016	0
5	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	03/2012	198.63	198.63	12.80	09/2014	06/2016	0
RAILWAYS								
1	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	548.01	199.92	NR	NR	0
2	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	406.99	141.55	NR	NR	0
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	595.67	03/1994	10/2014	0
4	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	703.18	255.54	NR	NR	0
5	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	445.40	180.72	03/2007	03/2015	0
ROAD TRANSPORT AND HIGHWAYS								
1	LUCKNOW-RAIBAREILI	07/1999	635.90	635.90	608.30	07/2012	09/2014	0
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	3466.00	11/2011	03/2015	0
3	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	05/2009	572.30	572.30	886.90	10/2011	06/2015	0
4	CHENNAI-TADA(SIX LANE)	04/2009	353.37	353.37	446.20	10/2011	12/2014	0

5	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	486.00	486.00	667.10	05/2010	12/2014	0
SHIPPING AND PORTS								
1	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	702.00	755.50	219.00	03/2011	03/2013	0
2	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	800.00	1571.60	9.70	10/2008	NR	0
3	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	11/2014	0
4	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	NR	0
5	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	882.00	1060.00	0.93	02/2011	12/2012	0
STEEL								
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	15525.00	5615.00	05/2015	12/2016	0
TELECOMMUNICATIONS								
1	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	48.95	10/2010	03/2015	0
2	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	195.94	01/2009	12/2014	0
3	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL	01/2009	149.15	158.72	86.05	06/2009	12/2014	0
URBAN DEVELOPMENT								
1	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARAstra	12/2012	315.00	315.00	53.96	06/2015	08/2015	0
2	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL	12/2012	188.87	188.87	10.64	12/2014	12/2016	0
3	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	11/2012	238.43	238.43	0.00	02/2015	08/2015	0
4	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	270.83	270.83	15.60	11/2014	10/2015	0
5	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	2727.89	2727.89	2637.11	03/2010	10/2014	0

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. Sector wise earliest initiated projects in which project agencies are not reporting/providing revised cost estimates are as follows:-

Sector wise List of Earliest Projects without Revised Cost Estimates(as on 30-11-2014)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL COST (Rs; crore)	REVISED COST (Rs; crore)	CUMMULATIVE EXPENDITURE (Rs; crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	17975.00
CIVIL AVIATION					
1	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	NR	311.25
COAL					
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3027.59	3064.56
2	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1248.89
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	NR	7974.30
PETROLEUM					
1	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5867.78
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	246.81	NR	262.21
POWER					
1	RAMPUR HEP(412 MW)	01/2007	2047.03	NR	3315.80
2	KISHANGANGA HEP	01/2009	3642.04	NR	3712.35
3	BARH STPP STAGE -II	02/2008	7341.04	NR	8023.00
4	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART- C	03/2011	2569.25	NR	2579.17
5	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	623.44	833.58
RAILWAYS					
1	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	NR	463.82
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	9987.13
3	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	155.74	164.36	726.70
4	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	NR	199.92
5	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	04/1994	320.66	NR	457.55
ROAD TRANSPORT AND HIGHWAYS					
1	4-LANNING OF CHAPRA-HAJIPUR	01/2011	575.00	NR	835.60
2	DEOLI-KOTA	01/2011	593.00	NR	761.30
3	JORBAT - BARAPANI	01/2011	536.00	NR	759.90
4	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	NR	2762.00

5	ARMUR TO KADLOOR YELLAREDDY	02/2010	390.56	NR	631.70
SHIPPING AND PORTS					
1	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	298.17	371.18
STEEL					
1	EXPANSION OF IISCO STEEL PLANT	06/2008	14443.00	NR	16489.58

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

Sector wise earliest initiated projects in which project agencies are not reporting/providing or updating revised commissioning schedules are as below:-

Sector wise List of Earliest Projects without Revised Commissioning Schedule(as on 31.10.2014)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURAIIDH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013

3	SYSTEM STRENGTHENING - XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.
4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.

2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

10.The Sector-wise details of additional delays are as under:-

i) In the **Atomic Energy Sector**, all 4 projects are delayed. During the month 2 projects have reported additional delay of one month each. Both are mega projects. The project 'KUDANKULAM APP, NPCIL' (Mega Project) has reported additional delay of one month due to local protest, agitation and contractual issues. And the project 'RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW), NPCIL' (Mega Project) has reported additional delay of 1 month due to delay in supply of equipments.

ii) In the **Civil Aviation Sector**, out of 7 projects, 4 projects are delayed. During the month, project namely 'CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA), AAI' has reported additional delay of 1 month due to change in structural design of foundation, delay in completing cargo and prolonged rainy season.

iii) In the **Railway Sector**, out of 290 projects, 34 projects are delayed. During the month 6 projects have reported additional delays in the range of 12-24 months, out of which 3 are mega projects. The project 'NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR' has reported additional delay of 24 months due to local agitation. The Project 'NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP), RVNL' has reported additional delay of 24 months. The Projects 'JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR), NFR', 'NEW COOCHBEHAR TO SAMUKTALA, NFR', 'NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT, NFR' and 'AMBARI FALAKATA TO NEW MAYNAGURI, NFR' have reported additional delay of 12 months each (however, no specific reasons

have been reported by the project implementing agency for the delay in these projects).

iv) In the **Road Sector**, out of 136 projects, 94 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-12 months. The project 'KOTA BYPASS, RJ-4, NH-76, NHAI' has reported additional delay of 12 months due to forest clearance, non-granting of NOC by PWD for laying road in water body and court cases; the project 'TIRUPATI - TIRUTHANI - CHENNAI, NHAI' has reported additional delay of one month due to delay in land acquisition, non-granting of NOC by PWD for laying road in water body and court cases; the projects 'DHARAMTUL TO SONAPUR (AS-19), NHAI' and 'REENGUS SIKAR, NHAI' have reported additional delay of 2 months each (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).

v) In the **Petroleum Sector**, out of 75 projects, 49 projects are delayed. During the month 9 projects have reported additional delays in the range of 1-14 months, out of which 5 are Mega projects. The project 'DEVELOPMENT OF C-26 CLUSTER FIELDS, ONGC' has reported additional delay of 10 months due to slow progress by contractor; the project 'REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY, IOCL' has reported additional delay of 5 months due to initial delay in lining up of PMC; the projects 'DE-BOTTLENECKING OF SMPL, IOCL' and 'AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE, IOCL' have reported additional delay of 4 months each due to delay in wild life clearance and land acquisition respectively; the project 'PARADIP-RAIPUR- RANCHI PIPELINE, IOCL' has reported additional delay of 3 months due to poor performance of contractor; the projects 'STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG, ISPR' and 'MARKETING TERMINAL AT PARADEEP, IOCL' have reported additional delay of 2 months each due to slow construction works and delay in CRZ approval for laying of Furnace Oil line respectively; the project 'WAX PROJECT, NRL' has reported additional delay of 1 month due to slow progress in construction activities and the project 'INTEGRATED DEVELOPMENT OF BASSEIN FIELD, ONGC' has reported additional delay of 14 months (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).

vii) In the **Steel Sector**, out of 21 projects, 17 projects are delayed. During the month 5 projects have reported additional delay in the range of 1-5 months, out of which 1 is Mega project. The project '7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT, NMDC' has reported additional delay of 5 months due to delay in retendering activities and external supplies; the projects 'EXPANSION OF LIQUID STEEL CAPACITY

FROM 3MT TO 6.3MT, (RINL)' and 'AUGMENTATION OF IRON ORE STORAGE IN RMHP, RINL' have reported additional delay of 3 months due to delay in tendering process and execution; the projects 'COKE OVEN BATTERY NO. 4 PHASE-II, RINL' and '1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) ' have reported additional delay of 1 month and 3 months respectively (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).

viii) In the Coal Sector, out of 64 projects, 37 projects are delayed. During the month, 4 projects have reported additional delay in the range of 1-9 months, out of which 1 is Mega project. The Project 'RG OC -III EXTENSION (PHASE -II) PROJECT, SCCL' has reported additional delay of 9 months due to delay in non-forest land acquisition and rehabilitation and resettlement problem; the project 'KALYANIKHANI OPENCAST PROJECT, SCCL' has reported additional delay of 8 months due to delay in non-forest land acquisition and rehabilitation and resettlement problem; the project 'TUTICORIN THERMAL POWER PROJECT- 2X500 MW, NLC' has reported additional delay of 2 months due to inadequate mobilization by the contractor; the project 'WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU, NLC' has reported additional delay of 1 month due to delay in acquisition of private land, supply of equipment and clearance from state government.

ix) In the Power Sector, out of 99 projects, 68 projects are delayed. During the month, 22 projects have reported additional delays in the range of 1-36 months, out of which 19 are Mega projects. The Project 'KUNADANKULAM APP TRANS SYSTEM, PGCIL' has reported additional delay of 36 months due to severe RoW problem; the projects 'BARH STPP(3X660MW), NTPC' and 'WESTERN REGION STRENGTHENING SCHEME-V, PGCIL' have reported additional delay of 12 months each due to delay in supply of equipments and severe RoW problem respectively; the projects 'PARBATI HEP II, NHPC' has reported additional delay of 8 months due to contractual issues; the project 'BONGAIGAON THERMAL POWER PROJECT, NTPC' has reported additional delay of 7 months due to law and order problem; the projects 'KOLDAM HEP (NTPC) NTPC' and 'TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC' have reported additional delay of 5 months each due to seepage problem in main dam and contractual issues respectively; the projects 'TEESTA LOW DAM HEP, STAGE-IV, NHPC', 'TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A, PGCIL', 'TRANSMISSION SYSTEM FOR PHASE-I GENERATION

PROJECTS IN ORISSA-PART B, PGCIL' and 'TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH, PGCIL' have reported additional delay of 4 months each due to law and order, RoW problem, environmental clearance and delay in land acquisition respectively; the projects 'TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT, PGCIL', 'EASTERN REGION STRENGTHENING SCHEME-III,PGCIL', 'COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND INDBARATH POWER(MADRAS) LIMITED, PGCIL' and 'TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH, PGCIL' have reported additional delay of 3 months each due to environment clearances, land acquisition, severe RoW problem and environment clearance respectively; the projects 'SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC, PGCIL', '765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC, PGCIL', 'TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C, PGCIL' and 'SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH, PGCIL' have reported additional delay of 1 month each due to law and order in first two projects and delay in environment clearance in last projects; the projects 'SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID, PGCIL', 'SYSTEM STRENGTHENING XIII OF SR GRID, PGCIL' and 'SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION), PGCIL' have reported additional delay of 3 months in first two projects and 1 month delay in the last project months (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).

x)In **Telecommunication Sector**, all 2 projects are delayed. During the month 1 project 'ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS, BSNL' has reported additional delay of 6 months due to delay in procurement of security stack and UPS.


11. The status as on 30.11.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	290	6
2	ROAD TRANSPORT AND HIGHWAYS	136	4
3	POWER	99	22
4	PETROLEUM	75	9
5	COAL	64	4
6	URBAN DEVELOPMENT	25	0
7	STEEL	21	5
8	CIVIL AVIATION	7	1
9	SHIPPING AND PORTS	6	0
10	ATOMIC ENERGY	4	2
11	TELECOMMUNICATIONS	2	1
12	FERTILISERS	1	0
13	PETROCHEMICALS	1	0
	Total	731	54

Sectoral break up of on-going infrastructure projects.

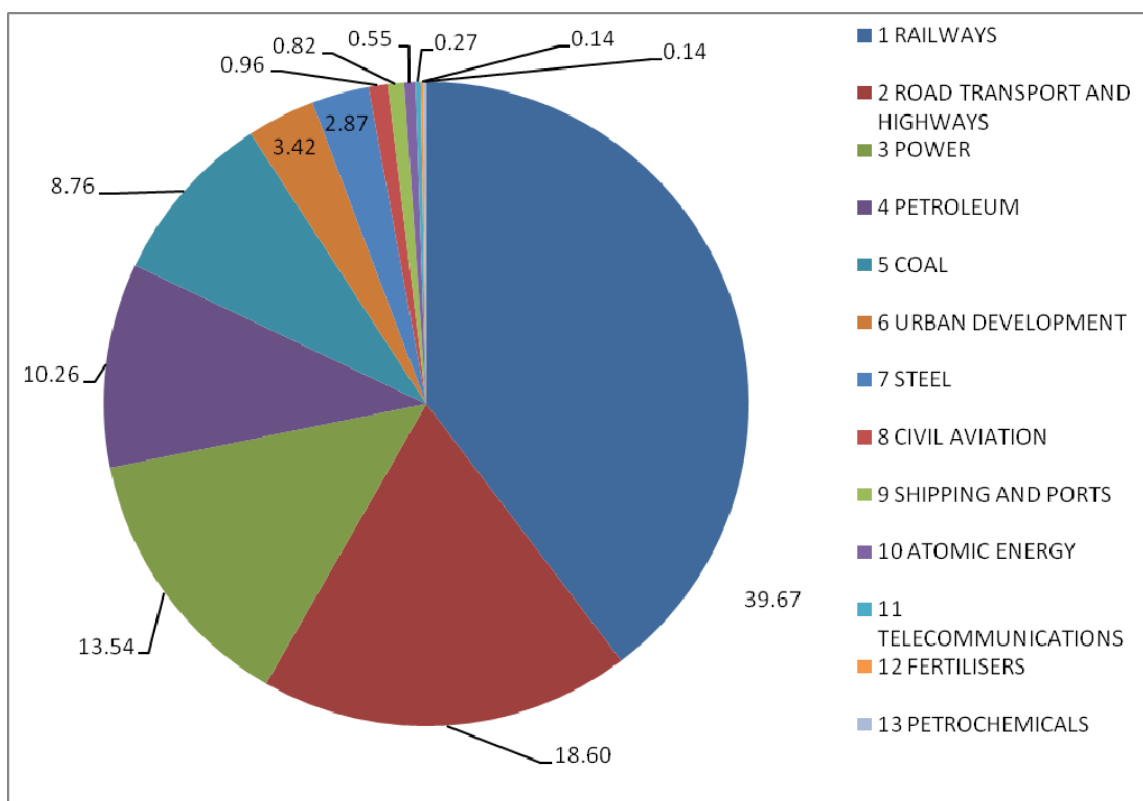

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	<u>COAL</u>			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	<u>POWER</u>			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2,349.46
	June,2014			
	<u>PETROLEUM</u>			
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000039]	5,713.03	05/2010	3,918.86
4	DEVELOPMENT OF B-46 CLUSTER FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000046]	1,436.21	07/2010	1,165.53
5	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000060]	7,133.39	09/2012	2,795.50
	<u>POWER</u>			
6	MOUDA STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000048]	5,459.28	08/2012	4,056.00
7	VINDHYACHAL STTP STAGE-IV (NATIONAL THERMAL POWER CORPORATION) - [N18000072]	5,915.00	10/2012	3,401.00
8	RIHAND STTP STAGE-III (2X500MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000073]	6,230.81	10/2012	4,357.00
	<u>RAILWAYS</u>			
9	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000083]	156.00	-	424.43
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106236]	166.27	03/2008	200.40
11	CHITRADURGA-TUMKUR(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000157]	839.00	-	692.50
	July,2014			
	<u>STEEL</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000068]	202.00	01/2010	294.84
13	330 TPH BOILER-6 AND AUXILIARY SYSTEM (RASTRIYA ISPAT NIGAM LIMITED) - [N12000069]	260.00	12/2009	260.75
	<u>PETROLEUM</u>			
14	DEVELOPMENT OF C-SERIES FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000023]	3,195.16	12/2008	3,886.15
15	DEVELOPMENT OF B-22 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000032]	2,323.40	09/2010	1,916.10
16	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000069]	3,284.00	09/2011	1,916.30
17	ADDITIONAL DEV. OF D-1 FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000086]	2,163.64	06/2012	2,182.31
	<u>POWER</u>			
18	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000106]	425.51	10/2013	386.32
	<u>TELECOMMUNICATIONS</u>			
19	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB (BHARAT SANCHAR NIGAM LIMITED) - [N26000041]	373.94	12/2008	227.58
20	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT (BHARAT SANCHAR NIGAM LIMITED) - [N26000072]	952.88	03/2010	20.00
21	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT (BHARAT SANCHAR NIGAM LIMITED) - [N26000073]	152.65	03/2010	29.05
22	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000088]	328.13	03/2009	164.58
23	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000090]	916.70	11/2010	828.48
	August,2014			
	<u>PETROLEUM</u>			
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000070]	238.68	01/2012	293.12
25	SINGLE POINT MOORING FACILITY(SMP) PROJECT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000152]	1,043.57	04/2012	648.92
	<u>SHIPPING AND PORTS</u>			
26	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN (PORT TRUST) - [N25000048]	3,500.00	01/2012	3,661.95

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	September,2014			
	<u>CIVIL AVIATION</u>			
27	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000037]	1,942.51	05/2011	2,573.92
28	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000038]	1,808.00	01/2011	1,939.20
	October,2014			
	<u>PETROLEUM</u>			
29	JHAJJAR HISSAR PIPE LINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000051]	281.07	10/2010	6.18
30	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) (GAS AUTHORITY OF INDIA LIMITED) - [N16000094]	540.92	06/2011	340.94
31	MRPL PHASE-III EXPANSION (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000114]	12,412.00	01/2012	12,205.74
	<u>POWER</u>			
32	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000063]	184.19	11/2011	165.67
33	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000111]	1,637.34	08/2014	1,499.95
	<u>TELECOMMUNICATIONS</u>			
34	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II (BHARAT SANCHAR NIGAM LIMITED) - [N26000100]	1,148.19	05/2011	251.27
	November,2014			
	<u>PETROLEUM</u>			
35	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000138]	246.81	08/2012	263.59
	<u>POWER</u>			
36	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000107]	1,391.97	12/2013	1,472.35
37	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP- PART C1 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000121]	324.33	08/2014	211.36

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>SHIPPING AND PORTS</u>			
38	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL (PORT TRUST) - [N25000003]	800.00	10/2008	9.70
39	DEEPENING OF CHANNEL AT PARADIP PORT (PORT TRUST) - [N25000004]	154.84	-	247.89
40	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS (SHIPPING CRP. OF INDIA) - [N25000014]	359.44	04/2011	218.00
41	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST (PORT TRUST) - [N25000037]	882.00	02/2011	1,098.00
42	ACQUISITION OF TWO NOS. OF 3060 DWT (SHIPPING CRP. OF INDIA) - [N25000043]	277.03	12/2011	263.08
43	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES (SHIPPING CRP. OF INDIA) - [N25000051]	612.72	12/2012	513.36
44	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. (SHIPPING CRP. OF INDIA) - [N25000052]	1,028.10	12/2013	554.60
45	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY (SHIPPING CRP. OF INDIA) - [N25000053]	966.46	02/2014	427.54
46	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST (RAIL VIKAS NIGAM LTD.) - [N25000059]	245.67	04/2009	373.22
47	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER (SHIPPING CRP. OF INDIA) - [N25000061]	220.49	01/2013	47.32
48	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY (SHIPPING CRP. OF INDIA) - [N25000062]	511.87	03/2014	106.72
	<u>TELECOMMUNICATIONS</u>			
49	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL (BHARAT SANCHAR NIGAM LIMITED) - [N26000058]	149.15	06/2009	86.34

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	October,2014			
	<u>WATER RESOURCES</u>			
1	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [N06000019]	542.90	12/2007	35.49


Summary of projects in the Flash Report for the month of November, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	747
Number of Projects completed/dropped/frozen in Current Month	16
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	2
Number of Projects in Current Month	731

Brief Analysis


Project Status with respect to Original Schedule: Out of 731 projects, 6 projects are ahead of schedule, 101 projects are on schedule and 324 projects are delayed. Of the balance, 268 projects do not have fixed dates of commissioning while 32 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

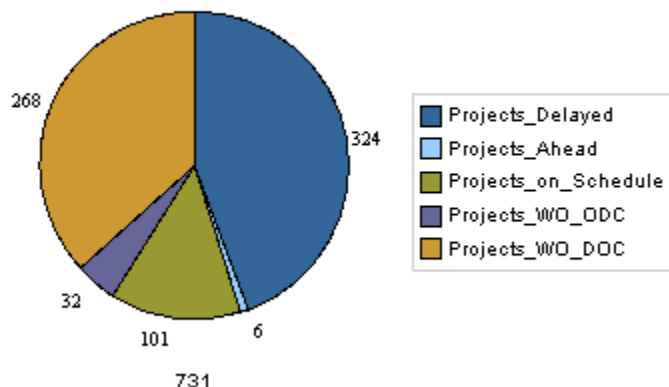

Investment Scenario

Total original cost of implementation of 731 projects when sanctioned, was of the order of Rs. 939753.89 crore but this was subsequently revised to Rs. 1149063.01 crore implying a cost overrun of 22.3%. The expenditure incurred on these projects till November, 2014 is Rs. 557015.12 crore, which is 48.5% of the revised cost of the projects.

Figures are in Rs. Crore

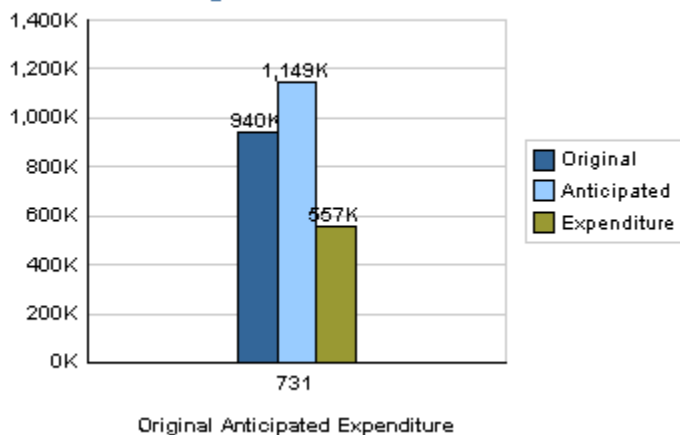

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	747
No of Projects Completed/Dropped/Frozen in Current Month	15
No of Projects elevated to status of Major Project during the current months	3
No of Projects added in Current Month	2
No of Projects in Current Month	731

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	324	6	101	32	268	731	44.32
Latest Approved (Date)	306	10	115	32	268	731	41.86

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	627	7,84,432.49	8,74,297.49	3,83,981.12	43.90	89,865.00	11.50
Project with Revision in Cost	104	2,15,614.89	2,74,765.52	1,73,034.00	63.00	59,150.63	27.40
Total	731	10,00,047.38	11,49,063.01	5,57,015.12	48.48	149015.63	14.90
Original Cost of All Projects							
Original Cost	731	9,39,753.89	11,49,063.01	5,57,015.12	48.50	2,09,309.12	22.30

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	324	562,594.44	691,241.48	433,804.46	62.80	128,647.04	22.90
Latest Approved (RCE)	307	581,478.72	654,801.31	418,247.58	63.90	73,322.59	12.60

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	54	123,712.99	155,929.35	109,942.23	70.50	32,216.36	26.00

Annexure-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	15.77
3	COAL	64	46,559.36	56,741.93	21.87	8	9,925.87	20,706.79	108.61
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	STEEL	21	81,920.10	87,874.06	7.27	4	23,538.89	29,522.85	25.42
6	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	63.35
7	PETROLEUM	75	165,614.37	182,323.41	10.09	18	62,296.27	83,031.58	33.29
8	POWER	99	241,739.71	273,378.26	13.09	17	45,781.10	77,419.65	69.11
9	RAILWAYS	290	164,135.33	290,709.13	77.12	163	87,659.91	214,613.12	144.82
10	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,391.34	2.02	9	2,866.62	4,961.13	73.07
11	SHIPPING AND PORTS	6	5,356.50	6,468.59	20.76	2	1,378.00	2,698.56	95.83
12	TELECOMMUNICATIONS	2	720.81	720.81	0.00	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	2	6,509.18	11,782.08	81.01
Total		731	939,753.89	1,149,063.01	22.27	227	262,415.06	476,991.29	81.77

[illegible]

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
Total		731	939,753.89	1,149,063.01	22.27	227	262,415.06	476,991.29	81.77

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	4	40,442.00	46,726.00	17 - 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	4	1,206.95	1,259.87	10 - 65
3	COAL	64	46,559.36	56,741.93	21.87	37	28,664.59	39,219.11	3 - 120
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	STEEL	21	81,920.10	87,874.06	7.27	17	80,463.54	86,417.50	8 - 75
6	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	-
7	PETROLEUM	75	165,614.37	182,323.41	10.09	49	102,068.53	116,537.47	2 - 110
8	POWER	99	241,739.71	273,378.26	13.09	68	203,485.03	235,123.58	1 - 114
9	RAILWAYS	290	164,135.33	290,709.13	77.12	34	29,123.25	85,426.94	3 - 261
10	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,391.34	2.02	94	68,982.88	71,052.78	2 - 120
11	SHIPPING AND PORTS	6	5,356.50	6,468.59	20.76	2	1,378.00	2,698.56	61 - 104
12	TELECOMMUNICATIONS	2	720.81	720.81	0.00	2	720.81	720.81	59 - 71
13	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	13	6,058.86	6,058.86	1 - 35
Total		731	939,753.89	1,149,063.01	22.27	324	562,594.44	691,241.48	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	24,649.56	30,169.08	22.39	8	17,332.30	20,538.98	12 - 75
2	ARUNACHAL PRADESH	3	9,356.22	21,082.33	125.33	3	9,356.22	21,082.33	25 - 99
3	ASSAM	39	26,819.37	42,173.91	57.25	28	18,441.19	26,996.83	8 - 120
4	BIHAR	48	37,027.18	51,405.82	38.83	14	22,850.50	34,226.02	5 - 99
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	31 - 31
6	GUJARAT	31	36,997.24	37,591.79	1.61	12	24,758.08	24,696.77	6 - 48
7	HARYANA	8	4,259.81	6,409.79	50.47	2	1,594.00	2,774.00	40 - 55
8	HIMACHAL PRADESH	6	13,728.27	21,028.89	53.18	4	10,764.60	16,145.11	11 - 114
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	6	13,202.50	32,123.18	6 - 193
10	KARNATAKA	33	65,925.98	80,757.70	22.50	8	21,020.68	21,908.25	5 - 99
11	KERALA	11	19,030.21	23,056.44	21.16	4	2,849.00	3,549.00	25 - 58
12	MADHYA PRADESH	17	23,452.88	25,436.80	8.46	10	16,512.83	16,625.63	2 - 74
13	MAHARASHTRA	41	67,520.43	79,631.16	17.94	21	43,037.84	51,170.53	1 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	536.00	536.00	11 - 11
16	MIZORAM	2	988.06	3,733.88	277.90	2	988.06	3,733.88	47 - 113
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	39	66,852.20	75,528.98	12.98	21	53,515.75	58,373.95	6 - 84
19	PUNJAB	4	1,497.50	1,470.46	-1.81	1	705.00	705.00	25 - 25
20	RAJASTHAN	25	25,638.72	25,694.20	0.22	8	18,085.51	17,639.23	4 - 85
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 65
22	TAMIL NADU	41	53,533.49	70,580.21	31.84	18	38,650.77	48,820.58	2 - 104
23	TRIPURA	6	2,966.26	6,552.28	120.89	4	2,417.39	5,366.76	16 - 108
24	UTTAR PRADESH	26	14,207.60	16,863.93	18.70	12	6,135.97	7,594.64	4 - 93
25	WEST BENGAL	39	55,900.06	67,857.95	21.39	16	31,998.89	37,724.12	3 - 153
26	CHANDIGARH	1	452.00	452.00	0.00	0	0.00	0.00	-
27	DELHI	9	44,464.60	44,464.60	0.00	4	4,045.16	4,045.16	8 - 29
28	CHHATISGARH	27	72,434.39	80,336.80	10.91	17	69,015.54	75,750.84	1 - 120
29	JHARKHAND	31	21,501.51	22,165.22	3.09	16	10,487.05	11,025.47	2 - 138
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	5	9,132.06	12,575.24	7 - 94
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	21	9,410.62	12,179.13	29.42	8	2,951.53	4,151.45	8 - 71
33	MULTI STATE	178	197,477.48	223,994.78	13.43	66	108,647.91	116,930.37	1 - 261
Total		731	939,753.89	1,149,063.01	22.27	324	562,594.44	691,241.48	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	17 - 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	4	1,206.95	1,259.87	10 - 65
3	COAL	64	46,559.36	56,741.93	21.87	37	28,664.59	39,219.11	3 - 120
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	STEEL	21	81,920.10	87,874.06	7.27	17	80,463.54	86,417.50	8 - 75
6	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	-
7	PETROLEUM	75	165,614.37	182,323.41	10.09	44	96,767.41	106,275.44	2 - 57
8	POWER	99	241,739.71	273,378.26	13.09	66	200,619.41	229,556.00	1 - 114
9	RAILWAYS	290	164,135.33	290,709.13	77.12	30	22,028.91	71,503.90	3 - 261
10	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,391.34	2.02	90	68,204.31	70,182.26	2 - 120
11	SHIPPING AND PORTS	6	5,356.50	6,468.59	20.76	1	1,228.00	2,098.56	61 - 61
12	TELECOMMUNICATIONS	2	720.81	720.81	0.00	1	336.81	336.81	71 - 71
13	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	13	6,058.86	6,058.86	1 - 35
Total		731	939,753.89	1,149,063.01	22.27	306	542,528.79	653,957.31	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	46,726.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	15.77
3	COAL	64	50,140.39	56,741.93	13.17	6	5,805.80	12,875.66	121.77
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	STEEL	21	85,939.06	87,874.06	2.25	1	14,443.00	16,408.00	13.61
6	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	63.35
7	PETROLEUM	75	182,254.77	182,323.41	0.04	4	16,979.93	20,207.92	19.01
8	POWER	99	257,327.57	273,378.26	6.24	7	20,070.39	36,121.08	79.97
9	RAILWAYS	290	177,495.66	290,709.13	63.78	156	88,416.33	202,009.21	128.48
10	ROAD TRANSPORT AND HIGHWAYS	136	102,692.45	104,391.34	1.65	8	2,906.07	4,651.57	60.06
11	SHIPPING AND PORTS	6	5,747.50	6,468.59	12.55	2	1,769.00	2,698.56	52.55
12	TELECOMMUNICATIONS	2	720.81	720.81	0.00	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	25	82,745.21	87,959.21	6.30	1	6,395.00	11,609.00	81.53
Total		731	1,000,047.38	1,149,063.01	14.90	187	162,581.74	315,889.53	94.30

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	0	0.00	0.00	0- 0
3	COAL	64	46,559.36	56,741.93	21.87	2	6,935.32	9,991.35	35- 66
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	STEEL	21	81,920.10	87,874.06	7.27	3	9,095.89	13,114.85	39- 75
6	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	PETROLEUM	75	165,614.37	182,323.41	10.09	8	41,801.67	57,482.87	8- 110
8	POWER	99	241,739.71	273,378.26	13.09	4	4,943.63	9,541.29	16- 113
9	RAILWAYS	290	164,135.33	290,709.13	77.12	4	5,873.07	9,145.95	0- 60
10	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,391.34	2.02	2	425.61	517.56	69- 72
11	SHIPPING AND PORTS	6	5,356.50	6,468.59	20.76	2	1,378.00	2,698.56	61- 104
12	TELECOMMUNICATIONS	2	720.81	720.81	0.00	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	0	0.00	0.00	0- 0
Total		731	939753.89	1149063.01	22.27	27	87116.19	125439.43	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	31- 31
3	COAL	64	46,559.36	56,741.93	21.87	6	9,285.28	20,018.10	30- 120
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	STEEL	21	81,920.10	87,874.06	7.27	4	23,538.89	29,522.85	39- 75
6	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	PETROLEUM	75	165,614.37	182,323.41	10.09	13	46,568.11	64,569.31	2- 110
8	POWER	99	241,739.71	273,378.26	13.09	15	32,560.98	55,103.98	10- 114
9	RAILWAYS	290	164,135.33	290,709.13	77.12	30	24,048.57	80,352.28	3- 261
10	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,391.34	2.02	9	2,866.62	4,961.13	40- 93
11	SHIPPING AND PORTS	6	5,356.50	6,468.59	20.76	2	1,378.00	2,698.56	61- 104
12	TELECOMMUNICATIONS	2	720.81	720.81	0.00	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	0	0.00	0.00	0- 0
Total		731	939753.89	1149063.01	22.27	82	157245.06	280561.74	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	246.81	08/2012	276.83	N.A.	263.59
	<u>POWER</u>						
2	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	08/2011	1,391.97	12/2013	1,391.97	11/2014	1,472.35
3	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1	02/2012	324.33	08/2014	324.33	11/2014	211.36
	<u>SHIPPING AND PORTS</u>						
4	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	800.00	10/2008	1,571.60	N.A.	9.70
5	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	154.84	N.A.	253.36	12/2010	247.89
6	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS	10/2007	359.44	04/2011	359.44	11/2011	218.00
7	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	882.00	02/2011	1,060.00	12/2012	1,098.00
8	ACQUISITION OF TWO NOS. OF 3060 DWT	04/2009	277.03	12/2011	277.03	10/2012	263.08
9	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES	08/2010	612.72	12/2012	532.83	11/2013	513.36
10	ACQUISTION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD.	10/2010	1,028.10	12/2013	1,012.23	11/2015	554.60
11	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY	10/2010	966.46	02/2014	994.82	11/2015	427.54
12	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	04/2009	373.22	02/2011	373.22
13	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER	07/2011	220.49	01/2013	220.49	11/2014	47.32
14	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY	01/2012	511.87	03/2014	511.87	11/2014	106.72
	<u>TELECOMMUNICATIONS</u>						
15	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL	01/2009	149.15	06/2009	158.72	12/2014	86.34

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>FERTILISERS</u>					
1	SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	2/2017	197.79	2/2017
	<u>PETROLEUM</u>					
2	TWENTY NOS. FEEDER GAS LINES	3/2009	228.64	12/2016	228.64	12/2016

Milestones (Cumulative due & achieved)

Total	3767
Achieved up to month	1431

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	03/2015	04/2015	1
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) NPCIL	12,320.00	12,320.00	12/2016	04/2018	05/2018	1
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) AAI	335.61	388.53	05/2012	11/2014	12/2014	1
	<u>COAL</u>						
4	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	12/2014	01/2015	1
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	12/2014	02/2015	2
6	KALYANIKHANI OPENCAST PROJECT SCCL	417.33	417.33	07/2016	07/2016	03/2017	8
7	RG OC -III EXTENSION (PHASE -II) PROJECT SCCL	365.01	365.01	06/2015	06/2015	03/2016	9
	<u>STEEL</u>						
8	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	09/2008	11/2014	12/2014	1
9	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) RINL	8,692.00	12,291.00	10/2009	12/2014	03/2015	3
10	AUGMENTATION OF IRON ORE STORAGE IN RMHP RINL	480.00	450.00	09/2009	03/2015	06/2015	3
11	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) NMDC	572.00	572.00	04/2013	03/2015	06/2015	3
12	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) NMDC	898.55	898.55	05/2013	03/2015	08/2015	5
	<u>PETROLEUM</u>						
13	WAX PROJECT NRL	576.60	676.05	12/2013	11/2014	12/2014	1

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG ISPRL	672.00	1,038.00	10/2011	12/2014	02/2015	2
15	MARKETING TERMINAL AT PARADEEP IOCL	199.75	199.75	07/2013	12/2014	02/2015	2
16	PARADIP-RAIPUR- RANCHI PIPELINE IOCL	1,793.00	1,793.00	09/2012	12/2015	03/2016	3
17	DE-BOTTLENECKING OF SMPL IOCL	1,584.00	1,584.00	N.A.	08/2015	12/2015	4
18	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	08/2015	08/2015	12/2015	4
19	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY IOCL	480.00	480.00	02/2016	02/2016	07/2016	5
20	DEVELOPMENT OF C-26 CLUSTER FIELDS ONGC	2,592.17	2,592.17	05/2014	05/2015	03/2016	10
21	INTEGRATED DEVELOPMENT OF BASSEIN FIELD ONGC	3,513.07	4,619.94	02/2016	02/2016	04/2017	14
	<u>POWER</u>						
22	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC PGCIL	2,360.95	2,580.90	08/2012	11/2014	12/2014	1
23	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC PGCIL	7,075.33	7,075.33	08/2012	11/2014	12/2014	1
24	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C PGCIL	2,569.25	2,569.25	03/2014	02/2015	03/2015	1
25	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	05/2015	06/2015	1
26	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	11/2014	12/2014	1
27	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	12/2015	03/2016	3
28	EASTERN REGION STRENGTHENING SCHEME- III PGCIL	1,272.80	1,272.80	11/2012	12/2015	03/2016	3
29	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L PGCIL	1,940.13	1,940.13	09/2014	03/2015	06/2015	3
30	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	12/2014	03/2015	3


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
31	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	03/2015	06/2015	3
32	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID PGCIL	1,935.35	1,935.35	12/2014	11/2014	02/2015	3
33	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,929.15	09/2009	03/2016	07/2016	4
34	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A PGCIL	2,074.86	2,074.86	03/2013	11/2014	03/2015	4
35	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B PGCIL	2,743.19	2,743.19	12/2013	02/2015	06/2015	4
36	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH PGCIL	1,366.34	1,366.34	12/2013	02/2015	06/2015	4
37	KOLDAM HEP (NTPC) NTPC	4,527.15	7,220.00	04/2009	05/2015	10/2015	5
38	TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC	2,978.48	3,846.30	03/2013	00/2018	05/2018	5
39	BONGAIGAON THERMAL POWER PROJECT NTPC	6,749.18	6,749.18	07/2011	08/2016	03/2017	7
40	PARBATI HEP (NHPC) II NHPC	3,919.59	5,366.00	09/2009	07/2018	03/2019	8
41	BARH STPP(3X660MW) NTPC NTPC	8,692.97	15,095.67	12/2009	03/2017	03/2018	12
42	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	721.81	09/2010	12/2014	12/2015	12
43	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,159.07	09/2008	03/2013	03/2016	36
	<u>RAILWAYS</u>						
44	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) NFR	727.56	6,570.75	03/2011	03/2018	03/2019	12
45	NEW COOCHBEHAR TO SAMUKTALA NFR	209.77	441.45	N.A.	03/2017	03/2018	12
46	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT NFR	283.55	288.81	N.A.	03/2017	03/2018	12
47	AMBARI FALAKATA TO NEW MAYNAGURI NFR	312.12	453.10	N.A.	03/2017	03/2018	12
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	733.00	2,531.34	12/2008	03/2016	03/2018	24


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
49	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
50	TIRUPATI - TIRUTHANI - CHENNAI NHAI	571.00	571.00	10/2013	11/2014	12/2014	1
51	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	10/2014	12/2014	2
52	REENGUS SIKAR NHAI	333.51	333.51	09/2014	11/2014	01/2015	2
53	KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	11/2014	11/2015	12
	<u>TELECOMMUNICATIONS</u>						
54	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS BSNL	384.00	384.00	10/2010	03/2015	09/2015	6

Graphical Presentation of All Projects w.r.t. Revised Schedule

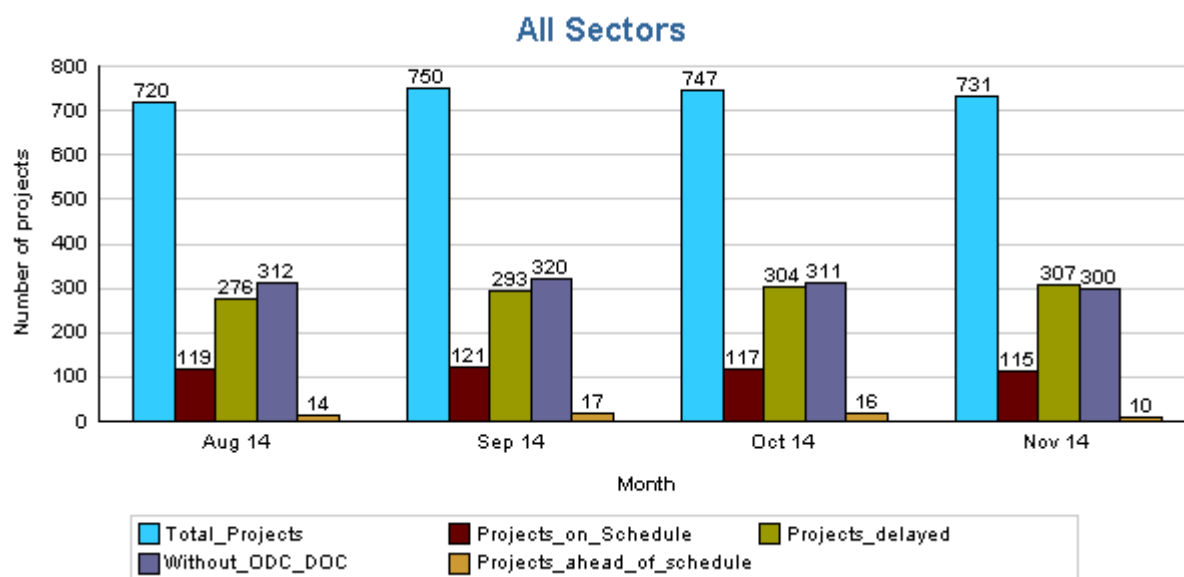


Break-up of 307 Delayed projects in November 2014

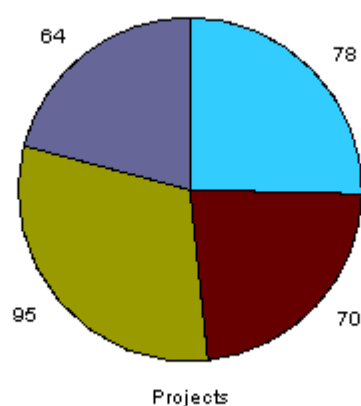


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

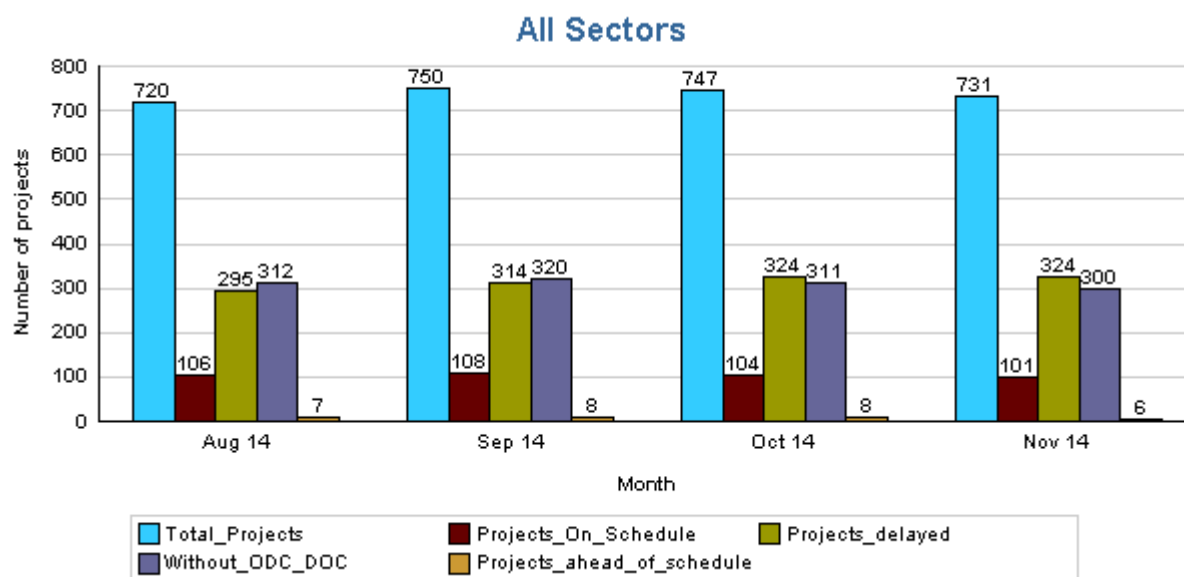

Break-up of 324 Delayed projects in November 2014

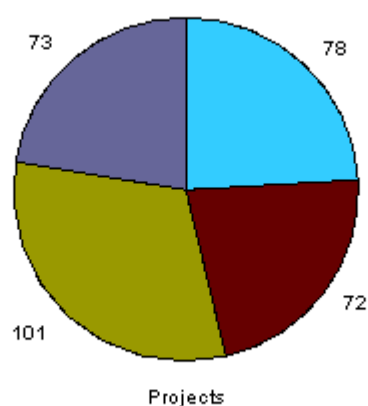


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

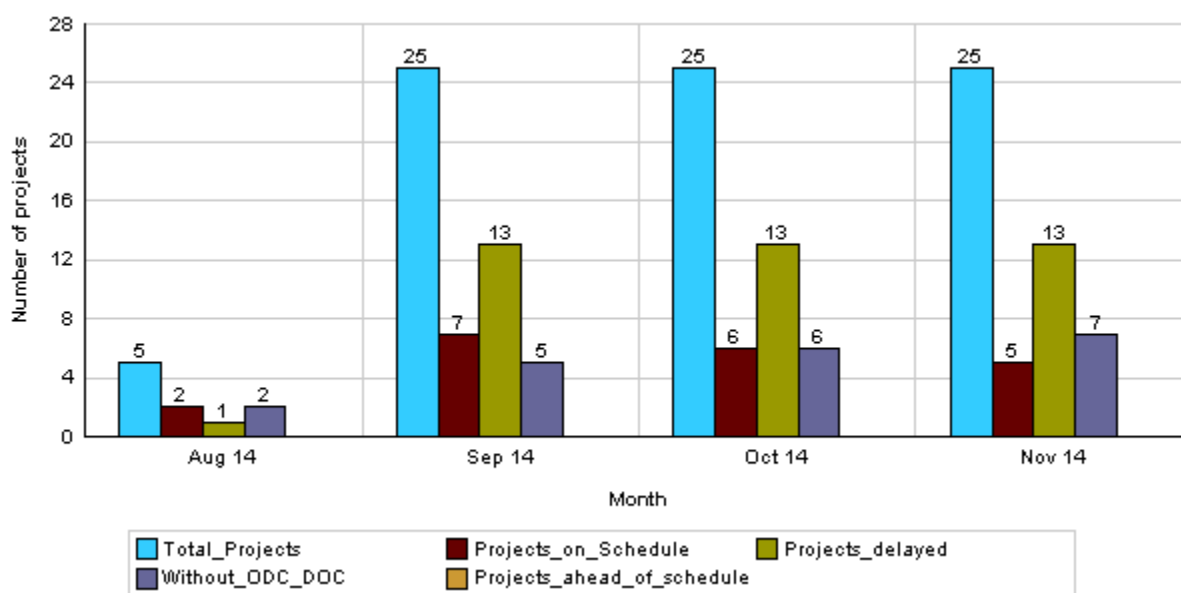


Break-up of 13 Delayed projects in November 2014

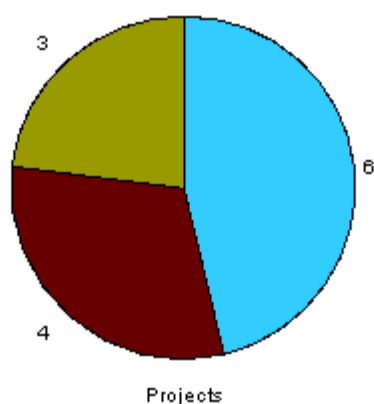


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	6	4	3	0

Graphical Presentation of TELECOMMUNICATIONS Sector

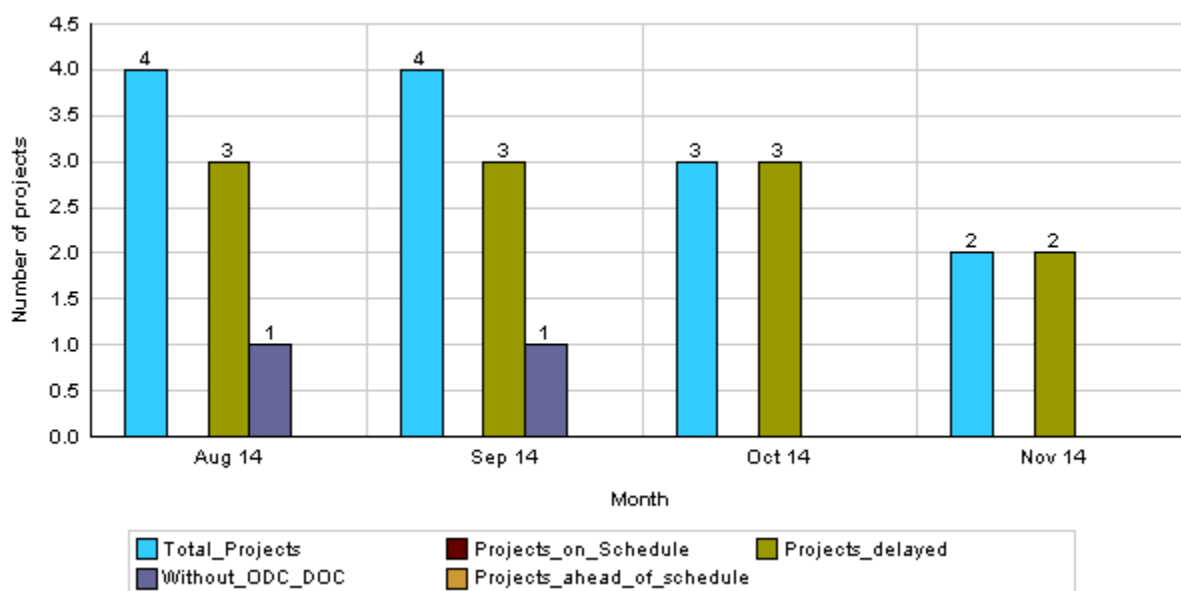


Break-up of 2 Delayed projects in November 2014

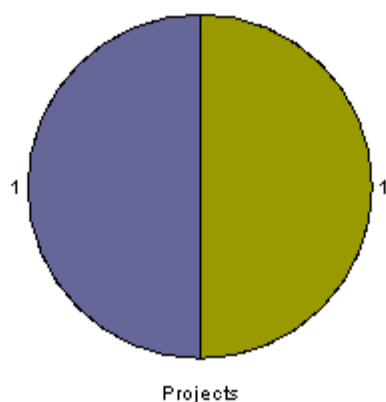


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	1	0	1	0

Graphical Presentation of SHIPPING AND PORTS Sector

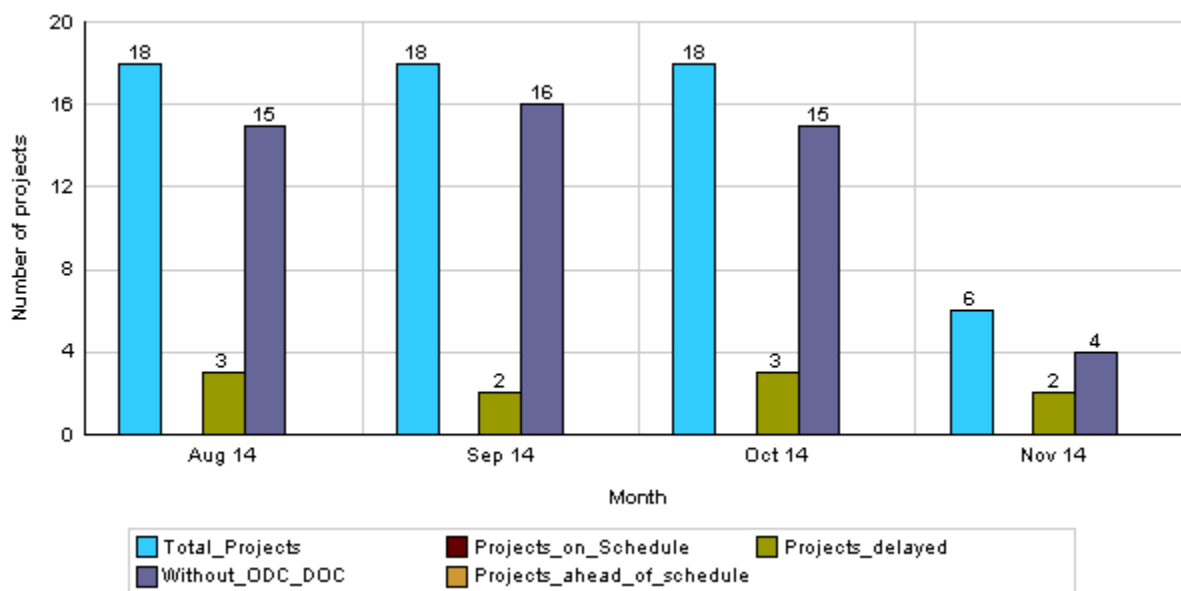


Break-up of 2 Delayed projects in November 2014




Delay in Months

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

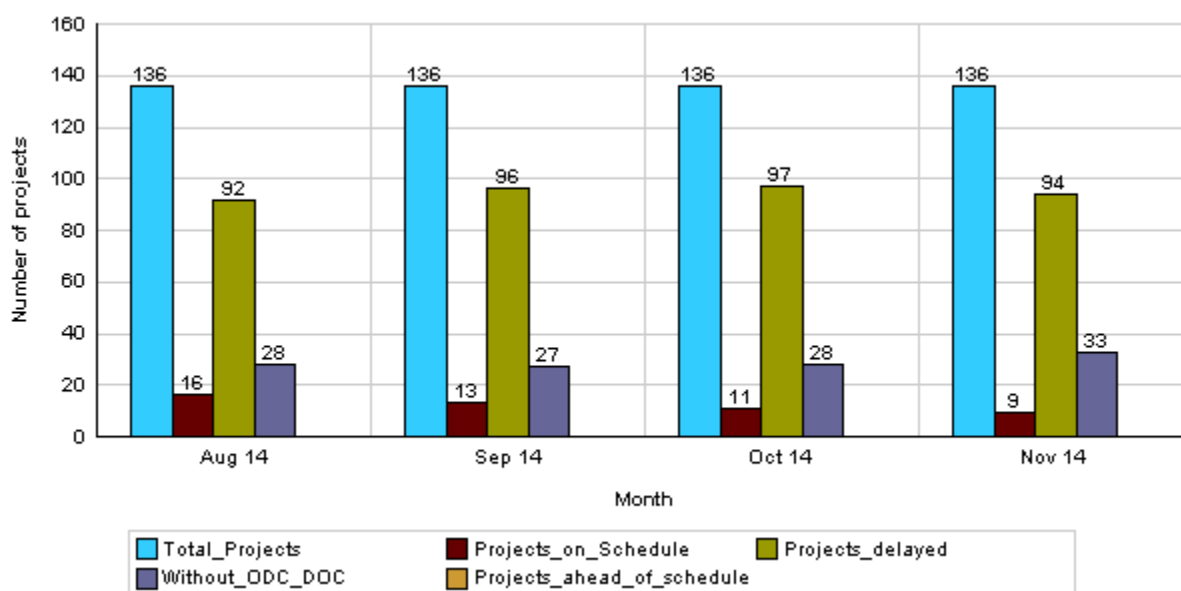


Break-up of 94 Delayed projects in November 2014

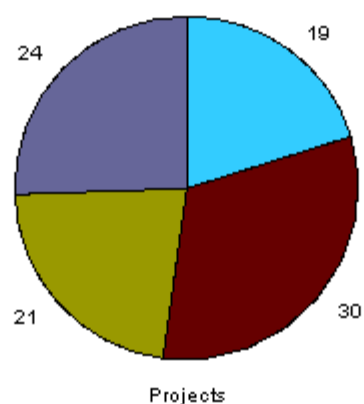


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of RAILWAYS Sector

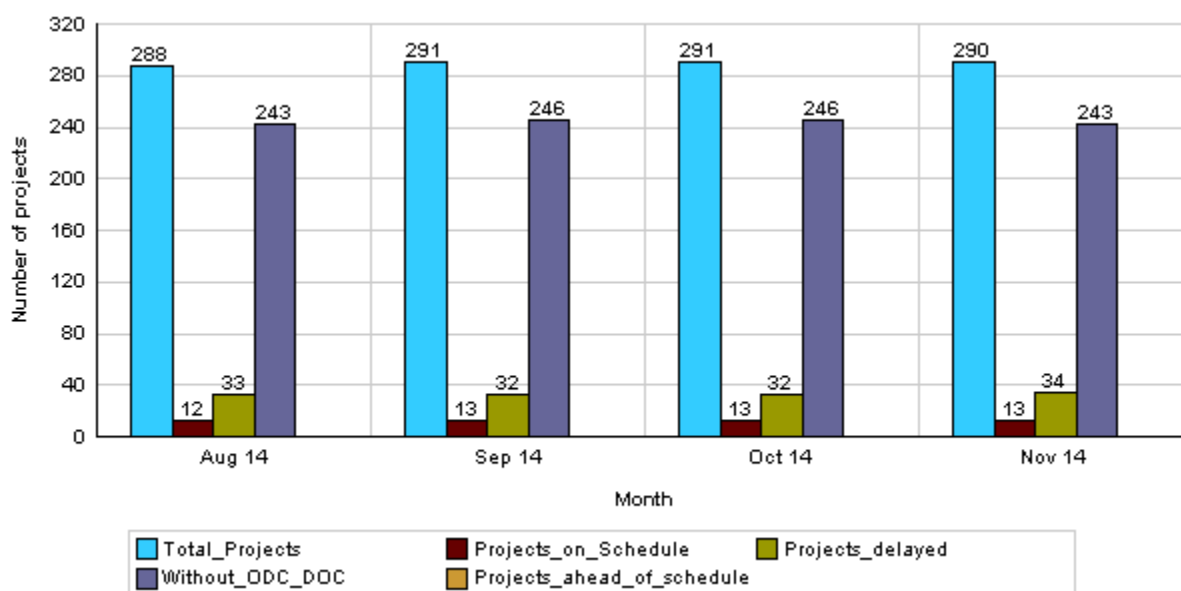


Break-up of 34 Delayed projects in November 2014

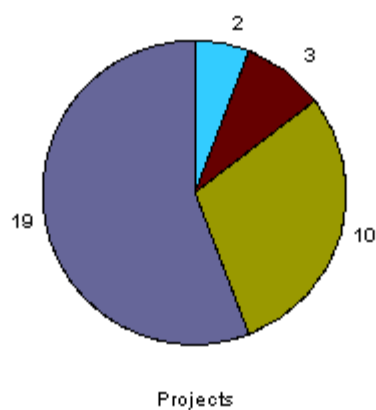


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of POWER Sector

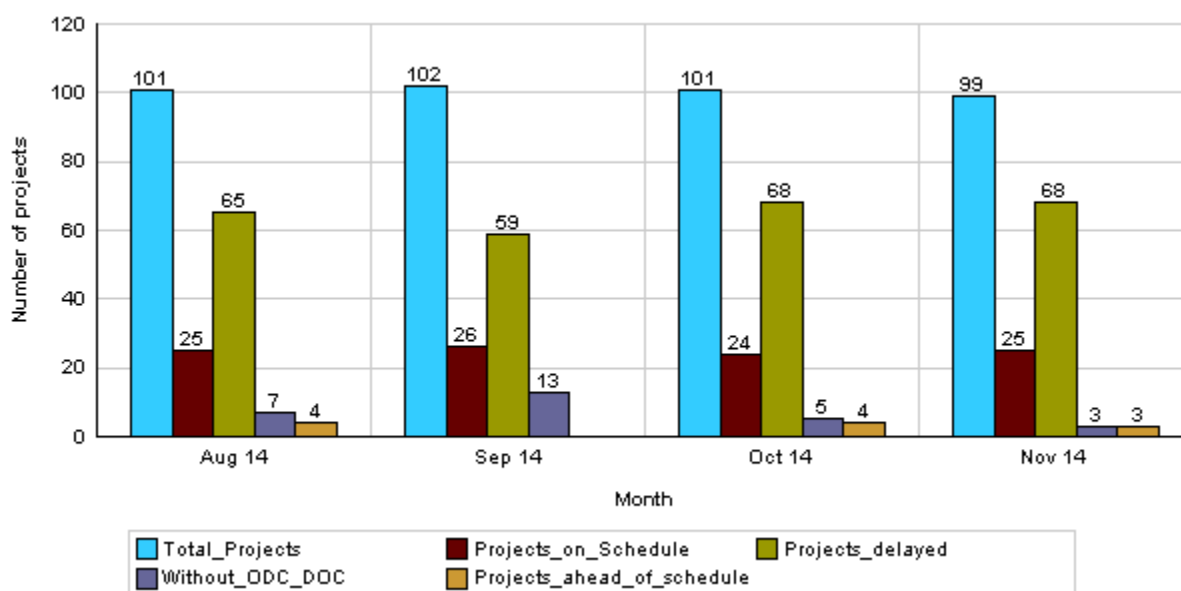


Break-up of 68 Delayed projects in November 2014

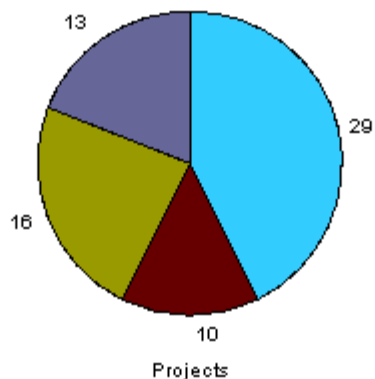


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	29	10	16	13

Graphical Presentation of PETROLEUM Sector

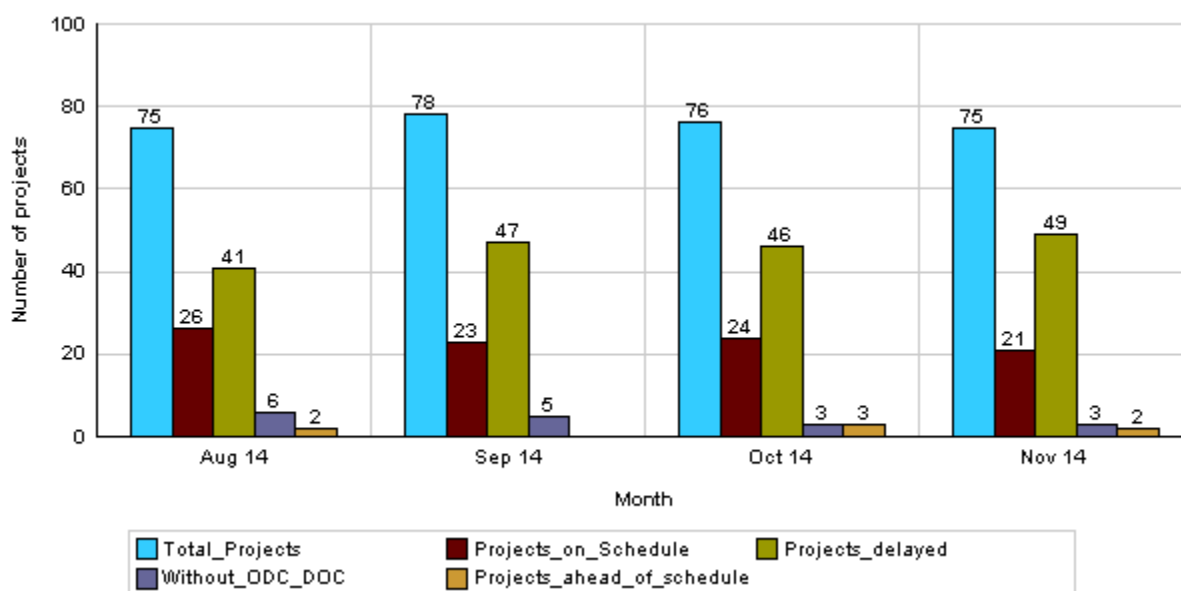


Break-up of 49 Delayed projects in November 2014

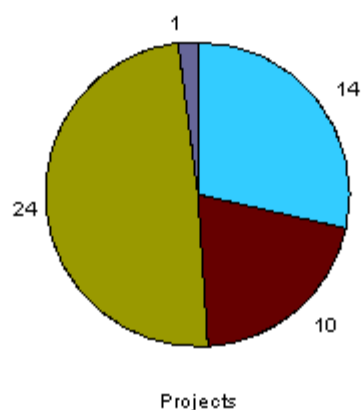


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of STEEL Sector

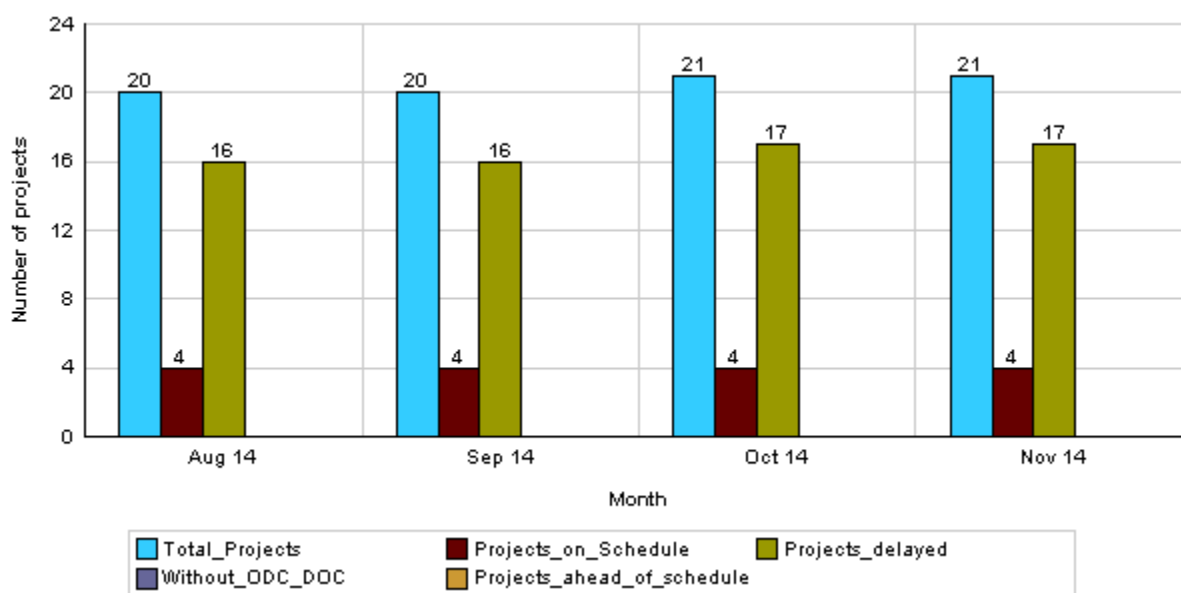


Break-up of 17 Delayed projects in November 2014

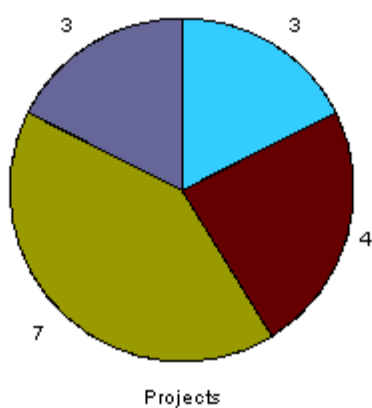


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	3	4	7	3

Graphical Presentation of COAL Sector

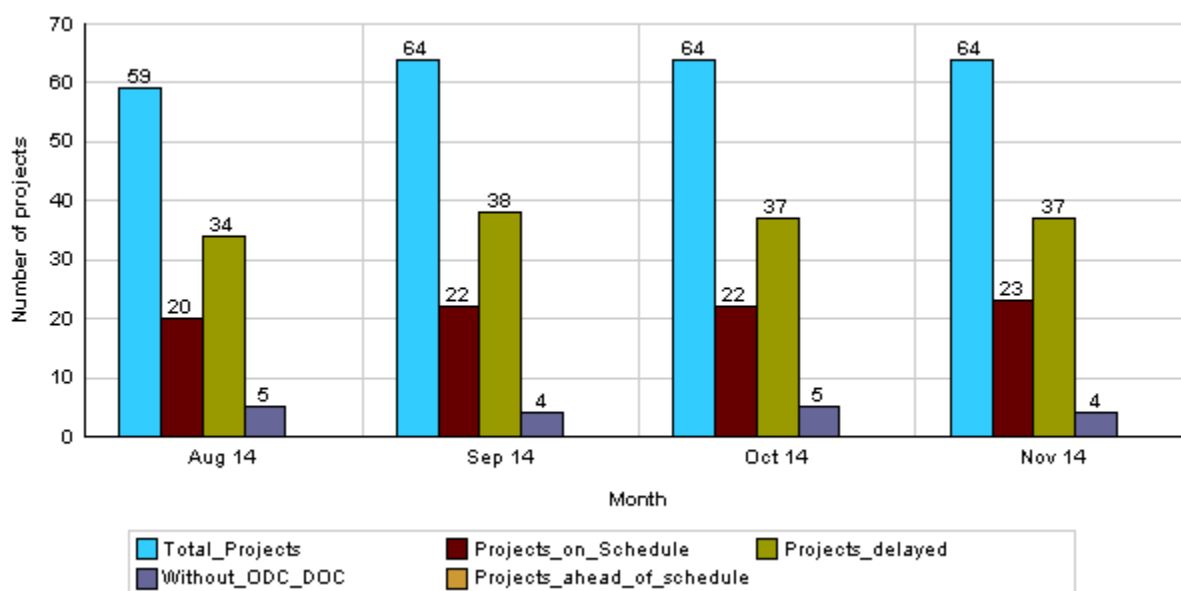


Break-up of 37 Delayed projects in November 2014

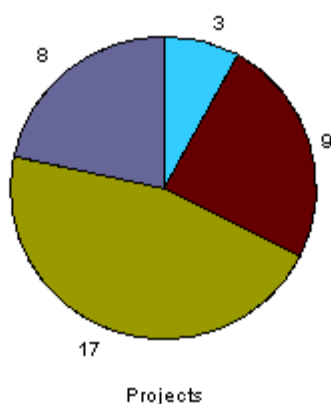


Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

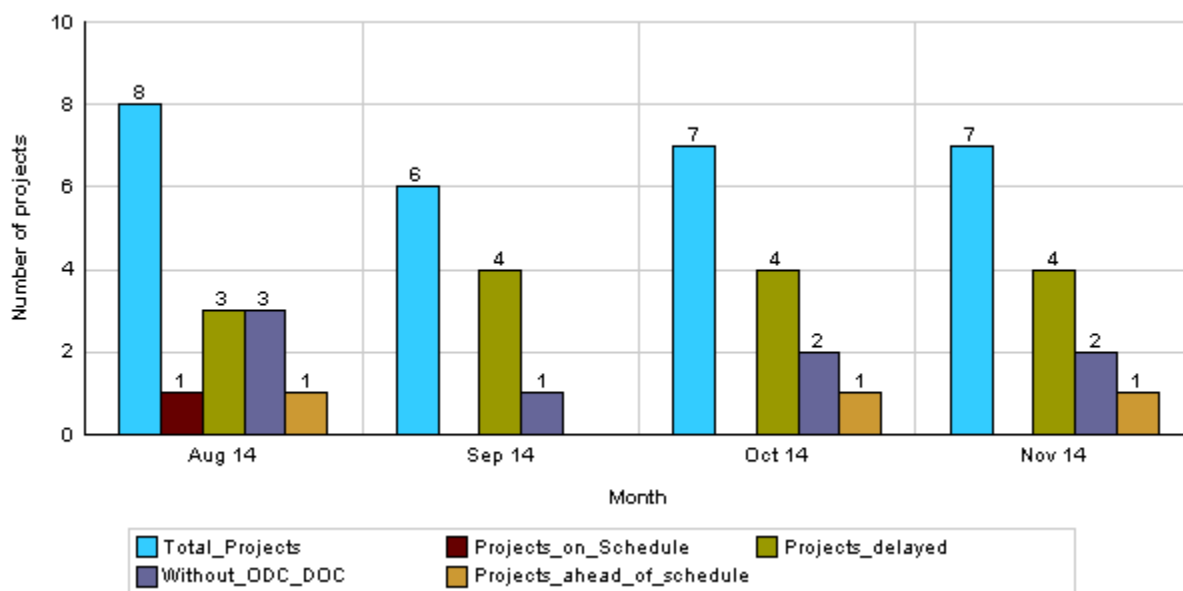


Break-up of 4 Delayed projects in November 2014

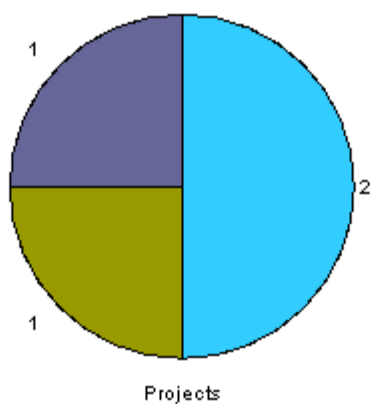


Delay in Months

Delay in Months	Count
1-12	2
13-24	0
25-60	1
MORE THAN 60	1

Graphical Presentation of ATOMIC ENERGY Sector

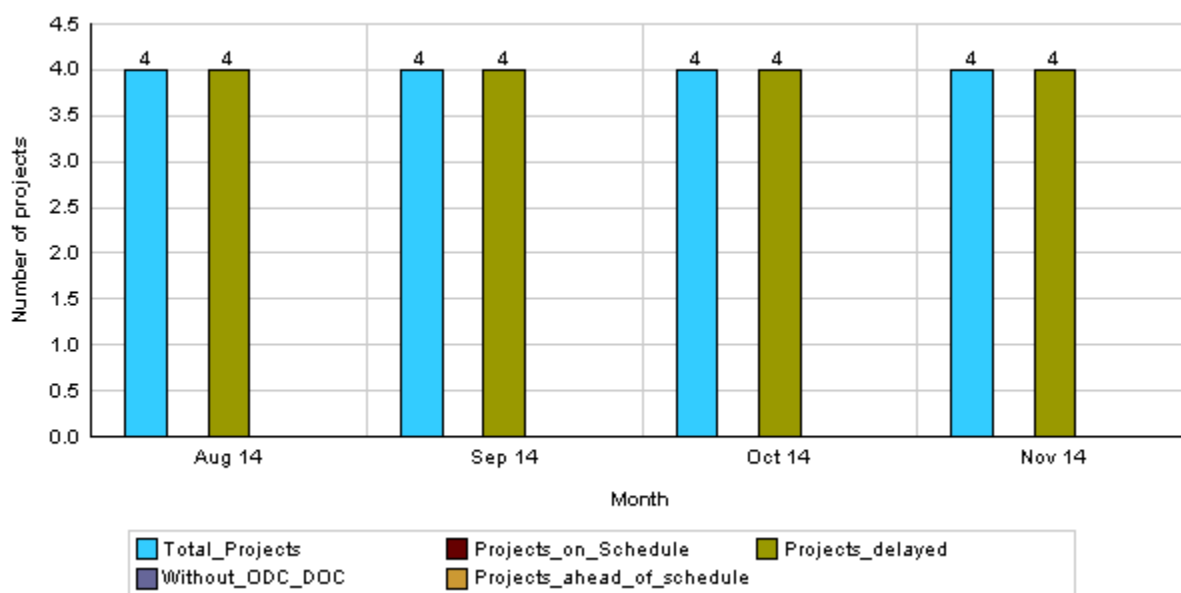

Break-up of 4 Delayed projects in November 2014

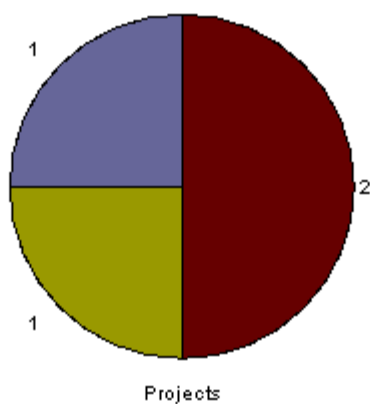

Delay in Months

Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	46,726.00	46,726.00	32,048.19
CIVIL AVIATION	7	2,599.56	2,599.56	2,652.48	1,504.77
COAL	64	46,559.36	50,140.39	56,741.93	19,260.36
FERTILISERS	1	197.79	197.79	197.79	0.00
STEEL	21	81,920.10	85,939.06	87,874.06	64,135.60
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	8,054.80
PETROLEUM	75	165,614.37	182,254.77	182,323.41	80,471.12
POWER	99	241,739.71	257,327.57	273,378.26	145,646.74
RAILWAYS	290	164,135.33	177,495.66	290,709.13	91,721.45
ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	102,692.45	104,391.34	96,990.44
SHIPPING AND PORTS	6	5,356.50	5,747.50	6,468.59	2,020.61
TELECOMMUNICATIONS	2	720.81	720.81	720.81	244.89
URBAN DEVELOPMENT	25	82,686.31	82,745.21	87,959.21	14,916.15
Grand total	731	939,753.89	1,000,047.38	1,149,063.01	557,015.12

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,764.00	12/2015 -	10/2017	22(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	18,034.00	12/2008 10/2013	04/2015	76(O) 18(R)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,754.19	09/2010 03/2015	03/2015	54(O) 0(R)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,496.00	12/2016 -	05/2018	17(O) -	4/69
	Total		40,442.00 -	46,726.00	32,048.19				60/329
	<u>CIVIL AVIATION</u>								
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	316.31	01/2011 04/2013	06/2016	65(O) 38(R)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	16.59	- -	-	-	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	285.20	05/2012 -	12/2014	31(O) -	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	346.36	03/2015 -	02/2015	-1(O) -	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	39.41	03/2014 -	01/2015	10(O) -	0/0
10	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	500.86	06/2013 -	06/2013	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2016	12(O) -	0/0
	Total		2,599.56 -	2,652.48	1,504.77				0/0
	<u>COAL</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	09/2015	30(O) 36(R)	21/22
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016	0(O) -	2/7
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 -	1,143.54	664.83	03/2016 -	03/2016	0(O) -	0/4
15	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	97.75	03/2020 -	03/2020	0(O) -	0/3
16	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	171.46	03/2012 -	03/2017	60(O) -	4/5

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	105.70	03/2011 -	03/2017	72(O) -	0/2
18	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84(O) -	2/4
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	64.72	03/2016 -	03/2016	0(O) -	0/6
20	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	-	03/2019 -	03/2019	0(O) -	1/8
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	184.38	03/2017 -	03/2017	0(O) -	3/11
23	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	22.10	03/2020 -	03/2020	0(O) -	0/0
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	281.79	03/2015 -	03/2015	0(O) -	0/3
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	0/7
26	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.57	03/2014 -	03/2016	24(O) -	2/9
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60(O) -	0/2
28	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,575.92	03/2014 -	03/2016	24(O) -	6/13
29	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,607.26	03/2014 -	03/2016	24(O) -	10/16
30	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	1/12
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	118.51	03/2013 -	03/2017	48(O) -	2/7
32	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	-	03/2019 -	03/2019	0(O) -	2/5
33	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24(O) -	1/7
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/31
35	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
36	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72(O) -	0/15
37	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	105.51	12/2012 -	03/2015	27(O) -	11/44
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.25	07/2016 -	03/2017	8(O) -	3/39
39	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	121.75	03/2013 -	03/2017	48(O) -	3/9
40	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	6.84	04/2017 -	04/2017	0(O) -	0/0
41	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	57.02	03/2014 -	03/2017	36(O) -	0/2
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	43.25	03/2018 -	03/2018	0(O) -	0/4
44	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.30	03/2015 -	03/2018	36(O) -	0/28
45	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	404.65	03/2013 -	03/2015	24(O) -	0/2
46	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	0/5
47	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.34	03/2010 -	03/2017	84(O) -	8/10
48	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	7,612.33	756.25	03/2013 -	03/2023	120(O) -	0/16
49	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44(O) -	0/3
50	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.63	03/2014 -	03/2016	24(O) -	1/6
51	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.22	03/2012 -	03/2016	48(O) -	4/6
52	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
53	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	-	-	0/0
54	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	398.36	12/2015 -	04/2018	28(O) -	10/35
55	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	7.45	03/2012 -	03/2015	36(O) -	0/2
56	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	6.84	03/2021 -	03/2021	0(O) -	0/0
57	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60(O) -	0/2
58	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	0.46	03/2015 -	03/2015	0(O) -	1/1
59	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.68	03/2014 -	03/2020	72(O) -	0/1
60	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	150.58	03/2013 -	03/2015	24(O) -	1/3
61	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	44.90	03/2014 -	03/2016	24(O) -	0/9
62	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	223.58	03/2016 -	03/2016	0(O) -	0/2
63	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	230.86	03/2012 -	-	-	24/27
64	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
65	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	430.14	68.12	03/2016 -	03/2016	0(O) -	6/48
66	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9(O) -	3/51
67	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	70.54	03/2015 -	03/2015	0(O) -	8/31

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	72.68	03/2012 -	-	-	25/42
69	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026	0(O) -	3/14
70	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	43.38	03/2018 -	03/2018	0(O) -	0/10
71	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	0/11
72	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	145.03	03/2012 -	03/2016	48(O) -	0/2
73	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,080.25	06/2009 03/2013	12/2014	66(O) 21(R)	21/23
74	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,693.37	03/2012 05/2014	02/2015	35(O) 9(R)	25/39
75	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	104.95	10/2014 -	01/2015	3(O) -	3/11
	Total		46,559.36 -	56,741.93	19,260.36				233/862
	<u>FERTILISERS</u>								
76	SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	197.79	-	02/2017 -	02/2017	0(O) -	0/0
	Total		197.79 -	197.79	.00				0/0
	<u>STEEL</u>								
77	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	414.19	04/2013 09/2014	06/2015	26(O) 9(R)	17/18
78	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	20.22	05/2016 -	05/2016	0(O) -	1/3
79	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	351.41	05/2013 01/2015	08/2015	27(O) 7(R)	14/20
80	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	335.82	09/2009 05/2012	06/2015	69(O) 37(R)	1/1
81	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	380.27	12/2011 01/2015	03/2015	39(O) 2(R)	17/20
82	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	167.28	09/2008 12/2013	12/2014	75(O) 12(R)	3/4
83	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	153.60	08/2014 -	06/2015	10(O) -	3/4
84	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	8.28	04/2015 -	04/2015	0(O) -	0/3
85	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	116.37	11/2013 -	06/2015	19(O) -	2/4
86	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,679.23	03/2013 -	09/2015	30(O) -	30/35
87	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,904.43	12/2011 -	06/2015	42(O) -	19/24

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,418.78	12/2012 -	05/2015	29(O) -	15/20
89	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,541.89	12/2011 -	03/2015	39(O) -	25/29
90	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,092.76	10/2009 10/2012	03/2015	65(O) 29(R)	68/68
91	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,627.12	03/2013 -	03/2015	24(O) -	18/20
92	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	142.27	10/2013 -	08/2015	22(O) -	2/5
93	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	102.83	09/2014 -	06/2015	9(O) -	0/2
94	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	1,384.00	05/2015 -	12/2016	19(O) -	6/78
95	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	154.50	06/2015 -	06/2015	0(O) -	2/3
96	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	109.08	12/2014 -	08/2015	8(O) -	0/2
97	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	31.27	04/2016 -	04/2016	0(O) -	0/2
	Total		81,920.10 -	87,874.06	64,135.60				243/365
	<u>PETROCHEMICALS</u>								
98	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 -	8,920.00	8,054.80	04/2012 -	-	-	22/29
	Total		5,460.61 -	8,920.00	8,054.80				22/29
	<u>PETROLEUM</u>								
99	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	12/2014	30(O) -	0/3
100	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/0
101	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36(O) -	0/0
102	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,040.60	12/2014 -	12/2018	48(O) -	0/0
103	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 -	2,378.89	1,711.73	03/2013 03/2015	03/2016	36(O) 12(R)	0/5
104	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	208.21	08/2015 -	12/2015	4(O) -	0/12
105	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 204.29	204.29	155.32	06/2012 09/2013	12/2014	30(O) 15(R)	0/0
106	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL, ANDHRA PRADESH	07/2014	419.04 -	762.00	2.89	01/2017 -	01/2017	0(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	470.29	09/2011 -	12/2015	51(O) -	0/0
108	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21(O) -	0/5
109	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	107.05	09/2012 -	04/2015	31(O) -	0/0
110	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 -	11/2017	46(O) -	0/5
111	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
112	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	673.97	05/2013 06/2014	03/2015	22(O) 9(R)	0/5
113	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	111.19	09/2013 -	02/2015	17(O) -	0/1
114	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,071.91	- -	12/2015	- -	0/12
115	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 04/2016	06/2015	110(O) -10(R)	0/0
116	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,867.78	08/2010 03/2012	05/2015	57(O) 38(R)	0/10
117	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	364.21	05/2014 -	03/2016	22(O) -	0/9
118	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,306.51	03/2013 11/2014	12/2014	21(O) 1(R)	0/10
119	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
120	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	249.01	12/2014 -	05/2015	5(O) -	0/8
121	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23(O) -	0/9
122	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	12/2014	2(O) -	0/0
123	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	11/2014	38(O) 32(R)	59/59
124	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	42.27	09/2017 -	09/2017	0(O) -	0/0
125	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	4.00	- -	-	-	0/0
126	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	186.43	10/2011 12/2014	12/2014	38(O) 0(R)	0/9
127	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]GAIL,GUJARAT	07/2014	716.00 -	716.00	-	01/2017 -	01/2017	0(O) -	0/0
128	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,027.35	05/2015 -	05/2015	0(O) -	0/17
129	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	6.07	07/2016 -	07/2016	0(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.15	03/2015 -	05/2015	2(O) -	0/12
131	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.27	02/2016 04/2017	04/2017	14(O) 0(R)	0/0
132	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 -	04/2016	0(O) -	0/0
133	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 -	16,504.00	4,032.33	05/2016 -	05/2016	0(O) -	0/18
134	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	99.82	03/2014 -	04/2015	13(O) -	0/5
135	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0
136	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,324.96	12/2012 -	06/2015	30(O) -	0/14
137	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.27	183.65	12/2015 -	03/2015	-9(O) -	0/66
138	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	49.94	01/2016 -	01/2016	0(O) -	0/0
139	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 701.00	701.00	335.61	11/2015 -	11/2015	0(O) -	23/29
140	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	154.93	07/2013 -	02/2015	19(O) -	0/0
141	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32(O) -	0/0
142	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 -	5,706.47	0.28	05/2017 -	05/2017	0(O) -	0/0
143	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	109.49	12/2014 -	02/2015	2(O) -	0/57
144	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	-	-	-	0/0
145	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	346.39	07/2015 -	12/2015	5(O) -	0/0
146	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	27,513.95	11/2012 11/2013	03/2015	28(O) 16(R)	74/100
147	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,035.09	09/2012 -	03/2016	42(O) -	6/7
148	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	7,155.15	02/2014 -	12/2014	10(O) -	0/0
149	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	36.33	07/2016 -	07/2016	0(O) -	0/5
150	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.28	05/2014 -	05/2015	12(O) -	0/5
151	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
152	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	995.25	07/2012 -	12/2014	29(O) -	0/31
153	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 03/2016	03/2016	15(O) 0(R)	0/0
154	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	686.58	194.35	04/2015 -	04/2015	0(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
155	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	965.03	12/2014 -	03/2015	3(O) -	0/20
156	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	3.32	02/2016 -	07/2016	5(O) -	0/0
157	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	319.32	11/2015 -	11/2015	0(O) -	0/52
158	RESITEMENT OF BILASPUR AND BISRAMPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 219.08	219.00	101.65	09/2016 -	12/2015	-9(O) -	0/12
159	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.00	57.96	05/2015 -	12/2015	7(O) -	0/12
160	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.50	05/2016 -	05/2016	0(O) -	0/0
161	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	1.94	03/2014 -	07/2016	28(O) -	0/0
162	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	794.82	11/2015 -	11/2015	0(O) -	14/25
163	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	352.56	10.60	03/2017 -	03/2017	0(O) -	0/0
164	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	901.28	10/2011 -	10/2015	48(O) -	0/0
165	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,316.95	01/2012 -	10/2015	45(O) -	0/0
166	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	999.73	10/2011 -	02/2015	40(O) -	0/0
167	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.52	04/2015 -	04/2015	0(O) -	0/0
168	TWENTY NOS. FEEDER GAS LINES - [N16000192]AAI,ASSAM	03/2009	228.64 -	228.64	-	12/2016 -	12/2016	0(O) -	0/0
169	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	221.08	08/2012 -	03/2015	31(O) -	0/5
170	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	68.23	03/2015 11/2015	11/2015	8(O) 0(R)	0/5
171	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	94.94	10/2014 -	10/2015	12(O) -	0/0
172	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	271.39	06/2011 -	03/2015	45(O) -	13/20
173	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	579.52	12/2013 05/2014	12/2014	12(O) 7(R)	69/69
	Total		165,614.37 -	182,323.41	80,471.12				258/748
	<u>POWER</u>								
174	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,408.16	08/2012 -	12/2014	28(O) -	2/11

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	285.27	- 03/2015	03/2015	- 0(R)	6/17
176	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2(O) -	0/0
177	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	83.96	10/2014 -	12/2014	2(O) -	5/7
178	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,111.00	08/2013 -	03/2015	19(O) -	15/20
179	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	09/2010	8,692.97 15,095.67	15,095.67	10,410.00	12/2009 -	03/2018	99(O) -	24/46
180	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,851.00	07/2011 -	03/2017	68(O) -	9/34
181	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	288.75	12/2015 -	12/2015	0(O) -	6/19
182	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,529.56	09/2014 -	06/2015	9(O) -	10/19
183	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	658.43	06/2015 -	06/2015	0(O) -	0/0
184	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	0/20
185	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	3/7
186	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	85.63	10/2014 -	02/2015	4(O) -	2/14
187	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	-	02/2016 -	02/2016	0(O) -	0/7
188	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	920.43	11/2012 -	03/2016	40(O) -	1/12
189	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	49.24	05/2016 -	04/2016	-1(O) -	1/20
190	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
191	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	13.30	09/2014 -	06/2016	21(O) -	0/0
192	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,561.05	05/2014 -	03/2015	10(O) -	2/11
193	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,659.00	09/2017 -	12/2017	3(O) -	16/39
194	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	765.90	08/2014 -	03/2015	7(O) -	3/15

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
195	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0
196	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	200.10	11/2016 -	03/2016	-8(O) -	2/17
197	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	952.31	12/2007 12/2009	03/2016	99(O) 75(R)	1/10
198	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 4,653.95	4,653.95	3,460.15	12/2009 03/2017	03/2017	87(O) 0(R)	12/29
199	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,755.33	01/2016 -	11/2016	10(O) -	4/6
200	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,248.00	04/2009 -	10/2015	78(O) -	3/9
201	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	5,698.00	12/2016 -	05/2017	5(O) -	21/24
202	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 -	03/2016	90(O) -	14/23
203	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	2,276.00	05/2017 -	06/2017	1(O) -	17/37
204	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	146.00	08/2017 -	03/2018	7(O) -	0/9
205	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,212.00	09/2016 -	06/2017	9(O) -	21/25
206	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,603.50	08/2013 -	03/2016	31(O) -	0/17
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	2/20
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	443.02	07/2013 -	03/2015	20(O) -	1/10
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	304.27	02/2012 -	03/2016	49(O) -	0/13
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	420.06	11/2011 -	03/2016	52(O) -	1/13
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	2.00	06/2016 -	06/2016	0(O) -	5/20
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,094.32	04/2013 -	03/2016	35(O) -	0/11
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	453.22	11/2014 -	03/2015	4(O) -	3/16
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	75.99	03/2016 -	03/2016	0(O) -	2/17
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	435.09	03/2015 -	03/2015	0(O) -	5/17
216	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	159.02	04/2015 -	05/2015	1(O) -	1/18
217	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	702.64	11/2012 -	03/2016	40(O) -	0/11
218	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
219	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,755.06	09/2009 -	03/2019	114(O) -	6/12
220	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	928.87	08/2013 -	09/2015	25(O) -	22/37
221	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	3,288.28	3,329.96	03/2012 -	11/2014	32(O) -	22/28
222	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,419.00	11/2016 -	11/2017	12(O) -	16/20
223	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	08/2016 -	08/2016	0(O) -	0/0
224	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	1/7
225	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/0
226	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,035.90	09/2010 -	12/2018	99(O) -	0/0
227	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,145.81	08/2012 -	12/2014	28(O) -	3/6
228	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	409.98	06/2016 -	12/2015	-6(O) -	0/19
229	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	-	02/2017 -	02/2017	0(O) -	0/0
230	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	187.19	06/2012 -	-	-	1/3
231	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35 -	1,935.35	929.48	12/2014 -	02/2015	2(O) -	7/13
232	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	170.74	03/2014 -	12/2014	9(O) -	5/7
233	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	621.33	08/2014 -	05/2015	9(O) -	1/17
234	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,033.99	08/2012 -	03/2015	31(O) -	0/6
235	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	11.00	08/2016 -	08/2016	0(O) -	2/20
236	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	924.13	02/2015 -	02/2015	0(O) -	3/14
237	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014	0(O) -	0/15
238	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	844.52	01/2015 -	06/2015	5(O) -	3/20
239	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	249.97	08/2014 -	02/2015	6(O) -	9/19
240	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	315.32	06/2014 -	03/2015	9(O) -	8/19

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
241	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,272.00	03/2013 -	05/2018	62(O) -	0/14
242	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,571.21	09/2009 -	07/2016	82(O) -	2/5
243	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	957.43	07/2010 02/2016	05/2018	94(O) 27(R)	5/15
244	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	178.42	01/2014 -	12/2014	11(O) -	4/16
245	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,287.86	08/2014 -	06/2015	10(O) -	2/19
246	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,882.21	10/2014 -	06/2015	8(O) -	3/17
247	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,000.58	10/2012 -	03/2016	41(O) -	0/11
248	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	04/2017 -	04/2017	0(O) -	0/0
249	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,926.30	12/2012 -	12/2015	36(O) -	0/11
250	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	0/0
251	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	-	03/2018 -	03/2018	0(O) -	0/0
252	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	891.45	01/2015 -	12/2015	11(O) -	7/21
253	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	11.20	10/2016 -	10/2016	0(O) -	0/20
254	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,370.47	10/2014 -	01/2015	3(O) -	4/15
255	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	135.70	05/2016 -	05/2016	0(O) -	1/18
256	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	457.70	02/2014 -	06/2015	16(O) -	5/16
257	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,163.26	12/2013 -	06/2015	18(O) -	7/12
258	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	345.71	11/2013 -	03/2015	16(O) -	7/20
259	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,698.44	03/2013 -	03/2015	24(O) -	5/14

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
260	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,605.17	03/2014 -	03/2015	12(O) -	5/14
261	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,474.00	12/2013 -	06/2015	18(O) -	2/12
262	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	85.00	01/2013 -	06/2015	29(O) -	5/21
263	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,361.96	11/2013 -	06/2015	19(O) -	4/15
264	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,452.17	11/2012 -	03/2015	28(O) -	0/10
265	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,028.33	07/2014 -	06/2015	11(O) -	2/13
266	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	842.77	07/2013 08/2014	11/2014	16(O) 3(R)	24/25
267	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 913.63	913.63	694.14	07/2006 12/2015	12/2015	113(O) 0(R)	2/13
268	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
269	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	1,355.00	08/2015 -	08/2015	0(O) -	20/20
270	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	509.51	07/2014 -	07/2018	48(O) -	1/2
271	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	508.99	09/2010 -	12/2015	63(O) -	0/7
272	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	3,020.29	06/2015 -	12/2015	6(O) -	4/28
	Total		241,739.71 -	273,378.26	145,646.74				450/1396
	<u>RAILWAYS</u>								
273	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	29.40	04/2012 03/2016	03/2018	71(O) 24(R)	0/0
274	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	184.06	7.83	- -	-	-	0/0
275	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.00	2,876.00	781.37	03/2014 -	03/2018	48(O) -	0/0
276	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	888.65	-	- -	03/2018	-	0/0
277	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	416.44	12/2009 03/2011	12/2014	60(O) 45(R)	0/0
278	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	17.33	- -	-	-	0/0
279	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	79.99	03/2013 -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.34	- -	-	-	0/0
281	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	23.91	- -	-	-	0/0
282	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
283	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
284	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 303.00	485.00	417.70	03/2011 -	-	-	0/0
285	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
286	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	122.62	- -	-	-	0/0
287	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.00	453.10	130.83	- -	03/2018	-	0/0
288	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	575.02	06/1999 -	-	-	0/0
289	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.81	- -	-	-	0/0
290	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
291	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
292	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
293	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
294	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
295	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	73.18	- -	-	-	0/0
296	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	71.73	- -	-	-	0/0
297	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	9.60	- -	-	-	0/0
298	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	04/2015	28(O) -	0/0
299	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	1,382.78	0.82	- -	-	-	0/0
300	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	2.95	- -	-	-	0/0
301	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	482.43	03/2005 12/2008	12/2017	153(O) 108(R)	0/0
302	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
303	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	13.53	- -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
304	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
305	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,803.17	396.47	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
306	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	337.49 -	337.50	8.38	- -	-	-	0/0
307	BHADRACHALAM-KOVVUR - [N22000264]SCR, MULTI STATE	04/2012	923.23 -	923.23	0.36	- -	-	-	0/0
308	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	837.33	0.84	- -	-	-	0/0
309	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	760.00	0.09	- -	-	-	0/0
310	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.00	2,820.25	195.01	04/2014 03/2020	03/2018	47(O) -24(R)	0/0
311	BHANUPALI-BILASPUR BERI NL - [N22000273]NR, HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
312	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	196.95	198.77	03/2011 -	-	-	0/0
313	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	195.64	87.46	- -	-	-	0/0
314	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69(O) -	0/0
315	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	2.37	03/2012 -	-	-	0/0
316	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
317	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0
318	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	434.00	35.28	- -	-	-	0/0
319	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,366.02	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
320	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
321	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	66.14	03/2015 -	12/2016	21(O) -	0/0
322	CHANDIGARH-BADDI NL - [N22000296]NR, MULTI STATE	04/2007	328.14 -	328.14	0.17	- -	-	-	0/0
323	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER, MULTI STATE	04/2003	337.96 -	337.96	61.36	- -	-	-	0/0
324	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	605.94	- -	03/2015	-	0/0
325	CHENGANNUR-CHINGAVANAM - [N22000203]SR, KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
326	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU	04/1998	271.24 -	520.00	462.44	- -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
327	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.07	- -	-	-	0/0
328	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.08	- -	-	-	0/0
329	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	107.03	- -	-	-	0/0
330	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
331	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
332	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	28.02	- -	-	-	0/0
333	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
334	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
335	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
336	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	161.63	- -	-	-	0/0
337	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
338	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,001.72	03/2007 -	03/2016	108(O) -	0/0
339	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
340	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
341	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	177.92	- -	-	-	0/0
342	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
343	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	968.60	142.11	12/2012 -	-	-	0/0
344	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	124.46	12/2015 -	03/2016	3(O) -	0/0
345	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	406.92	153.62	- -	-	-	0/0
346	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
347	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.20	- -	-	-	0/0
348	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	256.24	- -	-	-	0/0
349	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	234.71	116.12	03/2015 -	03/2015	0(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
350	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
351	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	143.30	- -	-	-	0/0
352	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
353	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	2.67	- -	-	-	0/0
354	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	4.66	02/2019 -	02/2019	0(O) -	0/0
355	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.25	- -	-	-	0/0
356	DIMPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	-	-	0/0
357	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	826.55	- -	03/2015	- -	0/0
358	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016	0(O) -	0/0
359	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36(O) 15(R)	0/0
360	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
361	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
362	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	235.70	12/2008 -	12/2014	72(O) -	0/0
363	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	289.04	06/2013 06/2013	-	-	0/0
364	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
365	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	0.86	- -	-	-	0/0
366	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	304.36	02/2011 02/2011	-	-	0/0
367	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.98	- -	-	-	0/0
368	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
369	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
370	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
371	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	151.15	02/2006 -	12/2015	118(O) -	0/0
372	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	04/1997	863.23 -	1,072.51	882.87	- -	03/2015	- -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
373	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
374	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.29	- -	-	-	0/0
375	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
376	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	630.94	- 05/2009	03/2015	- 70(R)	0/0
377	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	595.67	03/1994 -	10/2014	-	0/0
378	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	179.32	20.56	- -	-	-	0/0
379	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.03	02/2020 -	02/2020	0(O) -	0/0
380	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
381	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	367.17	9.98	- -	-	-	0/0
382	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	214.34	- -	-	-	0/0
383	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
384	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
385	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	321.71	- 09/2009	-	-	0/0
386	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	1.74	- -	-	-	0/0
387	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
388	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	983.58	- -	-	-	0/0
389	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	170.55	- -	-	-	0/0
390	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	79.26	03/2015 -	03/2015	0(O) -	0/0
391	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
392	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	101.80	- -	-	-	0/0
393	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	47.50	- -	-	-	0/0
394	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
395	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.23	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
396	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
397	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	108.42	- -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
398	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	221.31	01/1999 -	-	-	0/0
399	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	244.85	03/2014 -	-	-	0/0
400	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	142.23	- -	-	-	0/0
401	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	831.24	06/2007 -	-	-	0/0
402	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	1,043.56	756.33	03/2012 -	-	-	0/0
403	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	14.00	- -	-	-	0/0
404	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	230.00	218.58	- -	-	-	0/0
405	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	588.78	03/2012 03/2012	12/2012	-	0/0
406	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,676.64	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
407	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.02	- -	-	-	0/0
408	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
409	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
410	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.40	- -	-	-	0/0
411	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,615.26	- -	03/2015	-	0/0
412	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
413	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	571.84	- -	03/2016	-	1/1
414	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	779.90	- -	-	-	0/0
415	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	178.21	12/2012 -	03/2016	39(O) -	0/0
416	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	744.08	12/2010 -	03/2018	87(O) -	0/0
417	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	215.50	03/2017 -	03/2017	0(O) -	0/0
418	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	7.25	- -	-	-	0/0
419	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	162.87	136.88	- -	-	-	0/0
420	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	282.06	03/2009 03/2009	08/2014	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
421	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	338.16	- -	-	-	0/0
422	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	184.11	- -	03/2018	-	0/0
423	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 283.00	565.13	2.63	- -	03/2018	-	0/0
424	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	560.90	- 03/2010	03/2010	-	0/0
425	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,845.29	07/2005 -	-	-	0/0
426	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	236.16	- -	-	-	0/0
427	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
428	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	297.88	03/2012 -	-	-	0/0
429	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,045.20	0.03	- -	-	-	0/0
430	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
431	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
432	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
433	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
434	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	479.55	05/2008 -	-	-	0/0
435	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
436	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	364.06	0.30	- -	03/2019	-	0/0
437	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,610.58	03/2009 -	03/2016	84(O) -	0/0
438	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.19	07/2008 -	07/2008	-	0/0
439	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.16	- -	-	-	0/0
440	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.63	- -	-	-	0/0
441	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
442	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	214.79	- -	-	-	0/0
443	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
444	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
445	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	1.75	- -	12/2017	- -	0/0
446	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	105.34	- -	-	-	0/0
447	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	477.90	03/2012 -	-	-	0/0
448	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
449	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	2.32	01/1999 -	-	-	0/0
450	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.69	- -	-	-	0/0
451	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	452.94	- -	-	-	0/0
452	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	3.53	- -	-	-	0/0
453	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
454	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
455	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
456	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	- -	-	-	0/0
457	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.51	- -	-	-	0/0
458	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.30	- -	-	-	0/0
459	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,913.27	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
460	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	307.38	- -	12/2014	- -	0/0
461	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	318.57	- -	-	-	0/0
462	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 166.00	435.58	0.56	- -	03/2018	- -	0/0
463	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
464	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	0.02	- -	-	-	0/0
465	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	4.76	- -	-	-	0/0
466	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	739.76	02/2009 -	03/2012	-	0/0
467	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	1,036.78	404.01	07/2012 -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
468	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
469	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
470	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
471	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	209.48	- -	03/2017	- -	0/0
472	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	39.78	- -	03/2018	- -	0/0
473	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.64	- -	03/2020	- -	0/0
474	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NFR,MULTI STATE	04/1999	175.43 -	275.00	247.90	- -	-	-	0/0
475	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	- -	0/0
476	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.00	563.13	21.95	- -	03/2019	- -	0/0
477	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	1,336.57	255.54	- -	03/2019	- -	0/0
478	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
479	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.00	441.45	87.56	- -	03/2018	- -	0/0
480	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.00	288.81	11.74	- -	03/2018	- -	0/0
481	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 390.00	1,653.55	1,038.91	- -	03/2018	- -	0/0
482	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.34	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
483	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,723.76	12/2008 -	03/2018	111(O) -	0/0
484	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	71.96	03/2014 -	03/2016	24(O) -	0/0
485	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.51	500.80	03/2016 -	03/2016	0(O) -	0/0
486	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	128.62	03/2016 -	06/2016	3(O) -	0/0
487	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 4,259.48	4,259.48	542.29	03/2016 -	03/2016	0(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
488	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,117.11	459.60	03/2008 06/2008	-	-	0/0
489	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
490	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
491	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	260.16	237.08	- -	01/2015	- -	0/0
492	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,307.00	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
493	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	925.30	704.31	- -	02/2014	-	0/0
494	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	203.00	223.52	- -	03/2015	- -	0/0
495	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
496	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
497	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	0(O) -	0/0
498	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
499	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
500	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
501	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
502	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	1,122.00	885.13	- -	-	-	0/6
503	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	282.30	12/2007 03/2010	-	-	0/0
504	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,500.51	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
505	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	309.41	02/2009 02/2009	08/2014	-	0/0
506	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	209.00	2.06	12/2016 -	12/2016	0(O) -	0/0
507	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	913.48	457.55	- -	-	-	0/0
508	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	651.09	03/2013 -	03/2016	36(O) -	0/0
509	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	253.17	- -	-	-	0/0
510	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.66	06/2004 -	12/2015	138(O) -	0/0
511	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 913.00	3,700.00	3,137.84	- -	03/2015	- -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.09	- -	-	-	0/0
513	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	791.10	- -	-	-	0/0
514	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	35.28	- -	-	-	0/0
515	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	404.98	03/2012 -	-	-	0/0
516	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	307.10	- -	-	-	0/0
517	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	3.13	- -	-	-	0/0
518	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	51.98	04/2016 -	04/2016	0(O) -	0/0
519	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
520	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	249.67	- -	-	-	0/0
521	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	339.81	- -	-	-	0/0
522	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	232.60	03/2010 -	-	-	0/0
523	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	15.78	- -	-	-	0/0
524	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	40.29	- -	-	-	0/0
525	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
526	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.00	4,190.00	88.22	12/2015 -	03/2020	51(O) -	0/0
527	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.58	- -	-	-	0/0
528	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.47	- -	-	-	0/0
529	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
530	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
531	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.02	- -	-	-	0/0
532	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
533	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	115.88	02/2015 -	02/2015	0(O) -	0/0
534	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	579.41	03/2014 -	-	-	0/0
536	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	141.99	- -	-	-	0/0
537	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	464.34	06/2005 07/2011	-	-	0/0
538	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	150.55	06/2013 -	12/2014	18(O) -	0/0
539	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
540	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
541	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.18	- -	-	-	0/0
542	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	-	- -	-	-	0/0
543	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	820.00	190.44	- -	-	-	0/0
544	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	420.00	67.02	- -	-	-	0/0
545	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
546	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	900.00	595.96	- -	-	-	0/0
547	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	3,176.10	3,484.98	12/2006 -	-	-	0/0
548	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.29	- -	-	-	0/0
549	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.08	- -	-	-	0/0
550	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	9,987.13	11/2002 -	12/2018	193(O) -	0/0
551	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	946.45	03/2014 -	-	-	0/0
552	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0
553	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	374.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
554	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	70.89	- -	-	-	0/0
555	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
556	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	199.51	- 03/2010	-	-	0/0
557	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	165.31	- -	-	-	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
558	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	226.72	- -	-	-	0/0
559	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	77.71	- -	-	-	0/0
560	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	6.51	- -	-	-	0/0
561	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
562	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		164,135.33 -	290,709.13	91,721.45				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
563	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18(O) -	0/0
564	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
565	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	363.40	10/2014 -	10/2014	-	0/0
566	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	11/2014	4(O) -	0/0
567	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	05/2013	-	0/0
568	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2014	13(O) -	0/0
569	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13(O) -	0/0
570	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	12/2014	2(O) -	0/0
571	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8(O) -	0/0
572	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23(O) -	0/0
573	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
574	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	02/2014	-	0/0
575	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11(O) -	0/0
576	2LANING WITH PS GOPALGANJ-CHAPPRRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	171.00	05/2014 -	05/2014	-	0/0
577	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6(O) -	0/3
578	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11(O) -	0/0
579	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	06/2013	-	0/3

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
580	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39(O) -	0/0
581	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	941.00	08/2013 -	08/2013	-	0/3
582	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
583	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19(O) -	0/0
584	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	12/2014	16(O) -	0/0
585	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22(O) -	0/0
586	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	12/2015	28(O) -	0/0
587	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015	0(O) -	0/0
588	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	03/2015	20(O) -	0/0
589	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6(O) -	0/0
590	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93(O) -	0/0
591	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	0(O) -	0/3
592	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,208.00	11/2012 -	12/2014	25(O) -	0/0
593	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
594	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27(O) -	0/0
595	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12(O) -	0/0
596	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(O) -	0/0
597	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	665.80	-	10/2014	-	2/2
598	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35(O) -	0/0
599	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19(O) -	0/0
600	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	03/2015	81(O) -	0/0
601	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	03/2015	81(O) -	0/0
602	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	06/2015	120(O) -	0/0
603	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
604	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2016	77(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
605	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2014	21(O) -	0/0
606	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38(O) -	0/0
607	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
608	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19(O) -	0/0
609	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
610	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2015	0(O) -	0/0
611	DELHI HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	12/2014	55(O) -	0/0
612	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	11/2014	16(O) -	0/0
613	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	11/2014	17(O) -	0/0
614	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	808.70	- -	05/2013	-	1/1
615	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	12/2014	78(O) -	0/0
616	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	12/2014	79(O) -6(R)	0/0
617	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	03/2015	54(O) -	0/0
618	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015	0(O) -	0/0
619	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	12/2014	75(O) -	0/0
620	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016	0(O) -	0/0
621	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015	0(O) -	0/0
622	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25(O) -	0/0
623	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	12/2014	75(O) -	0/0
624	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	12/2014	16(O) -	0/0
625	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	12/2014	27(O) -	2/3
626	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	01/2014	-	0/0
627	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
628	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
629	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2014	70(O) -	0/0
630	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	12/2014	65(O) -	0/0
631	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90(O) -	0/0
632	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26(O) -	0/0
633	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	01/2013	-	0/0
634	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
635	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31(O) -	0/0
636	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20(O) -	0/0
637	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	02/2013	-	0/0
638	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	12/2012	-	0/0
639	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2014	17(O) -	0/0
640	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	536.00	01/2014 -	12/2014	11(O) -	0/0
641	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23(O) -	0/0
642	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	12/2014	31(O) -	0/0
643	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	11/2015	85(O) -	0/0
644	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17(O) -	0/0
645	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	06/2015	- -	2/3
646	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	616.50	07/2012 -	09/2014	-	0/0
647	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79(O) -	0/0
648	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	03/2015	71(O) -	0/0
649	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2014	73(O) -	0/0
650	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	12/2014	68(O) -	0/0
651	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21(O) -	0/0
652	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33(O) -	0/0
653	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	12/2014	78(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
654	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	458.30	10/2014 -	12/2014	2(O) -	0/0
655	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	04/2014	-	0/0
656	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	276.50	06/2008 04/2015	04/2015	82(O) 0(R)	0/0
657	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
658	NASHRI CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11(O) -	0/0
659	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	1,655.00	655.20	09/2013 -	09/2013	-	0/0
660	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	12/2014	58(O) -	0/0
661	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
662	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13(O) -	0/0
663	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40(O) -	0/0
664	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	-	0/0
665	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18(O) -	0/0
666	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	12/2014	9(O) -	0/0
667	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	12/2014	22(O) -	0/0
668	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,601.00	07/2012 -	07/2012	-	0/0
669	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2014	21(O) -	0/0
670	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14(O) -	0/0
671	PUNE-SHOLAPUR, PKG1 - [N24000127]NHAI, MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
672	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11(O) -	0/0
673	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	12/2014	74(O) -	0/0
674	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	1,479.00	368.50	06/2015 -	06/2015	0(O) -	0/0
675	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	01/2015	4(O) -	0/0
676	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	11/2013	-	0/0
677	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2014	21(O) -	0/0
678	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	982.20	05/2014 -	12/2014	7(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
679	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	268.50	09/2007 03/2014	12/2014	87(O) 9(R)	0/0
680	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
681	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	12/2014	6(O) -	0/0
682	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	03/2015	15(O) -	0/0
683	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2014	12(O) -	0/0
684	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12(O) -	0/0
685	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	159.90	08/2012 -	03/2016	43(O) -	0/0
686	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2014	-	0/0
687	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2014	6(O) -	0/0
688	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40(O) -	2/2
689	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,388.00	11/2013 -	11/2013	-	0/0
690	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	12/2014	14(O) -	0/0
691	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2014	19(O) -	0/0
692	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	383.20	- -	07/2014	-	2/2
693	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21(O) -	0/0
694	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	- -	-	-	0/0
695	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2014	25(O) -	0/0
696	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	11/2015	0(O) -	0/0
697	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	- -	-	-	0/0
698	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	- -	-	-	0/0
	Total		102,321.44 -	104,391.34	96,990.44				14/28
	SHIPPING AND PORTS								

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
699	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	1,049.37	12/2010 09/2012	01/2016	61(O) 40(R)	0/0
700	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 11/2014	11/2014	104(O) 0(R)	0/0
701	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
702	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
703	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
704	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		5,356.50 -	6,468.59	2,020.61				0/0
	<u>TELECOMMUNICATIONS</u>								
705	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	12/2014	71(O) -	0/0
706	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	48.95	10/2010 11/2015	09/2015	59(O) -2(R)	0/0
	Total		720.81 -	720.81	244.89				0/0
	<u>URBAN DEVELOPMENT</u>								
707	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
708	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35(O) -	0/0
709	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
710	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
711	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	8.78	08/2007 -	-	-	0/0
712	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
713	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARAstra - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2(O) -	0/0
714	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
715	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24(O) -	0/0

Sector Wise Details

(November 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
716	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
717	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17(O) -	0/0
718	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29(O) -	0/0
719	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
720	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15(O) -	0/0
721	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	2.04	03/2017 -	03/2017	0(O) -	0/0
722	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016	0(O) -	0/0
723	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	2,637.11	03/2010 -	10/2014	-	0/0
724	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11(O) -	0/0
725	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
726	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8(O) -	0/0
727	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	111.33	07/2012 -	07/2012	-	0/0
728	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	22.43	11/2014 -	12/2014	1(O) -	0/0
729	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	85.60	09/2014 -	09/2014	-	0/0
730	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	0.08	09/2016 -	09/2016	0(O) -	0/0
731	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34(O) -	0/0
	Total		82,686.31 -	87,959.21	14,916.15				3/3
	Grand Total		939,753.89	1,149,063.01	557,015.12				1284/3767


Summary of projects in the Flash Report for the month of November, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	747
Number of Projects completed/dropped/frozen in Current Month	16
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	2
Number of Projects in Current Month	731

Brief Analysis


Project Status with respect to Original Schedule: Out of 731 projects, 6 projects are ahead of schedule, 101 projects are on schedule and 324 projects are delayed. Of the balance, 268 projects do not have fixed dates of commissioning while 32 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

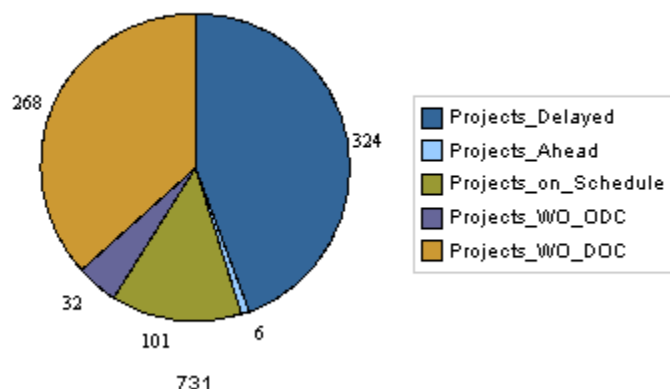

Investment Scenario

Total original cost of implementation of 731 projects when sanctioned, was of the order of Rs. 939753.89 crore but this was subsequently revised to Rs. 1149063.01 crore implying a cost overrun of 22.3%. The expenditure incurred on these projects till November, 2014 is Rs. 557015.12 crore, which is 48.5% of the revised cost of the projects.

Figures are in Rs. Crore

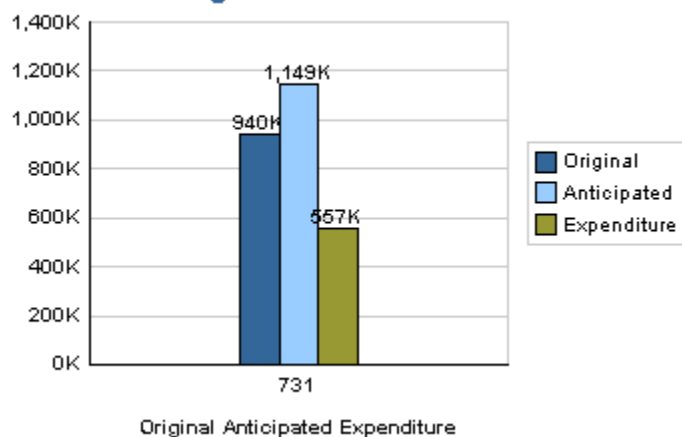

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	25
Number of Projects On Schedule	5
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	7
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 5 projects are on schedule and 13 projects are delayed .7 projects do not have fixed dates of commissioning.

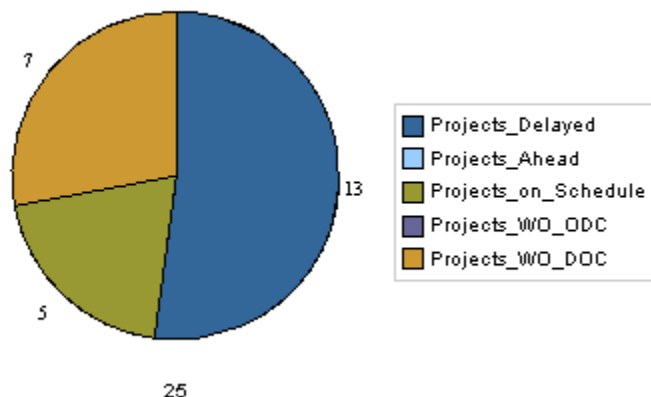

Investment Scenario

Total original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 82686.31 crore but this was subsequently revised to Rs. 87959.21 crore implying a cost overrun of 6.4%. The expenditure incurred on these projects till November, 2014 is Rs. 14916.15 crore, which is 17% of the revised cost of the projects.

Figures are in Rs. Crore

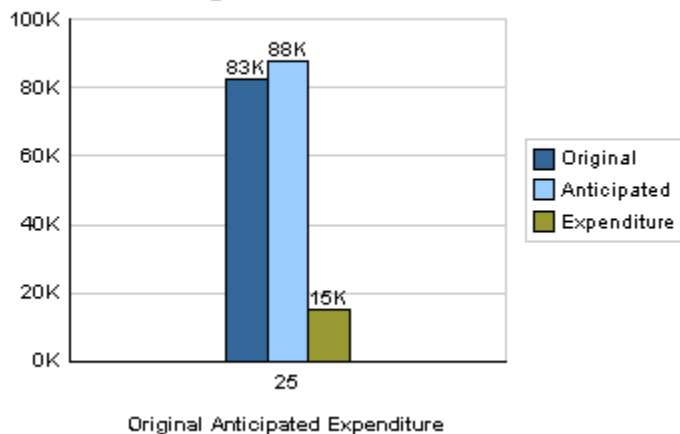

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed .



Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 720.81 crore but this was subsequently revised to Rs. 720.81 crore implying a cost overrun of 0%. The expenditure incurred on these projects till November, 2014 is Rs. 244.89 crore, which is 34% of the revised cost of the projects.

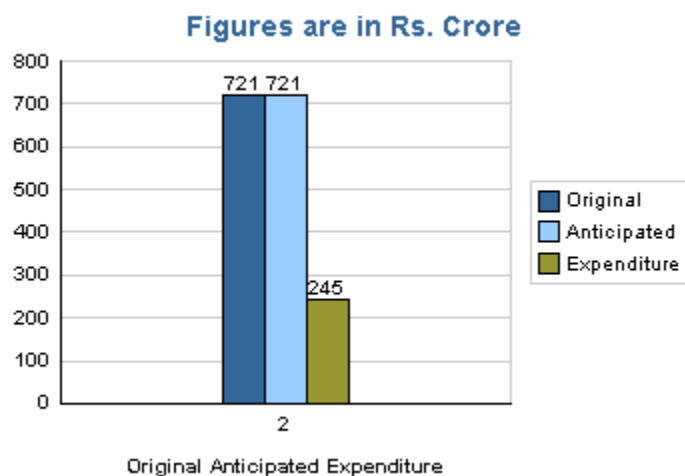

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	6
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are delayed .4 projects do not have fixed dates of commissioning.

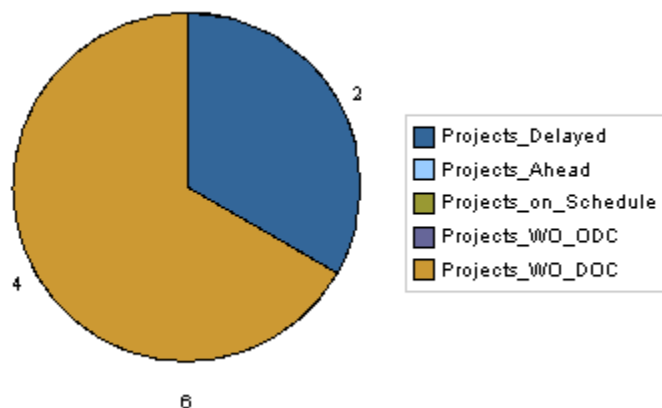

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5356.5 crore but this was subsequently revised to Rs. 6468.59 crore implying a cost overrun of 20.8%. The expenditure incurred on these projects till November, 2014 is Rs. 2020.61 crore, which is 31.2% of the revised cost of the projects.

Figures are in Rs. Crore

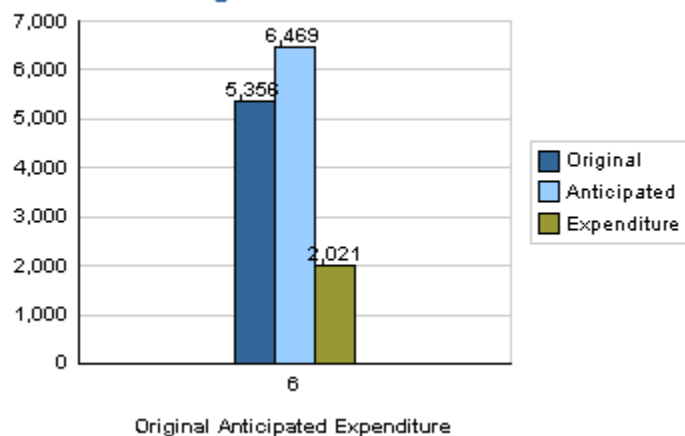

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	136
Number of Projects On Schedule	9
Number of Projects Delayed	94

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	32


Brief Analysis

Project Status with respect to Original Schedule: Out of 136 projects, 9 projects are on schedule and 94 projects are delayed .32 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

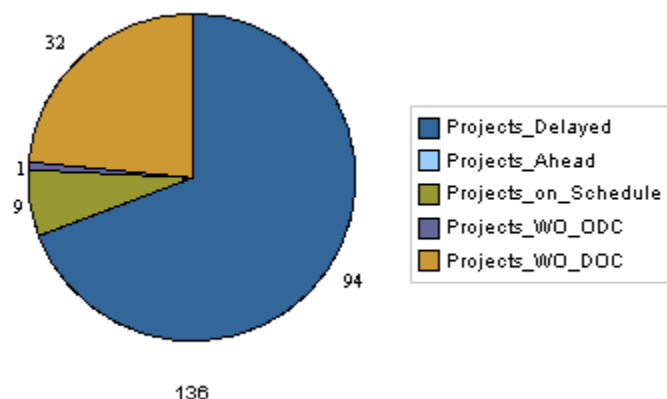

Investment Scenario

Total original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 102321.44 crore but this was subsequently revised to Rs. 104391.34 crore implying a cost overrun of 2%. The expenditure incurred on these projects till November, 2014 is Rs. 96990.44 crore, which is 92.9% of the revised cost of the projects.

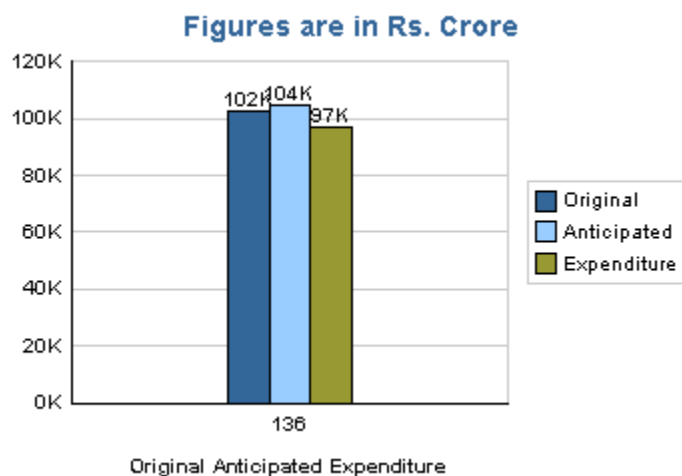

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	290
Number of Projects On Schedule	13
Number of Projects Delayed	34

Number of Projects Without Original Date of Commissioning	29
Number of Projects Without Date Of Commissioning	214

Brief Analysis


Project Status with respect to Original Schedule: Out of 290 projects, 13 projects are on schedule and 34 projects are delayed .214 projects do not have fixed dates of commissioning.29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

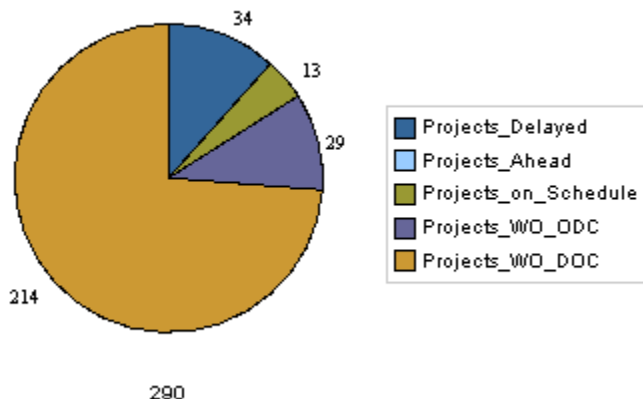

Investment Scenario

Total original cost of implementation of 290 projects when sanctioned, was of the order of Rs. 164135.33 crore but this was subsequently revised to Rs. 290709.13 crore implying a cost overrun of 77.1%. The expenditure incurred on these projects till November, 2014 is Rs. 91721.45 crore, which is 31.6% of the revised cost of the projects.

Figures are in Rs. Crore

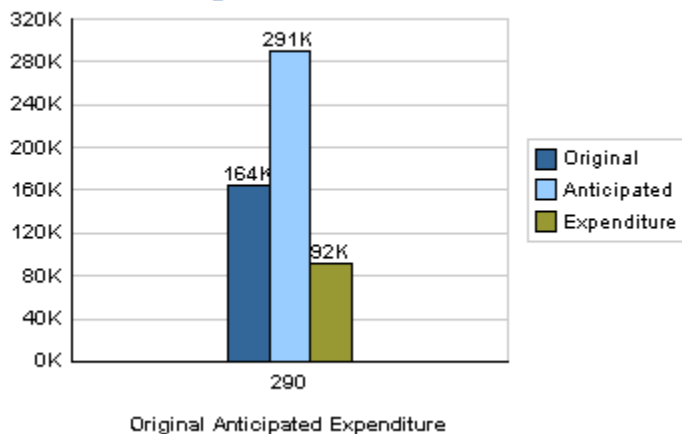

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	99
Number of Projects On Schedule	25
Number of Projects Delayed	68
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 99 projects, 3 projects are ahead of schedule, 25 projects are on schedule and 68 projects are delayed .2 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

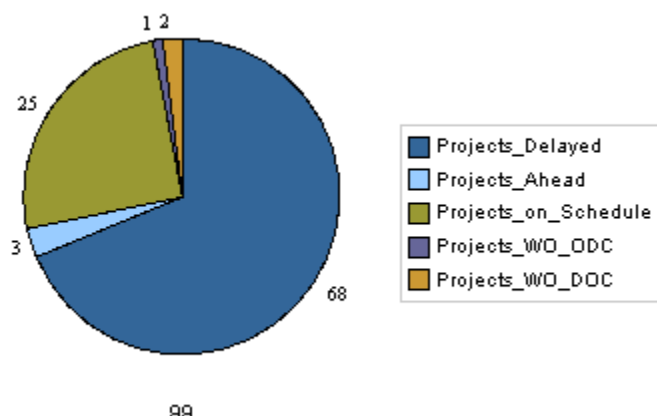

Investment Scenario

Total original cost of implementation of 99 projects when sanctioned, was of the order of Rs. 241739.71 crore but this was subsequently revised to Rs. 273378.26 crore implying a cost overrun of 13.1%. The expenditure incurred on these projects till November, 2014 is Rs. 145646.74 crore, which is 53.3% of the revised cost of the projects.

Figures are in Rs. Crore

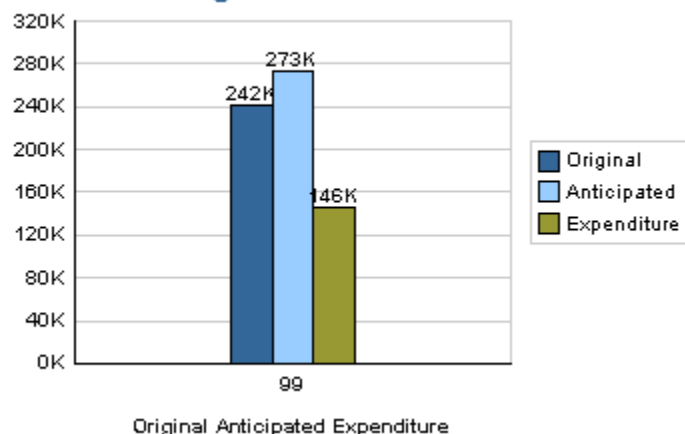

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	75
Number of Projects On Schedule	21
Number of Projects Delayed	49
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 75 projects, 2 projects are ahead of schedule, 21 projects are on schedule and 49 projects are delayed .2 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

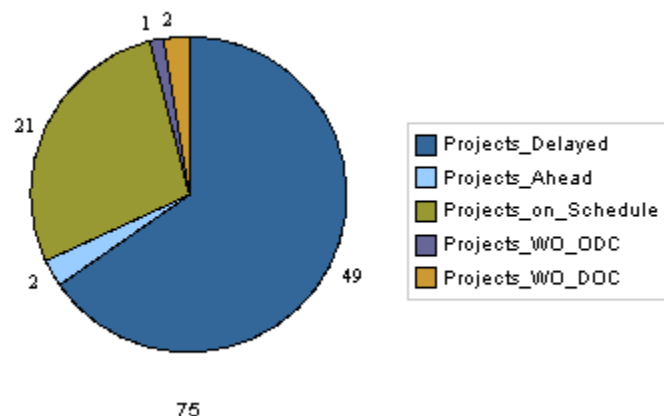

Investment Scenario

Total original cost of implementation of 75 projects when sanctioned, was of the order of Rs. 165614.37 crore but this was subsequently revised to Rs. 182323.41 crore implying a cost overrun of 10.1%. The expenditure incurred on these projects till November, 2014 is Rs. 80471.12 crore, which is 44.1% of the revised cost of the projects.

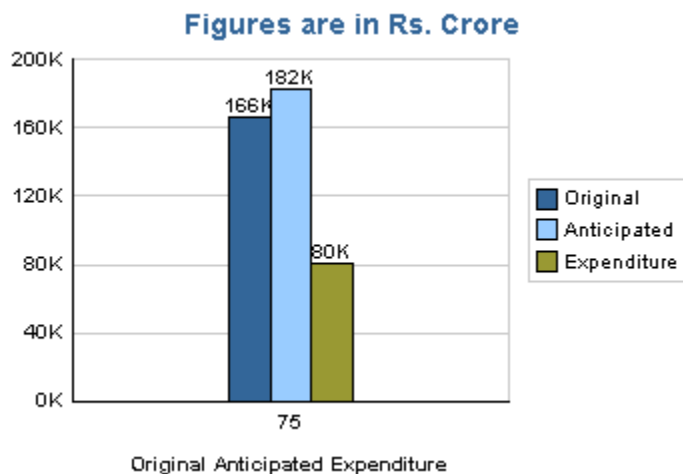

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	21
Number of Projects On Schedule	4
Number of Projects Delayed	17

Brief Analysis


Project Status with respect to Original Schedule: Out of 21 projects, 4 projects are on schedule and 17 projects are delayed.

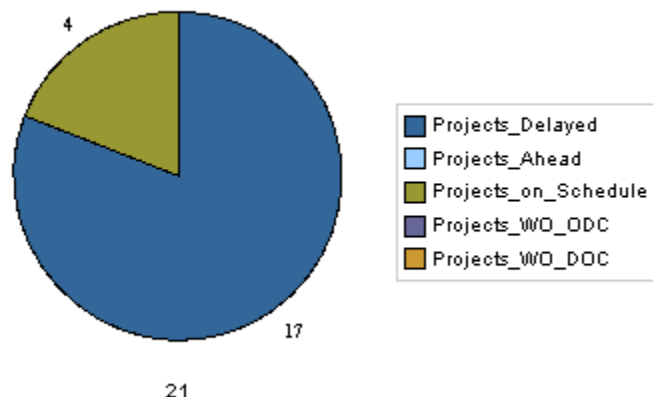

Investment Scenario

Total original cost of implementation of 21 projects when sanctioned, was of the order of Rs. 81920.1 crore but this was subsequently revised to Rs. 87874.06 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till November, 2014 is Rs. 64135.6 crore, which is 73% of the revised cost of the projects.

Figures are in Rs. Crore

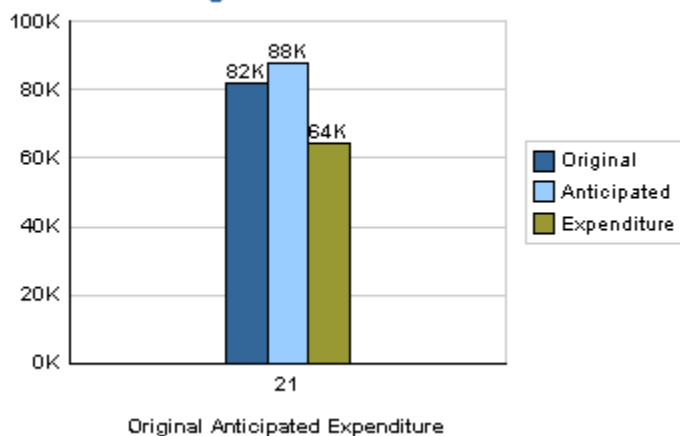

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	64
Number of Projects On Schedule	23
Number of Projects Delayed	37

Number of Projects Without Date Of Commissioning 4

Brief Analysis


Project Status with respect to Original Schedule: Out of 64 projects, 23 projects are on schedule and 37 projects are delayed .4 projects do not have fixed dates of commissioning.

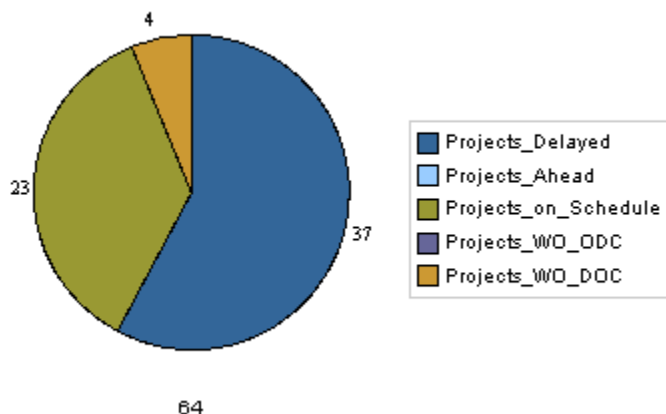

Investment Scenario

Total original cost of implementation of 64 projects when sanctioned, was of the order of Rs. 46559.36 crore but this was subsequently revised to Rs. 56741.93 crore implying a cost overrun of 21.9%. The expenditure incurred on these projects till November, 2014 is Rs. 19260.36 crore, which is 33.9% of the revised cost of the projects.

Figures are in Rs. Crore

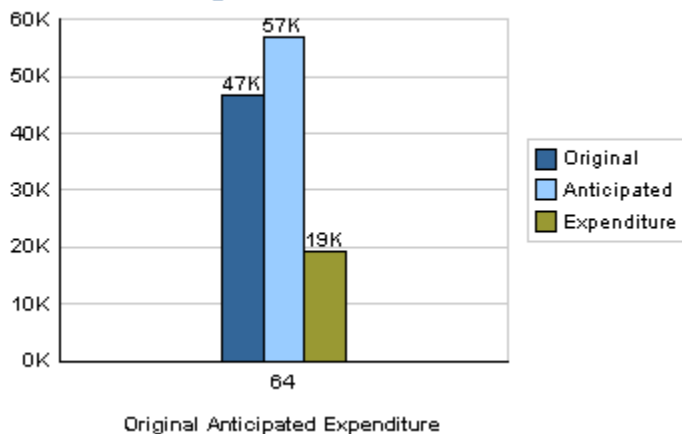

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	4
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 1 project are ahead of schedule, 4 projects are delayed .2 projects do not have fixed dates of commissioning.

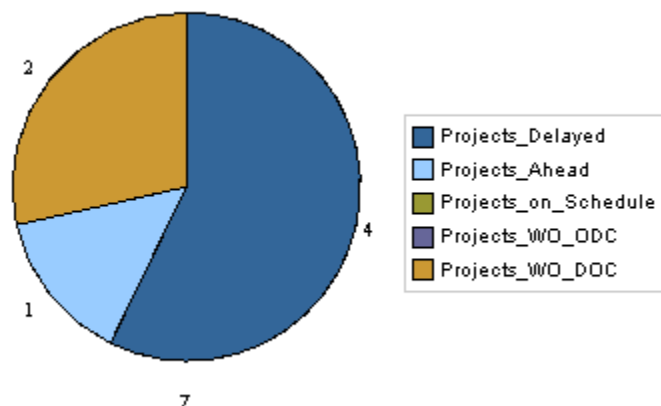

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently revised to Rs. 2652.48 crore implying a cost overrun of 2%. The expenditure incurred on these projects till November, 2014 is Rs. 1504.77 crore, which is 56.7% of the revised cost of the projects.

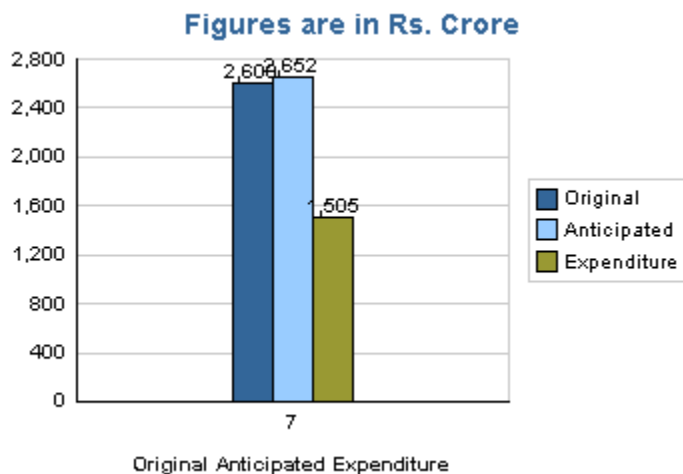

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

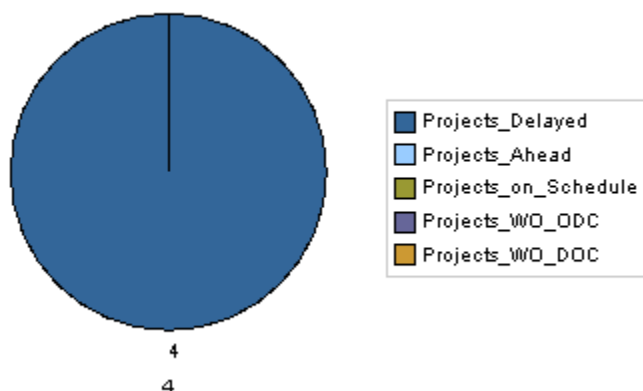

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till November, 2014 is Rs. 32048.19 crore, which is 68.6% of the revised cost of the projects.

Figures are in Rs. Crore

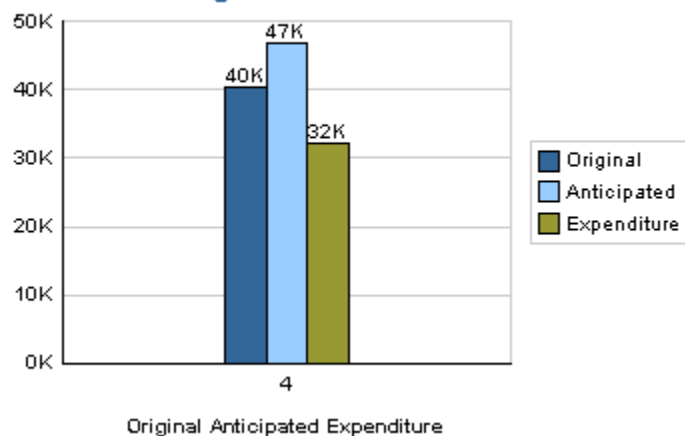

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	16.59
2	ANDHRA PRADESH	22	24,649.56	30,169.08	21,066.6
3	ARUNACHAL PRADESH	3	9,356.22	21,082.33	11,424.92
4	ASSAM	39	26,819.37	42,173.91	32,976.6
5	BIHAR	48	37,027.18	51,405.82	37,317.9
6	CHANDIGARH	1	452	452	346.36
7	CHHATISGARH	27	72,434.39	80,336.8	31,245.73
8	DELHI	9	44,464.6	44,464.6	9,755.1
9	GOA	1	335.61	388.53	285.2
10	GUJARAT	31	36,997.24	37,591.79	19,681.5
11	HARYANA	8	4,259.81	6,409.79	7,331.24
12	HIMACHAL PRADESH	6	13,728.27	21,028.89	14,662.62
13	JAMMU AND KASHMIR	7	21,314.62	40,235.3	17,031.16
14	JHARKHAND	31	21,501.51	22,165.22	11,897.94
15	KARNATAKA	33	65,925.98	80,757.7	18,743.29
16	KERALA	11	19,030.21	23,056.44	7,700.76
17	MADHYA PRADESH	17	23,452.88	25,436.8	8,567.35
18	MAHARASHTRA	41	67,520.43	79,631.16	32,873.61
19	MANIPUR	1	727.56	6,570.75	2,676.64
20	MEGHALAYA	3	4,845.02	6,069.9	825.94
21	MIZORAM	2	988.06	3,733.88	889.15
22	MULTI STATE	178	1,97,477.48	2,23,994.78	97,676.29
23	NAGALAND	2	5,124	7,461.12	10.34
24	ODISHA	39	66,852.2	75,528.98	49,674.87
25	PUNJAB	4	1,497.5	1,470.46	2,323.66
26	RAJASTHAN	25	25,638.72	25,694.2	14,255.61
27	SIKKIM	2	1,648.94	4,499.46	404.53
28	TAMIL NADU	41	53,533.49	70,580.21	47,226.07
29	TELANGANA	21	9,410.62	12,179.13	3,250.3
30	TRIPURA	6	2,966.26	6,552.28	3,132.21
31	UTTAR PRADESH	26	14,207.6	16,863.93	12,475.68
32	UTTARAKHAND	6	9,351.89	12,905.21	4,215.38
33	WEST BENGAL	39	55,900.06	67,857.95	35,053.98
TOTAL		731	9,39,753.89	11,49,063.01	5,57,015.12

Details of Projects Without Original Date of Commissioning

(November 2014)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,071.91	- -	12/2015	-	0/12
	Total		1,584.00 -	1,584.00	1,071.91				0/12
	<u>POWER</u>								
2	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO, TRIPURA	07/2012	296.87 -	296.87	285.27	- 03/2015	03/2015	0(R3)	0/17
	Total		296.87 -	296.87	285.27				0/17
	<u>RAILWAYS</u>								
3	MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	645.00	307.38	- -	12/2014	-	0/0
4	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	237.08	- -	01/2015	-	0/0
5	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,615.26	- -	03/2015	-	0/0
6	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	630.94	- 05/2009	03/2015	70(R1)	0/0
7	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23 -	1,072.51	882.87	- -	03/2015	-	0/0
8	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR, ASSAM	01/2004	915.70 913.00	3,700.00	3,137.84	- -	03/2015	-	0/0
9	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	826.55	- -	03/2015	-	0/0
10	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONG WITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	605.94	- -	03/2015	-	0/0
11	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	223.52	- -	03/2015	-	0/0
12	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71 -	744.71	571.84	- -	03/2016	-	0/1
13	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0

(November 2014)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	209.48	- -	03/2017	-	0/0
15	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
16	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	1.75	- -	12/2017	-	0/0
17	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 283.00	565.13	2.63	- -	03/2018	-	0/0
18	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	888.65	-	- -	03/2018	-	0/0
19	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.00	441.45	87.56	- -	03/2018	-	0/0
20	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.00	288.81	11.74	- -	03/2018	-	0/0
21	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	39.78	- -	03/2018	-	0/0
22	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 166.00	435.58	0.56	- -	03/2018	-	0/0
23	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 390.00	1,653.55	1,038.91	- -	03/2018	-	0/0
24	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.00	453.10	130.83	- -	03/2018	-	0/0
25	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	184.11	- -	03/2018	-	0/0
26	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	1,336.57	255.54	- -	03/2019	-	0/0
27	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
28	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
29	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.00	563.13	21.95	- -	03/2019	-	0/0
30	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	364.06	0.30	- -	03/2019	-	0/0
31	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.64	- -	03/2020	-	0/0
	Total		15,314.30 -	30,180.55	11,513.89				0/1
	ROAD TRANSPORT AND HIGHWAYS								

(November 2014)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
32	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	06/2015	-	2/3
	Total		671.00 -	671.00	1,273.00				2/3
	Grand Total		17,866.17	32,732.42	14,144.07				2/33

Annexure 4(b)

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- -	-
	Total		940.61 -		
	<u>COAL</u>				
3	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
4	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	03/2012 -	-
6	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
	Total		1,475.66 -		
	<u>PETROCHEMICALS</u>				
7	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
8	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
9	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
	Total		882.83 -		
	<u>POWER</u>				
10	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
11	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		438.78 -		

Date of Commissioning (Month/Year)					
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>RAILWAYS</u>				
12	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
13	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
14	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
15	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2012
16	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012
17	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012
18	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
19	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
20	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
21	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
22	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
23	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014
24	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	10/2014
25	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
26	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
27	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
28	VIRAMGAM-BHILD(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
29	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	-
30	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
31	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
32	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
33	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
34	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
35	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
36	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
38	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] WCR, MULTI STATE	09/1998	247.66 -	05/2008 -	-
39	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR - [220100240] ECR, BIHAR	04/1997	501.69 335.77	03/2012 -	-
40	ANGAMALI-SABARIMALA (N.L.) (SR) - [220100252] SR, KERALA	10/1998	550.00 517.70	- -	-
41	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, BIHAR	04/1997	162.87 -	- -	-
42	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258] NR, MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
43	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC) - [220100262] SR, TAMIL NADU	09/1995	100.00 -	- -	-
44	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC) - [220100263] SR, MULTI STATE	03/1998	280.00 -	- -	-
45	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	-
46	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268] MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 -	-
47	GADWAL - RAICHUR (NL), SCR - [220100270] SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
48	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272] ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
49	DEOGHAR - SULTANGANJ (INL), ER - [220100273] ER, MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
50	BANGLORE - SATYAMANGALAM (NL) (SWR) - [220100274] SWR, KARNATAKA	04/1996	138.00 -	- -	-
51	KHURDA ROAD-BOLANGIR (NL) (ECOR) - [220100284] ECR, ODISHA	04/1994	470.21 -	- -	-
52	HARIDASPUR-PARADEEP (NL) - [220100285] RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-
53	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303] ECR, BIHAR	04/2003	528.65 -	- -	-
54	KOSI BRIDGE (NL), ECR - [220100304] ECR, BIHAR	04/2002	322.95 -	03/2012 -	-
55	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, JHARKHAND	04/2002	459.91 -	- -	-
56	DANIAWAN-BIHARSARIF (NL), ECR - [220100311] ECR, BIHAR	04/2001	406.92 -	- -	-
57	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314] WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	-
58	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316] NER, BIHAR	04/2003	218.19 -	- -	-
59	HATHUA-BHATNI (NL) (NER) - [220100319] NER, MULTI STATE	04/2005	230.03 -	- -	-
60	TALCHER-BIMALAGARH (NL) (ECOR) - [220100328] ECR, ODISHA	04/2005	810.78 -	- -	-
61	RAICHUR-GUNTAKAL (DL) (SCR) - [220100329] RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
63	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-
64	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
65	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
66	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
67	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 303.00	03/2011 -	-
68	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
69	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
70	BARDHAMAN-KATWA (GC) - [N22000091]JER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
71	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	-
72	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
73	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-
74	TINPAHAR - SAHIBGANJ (ER) - [N22000115]JER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
75	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]JER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
76	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]JER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
77	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]JWR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
78	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]JWR,GUJARAT	04/2008	394.14 -	03/2013 -	-
79	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]JWR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
80	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]JWR,GUJARAT	04/2008	318.24 -	03/2012 -	-
81	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]JWR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
82	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
83	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
84	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
85	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
86	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
87	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
88	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	-	-
89	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	-	-
90	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	-	-
91	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	-	-
92	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	-	-
93	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	-	-
94	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	-	-
95	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	-	-
96	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	-	-
97	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	-	-
98	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	-	-
99	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	-	-
100	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	-	-
101	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	-	-
102	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	-	-
103	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	-	-
104	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	-	-
105	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	-	-
106	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	-	-
107	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	-	-
108	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	-	-
109	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	-	-
110	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	-	-
111	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	-	-
112	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	-	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
113	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
114	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
115	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
116	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
117	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
118	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
119	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
120	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
121	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
122	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
123	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
124	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
125	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
126	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
127	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
128	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
129	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
130	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
131	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
132	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
133	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
134	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
135	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
136	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NFR,MULTI STATE	04/1999	175.43 -	- -	-
137	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
138	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
139	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
140	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
141	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
142	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
143	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
144	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
145	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
146	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
147	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
148	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
149	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
150	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
151	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
152	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
153	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
154	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
155	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
156	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
157	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
158	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
159	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
160	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
161	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
163	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
164	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
165	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
166	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
167	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
168	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
169	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
170	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
171	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
172	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
173	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
174	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
175	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
176	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
177	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
178	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
179	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
180	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
181	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
182	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
183	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
184	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
185	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
186	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
187	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
188	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
189	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
190	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
191	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
192	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
193	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
194	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
195	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
196	MUDKHEDE-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
197	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
198	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
199	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
200	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
201	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
202	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
203	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
204	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
205	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
206	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
207	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
208	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
209	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
210	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
211	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
213	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
214	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	01/1999 -	-
215	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	01/1999 -	-
216	MM FROM BURAMARA-CHAKULIA - [N22000305]SER, MULTI STATE	04/2008	466.48 -	01/1999 -	-
217	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	285.57 -	01/1999 -	-
218	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
219	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-
220	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-
221	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 -	- -	-
222	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	-
223	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
224	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR, TAMIL NADU	04/2011	190.10 -	- -	-
225	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	- -	-
	Total		103,146.88 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
226	PUNE-SHOLAPUR, PKG1 - [N24000127]NHAI, MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
227	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
228	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012
229	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013
230	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013
231	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	- -	05/2013
232	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	05/2013
233	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
234	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
235	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	08/2013

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
236	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
237	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
238	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013
239	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
240	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	01/2014
241	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2014
242	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
243	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014
244	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 04/2015	04/2014
245	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
246	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
247	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	09/2014
248	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
249	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	10/2014
250	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014
251	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
252	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
253	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
254	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
255	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
256	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
257	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		19,575.51 -		
	<u>SHIPPING AND PORTS</u>				
258	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
259	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
260	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
261	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		3,978.50 -		
	<u>URBAN DEVELOPMENT</u>				
262	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	07/2012
263	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
264	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	09/2014
265	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
266	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-
267	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
268	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		9,927.54 -		
	Grand Total		145,826.92		

Details of Projects Without Milestones w.r.t. Original Schedule

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	12/2014	0/0
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	01/2015	0/0
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	02/2015	0/0
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2016	0/0
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	06/2016	0/0
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- -	-	0/0
	Total		2,599.56 -			0/0
	<u>COAL</u>					
8	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
9	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	04/2017	0/0
10	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	03/2020 -	03/2020	0/0
11	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	03/2021 -	03/2021	0/0
12	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-	0/0
	Total		3,278.51 -			0/0
	<u>FERTILISERS</u>					
13	SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	02/2017 -	02/2017	0/0
	Total		197.79 -			0/0
	<u>PETROLEUM</u>					
14	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	12/2014	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	10/2014 -	12/2014	0/0
16	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 204.29	06/2012 09/2013	12/2014	0/0
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	02/2015	0/0
18	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	07/2013 -	02/2015	0/0
19	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	09/2012 -	04/2015	0/0
20	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
21	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	04/2015 -	04/2015	0/0
22	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	04/2015 -	04/2015	0/0
23	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	04/2006 04/2016	06/2015	0/0
24	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	10/2014 -	10/2015	0/0
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
27	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
28	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2015	0/0
29	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	07/2015 -	12/2015	0/0
30	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	01/2016 -	01/2016	0/0
31	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	12/2014 03/2016	03/2016	0/0
32	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0
33	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	05/2016 -	05/2016	0/0
34	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0
35	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	02/2016 -	07/2016	0/0
36	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	07/2016 -	07/2016	0/0
37	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	03/2014 -	07/2016	0/0
38	TWENTY NOS. FEEDER GAS LINES - [N16000192]AAI,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
39	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]GAIL,GUJARAT	07/2014	716.00 -	01/2017 -	01/2017	0/0
40	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	01/2017 -	01/2017	0/0
41	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
42	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	02/2016 04/2017	04/2017	0/0
43	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 -	05/2017 -	05/2017	0/0
44	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 -	09/2017	0/0
45	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
46	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2017	0/0
47	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	12/2017	0/0
48	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2018	0/0
49	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	12/2018 -	12/2018	0/0
50	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
51	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
	Total		71,194.06 -			0/0
	<u>POWER</u>					
52	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
53	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
54	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	03/2016 -	05/2016	0/0
55	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
56	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0
57	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	08/2016 -	08/2016	0/0
58	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
59	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	02/2017 -	02/2017	0/0
60	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	02/2017 -	02/2017	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
61	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	04/2017 -	04/2017	0/0
62	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	11/2017 -	11/2017	0/0
63	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	03/2018	0/0
64	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	12/2018	0/0
65	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
	Total		25,692.36 -			0/0
	<u>RAILWAYS</u>					
66	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
67	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
68	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
69	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2012	0/0
70	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
71	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
72	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
73	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
74	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
75	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
76	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
77	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
78	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	10/2014	0/0
79	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	12/2014	0/0
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014	0/0
81	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	12/2014	0/0
82	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	12/2014	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
83	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2014	0/0
84	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
85	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
86	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2015	0/0
87	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
88	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
89	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23 -	- -	03/2015	0/0
90	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR, ASSAM	01/2004	915.70 913.00	- -	03/2015	0/0
91	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	- -	03/2015	0/0
92	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2015	0/0
93	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
94	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
95	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
96	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
97	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
98	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	04/2015	0/0
99	RANCHI-LOHARDAGA(GC),SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
100	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
101	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER, JHARKHAND	03/1997	261.70 -	02/2006 -	12/2015	0/0
102	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
103	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	03/2004 12/2010	03/2016	0/0
104	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	03/2016	0/0
105	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
106	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 4,259.48	03/2016 -	03/2016	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
107	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
108	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
109	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
110	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
111	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
112	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
113	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	04/2016	0/0
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
115	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
116	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
117	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
118	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
119	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
120	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
121	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
122	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
123	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	04/2008 03/2014	06/2017	0/0
124	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2017	0/0
125	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
126	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
127	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
128	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.00	03/2014 -	03/2018	0/0
129	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.00	04/2014 03/2020	03/2018	0/0
130	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 283.00	- -	03/2018	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
131	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	- -	03/2018	0/0
132	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.00	- -	03/2018	0/0
133	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.00	- -	03/2018	0/0
134	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0
135	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 166.00	- -	03/2018	0/0
136	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 390.00	- -	03/2018	0/0
137	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.00	- -	03/2018	0/0
138	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	04/2012 03/2016	03/2018	0/0
139	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
140	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
141	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
142	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2019	0/0
143	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
144	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
145	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	03/2014 03/2019	03/2019	0/0
146	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
147	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.00	- -	03/2019	0/0
148	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
149	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
150	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
151	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.00	12/2015 -	03/2020	0/0
152	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
153	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2020	0/0
154	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
155	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
156	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
157	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
158	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	-	0/0
159	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
160	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
161	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
162	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
163	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
164	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
165	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
166	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
167	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
168	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
169	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
170	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
171	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
172	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
173	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
174	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 -	-	0/0
175	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
176	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
177	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
178	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
179	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
180	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
181	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
182	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
183	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
184	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
185	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-	0/0
186	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
187	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
188	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
189	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
190	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
191	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-	0/0
192	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
193	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
194	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
195	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 303.00	03/2011 -	-	0/0
196	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
197	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
198	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
199	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	-	0/0
200	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
201	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-	0/0
202	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
203	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
204	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
205	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
206	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
207	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
208	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
209	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
210	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
211	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-	0/0
212	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
213	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
214	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-	0/0
215	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
216	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-	0/0
217	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
218	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
219	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-	0/0
220	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	- -	-	0/0
221	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-	0/0
222	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	- -	-	0/0
223	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-	0/0
224	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	-	0/0
225	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-	0/0
226	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
227	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
228	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
229	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
230	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
231	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
232	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
233	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
234	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
235	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
236	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
237	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	- -	-	0/0
238	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
239	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-	0/0
240	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
241	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
242	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-	0/0
243	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
244	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-	0/0
245	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-	0/0
246	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-	0/0
247	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
248	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
249	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
250	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
251	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
252	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
253	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
254	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
255	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
256	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
257	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
258	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
259	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
260	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
261	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
262	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
263	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
264	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NFR,MULTI STATE	04/1999	175.43 -	- -	-	0/0
265	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
266	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
267	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
268	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
269	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
270	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
271	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
272	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
273	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
274	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
275	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
276	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
277	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
278	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
279	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
280	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
281	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
282	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
283	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
284	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
285	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
286	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
287	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
288	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
289	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
290	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
291	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
292	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
293	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
294	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
295	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
296	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
297	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
298	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
299	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
300	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
301	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
302	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
303	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
304	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
305	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
306	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
307	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
308	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
309	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
310	MANSABHADINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
311	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
312	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
313	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
314	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
315	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
316	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
317	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
318	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
319	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
320	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
321	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
322	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
323	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
324	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
325	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
326	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
327	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
328	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
329	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
330	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
331	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
332	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
333	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
334	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
335	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
336	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
337	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
338	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
339	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
340	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
341	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
342	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
343	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
344	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
345	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
346	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
347	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
348	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
349	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
350	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-	0/0
351	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
352	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
353	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-	0/0
	Total		163,110.62 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
354	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012	0/0
355	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
356	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012	0/0
357	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013	0/0
358	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013	0/0
359	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013	0/0
360	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
361	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
362	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
363	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013	0/0
364	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0
365	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	01/2014	0/0
366	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2014	0/0
367	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
368	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
369	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 04/2015	04/2014	0/0
370	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
371	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	09/2014	0/0
372	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
373	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
374	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	11/2014	0/0
375	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	11/2014	0/0
376	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	11/2014	0/0
377	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	12/2014	0/0
378	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	12/2014	0/0
379	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2014	0/0
380	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	12/2014	0/0
381	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	12/2014	0/0
382	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	12/2014	0/0
383	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	12/2014	0/0
384	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	12/2014	0/0
385	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 06/2015	12/2014	0/0
386	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	12/2014	0/0
387	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	12/2014	0/0
388	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	12/2014	0/0
389	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	12/2014	0/0
390	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	12/2014	0/0
391	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	12/2014	0/0
392	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	12/2014	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
393	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2014	0/0
394	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2014	0/0
395	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	12/2014	0/0
396	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2014	0/0
397	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2014	0/0
398	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	12/2014	0/0
399	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2014	0/0
400	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	12/2014	0/0
401	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2014	0/0
402	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2014	0/0
403	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2014	0/0
404	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2014	0/0
405	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	12/2014	0/0
406	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	12/2014	0/0
407	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2014	0/0
408	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2014	0/0
409	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	12/2014	0/0
410	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	12/2014	0/0
411	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	12/2014	0/0
412	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	12/2014	0/0
413	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	12/2014	0/0
414	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 01/2015	01/2015	0/0
415	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	01/2015	0/0
416	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	02/2015	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
417	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	03/2015	0/0
418	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2015	0/0
419	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2015	0/0
420	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	03/2015	0/0
421	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	03/2015	0/0
422	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2015	0/0
423	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2015	0/0
424	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	03/2015	0/0
425	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2015	0/0
426	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2015	0/0
427	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2015	0/0
428	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2015	0/0
429	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	03/2015	0/0
430	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	03/2015	0/0
431	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2015	04/2015	0/0
432	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
433	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2015	0/0
434	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	05/2015	0/0
435	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	06/2015	0/0
436	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	06/2015	0/0
437	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	06/2015	0/0
438	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	06/2015	0/0
439	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2015	0/0
440	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	06/2015	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
441	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
442	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
443	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
444	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
445	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
446	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
447	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
448	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	11/2015	0/0
449	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	11/2015	0/0
450	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
451	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
452	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2015	0/0
453	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	12/2015	0/0
454	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2015	0/0
455	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
456	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2015	0/0
457	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2015	0/0
458	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	12/2015	0/0
459	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
460	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	12/2015	0/0
461	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	12/2015	0/0
462	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2015	0/0
463	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
464	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2016	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
465	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2016	0/0
466	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
467	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
468	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	07/2016	0/0
469	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
470	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
471	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
472	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
473	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
474	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
475	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
476	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
477	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
478	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		91,141.35 -			0/0
	<u>SHIPPING AND PORTS</u>					
479	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
480	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
481	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
482	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 11/2014	11/2014	0/0
483	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	01/2016	0/0
484	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
	Total		5,356.50 -			0/0
	<u>TELECOMMUNICATIONS</u>					

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
485	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	12/2014	0/0
486	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 11/2015	09/2015	0/0
	Total		720.81 -			0/0
	<u>URBAN DEVELOPMENT</u>					
487	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	07/2012	0/0
488	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	09/2014	0/0
489	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014	0/0
490	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014	0/0
491	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	01/2015	0/0
492	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
493	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	06/2012 -	05/2015	0/0
494	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	08/2015	0/0
495	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	08/2015	0/0
496	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	10/2015	0/0
497	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 -	10/2015	0/0
498	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	01/2016	0/0
499	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
500	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
501	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	05/2016	0/0
502	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	09/2016	0/0
503	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
504	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	09/2015 -	12/2016	0/0
505	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
506	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0

			(November 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
507	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
508	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-	0/0
509	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
510	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		76,291.31 -			0/0
	Grand Total		439,582.87			0/0

Details of On Schedule Projects w.r.t. Original Schedule

						(November 2014)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	281.79	03/2015 -	03/2015
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	664.83	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.00 -	490.10	184.38	03/2017 -	03/2017
4	BATURA OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
6	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	43.25	03/2018 -	03/2018
7	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
8	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	430.14	68.12	03/2016 -	03/2016
9	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
10	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
11	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
12	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
13	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
14	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	43.38	03/2018 -	03/2018
16	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
17	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
18	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	97.75	03/2020 -	03/2020
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	64.72	03/2016 -	03/2016
20	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
21	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	223.58	03/2016 -	03/2016

(November 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
22	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	70.54	03/2015 -	03/2015
23	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
	Total		16,419.11 -	16,047.16	1,876.52		
	<u>FERTILISERS</u>						
24	SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	-	02/2017 -	02/2017
	Total		197.79 -	197.79	.00		
	<u>PETROLEUM</u>						
25	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	3,027.35	05/2015 -	05/2015
26	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	228.64	-	12/2016 -	12/2016
27	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	762.00	2.89	01/2017 -	01/2017
28	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]	7/2014	716.00 -	716.00	-	01/2017 -	01/2017
29	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,706.47	0.28	05/2017 -	05/2017
30	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	319.32	11/2015 -	11/2015
31	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
32	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,913.10	9.50	05/2016 -	05/2016
33	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	6.07	07/2016 -	07/2016
34	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
35	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.27	09/2017 -	09/2017
36	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
37	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 -	04/2016
38	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	49.94	01/2016 -	01/2016
39	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	352.56	10.60	03/2017 -	03/2017
40	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.52	04/2015 -	04/2015
41	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	194.35	04/2015 -	04/2015

(November 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	36.33	07/2016 -	07/2016
43	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	701.00	335.61	11/2015 -	11/2015
44	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	4,032.33	05/2016 -	05/2016
45	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	794.82	11/2015 -	11/2015
	Total		60,660.89 -	62,823.84	9,030.91		
	<u>POWER</u>						
46	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	924.13	02/2015 -	02/2015
47	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014
48	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,355.00	08/2015 -	08/2015
49	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	435.09	03/2015 -	03/2015
50	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	288.75	12/2015 -	12/2015
51	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	75.99	03/2016 -	03/2016
52	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
53	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
54	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
55	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
56	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
57	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	-	03/2018 -	03/2018
58	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
59	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]	2/2014	378.71 -	378.71	11.20	10/2016 -	10/2016
60	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
61	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
62	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016

(November 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
64	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	11.00	08/2016 -	08/2016
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	2.00	06/2016 -	06/2016
67	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
68	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	135.70	05/2016 -	05/2016
69	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	658.43	06/2015 -	06/2015
70	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
	Total		33,329.87 -	33,329.87	3,897.29		
	<u>RAILWAYS</u>						
71	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	115.88	02/2015 -	02/2015
72	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	542.29	03/2016 -	03/2016
73	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	500.80	03/2016 -	03/2016
74	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016
75	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	4.66	02/2019 -	02/2019
76	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	29.10	03/2015 -	03/2015
77	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.06	12/2016 -	12/2016
78	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	116.12	03/2015 -	03/2015
79	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	215.50	03/2017 -	03/2017
80	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
81	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]	4/2012	714.10 -	714.10	51.98	04/2016 -	04/2016
82	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.03	02/2020 -	02/2020
83	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	79.26	03/2015 -	03/2015

(November 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		16,550.90 -	21,700.84	3,401.78		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
84	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	368.50	06/2015 -	06/2015
85	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
86	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
87	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015
88	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.40	11/2015 -	11/2015
89	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2015
90	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015
91	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
92	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
	Total		13,092.05 -	13,092.05	3,731.20		
	<u>STEEL</u>						
93	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	154.50	06/2015 -	06/2015
94	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	20.22	05/2016 -	05/2016
95	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	31.27	04/2016 -	04/2016
96	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]	4/2014	188.93 -	188.93	8.28	04/2015 -	04/2015
	Total		1,456.56 -	1,456.56	214.27		
	<u>URBAN DEVELOPMENT</u>						
97	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
98	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
99	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	0.08	09/2016 -	09/2016
100	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
101	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	2.04	03/2017 -	03/2017

(November 2014)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		66,699.91	66,699.91	8,701.61		
	Grand Total		208,407.08	215,348.02	30,853.58		

Annexure-1

Details of Projects Ahead of Schedule w.r.t. Original Schedule

						(November 2014)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	346.36	03/2015 -	02/2015
	Total		452.00 -	452.00	346.36		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	409.98	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	409.98		
	<u>PETROLEUM</u>						
3	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26	276.27	183.65	12/2015 -	03/2015
4	RESITEMENT OF BILASPUR AND BISRAMPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]	1/2011	141.86 219.08	219.00	101.65	09/2016 -	12/2015
	Total		418.12 -	495.27	285.30		
	<u>POWER</u>						
5	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	200.10	11/2016 -	03/2016
6	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	49.24	05/2016 -	04/2016
	Total		2,680.42 -	2,680.42	249.34		
	Grand Total		5,059.28	5,136.43	1,290.98		

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	18,034
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,080.25
3	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,755.06
4	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	7,035.9
5	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,571.21
6	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	199.51
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	-	704.31
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	3000	9,987.13
9	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
10	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	983.58
11	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	-	779.9
12	NANDYAL-YERRAGUNTALA(NL), SCR	RAILWAYS	03/1996	155.74	164.36	739.76
13	KANPUR-KASGANJ-MATHURA(GC), NERR	RAILWAYS	03/1997	677.97	1062.36	1,615.26
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,500	1000	3,366.02

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	MUNEERABAD-MAHABOONAGAR(NL), SCR	RAILWAYS	04/1997	218.24	236.41	307.38
16	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	-	230.66
17	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	479.55
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	501.69	335.77	756.33
19	KATIHAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	744.08
20	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	630.94
21	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	RAILWAYS	04/1997	863.23	-	882.87
22	JALANDHAR-PATHANKOT-JAMMU-TAWI(LD), NR	RAILWAYS	03/2002	625.3	408.76	831.24
23	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	-	595.96
24	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	885.13
25	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,723.76
26	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3156.32	3,484.98
27	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	304.36
28	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	588.78

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	HARIDASPUR-PARADEEP(NL)	RAILWAYS	04/1996	301.64	-	321.71
30	RAJATGARH-BARANG(DL), ECR	RAILWAYS	04/1999	166.16	-	309.41
31	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.56	2,676.64
32	RAIL-CUM-ROAD BRIDGE AT MUNGERRA(NL), ECR	RAILWAYS	04/2002	921	-	1,500.51
33	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,307
34	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	913	3,137.84
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	282.06
36	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	282.3
37	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	268.5
38	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.8
39	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	251.5
40	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	366.8
41	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	173.8
42	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	207.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	280.3
44	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	328.6
45	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	550.3
46	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	285.3
47	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	385.1
48	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	316.31
49	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1,248.89
50	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	16,541.89
51	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,867.78
52	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	8,054.8
53	RAMPUR HEP(412 MW)	POWER	01/2007	2,047.03	-	3,329.96
54	KISHANGANGA HEP	POWER	01/2009	3,642.04	-	3,755.33
55	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	8,111
56	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	842.77

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	POWER	03/2011	2,569.25	-	2,605.17
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	477.9
59	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	798.47
60	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	452.94
61	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	826.55
62	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	303	417.7
63	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	209.48
64	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	374.71
65	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	651.09
66	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	RAILWAYS	04/2008	516.23	-	579.41
67	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
68	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.77
69	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,610.58
70	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	457.55

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.69
72	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	791.1
73	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	249.67
74	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
75	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.44
76	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
77	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	247.9
78	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,001.72
79	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	605.94
80	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	390	1,038.91
81	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	223.52
82	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	237.08
83	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	318.57
84	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.58
86	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
87	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
88	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	315.9
89	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
90	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	345.8
91	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	276.5
92	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	334.8
93	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.8
94	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
95	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,125
96	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	317.5
97	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	667.1
98	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,601

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,686
100	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
101	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,133
102	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
103	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
104	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
105	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
106	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
107	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,388
108	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
109	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
110	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	901.6
111	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273
112	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,208

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	761.3
114	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
115	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	808.7
116	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
117	4 LANNING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,786
118	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	665.8
119	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	611.8
120	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.6
121	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,392
122	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	941
123	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,178
124	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	2,445
125	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,374
126	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	842.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
128	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
129	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	776.4
130	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	991.7
131	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	408.1
132	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	835.6
133	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
134	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	462
135	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	633.3
136	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.2
137	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
138	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,922
139	4-LANING OF BRAHAMPURE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,610
140	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,934

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
141	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	726.4
142	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2011	682	-	752.7
143	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	363.4
144	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC	ROAD TRANSPORT AND HIGHWAYS	10/2011	1,565	-	1,592

Details of Delayed Projects w.r.t. Original and Revised Schedule

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,754.19	09/2010 03/2015	03/2015	54	62.57	
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	18,034.00	12/2008 10/2013	04/2015	76	31.12	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	5,764.00	12/2015 -	10/2017	22	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,496.00	12/2016 -	05/2018	17	0	
	Total		40,442.00 -	46,726.00	32,048.19					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 335.61	388.53	285.20	05/2012 -	12/2014	31	15.77	
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28 -	344.28	39.41	03/2014 -	01/2015	10	0	
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2016	12	0	
8	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	316.31	01/2011 04/2013	06/2016	65	0	
	Total		1,206.95 -	1,259.87	640.96					
	<u>COAL</u>									
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,080.25	06/2009 03/2013	12/2014	66	66.86	
10	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	104.95	10/2014 -	01/2015	3	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,693.37	03/2012 05/2014	02/2015	35	34.63	
12	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	404.65	03/2013 -	03/2015	24	-6.11	
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	7.45	03/2012 -	03/2015	36	0	
14	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	105.51	12/2012 -	03/2015	27	0	
15	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	150.58	03/2013 -	03/2015	24	0	
16	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	09/2015	30	478.5	
17	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,607.26	03/2014 -	03/2016	24	0	
18	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,575.92	03/2014 -	03/2016	24	0	
19	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44	50.37	
20	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.57	03/2014 -	03/2016	24	0	
21	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	44.90	03/2014 -	03/2016	24	0	
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0	
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.22	03/2012 -	03/2016	48	0	
24	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.63	03/2014 -	03/2016	24	0	
25	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60	0	
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	145.03	03/2012 -	03/2016	48	0	
27	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	0	
28	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.34	03/2010 -	03/2017	84	0	
29	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	105.70	03/2011 -	03/2017	72	-27.57	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72	0	
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	121.75	03/2013 -	03/2017	48	0	
32	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84	0	
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	171.46	03/2012 -	03/2017	60	0	
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	118.51	03/2013 -	03/2017	48	.02	
35	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	0	
36	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60	0	
37	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	57.02	03/2014 -	03/2017	36	0	
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.25	07/2016 -	03/2017	8	0	
39	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.30	03/2015 -	03/2018	36	0	
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	398.36	12/2015 -	04/2018	28	0	
42	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
43	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.68	03/2014 -	03/2020	72	0	
44	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	7,612.33	756.25	03/2013 -	03/2023	120	540.6	
	Total		28,664.59 -	39,219.11	17,077.45					
	<u>STEEL</u>									
46	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	167.28	09/2008 12/2013	12/2014	75	100.63	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
47	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,092.76	10/2009 10/2012	03/2015	65	41.41	
48	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	380.27	12/2011 01/2015	03/2015	39	105.2	
49	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,541.89	12/2011 -	03/2015	39	13.61	
50	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,627.12	03/2013 -	03/2015	24	0	
51	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,418.78	12/2012 -	05/2015	29	0	
52	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	335.82	09/2009 05/2012	06/2015	69	-6.25	
53	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	4,904.43	12/2011 -	06/2015	42	0	
54	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	414.19	04/2013 09/2014	06/2015	26	0	
55	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	116.37	11/2013 -	06/2015	19	0	
56	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	153.60	08/2014 -	06/2015	10	0	
57	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	102.83	09/2014 -	06/2015	9	0	
58	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	351.41	05/2013 01/2015	08/2015	27	0	
59	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	142.27	10/2013 -	08/2015	22	0	
60	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	109.08	12/2014 -	08/2015	8	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
61	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,679.23	03/2013 -	09/2015	30	0	
62	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	1,384.00	05/2015 -	12/2016	19	0	
	Total		80,463.54 -	86,417.50	63,921.33					
	<u>PETROLEUM</u>									
63	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	11/2014	38	-24.1	
64	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	579.52	12/2013 05/2014	12/2014	12	17.25	
65	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,306.51	03/2013 11/2014	12/2014	21	104.84	
66	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	7,155.15	02/2014 -	12/2014	10	0	
67	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	995.25	07/2012 -	12/2014	29	0	
68	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	12/2014	30	-38.7	
69	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	12/2014	2	0	
70	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	186.43	10/2011 12/2014	12/2014	38	0	
71	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 204.29	204.29	155.32	06/2012 09/2013	12/2014	30	41.85	
72	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	111.19	09/2013 -	02/2015	17	0	
73	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	109.49	12/2014 -	02/2015	2	0	
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	999.73	10/2011 -	02/2015	40	54.46	
75	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	154.93	07/2013 -	02/2015	19	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
76	PARADIP REFINERY PROJECT - [N16000058]OCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	27,513.95	11/2012 11/2013	03/2015	28	16.05	
77	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	271.39	06/2011 -	03/2015	45	-28.67	
78	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	221.08	08/2012 -	03/2015	31	-11.94	
79	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	673.97	05/2013 06/2014	03/2015	22	-11.62	
80	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	965.03	12/2014 -	03/2015	3	0	
81	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	107.05	09/2012 -	04/2015	31	-20.28	
82	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	99.82	03/2014 -	04/2015	13	0	
83	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,867.78	08/2010 03/2012	05/2015	57	73.4	
84	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-18.75	
85	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.15	03/2015 -	05/2015	2	29.42	
86	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	249.01	12/2014 -	05/2015	5	0	
87	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.28	05/2014 -	05/2015	12	-44.37	
88	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 04/2016	06/2015	110	820.2	
89	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,324.96	12/2012 -	06/2015	30	-21.1	
90	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	94.94	10/2014 -	10/2015	12	49.38	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
91	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	901.28	10/2011 -	10/2015	48	67.62	
92	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,316.95	01/2012 -	10/2015	45	70.49	
93	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	68.23	03/2015 11/2015	11/2015	8	37.72	
94	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	0	
95	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	470.29	09/2011 -	12/2015	51	0	
96	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23	0	
97	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	346.39	07/2015 -	12/2015	5	0	
98	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	208.21	08/2015 -	12/2015	4	0	
99	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.00	57.96	05/2015 -	12/2015	7	-5	
100	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,711.73	03/2013 03/2015	03/2016	36	-3.5	
101	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,035.09	09/2012 -	03/2016	42	0	
102	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	364.21	05/2014 -	03/2016	22	0	
103	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 03/2016	03/2016	15	0	
104	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
105	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	3.32	02/2016 -	07/2016	5	0	
106	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	1.94	03/2014 -	07/2016	28	0	
107	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.27	02/2016 04/2017	04/2017	14	31.51	
108	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 -	11/2017	46	-6.92	
109	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	0	
110	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	0	
111	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,040.60	12/2014 -	12/2018	48	0	
	Total		102,068.53 -	116,537.47	70,079.00					
	<u>POWER</u>									
112	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	3,288.28	3,329.96	03/2012 -	11/2014	32	60.64	
113	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	842.77	07/2013 08/2014	11/2014	16	136.3	
114	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,145.81	08/2012 -	12/2014	28	9.32	
115	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,408.16	08/2012 -	12/2014	28	0	
116	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	178.42	01/2014 -	12/2014	11	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
117	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	170.74	03/2014 -	12/2014	9	0	
118	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	83.96	10/2014 -	12/2014	2	0	
119	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,370.47	10/2014 -	01/2015	3	0	
120	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	249.97	08/2014 -	02/2015	6	0	
121	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35 -	1,935.35	929.48	12/2014 -	02/2015	2	0	
122	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	85.63	10/2014 -	02/2015	4	0	
123	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,111.00	08/2013 -	03/2015	19	0	
124	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,452.17	11/2012 -	03/2015	28	0	
125	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,033.99	08/2012 -	03/2015	31	0	
126	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,698.44	03/2013 -	03/2015	24	0	
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	443.02	07/2013 -	03/2015	20	0	
128	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,605.17	03/2014 -	03/2015	12	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
129	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,561.05	05/2014 -	03/2015	10	0	
130	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	345.71	11/2013 -	03/2015	16	0	
131	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	315.32	06/2014 -	03/2015	9	0	
132	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	765.90	08/2014 -	03/2015	7	0	
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	453.22	11/2014 -	03/2015	4	0	
134	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	621.33	08/2014 -	05/2015	9	0	
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	159.02	04/2015 -	05/2015	1	0	
136	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,474.00	12/2013 -	06/2015	18	0	
137	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	85.00	01/2013 -	06/2015	29	0	
138	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,361.96	11/2013 -	06/2015	19	0	
139	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,529.56	09/2014 -	06/2015	9	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
140	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,163.26	12/2013 -	06/2015	18	0	
141	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,028.33	07/2014 -	06/2015	11	0	
142	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,287.86	08/2014 -	06/2015	10	0	
143	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	457.70	02/2014 -	06/2015	16	0	
144	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	844.52	01/2015 -	06/2015	5	0	
145	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,882.21	10/2014 -	06/2015	8	0	
146	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	928.87	08/2013 -	09/2015	25	96.59	
147	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,248.00	04/2009 -	10/2015	78	59.48	
148	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	508.99	09/2010 -	12/2015	63	51.1	
149	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	891.45	01/2015 -	12/2015	11	0	
150	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,926.30	12/2012 -	12/2015	36	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 913.63	913.63	694.14	07/2006 12/2015	12/2015	113	147.78	
152	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	3,020.29	06/2015 -	12/2015	6	0	
153	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	952.31	12/2007 12/2009	03/2016	99	0	
154	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 -	03/2016	90	21.34	
155	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	420.06	11/2011 -	03/2016	52	0	
156	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	304.27	02/2012 -	03/2016	49	0	
157	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,000.58	10/2012 -	03/2016	41	0	
158	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,603.50	08/2013 -	03/2016	31	0	
159	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	702.64	11/2012 -	03/2016	40	0	
160	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,094.32	04/2013 -	03/2016	35	0	
161	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	920.43	11/2012 -	03/2016	40	0	
162	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	0	
163	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	13.30	09/2014 -	06/2016	21	0	
164	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,571.21	09/2009 -	07/2016	82	81.76	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
165	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,755.33	01/2016 -	11/2016	10	50.95	
166	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 4,653.95	4,653.95	3,460.15	12/2009 03/2017	03/2017	87	86.39	
167	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,851.00	07/2011 -	03/2017	68	0	
168	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	5,698.00	12/2016 -	05/2017	5	0	
169	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,212.00	09/2016 -	06/2017	9	0	
170	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	2,276.00	05/2017 -	06/2017	1	0	
171	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,419.00	11/2016 -	11/2017	12	0	
172	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,659.00	09/2017 -	12/2017	3	0	
173	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	09/2010	8,692.97 15,095.67	15,095.67	10,410.00	12/2009 -	03/2018	99	73.65	
174	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	146.00	08/2017 -	03/2018	7	0	
175	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	957.43	07/2010 02/2016	05/2018	94	79.77	
176	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,272.00	03/2013 -	05/2018	62	29.14	
177	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	509.51	07/2014 -	07/2018	48	50.31	
178	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,035.90	09/2010 -	12/2018	99	143.42	
179	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,755.06	09/2009 -	03/2019	114	36.9	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		203,485.03 -	235,123.58	140,573.70					
	<u>RAILWAYS</u>									
180	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	416.44	12/2009 03/2011	12/2014	60	300.67	
181	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,500.51	03/2009 12/2012	12/2014	69	156.57	
182	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	235.70	12/2008 -	12/2014	72	104.49	
183	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	150.55	06/2013 -	12/2014	18	-.01	
184	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.23	03/2007 03/2007	03/2015	96	160.76	
185	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	59.2	
186	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	04/2015	28	0	
187	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.66	06/2004 -	12/2015	138	72.62	
188	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,307.00	10/2007 12/2012	12/2015	98	367.76	
189	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	151.15	02/2006 -	12/2015	118	6.99	
190	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	16.41	
191	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,803.17	396.47	03/2004 12/2010	03/2016	144	263.95	
192	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	651.09	03/2013 -	03/2016	36	81.45	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
193	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	71.96	03/2014 -	03/2016	24	0	
194	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	178.21	12/2012 -	03/2016	39	45.41	
195	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,610.58	03/2009 -	03/2016	84	228.1	
196	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	124.46	12/2015 -	03/2016	3	88.4	
197	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,001.72	03/2007 -	03/2016	108	38.8	
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	128.62	03/2016 -	06/2016	3	0	
199	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	66.14	03/2015 -	12/2016	21	53.44	
200	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,116.53	374.71	03/2010 03/2017	03/2017	84	243.55	
201	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,366.02	04/2008 03/2014	06/2017	110	233.08	
202	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	482.43	03/2005 12/2008	12/2017	153	2019.62	
203	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	744.08	12/2010 -	03/2018	87	250.37	
204	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,723.76	12/2008 -	03/2018	111	245.34	
205	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.00	2,876.00	781.37	03/2014 -	03/2018	48	253.6	
206	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.00	2,820.25	195.01	04/2014 03/2020	03/2018	47	355.36	
207	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	29.40	04/2012 03/2016	03/2018	71	29.06	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
208	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	9,987.13	11/2002 -	12/2018	193	682.6	
209	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,676.64	03/2011 03/2014	03/2019	96	803.12	
210	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,913.27	03/2014 03/2019	03/2019	60	32.32	
211	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	
212	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.00	4,190.00	88.22	12/2015 -	03/2020	51	212.81	
213	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.34	03/2015 03/2020	03/2020	60	249.81	
	Total		29,123.25 -	85,426.94	36,528.59					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
214	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	11/2014	16	0	
215	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	11/2014	17	0	
216	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	11/2014	4	0	
217	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	268.50	09/2007 03/2014	12/2014	87	0	
218	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	12/2014	75	30.1	
219	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2014	70	0	
220	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2014	73	0	
221	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	12/2014	68	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
222	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	12/2014	75	0	
223	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	12/2014	74	0	
224	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	12/2014	78	0	
225	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	12/2014	79	0	
226	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	12/2014	78	0	
227	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	12/2014	65	85.58	
228	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	12/2014	58	0	
229	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	12/2014	55	0	
230	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	12/2014	27	0	
231	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	12/2014	31	0	
232	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	0	
233	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	0	
234	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	0	
235	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2014	21	0	
236	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	0	
237	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,208.00	11/2012 -	12/2014	25	0	
238	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2014	25	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
239	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2014	21	0	
240	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2014	17	0	
241	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	12/2014	22	0	
242	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	12/2014	16	0	
243	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2014	12	0	
244	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2014	19	0	
245	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	12/2014	14	0	
246	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2014	21	0	
247	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	536.00	01/2014 -	12/2014	11	0	
248	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	12/2014	9	0	
249	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2014	13	0	
250	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2014	6	0	
251	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.20	05/2014 -	12/2014	7	0	
252	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	12/2014	16	0	
253	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	12/2014	6	0	
254	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	458.30	10/2014 -	12/2014	2	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
255	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	12/2014	2	0	
256	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	01/2015	81	0	
257	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	01/2015	4	0	
258	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18	0	
259	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	03/2015	71	92.75	
260	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	03/2015	81	0	
261	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	03/2015	81	0	
262	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90	82.12	
263	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	03/2015	54	0	
264	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	106.5	
265	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	0	
266	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	03/2015	15	0	
267	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	0	
268	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	03/2015	20	0	
269	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	0	
270	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
271	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6	0	
272	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8	0	
273	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6	0	
274	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	276.50	06/2008 04/2015	04/2015	82	0	
275	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	0	
276	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13	0	
277	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	06/2015	120	0	
278	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	80.68	
279	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	33.7	
280	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0	
281	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	0	
282	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22	0	
283	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	0	
284	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	0	
285	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13	0	
286	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	11/2015	85	-8.95	
287	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
288	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	0	
289	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0	
290	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	0	
291	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21	0	
292	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	0	
293	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27	0	
294	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	0	
295	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	12/2015	28	0	
296	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	0	
297	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17	0	
298	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	0	
299	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	0	
300	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	42.25	
301	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	0	
302	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	159.90	08/2012 -	03/2016	43	0	
303	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0	
304	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0	
305	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2016	77	2.29	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
306	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0	
307	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
	Total		68,982.88 -	71,052.78	70,397.03					
	<u>SHIPPING AND PORTS</u>									
308	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 11/2014	11/2014	104	300	
309	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	1,049.37	12/2010 09/2012	01/2016	61	70.89	
	Total		1,378.00 -	2,698.56	1,189.17					
	<u>TELECOMMUNICATIONS</u>									
310	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	12/2014	71	0	
311	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	48.95	10/2010 11/2015	09/2015	59	0	
	Total		720.81 -	720.81	244.89					
	<u>URBAN DEVELOPMENT</u>									
312	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	22.43	11/2014 -	12/2014	1	0	
313	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	0	
314	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
315	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	0	
316	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	
317	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	0	
318	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	0	
319	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	0	
320	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	0	
321	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	
322	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
323	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	0	
324	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0	

(November 2014) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		6,058.86	6,058.86	1,104.15					
	Grand Total		562,594.44	691,241.48	433,804.46					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2014)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	04/2015	31.12	76
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	12/2014	15.77	31
	Total		335.61 -	23,335.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,388.61	06/2009 -	12/2014	66.86	66
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	02/2015	34.63	35
	Total		9,285.28 -	43,353.63				
	<u>PETROLEUM</u>							
10	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2014	41.85	30
11	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2015	49.38	12
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110
13	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	12/2014	17.25	12
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	02/2015	54.46	40

(November 2014)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72	8
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2015	29.42	2
19	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	12/2014	104.84	21
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2015	73.40	57
21	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51	14
22	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05	28
	Total		46,568.11 -	107,922.94				
	<u>POWER</u>							
23	TUJIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	913.63	07/2006 02/2015	12/2015	147.78	113
24	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30	16
25	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	12/2015	51.10	63
26	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
27	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	07/2016	81.76	82
28	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34	90
30	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	3,288.28	03/2012 -	11/2014	60.64	32
31	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	12/2014	9.32	28
32	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	05/2018	29.14	62

(November 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
35	KISHANGANGA HEP - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
36	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2019	36.90	114
37	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	15,300.00	09/2010 -	12/2018	143.42	99
	Total		32,560.98 -	163,026.92				
	<u>RAILWAYS</u>							
38	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67	60
39	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2017	2,019.62	153
40	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	12/2014	104.49	72
41	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
42	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20	36
43	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
44	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
45	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	12/2015	6.99	118
46	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
47	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
48	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
49	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76	96
50	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45	36
51	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
52	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,803.17	03/2004 -	03/2016	263.95	144
53	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
54	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
55	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2018	29.06	71

(November 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
56	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
57	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
58	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
59	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
60	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
61	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
62	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
63	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
64	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
65	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
66	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
67	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32	60
	Total		24,048.57 -	243,379.20				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
68	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10	75
69	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68	79
70	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58	65
71	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75	71
72	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12	90
73	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
74	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29	77
75	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93

(November 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50	40
	Total		2,866.62 -	248,340.33				
	<u>SHIPPING AND PORTS</u>							
77	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	11/2014	300.00	104
78	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	2,098.56	12/2010 -	01/2016	70.89	61
	Total		1,378.00 -	251,038.89				
	<u>STEEL</u>							
79	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	12/2014	100.63	75
80	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	03/2015	105.20	39
81	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2015	41.41	65
82	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	03/2015	13.61	39
	Total		23,538.89 -	280,561.74				
	Grand Total		157,245.06	1,383,906.18				

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2014)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	04/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	12/2014	15.77
	Total		335.61 -	23,335.53			
	<u>COAL</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,388.61	06/2009 -	12/2014	66.86
5	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
8	BHUBANESWAR OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	02/2015	34.63
10	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,925.87 -	44,042.32			
	<u>PETROCHEMICALS</u>						
12	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	52,962.32			
	<u>PETROLEUM</u>						

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
14	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2015	73.40
15	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05
16	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	12/2014	17.25
17	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	12/2014	104.84
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2015	29.42
19	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
20	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	02/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
21	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	462.79	10/2014 -	10/2015	49.38
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	02/2015	54.46
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
24	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
26	KOTA JOBNER PIPELINE PROJECT - [N16000170	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
27	RESITEMENT OF BILASPUR AND BISRAPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186	01/2011	141.86 -	219.00	09/2016 -	12/2015	54.38
28	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190	07/2014	419.04 -	762.00	01/2017 -	01/2017	81.84
29	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72
30	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	12/2014	41.85
	Total		62,296.27 -	135,993.90			
	<u>POWER</u>						
31	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2019	36.90
32	KOLDAM HEP (NTPC) - [180100211	01/2011	4,527.15 -	7,220.00	04/2009 -	10/2015	59.48
33	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	15,300.00	09/2010 -	12/2018	143.42
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
35	BARH STPP(3X660MW) NTPC - [180100242	09/2010	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65
36	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	07/2016	81.76
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34
38	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
39	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	05/2018	29.14
40	RAMPUR HEP(412 MW) - [N18000024	01/2007	2,047.03 -	3,288.28	03/2012 -	11/2014	60.64
41	KISHANGANGA HEP - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
42	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	721.81	09/2010 -	12/2015	51.10
43	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
44	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
45	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	12/2014	9.32
46	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30
47	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	913.63	07/2006 02/2015	12/2015	147.78
	Total		45,781.10 -	213,413.55			
	<u>RAILWAYS</u>						
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	10/2014	282.96
49	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
50	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
51	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	-	9.35
52	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
53	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
54	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
55	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
56	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,803.17	03/2004 -	03/2016	263.95

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
57	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
58	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
59	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
60	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	1,036.78	07/2012 -	-	130.40
61	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
62	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
63	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
64	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
65	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
66	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	12/2014	195.55
67	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
68	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
69	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
70	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
71	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
72	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
73	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
74	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
75	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
76	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	04/1997	863.23 -	1,072.51	- -	03/2015	24.24
77	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
78	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	900.00	- -	-	800.00
79	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
80	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,045.20	- -	-	216.73
81	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
82	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,176.10	12/2006 -	-	202.58
83	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
84	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
85	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2017	2,019.62
86	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
87	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
88	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
89	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
91	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
92	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
93	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
94	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	-	160.32
95	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
96	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
97	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	12/2014	104.49
98	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
99	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
100	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
101	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
102	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
103	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
104	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
105	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	280.00	02/2006 -	12/2015	6.99
106	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
107	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
108	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
109	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
110	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
111	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
112	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
113	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
114	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
115	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
116	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
117	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
118	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
119	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32
120	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20
121	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	-	385.76
122	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
123	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
124	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
125	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
126	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
127	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
128	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
129	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
130	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
131	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
132	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
133	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
134	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
135	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
136	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
137	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
138	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
139	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
140	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
141	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
142	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
143	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
144	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
145	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
146	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
147	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
148	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
149	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
150	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
151	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
152	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
153	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
154	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
155	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
156	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
157	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
158	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
159	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
160	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
161	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
162	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	275.00	- -	-	56.76
163	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
164	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
165	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	888.65	- -	03/2018	252.64
166	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
167	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
168	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
169	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
170	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
171	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
172	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95 -	- -	-	16.29
173	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90 -	- -	03/2020	30.00
174	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57 -	- -	03/2018	180.56
175	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28 -	- -	03/2017	63.25
176	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58 -	- -	03/2018	162.68
177	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55 -	- -	03/2018	216.06
178	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10 -	- -	03/2018	45.17
179	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06 -	- -	03/2019	47.95
180	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55 -	04/2012 -	03/2018	29.06
181	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00 -	- -	-	33.02
182	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05 -	- -	-	400.91
183	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70 -	- -	-	0.72
184	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00 -	- -	03/2015	105.59
185	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16 -	- -	01/2015	170.55
186	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01 -	- -	-	97.26
187	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91 -	- -	-	651.97
188	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30 -	- -	-	160.97
189	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00 -	- -	-	985.42
190	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54 -	- -	-	163.25
191	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99 -	- -	-	183.41
192	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43 -	- -	-	24.09
193	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65 -	- -	-	57.65
194	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47 -	- -	-	47.93
195	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00 -	- -	-	79.63

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
196	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
197	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
198	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
199	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
200	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
201	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
202	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
203	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
204	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
205	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
206	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
207	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
208	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
209	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
210	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		87,659.91 -	428,026.67			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
211	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
212	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75
213	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
214	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
215	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58
216	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
217	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29

(November 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
218	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
219	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,866.62 -	432,987.80			
	<u>SHIPPING AND PORTS</u>						
220	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,098.56	12/2010 -	01/2016	70.89
221	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	11/2014	300.00
	Total		1,378.00 -	435,686.36			
	<u>STEEL</u>						
222	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2015	41.41
223	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	03/2015	105.20
224	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	12/2014	100.63
225	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	03/2015	13.61
	Total		23,538.89 -	465,209.21			
	<u>URBAN DEVELOPMENT</u>						
226	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
227	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	476,991.29			
	Grand Total		262,415.06	2,731,595.95			

List of Projects on schedule w.r.t. Latest Schedule

(November 2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	9/2003	3,492.00 -	5,677.00	4,754.19	09/2010 03/2015	03/2015
	Total		3,492.00 -	5,677.00	4,754.19		
	<u>COAL</u>						
2	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	281.79	03/2015 -	03/2015
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	664.83	03/2016 -	03/2016
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.00 -	490.10	184.38	03/2017 -	03/2017
5	BATURA OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091	6/2011	1,131.28 -	1,131.28	43.25	03/2018 -	03/2018
8	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
9	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	430.14	68.12	03/2016 -	03/2016
10	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
11	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
12	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
13	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
14	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	43.38	03/2018 -	03/2018
15	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
16	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
17	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
18	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	97.75	03/2020 -	03/2020

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	64.72	03/2016 -	03/2016
21	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
22	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	223.58	03/2016 -	03/2016
23	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	70.54	03/2015 -	03/2015
24	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
	Total		16,419.11 -	16,047.16	1,876.52		
	<u>FERTILISERS</u>						
25	SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009	10/2014	197.79 -	197.79	-	02/2017 -	02/2017
	Total		197.79 -	197.79	.00		
	<u>PETROLEUM</u>						
26	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132	3/2012	5,608.40 -	5,608.40	3,027.35	05/2015 -	05/2015
27	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	9/2012	871.35 -	1,200.00	68.23	03/2015 11/2015	11/2015
28	GAS TURBINE GENERATION SET - [N18000146	7/2009	216.88 -	216.88	186.43	10/2011 12/2014	12/2014
29	TWENTY NOS. FEEDER GAS LINES - [N16000192	3/2009	228.64 -	228.64	-	12/2016 -	12/2016
30	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190	7/2014	419.04 -	762.00	2.89	01/2017 -	01/2017
31	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189	7/2014	716.00 -	716.00	-	01/2017 -	01/2017
32	MH NORTH REDEVELOPMENT PHASE III - [N16000188	6/2014	5,706.47 -	5,706.47	0.28	05/2017 -	05/2017
33	RESID UPGRADATION PROJECT - [N16000184	2/2011	3,110.36 -	3,110.36	319.32	11/2015 -	11/2015
34	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
35	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181	3/2013	2,913.10 -	2,913.10	9.50	05/2016 -	05/2016
36	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY [N16000180	2/2014	163.88 -	163.88	6.07	07/2016 -	07/2016
37	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
38	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.27	09/2017 -	09/2017
39	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
40	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 -	04/2016
41	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	49.94	01/2016 -	01/2016
42	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	352.56	10.60	03/2017 -	03/2017
43	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	270.00	-	12/2014 03/2016	03/2016
44	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.52	04/2015 -	04/2015
45	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	194.35	04/2015 -	04/2015
46	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	0.27	02/2016 04/2017	04/2017
47	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	36.33	07/2016 -	07/2016
48	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	701.00	335.61	11/2015 -	11/2015
49	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	794.82	11/2015 -	11/2015
50	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	4,032.33	05/2016 -	05/2016
	Total		65,532.19 -	69,130.66	9,285.84		
	POWER						
51	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	3,460.15	12/2009 03/2017	03/2017
52	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014
53	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	924.13	02/2015 -	02/2015
54	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	913.63	694.14	07/2006 12/2015	12/2015
55	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,355.00	08/2015 -	08/2015
56	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145	6/2012	1,909.24 -	1,909.24	658.43	06/2015 -	06/2015
58	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
59	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
60	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
61	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
62	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168	6/2014	5,151.37 -	5,151.37	-	03/2018 -	03/2018
63	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
64	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166	2/2014	378.71 -	378.71	11.20	10/2016 -	10/2016
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
66	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
67	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
68	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
69	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
70	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160	2/2014	243.53 -	243.53	11.00	08/2016 -	08/2016
71	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158	2/2014	539.82 -	539.82	2.00	06/2016 -	06/2016
73	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
74	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153	9/2013	1,575.30 -	1,575.30	135.70	05/2016 -	05/2016
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152	9/2013	680.69 -	680.69	75.99	03/2016 -	03/2016

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144	3/2013	2,514.88 -	2,514.88	288.75	12/2015 -	12/2015
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	435.09	03/2015 -	03/2015
	Total		36,195.49 -	38,897.45	8,051.58		
	<u>RAILWAYS</u>						
78	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	115.88	02/2015 -	02/2015
79	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	4/2006	325.00 -	1,116.53	374.71	03/2010 03/2017	03/2017
80	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00 -	7,012.84	1,913.27	03/2014 03/2019	03/2019
81	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	4/2010	2,913.51 -	2,913.51	500.80	03/2016 -	03/2016
82	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	4/2006	850.00 -	2,973.42	10.34	03/2015 03/2020	03/2020
83	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	2.03	02/2020 -	02/2020
84	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	209.00	2.06	12/2016 -	12/2016
85	DELANG-PURI DOUBLING - [N22000320	3/2011	165.16 -	234.71	116.12	03/2015 -	03/2015
86	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245	4/2010	423.66 -	423.66	215.50	03/2017 -	03/2017
87	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
88	PLASSEY-JIAGANJ DOUBLING - [N22000220	4/2011	248.07 -	248.07	29.10	03/2015 -	03/2015
89	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214	4/2012	714.10 -	714.10	51.98	04/2016 -	04/2016
90	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	4.66	02/2019 -	02/2019
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016
92	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	4/2008	829.74 -	829.74	79.26	03/2015 -	03/2015
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	4/2010	3,951.98 -	4,259.48	542.29	03/2016 -	03/2016
	Total		23,025.90 -	32,803.63	5,700.10		

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
94	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	01/2015
95	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	276.50	06/2008 04/2015	04/2015
96	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	258.40	04/2010 01/2016	01/2016
97	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015
98	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
99	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.40	11/2015 -	11/2015
100	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
101	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
102	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015
103	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2015
104	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
105	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	368.50	06/2015 -	06/2015
	Total		13,710.62 -	13,802.57	4,448.60		
	<u>SHIPPING AND PORTS</u>						
106	ENNORE MANALI EXPRESS WAY ,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 11/2014	11/2014
	Total		150.00 -	600.00	139.80		
	<u>STEEL</u>						
107	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	154.50	06/2015 -	06/2015
108	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	20.22	05/2016 -	05/2016
109	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	31.27	04/2016 -	04/2016
110	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]	4/2014	188.93 -	188.93	8.28	04/2015 -	04/2015

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,456.56 -	1,456.56	214.27		
	<u>URBAN DEVELOPMENT</u>						
111	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
112	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
113	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	4/2014	332.72 -	332.72	0.08	09/2016 -	09/2016
114	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
115	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	2.04	03/2017 -	03/2017
	Total		66,699.91 -	66,699.91	8,701.61		
	Grand Total		226,879.57	245,312.73	43,172.51		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(November 2014)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	DEV OF G1 AND GS-15 (ONGCL) - [160100231	4/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 04/2016	06/2015
	Total		429.82 -	3,955.21	3,413.13		
	<u>CIVIL AVIATION</u>						
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	346.36	03/2015 -	02/2015
	Total		452.00 -	452.00	346.36		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	409.98	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	409.98		
	<u>PETROLEUM</u>						
4	KOTA JOBNER PIPELINE PROJECT - [N16000170	4/2011	276.26	276.27	183.65	12/2015 -	03/2015
5	RESITEMENT OF BILASPUR AND BISRAMPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186	1/2011	141.86 219.08	219.00	101.65	09/2016 -	12/2015
	Total		418.12 -	495.27	285.30		
	<u>POWER</u>						
6	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	200.10	11/2016 -	03/2016
7	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,364.52	49.24	05/2016 -	04/2016
	Total		2,680.42 -	2,680.42	249.34		
	<u>RAILWAYS</u>						
8	BHAIRABI SAIRONG, NL, NEFR - [N22000100	4/2008	619.34 619.00	2,820.25	195.01	04/2014 03/2020	03/2018

(November 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		619.34 -	2,820.25	195.01		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
9	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	12/2014
	Total		160.00 -	160.00	211.80		
	<u>TELECOMMUNICATIONS</u>						
10	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096	10/2009	384.00 -	384.00	48.95	10/2010 11/2015	09/2015
	Total		384.00 -	384.00	48.95		
	Grand Total		6,652.44	12,455.89	5,159.87		

List of Delayed Projects w.r.t. Latest Schedule

(November 2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	18,034.00	12/2008 10/2013	04/2015	76	18
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,764.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,496.00	12/2016 -	05/2018	17	-
	Total		36,950.00 -	41,049.00	27,294.00				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	285.20	05/2012 -	12/2014	31	-
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	39.41	03/2014 -	01/2015	10	-
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2016	12	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	316.31	01/2011 04/2013	06/2016	65	38
	Total		1,206.95 -	1,259.87	640.96				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,080.25	06/2009 03/2013	12/2014	66	21
9	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	104.95	10/2014 -	01/2015	3	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,693.37	03/2012 05/2014	02/2015	35	9
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	404.65	03/2013 -	03/2015	24	-
12	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	7.45	03/2012 -	03/2015	36	-
13	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	105.51	12/2012 -	03/2015	27	-
14	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	150.58	03/2013 -	03/2015	24	-
15	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	09/2015	30	36
16	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,607.26	03/2014 -	03/2016	24	-
17	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,575.92	03/2014 -	03/2016	24	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44	-
19	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.57	03/2014 -	03/2016	24	-
20	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	44.90	03/2014 -	03/2016	24	-
21	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
22	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.22	03/2012 -	03/2016	48	-
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.63	03/2014 -	03/2016	24	-
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60	-
25	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	145.03	03/2012 -	03/2016	48	-
26	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	-
27	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.34	03/2010 -	03/2017	84	-
28	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	105.70	03/2011 -	03/2017	72	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	121.75	03/2013 -	03/2017	48	-
31	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84	-
32	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	171.46	03/2012 -	03/2017	60	-
33	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	118.51	03/2013 -	03/2017	48	-
34	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60	-
36	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	57.02	03/2014 -	03/2017	36	-
37	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.25	07/2016 -	03/2017	8	-
38	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.30	03/2015 -	03/2018	36	-
39	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	-
40	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	398.36	12/2015 -	04/2018	28	-
41	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-
42	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.68	03/2014 -	03/2020	72	-
43	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
44	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	7,612.33	756.25	03/2013 -	03/2023	120	-
	Total		28,664.59 -	39,219.11	17,077.45				
	<u>STEEL</u>								
45	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	167.28	09/2008 12/2013	12/2014	75	12
46	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,092.76	10/2009 10/2012	03/2015	65	29
47	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	380.27	12/2011 01/2015	03/2015	39	2
48	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,541.89	12/2011 -	03/2015	39	-
49	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,627.12	03/2013 -	03/2015	24	-
50	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,418.78	12/2012 -	05/2015	29	-
51	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	335.82	09/2009 05/2012	06/2015	69	37
52	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,904.43	12/2011 -	06/2015	42	-
53	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	414.19	04/2013 09/2014	06/2015	26	9
54	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	116.37	11/2013 -	06/2015	19	-
55	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	153.60	08/2014 -	06/2015	10	-
56	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	102.83	09/2014 -	06/2015	9	-
57	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	351.41	05/2013 01/2015	08/2015	27	7
58	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	142.27	10/2013 -	08/2015	22	-
59	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	109.08	12/2014 -	08/2015	8	-
60	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,679.23	03/2013 -	09/2015	30	-
61	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	1,384.00	05/2015 -	12/2016	19	-
	Total		80,463.54 -	86,417.50	63,921.33				
	<u>PETROLEUM</u>								

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	11/2014	38	32
63	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	579.52	12/2013 05/2014	12/2014	12	7
64	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,306.51	03/2013 11/2014	12/2014	21	1
65	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	7,155.15	02/2014 -	12/2014	10	-
66	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	995.25	07/2012 -	12/2014	29	-
67	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	12/2014	30	-
68	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	12/2014	2	-
69	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 204.29	204.29	155.32	06/2012 09/2013	12/2014	30	15
70	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	111.19	09/2013 -	02/2015	17	-
71	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	109.49	12/2014 -	02/2015	2	-
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	999.73	10/2011 -	02/2015	40	-
73	MARKETING TERMINAL AT PARADEEP - [N16000168]OCL,ODISHA	07/2009	199.75 -	199.75	154.93	07/2013 -	02/2015	19	-
74	PARADIP REFINERY PROJECT - [N16000058]OCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	27,513.95	11/2012 11/2013	03/2015	28	16
75	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	271.39	06/2011 -	03/2015	45	-
76	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	221.08	08/2012 -	03/2015	31	-
77	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	673.97	05/2013 06/2014	03/2015	22	9
78	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	965.03	12/2014 -	03/2015	3	-
79	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	107.05	09/2012 -	04/2015	31	-
80	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	99.82	03/2014 -	04/2015	13	-
81	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,867.78	08/2010 03/2012	05/2015	57	38
82	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-
83	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.15	03/2015 -	05/2015	2	-
84	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	249.01	12/2014 -	05/2015	5	-

(November 2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
85	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.28	05/2014 -	05/2015	12	-
86	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,324.96	12/2012 -	06/2015	30	-
87	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	94.94	10/2014 -	10/2015	12	-
88	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPR,L,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	901.28	10/2011 -	10/2015	48	-
89	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,L,KERALA	01/2006	993.00 1,693.00	1,693.00	1,316.95	01/2012 -	10/2015	45	-
90	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
91	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	470.29	09/2011 -	12/2015	51	-
92	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23	-
93	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	346.39	07/2015 -	12/2015	5	-
94	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	208.21	08/2015 -	12/2015	4	-
95	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.00	57.96	05/2015 -	12/2015	7	-
96	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,711.73	03/2013 03/2015	03/2016	36	12
97	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,035.09	09/2012 -	03/2016	42	-
98	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	364.21	05/2014 -	03/2016	22	-
99	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
100	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	3.32	02/2016 -	07/2016	5	-
101	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	1.94	03/2014 -	07/2016	28	-
102	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 -	11/2017	46	-
103	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	-
104	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	-
105	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,040.60	12/2014 -	12/2018	48	-
	Total		96,767.41 -	106,275.44	66,410.94				

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
106	RAMPUR HEP(412 MW) - [N18000024]SJVNL,HIMACHAL PRADESH	01/2007	2,047.03 -	3,288.28	3,329.96	03/2012 -	11/2014	32	-
107	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	842.77	07/2013 08/2014	11/2014	16	3
108	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,145.81	08/2012 -	12/2014	28	-
109	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,408.16	08/2012 -	12/2014	28	-
110	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	178.42	01/2014 -	12/2014	11	-
111	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	170.74	03/2014 -	12/2014	9	-
112	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	83.96	10/2014 -	12/2014	2	-
113	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,370.47	10/2014 -	01/2015	3	-
114	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	249.97	08/2014 -	02/2015	6	-
115	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35 -	1,935.35	929.48	12/2014 -	02/2015	2	-
116	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	85.63	10/2014 -	02/2015	4	-
117	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,111.00	08/2013 -	03/2015	19	-
118	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,452.17	11/2012 -	03/2015	28	-
119	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,033.99	08/2012 -	03/2015	31	-
120	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,698.44	03/2013 -	03/2015	24	-
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	443.02	07/2013 -	03/2015	20	-
122	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,605.17	03/2014 -	03/2015	12	-
123	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,561.05	05/2014 -	03/2015	10	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
124	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	345.71	11/2013 -	03/2015	16	-
125	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	315.32	06/2014 -	03/2015	9	-
126	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	765.90	08/2014 -	03/2015	7	-
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	453.22	11/2014 -	03/2015	4	-
128	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	621.33	08/2014 -	05/2015	9	-
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	159.02	04/2015 -	05/2015	1	-
130	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,474.00	12/2013 -	06/2015	18	-
131	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	85.00	01/2013 -	06/2015	29	-
132	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,361.96	11/2013 -	06/2015	19	-
133	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,529.56	09/2014 -	06/2015	9	-
134	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,163.26	12/2013 -	06/2015	18	-
135	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,028.33	07/2014 -	06/2015	11	-
136	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,287.86	08/2014 -	06/2015	10	-
137	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	457.70	02/2014 -	06/2015	16	-
138	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	844.52	01/2015 -	06/2015	5	-
139	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,882.21	10/2014 -	06/2015	8	-
140	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	928.87	08/2013 -	09/2015	25	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
141	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,248.00	04/2009 -	10/2015	78	-
142	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	508.99	09/2010 -	12/2015	63	-
143	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	891.45	01/2015 -	12/2015	11	-
144	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,926.30	12/2012 -	12/2015	36	-
145	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	3,020.29	06/2015 -	12/2015	6	-
146	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	952.31	12/2007 12/2009	03/2016	99	75
147	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 -	03/2016	90	-
148	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	420.06	11/2011 -	03/2016	52	-
149	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	304.27	02/2012 -	03/2016	49	-
150	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,000.58	10/2012 -	03/2016	41	-
151	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,603.50	08/2013 -	03/2016	31	-
152	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	702.64	11/2012 -	03/2016	40	-
153	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,094.32	04/2013 -	03/2016	35	-
154	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	920.43	11/2012 -	03/2016	40	-
155	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	-
156	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	13.30	09/2014 -	06/2016	21	-
157	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,571.21	09/2009 -	07/2016	82	-
158	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,755.33	01/2016 -	11/2016	10	-
159	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,851.00	07/2011 -	03/2017	68	-
160	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	5,698.00	12/2016 -	05/2017	5	-
161	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,212.00	09/2016 -	06/2017	9	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
162	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	2,276.00	05/2017 -	06/2017	1	-
163	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,419.00	11/2016 -	11/2017	12	-
164	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,659.00	09/2017 -	12/2017	3	-
165	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	09/2010	8,692.97 15,095.67	15,095.67	10,410.00	12/2009 -	03/2018	99	-
166	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	146.00	08/2017 -	03/2018	7	-
167	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	957.43	07/2010 02/2016	05/2018	94	27
168	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,272.00	03/2013 -	05/2018	62	-
169	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	509.51	07/2014 -	07/2018	48	-
170	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,035.90	09/2010 -	12/2018	99	-
171	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,755.06	09/2009 -	03/2019	114	-
	Total		200,619.41 -	229,556.00	136,419.41				
	<u>RAILWAYS</u>								
172	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	416.44	12/2009 03/2011	12/2014	60	45
173	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,500.51	03/2009 12/2012	12/2014	69	24
174	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	235.70	12/2008 -	12/2014	72	-
175	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	150.55	06/2013 -	12/2014	18	-
176	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.23	03/2007 03/2007	03/2015	96	96
177	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	15
178	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	04/2015	28	-
179	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.66	06/2004 -	12/2015	138	-
180	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,307.00	10/2007 12/2012	12/2015	98	36
181	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	151.15	02/2006 -	12/2015	118	-
182	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
183	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,803.17	396.47	03/2004 12/2010	03/2016	144	63
184	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	651.09	03/2013 -	03/2016	36	-
185	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	71.96	03/2014 -	03/2016	24	-
186	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	178.21	12/2012 -	03/2016	39	-
187	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,610.58	03/2009 -	03/2016	84	-
188	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	124.46	12/2015 -	03/2016	3	-
189	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,001.72	03/2007 -	03/2016	108	-
190	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	128.62	03/2016 -	06/2016	3	-
191	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	66.14	03/2015 -	12/2016	21	-
192	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,366.02	04/2008 03/2014	06/2017	110	39
193	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	482.43	03/2005 12/2008	12/2017	153	108
194	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	744.08	12/2010 -	03/2018	87	-
195	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,723.76	12/2008 -	03/2018	111	-
196	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.00	2,876.00	781.37	03/2014 -	03/2018	48	-
197	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	29.40	04/2012 03/2016	03/2018	71	24
198	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	9,987.13	11/2002 -	12/2018	193	-
199	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,676.64	03/2011 03/2014	03/2019	96	60
200	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
201	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.00	4,190.00	88.22	12/2015 -	03/2020	51	-
	Total		22,028.91 -	71,503.90	34,035.26				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
202	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	11/2014	16	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
203	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	11/2014	17	-
204	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	11/2014	4	-
205	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	268.50	09/2007 03/2014	12/2014	87	9
206	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	12/2014	75	-
207	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2014	70	-
208	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2014	73	-
209	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	12/2014	68	-
210	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	12/2014	75	-
211	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	12/2014	74	-
212	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	12/2014	78	-
213	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	12/2014	78	-
214	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	12/2014	65	-
215	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	12/2014	58	-
216	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	12/2014	55	-
217	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	12/2014	27	-
218	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	12/2014	31	-
219	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	-
220	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	-
221	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	-
222	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2014	21	-
223	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	-
224	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,208.00	11/2012 -	12/2014	25	-
225	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2014	25	-
226	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2014	21	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
227	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2014	17	-
228	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	12/2014	22	-
229	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	12/2014	16	-
230	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2014	12	-
231	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2014	19	-
232	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	12/2014	14	-
233	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2014	21	-
234	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	536.00	01/2014 -	12/2014	11	-
235	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	12/2014	9	-
236	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2014	13	-
237	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2014	6	-
238	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.20	05/2014 -	12/2014	7	-
239	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	12/2014	16	-
240	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	12/2014	6	-
241	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	458.30	10/2014 -	12/2014	2	-
242	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	12/2014	2	-
243	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	01/2015	4	-
244	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18	-
245	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	03/2015	71	-
246	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	03/2015	81	-
247	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	03/2015	81	-
248	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90	-
249	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	03/2015	54	-
250	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
251	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	-
252	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	03/2015	15	-
253	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	-
254	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	03/2015	20	-
255	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	-
256	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	-
257	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6	-
258	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8	-
259	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6	-
260	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	-
261	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13	-
262	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	06/2015	120	-
263	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	-
264	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	-
265	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	-
266	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	-
267	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22	-
268	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	-
269	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	-
270	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13	-
271	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	11/2015	85	-
272	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	-
273	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
274	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	-
275	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	-
276	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21	-
277	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	-
278	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27	-
279	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	-
280	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	12/2015	28	-
281	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	-
282	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17	-
283	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	-
284	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	-
285	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	-
286	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	159.90	08/2012 -	03/2016	43	-
287	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	-
288	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	-
289	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2016	77	-
290	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	-
291	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
	Total		68,204.31 -	70,182.26	69,467.83				
	<u>SHIPPING AND PORTS</u>								
292	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	1,049.37	12/2010 09/2012	01/2016	61	40
	Total		1,228.00 -	2,098.56	1,049.37				
	<u>TELECOMMUNICATIONS</u>								
293	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	12/2014	71	-

(November 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		336.81 -	336.81	195.94				
	<u>URBAN DEVELOPMENT</u>								
294	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	22.43	11/2014 -	12/2014	1	-
295	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	-
296	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	-
297	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	-
298	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
299	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	-
300	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	-
301	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	-
302	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	-
303	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
304	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
305	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	-
306	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-
	Total		6,058.86 -	6,058.86	1,104.15				
	Grand Total		542,528.79	653,957.31	417,616.64				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(November 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	12/2014	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,388.61	06/2009 -	12/2014	66.86
3	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
4	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
5	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
7	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		4,808.99 -	13,264.19			
	<u>PETROCHEMICALS</u>						
8	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	22,184.19			
	<u>PETROLEUM</u>						
9	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2015	29.42
10	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
11	KOTA JOBNER PIPELINE PROJECT - [N16000170]	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
12	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	07/2014	419.04 -	762.00	01/2017 -	01/2017	81.84
	Total		16,979.93 -	42,392.11			
	<u>POWER</u>						

(November 2014)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
13	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2019	36.90
14	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	12/2018	143.42
15	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	07/2016	81.76
16	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	3,288.28	03/2012 -	11/2014	60.64
17	KISHANGANGA HEP - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
18	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
19	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30
	Total		19,867.96 -	78,513.19			
	<u>RAILWAYS</u>						
20	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
21	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
22	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	-	9.35
23	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
24	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
25	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
26	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
27	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,803.17	03/2004 -	03/2016	263.95
28	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
29	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
30	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
31	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	1,036.78	07/2012 -	-	130.40
32	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
33	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97

(November 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
34	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
35	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
36	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
37	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	12/2014	195.55
38	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
39	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
40	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
41	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
42	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
44	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
45	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
46	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
47	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	04/1997	863.23 -	1,072.51	- -	03/2015	24.24
48	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	900.00	- -	-	800.00
50	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
51	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,045.20	- -	-	216.73
52	NEW MAYNAGURI TO JOGIGHOPA VIA CHAGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
53	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,176.10	12/2006 -	-	202.58
54	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
55	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01

(November 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
56	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2017	2,019.62
57	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
58	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
59	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
60	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
61	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
62	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
63	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
64	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
65	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	-	160.32
66	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
67	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
68	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
69	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
72	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
74	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
75	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	261.70 -	280.00	02/2006 -	12/2015	6.99
76	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
77	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N220000052	04/2003	98.74 -	337.30	- -	03/2012	241.60
78	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
79	BHOPAL BINA 3D LINE DOUBLING - [N220000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41

(November 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
80	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
81	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
82	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
83	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
84	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
85	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
86	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
87	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
88	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32
89	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20
90	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	-	385.76
91	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
92	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
93	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
94	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
95	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45
96	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
97	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
98	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
99	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
100	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
101	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10

(November 2014)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
102	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
103	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
104	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
105	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
106	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
107	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
108	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
109	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
110	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
111	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
112	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
113	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
114	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
115	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
116	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
117	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
118	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
119	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
120	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
121	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
122	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
123	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17

(November 2014)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
124	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
125	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
126	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
127	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	275.00	- -	-	56.76
128	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
129	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
130	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	888.65	- -	03/2018	252.64
131	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
132	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
133	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
134	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
135	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
136	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
137	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
138	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
139	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
140	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
141	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
142	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
143	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
144	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
145	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2018	29.06
146	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02

(November 2014)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
147	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
148	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
149	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
150	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
151	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
152	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
153	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
154	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
155	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
156	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
157	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
158	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
159	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
160	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
161	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
162	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
163	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
164	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
165	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
166	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
167	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
168	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
169	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
170	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70

(November 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
171	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
172	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
173	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
174	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
175	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		81,043.21 -	280,522.40			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
177	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75
178	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
179	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
180	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58
181	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29
182	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
183	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,649.01 -	285,173.97			
	<u>SHIPPING AND PORTS</u>						
184	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,098.56	12/2010 -	01/2016	70.89
185	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	11/2014	300.00
	Total		1,378.00 -	287,872.53			
	<u>STEEL</u>						
186	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	03/2015	13.61
	Total		14,443.00 -	304,280.53			

(November 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>URBAN DEVELOPMENT</u>						
187	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
	Total		6,395.00 -	315,889.53			
	Grand Total		153,361.32	1,630,481.17			
