

397th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
November, 2018



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for November 2018 contains information on the status of the 1443 Central Sector Infrastructure Projects costing ₹150 crore and above. During November 2018, 12 projects (7 projects in Railways, 2 projects in Telecommunication and 1 project each is in Civil Aviation, Petroleum and Urban Development sectors) have reported completion.

2. During the reference month, out of 1443 projects, 360 projects are delayed with respect to their original schedules and 21 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 21 projects, 8 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	607	100	5	1
2	RAILWAYS	371	94	6	4
3	PETROLEUM	139	25	1	1
4	POWER	105	56	2	2
5	COAL	96	35	3	0
6	URBAN DEVELOPMENT	58	22	2	0
7	HEALTH AND FAMILY WELFARE	22	10	0	0
8	STEEL	13	2	1	0
9	TELECOMMUNICATIONS	7	5	0	0
10	FERTILISERS	6	2	0	0
11	MINES	5	2	1	0
12	SHIPPING AND PORTS	5	4	0	0
13	ATOMIC ENERGY	4	0	0	0
14	HEAVY INDUSTRY	2	1	0	0
15	DEFENCE PRODUCTION	2	1	0	0
16	CIVIL AVIATION	1	1	0	0
Total		1443	360	21	8

3. Total original cost of implementation of the 1443 projects was ₹18,30,362.48 crore and their anticipated completion cost is likely to be ₹21,51,136.69 crore, which reflects overall cost overruns of ₹3,20,774.21 crore (17.53% of original cost). The expenditure incurred on these projects till November 2018 is ₹7,97,496.44 crore, which is 37.07% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-12-2018)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	74.68
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
	CIVIL AVIATION				
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
	COAL				
4	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
5	BHANEGAON OC	02/2015	187.94	409.68	117.98
6	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
7	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
8	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
	DEFENCE PRODUCTION				
9	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	291.29	1.87
10	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	170.37	1.60
	FERTILISERS				
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
	HEALTH AND FAMILY WELFARE				
12	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	13.31
13	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
14	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	322.00	2.88
	HEAVY INDUSTRY				
15	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
	PETROLEUM				
16	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	83.01
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	330.35	62.78
20	PARADIP HALDIA DURGAPUR LPG PIPELINE	02/2011	913.00	1330.00	45.67
	POWER				
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
22	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4401.90	165.65
23	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1078.31	156.12
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
25	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	139.69
	RAILWAYS				
26	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
27	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	1800.00	1391.30
28	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
29	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
30	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	1025.00	723.76
	ROAD TRANSPORT AND HIGHWAYS				
31	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	880.06
32	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	114.56
33	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50

34	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
35	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
SHIPPING AND PORTS					
36	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
37	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
38	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
39	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
TELECOMMUNICATIONS					
40	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
41	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
42	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
43	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
44	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
45	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-12-2018)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	2608.00
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
4	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
5	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
6	BHANEAGON OC	02/2015	187.94	409.68	221.74
7	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
8	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
DEFENCE PRODUCTION					
9	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	291.29	5.34
10	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	170.37	2.68
FERTILISERS					

11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
12	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	22.48
13	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
14	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	322.00	9.01
15	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROLEUM					
16	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	03/2014	3076.00	4190.00	1114.00
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	715.36
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
19	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	5245.96	657.67
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
POWER					
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
22	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
23	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	5475.21
24	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9141.97	4387.55
25	BONGAIGAON THERMAL POWER PROJECT	01/2008	4375.35	8150.00	3774.65
RAILWAYS					
26	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
27	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
28	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
29	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	13809.00	9354.83
30	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
ROAD TRANSPORT AND HIGHWAYS					
31	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82
32	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	1728.77
33	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
34	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
35	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
SHIPPING AND PORTS					
36	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
37	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
38	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
STEEL					
39	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
TELECOMMUNICATIONS					
40	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
41	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
42	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
43	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
44	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23

45	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74
----	---	---------	--------	--------	--------

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1443 projects, 350 are on schedule, 296 are delayed, 347 projects reported cost overrun and 128 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 302 if delay is calculated on the basis of latest schedule of completion. Further, for 710 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 360 delayed projects, 106(29.44%) projects have overall delay in the range of 1 to 12 months, 60(16.67%) projects have delay in the range of 13 to 24 months, 93(25.83%) projects have delay in the range of 25 to 60 months and 101(28.06%) projects have delay of 61 months and above. **The average time overrun in these 360 delayed projects is 44.43 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-12-2018)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	03/2019	102
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
	CIVIL AVIATION				
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
	COAL				
6	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
7	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
8	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2020	120
9	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2020	108
10	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	03/2021	108
	DEFENCE PRODUCTION				
11	CONSTRUCTION WORKS PHASE 4	12/2016	05/2018	01/2019	8
	FERTILISERS				
12	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	04/2019	29
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	02/2016	12/2017	12/2018	12
	HEALTH AND FAMILY WELFARE				
14	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	08/2019	15
15	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	12/2018	10
	HEAVY INDUSTRY				

16	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	08/2016	09/2019	37
	PETROLEUM				
17	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	06/2019	78
18	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	03/2019	72
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	03/2019	70
20	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
21	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	12/2019	57
	POWER				
22	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
23	BARH STPP(3X660MW) NTPC	02/2005	01/2011	04/2021	123
24	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2018	121
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	03/2019	111
26	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103
	RAILWAYS				
27	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
28	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
29	MANDHANA - BRAHMAWART NEW LINE PROJECT.	04/1997	04/1999	12/2018	236
30	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2019	228
31	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	03/2021	220
	ROAD TRANSPORT AND HIGHWAYS				
32	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2019	131
33	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	04/2019	130
34	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	12/2018	129
35	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	02/2019	129
36	GWALIOR-JHANSI, NH-75	12/2003	12/2009	08/2020	128
	SHIPPING AND PORTS				
37	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	12/2018	96
38	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29
	STEEL				
39	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	06/2019	49
40	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
41	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2019	29
42	COKE OVEN BATTERY-5	12/2011	12/2017	09/2019	21
43	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	06/2019	18
	TELECOMMUNICATIONS				
44	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
45	MAHARASHTRA NODAL (LOT 1)	08/2017	04/2018	12/2018	8
46	MAHARASHTRA CORE (LOT1)	08/2017	04/2018	12/2018	8
47	MADHYA PRADESH ACCESS (LOT1)	08/2017	05/2018	12/2018	7
48	MAHARAstra ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	12/2018	2
	URBAN DEVELOPMENT				
49	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2019	77
50	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
51	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
52	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64
53	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	11/2019	56

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-12-2018)**

[illegible]

13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
14	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
15	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.12	02/2017	N.A.
16	MMPL PIPELINE REROUTING PROJECT	04/2013	449.58	449.58	115.17	12/2019	12/2019
17	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
POWER							
18	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10385.81	09/2010	N.A.
19	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	2922.12	10/2017	12/2016
20	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	08/2008	771.00	1624.00	1429.45	02/2013	10/2018
21	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL-KHALSTI-LEH PROJECT	01/2014	1788.41	2333.71	1528.12	09/2017	09/2018
22	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	187.24	04/2016	10/2018
RAILWAYS							
23	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
24	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	484.14	07/2012	N.A.
25	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	267.93	03/2019	03/2020
26	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	749.69	0.00	06/2005	N.A.
27	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	634.48	629.43	03/1994	N.A.
ROAD TRANSPORT AND HIGHWAYS							
28	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	520.01	520.01	0.00	N.A.	N.A.
29	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	0.00	N.A.	10/2020
30	REHABILITATION AND UPGRADING TO 2 LANES- 2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
31	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	319.68	0.00	N.A.	N.A.
32	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
SHIPPING AND PORTS							
33	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	N.A.
34	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
35	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	411.12	12/2010	12/2018

36	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	257.90	1.45	12/2017	05/2020
	STEEL						
37	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	4749.00	4749.00	106.59	09/2017	N.A.
	TELECOMMUNICATIONS						
38	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
39	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	172.30	06/2017	N.A.
40	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	214.10	33.46	05/2018	12/2018
41	MAHARASHTRA CORE (LOT1)	08/2017	167.68	167.68	32.44	04/2018	12/2018
42	MAHARASHTRA NODAL (LOT 1)	08/2017	159.30	159.30	60.27	04/2018	12/2018
	URBAN DEVELOPMENT						
43	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
44	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
45	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
46	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-12-2018)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5687.52
	COAL				
2	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	0.00	266.38
3	BALRAM OCP EXTENSION, MCL 8.00 MTY	12/2007	172.08	0.00	266.97
4	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	583.96
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	234.29
6	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	0.00	477.74

	HEALTH AND FAMILY WELFARE				
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	237.80
8	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	191.38
9	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	0.00	469.00
	HEAVY INDUSTRY				
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	0.00	2289.00
	PETROLEUM				
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
	POWER				
12	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7121.50
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10385.81
14	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	6838.94
15	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	0.00	2051.63
16	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	0.00	3690.33
	RAILWAYS				
17	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	484.14
18	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	274.56	629.43
19	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.21
20	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	759.20
21	AMRAVATI-NARKHER NL(CR)	06/1994	663.01	668.34	716.67
	ROAD TRANSPORT AND HIGHWAYS				
22	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	410.32
23	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	268.94
24	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	209.80
25	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	200.00	0.00	245.83
26	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	0.00	195.35
	SHIPPING AND PORTS				
27	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	411.12
28	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.00	275.98
	URBAN DEVELOPMENT				
29	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
30	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
31	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77
32	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	391.23

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on as on 01-12-2018)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	COAL				
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	N.A.	03/2018
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	03/2012	N.A.	N.A.
3	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
4	RAJMAHAL OC EXP.	09/2009	03/2014	N.A.	N.A.
5	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
	HEALTH AND FAMILY WELFARE				
6	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
7	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	N.A.
8	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	N.A.
9	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	N.A.
10	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
	HEAVY INDUSTRY				
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	N.A.	N.A.
	PETROLEUM				
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
13	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	N.A.	N.A.
14	PARADIP-RAIPUR- RANCHI PIPELINE	08/2009	12/2016	N.A.	N.A.
15	PARADIP HALDIA DURGAPUR LPG PIPELINE	02/2011	06/2018	N.A.	10/2018
16	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
	POWER				
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
18	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	12/2016
19	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	08/2008	02/2013	N.A.	N.A.
20	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
21	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	02/2010	12/2012	N.A.	N.A.
	RAILWAYS				
22	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
23	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
24	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	N.A.	N.A.
25	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	N.A.	N.A.
26	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	03/2006	N.A.	N.A.
	ROAD TRANSPORT AND HIGHWAYS				
27	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
28	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	N.A.

29	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
30	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
31	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	01/1991	10/2016	N.A.	N.A.
SHIPPING AND PORTS					
32	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
33	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
34	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	N.A.	N.A.
STEEL					
35	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	N.A.	N.A.
36	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	09/2017	N.A.	N.A.
37	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	N.A.	N.A.
TELECOMMUNICATIONS					
38	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
39	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
40	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
41	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
42	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
43	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
44	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 30.12.2018 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	607	5
2	RAILWAYS	371	6
3	PETROLEUM	139	1
4	POWER	105	2
5	COAL	96	3
6	URBAN DEVELOPMENT	58	2
7	HEALTH AND FAMILY WELFARE	22	0
8	STEEL	13	1
9	TELECOMMUNICATIONS	7	0
10	FERTILISERS	6	0
11	MINES	5	1
12	SHIPPING AND PORTS	5	0
13	ATOMIC ENERGY	4	0
14	HEAVY INDUSTRY	2	0
15	DEFENCE PRODUCTION	2	0
16	CIVIL AVIATION	1	0
	Total	1443	21

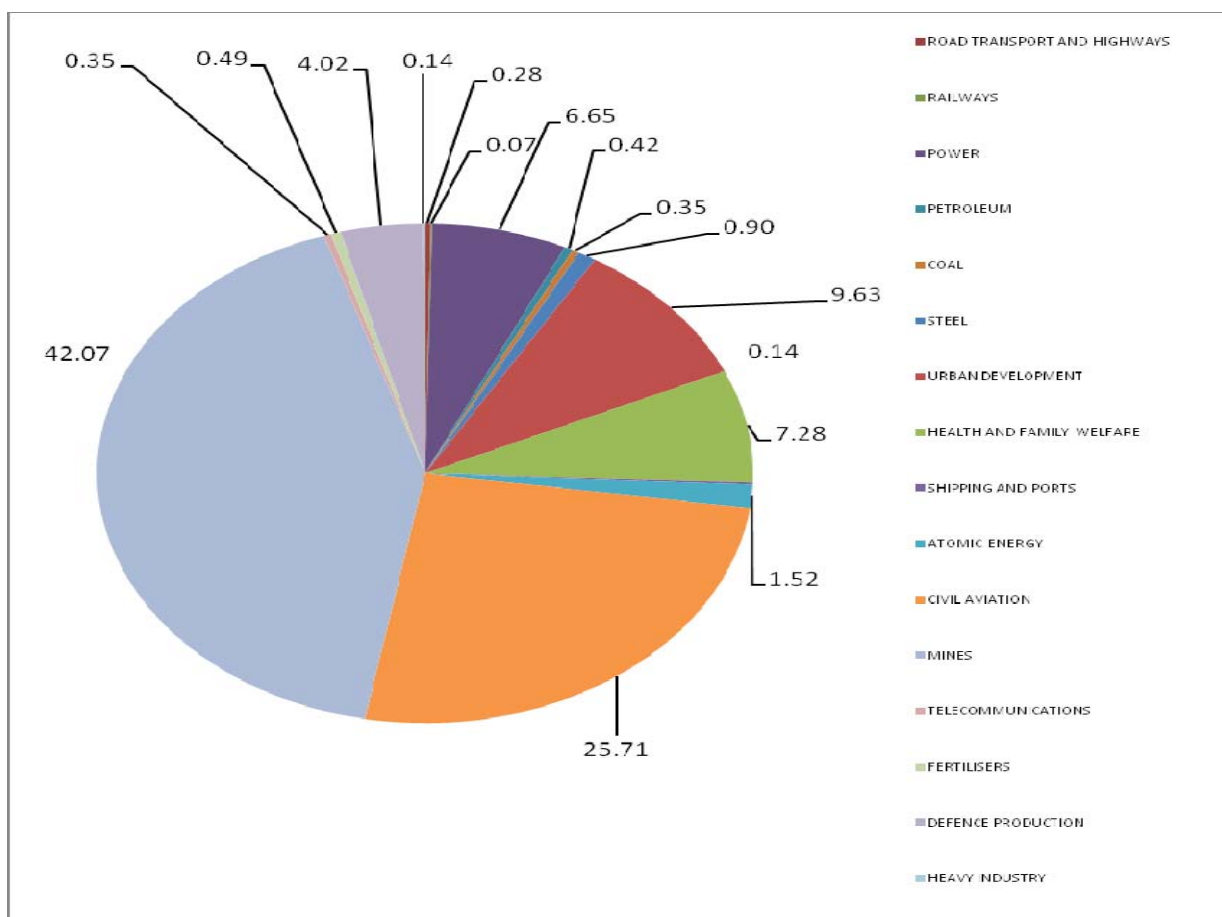


TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2018			
	<u>STEEL</u>			
1	ALTERNATE GAS NETWORK AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000093]	255.19	03/2018	177.21
	<u>PETROLEUM</u>			
2	ENNORE TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000224]	393.00	04/2018	281.45
	<u>POWER</u>			
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000123]	198.63	09/2014	127.13
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000179]	6,517.36	04/2018	3,772.80
5	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000210]	207.88	07/2018	17.00
	<u>HEALTH AND FAMILY WELFARE</u>			
6	AIIMS-RAE BARELI-HOUSING (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000006]	159.50	11/2013	158.65
	<u>RAILWAYS</u>			
7	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000189]	822.39	-	1,713.20
8	NEW COOCHBEHAR TO SAMUKTALA (NORTH EAST FRONTIER RAILWAY) - [N22000197]	209.77	-	620.04
9	DELANG-PURI DOUBLING (EAST COAST RAILWAY) - [N22000320]	165.16	03/2015	226.35
10	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) (RAIL VIKAS NIGAM LTD.) - [N22000322]	190.10	-	320.41
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	TALEGAON-AMRAVATI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000140]	567.00	11/2013	1,055.94
12	MURADABAD-BAREILY PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000154]	1,267.00	06/2013	2,667.96
	<u>SHIPPING AND PORTS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED PPP (ANNUITY)(KAMARAJAR PORT LIMITED) - [N25000065]	198.94	06/2017	255.02
14	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000067]	274.85	04/2017	251.64
	<u>URBAN DEVELOPMENT</u>			
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN Central Sector Projects(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000091]	350.02	03/2015	452.35
	May,2018			
	<u>PETROLEUM</u>			
16	TWENTY NOS. FEEDER GAS LINES (OIL INDIA LIMITED) - [N16000192]	228.64	12/2016	149.73
17	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000201]	238.50	03/2017	203.98
18	SIX PIPELINE REPLACEMENT PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000214]	181.02	01/2017	174.88
19	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000245]	931.00	07/2017	684.74
	<u>POWER</u>			
20	PARE HYDRO ELECTRIC PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000045]	573.99	08/2013	1,637.60
	<u>RAILWAYS</u>			
21	GADWAL - RAICHUR (NL), SCR (SOUTH CENTRAL RAILWAY) - [220100270]	92.63	02/2011	319.43
22	JAGGAYYAPET - MELLACHERUVU (SOUTH CENTRAL RAILWAY) - [N22000304]	313.24	01/1999	578.00
	June,2018			
	<u>POWER</u>			
23	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000197]	1,479.30	04/2017	897.12
24	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000237]	167.75	04/2019	86.62
	<u>RAILWAYS</u>			
25	RANCHI-LOHARDAGA(GC),SER (SOUTH EASTERN RAILWAY) - [220100214]	194.07	06/2004	194.07
26	BHOPAL BINA 3D LINE DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000077]	687.20	03/2010	1,033.77

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	July, 2018			
	<u>STEEL</u>			
27	EXPANSION OF BHILAI STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000057]	17,265.00	03/2013	19,855.23
	<u>PETROLEUM</u>			
28	DEVELOPMENT OF C-26 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000133]	2,592.17	05/2014	2,049.26
29	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000134]	200.69	07/2014	109.58
30	CONSTRUCTION OF THREE ETPS, MEHSANA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000135]	260.74	11/2014	83.44
31	PIPELINE REPLACEMENT PROJECT, AHMEDABAD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000159]	202.25	07/2016	130.21
32	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000172]	4,124.35	04/2016	5,347.49
33	MH NORTH REDEVELOPMENT PHASE III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000188]	5,706.47	05/2017	5,724.54
34	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000246]	215.38	06/2017	198.98
	<u>POWER</u>			
35	BOKARO THERMAL POWER STATION-A (DAMODAR VALLEY CORPORATION) - [N18000199]	2,313.00	12/2011	3,965.00
36	RAGHUNATHPUR THERMAL POWER STATION PHASE-I (DAMODAR VALLEY CORPORATION) - [N18000202]	4,122.00	02/2011	8,479.00
	September, 2018			
	<u>PETROLEUM</u>			
37	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000199]	257.87	11/2016	243.30
38	NAWAGAM-KOYALI PIPELINE PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000211]	195.63	09/2018	174.68
39	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000264]	337.06	08/2018	167.16
	<u>POWER</u>			
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000143]	514.20	06/2015	605.50
41	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000169]	288.49	02/2017	276.10

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000220]	810.48	12/2018	528.50
43	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000254]	2,525.00	11/2017	2,015.38
44	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000255]	2,225.00	01/2018	1,655.02
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
45	CHAMBAL BRIDGE, NH-76 (RJ-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000068]	275.00	02/2010	252.25
46	DEOLI KOTA PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000148]	593.00	07/2013	1,073.73
47	2-LANNING WITH PS KHAGARIA-PURNEA PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000184]	664.00	02/2014	654.59
48	2-LANING WITH PS BHILWARA-LODPURA SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000240]	240.10	03/2016	194.69
49	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000337]	538.08	02/2018	335.24
50	JAISALMER - BARMER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000348]	482.27	02/2018	308.83
51	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000352]	455.60	07/2017	202.68
52	JODHPUR - BARMER SECTION OF PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000354]	264.72	04/2017	98.18
53	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 2) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000358]	562.34	04/2018	109.07
54	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000433]	768.56	03/2018	774.99
55	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000436]	664.53	03/2018	702.97
56	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000440]	789.31	03/2018	867.54
57	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000481]	1,232.00	08/2015	1,091.17
58	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000484]	239.23	12/2017	123.47
59	FOUR LANING OF KAITHAL - RAJASTHAN BORDER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000487]	1,393.00	-	1,917.40
60	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000500]	830.36	07/2018	326.23

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
61	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000597]	600.85	05/2018	109.84
	October,2018			
	<u>COAL</u>			
62	NEYVELI SOLAR POWER PROJECT 130 MW (NEYVELI LIGNITE CORPORATION) - [N06000151]	687.28	06/2017	758.30
	<u>PETROLEUM</u>			
63	DIESEL HYDROTREATOR Central Sector Projects(NUMALIGARH REFINERY LIMITED) - [N16000207]	1,031.37	01/2018	562.77
	<u>RAILWAYS</u>			
64	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) (WESTERN RAILWAY) - [N22000122]	1,389.62	03/2014	2,140.08
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
65	PADI - DAHOD (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000353]	279.14	05/2017	212.40
	<u>TELECOMMUNICATIONS</u>			
66	UP (EAST) ACCESS LOT1 (BHARAT SANCHAR NIGAM LIMITED) - [N26000112]	169.45	08/2018	78.34
	<u>URBAN DEVELOPMENT</u>			
67	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY EPC(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000095]	164.00	11/2018	123.90
	November,2018			
	<u>CIVIL AVIATION</u>			
68	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000050]	309.46	01/2011	546.69
	<u>PETROLEUM</u>			
69	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000262]	193.40	01/2019	106.79
	<u>RAILWAYS</u>			
70	GOELKERA-MANOHARPUR,(LD)(SER) (RAIL VIKAS NIGAM LTD.) - [N22000045]	261.70	02/2006	393.23
71	TINPAHAR - SAHIBGANJ (ER) (EASTERN RAILWAYS) - [N22000115]	167.73	03/2012	238.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
72	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) (EASTERN RAILWAYS) - [N22000119]	207.52	12/2012	335.35
73	VIRAMGAM-SURENDRANAGAR (DL) (WESTERN RAILWAY) - [N22000146]	279.40	-	334.93
74	PLASSEY-JIAGANJ DOUBLING (EASTERN RAILWAYS) - [N22000220]	248.07	03/2015	266.25
75	SAINTHIA-TARAPITH 3RD LINE (EASTERN RAILWAYS) - [N22000237]	193.44	-	280.68
76	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC (EASTERN RAILWAYS) - [N22000245]	423.66	03/2017	652.79
	<u>TELECOMMUNICATIONS</u>			
77	MAHARASHTRA ACCESS (LOT 1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000109]	212.70	05/2018	37.25
78	GUJARAT ACCESS (LOT 1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000111]	171.54	05/2018	72.46
	<u>URBAN DEVELOPMENT</u>			
79	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-43 G BLOCK BANDRA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000068]	241.33	03/2016	357.50

TABLE-3

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1452
No of Projects Completed/Dropped/Frozen in Current Month	12
No of Projects Fell Down in Current Month	1
No of Projects added in Current Month	4
No of Projects in Current Month	1443

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	360 (24.95%)	23 (1.59%)	350(24.26%)	67 (4.64%)	643(4.56%)	1443
Latest Approved (Date)	302 (20.93%)	22 (1.52%)	422(29.24%)	54 (3.74%)	643(4.56%)	1443

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1284	15,92,845.50	17,92,444.77	6,24,312.80	34.80	1,99,599.27	12.50
Project with Revision in Cost	159	3,51,180.50	3,58,691.92	1,73,183.64	48.30	7,511.42	2.10
Total	1,443	19,44,026.00	21,51,136.69	7,97,496.44	37.07	2,07,110.69	10.65
Original Cost of All Projects							
Original Cost	1,443	18,30,362.48	21,51,136.69	7,97,496.44	37.07	3,20,774.21	17.53

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	360	6,93,647.42	8,39,455.12	4,19,996.34	50.00	1,45,807.70	21.00
Latest Approved (RCE)	302	4,87,690.40	5,67,159.59	2,67,988.64	47.30	79,469.19	16.30

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	21	23,297.77	28,126.75	18,782.39	66.80	4,828.98	20.70
Total	21	23,297.77	28,126.75	18,782.39	66.78	4,828.98	20.73

TABLE-4

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	96	94,283.98	93,710.95	-0.61	9	19,342.27	20,637.06	6.69
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	5.89
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	42.39
7	PETROLEUM	139	2,24,277.86	2,24,729.39	0.20	15	19,129.74	24,806.72	29.68
8	POWER	105	3,07,223.51	3,72,561.25	21.27	43	1,77,202.39	2,42,540.13	36.87
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	3	987.47	1,036.38	4.95
11	RAILWAYS	371	4,90,540.40	7,04,794.36	43.68	206	1,69,908.33	3,95,407.52	132.72
12	ROAD TRANSPORT AND HIGHWAYS	607	4,11,883.30	4,26,107.82	3.45	49	29,654.32	44,654.88	50.58
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	3	760.89	1,545.44	103.11
14	TELECOMMUNICATIONS	7	16,637.51	27,866.31	67.49	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	58	1,60,566.07	1,66,153.31	3.48	10	22,323.08	27,919.21	25.07
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	2	453.64	461.66	1.77
Total		1443	18,30,362.48	21,51,136.69	17.53	347	4,70,620.53	8,11,319.47	72.39

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-5

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	69	1,07,461.29	1,11,065.37	3.35	9	7,934.53	12,408.72	56.39
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	5	9,181.79	26,308.30	186.53
3	ASSAM	47	31,134.20	39,863.20	28.04	14	11,041.39	20,098.59	82.03
4	BIHAR	91	76,252.26	1,11,749.59	46.55	33	40,972.00	76,544.96	86.82
5	GOA	10	4,292.52	4,300.54	0.19	2	453.64	461.66	1.77
6	GUJARAT	50	51,775.98	57,577.15	11.20	5	13,724.36	21,201.45	54.48
7	HARYANA	30	21,396.40	23,309.06	8.94	5	2,452.13	4,498.00	83.43
8	HIMACHAL PRADESH	13	17,058.17	26,566.39	55.74	2	6,886.58	16,394.80	138.07
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	606.15
10	KARNATAKA	46	82,156.70	87,206.53	6.15	11	20,744.24	25,990.82	25.29
11	KERALA	22	25,879.48	28,054.10	8.40	6	7,475.98	9,846.14	31.70
12	MADHYA PRADESH	62	69,588.01	74,746.47	7.41	10	26,531.45	35,146.93	32.47
13	MAHARASHTRA	131	1,88,756.03	2,00,480.70	6.21	24	31,356.78	45,492.09	45.08
14	MANIPUR	2	4,670.86	14,025.69	200.28	1	4,454.17	13,809.00	210.02
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	1	906.46	6,000.00	561.92
16	MIZORAM	4	3,406.61	5,981.14	75.57	1	2,393.47	4,968.00	107.56
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	28.95
18	ODISHA	82	92,455.45	98,016.41	6.01	19	24,847.39	30,409.01	22.38
19	PUNJAB	34	17,565.89	17,571.62	0.03	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	57	46,334.89	48,591.45	4.87	12	5,449.18	7,714.63	41.57
21	SIKKIM	9	3,476.73	6,281.03	80.66	2	1,727.48	4,532.06	162.35
22	TAMIL NADU	76	1,19,890.58	1,37,384.34	14.59	26	29,413.59	47,998.56	63.19
23	TRIPURA	9	4,422.36	8,312.05	87.96	7	3,555.47	7,445.16	109.40
24	UTTAR PRADESH	110	1,34,449.08	1,35,916.30	1.09	18	25,563.98	29,709.84	16.22
25	WEST BENGAL	56	59,037.58	69,912.40	18.42	21	18,436.07	29,630.58	60.72
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	23	56,043.88	63,419.24	13.16	4	6,411.04	13,786.40	115.04
29	CHHATISGARH	44	78,294.07	81,695.60	4.34	7	17,333.75	22,308.14	28.70
30	JHARKHAND	48	47,384.82	51,290.09	8.24	8	21,178.14	25,087.19	18.46
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	9	9,874.84	15,740.60	59.40
32	TELANGANA	42	34,502.53	38,040.07	10.25	12	5,455.32	9,323.89	70.91
33	MULTI STATE	170	3,50,660.19	4,53,147.35	29.23	66	1,06,369.47	2,13,140.64	100.38
Total		1443	18,30,362.48	21,51,136.69	17.53	347	4,70,620.53	8,11,319.47	72.39

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 102
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	96	94,283.98	93,710.95	-0.61	35	20,438.89	20,353.64	12 - 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	2	680.64	692.29	12 - 29
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	13	32,529.65	32,317.05	-0.65	10	26,773.72	26,561.12	6 - 49
7	PETROLEUM	139	2,24,277.86	2,24,729.39	0.20	25	82,289.24	83,969.10	1 - 78
8	POWER	105	3,07,223.51	3,72,561.25	21.27	56	2,01,764.40	2,46,979.62	2 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	2	516.94	516.94	10 - 15
11	RAILWAYS	371	4,90,540.40	7,04,794.36	43.68	94	1,20,697.25	1,96,761.58	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	607	4,11,883.30	4,26,107.82	3.45	100	86,085.99	89,553.86	1 - 131
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	2	966.39	927.36	29 - 96
14	TELECOMMUNICATIONS	7	16,637.51	27,866.31	67.49	5	14,108.08	25,436.88	2 - 58
15	URBAN DEVELOPMENT	58	1,60,566.07	1,66,153.31	3.48	22	70,169.58	70,688.03	2 - 77
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	1	167.69	170.37	8 - 8
Total		1443	18,30,362.48	21,51,136.69	17.53	360	6,93,647.42	8,39,455.12	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-7

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	69	1,07,461.29	1,11,065.37	3.35	14	49,468.81	51,381.38	2 - 168
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	2	2,635.83	6,334.96	36 - 111
3	ASSAM	47	31,134.20	39,863.20	28.04	10	8,834.25	13,899.37	8 - 131
4	BIHAR	91	76,252.26	1,11,749.59	46.55	21	38,604.17	55,153.15	6 - 123
5	GOA	10	4,292.52	4,300.54	0.19	1	167.69	170.37	8 - 8
6	GUJARAT	50	51,775.98	57,577.15	11.20	9	16,187.08	21,721.98	2 - 84
7	HARYANA	30	21,396.40	23,309.06	8.94	4	2,534.20	3,714.20	3 - 91
8	HIMACHAL PRADESH	13	17,058.17	26,566.39	55.74	4	7,041.67	12,516.88	12 - 147
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	5	16,904.75	42,353.75	10 - 220
10	KARNATAKA	46	82,156.70	87,206.53	6.15	17	42,870.25	43,901.25	3 - 264
11	KERALA	22	25,879.48	28,054.10	8.40	9	16,657.20	17,490.70	8 - 79
12	MADHYA PRADESH	62	69,588.01	74,746.47	7.41	11	20,358.92	22,950.08	5 - 96
13	MAHARASHTRA	131	1,88,756.03	2,00,480.70	6.21	39	83,816.10	89,544.59	2 - 192
14	MANIPUR	2	4,670.86	14,025.69	200.28	2	4,670.86	14,025.69	56 - 108
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	4	1,530.52	1,530.52	10 - 60
16	MIZORAM	4	3,406.61	5,981.14	75.57	1	2,393.47	4,968.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	4	3,525.63	4,199.11	36 - 79
18	ODISHA	82	92,455.45	98,016.41	6.01	25	34,878.63	40,122.05	3 - 147
19	PUNJAB	34	17,565.89	17,571.62	0.03	5	2,036.78	2,038.51	1 - 22
20	RAJASTHAN	57	46,334.89	48,591.45	4.87	19	23,064.29	24,068.76	1 - 86
21	SIKKIM	9	3,476.73	6,281.03	80.66	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	76	1,19,890.58	1,37,384.34	14.59	20	66,722.54	69,276.72	1 - 121
23	TRIPURA	9	4,422.36	8,312.05	87.96	2	1,711.63	4,024.00	31 - 60
24	UTTAR PRADESH	110	1,34,449.08	1,35,916.30	1.09	21	39,346.37	40,475.25	2 - 236
25	WEST BENGAL	56	59,037.58	69,912.40	18.42	12	15,476.08	17,881.29	2 - 324
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	23	56,043.88	63,419.24	13.16	4	4,365.06	4,737.85	5 - 37
29	CHHATISGARH	44	78,294.07	81,695.60	4.34	11	30,819.18	32,754.74	13 - 117
30	JHARKHAND	48	47,384.82	51,290.09	8.24	17	24,303.13	25,545.20	9 - 108
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	6	23,935.83	29,313.50	15 - 102
32	TELANGANA	42	34,502.53	38,040.07	10.25	15	18,452.17	19,234.54	3 - 144
33	MULTI STATE	170	3,50,660.19	4,53,147.35	29.23	43	82,594.16	1,13,758.40	1 - 228
Total		1443	18,30,362.48	21,51,136.69	17.53	360	6,93,647.42	8,39,455.12	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	4	72,241.00	74,849.00	36 - 102
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	96	93,116.54	93,710.95	0.64	34	19,273.66	19,594.77	0 - 144
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	-
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	13	32,529.65	32,317.05	-0.65	9	11,248.72	11,036.12	6 - 32
7	PETROLEUM	139	2,27,148.34	2,24,729.39	-1.06	7	9,668.79	9,533.20	1 - 78
8	POWER	105	3,22,819.00	3,72,561.25	15.41	45	1,11,843.19	1,36,782.39	2 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	2	516.94	516.94	10 - 15
11	RAILWAYS	371	5,80,999.42	7,04,794.36	21.31	77	99,750.25	1,36,142.23	-12 - 236
12	ROAD TRANSPORT AND HIGHWAYS	607	4,12,453.43	4,26,107.82	3.31	100	86,123.35	89,553.86	1 - 131
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	2	624.39	927.36	29 - 96
14	TELECOMMUNICATIONS	7	16,636.31	27,866.31	67.50	1	13,334.00	24,664.00	58 - 58
15	URBAN DEVELOPMENT	58	1,61,098.60	1,66,153.31	3.14	19	61,197.50	61,564.39	2 - 77
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	0	0.00	0.00	-
Total		1443	19,44,026.00	21,51,136.69	10.65	302	4,87,690.40	5,67,159.59	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	74.69
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	96	93,116.54	93,710.95	0.64	6	18,724.25	19,454.55	3.90
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0.00
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	42.39
7	PETROLEUM	139	2,27,148.34	2,24,729.39	-1.06	7	6,531.66	7,870.53	20.50
8	POWER	105	3,22,819.00	3,72,561.25	15.41	38	1,58,525.65	2,08,267.90	31.38
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	3	987.47	1,036.38	4.95
11	RAILWAYS	371	5,80,999.42	7,04,794.36	21.31	193	1,35,635.19	2,73,685.39	101.78
12	ROAD TRANSPORT AND HIGHWAYS	607	4,12,453.43	4,26,107.82	3.31	39	27,295.62	41,914.00	53.56
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	3	774.39	1,545.44	99.57
14	TELECOMMUNICATIONS	7	16,636.31	27,866.31	67.50	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	58	1,61,098.60	1,66,153.31	3.14	7	22,155.90	27,219.50	22.85
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	2	454.00	461.66	1.69
Total		1443	19,44,026.00	21,51,136.69	10.65	303	3,90,285.74	6,16,976.38	58.08

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-10

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	102- 102
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	96	93,116.54	93,710.95	0.64	3	830.76	1,287.76	72- 144
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0- 0
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	29- 29
7	PETROLEUM	139	2,27,148.34	2,24,729.39	-1.06	1	607.06	714.25	17- 17
8	POWER	105	3,22,819.00	3,72,561.25	15.41	23	65,331.09	90,270.29	8- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	0	0.00	0.00	0- 0
11	RAILWAYS	371	5,80,999.42	7,04,794.36	21.31	39	37,827.89	77,197.57	1- 236
12	ROAD TRANSPORT AND HIGHWAYS	607	4,12,453.43	4,26,107.82	3.31	17	14,520.39	17,951.92	1- 131
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	7	16,636.31	27,866.31	67.50	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	58	1,61,098.60	1,66,153.31	3.14	2	1,715.21	2,090.99	5- 36
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	0	0.00	0.00	0- 0
Total		1443	19,44,026.00	21,51,136.69	10.65	90	1,38,682.40	2,21,875.97	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-11

Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 102
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	96	94,283.98	93,710.95	-0.61	5	1,260.84	2,060.59	36- 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	29- 29
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	13	32,529.65	32,317.05	-0.65	1	343.00	488.40	29- 29
7	PETROLEUM	139	2,24,277.86	2,24,729.39	0.20	8	12,172.77	14,942.79	9- 70
8	POWER	105	3,07,223.51	3,72,561.25	21.27	32	1,33,131.92	1,78,347.14	8- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	0	0.00	0.00	0- 0
11	RAILWAYS	371	4,90,540.40	7,04,794.36	43.68	54	54,913.26	1,32,411.14	1- 324
12	ROAD TRANSPORT AND HIGHWAYS	607	4,11,883.30	4,26,107.82	3.45	18	14,567.07	18,106.92	1- 131
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	7	16,637.51	27,866.31	67.49	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	58	1,60,566.07	1,66,153.31	3.48	3	1,829.65	2,356.99	5- 70
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	1	167.69	170.37	8- 8
Total		1443	18,30,362.48	21,51,136.69	17.53	128	2,47,549.99	3,97,548.57	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

State-Wise Position of Central Sector Projects costing Rs. 150Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	69	1,07,461.29	1,11,065.37	3.35	5	3,397.13	5,880.66	2 - 168
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	2	2,635.83	6,334.96	36 - 111
3	ASSAM	47	31,134.20	39,863.20	28.04	6	5,549.10	10,771.17	12 - 131
4	BIHAR	91	76,252.26	1,11,749.59	46.55	11	31,379.06	47,928.04	12 - 123
5	GOA	10	4,292.52	4,300.54	0.19	1	167.69	170.37	8 - 8
6	GUJARAT	50	51,775.98	57,577.15	11.20	3	12,097.90	17,760.58	36 - 84
7	HARYANA	30	21,396.40	23,309.06	8.94	1	1,108.00	2,288.00	91 - 91
8	HIMACHAL PRADESH	13	17,058.17	26,566.39	55.74	1	3,919.59	9,394.80	147 - 147
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	1	2,500.00	27,949.00	220 - 220
10	KARNATAKA	46	82,156.70	87,206.53	6.15	3	2,469.52	3,500.52	3 - 36
11	KERALA	22	25,879.48	28,054.10	8.40	3	5,451.10	6,308.64	9 - 17
12	MADHYA PRADESH	62	69,588.01	74,746.47	7.41	4	14,425.09	17,016.25	21 - 96
13	MAHARASHTRA	131	1,88,756.03	2,00,480.70	6.21	13	17,403.64	23,529.16	2 - 192
14	MANIPUR	2	4,670.86	14,025.69	200.28	1	4,454.17	13,809.00	108 - 108
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	0	0.00	0.00	-
16	MIZORAM	4	3,406.61	5,981.14	75.57	1	2,393.47	4,968.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	79 - 79
18	ODISHA	82	92,455.45	98,016.41	6.01	9	20,893.26	26,136.98	3 - 147
19	PUNJAB	34	17,565.89	17,571.62	0.03	1	754.54	756.27	1 - 1
20	RAJASTHAN	57	46,334.89	48,591.45	4.87	4	2,013.99	3,027.35	1 - 60
21	SIKKIM	9	3,476.73	6,281.03	80.66	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	76	1,19,890.58	1,37,384.34	14.59	4	5,954.29	9,599.68	69 - 121
23	TRIPURA	9	4,422.36	8,312.05	87.96	2	1,711.63	4,024.00	31 - 60
24	UTTAR PRADESH	110	1,34,449.08	1,35,916.30	1.09	5	3,129.18	4,602.83	5 - 236
25	WEST BENGAL	56	59,037.58	69,912.40	18.42	4	7,575.12	9,980.34	12 - 324
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	23	56,043.88	63,419.24	13.16	1	1,219.21	1,592.00	5 - 5
29	CHHATISGARH	44	78,294.07	81,695.60	4.34	4	13,013.75	14,949.31	24 - 117
30	JHARKHAND	48	47,384.82	51,290.09	8.24	3	14,824.79	16,066.86	20 - 36
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	4	7,241.32	12,619.50	63 - 102
32	TELANGANA	42	34,502.53	38,040.07	10.25	5	2,730.04	3,648.31	33 - 144
33	MULTI STATE	170	3,50,660.19	4,53,147.35	29.23	23	53,156.97	85,409.97	1 - 178
Total		1443	18,30,362.48	21,51,136.69	17.53	128	2,47,549.99	3,97,548.57	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	165	4
2	ROAD TRANSPORT AND HIGHWAYS	136	1
3	POWER	56	2
4	PETROLEUM	50	1
5	COAL	14	0
6	URBAN DEVELOPMENT	13	0
7	STEEL	7	0
8	ATOMIC ENERGY	4	0
9	HEAVY INDUSTRY	2	0
10	TELECOMMUNICATIONS	2	0
11	MINES	1	0
12	SHIPPING AND PORTS	1	0
	Total	451	8

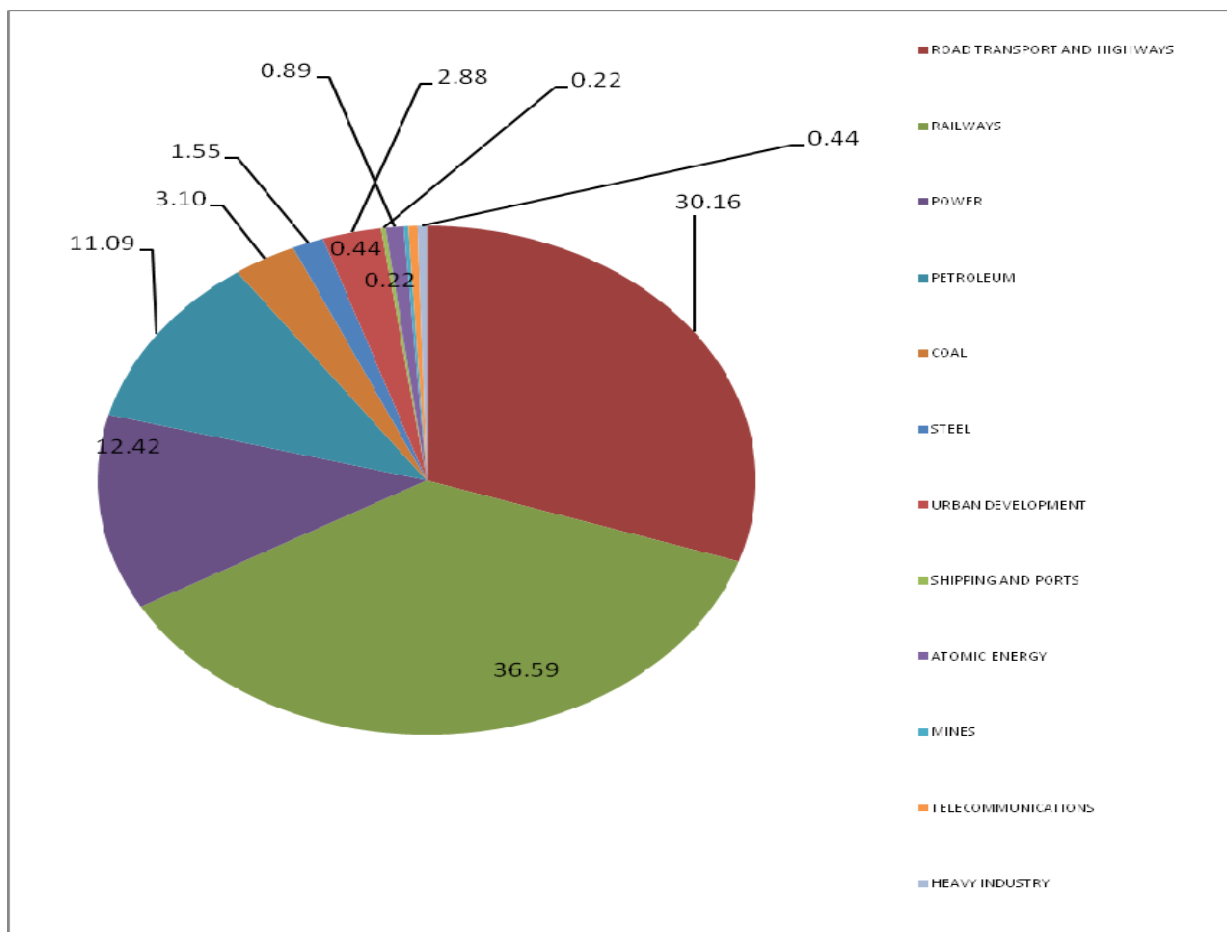


TABLE-14

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	456
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects Fell Down in Current Month	7
No of Projects added in Current Month	2
No of Projects in Current Month	451

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	160 (35.48%)	7 (1.55%)	121(26.83%)	25 (5.54%)	138(0.60%)	451
Latest Approved (Date)	124 (27.49%)	7 (1.55%)	161(35.70%)	21 (4.66%)	138(0.60%)	451

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	384	12,11,668.30	13,95,779.80	5,08,146.36	36.40	1,84,111.50	15.20
Project with Revision in Cost	67	3,14,150.17	3,19,887.82	1,55,238.62	48.50	5,737.65	1.80
Total	451	15,25,818.47	17,15,667.62	6,63,384.98	38.67	1,89,849.15	12.44
Original Cost of All Projects							
Original Cost	451	14,10,817.93	17,15,667.62	6,63,384.98	38.67	3,04,849.69	21.61

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	160	6,04,047.11	7,45,367.39	3,73,211.66	50.10	1,41,320.28	23.40
Latest Approved (RCE)	124	4,07,610.54	4,83,092.33	2,26,173.30	46.80	75,481.79	18.50

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	8	18,288.14	22,814.84	14,675.71	64.30	4,526.70	24.80
Total	8	18,288.14	22,814.84	14,675.71	64.33	4,526.70	24.75

TABLE-15

<u>Extent of cost overrun in projects with respect to original schedule(Sector Wise)</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	COAL	14	60,321.08	60,321.88	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0.00
5	PETROLEUM	50	1,85,879.16	1,87,511.67	0.88	8	16,553.75	21,148.95	27.76
6	POWER	56	2,88,605.36	3,52,792.27	22.24	32	1,73,171.13	2,37,358.04	37.07
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	165	4,04,092.92	6,03,759.14	49.41	97	1,34,939.14	3,39,844.67	151.85
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	17	20,393.80	33,696.27	65.23
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,002.50	3.62	4	20,852.09	26,202.57	25.66
Total		451	14,10,817.93	17,15,667.62	21.61	163	4,13,149.91	7,26,659.60	75.88

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-16

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	90,958.16	94,896.23	4.33	6	7,059.25	11,355.32	60.86
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	2	8,782.23	25,676.30	192.37
3	ASSAM	8	17,363.39	25,066.86	44.37	4	8,861.92	16,702.00	88.47
4	BIHAR	25	46,998.89	79,080.11	68.26	17	34,744.64	66,825.86	92.33
5	GUJARAT	14	33,092.23	39,942.00	20.70	2	12,968.10	19,817.87	52.82
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	2	6,886.58	16,394.80	138.07
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	606.15
9	KARNATAKA	20	68,819.94	73,410.38	6.67	6	18,932.46	23,702.90	25.20
10	KERALA	8	19,741.86	21,625.11	9.54	2	6,154.29	8,061.58	30.99
11	MADHYA PRADESH	20	46,362.91	52,277.82	12.76	9	26,272.05	34,660.36	31.93
12	MAHARASHTRA	44	1,52,492.80	1,62,796.01	6.76	15	28,028.61	40,609.03	44.88
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	210.02
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	107.56
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	27	68,182.00	72,783.08	6.75	7	20,821.88	25,422.96	22.10
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	13	25,544.64	26,900.58	5.31	4	3,178.64	4,534.58	42.66
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	27	99,477.88	1,14,735.82	15.34	11	25,501.52	40,759.46	59.83
22	TRIPURA	3	2,458.01	6,185.51	151.65	3	2,458.01	6,185.51	151.65
23	UTTAR PRADESH	41	1,00,801.99	1,02,948.61	2.13	5	21,465.64	24,384.21	13.60
24	WEST BENGAL	25	47,310.16	55,677.29	17.69	9	15,026.71	23,408.27	55.78
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	7	50,481.91	57,816.75	14.53	3	6,254.39	13,589.23	117.28
27	CHHATISGARH	14	64,313.38	68,809.25	6.99	5	16,797.78	21,293.65	26.76
28	JHARKHAND	12	34,294.40	37,393.78	9.04	3	19,637.61	22,736.99	15.78
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	4	8,654.06	14,154.57	63.56
30	TELANGANA	7	20,115.45	23,093.25	14.80	3	2,503.03	5,480.84	118.97
31	MULTI STATE	72	3,08,255.68	4,07,202.01	32.10	33	95,344.00	1,96,470.91	106.07
Total		451	14,10,817.93	17,15,667.62	21.61	163	4,13,149.91	7,26,659.60	75.88

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 102
2	COAL	14	60,321.08	60,321.88	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	29,772.34	-1.19	6	25,381.34	25,023.34	6 - 49
5	PETROLEUM	50	1,85,879.16	1,87,511.67	0.88	14	77,477.38	78,763.51	5 - 78
6	POWER	56	2,88,605.36	3,52,792.27	22.24	34	1,93,638.89	2,37,703.45	3 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
8	RAILWAYS	165	4,04,092.92	6,03,759.14	49.41	57	1,02,256.43	1,75,896.07	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	34	49,339.22	52,595.38	2 - 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,002.50	3.62	5	64,622.14	64,994.93	5 - 64
Total		451	14,10,817.93	17,15,667.62	21.61	160	6,04,047.11	7,45,367.39	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-18

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	94,896.23	4.33	8	47,113.04	49,092.67	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	8	17,363.39	25,066.86	44.37	3	7,225.70	12,060.86	12 - 87
4	BIHAR	25	46,998.89	79,080.11	68.26	10	32,659.99	48,769.28	12 - 123
5	GUJARAT	14	33,092.23	39,942.00	20.70	2	13,417.88	18,538.88	2 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	2	5,836.38	11,311.59	29 - 147
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	5	16,904.75	42,353.75	10 - 220
9	KARNATAKA	20	68,819.94	73,410.38	6.67	8	36,654.45	37,440.71	3 - 264
10	KERALA	8	19,741.86	21,625.11	9.54	4	14,207.19	14,840.82	8 - 33
11	MADHYA PRADESH	20	46,362.91	52,277.82	12.76	7	18,951.92	21,543.08	6 - 96
12	MAHARASHTRA	44	1,52,492.80	1,62,796.01	6.76	20	74,783.82	79,902.82	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	27	68,182.00	72,783.08	6.75	10	28,186.73	32,655.88	3 - 147
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	13	25,544.64	26,900.58	5.31	4	15,476.63	16,325.70	48 - 86
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	27	99,477.88	1,14,735.82	15.34	8	59,728.51	63,091.22	18 - 121
22	TRIPURA	3	2,458.01	6,185.51	151.65	1	1,142.00	3,374.00	60 - 60
23	UTTAR PRADESH	41	1,00,801.99	1,02,948.61	2.13	13	35,489.37	36,664.49	2 - 236
24	WEST BENGAL	25	47,310.16	55,677.29	17.69	7	13,711.20	15,799.73	11 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	7	50,481.91	57,816.75	14.53	3	4,167.73	4,540.52	5 - 37
27	CHHATISGARH	14	64,313.38	68,809.25	6.99	3	28,002.78	29,459.82	24 - 111
28	JHARKHAND	12	34,294.40	37,393.78	9.04	6	20,635.13	21,432.60	9 - 48
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	4	23,343.06	28,569.50	15 - 102
30	TELANGANA	7	20,115.45	23,093.25	14.80	4	14,450.02	14,727.41	3 - 144
31	MULTI STATE	72	3,08,255.68	4,07,202.01	32.10	21	71,754.21	1,02,700.10	5 - 178
Total		451	14,10,817.93	17,15,667.62	21.61	160	6,04,047.11	7,45,367.39	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	4	72,241.00	74,849.00	36 - 102
2	COAL	14	60,321.08	60,321.88	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	29,772.34	-1.19	5	9,856.34	9,498.34	6 - 32
5	PETROLEUM	50	1,88,840.40	1,87,511.67	-0.70	2	7,527.00	7,412.00	24 - 78
6	POWER	56	3,04,101.67	3,52,792.27	16.01	23	1,03,618.50	1,27,506.22	5 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
8	RAILWAYS	165	4,95,212.82	6,03,759.14	21.92	46	84,874.63	1,19,374.75	-12 - 236
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	34	49,339.22	52,595.38	2 - 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,002.50	3.41	4	55,942.14	56,314.93	5 - 64
Total		451	15,25,818.47	17,15,667.62	12.44	124	4,07,610.54	4,83,092.33	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	74.69
2	COAL	14	60,321.08	60,321.88	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0.00
5	PETROLEUM	50	1,88,840.40	1,87,511.67	-0.70	3	5,055.04	6,140.19	21.47
6	POWER	56	3,04,101.67	3,52,792.27	16.01	28	1,54,689.81	2,03,380.41	31.48
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	165	4,95,212.82	6,03,759.14	21.92	87	1,01,365.44	2,19,328.99	116.37
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	17	20,393.80	33,696.27	65.23
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,002.50	3.41	4	21,154.18	26,202.57	23.86
Total		451	15,25,818.47	17,15,667.62	12.44	143	3,38,439.27	5,40,577.53	59.73

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-21

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	74,849.00	3.61	1	3,492.00	6,100.00	102- 102
2	COAL	14	60,321.08	60,321.88	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0- 0
5	PETROLEUM	50	1,88,840.40	1,87,511.67	-0.70	0	0.00	0.00	0- 0
6	POWER	56	3,04,101.67	3,52,792.27	16.01	14	62,285.38	86,173.10	12- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	165	4,95,212.82	6,03,759.14	21.92	22	31,252.54	68,200.18	3- 236
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	12	12,832.24	16,088.40	2- 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,002.50	3.41	1	1,219.21	1,592.00	5- 5
Total		451	15,25,818.47	17,15,667.62	12.44	51	1,24,415.37	2,02,817.68	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-22

Extent of time & cost overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 102
2	COAL	14	60,321.08	60,321.88	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	29,772.34	-1.19	0	0.00	0.00	0- 0
5	PETROLEUM	50	1,85,879.16	1,87,511.67	0.88	4	10,700.40	12,735.95	9- 70
6	POWER	56	2,88,605.36	3,52,792.27	22.24	22	1,29,890.79	1,73,955.35	10- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	165	4,04,092.92	6,03,759.14	49.41	33	46,567.30	1,20,355.97	3- 324
9	ROAD TRANSPORT AND HIGHWAYS	136	2,00,332.48	2,13,634.95	6.64	12	12,832.24	16,088.40	2- 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,002.50	3.62	1	1,219.21	1,592.00	5- 5
Total		451	14,10,817.93	17,15,667.62	21.61	75	2,29,494.94	3,72,071.67	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	94,896.23	4.33	3	2,819.63	5,157.26	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	8	17,363.39	25,066.86	44.37	2	4,760.55	9,682.00	12 - 87
4	BIHAR	25	46,998.89	79,080.11	68.26	8	29,968.32	46,077.61	12 - 123
5	GUJARAT	14	33,092.23	39,942.00	20.70	1	11,459.00	16,580.00	54 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	1	3,919.59	9,394.80	147 - 147
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	1	2,500.00	27,949.00	220 - 220
9	KARNATAKA	20	68,819.94	73,410.38	6.67	2	1,824.74	2,611.00	3 - 3
10	KERALA	8	19,741.86	21,625.11	9.54	1	4,588.29	5,245.96	9 - 9
11	MADHYA PRADESH	20	46,362.91	52,277.82	12.76	4	14,425.09	17,016.25	21 - 96
12	MAHARASHTRA	44	1,52,492.80	1,62,796.01	6.76	9	16,084.12	21,598.44	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	27	68,182.00	72,783.08	6.75	6	19,533.81	24,002.96	3 - 147
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	13	25,544.64	26,900.58	5.31	2	1,482.93	2,332.00	60 - 60
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	27	99,477.88	1,14,735.82	15.34	2	5,271.29	8,634.00	102 - 121
22	TRIPURA	3	2,458.01	6,185.51	151.65	1	1,142.00	3,374.00	60 - 60
23	UTTAR PRADESH	41	1,00,801.99	1,02,948.61	2.13	2	1,793.75	3,117.88	5 - 236
24	WEST BENGAL	25	47,310.16	55,677.29	17.69	3	7,277.80	9,366.34	108 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	7	50,481.91	57,816.75	14.53	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	14	64,313.38	68,809.25	6.99	2	12,477.78	13,934.82	24 - 111
28	JHARKHAND	12	34,294.40	37,393.78	9.04	1	14,366.58	15,164.05	20 - 20
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	3	7,127.06	12,353.50	63 - 102
30	TELANGANA	7	20,115.45	23,093.25	14.80	1	1,266.60	1,544.00	33 - 33
31	MULTI STATE	72	3,08,255.68	4,07,202.01	32.10	13	50,068.26	81,014.15	12 - 178
Total		451	14,10,817.93	17,15,667.62	21.61	75	2,29,494.94	3,72,071.67	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	01/2011	553.53	11/2018	546.69
	<u>PETROLEUM</u>						
2	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY	05/2015	193.40	01/2019	193.40	11/2018	106.79
	<u>RAILWAYS</u>						
3	GOELKERA-MANOHARPUR,(LD)(SER)	03/1997	261.70	02/2006	388.00	12/2018	393.23
4	TINPAHAR - SAHIBGANJ (ER)	04/2008	167.73	03/2012	182.56	11/2018	238.53
5	SAINTHIA-TARAPITH 3RD LINE	04/2011	193.44	N.A.	186.64	11/2018	280.68
6	VIRAMGAM-SURENDRANAGAR (DL)	04/2010	279.40	N.A.	355.00	11/2018	334.93
7	PLASSEY-JAGANJ DOUBLING	04/2011	248.07	03/2015	234.41	11/2018	266.25
8	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	04/2010	423.66	03/2017	479.03	11/2018	652.79
9	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	04/1999	207.52	12/2012	334.87	11/2018	335.35
	<u>TELECOMMUNICATIONS</u>						
10	MAHARASHTRA ACESS (LOT 1) Central Sector Projects	08/2017	212.70	05/2018	212.70	11/2018	37.25
11	GUJARAT ACCESS (LOT 1) Central Sector Projects	09/2017	171.54	05/2018	170.91	11/2018	72.46
	<u>URBAN DEVELOPMENT</u>						
12	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	03/2016	349.33	11/2018	357.50

TABLE-26

List of projects added Rs.150 Crore and above					(November 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>RAILWAYS</u>					
1	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	700.00	6/2020	700.00	6/2020
2	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	691.84	3/2020	691.84	3/2020
3	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	4,329.53	3/2023	4,329.53	3/2023
4	JHANSI BINA DOUBLING	9/2016	2,001.00	3/2021	2,001.00	3/2021

TABLE-27


Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		4554	
Achieved up to month		2242	

TABLE-28


List of projects reporting additional delayed Rs.150 Crore and above							(November 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	KANIHA OCP, MCL, (10.0 MTY) MCL	457.77	457.77	03/2013	03/2019	03/2020	12
2	BALRAM OCP EXTENSION,MCL 8.00 MTY MCL	172.08	172.08	03/2010	03/2019	03/2020	12
3	BASUNDHARA (WEST) OC EXTN(7.00 MTY) MCL	479.15	479.15	03/2019	03/2021	03/2024	36
	<u>MINES</u>						
4	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU NALCO	166.62	166.62	06/2019	12/2018	06/2019	6
	<u>STEEL</u>						
5	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) RINL	465.85	465.85	07/2018	11/2018	01/2019	2
	<u>PETROLEUM</u>						
6	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II GAIL Central Sector Projects	2,915.00	2,915.00	12/2012	02/2019	06/2019	4
	<u>POWER</u>						
7	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A PGCIL Central Sector Projects	955.00	1,364.00	12/2015	11/2018	12/2018	1
8	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	8,150.00	09/2011	10/2018	12/2018	2
	<u>RAILWAYS</u>						
9	ALWAR-BANDIKUI DOUBLING NWR	242.09	349.00	02/2019	02/2019	03/2019	1
10	MAHARAJGANJ-MASRAKH (NL) - NER NER	218.19	413.56	06/2018	06/2018	10/2018	4
11	BONDAMUNDA RANCHI DOUBLING SER	1,724.20	1,724.20	03/2021	03/2021	12/2021	9
12	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION SCR	1,856.95	2,200.00	03/2023	03/2023	03/2024	12
13	HUBLI- CHIKJAJUR SWR	1,156.94	1,156.94	03/2020	03/2020	03/2021	12

List of projects reporting additional delayed Rs.150 Crore and above							(November 2018)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
14	GUNTUR-GUNTAKAL SCR	3,631.00	3,631.00	03/2022	03/2022	03/2023	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
15	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS NHAI	567.51	567.51	03/2018	11/2018	12/2018	1
16	2 LANING WITH PS OF GULABPURA - UNIARA NHAI	597.00	597.00	10/2017	10/2018	12/2018	2
17	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) NHAI PPP (BOT)	1,673.70	1,673.70	10/2011	10/2018	12/2018	2
18	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPAS - DHOLPUR NHAI	275.90	275.90	N.A.	10/2018	12/2018	2
19	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM NHAI PPP (BOT)	822.90	822.90	04/2018	12/2018	03/2019	3
	<u>URBAN DEVELOPMENT</u>						
20	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA CPWD	156.57	156.57	08/2016	01/2019	03/2019	2
21	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB CPWD	388.00	388.00	05/2017	12/2018	03/2019	3

Graphical Presentation of All Projects w.r.t. Original Schedule

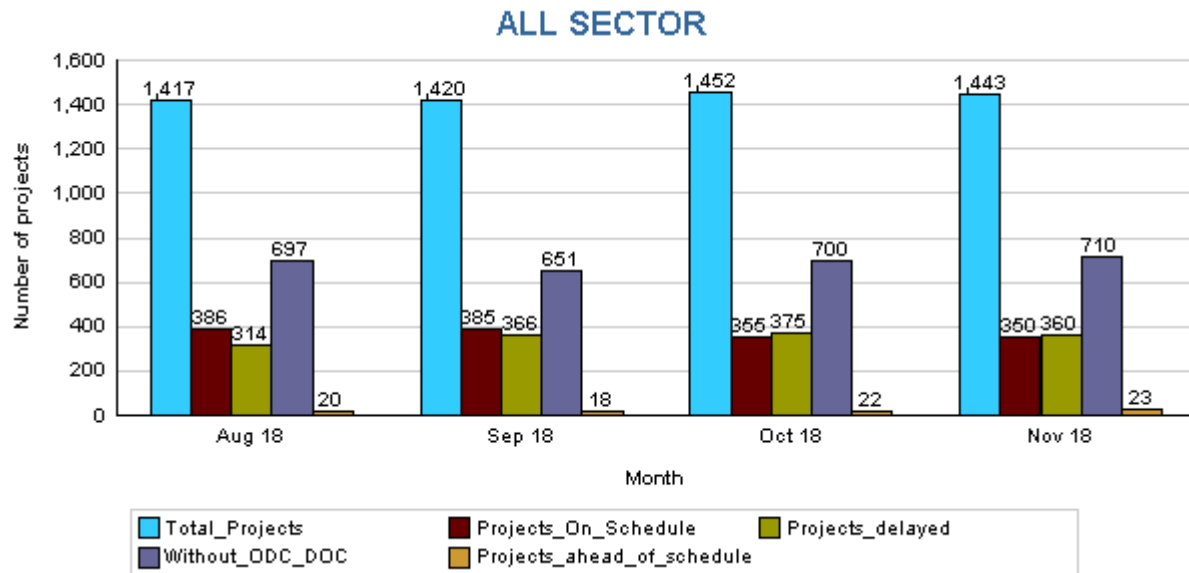


Break-up of 360 Delayed projects in November 2018

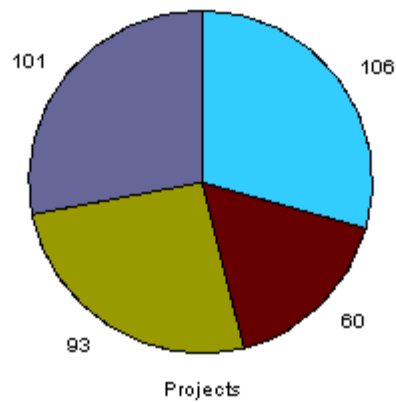


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

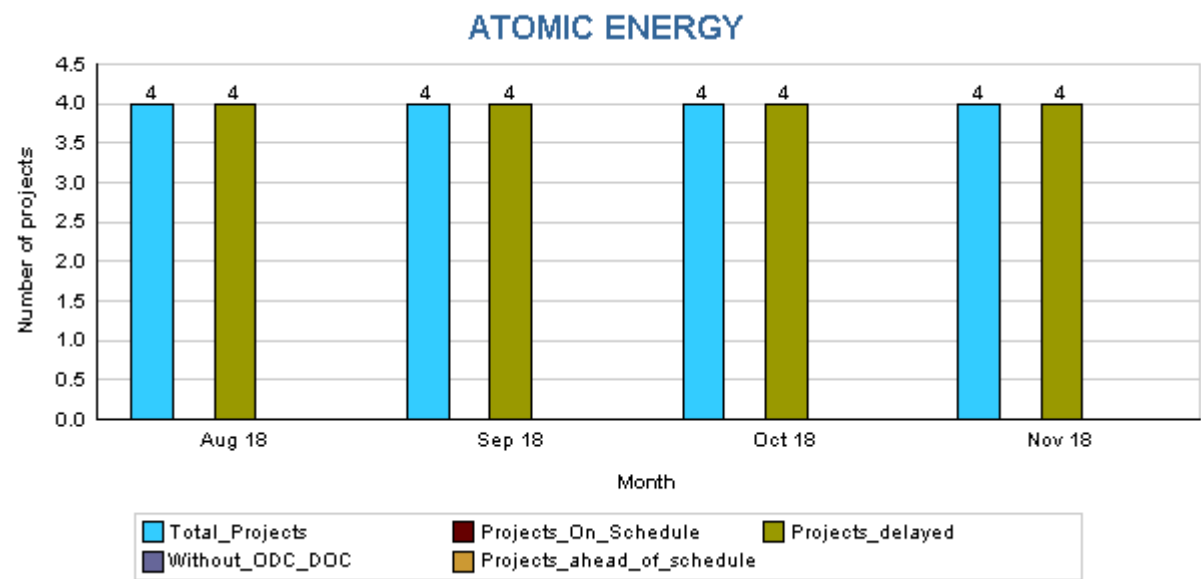


Break-up of 4 Delayed projects in November 2018

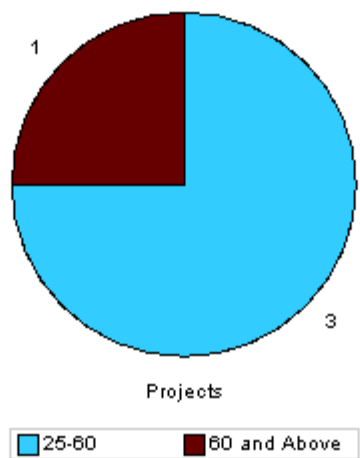


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

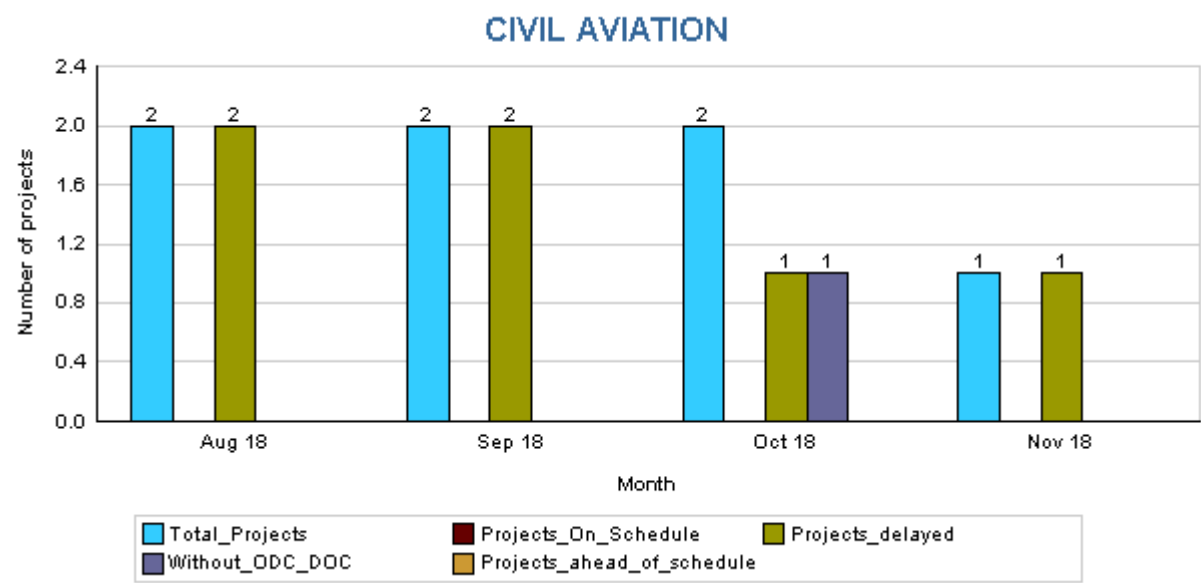


Break-up of 1 Delayed projects in November 2018

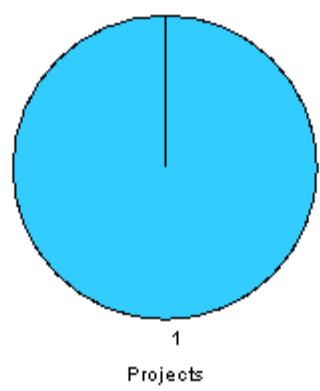


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

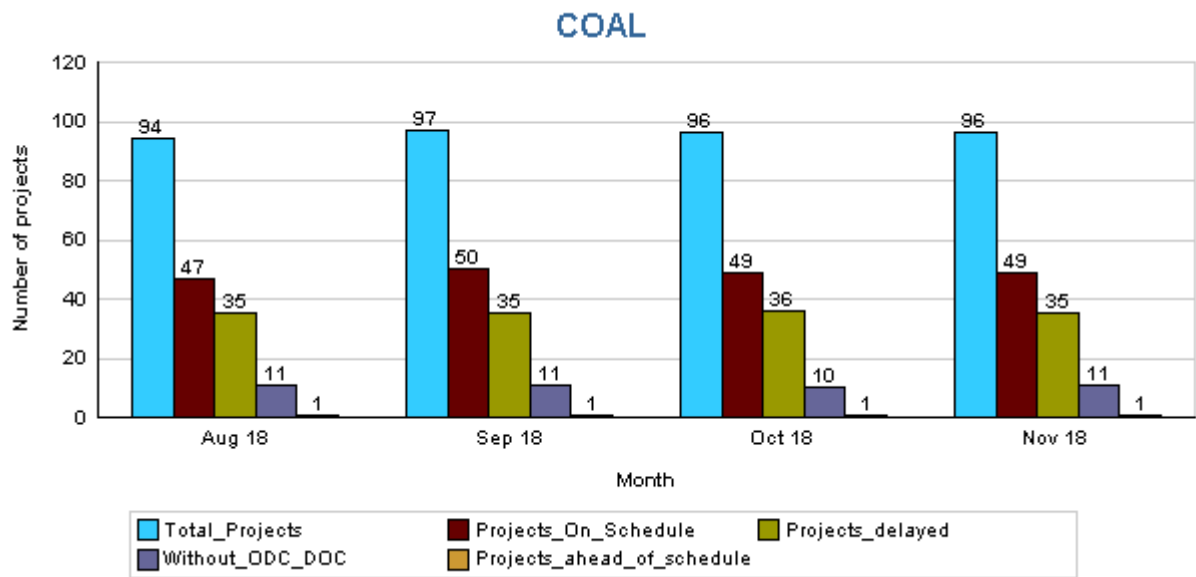


Break-up of 35 Delayed projects in November 2018

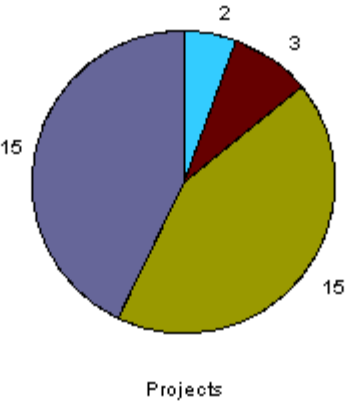


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

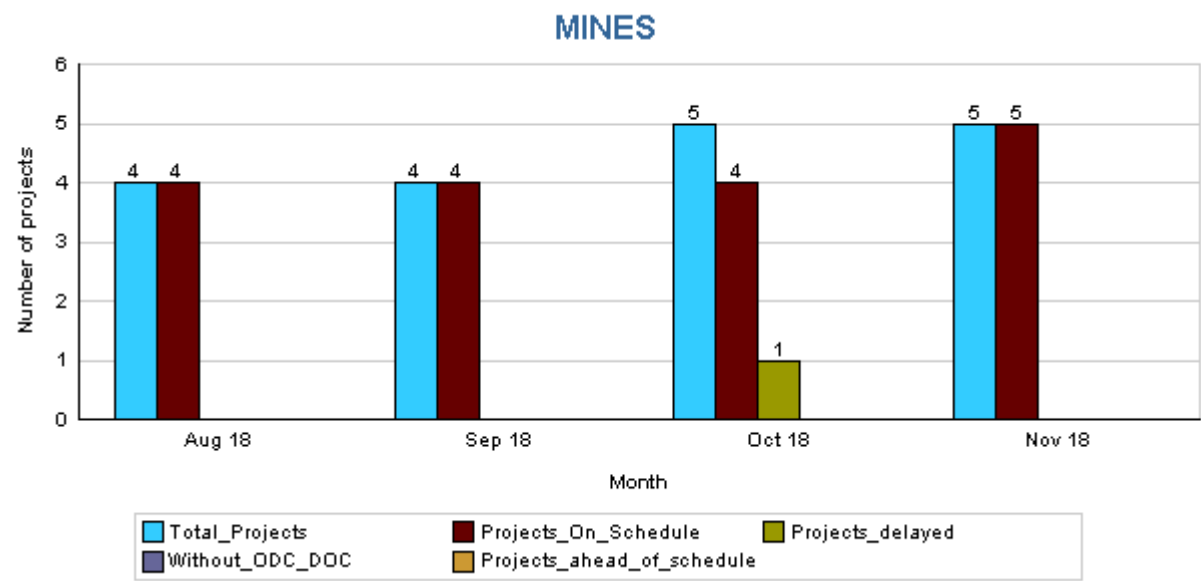


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

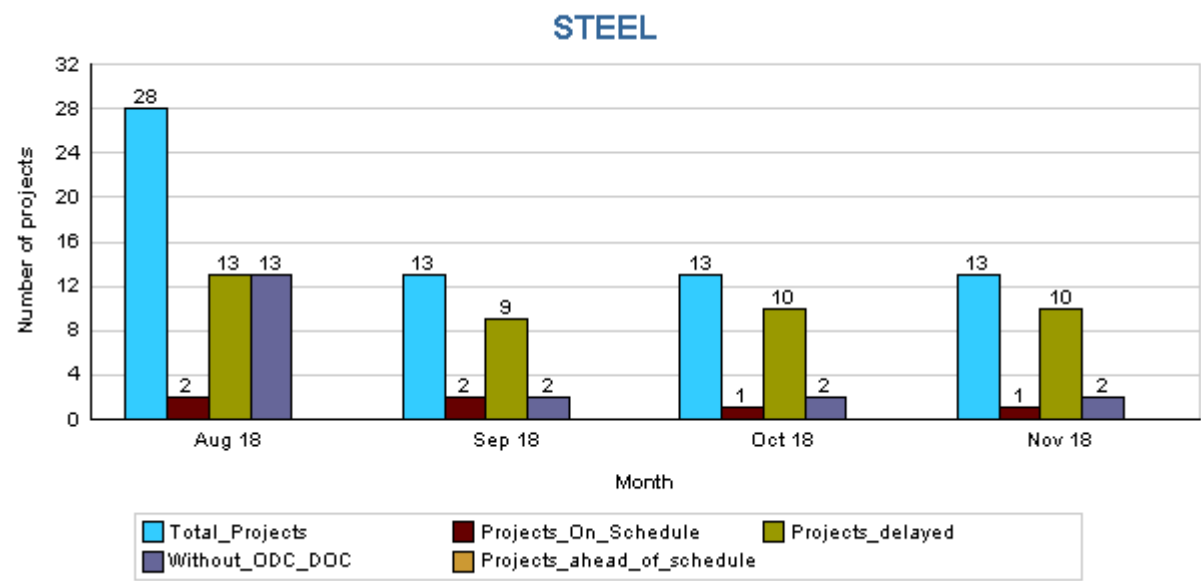


Break-up of 10 Delayed projects in November 2018

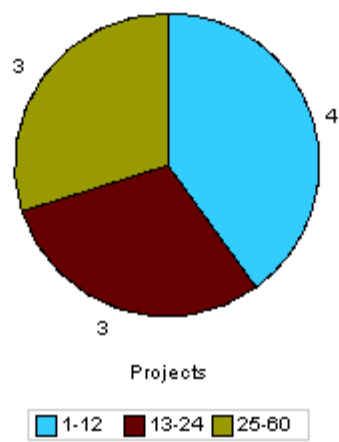


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

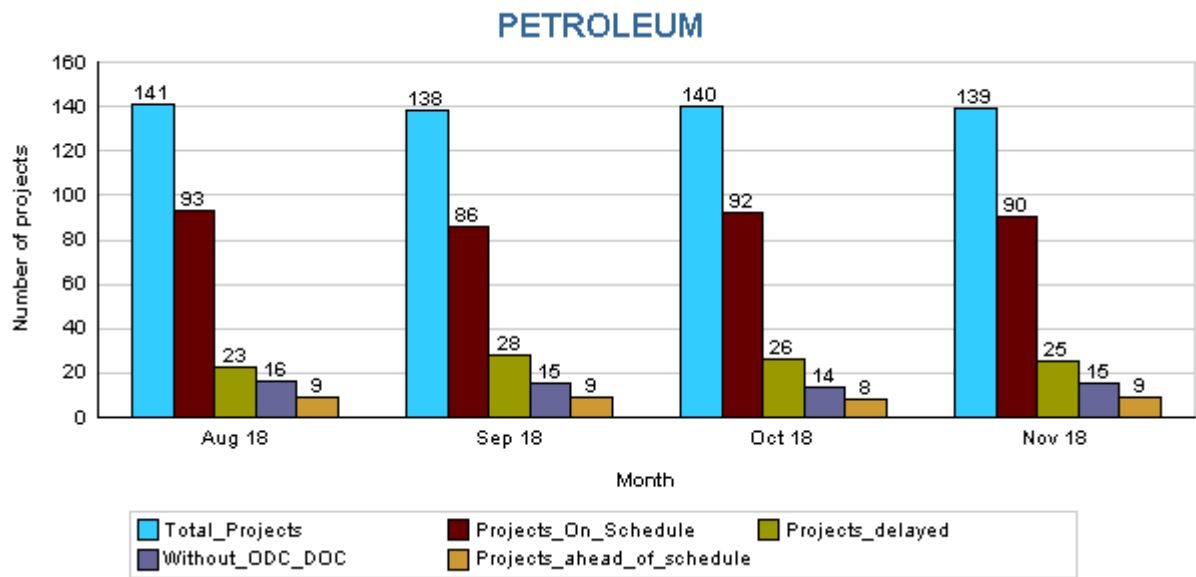


Break-up of 25 Delayed projects in November 2018

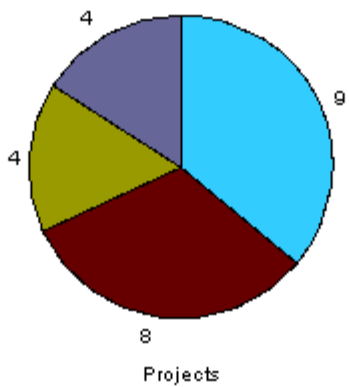


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

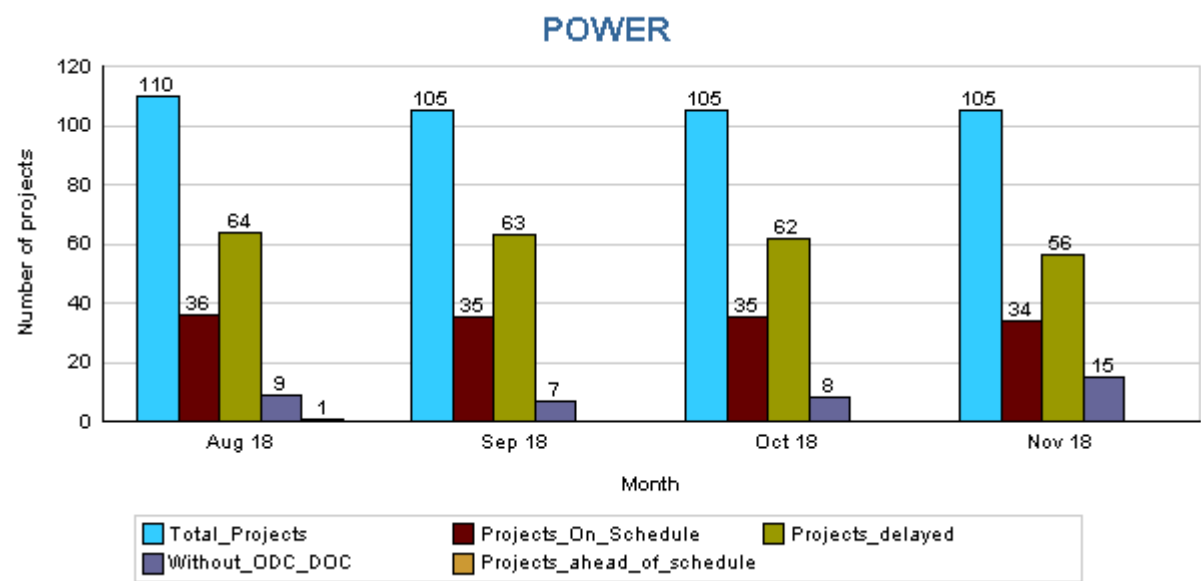


Break-up of 56 Delayed projects in November 2018

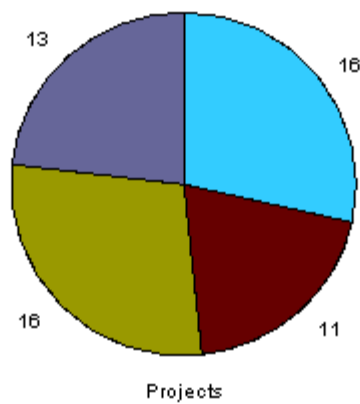


Delay in Months 1-12 13-24 25-60 60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

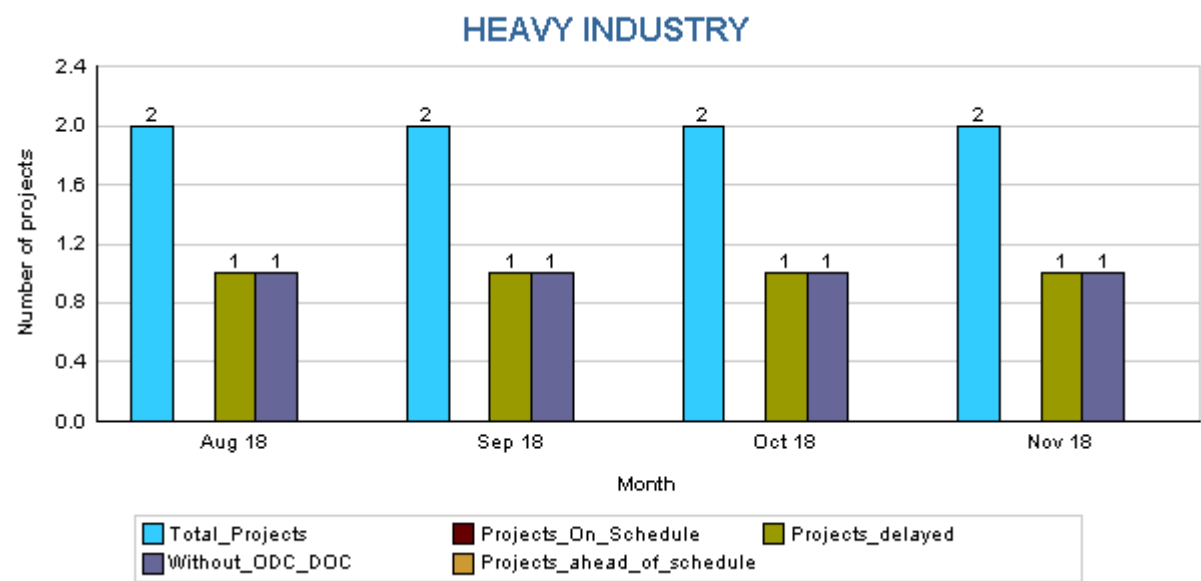


Break-up of 1 Delayed projects in November 2018




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

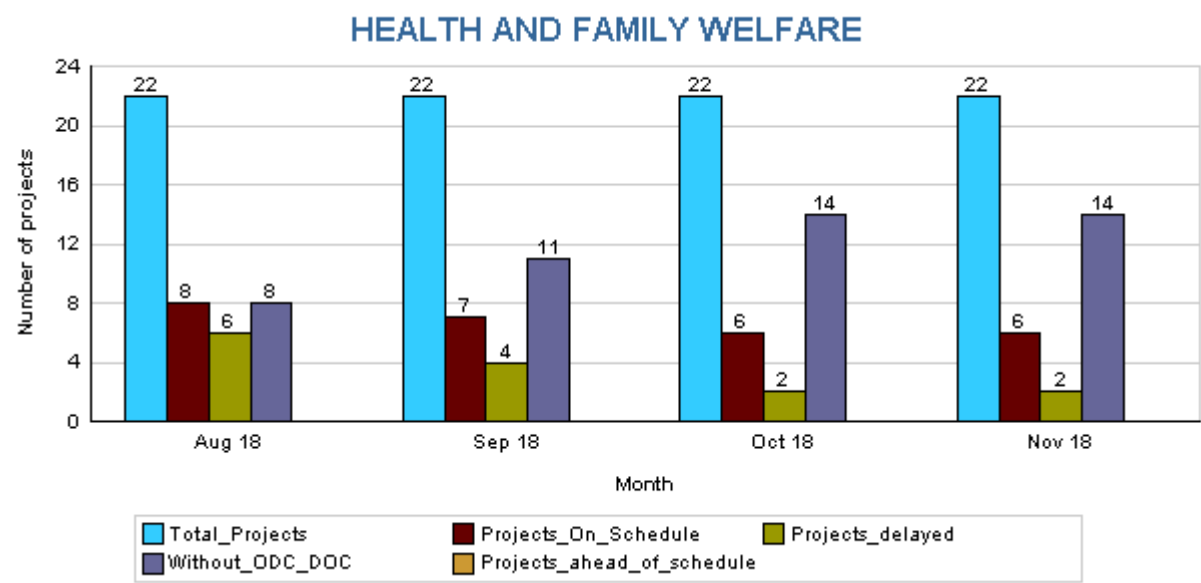


Break-up of 2 Delayed projects in November 2018

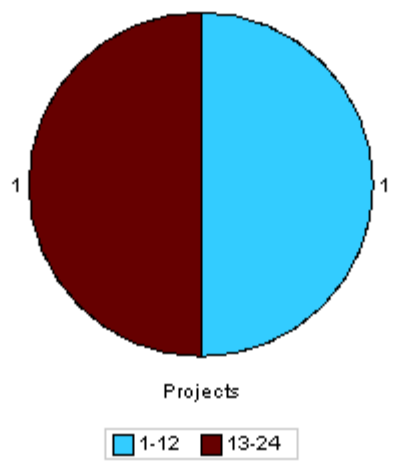


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

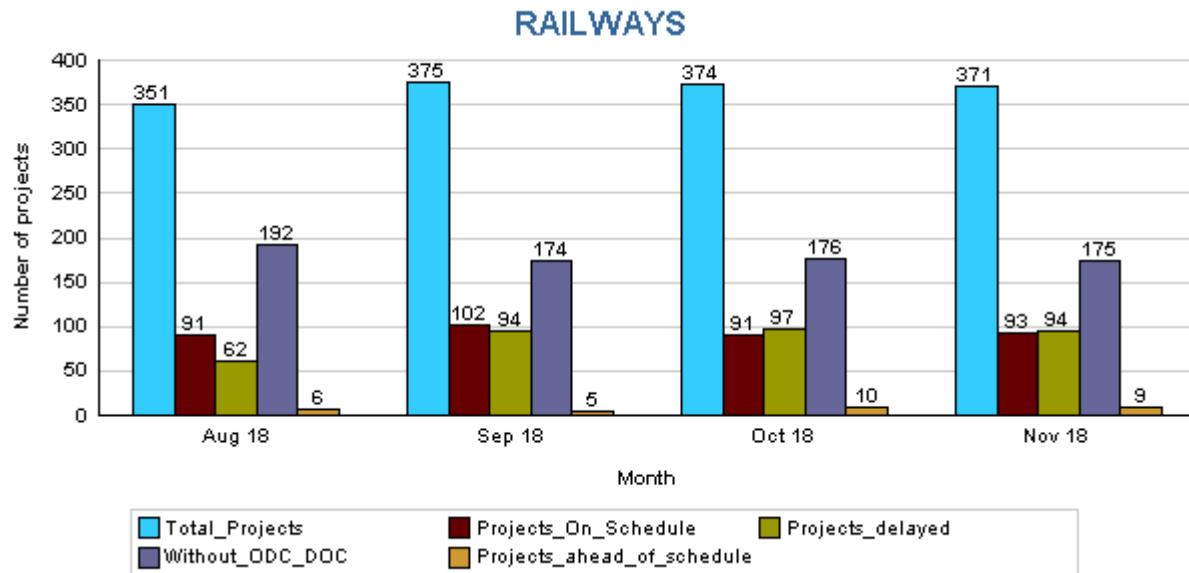


Break-up of 94 Delayed projects in November 2018

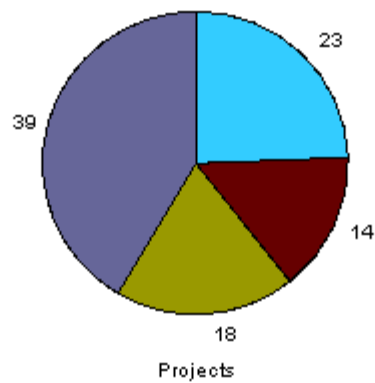


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

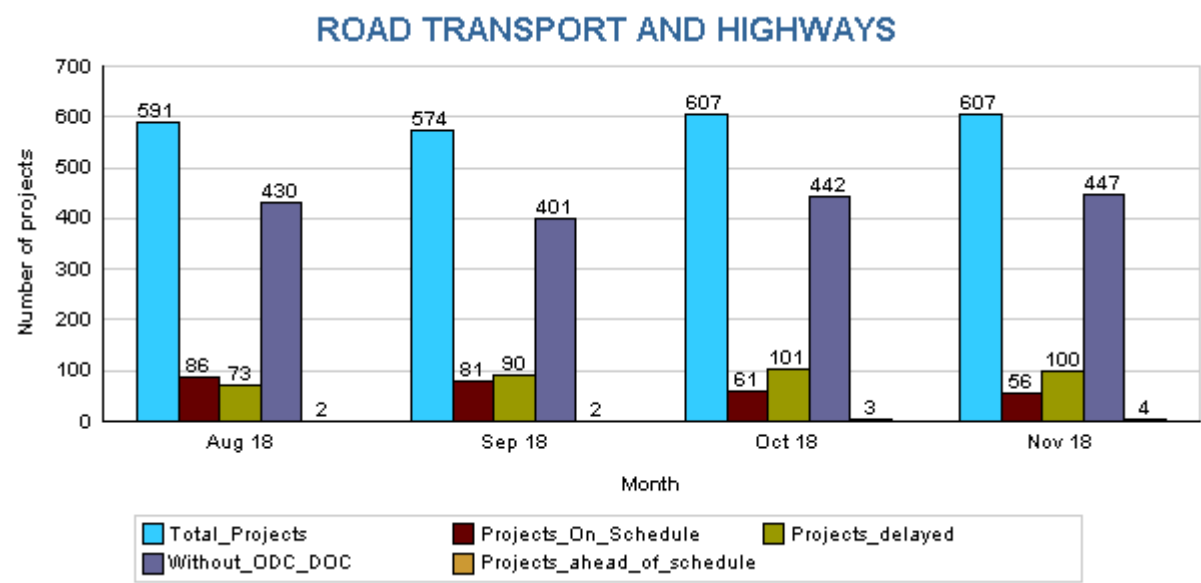


Break-up of 100 Delayed projects in November 2018

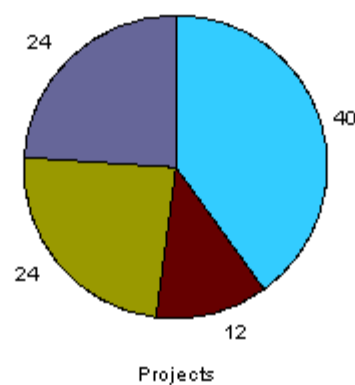


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	40	12	24	24

Graphical Presentation of All Projects w.r.t. Original Schedule

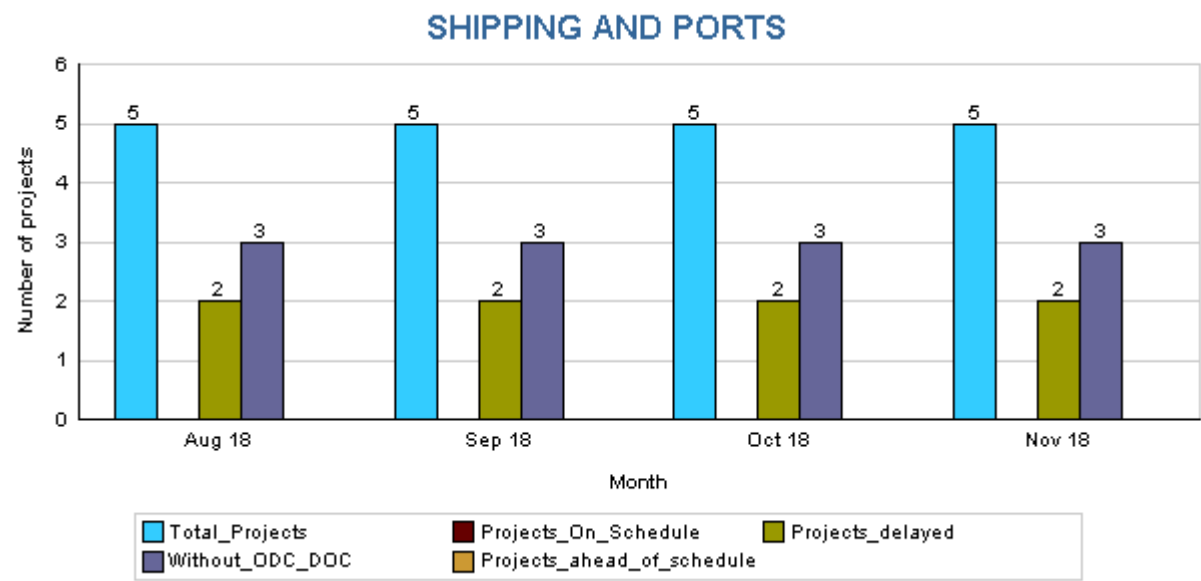


Break-up of 2 Delayed projects in November 2018

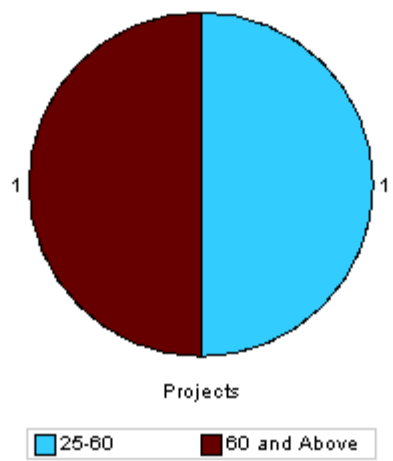


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

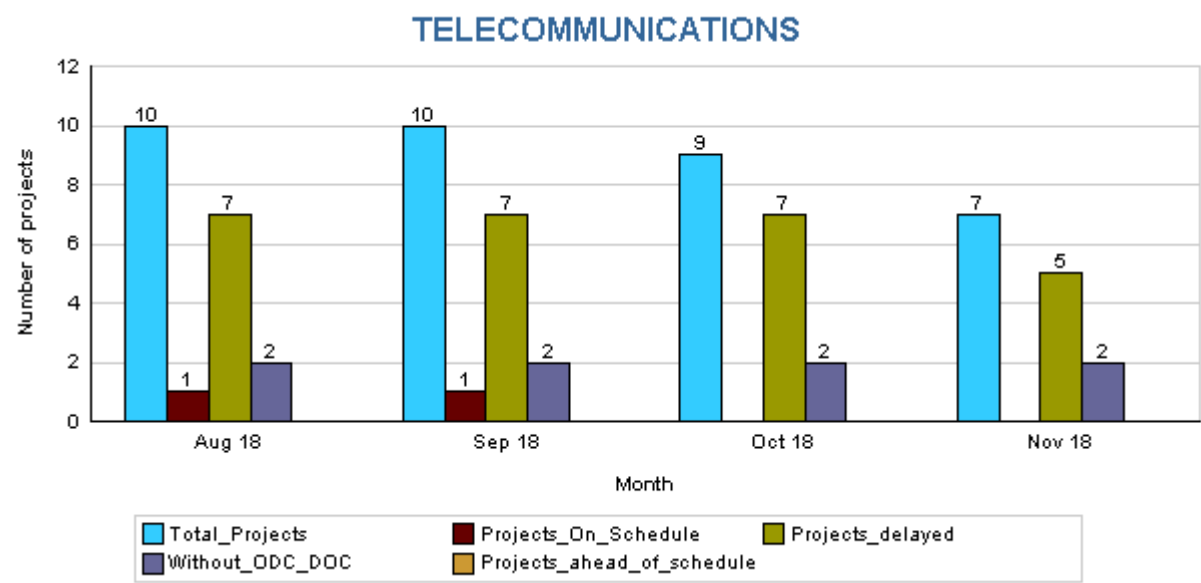


Break-up of 5 Delayed projects in November 2018

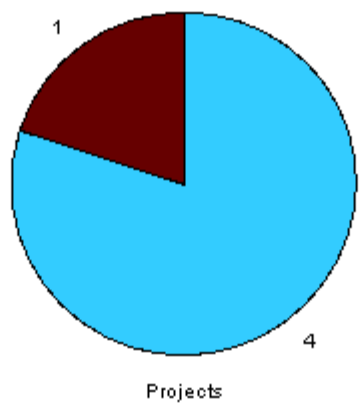


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

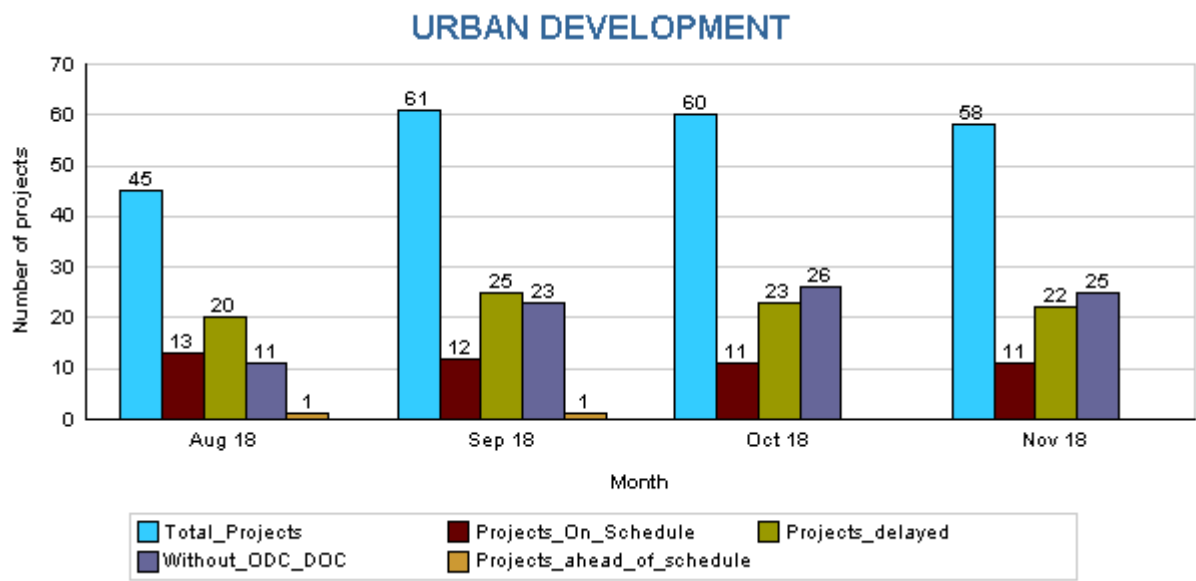


Break-up of 22 Delayed projects in November 2018

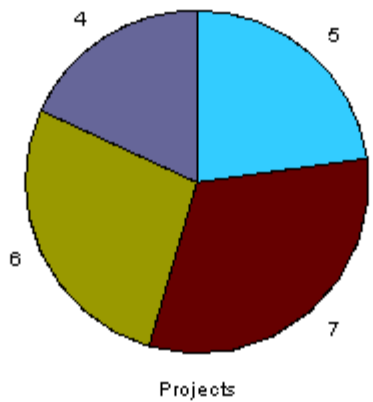


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	5	7	6	4

Graphical Presentation of All Projects w.r.t. Original Schedule

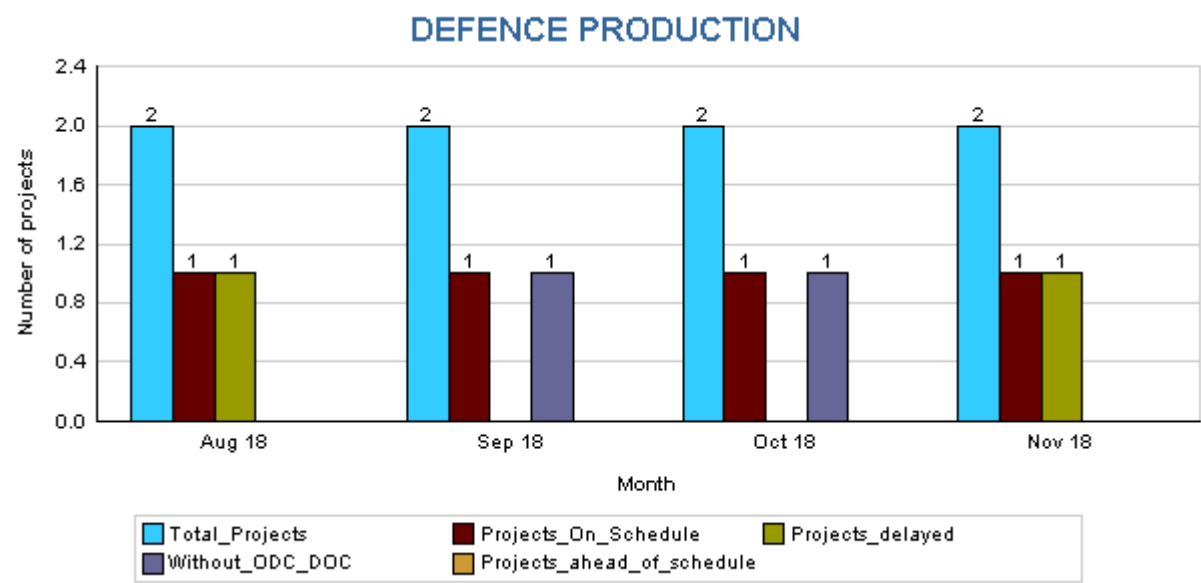

Break-up of 1 Delayed projects in November 2018

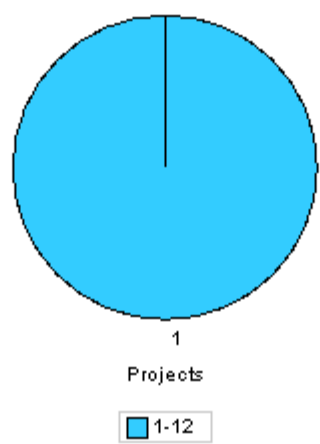

Delay in Months

TABLE-29

Sector wise analysis of projects Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	722,41.00	74,849.00	38,963.52
CIVIL AVIATION	1	314.61	3,14.61	441.33	85.79
COAL	96	94,283.98	931,16.54	93,710.95	28,239.72
FERTILISERS	6	1,781.92	17,93.57	1,793.57	657.54
MINES	5	7,078.62	70,78.62	7,078.62	556.09
STEEL	13	32,529.65	325,29.65	32,317.05	20,968.38
PETROLEUM	139	2,24,277.86	2,271,48.34	2,24,729.39	70,611.62
POWER	105	3,07,223.51	3,228,19.00	3,72,561.25	2,37,045.39
HEAVY INDUSTRY	2	3,272.00	32,72.00	5,381.30	2,450.86
HEALTH AND FAMILY WELFARE	22	8,611.12	86,11.12	8,660.03	2,965.39
RAILWAYS	371	4,90,540.40	5,809,99.42	7,04,794.36	1,71,075.46
ROAD TRANSPORT AND HIGHWAYS	607	4,11,883.30	4,124,53.43	4,26,107.82	1,41,033.89
SHIPPING AND PORTS	5	3,788.29	34,59.79	4,230.74	1,659.56
TELECOMMUNICATIONS	7	16,637.51	166,36.31	27,866.31	9,027.02
URBAN DEVELOPMENT	58	1,60,566.07	1,610,98.60	1,66,153.31	72,017.41
DEFENCE PRODUCTION	2	453.64	4,54.00	461.66	138.80
Grand total	1443	18,30,362.48	19,44,026.00	21,51,136.69	7,97,496.44

Table-30

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	12,707.00	12/2015 11/2016	06/2020	54(O) 43(R)	50/70
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	9,937.00	12/2016 03/2017	12/2020	48(O) 45(R)	37/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,100.00	5,687.52	09/2010 -	03/2019	102(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	10,632.00	11/2020 -	11/2023	36(O) -	18/76
	Total		67,120.00 -	74,849.00	38,963.52				188/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
	Total		314.61 -	441.33	85.79				0/0
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,842.98	03/2023 -	03/2023	0(O) -	14/18
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,902.85	03/2023 -	03/2023	0(O) -	6/20
8	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.13	03/2023 -	03/2023	0(O) -	1/12
9	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	172.27	03/2015 03/2020	03/2020	60(O) 0(R)	5/9
10	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	1/7
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	202.68	03/2014 -	03/2020	72(O) -	0/4
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.50	03/2016 -	03/2019	36(O) -	7/9
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	163.85	03/2016 -	03/2019	36(O) -	4/7
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	74.81	03/2022 -	03/2022	0(O) -	2/9
15	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	58.15	03/2020 -	03/2020	0(O) -	4/8
16	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	52.39	03/2018 -	03/2018	-	1/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMGAON OPENCAS T PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	56.54	03/2020 -	03/2020	0(O) -	0/6
18	DURGAPUR OPENCAS T PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	3.81	03/2023 -	03/2023	0(O) -	1/10
19	MADANNAGAR OPENCAS T PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	0/4
20	VIJAY WEST OPENCAS T PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
21	MAHAMAYA OPENCAS T PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/0
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	184.20	07/2012 -	03/2021	104(O) -	4/5
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	131.07	03/2014 -	-	-	6/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	103.27	03/2011 -	03/2020	108(O) -	3/5
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	174.69	03/2012 -	03/2019	84(O) -	3/5
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	176.72	03/2012 -	03/2019	84(O) -	4/5
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	340.06	03/2016 -	03/2019	36(O) -	5/5
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	89.21	03/2014 -	03/2019	60(O) -	5/5
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	-	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	325.14	04/2015 -	04/2019	48(O) -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	184.43	03/2020 -	03/2020	0(O) -	6/6
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	194.20	05/2014 -	04/2018	-	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	178.53	04/2014 -	04/2018	-	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	42.45	03/2022 -	03/2022	0(O) -	1/22
37	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 -	486.57	266.38	03/2012 -	-	-	1/3
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 203.82	203.82	103.85	03/2023 03/2021	03/2021	-24(O) 0(R)	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/8
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	113.19	03/2021 -	03/2021	0(O) -	3/9
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	41.51	03/2021 -	03/2021	0(O) -	1/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92	231.92	.00	03/2022	03/2022	0(O)	1/7
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33	488.33	4.06	03/2023	03/2023	0(O)	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44	869.44	111.53	03/2021	03/2021	0(O)	2/4
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87	409.87	16.21	03/2022	03/2022	0(O)	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09	1,783.09	207.63	03/2021	03/2021	0(O)	0/9
47	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17	1,255.17	94.68	03/2022	03/2022	0(O)	0/9
48	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82	441.82	184.45	03/2020	03/2020	0(O)	7/11
49	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16	611.16	391.37	03/2020	03/2020	0(O)	2/8
50	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23	266.23	143.29	03/2021	03/2021	0(O)	12/12
51	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67	267.67	207.74	03/2018	03/2018	-	7/7
52	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94	409.68	95.81	03/2023	03/2023	0(O)	7/11
53	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56	295.56	88.13	03/2019	03/2019	0(O)	10/13
54	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49	205.49	102.75	03/2020	03/2020	0(O)	5/10
55	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69	483.69	83.52	03/2021	03/2021	0(O)	2/6
56	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28	727.28	236.66	03/2025	03/2025	0(O)	5/13
57	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90	288.90	.00	03/2023	03/2023	0(O)	2/10
58	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65	313.34	6.12	03/2021	03/2024	36(O)	3/6
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42	498.42	52.87	03/2020	03/2020	0(O)	2/6
60	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68	198.68	254.72	03/2019	03/2019	0(O)	2/9
61	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52	304.52	129.39	03/2019	03/2019	0(O)	2/8
62	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73	362.73	257.36	03/2020	03/2020	0(O)	0/0
63	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76	319.76	58.04	03/2022	03/2022	0(O)	0/3
64	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07	458.07	16.00	03/2022	03/2022	0(O)	0/12
65	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00	328.00	88.46	03/2021	03/2021	0(O)	1/6
66	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96	302.96	302.96	03/2010	03/2018	-	10/10

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10	490.10	387.94	03/2017	03/2020	36(O)	11/12
68	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77	457.77	583.96	03/2013	03/2020	84(O)	8/9
69	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08	172.08	266.97	03/2010	03/2020	120(O)	3/4
70	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28	207.28	234.29	03/2012	03/2021	108(O)	5/5
71	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53	479.53	251.75	03/2013	03/2020	84(O)	6/9
72	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15	479.15	116.85	03/2019	03/2024	60(O)	2/9
73	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36	3,756.36	689.19	03/2026	03/2026	0(O)	5/15
74	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66	337.66	60.36	03/2019	03/2021	24(O)	5/6
75	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03	289.03	27.48	03/2018	03/2020	24(O)	3/5
76	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38	1,375.38	435.69	03/2021	03/2021	0(O)	5/9
77	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45	522.45	8.71	09/2019	09/2019	0(O)	0/0
78	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63	513.63	173.06	12/2019	12/2019	0(O)	0/0
79	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11	5,907.11	5,770.46	12/2015 12/2018	03/2019	39(O) 3(R)	26/35
80	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	391.20	06/2015 09/2019	09/2019	51(O) 0(R)	5/7
81	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03	448.86	186.91	03/2012	03/2024	144(O)	35/42
82	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63	453.63	121.91	12/2012	-	-	11/44
83	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97	489.62	477.74	03/2012	03/2023	132(O)	0/2
84	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78	209.78	154.21	03/2015	03/2019	48(O)	30/31
85	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19	181.19	159.87	03/2012	-	-	5/6
86	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29	164.04	12.69	03/2015	03/2021	72(O)	0/5
87	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76	349.28	1.31	03/2015	03/2021	72(O)	4/29
88	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06	437.51	353.61	03/2015	03/2021	72(O)	6/13
89	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01	365.01	204.26	06/2015	03/2019	45(O)	35/36
90	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33	384.32	146.45	07/2016	03/2020	44(O)	21/28
91	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45	415.37	160.45	03/2016	03/2019	36(O)	37/39

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	79.96	03/2019 -	03/2019	0(O) -	10/18
93	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.00	03/2018 -	03/2019	12(O) -	0/9
94	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	.00	03/2020 -	03/2020	0(O) -	1/17
95	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	.00	03/2019 -	03/2019	0(O) -	0/11
96	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA 6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	572.40	03/2018 -	03/2019	12(O) -	10/10
97	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	3,716.05	11/2021 -	11/2021	0(O) -	0/0
98	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	296.64	03/2022 -	03/2022	0(O) -	8/13
99	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	382.14	03/2018 -	03/2020	24(O) -	11/16
100	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	2,661.73	174.04	08/2019 -	08/2019	0(O) -	0/19
101	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/21
	Total		94,283.98 -	93,710.95	28,239.72				490/996
	<u>FERTILISERS</u>								
102	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	27.20	11/2019 -	11/2019	0(O) -	0/2
103	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	126.30	11/2016 04/2019	04/2019	29(O) 0(R)	1/13
104	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 482.85	482.85	413.00	12/2017 12/2018	12/2018	12(O) 0(R)	0/1
105	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	38.65	04/2020 -	04/2020	0(O) -	0/14
106	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	23.79	11/2019 -	11/2019	0(O) -	0/2
107	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	28.60	11/2019 -	11/2019	0(O) -	0/2
	Total		1,781.92 -	1,793.57	657.54				1/34
	<u>MINES</u>								
108	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	96.98	04/2021 04/2021	04/2021	0(O) 0(R)	3/3

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	302.19	01/2020 01/2020	01/2020	0(O) 0(R)	1/2
110	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2
111	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.00	04/2021 04/2021	04/2021	0(O) 0(R)	1/1
112	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 166.62	166.62	125.00	06/2019 06/2019	06/2019	0(O) 0(R)	0/1
	Total		7,078.62 -	7,078.62	556.09				7/9
	<u>STEEL</u>								
113	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	239.65	10/2016 -	03/2019	29(O) -	1/2
114	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,013.76	12/2017 -	09/2019	21(O) -	4/6
115	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	115.36	08/2018 -	02/2019	6(O) -	2/4
116	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	244.25	07/2018 -	01/2019	6(O) -	2/4
117	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	124.84	04/2015 -	-	-	4/5
118	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	14,485.63	05/2015 06/2019	06/2019	49(O) 0(R)	62/86
119	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020	0(O) -	5/12
120	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	362.48	10/2017 -	06/2020	32(O) -	0/2
121	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	855.62	12/2017 -	06/2019	18(O) -	1/2
122	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	106.59	09/2017 -	-	-	0/0
123	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	76.61	06/2019 -	06/2020	12(O) -	0/1
124	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,509.89	04/2018 -	05/2019	13(O) -	3/3
125	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	802.10	09/2018 -	03/2019	6(O) -	3/5
	Total		32,529.65 -	32,317.05	20,968.38				87/132
	<u>PETROLEUM</u>								
126	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0(O) -	0/111

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
127	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	241.80	09/2019 -	09/2019	0(O) -	19/27
128	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	1,450.26	06/2020 08/2021	08/2021	14(O) 0(R)	0/20
129	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
130	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
131	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 207.80	207.80	27.54	09/2018 02/2019	02/2019	5(O) 0(R)	0/5
132	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	38.79	04/2021 -	04/2021	0(O) -	0/0
133	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	1.12	04/2021 -	04/2021	0(O) -	0/0
134	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	.00	04/2022 -	04/2022	0(O) -	0/0
135	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	139.42	02/2019 -	12/2018	-2(O) -	3/10
136	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.86	2,107.69	03/2013 03/2019	03/2019	72(O) 0(R)	5/15
137	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	60.44	01/2014 11/2019	11/2019	70(O) 0(R)	6/7
138	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	208.63	08/2019 -	08/2019	0(O) -	2/13
139	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,208.92	11/2019 -	11/2019	0(O) -	12/17
140	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 249.85	244.70	98.10	05/2020 05/2020	05/2020	0(O) 0(R)	0/5
141	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8(O) -	0/0
142	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	268.88	09/2019 -	09/2019	0(O) -	5/7
143	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	543.91	1.65	02/2020 -	02/2020	0(O) -	1/14
144	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	69.88	02/2020 -	02/2020	0(O) -	0/0
145	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
146	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	809.78	11/2018 -	11/2018	0(O) -	7/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
147	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	385.61	12/2020 -	02/2020	-10(O) -	2/2
148	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	78.63	06/2020 -	06/2020	0(O) -	2/2
149	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	.00	03/2021 -	03/2021	0(O) -	5/26
150	DEVLOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	.00	10/2020 -	10/2020	0(O) -	0/0
151	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	28.18	10/2022 -	10/2022	0(O) -	0/0
152	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	3.64	01/2021 -	01/2021	0(O) -	0/0
153	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	1.88	03/2021 -	03/2021	0(O) -	0/0
154	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	.00	04/2021 -	04/2021	0(O) -	0/0
155	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,449.66	05/2019 10/2019	10/2019	5(O) 0(R)	0/14
156	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 567.22	567.22	449.95	11/2019 -	11/2019	0(O) -	0/5
157	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	156.83	03/2018 -	03/2018	-	20/22
158	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	110.98	04/2018 -	12/2018	8(O) -	18/20
159	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	285.28	03/2026 03/2026	03/2026	0(O) 0(R)	0/10
160	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	67.71	07/2020 -	07/2020	0(O) -	0/0
161	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	-	-	0/0
162	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	3.67	08/2020 -	08/2020	0(O) -	0/0
163	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,151.10	09/2019 -	09/2019	0(O) -	0/9
164	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020	0(O) -	0/0
165	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	.00	- -	-	-	2/17
166	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	4.33	11/2020 -	11/2020	0(O) -	0/46
167	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	.12	02/2020 -	02/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
168	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	857.95	07/2019 -	07/2019	0(O) -	0/9
169	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	123.17	08/2020 -	08/2020	0(O) -	0/0
170	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	194.38	05/2019 -	12/2018	-5(O) -	4/13
171	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	99.30	09/2019 -	09/2019	0(O) -	2/2
172	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 -	-	-	8/12
173	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	87.79	03/2023 03/2022	03/2022	-12(O) 0(R)	0/10
174	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
175	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	22.11	10/2022 -	10/2022	0(O) -	5/9
176	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	21.92	10/2022 -	10/2022	0(O) -	0/0
177	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
178	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	733.62	02/2020 -	02/2020	0(O) -	0/0
179	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019	0(O) -	6/8
180	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	124.25	03/2019 03/2019	03/2019	0(O) 0(R)	5/11
181	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019	0(O) -	7/9
182	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	581.00	.00	03/2020 -	03/2020	0(O) -	0/0
183	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	341.79	10/2017 -	03/2019	17(O) -	39/52
184	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	2,420.04	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
185	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	360.27	02/2020 10/2020	10/2020	8(O) 0(R)	0/20
186	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019	0(O) -	0/0
187	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	11.66	06/2020 -	06/2020	0(O) -	0/0
188	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,577.15	1,577.15	1,195.62	05/2013 03/2019	03/2019	70(O) 0(R)	1/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 12/2019	12/2019	57(O) 0(R)	0/17
190	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,559.88	04/2019 03/2019	03/2019	-1(O) 0(R)	0/9
191	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 -	2,504.61	2,119.15	05/2017 12/2018	12/2018	19(O) 0(R)	0/4
192	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	1,687.43	03/2019 05/2020	05/2020	14(O) 0(R)	0/5
193	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 4,619.94	4,619.94	3,931.91	12/2017 03/2019	03/2019	15(O) 0(R)	4/5
194	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,102.45	04/2018 05/2019	05/2019	13(O) 0(R)	0/10
195	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	499.85	08/2021 -	08/2021	0(O) -	2/2
196	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	135.68	02/2020 -	02/2020	0(O) -	0/10
197	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	115.17	12/2019 -	12/2019	0(O) -	0/0
198	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	14.11	01/2021 -	01/2021	0(O) -	0/0
199	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	8.48	01/2021 -	01/2021	0(O) -	0/0
200	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	8.48	01/2021 -	01/2021	0(O) -	0/0
201	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
202	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	299.26	05/2019 05/2019	05/2019	0(O) 0(R)	0/5
203	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	191.39	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
204	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	167.64	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
205	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	502.40	11/2019 11/2019	11/2019	0(O) 0(R)	0/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
206	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,006.83	4,006.83	1,226.29	05/2021 05/2021	05/2021	0(O) 0(R)	0/15
207	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	56.69	08/2020 -	08/2020	0(O) -	0/15
208	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(O) -	0/0
209	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	.00	12/2019 -	12/2019	0(O) -	4/5
210	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	2,313.08	12/2018 -	12/2018	0(O) -	34/39
211	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	543.05	09/2011 -	-	-	0/3
212	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8
213	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	1,308.86	06/2018 -	10/2018	-	1/1
214	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	586.10	10/2014 02/2019	02/2019	52(O) 0(R)	32/40
215	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	196.39	03/2017 06/2019	06/2019	27(O) 0(R)	2/15
216	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	569.04	12/2020 -	12/2020	0(O) -	0/0
217	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	619.33	12/2020 -	08/2020	-4(O) -	2/2
218	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	516.56	10/2019 -	03/2019	-7(O) -	3/3
219	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	169.70	07/2018 10/2020	10/2020	27(O) 0(R)	21/36
220	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	961.58	06/2020 -	06/2020	0(O) -	14/24
221	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	110.04	02/2019 -	02/2019	0(O) -	10/13
222	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	23.61	10/2020 -	10/2020	0(O) -	6/12
223	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	42.33	12/2019 -	12/2019	0(O) -	6/22
224	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	774.62	12/2019 12/2020	12/2019	0(O) -12(R)	15/24
225	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	776.24	12/2020 -	12/2020	0(O) -	14/24
226	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	663.13	12/2020 -	12/2020	0(O) -	14/24

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
227	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 3,030.00	2,915.00	1,965.67	12/2012 02/2019	06/2019	78(O) 4(R)	14/42
228	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	49.88	03/2021 -	03/2021	0(O) -	3/26
229	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
230	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	1.66	12/2021 -	12/2021	0(O) -	0/0
231	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,443.76	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
232	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	652.51	12/2020 -	12/2020	0(O) -	15/24
233	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	256.93	01/2019 -	01/2019	0(O) -	5/6
234	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	33.81	12/2019 -	12/2019	0(O) -	17/26
235	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	29.39	07/2022 -	07/2022	0(O) -	0/0
236	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	2.56	12/2021 -	12/2021	0(O) -	0/0
237	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	181.20 -	181.20	14.06	07/2022 -	07/2022	0(O) -	0/0
238	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	4,807.08 -	4,807.08	24.09	07/2021 -	07/2021	0(O) -	0/0
239	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	19.99	12/2020 -	12/2020	0(O) -	0/14
240	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
241	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.04	- -	-	-	2/26
242	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
243	RESID UPGRADEATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.42	11/2015 -	-	-	52/52
244	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.12	02/2017 -	-	-	0/0
245	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 390.52	390.52	172.79	03/2019 -	04/2019	1(O) -	0/5
246	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	302.17	12/2018 -	12/2020	24(O) -	2/2
247	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	.17	06/2020 -	06/2020	0(O) -	2/3
248	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	575.65	12/2019 -	12/2019	0(O) -	0/0
249	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	16.73	08/2020 -	08/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
250	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	1.18	10/2020 -	05/2021	7(O) -	0/0
251	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	800.00	600.58	12/2018 -	12/2018	0(O) -	16/20
252	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	99.03	04/2022 -	04/2022	0(O) -	27/33
253	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	12.65	08/2021 -	08/2021	0(O) -	0/0
254	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	200.89	09/2019 -	09/2019	0(O) -	0/6
255	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.00	08/2020 -	08/2020	0(O) -	0/0
256	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	3.41	12/2021 -	12/2021	0(O) -	0/0
257	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	25.56	02/2020 -	02/2020	0(O) -	18/26
258	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,	03/2014	3,076.00 4,190.00	4,190.00	3,184.09	09/2017 06/2018	06/2018	-	6/7
259	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	694.00	507.96	10/2018 12/2018	12/2018	2(O) 0(R)	0/15
260	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
261	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	21.02	12/2020 -	12/2020	0(O) -	10/24
262	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	32.69	04/2020 -	04/2020	0(O) -	15/26
263	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	738.18	09/2019 -	09/2019	0(O) -	0/11
264	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,712.00	6.28	09/2022 -	06/2021	-15(O) -	0/0
	Total		2,24,277.86 -	2,24,729.39	70,611.62				587/1451
	POWER								
265	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,385.81	09/2010 -	-	-	0/0
266	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,838.94	12/2009 03/2019	03/2019	111(O) 0(R)	30/30
267	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	7,186.04	09/2011 06/2018	12/2018	87(O) 6(R)	35/37

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
268	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	15,031.14	01/2011 04/2021	04/2021	123(O) 0(R)	26/47
269	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 -	05/2019	60(O) -	3/18
270	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	12,079.00	01/2018 -	05/2020	28(O) -	31/34
271	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	506.97	12/2016 -	12/2018	24(O) -	13/19
272	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.30	502.54	06/2019 -	06/2019	0(O) -	0/0
273	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	10,490.56	06/2017 06/2019	06/2019	24(O) 0(R)	34/40
274	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,293.72	11/2019 -	11/2019	0(O) -	0/0
275	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	191.64	05/2017 -	06/2019	25(O) -	4/9
276	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	516.25	10/2018 -	10/2018	-	0/0
277	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	194.26	12/2018 -	12/2018	0(O) -	0/0
278	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	309.64	11/2017 -	12/2018	13(O) -	1/4
279	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	52.14	09/2018 -	06/2019	9(O) -	0/0
280	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	2.50	06/2019 -	06/2019	0(O) -	0/0
281	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,394.80	7,121.50	09/2009 -	12/2021	147(O) -	2/3
282	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	982.71	04/2020 -	10/2023	42(O) -	0/0
283	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,333.71	1,528.12	09/2017 -	09/2018	-	0/0
284	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	7,673.86	02/2019 10/2020	10/2020	20(O) 0(R)	20/23
285	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	2,922.12	10/2017 -	12/2016	-	0/0
286	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 -	-	-	48/48
287	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	197.76	02/2019 -	02/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
288	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	9,958.55	09/2017 06/2019	06/2019	21(O) 0(R)	34/41
289	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	6,135.72	09/2019 -	09/2019	0(O) -	26/31
290	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	215.81	03/2017 -	11/2018	20(O) -	0/0
291	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	161.82	06/2018 -	12/2018	6(O) -	0/0
292	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	65.37	09/2020 -	09/2020	0(O) -	9/16
293	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	1,324.00	06/2018 -	12/2018	6(O) -	0/0
294	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 -	738.48	669.46	09/2010 -	12/2018	99(O) -	5/8
295	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
296	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	8,911.13	11/2016 03/2019	03/2019	28(O) 0(R)	34/38
297	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 -	5,071.94	4,538.37	10/2012 -	02/2019	76(O) -	8/11
298	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 -	13,762.80	12,714.20	08/2013 -	03/2022	103(O) -	23/26
299	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 -	2,932.88	2,654.96	12/2012 -	11/2018	71(O) -	18/23
300	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 -	1,731.10	1,461.65	11/2012 -	10/2018	-	12/13
301	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	499.90	06/2014 -	12/2018	54(O) -	10/12
302	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 -	534.02	426.98	08/2014 -	12/2018	52(O) -	8/10
303	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	3,190.27	2,281.28	12/2015 -	11/2018	35(O) -	15/18
304	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 -	1,891.41	1,202.20	04/2016 -	12/2018	32(O) -	8/12
305	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	187.24	04/2016 -	10/2018	-	0/0
306	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	419.63	06/2016 -	12/2018	30(O) -	9/11
307	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	550.18	433.43	11/2016 -	06/2019	31(O) -	8/12
308	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 -	206.42	145.22	03/2016 -	11/2018	32(O) -	4/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
309	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	2,716.40	03/2018 -	03/2019	12(O) -	9/12
310	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 -	225.28	148.92	02/2016 -	11/2018	33(O) -	16/17
311	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 -	340.88	229.40	03/2018 -	11/2018	8(O) -	1/3
312	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	407.22	10/2017 -	09/2019	23(O) -	0/5
313	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	181.16	07/2017 -	06/2019	23(O) -	3/5
314	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	74.71	03/2018 -	12/2018	9(O) -	0/0
315	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	630.56	09/2017 -	11/2018	14(O) -	0/0
316	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	2,518.90	04/2018 -	12/2018	8(O) -	5/9
317	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	1,420.89	07/2018 -	12/2018	5(O) -	0/0
318	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	1,028.69	07/2018 -	10/2018	-	0/0
319	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	332.96	01/2018 -	03/2019	14(O) -	0/0
320	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	375.34	11/2018 -	11/2018	0(O) -	0/0
321	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	1,861.40	05/2019 -	05/2019	0(O) -	0/0
322	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	3,710.05	11/2019 -	11/2019	0(O) -	0/0
323	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	97.53	11/2018 -	11/2018	0(O) -	0/0
324	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	88.66	07/2018 -	10/2018	-	0/0
325	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	250.73	03/2019 -	03/2019	0(O) -	0/0
326	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	191.76	02/2019 -	02/2019	0(O) -	0/0
327	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	76.98	02/2019 -	02/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
328	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	26.40	03/2019 -	03/2019	0(O) -	0/0
329	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	79.31	06/2019 -	06/2019	0(O) -	0/0
330	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	25.85	11/2019 -	11/2019	0(O) -	0/0
331	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	139.34	01/2019 -	03/2019	2(O) -	0/0
332	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	354.00	04/2019 -	04/2019	0(O) -	0/0
333	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	55.10	02/2020 -	02/2020	0(O) -	0/0
334	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	103.28	02/2019 -	02/2019	0(O) -	0/0
335	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	22.42	03/2019 -	03/2019	0(O) -	0/0
336	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	20.09	06/2019 -	06/2019	0(O) -	0/0
337	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	21.82	12/2019 -	12/2019	0(O) -	0/0
338	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	89.17	09/2019 -	09/2019	0(O) -	0/0
339	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	552.21	04/2020 -	04/2020	0(O) -	0/0
340	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	16.10	06/2019 -	06/2019	0(O) -	0/0
341	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,141.97	840.87	12/2018 -	12/2019	12(O) -	0/0
342	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,652.57	802.18	12/2018 -	12/2019	12(O) -	0/0
343	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 -	1,364.00	1,237.00	12/2015 -	12/2018	36(O) -	0/0
344	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	2,798.00	04/2019 -	04/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
345	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	597.00	07/2020 -	07/2020	0(O) -	0/0
346	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	321.99	02/2020 -	02/2020	0(O) -	0/0
347	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	.80	09/2019 -	02/2020	5(O) -	0/0
348	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	.00	05/2020 -	05/2020	0(O) -	0/0
349	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE ,	08/2008	771.00 -	1,624.00	1,429.45	02/2013 -	10/2018	-	0/0
350	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	8,122.05	08/2018 06/2019	06/2019	10(O) 0(R)	27/37
351	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	303.70	04/2019 -	04/2019	0(O) -	0/0
352	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	206.21	11/2017 -	11/2018	12(O) -	0/0
353	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	743.82	01/2019 -	01/2019	0(O) -	0/0
354	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 -	2,534.00	2,051.63	11/2008 -	12/2018	121(O) -	20/22
355	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 -	2,702.65	2,529.92	09/2014 -	10/2018	-	11/13
356	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	50.27	07/2019 -	07/2019	0(O) -	0/0
357	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	2,701.10	07/2020 10/2020	10/2020	3(O) 0(R)	19/22
358	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 -	1,078.31	963.23	07/2013 -	-	-	26/26
359	FGUTPP UNCHAHAAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
360	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	5,195.95	03/2019 09/2019	09/2019	6(O) 0(R)	19/32
361	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	215.93	02/2014 02/2018	03/2019	61(O) 13(R)	7/8
362	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	8,789.00	12/2016 -	08/2019	32(O) -	31/34
363	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	4,401.90	2,672.04	02/2016 12/2020	05/2021	63(O) 5(R)	16/30
364	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,690.33	03/2013 12/2020	12/2020	93(O) 0(R)	6/15
365	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,105.30	1,583.40	06/2013 -	12/2021	102(O) -	9/13

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
366	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	151.99	08/2017 -	-	-	0/15
367	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	131.82	12/2021 -	12/2021	0(O) -	1/32
368	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	376.58	09/2019 02/2022	02/2022	29(O) 0(R)	5/9
369	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	238.92	04/2018 -	11/2019	19(O) -	0/0
	Total		3,07,223.51 -	3,72,561.25	2,37,045.39				778/1028
	<u>HEAVY INDUSTRY</u>								
370	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37(O) -	0/0
371	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-	-	0/25
	Total		3,272.00 -	5,381.30	2,450.86				0/25
	<u>HEALTH AND FAMILY WELFARE</u>								
372	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	76.88	03/2019 -	03/2019	0(O) -	0/0
373	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	36.93	- -	-	-	0/0
374	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
375	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	174.00	05/2021 -	05/2021	0(O) -	0/0
376	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
377	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	237.80	05/2017 -	-	-	0/2
378	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	237.86	05/2017 -	-	-	0/5
379	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.56	22.59	- -	-	-	0/0
380	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	17.00	- -	-	-	0/0
381	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	355.00	03/2018 -	-	-	0/2
382	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	322.00	469.00	08/2018 -	-	-	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
383	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	122.66	03/2019 -	03/2019	0(O) -	0/0
384	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	4.80	- -	-	-	0/0
385	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	71.00	05/2018 -	08/2019	15(O) -	0/0
386	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	58.52	02/2018 -	12/2018	10(O) -	0/1
387	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	272.00	06/2020 -	06/2020	0(O) -	0/0
388	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	18.50	- -	-	-	0/0
389	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	39.35	04/2020 -	04/2020	0(O) -	0/0
390	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.38	191.38	05/2017 -	-	-	0/3
391	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	214.62	09/2018 -	-	-	0/0
392	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	71.50	03/2019 -	03/2019	0(O) -	0/0
393	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	19.50	- -	-	-	0/0
	Total		8,611.12 -	8,660.03	2,965.39				0/14
	<u>RAILWAYS</u>								
394	NANDYAL-YERRAGUNTALA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	10/2018	-	0/0
395	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	289.91	03/2009 03/2023	03/2023	168(O) 0(R)	0/0
396	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	732.81 -	1,850.00	1,972.23	03/2008 -	03/2020	144(O) -	0/0
397	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
398	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	- -	-	-	0/1
399	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	375.28	03/2021 03/2022	03/2022	12(O) 0(R)	0/1
400	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	931.68	03/2020 -	03/2022	24(O) -	0/0
401	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.07	- -	-	-	0/0
402	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	124.49	03/2022 03/2023	03/2023	12(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
403	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	249.33	12/2023 -	12/2023	0(O) -	0/0
404	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	2,499.71	183.68	03/2022 -	03/2022	0(O) -	0/0
405	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
406	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	2.98	03/2019 -	12/2020	21(O) -	0/0
407	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM ,	09/1997	3,230.02 4,857.00	5,820.00	5,224.22	04/2008 12/2011	06/2018	-	0/0
408	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020	12(O) -	0/0
409	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 -	551.00	595.01	03/2019 -	03/2019	0(O) -	0/0
410	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	264.69	03/2019 -	03/2019	0(O) -	0/0
411	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	193.12	03/2022 -	03/2020	-24(O) -	0/0
412	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	821.00	163.08	03/2021 -	03/2021	0(O) -	0/0
413	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96(O) -	0/0
414	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	792.46 -	1,320.00	928.50	12/2010 -	-	-	0/0
415	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	589.15	183.72	- -	03/2022	-	0/0
416	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.77	330.82	- -	03/2023	-	0/0
417	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	640.78	03/2020 -	03/2020	0(O) -	0/0
418	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
419	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	413.56	364.21	06/2018 -	10/2018	-	0/0
420	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96(O) -	0/0
421	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2020	12(O) -	0/0
422	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	4.11	- -	03/2020	-	0/0
423	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	633.87 -	2,396.88	.39	- -	-	-	0/0
424	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	2,626.98	.00	- -	-	-	0/0
425	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	2,860.55	.00	- -	-	-	0/0
426	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	2,995.01	1.68	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
427	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	325.00 -	729.92	253.10	-	03/2021	-	0/0
428	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	378.56 -	2,614.36	111.71	-	03/2022	-	0/0
429	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
430	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
431	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	-	-	-	0/0
432	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
433	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	.19	-	03/2023	-	0/0
434	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	-	-	-	0/0
435	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	-	-	-	0/0
436	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,474.47	338.44	-	03/2021	-	0/0
437	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	785.87	40.00	03/2020 -	03/2020	0(O) -	0/0
438	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	-	-	-	0/0
439	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	.00	-	-	-	0/0
440	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	.00	03/2020 -	10/2021	19(O) -	0/1
441	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	.00	03/2020 -	10/2021	19(O) -	1/1
442	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
443	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12(O) -	0/0
444	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	.00	03/2021 -	03/2022	12(O) -	0/0
445	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR ,	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61(O) -	0/0
446	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	528.26	462.75	-	12/2018	-	0/0
447	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	566.41	759.20	-	12/2021	-	0/0
448	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) NL RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	631.78 632.00	1,195.00	653.64	12/2012 -	03/2022	111(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
449	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	383.54 -	555.00	575.93	03/2010 -	12/2019	117(O) -	0/3
450	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	571.51	03/2020 -	03/2020	0(O) -	1/1
451	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	758.09	849.72	03/2020 -	03/2020	0(O) -	0/0
452	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
453	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH ,	04/2011	1,471.93 -	543.00	.00	03/2022 -	03/2022	0(O) -	0/0
454	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,279.00	.00	12/2019 -	12/2019	0(O) -	0/0
455	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021	0(O) -	0/0
456	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH ,	02/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022	0(O) -	0/0
457	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	600.00	09/2018 -	-	-	0/0
458	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	-	-	-	0/0
459	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	-	-	-	0/0
460	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 416.86	385.60	500.42	03/2020 03/2020	03/2020	0(O) 0(R)	0/0
461	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	83.53	03/2012 -	03/2019	84(O) -	0/0
462	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
463	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	975.62	623.78	12/2021 -	12/2021	0(O) -	0/0
464	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	101.07	03/2021 -	03/2021	0(O) -	0/0
465	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	844.10	61.85	- 03/2022	03/2023	- 12(R)	0/0
466	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.12	858.96	549.56	03/2019 03/2019	03/2022	36(O) 36(R)	0/0
467	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	835.70	12/2021 -	12/2021	0(O) -	0/0
468	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	232.37	03/2021 03/2019	03/2020	-12(O) 12(R)	0/0
469	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	289.08	03/2019 -	12/2019	9(O) -	0/0
470	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
471	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
472	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
473	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 -	551.51	257.05	03/2019 -	03/2019	0(O) -	0/0
474	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 -	691.84	15.31	03/2020 -	03/2020	0(O) -	0/0
475	JIND-SONEPAT (NL) NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
476	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	12/2011 -	-	-	0/0
477	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	.00	- -	-	-	0/0
478	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	272.72	03/2019 -	03/2019	0(O) -	0/0
479	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	354.55	12/2026 -	12/2026	0(O) -	0/0
480	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	16,834.42	11/2002 03/2021	03/2021	220(O) 0(R)	0/0
481	MANDARHILL-DUMKA-RAMPURHAT (NL) ER - [220100168]ER,JHARKHAND ,	04/1995	1,125.89 -	1,125.89	2,007.32	03/2016 -	03/2020	48(O) -	0/0
482	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 -	3,020.94	.00	- -	03/2021	- -	0/0
483	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
484	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	525.81	495.14	12/2015 12/2018	12/2018	36(O) 0(R)	0/0
485	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	184.85	- 12/2018	12/2018	- 0(R)	0/0
486	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	152.45	12/2016 08/2018	12/2018	24(O) 4(R)	0/0
487	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 1,724.20	1,724.20	175.49	03/2021 03/2021	12/2021	9(O) 9(R)	0/0
488	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	100.63	03/2021 -	12/2020	-3(O) -	0/0
489	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.75	- 12/2024	12/2024	- 0(R)	0/0
490	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264(O) 0(R)	0/0
491	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,801.01	12.54	- 12/2023	12/2023	- 0(R)	0/0
492	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	913.65	- -	12/2023	- -	0/1
493	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 986.30	986.30	285.06	03/2016 12/2023	12/2023	93(O) 0(R)	0/1
494	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- 12/2023	12/2023	- 0(R)	0/0
495	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
496	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	- 12/2023	12/2023	- 0(R)	0/0
497	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	1,161.88	03/2023 -	03/2023	0(O) -	0/1
498	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	- 0(R)	0/0
499	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 2,841.84	2,841.84	27.34	12/2018 12/2024	12/2024	72(O) 0(R)	0/0
500	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	- 0(R)	0/0
501	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 279.54	279.54	8.66	03/2016 12/2023	12/2023	93(O) 0(R)	0/0
502	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 1,156.94	1,156.94	680.39	03/2020 03/2020	03/2021	12(O) 12(R)	0/5
503	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 578.00	578.00	448.98	03/2020 03/2020	03/2020	0(O) 0(R)	0/2
504	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	889.52	433.36	03/2017 -	03/2020	36(O) -	0/0
505	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 1,566.00	2,815.62	254.53	- -	-	-	0/0
506	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0
507	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 342.85	369.83	432.50	- -	-	-	0/0
508	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.70	- -	-	-	0/0
509	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	23.84	- -	-	-	0/0
510	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.08	- -	-	-	0/0
511	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
512	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA ,	02/2005	241.00 -	241.00	294.63	03/2014 -	-	-	0/0
513	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021	0(O) -	0/0
514	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	-	-	0/0
515	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 2,473.40	1,030.29	1,081.52	03/2022 03/2019	03/2022	0(O) 36(R)	0/0
516	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,763.93	.00	03/2020 -	10/2021	19(O) -	1/1
517	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	867.07	12/2020 -	12/2020	0(O) -	0/0
518	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022	0(O) -	0/1
519	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,260.61	.00	03/2022 -	03/2022	0(O) -	0/1
520	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	139.04	03/2019 -	08/2019	5(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
521	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019	0(O) -	0/0
522	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH ,	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96(O) -	0/0
523	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021	0(O) -	0/0
524	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 -	700.00	11.19	06/2020 -	06/2020	0(O) -	0/0
525	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.96	716.67	06/1999 -	-	-	0/0
526	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	1,329.00	03/2004 -	03/2020	192(O) -	0/0
527	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 2,271.50	3,712.50	1,870.67	03/2021 -	03/2021	0(O) -	0/0
528	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
529	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
530	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 3,168.29	3,168.29	979.05	03/2023 -	03/2023	0(O) -	0/0
531	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 792.89	792.89	272.78	03/2021 -	03/2021	0(O) -	0/0
532	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	298.70	240.89	03/2019 -	03/2019	0(O) -	0/0
533	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 540.02	540.02	156.10	03/2022 -	03/2022	0(O) -	0/0
534	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	.00	03/2024 -	03/2024	0(O) -	0/0
535	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
536	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
537	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 1,272.19	1,272.19	132.09	03/2022 -	03/2022	0(O) -	0/0
538	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 2,449.91	2,449.91	87.60	03/2023 -	03/2023	0(O) -	0/0
539	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.47	3,627.47	309.54	03/2024 -	03/2024	0(O) -	0/0
540	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	1.27	03/2023 -	03/2023	0(O) -	0/0
541	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 1,035.16	1,035.16	18.99	03/2022 -	03/2023	12(O) -	0/0
542	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 637.95	637.95	26.63	03/2023 -	03/2023	0(O) -	0/0
543	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,750.00	1,563.47	03/2020 -	03/2020	0(O) -	0/0
544	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.22	12/2025 -	03/2025	-9(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
545	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 -	2,686.63	.00	03/2023 -	03/2023	0(O) -	0/0
546	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	253.28	03/2019 -	03/2019	0(O) -	0/0
547	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	-	-	-	0/0
548	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	-	-	-	0/0
549	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	403.00	36.28	12/2021 -	12/2021	0(O) -	0/0
550	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2020	108(O) -	0/0
551	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	259.43	03/2021 -	03/2021	0(O) -	0/0
552	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 2,393.48	4,968.00	2,318.33	03/2014 12/2020	12/2020	81(O) 0(R)	0/0
553	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
554	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	-	-	-	0/0
555	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020	0(O) -	0/0
556	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
557	MUNEERABAD-MAHABOONAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	645.00	725.63	03/2000 03/2019	03/2019	228(O) 0(R)	0/0
558	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
559	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 -	1,126.79	751.05	-	-	-	1/1
560	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
561	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.87	-	-	-	0/6
562	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	03/2019	123(O) -	0/0
563	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	607.91	1,067.93	02/2013 -	06/2016	-	0/0
564	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	770.08	274.48	12/2022 -	05/2019	-43(O) -	0/0
565	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	97.92	12/2021 -	-	-	0/0
566	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	181.09	01/2019 -	02/2019	1(O) -	0/0
567	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	606.41	03/2022 03/2019	03/2022	0(O) 36(R)	0/0
568	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	603.75	03/2022 03/2019	03/2022	0(O) 36(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
569	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,878.97	183.63	-	-	-	0/1
570	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022	0(O) -	0/0
571	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	10.34	-	12/2022	-	0/0
572	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108(O) 0(R)	0/0
573	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	-	-	-	0/0
574	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	.00	03/2019 -	03/2019	0(O) -	0/0
575	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	-	-	-	0/0
576	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 346.15	457.08	317.14	-	-	-	0/0
577	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	64.09	03/2020 -	03/2020	0(O) -	0/0
578	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	-	-	-	0/0
579	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	123.11	03/2020 -	03/2020	0(O) -	0/0
580	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	-	03/2018	-	0/0
581	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	112.10	03/2019 -	03/2019	0(O) -	0/0
582	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	544.72	147.26	03/2006 -	-	-	0/0
583	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	288.85	9.31	-	-	-	0/0
584	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.84	-	-	-	0/0
585	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	915.96	319.21	03/2022 -	03/2022	0(O) -	0/0
586	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	273.54	-	-	-	0/0
587	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	360.58	-	-	-	0/0
588	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	792.27	335.88	03/2016 -	-	-	0/0
589	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	538.37	108.62	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
590	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	175.99	57.51	- -	-	-	0/0
591	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.52	137.85	03/2016 -	03/2020	48(O) -	0/0
592	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	118.48	03/2017 -	-	-	0/0
593	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	50.69	11/2018 -	11/2018	0(O) -	0/0
594	BARIARPIUR-MANANPUR VIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	19.82	- -	-	-	0/0
595	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.73	- -	-	-	0/0
596	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	542.18	303.58	03/2020 -	03/2020	0(O) -	0/0
597	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	139.80	- -	-	-	0/0
598	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.12	03/2017 -	-	-	0/0
599	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	492.68	32.00	03/2005 -	-	-	0/0
600	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKUPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	153.02	52.10	- -	-	-	0/0
601	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	355.44	72.84	- -	-	-	0/0
602	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	665.75	148.88	02/2012 -	-	-	0/0
603	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	258.73	113.51	03/2014 -	-	-	0/0
604	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
605	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	-	-	0/0
606	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 1,856.95	2,200.00	227.19	03/2023 03/2024	03/2024	12(O) 0(R)	0/0
607	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.46	- -	-	-	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
608	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	.00	- -	-	-	0/0
609	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
610	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- 12/2023	12/2023	- 0(R)	0/0
611	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 -	2,062.20	674.76	- -	03/2022	- -	0/2
612	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 704.31	704.31	119.69	03/2020 03/2020	03/2020	0(O) 0(R)	0/1
613	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	216.07	03/2014 03/2023	03/2023	108(O) 0(R)	0/1
614	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
615	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
616	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	.00	- -	-	-	0/0
617	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
618	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	199.46	- -	-	-	0/0
619	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	- 0(R)	0/0
620	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	3.51	03/2020 -	03/2020	0(O) -	0/0
621	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	190.63	- 03/2021	03/2021	- 0(R)	0/0
622	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	860.43	490.28	03/2020 03/2020	03/2020	0(O) 0(R)	0/0
623	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,614.59	1,614.59	696.73	03/2019 03/2021	03/2021	24(O) 0(R)	0/0
624	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 -	678.54	.00	03/2019 -	03/2020	12(O) -	0/38
625	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
626	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	368.22	03/2021 -	03/2021	0(O) -	0/0
627	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
628	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	899.56	12/2023 12/2023	12/2023	0(O) 0(R)	0/0
629	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
630	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023	0(O) -	0/0
631	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	845.58	.00	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
632	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 2,446.57	3,000.00	655.38	03/2015 10/2021	10/2021	79(O) 0(R)	0/0
633	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
634	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147(O) -	0/0
635	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,367.66	12/2017 -	06/2019	18(O) -	0/0
636	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 245.00	1,202.70	631.11	02/2015 -	12/2021	82(O) -	0/0
637	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	373.73	03/2009 03/2009	12/2018	117(O) 117(R)	1/1
638	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	574.98	06/2021 -	03/2023	21(O) -	0/0
639	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
640	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	765.60	02/2019 -	03/2021	25(O) -	0/0
641	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	81.26	10/2020 -	03/2021	5(O) -	0/0
642	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	180.78	03/2020 -	03/2020	0(O) -	0/0
643	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	189.40	03/2022 -	03/2022	0(O) -	0/0
644	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	81.06	03/2022 -	03/2022	0(O) -	0/0
645	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28(O) -	0/0
646	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27(O) -	0/0
647	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,151.81	375.59	03/2020 03/2020	06/2020	3(O) 3(R)	0/0
648	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024	36(O) 0(R)	0/0
649	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 2,335.67	2,335.67	300.05	12/2024 -	12/2024	0(O) -	0/0
650	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	970.00	975.36	03/2020 -	03/2020	0(O) -	0/0
651	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	887.88	03/2019 -	03/2021	24(O) -	0/0
652	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	.00	03/2020 -	03/2020	0(O) -	0/0
653	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
654	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	3.18	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
655	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	450.57	02/2019 -	02/2019	0(O) -	0/0
656	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,216.00	712.13	03/2015 -	03/2020	60(O) -	0/0
657	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	1,116.00	795.27	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
658	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	127.14	12/2019 -	06/2019	-6(O) -	0/0
659	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	162.66	10/2018 -	10/2018	-	0/0
660	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
661	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
662	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 295.02	420.18	81.44	03/2020 -	12/2019	-3(O) -	0/0
663	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	206.88	11/2019 -	11/2019	0(O) -	0/0
664	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	346.35	295.70	11/2018 -	12/2018	1(O) -	0/0
665	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	278.89	02/2019 -	03/2019	1(O) -	0/0
666	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,103.04	2.32	- -	-	-	0/0
667	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	410.89	03/2018 -	12/2019	21(O) -	0/0
668	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	.00	08/2022 -	08/2022	0(O) -	0/0
669	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
670	KARUR-SALEM(NL) SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0
671	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 495.74	734.01	445.91	06/2013 03/2019	03/2019	69(O) 0(R)	1/4
672	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019	0(O) -	0/0
673	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
674	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	61.97	- -	-	-	0/0
675	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	237.73	- -	-	-	0/0
676	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019	0(O) -	0/0
677	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
678	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	303.72	-	-	-	0/0
679	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	-	-	-	0/0
680	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	-	-	-	0/0
681	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	83.15	-	03/2020	-	0/0
682	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71(O) -	0/0
683	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU ,	02/1997	458.63 -	458.63	.92	03/2015 -	-	-	0/0
684	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU ,	02/2000	200.84 -	200.84	394.26	03/2014 -	-	-	0/0
685	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	302.02	304.07	03/2005 -	-	-	0/0
686	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	.00	03/2018 -	03/2018	-	0/0
687	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
688	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU ,	02/2005	600.00 600.00	645.54	671.00	03/2010 -	-	-	0/0
689	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,700.00	.00	03/2022 -	03/2022	0(O) -	0/0
690	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU ,	02/2003	199.55 -	330.32	2.12	03/2009 -	-	-	0/0
691	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	.00	03/2020 -	03/2020	0(O) -	0/0
692	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU ,	02/2006	208.00 -	208.00	3.58	03/2012 -	-	-	0/0
693	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 926.23	1,025.00	1,021.82	- 03/2017	03/2017	-	0/0
694	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.26	3.69	-	-	-	0/0
695	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.47	111.36	03/2010 03/2022	03/2022	144(O) 0(R)	0/1
696	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	595.33	03/2016 03/2017	12/2020	57(O) 45(R)	0/0
697	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 2,911.84	2,911.84	.92	-	-	-	0/1
698	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 -	616.08	.00	-	-	-	0/1
699	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
700	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	219.80	12/2024 -	12/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
701	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	.00	03/2022 -	03/2022	0(O) -	0/0
702	AGARTALA SABROOM NL NEFR - [N22000099]NFR,TRIPURA ,	04/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019	60(O) -9(R)	0/0
703	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 4,118.00	1,733.20	1,543.99	03/2007 -	04/2016	-	0/0
704	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	650.00	.00	03/2020 -	10/2022	31(O) -	2/3
705	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
706	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
707	UTRATIA-ZAFRABAD NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	369.90 -	1,581.53	618.19	03/2010 -	-	-	0/0
708	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
709	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	308.00	.00	- -	-	-	0/0
710	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	435.00	447.20	- -	03/2018	-	0/0
711	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	270.00	265.14	08/2018 -	08/2018	-	0/0
712	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
713	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
714	FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	.00	- -	-	-	0/0
715	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	380.00	4.12	- -	-	-	0/0
716	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
717	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	99.33	03/2022 -	02/2019	-37(O) -	0/0
718	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	668.00	.00	03/2020 -	03/2020	0(O) -	0/6
719	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	943.60	122.70	03/2022 -	12/2024	33(O) -	0/0
720	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	977.00	978.21	03/2019 -	03/2020	12(O) -	0/0
721	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	335.37	03/2023 -	12/2024	21(O) -	0/0
722	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	894.91	12/2020 -	03/2021	3(O) -	0/0
723	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	256.36	03/2020 -	03/2021	12(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
724	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	15.79	03/2019 -	12/2019	9(O) -	0/0
725	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH ,	04/1997	233.00 -	318.42	334.60	04/1999 -	-	-	0/0
726	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	.55	04/2016 -	01/2022	69(O) -	0/0
727	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
728	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH ,	04/1997	609.04 1,063.00	1,807.88	1,805.26	04/1999 -	12/2018	236(O) -	0/0
729	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
730	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,343.00	.00	01/2018 -	-	-	0/0
731	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	22.53	04/2017 -	10/2022	66(O) -	0/0
732	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
733	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	.00	-	-	-	0/0
734	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	.45	01/2022 -	01/2022	0(O) -	0/0
735	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	.60	03/2014 -	04/2021	85(O) -	0/0
736	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	.00	03/2023 -	03/2023	0(O) -	0/0
737	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	.00	03/2021 -	03/2021	0(O) -	0/0
738	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
739	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	-	-	-	0/0
740	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,081.06	12/2024 -	03/2026	15(O) -	0/0
741	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	267.93	03/2019 -	03/2020	12(O) -	0/0
742	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
743	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
744	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,620.01	843.85	03/2019 12/2009	03/2019	0(O) 111(R)	0/0
745	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,092.20	620.73	12/2010 -	-	-	7/7
746	TAMLUK DIGHA LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 -	749.69	.00	06/2005 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
747	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL ,	04/2010	2,397.72	2,397.72	197.20	03/2016	-	-	0/0
748	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42	2,733.86	40.13	03/2014	12/2025	141(O)	0/0
749	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98	4,259.48	1,866.83	03/2016	03/2025	108(O)	0/0
750	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51	2,913.50	768.02	03/2016	03/2025	108(O)	0/0
751	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL ,	04/2009	259.51	533.59	144.46	02/2012	-	-	0/0
752	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL ,	04/2009	193.08	612.45	150.70	12/2011	-	-	0/0
753	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58	4,874.58	1,881.65	03/2016	-	-	0/0
754	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37	620.00	40.77	-	03/2025	-	0/0
755	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL ,	04/2011	289.64	760.00	.13	-	-	-	0/0
756	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42	380.00	97.55	-	03/2020	-	0/0
757	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL ,	04/2012	283.55	451.00	457.51	03/2019	03/2019	0(O)	0/0
758	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78	268.52	.67	-	-	-	0/0
759	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64	272.20	88.25	-	-	-	0/0
760	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69	426.00	.00	-	03/2030	-	0/0
761	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27	612.00	18.38	12/2021	03/2020	-21(O)	0/0
762	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	1,013.45	1,428.00	484.48	12/2021	12/2021	0(O)	0/0
763	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40	2,373.00	484.85	03/2003	03/2030	324(O)	0/0
764	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]SER,WEST BENGAL ,	04/1998	1,027.40	2,373.00	481.65	03/2022	03/2022	0(O)	0/0
	Total		4,90,540.40	7,04,794.36	1,71,075.46				18/104

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
765	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/0
766	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	.00	12/2017 -	-	-	0/4
767	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	.00	04/2017 -	-	-	0/4
768	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	.00	10/2018 -	-	-	0/4
769	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	.00	10/2018 -	-	-	0/4
770	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000820]MORTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	.00	11/2019 -	11/2019	0(O) -	0/0
771	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
772	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,159.63	05/2013 -	-	-	0/0
773	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62(O) -	0/0
774	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,993.77	05/2014 -	-	-	0/0
775	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	.00	02/2015 -	-	-	0/4
776	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	-	-	0/1
777	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	.00	02/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
778	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 -	207.40	44.08	07/2014 -	-	-	0/1
779	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	-	-	0/1
780	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/1
781	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	.00	- -	-	-	0/1
782	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	.00	- -	-	-	0/4
783	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	.00	- -	-	-	0/0
784	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	.00	12/2015 -	-	-	0/2
785	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
786	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	-	-	0/4
787	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	.00	- -	-	-	0/0
788	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	05/2015 -	-	-	2/4
789	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDON - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	.00	09/2015 -	-	-	0/4
790	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	.00	10/2015 -	-	-	0/0
791	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	.00	12/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
792	REHABILITATION AND UPGRADE OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	.00	06/2014 -	-	-	0/2
793	FOUR LANNING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	.00	11/2015 -	-	-	0/0
794	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	04/2015 -	-	-	0/0
795	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018	0(O) -	0/0
796	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
797	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	03/2020	0(O) -	0/0
798	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2(O) -	0/0
799	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	.00	06/2017 -	-	-	0/0
800	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	.00	-	-	-	0/0
801	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	-	-	-	0/0
802	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	-	-	-	0/0
803	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	.00	-	-	-	0/0
804	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	1,532.62	.00	03/2021 -	03/2021	0(O) -	0/0
805	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	.00	-	-	-	0/0
806	REHABILITATION AND UPGRADE OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
807	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	.00	- -	-	-	0/0
808	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	.00	- -	-	-	0/0
809	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
810	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2011 -	-	-	0/0
811	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	.00	05/2012 -	-	-	0/0
812	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	-	-	1/4
813	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(0) -	1/4
814	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	-	-	1/4
815	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	.00	06/2018 -	-	-	0/3
816	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	.00	- -	-	-	0/0
817	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	.00	09/2010 -	-	-	0/0
818	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	.00	09/2010 -	-	-	0/0
819	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
820	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450 - [N24000614] NHIDCL, ARUNACHAL PRADESH ,	01/2016	183.65	183.65	.00	11/2016	-	-	0/0
821	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615] NHIDCL, ARUNACHAL PRADESH ,	01/2016	334.22	334.22	.00	06/2016	-	-	0/4
822	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616] NHIDCL, ARUNACHAL PRADESH ,	04/2016	245.79	245.79	.00	-	-	-	0/0
823	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617] NHIDCL, ARUNACHAL PRADESH ,	04/2016	198.00	198.00	.00	10/2016	-	-	0/4
824	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618] NHIDCL, ARUNACHAL PRADESH ,	11/2015	434.06	434.06	.00	-	-	-	0/0
825	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676] NHIDCL, ARUNACHAL PRADESH ,	12/2016	138.93	155.00	.00	01/2017	01/2020	36(O)	0/0
826	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677] NHIDCL, ARUNACHAL PRADESH ,	01/2017	1,253.10	1,253.10	.00	03/2017	-	-	0/0
827	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678] NHIDCL, ARUNACHAL PRADESH ,	03/2017	284.09	284.09	.00	04/2017	-	-	0/0
828	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679] NHIDCL, ARUNACHAL PRADESH ,	02/2017	195.23	195.23	.00	04/2017	-	-	0/0
829	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680] NHIDCL, ARUNACHAL PRADESH ,	02/2017	203.36	203.36	.00	04/2017	-	-	0/0
830	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681] NHIDCL, ARUNACHAL PRADESH ,	01/2017	194.66	194.66	.00	04/2017	-	-	0/0
831	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682] NHIDCL, ARUNACHAL PRADESH ,	02/2017	168.32	168.32	.00	04/2017	-	-	0/0
832	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683] NHIDCL, ARUNACHAL PRADESH ,	02/2017	180.57	180.57	.00	04/2017	-	-	0/0
833	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684] NHIDCL, ARUNACHAL PRADESH ,	02/2017	216.71	216.71	.00	04/2017	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
834	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	.00	04/2017 -	-	-	0/0
835	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	.00	04/2017 -	-	-	0/0
836	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	-	-	-	0/0
837	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	410.32	02/2009 -	-	-	0/0
838	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	209.80	04/2009 -	-	-	0/0
839	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	-	0/0
840	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
841	MAIBANG TO LUMDING (AS-27) KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	-	0/0
842	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 174.34	174.34	214.88	03/2008 -	12/2018	129(O)	0/0
843	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130(O)	0/0
844	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	297.81	04/2008 -	03/2019	131(O)	0/0
845	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	198.82	05/2008 -	02/2019	129(O)	0/0
846	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
847	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	389.08	04/2010 -	04/2019	108(O)	0/0
848	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	-	-	0/4
849	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	-	-	0/4
850	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	-	-	0/4
851	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O)	0/4
852	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O)	0/4
853	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O)	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
854	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	.00	05/2017 -	-	-	0/0
855	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	.00	02/2011 -	-	-	0/0
856	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	.00	02/2018 -	-	-	0/0
857	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	.00	02/2018 -	-	-	0/0
858	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	.00	12/2018 -	12/2018	0(O) -	0/4
859	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	.00	06/2018 -	-	-	0/0
860	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	.00	- -	-	-	0/0
861	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	.00	12/2018 -	12/2018	0(O) -	0/0
862	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	.00	01/2016 -	-	-	0/4
863	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4
864	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	.00	01/2016 -	-	-	0/0
865	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	884.12	02/2013 -	12/2018	70(O) -	0/0
866	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	-	-	0/0
867	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.62	03/2014 -	09/2018	-	0/0
868	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
869	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	831.33	07/2013 -	06/2019	71(O) -	0/0
870	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	564.35	11/2013 -	12/2018	61(O) -	0/0
871	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
872	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	-	-	0/0
873	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	-	-	0/0
874	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
875	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	159.02	04/2019 -	04/2019	0(O) -	0/0
876	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	229.41	- -	01/2020	- -	0/0
877	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	57.86	04/2018 -	04/2020	24(O) -	0/0
878	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	.00	- -	10/2020	- -	0/0
879	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	28.96	- -	12/2019	- -	0/0
880	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	142.41	04/2019 -	10/2019	6(O) -	0/0
881	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
882	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	545.46	- -	03/2019	- -	0/0
883	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	400.35	04/2018 -	12/2018	8(O) -	0/0
884	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
885	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	.00	- -	-	-	0/0
886	REHABILITATION AND UPGRADING TO 2 LANES WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	.00	03/2014 -	-	-	0/0
887	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
888	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	.00	08/2014 -	-	-	0/0
889	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	.00	07/2016 -	-	-	0/0
890	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
891	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	.00	05/2016 -	-	-	0/0
892	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
893	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	.00	05/2016 -	-	-	0/0
894	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	.00	10/2016 -	-	-	0/0
895	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	.00	07/2016 -	-	-	0/0
896	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	.00	11/2015 -	-	-	0/0
897	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25(O) -	0/0
898	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	.00	12/2016 -	-	-	0/0
899	TWO-LANING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
900	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	03/2020	0(O) -	0/0
901	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	.00	08/2017 -	-	-	0/0
902	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	-	-	-	0/0
903	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	-	-	-	0/0
904	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	-	-	-	0/0
905	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	-	-	-	0/0
906	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	.00	03/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
907	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	.00	03/2015 -	-	-	0/0
908	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	.00	03/2015 -	-	-	0/0
909	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	.00	- -	-	-	0/0
910	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	.00	12/2012 -	-	-	0/0
911	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	.00	- -	-	-	0/0
912	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	.00	12/2015 -	-	-	0/0
913	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
914	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	25.84	05/2018 -	06/2019	13(O) -	0/0
915	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	7.21	04/2018 -	-	-	0/0
916	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	50.67	04/2018 -	06/2019	14(O) -	0/0
917	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,029.96	.00	- -	-	-	0/0
918	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) ,NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	07/2018	-	0/0
919	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	04/2018 -	-	-	0/1
920	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
921	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
922	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
923	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
924	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	.00	- -	-	-	0/0
925	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	.00	- -	-	-	0/0
926	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	3,176.22	09/2012 -	08/2018	-	2/3
927	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	975.23	07/2013 -	12/2018	65(O) -	0/0
928	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3
929	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	346.60	08/2016 -	-	-	0/0
930	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	199.22	- -	08/2019	- -	0/0
931	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	137.94	- -	10/2019	- -	0/0
932	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	216.34	- -	09/2019	- -	0/0
933	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	133.37	- -	08/2019	- -	0/0
934	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	03/2019	- -	0/0
935	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	364.56	76.83	- -	12/2019	- -	0/0
936	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	60.20	- -	01/2020	- -	0/0
937	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	35.80	- -	09/2019	- -	0/0
938	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	.00	- -	-	-	0/0
939	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	211.17	06/2020 -	08/2020	2(O) -	0/0
940	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
941	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,052.21	.00	- -	-	-	0/0
942	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
943	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	.00	- -	-	-	0/0
944	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
945	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	-	0/0
946	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,871.89	11/2011 -	06/2019	91(O) -	0/0
947	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	-	-	0/0
948	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
949	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 -	602.95	54.89	06/2016 -	12/2018	30(O) -	0/0
950	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 -	574.28	73.66	07/2018 -	03/2019	8(O) -	0/0
951	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	218.51	04/2019 -	04/2019	0(O) -	0/0
952	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
953	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	17.07	05/2019 -	08/2019	3(O) -	0/0
954	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	05/2019	0(O) -	0/0
955	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA ,	03/2017	639.79 -	552.90	41.21	03/2020 -	06/2019	-9(O) -	0/0
956	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA ,	03/2018	1,484.30 -	1,484.30	.00	- -	-	-	0/0
957	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA ,	03/2018	275.12 -	275.12	.00	- -	-	-	0/0
958	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI, HARYANA ,	03/2018	307.79 -	307.79	.00	- -	-	-	0/0
959	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA ,	03/2018	634.70 -	634.70	.00	- -	-	-	0/0
960	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I - [N24000841]NHAI, HARYANA ,	03/2018	795.50 -	795.50	.00	- -	-	-	0/0
961	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA ,	03/2018	198.05 -	198.05	.00	- -	-	-	0/0
962	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA ,	03/2018	181.78 -	181.78	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
963	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	.00	- -	-	-	0/0
964	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29(O) -	0/0
965	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	104.98	03/2018 -	03/2019	12(O) -	0/0
966	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	32.98	02/2019 -	02/2019	0(O) -	0/0
967	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	09/2020	- -	0/0
968	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	- -	0/0
969	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	37.26	- -	11/2019	- -	0/0
970	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	.00	06/2020 -	06/2020	0(O) -	0/0
971	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	.00	- -	-	-	0/0
972	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,615.69	07/2015 -	03/2019	44(O) -	0/0
973	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
974	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
975	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,246.47	06/2014 -	-	-	0/0
976	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	.00	06/2019 -	12/2020	18(O) -	0/0
977	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	65.48	12/2018 -	10/2019	10(O) -	0/0
978	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	.00	- -	-	-	0/0
979	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
980	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	328.14	03/2019 -	03/2019	0(O) -	0/0
981	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
982	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	37.20	08/2018 -	08/2018	-	0/0
983	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	10.57	03/2020 -	06/2019	-9(O) -	0/0
984	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	21.98	03/2020 -	03/2020	0(O) -	0/0
985	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	-	-	-	0/0
986	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	-	-	-	0/0
987	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	-	-	-	0/0
988	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9(O) -	3/3
989	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
990	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
991	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	351.24	09/2017 -	12/2018	15(O) -	0/0
992	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
993	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31(O) -	0/0
994	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	846.58	08/2018 -	04/2019	8(O) -	0/0
995	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	22.02	03/2019 -	07/2019	4(O) -	0/0
996	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	9.12	03/2019 -	11/2020	20(O) -	0/0
997	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	-	-	-	0/0
998	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	270.31	04/2020 -	04/2020	0(O) -	0/0
999	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	191.05	03/2019 -	03/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1000	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	388.34	08/2019 -	08/2019	0(O) -	0/0
1001	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	121.00	03/2020 -	06/2020	3(O) -	0/0
1002	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	325.34	03/2020 -	06/2020	3(O) -	0/0
1003	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	.00	- -	-	-	0/0
1004	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	1,995.34	.00	- -	-	-	0/0
1005	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,177.80	.00	- -	-	-	0/0
1006	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2019	79(O) -	0/0
1007	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	231.56	09/2017 -	11/2018	14(O) -	0/0
1008	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	201.35	11/2017 -	-	-	0/0
1009	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	108.06	- -	04/2019	-	0/0
1010	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	21.80	06/2018 -	04/2019	10(O) -	0/0
1011	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	.00	09/2017 -	06/2020	33(O) -	0/0
1012	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,424.77	.00	- -	-	-	0/0
1013	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67(O) -	0/0
1014	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
1015	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	-	-	0/0
1016	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1017	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1018	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	.00	05/2015 -	-	-	0/0
1019	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	-	-	0/0
1020	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	.00	05/2017 -	-	-	0/0
1021	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	-	-	0/0
1022	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1023	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	-	-	0/0
1024	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	-	-	0/0
1025	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	-	-	0/0
1026	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	-	-	0/0
1027	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	131.52	- -	12/2018	-	0/0
1028	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	117.99	- -	12/2018	-	0/0
1029	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	-	-	0/0
1030	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	-	-	0/0
1031	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	-	-	0/0
1032	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	195.21	- -	12/2018	-	0/0
1033	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	12/2018	37(O) -	0/0
1034	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36(O) -	0/0
1035	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	111.65	- -	12/2018	-	0/0
1036	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	496.70	01/2019 -	01/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1037	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	-	-	0/0
1038	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	15.03	01/2019 -	01/2019	0(O) -	0/0
1039	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	23.98	10/2017 -	01/2020	27(O) -	0/0
1040	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1041	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0
1042	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	-	-	-	0/0
1043	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	-	-	-	0/0
1044	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	-	-	-	0/0
1045	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,058.04	03/2013 -	06/2019	75(O) -	0/0
1046	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	396.59	06/2014 -	06/2019	60(O) -	0/0
1047	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019	64(O) -	2/2
1048	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	-	-	0/2
1049	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	-	-	-	0/4
1050	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	-	-	0/12
1051	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	-	-	-	0/4
1052	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1053	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	.00	- -	-	-	0/0
1054	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	65.16	- -	-	-	0/0
1055	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	205.97	- -	-	-	0/0
1056	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
1057	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	05/2019	0(O) -	0/0
1058	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	210.66	05/2018 -	03/2019	10(O) -	0/0
1059	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12(O) -	0/0
1060	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,622.44	05/2019 -	05/2019	0(O) -	0/0
1061	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	45.11	05/2018 -	04/2019	11(O) -	0/0
1062	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	80.89	03/2019 -	03/2019	0(O) -	0/0
1063	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	194.09	05/2018 -	04/2019	11(O) -	0/0
1064	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,302.51	07/2017 -	12/2018	17(O) -	0/0
1065	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	473.93	11/2016 -	06/2019	31(O) -	0/0
1066	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1067	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,304.41	01/2018 -	12/2018	11(O) -	0/0
1068	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018	78(O) -	0/0
1069	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	-	-	0/0
1070	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	.00	07/2018 -	07/2018	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1071	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	87.19	07/2019 -	07/2019	0(O) -	0/0
1072	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	237.07	07/2019 -	07/2019	0(O) -	0/0
1073	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	.00	07/2018 -	-	-	0/0
1074	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	.00	-	-	-	0/0
1075	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	-	-	-	0/0
1076	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	-	-	-	0/0
1077	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	-	-	-	0/0
1078	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	38.57	03/2019 -	03/2019	0(O) -	0/0
1079	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	2.42	03/2019 -	11/2019	8(O) -	0/0
1080	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	57.93	-	05/2019	-	0/0
1081	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	77.00	05/2019 -	05/2019	0(O) -	0/0
1082	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	155.12	02/2020 -	05/2020	3(O) -	0/0
1083	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	03/2020	0(O) -	0/0
1084	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1085	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	303.24	03/2020 -	05/2020	2(O) -	0/0
1086	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	289.99	03/2020 -	08/2020	5(O) -	0/0
1087	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	86.58	03/2017 -	11/2020	44(O) -	0/0
1088	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	86.95	03/2020 -	05/2019	-10(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1089	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	177.05	03/2020 -	08/2020	5(O) -	0/0
1090	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	.00	- -	-	-	0/0
1091	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	.00	- -	-	-	0/0
1092	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	.00	- -	-	-	0/0
1093	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	.00	- -	-	-	0/0
1094	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	.00	- -	-	-	0/0
1095	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	.00	- -	-	-	0/0
1096	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	642.13	.00	- -	-	-	0/0
1097	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	678.87	01/2014 -	01/2019	60(O) -	0/0
1098	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	.00	02/2011 -	-	-	0/0
1099	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	14.31	05/2018 -	03/2019	10(O) -	0/0
1100	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	159.00	- -	-	-	0/0
1101	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	.00	03/2011 -	-	-	0/0
1102	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	.00	10/2010 -	-	-	0/0
1103	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	-	-	0/0
1104	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128(O) -	0/0
1105	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	-	-	2/2

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1106	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,489.54	08/2014 -	-	-	0/0
1107	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,141.90	03/2014 -	12/2019	69(O) -	0/0
1108	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81(O) -	0/0
1109	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	2,335.94	04/2015 -	-	-	0/0
1110	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	-	-	-	0/0
1111	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1112	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	85.00	-	02/2020	-	0/0
1113	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,294.47	.00	-	-	-	0/0
1114	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	998.70	.00	-	-	-	0/0
1115	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1116	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	.00	08/2016 -	08/2019	36(O) -	0/0
1117	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	.00	08/2016 -	08/2019	36(O) -	0/0
1118	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	.00	08/2016 -	08/2019	36(O) -	0/0
1119	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	.00	04/2017 -	-	-	0/0
1120	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	.00	09/2018 -	-	-	0/0
1121	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0
1122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	-	-	0/0
1124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/0
1125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	.00	09/2018 -	-	-	0/0
1126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	.00	09/2018 -	-	-	0/0
1127	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	.00	09/2018 -	-	-	0/0
1128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	.00	09/2018 -	-	-	0/0
1129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	.00	09/2018 -	-	-	0/0
1130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	.00	09/2018 -	-	-	0/0
1131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	0/0
1132	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1133	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1134	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	10/2015	-	0/0
1135	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	-	-	0/0
1136	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1137	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	.00	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1138	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1139	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	.00	01/2017 -	-	-	0/0
1140	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	-	-	-	0/0
1141	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	-	0/0
1142	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	.00	11/2017 -	-	-	0/0
1143	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	.00	08/2015 -	-	-	0/0
1144	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	-	-	-	0/0
1145	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0(0)	0/0
1146	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	.00	-	-	-	0/0
1147	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	.00	05/2016 -	-	-	0/0
1148	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	.00	04/2018 -	-	-	0/0
1149	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	.00	10/2017 -	-	-	0/0
1150	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	.00	10/2017 -	-	-	0/0
1151	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	.00	05/2016 -	-	-	0/0
1152	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	.00	01/2017 -	-	-	0/0
1153	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	.00	06/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1154	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	.00	06/2018 -	11/2018	5(O) -	0/0
1155	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	.00	05/2016 -	-	-	0/0
1156	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	.00	03/2020 -	03/2020	0(O) -	0/0
1157	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	11/2020	40(O) -	0/0
1158	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	.00	- -	-	-	0/0
1159	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1160	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	-	-	0/0
1161	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	-	-	0/0
1162	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1163	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	-	-	0/0
1164	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	-	-	0/0
1165	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	.00	- -	-	-	0/0
1166	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1167	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1168	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	-	-	0/0
1169	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	.00	- -	-	-	0/0
1170	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1171	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1172	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1173	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1174	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	170.68	01/2016 -	-	-	0/0
1175	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1176	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1177	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1178	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1179	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1180	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1181	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1182	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1183	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1184	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	28.90	- -	04/2019	-	0/0
1185	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	392.14	- -	03/2019	-	0/0
1186	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	31.96	12/2017 -	04/2019	16(O) -	0/0
1187	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1188	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1189	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	206.87	09/2019 -	09/2019	0(O) -	0/0
1190	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	481.60	- -	04/2020	- -	0/0
1191	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	.00	03/2020 -	04/2020	1(O) -	0/0
1192	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	261.76	.00	- -	-	-	0/0
1193	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	.00	- -	-	-	0/0
1194	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	21.93	- -	01/2020	- -	0/0
1195	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1196	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1197	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1198	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1199	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51(O) -	0/0
1200	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	.00	06/2018 -	-	-	0/0
1201	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30(O) -	0/0
1202	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	53.70	03/2018 -	12/2018	9(O) -	0/0
1203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	206.78	05/2016 -	-	-	0/0
1205	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	604.80	10/2017 -	12/2018	14(O) -	0/0
1206	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27(O) -	0/0
1207	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	688.00	04/2018 -	03/2019	11(O) -	0/0
1208	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1209	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1210	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	12/2018	86(O) 15(R)	0/0
1211	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	242.51	- -	12/2018	- -	0/0
1212	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3(O) -	0/0
1213	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	167.09	06/2019 -	11/2019	5(O) -	0/0
1214	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1215	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	470.78	- -	11/2019	- -	0/0
1216	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	247.91	10/2018 -	11/2018	1(O) -	0/0
1217	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	193.54	01/2019 -	01/2019	0(O) -	0/0
1218	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	475.69	- -	05/2020	- -	0/0
1219	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	610.00	- -	12/2019	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1220	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1221	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	15.00	04/2020 -	11/2019	-5(O) -	0/0
1222	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	.00	10/2017 -	-	-	0/0
1223	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	-	-	0/0
1224	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	.00	- -	-	-	0/0
1225	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1226	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	.00	- -	-	-	0/0
1227	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	.00	- -	-	-	0/0
1228	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	.00	- -	-	-	0/0
1229	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	.00	08/2013 -	-	-	0/0
1230	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	.00	08/2013 -	-	-	0/0
1231	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1232	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	.00	10/2017 -	-	-	0/0
1233	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	7.50	11/2017 -	-	-	0/0
1234	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	.00	- -	-	-	0/0
1235	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	18.12	11/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1236	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/0
1237	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018	60(O) -	0/0
1238	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	325.55	06/2013 -	-	-	0/0
1239	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67(O) -	0/0
1240	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64(O) -	0/0
1241	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2019	68(O) -	0/0
1242	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1243	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1244	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1245	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	895.57	11/2017 -	05/2019	18(O) -	0/0
1246	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18(O) -	0/0
1247	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1248	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	-	-	0/0
1249	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	627.37	07/2008 -	-	-	0/0
1250	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	180.17	08/2018 -	06/2019	10(O) -	0/0
1251	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	204.31	07/2018 -	-	-	0/0
1252	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	5.00	03/2020 -	03/2020	0(O) -	0/0
1253	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1254	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	-	-	0/0
1255	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	.00	09/2017 -	-	-	0/0
1256	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	-	-	0/0
1257	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	.00	-	-	-	0/0
1258	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	-	-	-	0/0
1259	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	.00	-	-	-	0/0
1260	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	.00	-	-	-	0/0
1261	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	633.55	.00	-	-	-	0/0
1262	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,016.92	.00	-	-	-	0/0
1263	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,065.96	.00	-	-	-	0/0
1264	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,410.94	09/2016 -	06/2019	33(O) -	0/0
1265	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1266	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1267	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1268	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	.00	03/2016 -	-	-	0/2
1269	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1270	REHABILITATION AND UPGRADE OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	.00	12/2016 -	-	-	0/4
1271	REHABILITATION AND UPGRADE OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1272	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1273	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1274	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	502.66	11/2018 -	07/2019	8(O) -	0/0
1275	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1276	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	.00	- -	-	-	0/0
1277	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	.00	- -	-	-	0/0
1278	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	.00	- -	-	-	0/0
1279	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1280	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	246.46	03/2018 -	-	-	3/4
1281	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	-	-	0/4
1282	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	-	-	0/0
1283	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	09/2018	-	0/0
1284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	430.61	01/2014 -	09/2018	-	0/0
1285	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1286	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1287	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	.00	03/2016 -	-	-	0/0
1288	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	.00	10/2016 -	-	-	0/0
1289	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1290	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	425.99	01/2016 -	-	-	0/0
1291	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	232.93	09/2016 -	-	-	0/0
1292	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	191.48	01/2016 -	-	-	0/0
1293	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	603.13	01/2016 -	-	-	0/0
1294	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	.00	03/2017 -	-	-	0/0
1295	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1296	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	.00	10/2016 -	-	-	0/0
1297	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	.00	03/2018 -	-	-	0/0
1298	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	-	-	0/0
1299	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	.00	10/2016 -	-	-	0/0
1300	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	.00	03/2017 -	-	-	0/0
1301	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.63	03/2018 -	-	-	0/0
1302	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	1,945.00	01/2019 -	01/2019	0(0) -	0/0
1303	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	681.34	06/2016 -	-	-	0/0
1304	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	328.63	06/2018 -	-	-	0/0
1305	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	433.51	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1306	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	372.80	07/2018 -	-	-	0/0
1307	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	439.40	06/2018 -	-	-	0/0
1308	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	.00	08/2015 -	-	-	0/0
1309	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1310	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1311	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	531.60	- -	-	-	0/0
1312	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	842.34	05/2019 -	05/2019	0(O) -	0/0
1313	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	784.53	06/2019 -	06/2019	0(O) -	0/0
1314	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	409.11	04/2019 -	04/2019	0(O) -	0/0
1315	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	193.08	- -	-	-	0/0
1316	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	135.54	- -	-	-	0/0
1317	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	145.81	04/2019 -	04/2019	0(O) -	0/0
1318	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	351.90	04/2019 -	04/2019	0(O) -	0/0
1319	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	297.13	- -	02/2020	- -	0/0
1320	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	.00	- -	07/2020	- -	0/0
1321	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	50.71	- -	04/2020	- -	0/0
1322	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,580.02	04/2019 -	11/2019	7(O) -	0/0
1323	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	211.60	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1324	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	314.70	- -	-	-	0/0
1325	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	.00	03/2020 -	11/2020	8(O) -	0/0
1326	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	.00	03/2020 -	08/2020	5(O) -	0/0
1327	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2(O) -	0/0
1328	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	886.98	03/2020 -	03/2020	0(O) -	0/0
1329	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	637.48	- -	05/2020	-	0/0
1330	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1331	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1332	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1333	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1334	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1335	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1336	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	-	-	0/0
1337	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1338	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1339	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	1,025.80	.00	- -	-	-	0/0
1340	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	1,115.28	.00	- -	-	-	0/0
1341	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	.00	- -	-	-	0/0
1342	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69(O) -	0/0
1343	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	181.70	- -	10/2019	- -	0/0
1344	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	122.72	- -	02/2020	- -	0/0
1345	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018	-	0/0
1346	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	.00	05/2018 -	-	-	0/4
1347	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	.00	06/2018 -	-	-	0/4
1348	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	.00	05/2018 -	-	-	0/4
1349	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	.00	12/2019 -	12/2019	0(O) -	0/0
1350	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019	0(O) -	0/0
1351	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019	0(O) -	0/0
1352	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	45.92	06/2019 -	06/2019	0(O) -	0/0
1353	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1354	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019	0(O) -	0/0
1355	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019	0(O) -	0/0
1356	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	74.52	02/2020 -	02/2020	0(O) -	0/0
1357	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	.14	- -	-	-	0/0
1358	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1359	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.74	- -	-	-	0/0
1360	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,310.60	08/2013 -	-	-	0/0
1361	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,822.70	08/2013 -	-	-	0/0
1362	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	-	-	0/0
1363	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	441.57	07/2014 -	-	-	0/0
1364	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1365	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	.00	- -	12/2019	-	0/0
1366	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	105.70	06/2018 -	05/2019	11(O) -	0/0
1367	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,836.44	- -	-	-	0/0
1368	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	6.39	11/2018 -	11/2018	0(O) -	0/0
1369	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	123.31	08/2018 -	08/2018	-	0/0
1370	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	.00	06/2018 -	-	-	0/0
1371	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		4,11,883.30	4,26,107.82	1,41,033.89				26/210
	<u>SHIPPING AND PORTS</u>								
1372	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39	669.46	411.12	12/2010	12/2018	96(O)	0/0
1373	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40	2,427.40	831.21	10/2008	-	-	0/0
1374	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00	600.00	139.80	03/2006	-	-	0/0
1375	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50	275.98	275.98	12/2017	-	-	1/1
1376	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU ,	03/2016	600.00	257.90	1.45	12/2017	05/2020	29(O)	0/0
	Total		3,788.29	4,230.74	1,659.56				1/1
	<u>TELECOMMUNICATIONS</u>								
1377	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26	418.26	172.30	06/2017	-	-	0/0
1378	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	159.30	159.30	60.27	04/2018	12/2018	8(O)	0/0
1379	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	167.68	167.68	32.44	04/2018	12/2018	8(O)	0/0
1380	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30	214.10	33.46	05/2018	12/2018	7(O)	0/0
1381	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80	231.80	77.65	10/2018	12/2018	2(O)	0/0
1382	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00	24,664.00	8,397.00	07/2015	05/2020	58(O)	0/0
1383	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17	2,011.17	253.90	09/2014	-	-	0/70
	Total		16,637.51	27,866.31	9,027.02				0/70
	<u>URBAN DEVELOPMENT</u>								
1384	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00	232.00	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1385	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	134.62	03/2017 -	-	-	4/5
1386	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1387	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	.02	03/2019 -	03/2019	0(O) -	0/7
1388	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1389	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	34.09	06/2017 07/2017	06/2020	36(O) 35(R)	0/0
1390	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	-	-	0/0
1391	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	331.12	10/2019 -	03/2020	5(O) -	0/7
1392	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	647.07	12/2015 -	-	-	0/0
1393	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,581.53	11/2019 -	11/2019	0(O) -	3/7
1394	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	10.14	04/2019 06/2020	06/2020	14(O) 0(R)	0/2
1395	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1396	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	3.36	05/2020 -	05/2020	0(O) -	0/0
1397	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	85.71	06/2019 -	06/2019	0(O) -	0/0
1398	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	.00	- -	-	-	0/0
1399	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	.00	- -	-	-	0/0
1400	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	1.21	04/2018 -	-	-	0/0
1401	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	4.44	11/2019 -	11/2019	0(O) -	0/0
1402	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1403	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	163.97	11/2014 -	02/2019	51(O) -	2/8
1404	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1405	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1406	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
1407	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1408	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	41.28	03/2016 -	04/2020	49(O) -	1/6
1409	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1410	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1411	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1412	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	29.78	02/2020 09/2020	09/2020	7(O) 0(R)	0/0
1413	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77(O) -	1/6
1414	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,181.79	.00	07/2017 -	12/2019	29(O) -	0/0
1415	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020	0(O) -3(R)	2/7
1416	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 8,680.00	8,680.00	4,631.87	03/2018 12/2019	12/2019	21(O) 0(R)	0/0
1417	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1418	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	4.00	07/2020 09/2018	09/2020	2(O) 24(R)	0/14
1419	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	1,881.14	11/2021 -	11/2021	0(O) -	0/0
1420	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2019	56(O) -	0/10
1421	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0
1422	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	391.23	05/2017 08/2018	03/2019	22(O) 7(R)	8/12

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1423	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	127.86	04/2019 06/2019	09/2019	5(O) 3(R)	4/8
1424	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	25.49	09/2018 -	09/2018	-	0/5
1425	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1426	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	540.42	197.12	07/2019 -	10/2019	3(O) -	0/0
1427	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	342.00	321.13	09/2016 -	-	-	0/0
1428	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-	-	12/24
1429	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	52.00	10/2019 -	10/2019	0(O) -	0/6
1430	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/0
1431	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	.00	- -	-	-	0/0
1432	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	9.96	03/2020 -	03/2020	0(O) -	0/5
1433	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1434	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1435	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1436	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1437	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	.00	03/2020 -	03/2020	0(O) -	0/0
1438	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1439	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1440	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	146.31	08/2016 -	03/2019	31(O) -	8/16

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(November 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1441	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	89.94	04/2018 -	07/2019	15(O) -	3/6
	Total		1,60,566.07 -	1,66,153.31	72,017.41				48/161
	<u>DEFENCE PRODUCTION</u>								
1442	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA ,	12/2016	167.69 168.00	170.37	86.93	05/2018 01/2019	01/2019	8(O) 0(R)	6/10
1443	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA ,	12/2016	285.95 286.00	291.29	51.87	08/2020 -	08/2020	0(O) -	5/8
	Total		453.64 -	461.66	138.80				11/18
	Grand Total		18,30,362.48	21,51,136.69	7,97,496.44				2242/4554


Summary of projects in the Flash Report for the month of November, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1452
Number of Projects completed/dropped/frozen in Current Month	12
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	4
Number of Projects in Current Month	1443

Brief Analysis

Project Status with respect to Original Schedule: Out of 1443 projects, 23 projects are ahead of schedule, 350 projects are on schedule 360 projects are delayed. 643 projects do not have fixed dates of commissioning. 67 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

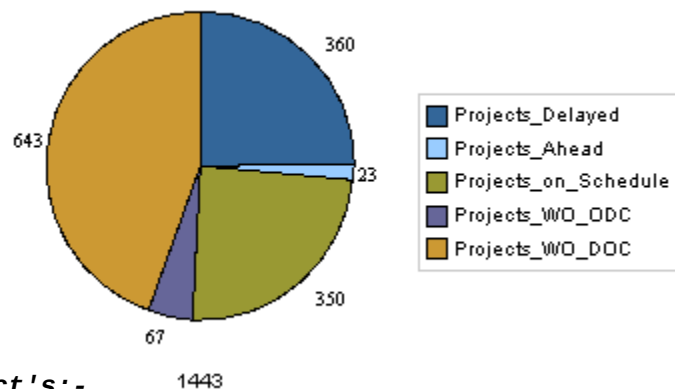


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1443 projects when sanctioned, was of the order of Rs. 1830362.48 crore but this was subsequently revised to Rs. 2151136.69 crore implying a cost overrun of 17.5%. The expenditure incurred on these projects till November, 2018 is Rs. 797496.44 crore, which is 37.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

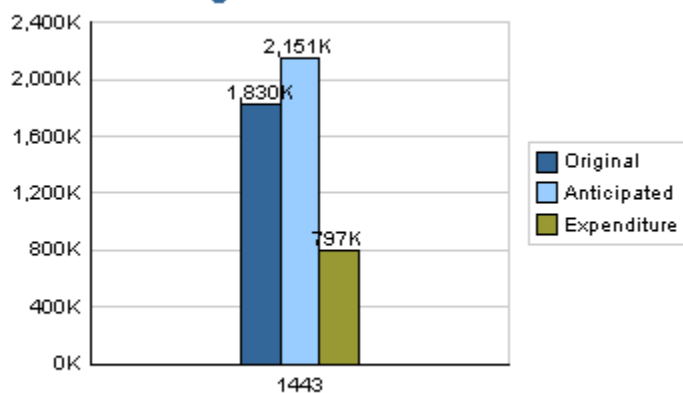

Sector wise current status of projects on the Flash Report

ATOMIC ENERGY


Current Status:

Number of Projects 4

Number of Projects Delayed 4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 74849 crore implying a cost overrun of 11.5%. The expenditure incurred on these projects till November, 2018 is Rs. 38963.52 crore, which is 52.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

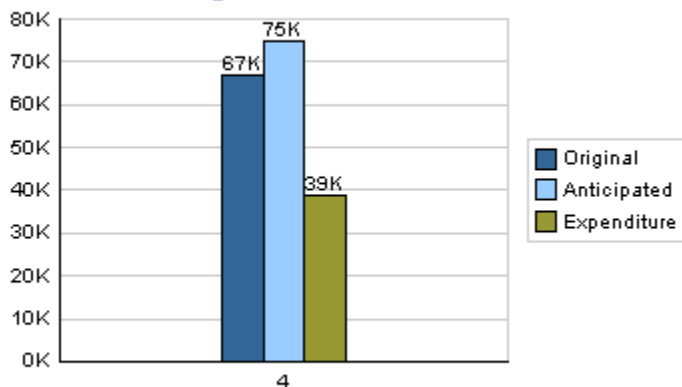

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

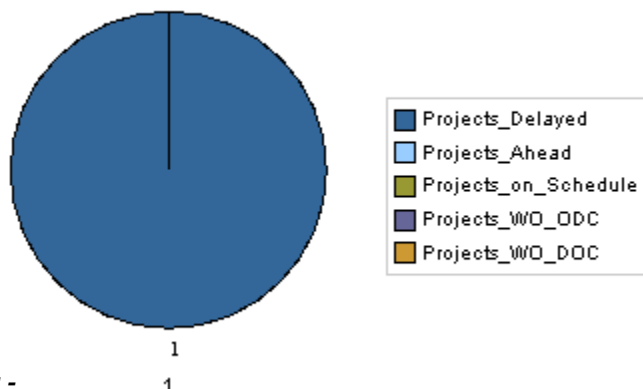


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 314.61 crore but this was subsequently anticipated to Rs. 441.33 crore implying a cost overrun of 40.3%. The expenditure incurred on these projects till November, 2018 is Rs. 85.79 crore, which is 19.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

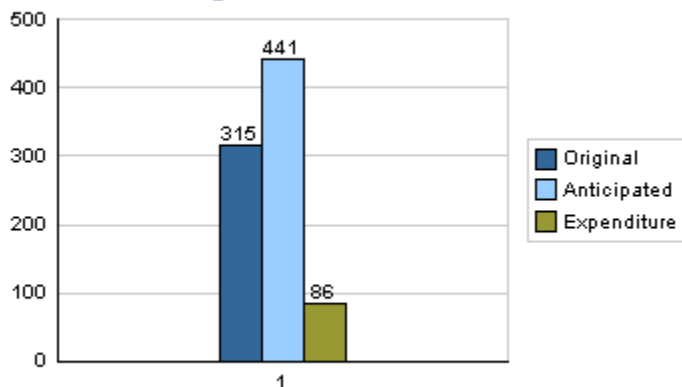

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	96
Number of Projects On Schedule	49
Number of Projects Delayed	35
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 96 projects, 1 project is ahead of schedule, 49 projects are on schedule 35 projects are delayed. 11 projects do not have fixed dates of commissioning.

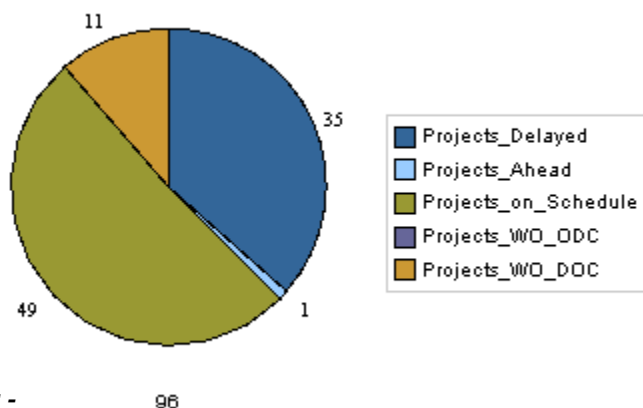


Total No Of Project's:-

96

Investment Scenario

Total original cost of implementation of 96 projects when sanctioned, was of the order of Rs. 94283.98 crore but this was subsequently anticipated to Rs. 93710.95 cr The expenditure incurred on these projects till November, 2018 is Rs. 28239.72 crore, which is 30.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

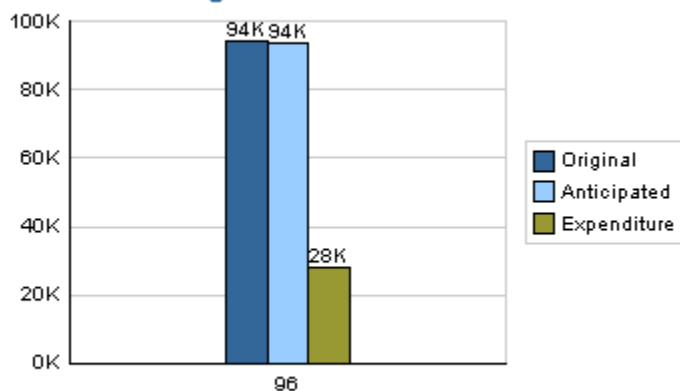

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule 2 projects are delayed.

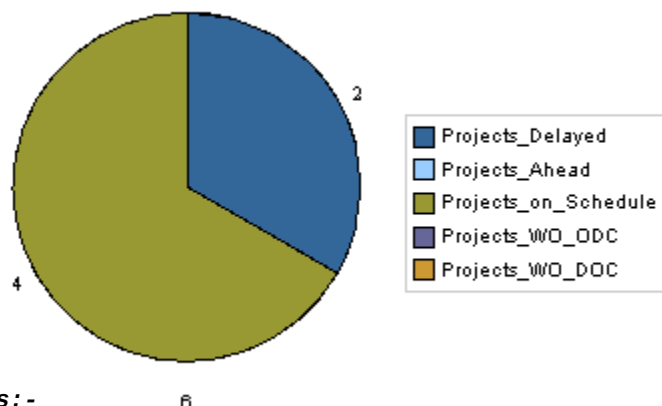


Total No Of Project's:-

6

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1781.92 crore but this was subsequently anticipated to Rs. 1793.57 crore implying a cost overrun of .7%. The expenditure incurred on these projects till November, 2018 is Rs. 657.54 crore, which is 36.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

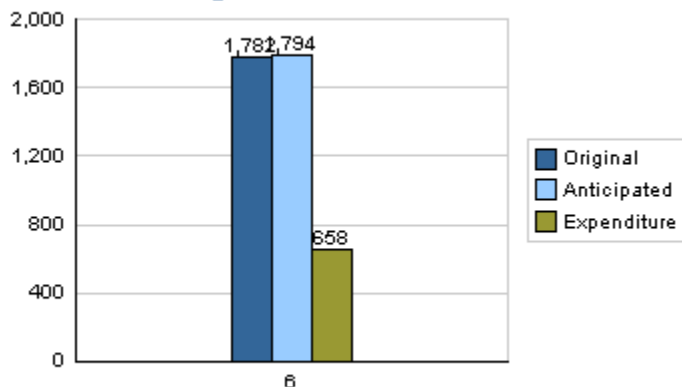

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects On Schedule	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are on schedule

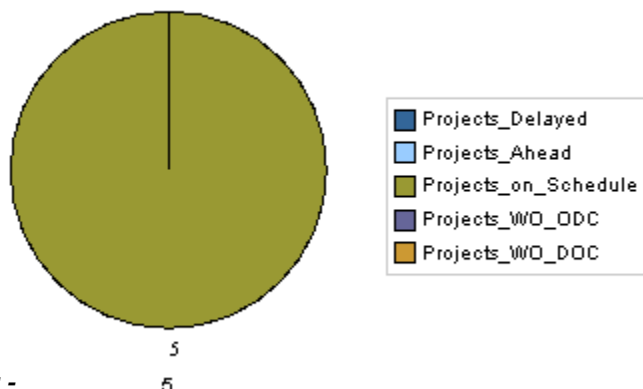


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till November, 2018 is Rs. 556.09 crore, which is 7.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

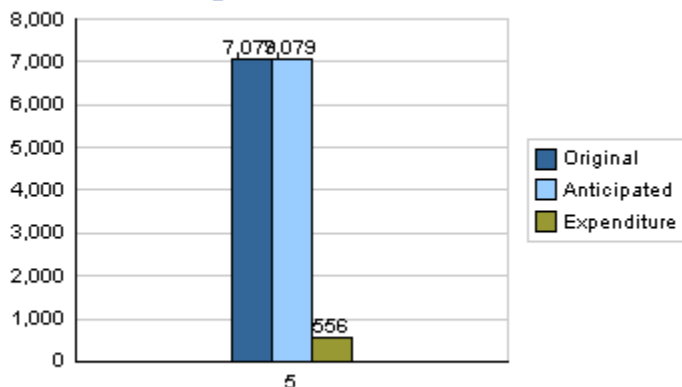

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	13
Number of Projects On Schedule	1
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 1 project is on schedule 10 projects are delayed. 2 projects do not have fixed dates of commissioning.

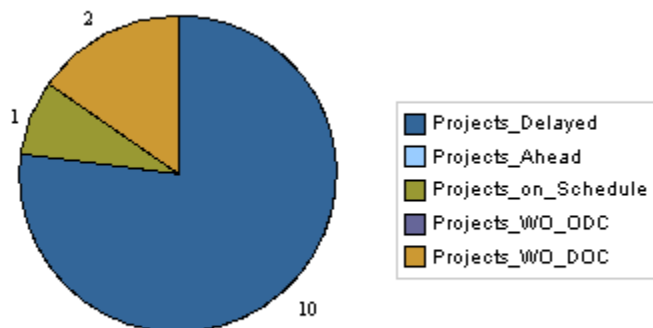


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 32529.65 crore but this was subsequently anticipated to Rs. 32317.05 cr The expenditure incurred on these projects till November, 2018 is Rs. 20968.38 crore, which is 64.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

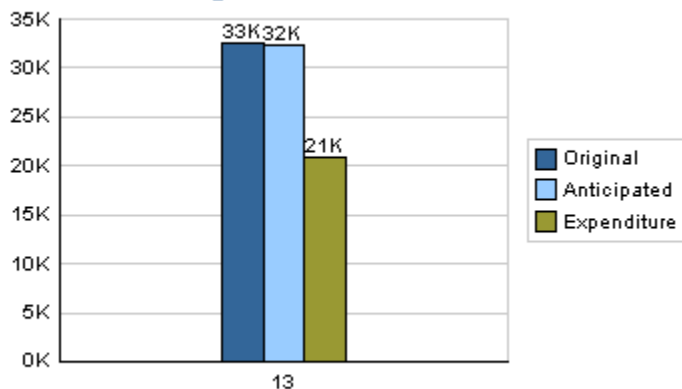

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	139
Number of Projects On Schedule	90
Number of Projects Delayed	25
Number of Projects Ahead	9
Number of Projects Without Date Of Commissioning	15

Brief Analysis

Project Status with respect to Original Schedule: Out of 139 projects, 9 projects are ahead of schedule, 90 projects are on schedule 25 projects are delayed. 15 projects do not have fixed dates of commissioning.

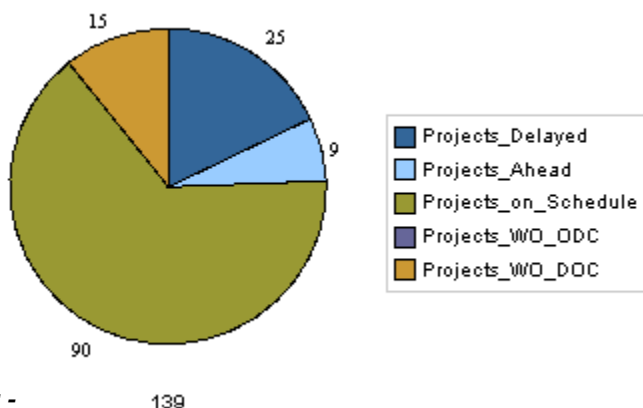


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 139 projects when sanctioned, was of the order of Rs. 224277.86 crore but this was subsequently anticipated to Rs. 224729.39 crore implying a cost overrun of .2%. The expenditure incurred on these projects till November, 2018 is Rs. 70611.62 crore, which is 31.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

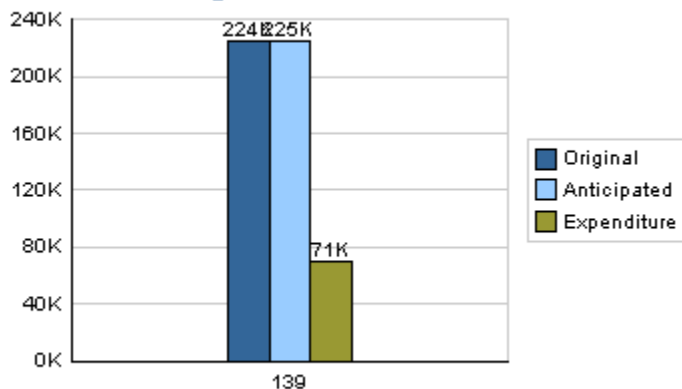

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	105
Number of Projects On Schedule	34
Number of Projects Delayed	56

Number of Projects Without Date Of Commissioning 15

Brief Analysis

Project Status with respect to Original Schedule: Out of 105 projects, 34 projects are on schedule 56 projects are delayed. 15 projects do not have fixed dates of commissioning.

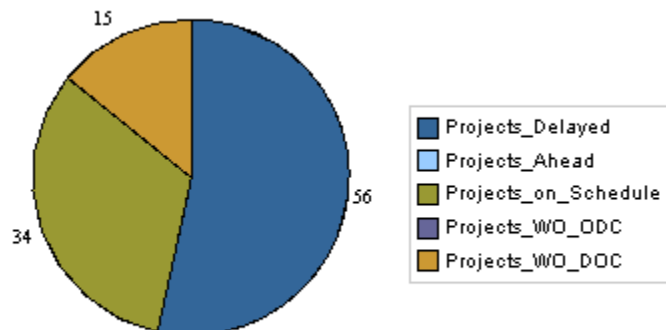


Total No Of Project's:-

105

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 307223.51 crore but this was subsequently anticipated to Rs. 372561.25 crore implying a cost overrun of 21.3%. The expenditure incurred on these projects till November, 2018 is Rs. 237045.39 crore, which is 63.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

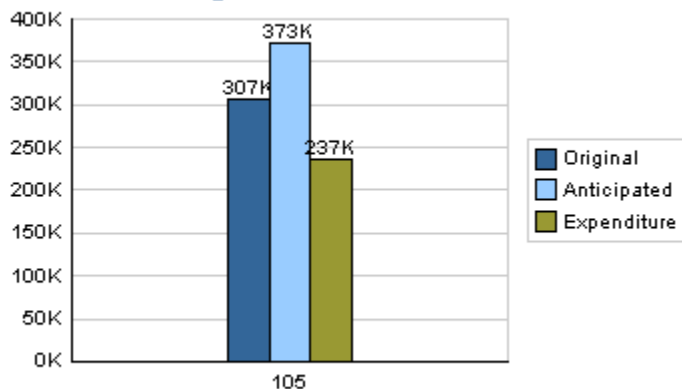

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

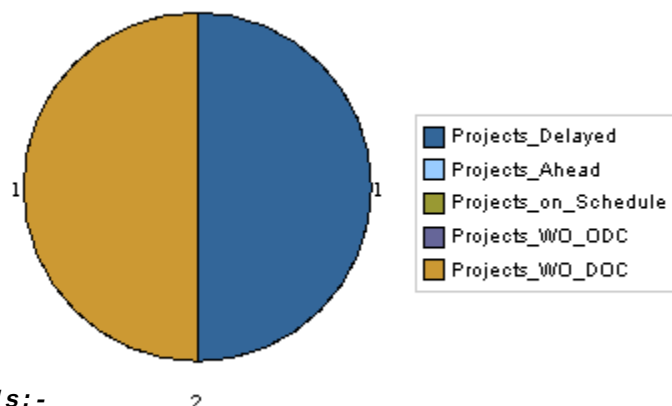


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5381.3 crore implying a cost overrun of 64.5%. The expenditure incurred on these projects till November, 2018 is Rs. 2450.86 crore, which is 45.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

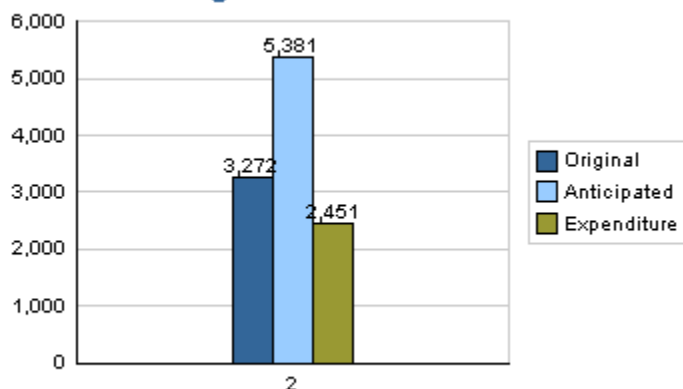

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	22
Number of Projects On Schedule	6
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning 14

Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 6 projects are on schedule 2 projects are delayed. 14 projects do not have fixed dates of commissioning.

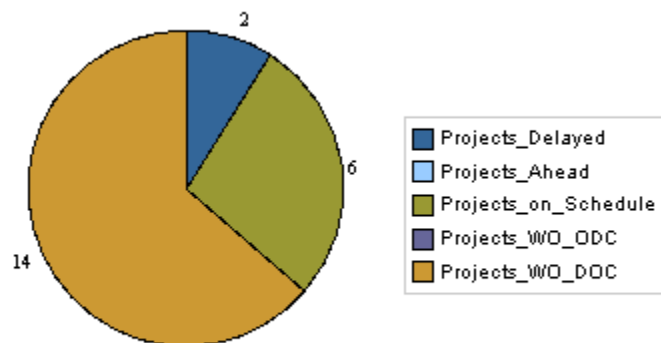


Total No Of Project's:-

22

Investment Scenario

Total original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 8611.12 crore but this was subsequently anticipated to Rs. 8660.03 crore implying a cost overrun of .6%. The expenditure incurred on these projects till November, 2018 is Rs. 2965.39 crore, which is 34.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

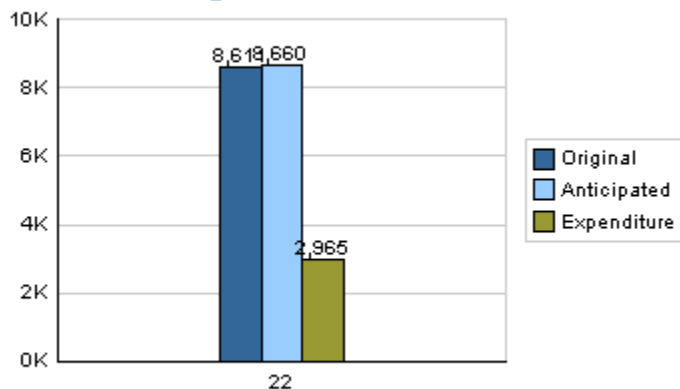

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	371
Number of Projects On Schedule	93
Number of Projects Delayed	94
Number of Projects Ahead	9
Number of Projects Without Original Date of Commissioning	28
Number of Projects Without Date Of Commissioning	147

Brief Analysis

Project Status with respect to Original Schedule: Out of 371 projects, 9 projects are ahead of schedule, 93 projects are on schedule 94 projects are delayed. 147 projects do not have fixed dates of commissioning. 28 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

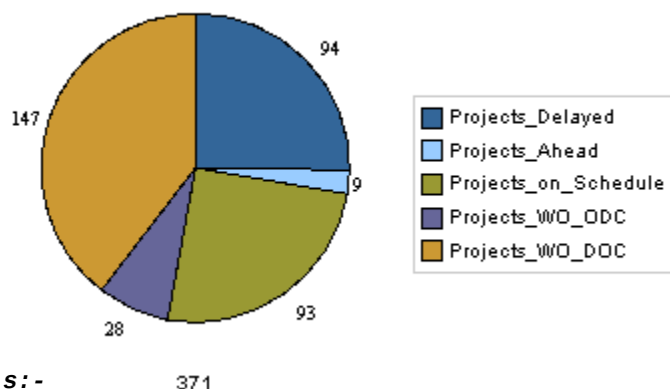


Total No Of Project's:-

371

Investment Scenario

Total original cost of implementation of 371 projects when sanctioned, was of the order of Rs. 490540.4 crore but this was subsequently anticipated to Rs. 704794.36 crore implying a cost overrun of 43.7%. The expenditure incurred on these projects till November, 2018 is Rs. 171075.46 crore, which is 24.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

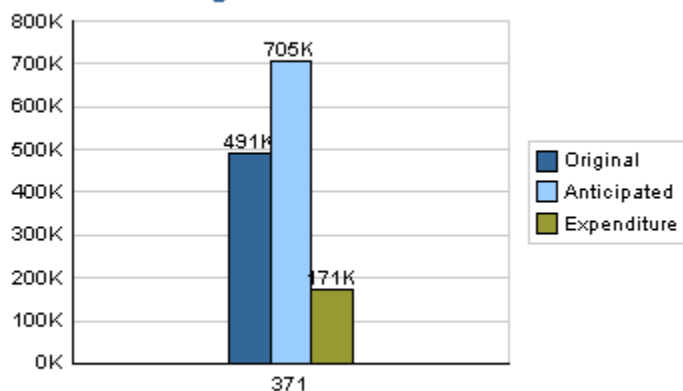

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	607
Number of Projects On Schedule	56
Number of Projects Delayed	100
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	39
Number of Projects Without Date Of Commissioning	408

Brief Analysis

Project Status with respect to Original Schedule: Out of 607 projects, 4 projects are ahead of schedule, 56 projects are on schedule 100 projects are delayed. 408 projects do not have fixed dates of commissioning. 39 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

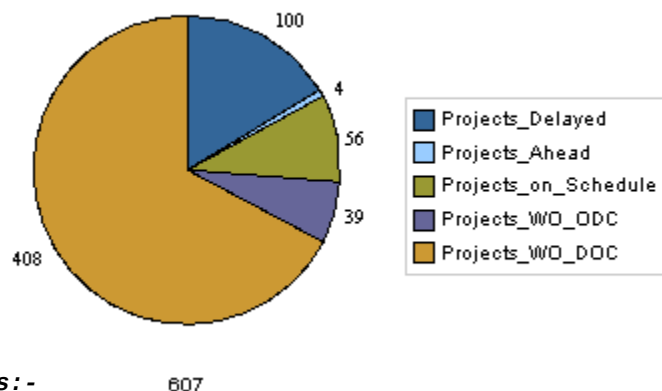


Total No Of Project's:-

607

Investment Scenario

Total original cost of implementation of 607 projects when sanctioned, was of the order of Rs. 411883.3 crore but this was subsequently anticipated to Rs. 426107.82 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till November, 2018 is Rs. 141033.89 crore, which is 33.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

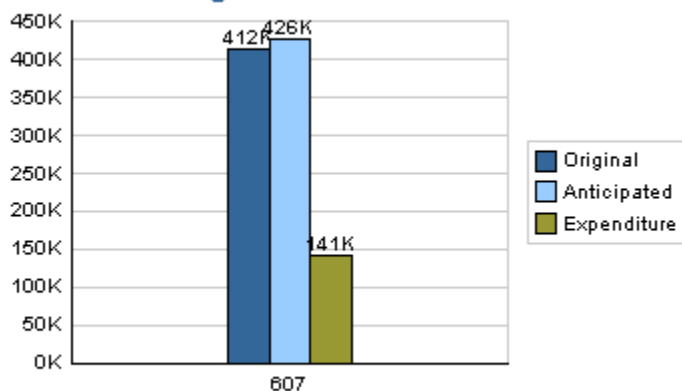

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	5
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

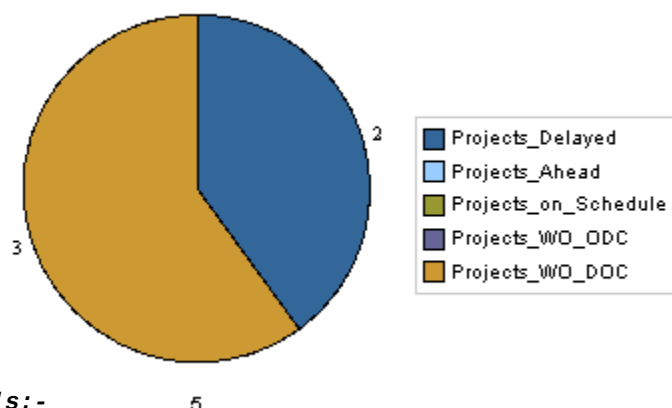


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 3788.29 crore but this was subsequently anticipated to Rs. 4230.74 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till November, 2018 is Rs. 1659.56 crore, which is 39.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

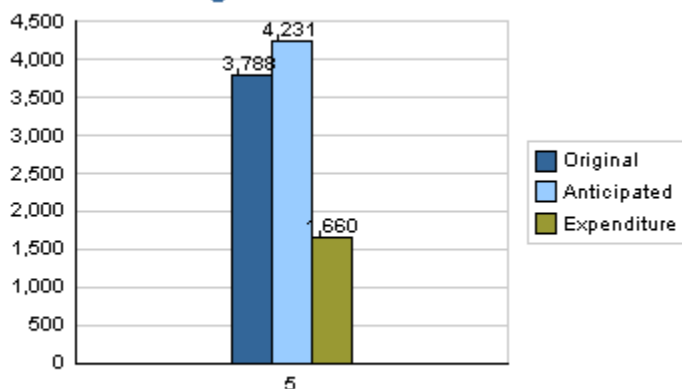

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:


Number of Projects 7

Number of Projects Delayed 5

Number of Projects Without Date Of Commissioning 2

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 5 projects are delayed. 2 projects do not have fixed dates of commissioning.

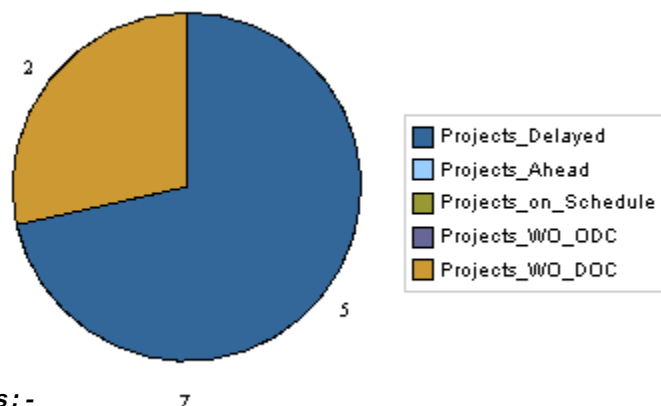


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 16637.51 crore but this was subsequently anticipated to Rs. 27866.31 crore implying a cost overrun of 67.5%. The expenditure incurred on these projects till November, 2018 is Rs. 9027.02 crore, which is 32.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

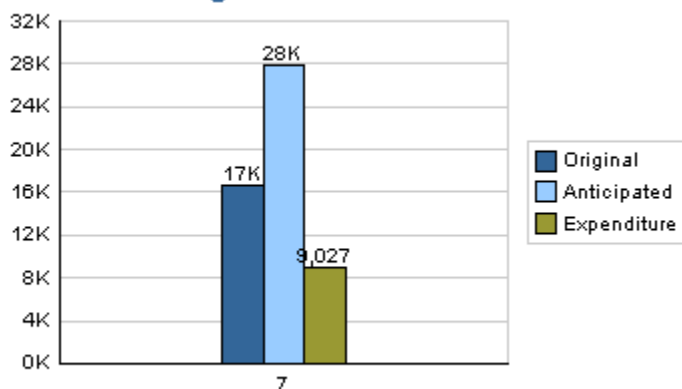

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	58
Number of Projects On Schedule	11
Number of Projects Delayed	22

Number of Projects Without Date Of Commissioning	25
--	----

Brief Analysis

Project Status with respect to Original Schedule: Out of 58 projects, 11 projects are on schedule 22 projects are delayed. 25 projects do not have fixed dates of commissioning.

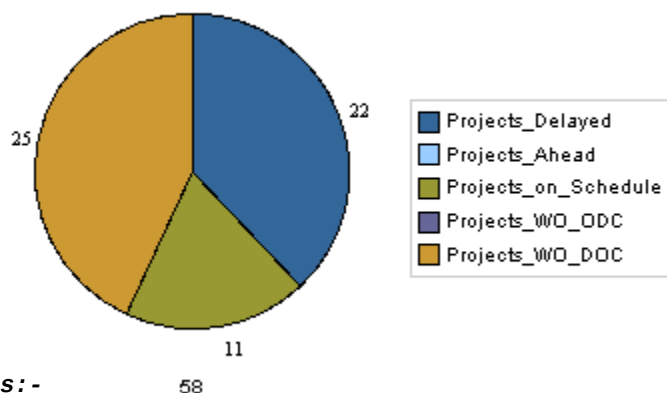


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 58 projects when sanctioned, was of the order of Rs. 160566.07 crore but this was subsequently anticipated to Rs. 166153.31 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till November, 2018 is Rs. 72017.41 crore, which is 43.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

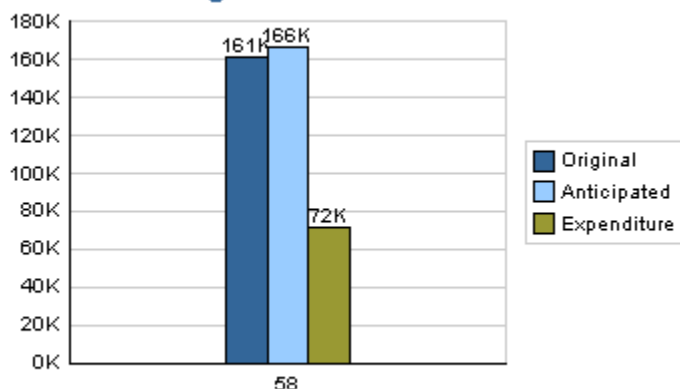

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

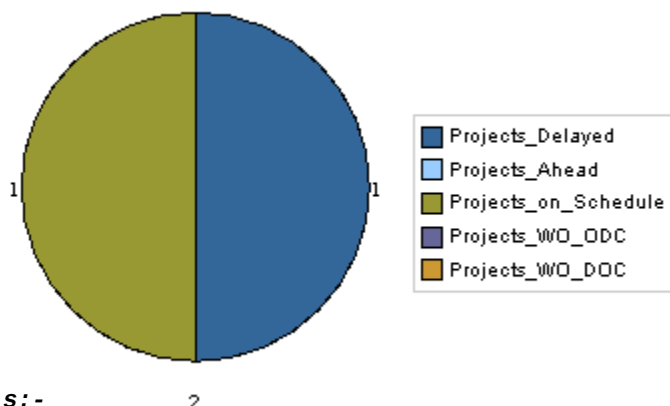


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 461.66 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till November, 2018 is Rs. 138.8 crore, which is 30.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

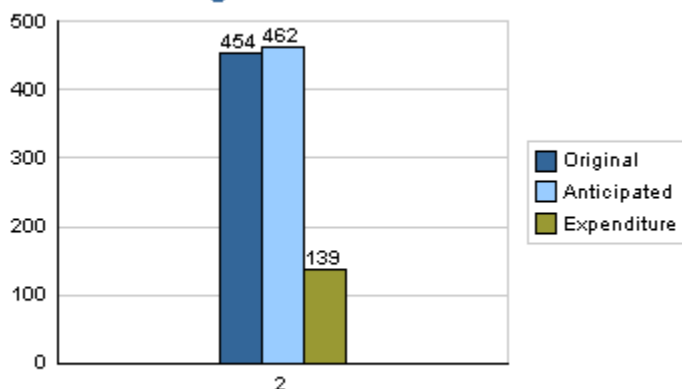

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (NOVEMBER 2018)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	8	2,385.01	2,492.59	126.88
2	ANDHRA PRADESH	69	1,07,461.29	1,11,065.37	15,524.68
3	ARUNACHAL PRADESH	31	16,421.02	33,547.53	17,622.22
4	ASSAM	47	31,134.2	39,863.2	22,338
5	BIHAR	91	76,252.26	1,11,749.59	50,632.8
6	CHHATISGARH	44	78,294.07	81,695.6	35,878.56
7	D & N HAVELI	1	6,086.08	5,842.31	4,449.66
8	DELHI	23	56,043.88	63,419.24	40,935.27
9	GOA	10	4,292.52	4,300.54	237.01
10	GUJARAT	50	51,775.98	57,577.15	29,686.32
11	HARYANA	30	21,396.4	23,309.06	9,455.31
12	HIMACHAL PRADESH	13	17,058.17	26,566.39	9,846.83
13	JAMMU AND KASHMIR	10	25,238.37	51,232.67	28,653.7
14	JHARKHAND	48	47,384.82	51,290.09	19,725.22
15	KARNATAKA	46	82,156.7	87,206.53	31,053.7
16	KERALA	22	25,879.48	28,054.1	5,121.76
17	MADHYA PRADESH	62	69,588.01	74,746.47	29,273.5
18	MAHARASHTRA	131	1,88,756.03	2,00,480.7	73,242.94
19	MANIPUR	2	4,670.86	14,025.69	7,971.05
20	MEGHALAYA	7	4,484.97	9,578.51	1,189.76
21	MIZORAM	4	3,406.61	5,981.14	2,449.15
22	MULTI STATE	170	3,50,660.19	4,53,147.35	1,33,828.91
23	NAGALAND	21	13,711.07	14,384.55	655.38
24	ODISHA	82	92,455.45	98,016.41	29,887.21
25	PUNJAB	34	17,565.89	17,571.62	4,410.91
26	RAJASTHAN	57	46,334.89	48,591.45	24,185.65
27	SIKKIM	9	3,476.73	6,281.03	433.9
28	TAMIL NADU	76	1,19,890.58	1,37,384.34	60,641
29	TELANGANA	42	34,502.53	38,040.07	9,216.56
30	TRIPURA	9	4,422.36	8,312.05	6,360.01
31	UTTAR PRADESH	110	1,34,449.08	1,35,916.3	52,377.42
32	UTTARAKHAND	28	33,689.4	39,554.65	11,230.14
33	WEST BENGAL	56	59,037.58	69,912.4	28,855.03
TOTAL		1,443	18,30,362.48	21,51,136.69	7,97,496.44

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,100.00	5,687.52	09/2010 -	03/2019
	Total		3,492.00 -	6,100.00	5,687.52		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
2	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	583.96	03/2013 -	03/2020
3	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	234.29	03/2012 -	03/2021
4	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	266.97	03/2010 -	03/2020
	<u>Northern Coal Fields Limited</u>						
5	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	266.38	03/2012 -	-
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023
	<u>Western Coal Fields Limited</u>						
7	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
	Total		1,714.18 -	2,012.00	2,084.06		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
8	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	237.80	05/2017 -	-
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.38	191.38	05/2017 -	-
10	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	322.00	469.00	08/2018 -	-
	Total		686.33 -	717.82	898.18		
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	4/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,718.00 -	3,827.30	2,289.00		
	<u>PETROLEUM</u>						
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	Total		993.00 -	1,693.00	1,549.85		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
13	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,394.80	7,121.50	09/2009 -	12/2021
14	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,496.34	10,385.81	09/2010 -	-
	<u>National Thermal Power Corporation</u>						
15	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,690.33	03/2013 12/2020	12/2020
16	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	16,934.65	15,364.00	01/2017 -	-
17	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	1/2007	5,353.00 -	7,998.00	7,128.72	05/2014 -	05/2019
	<u>North East Electric Power Corporation</u>						
18	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,838.94	12/2009 03/2019	03/2019
19	TRIPURA GAS BASED POWER PROJECT - [N18000071]	7/2009	421.01 -	1,078.31	963.23	07/2013 -	-
	<u>Power Grid Corporation Of India Limited</u>						
20	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	669.46	09/2010 -	12/2018
21	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	9/2011	1,940.13 -	2,702.65	2,529.92	09/2014 -	10/2018
22	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	3/2015	955.00 -	1,364.00	1,237.00	12/2015 -	12/2018
23	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]	8/2008	771.00 -	1,624.00	1,429.45	02/2013 -	10/2018
24	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	426.98	08/2014 -	12/2018
25	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,534.00	2,051.63	11/2008 -	12/2018
26	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	499.90	06/2014 -	12/2018

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,714.20	08/2013 -	03/2022
28	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	7/2010	1,272.80 -	1,731.10	1,461.65	11/2012 -	10/2018
29	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	2/2010	2,144.00 -	2,932.88	2,654.96	12/2012 -	11/2018
	<u>Satluj Jal Vidyut Nigam Limited</u>						
30	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	602.44	506.97	12/2016 -	12/2018
	Total		58,312.10 -	94,094.19	77,674.65		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
31	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	298.70	240.89	03/2019 -	03/2019
32	AMRAVATI-NARKHER NL(CR) - [220100118]	6/1994	663.01 175.30	858.96	716.67	06/1999 -	-
	<u>East Central Railways</u>						
33	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020
34	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020
35	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	4/1998	180.82 -	528.26	462.75	- -	12/2018
36	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	559.91	538.21	07/2014 -	-
37	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
38	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	589.15	183.72	- -	03/2022
39	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	566.41	759.20	- -	12/2021
	<u>East Coast Railway</u>						
40	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
41	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	607.91	1,067.93	02/2013 -	06/2016
42	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]	4/2011	166.89 -	166.89	246.00	- -	-
43	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	4/1995	1,125.89 -	1,125.89	2,007.32	03/2016 -	03/2020
44	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	332.14	360.58	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Metropolitan Rapid Transport Projects</u>						
45	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-
	<u>North Central Railway</u>						
46	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	4/1986	158.77 274.56	634.48	629.43	03/1994 -	-
47	ETAWAH-MAINPURI (NL),NCR - [220100318]	4/1997	120.00 -	245.39	210.67	12/2008 -	-
48	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	4/1999	108.00 -	432.72	446.52	12/2009 -	-
	<u>North East Frontier Railway</u>						
49	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	9/2001	792.46 -	1,320.00	928.50	12/2010 -	-
50	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	03/2019
51	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2020
52	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2020
54	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	9/1997	3,230.02 -	5,820.00	5,224.22	04/2008 12/2011	06/2018
55	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	1,142.00 -	3,374.00	3,015.98	03/2014 12/2019	03/2019
56	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	264.69	03/2019 -	03/2019
57	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	551.00	595.01	03/2019 -	03/2019
58	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	- -	03/2018
59	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	457.51	03/2019 -	03/2019
	<u>North Eastern Railway</u>						
60	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	4/2003	218.19 -	413.56	364.21	06/2018 -	10/2018
61	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	274.48	12/2022 -	05/2019
62	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	3/2008	195.64 -	435.00	447.20	- -	03/2018
63	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	4/1999	744.71 -	1,126.79	751.05	- -	-
64	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	4/1997	609.04 1,063.00	1,807.88	1,805.26	04/1999 -	12/2018
65	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	4/1997	233.00 -	318.42	334.60	04/1999 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
66	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	3/2012	199.75 -	270.00	265.14	08/2018 -	08/2018
	<u>North Western Railway</u>						
67	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	1,116.00	795.27	03/2014 03/2019	03/2019
68	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	4/2012	288.97 -	346.35	295.70	11/2018 -	12/2018
69	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	349.00	278.89	02/2019 -	03/2019
	<u>Northern Railway</u>						
70	JIND-SONEPAT (NL),NR - [220100280]	1/2004	238.56 -	740.00	722.65	03/2012 -	-
71	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	369.90 -	1,581.53	618.19	03/2010 -	-
72	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	3/2002	625.30 408.76	876.10	841.57	06/2007 -	-
73	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,100.00	484.14	07/2012 -	-
	<u>Rail Vikas Nigam Ltd.</u>						
74	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	1,185.64 -	1,844.47	1,367.66	12/2017 -	06/2019
75	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	4/1995	631.78 -	1,195.00	653.64	12/2012 -	03/2022
76	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	9/2006	383.54 -	555.00	575.93	03/2010 -	12/2019
77	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	7/2006	732.81 -	1,850.00	1,972.23	03/2008 -	03/2020
78	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	385.00	373.73	03/2009 03/2009	12/2018
79	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	978.21	03/2019 -	03/2020
80	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	970.00	975.36	03/2020 -	03/2020
81	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,750.00	1,563.47	03/2020 -	03/2020
	<u>South Central Railway</u>						
82	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	164.36 -	1,050.00	999.64	02/2009 -	10/2018
83	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,025.00	1,021.82	- 03/2017	03/2017
	<u>South East Central Railway</u>						
84	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
	<u>South Eastern Railway</u>						
85	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	152.45	12/2016 08/2018	12/2018

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164 <u>Southern Railway</u>	4/2010	309.44 -	525.81	495.14	12/2015 12/2018	12/2018
87	CALICUT-MANGALORE (DL) (SR) - [220100151	2/1996	240.00 -	579.37	537.30	- -	-
88	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454	2/2005	241.00 -	241.00	294.63	03/2014 -	-
89	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446	2/2005	600.00 600.00	645.54	671.00	03/2010 -	-
90	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	302.02	304.07	03/2005 -	-
91	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440	2/2000	200.84 -	200.84	394.26	03/2014 -	-
92	CHENGANNUR-CHINGAVANAM - [N22000203	4/2006	191.72 -	369.83	432.50	- -	-
93	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188	4/1998	271.24 -	520.00	468.18	- -	-
94	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	556.64	303.72	- -	-
95	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	9/2006	343.17 -	1,065.00	1,049.68	- -	-
96	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019
97	KARUR-SALEM(NL),SR - [220100191	2/1997	155.55 -	920.00	856.94	- -	-
98	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263 <u>West Central Railway</u>	3/1998	280.00 -	1,122.00	834.87	- -	-
99	RAMGANJMUJUNDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
100	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232 <u>Western Railway</u>	9/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023
101	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	203.00	202.29	03/2011 -	-
	Total		37,005.92 -	91,438.25	67,363.94		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
102	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	410.32	02/2009 -	-
103	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019
104	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]	1/2016	701.12 -	701.12	842.34	05/2019 -	05/2019
106	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	627.37	07/2008 -	-
107	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	1,665.00	1,836.44	- -	-
108	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018
109	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	2,304.41	01/2018 -	12/2018
110	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	5/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	12/2018
111	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	12/2018
112	NAGPUR - KONDHALI - [N24000472]	9/2005	168.00 -	168.00	279.92	06/2006 -	-
113	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	681.34	06/2016 -	-
114	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,302.51	07/2017 -	12/2018
115	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	-
116	ROHTAK-BAWAL - [N24000169]	5/2011	650.00 -	650.00	832.39	11/2013 -	-
117	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	884.12	02/2013 -	12/2018
118	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
119	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-
120	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]	2/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	-
121	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018
122	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	3,237.87	3,176.22	09/2012 -	08/2018
123	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]	11/2010	1,585.00 -	1,585.00	2,159.63	05/2013 -	-
124	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	564.35	11/2013 -	12/2018
125	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	831.33	07/2013 -	06/2019
126	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
127	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.62	03/2014 -	09/2018

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
128	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	2,993.77	05/2014 -	-
129	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	678.87	01/2014 -	01/2019
130	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.52	10/2013 -	12/2018
131	KANDLA - MUNDRA PORT - [N24000175]	1/2011	953.88 -	953.88	975.23	07/2013 -	12/2018
132	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018
133	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	1,945.00	01/2019 -	01/2019
134	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	839.63	03/2018 -	-
135	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018
136	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	604.80	10/2017 -	12/2018
137	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	495.78	603.13	01/2016 -	-
138	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	351.34	425.99	01/2016 -	-
139	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	2,335.94	04/2015 -	-
140	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-
141	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-
142	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	430.61	01/2014 -	09/2018
143	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	-
144	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	-
145	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,822.70	08/2013 -	-
146	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,310.60	08/2013 -	-
147	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019
148	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	10/2015
149	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	1,246.47	06/2014 -	-
150	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
151	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	297.81	04/2008 -	03/2019
152	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	389.08	04/2010 -	04/2019
153	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	325.00	469.54	05/2013 -	-
154	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,058.04	03/2013 -	06/2019
155	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,288.00	3,871.89	11/2011 -	06/2019
156	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	340.12	07/2009 -	-
157	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	209.80	04/2009 -	-
158	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,410.94	09/2016 -	06/2019
159	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018
160	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	198.82	05/2008 -	02/2019
161	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	195.35	11/2008 -	-
162	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018
	Total		56,192.04 -	61,672.71	84,538.88		
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
163	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	275.98	275.98	12/2017 -	-
	<u>Mumbai Port Trust</u>						
164	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	1/2007	366.39 -	669.46	411.12	12/2010 -	12/2018
	Total		610.89 -	945.44	687.10		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
165	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	391.23	05/2017 08/2018	03/2019
	<u>Chennai Metro Rail Ltd</u>						
166	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-
	<u>Hindustan Steelwork Construction Limited</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(November 2018)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
167	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
168	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	178.65	12/2015 -	-
	Total		15,906.61 -	20,735.28	18,008.29		
	Grand Total		1,76,631.07	2,83,235.99	2,60,781.47		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs.150 Crore and above						(November 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	774.62	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	619.33	12/2020 -	08/2020
4	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	516.56	10/2019 -	03/2019
5	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52	247.52	139.42	02/2019 -	12/2018
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00	356.00	194.38	05/2019 -	12/2018
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	6.28	09/2022 -	06/2021
8	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	385.61	12/2020 -	02/2020
	Total		15,270.92 -	14,386.52	2,831.17		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
9	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	100.63	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
10	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019
11	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	193.12	03/2022 -	03/2020
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	18.38	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
13	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	274.48	12/2022 -	05/2019
14	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	99.33	03/2022 -	02/2019
	<u>North Western Railway</u>						
15	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	127.14	12/2019 -	06/2019

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
16	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]	4/2013	420.18 295.02	420.18	81.44	03/2020 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
17	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.22	12/2025 -	03/2025
	Total		7,240.31 -	10,074.24	3,910.72		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
18	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	86.95	03/2020 -	05/2019
19	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	41.21	03/2020 -	06/2019
20	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	10.57	03/2020 -	06/2019
21	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	15.00	04/2020 -	11/2019
	Total		1,995.48 -	1,873.06	153.73		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
22	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020
	Total		150.29 -	150.29	2.58		
	Grand Total		24,657.00	26,484.11	6,898.20		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs.150 Crore and above						(November 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	184.43	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	296.64	03/2022 -	03/2022
4	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
5	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	174.04	08/2019 -	08/2019
6	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.45	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
7	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	435.69	03/2021 -	03/2021
8	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	689.19	03/2026 -	03/2026
	<u>Neyveli Lignite Corporation</u>						
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	3,716.05	11/2021 -	11/2021
10	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	173.06	12/2019 -	12/2019
11	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	8.71	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
12	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022
13	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	207.63	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
14	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
15	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
16	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 -	03/2019
	<u>South-Eastern Coal Fields Limited</u>						
17	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.53	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	4.06	03/2023 -	03/2023
19	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.51	03/2021 -	03/2021
20	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,902.85	03/2023 -	03/2023
21	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
22	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.81	03/2023 -	03/2023
23	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
24	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,842.98	03/2023 -	03/2023
25	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.13	03/2023 -	03/2023
26	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	58.15	03/2020 -	03/2020
27	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	74.81	03/2022 -	03/2022
28	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
29	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
30	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
31	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	56.54	03/2020 -	03/2020
32	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.19	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
33	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
34	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
35	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	102.75	03/2020 -	03/2020
36	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
37	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	83.52	03/2021 -	03/2021
38	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	391.37	03/2020 -	03/2020
39	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	257.36	03/2020 -	03/2020
40	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
42	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	16.21	03/2022 -	03/2022
43	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	95.81	03/2023 02/2017	03/2023
44	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.29	03/2021 -	03/2021
45	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	52.87	03/2020 -	03/2020
46	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	184.45	03/2020 -	03/2020
47	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	88.46	03/2021 -	03/2021
48	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	236.66	03/2025 -	03/2025
49	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	129.39	03/2019 -	03/2019
	Total		68,816.31 -	69,084.18	13,607.18		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
50	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	51.87	08/2020 -	08/2020
	Total		285.95 -	291.29	51.87		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	28.60	11/2019 -	11/2019
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	27.20	11/2019 -	11/2019
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	23.79	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
54	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	38.65	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	118.24		
	<u>HEALTH AND FAMILY WELFARE</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HII Infra Tech Services Limited</u>						
55	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
56	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
57	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
	<u>Hospital Services Consultancy Corporation</u>						
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	76.88	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	122.66	03/2019 -	03/2019
60	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	71.50	03/2019 -	03/2019
	Total		3,264.53 -	3,264.53	756.39		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
61	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	302.19	01/2020 01/2020	01/2020
62	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
63	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
64	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	166.62	125.00	06/2019 06/2019	06/2019
65	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
	Total		7,078.62 -	7,078.62	556.09		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
66	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	115.17	12/2019 -	12/2019
67	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	56.69	08/2020 -	08/2020
68	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
69	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	19.99	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
70	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	135.68	02/2020 -	02/2020
	<u>Chennai Petroleum Corporation Limited</u>						
71	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	575.65	12/2019 -	12/2019
72	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	16.73	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
73	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	22.11	10/2022 -	10/2022
74	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	774.62	12/2019 12/2020	12/2019
75	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	800.00	600.58	12/2018 -	12/2018
76	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	14.06	07/2022 -	07/2022
77	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	776.24	12/2020 -	12/2020
78	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	99.03	04/2022 -	04/2022
79	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	29.39	07/2022 -	07/2022
80	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	733.62	02/2020 -	02/2020
81	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	2,313.08	12/2018 -	12/2018
82	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	21.92	10/2022 -	10/2022
83	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	652.51	12/2020 -	12/2020
84	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	28.18	10/2022 -	10/2022
85	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	21.02	12/2020 -	12/2020
86	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	663.13	12/2020 -	12/2020
87	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1.66	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
88	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	110.04	02/2019 -	02/2019
89	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
90	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	4.33	11/2020 -	11/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
91	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
92	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
93	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	961.58	06/2020 -	06/2020
94	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	241.80	09/2019 -	09/2019
95	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
96	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	49.88	03/2021 -	03/2021
	<u>Indian Oil Corporation Limited</u>						
97	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	857.95	07/2019 -	07/2019
98	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	2.56	12/2021 -	12/2021
99	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020
100	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
101	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	3.64	01/2021 -	01/2021
102	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	1.88	03/2021 -	03/2021
103	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,208.92	11/2019 -	11/2019
104	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
105	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
106	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	569.04	12/2020 -	12/2020
107	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	499.85	08/2021 -	08/2021
108	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	208.63	08/2019 -	08/2019
109	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
110	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	14.11	01/2021 -	01/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
111	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
112	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	809.78	11/2018 -	11/2018
113	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]	4/2018	355.00 -	355.00	-	04/2022 -	04/2022
114	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	268.88	09/2019 -	09/2019
115	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	99.30	09/2019 -	09/2019
116	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	8.48	01/2021 -	01/2021
117	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	38.79	04/2021 -	04/2021
118	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.67	08/2020 -	08/2020
119	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	200.89	09/2019 -	09/2019
120	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	-	08/2020 -	08/2020
121	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	12.65	08/2021 -	08/2021
122	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	256.93	01/2019 -	01/2019
123	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	69.88	02/2020 -	02/2020
124	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	25.56	02/2020 -	02/2020
125	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	33.81	12/2019 -	12/2019
126	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	67.71	07/2020 -	07/2020
127	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	0.17	06/2020 -	06/2020
128	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
129	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	78.63	06/2020 -	06/2020
130	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	8.48	01/2021 -	01/2021
131	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]	8/2018	466.00 -	466.00	1.12	04/2021 -	04/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
132	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	8/2017	236.00 -	236.00	11.66	06/2020 -	06/2020
133	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340	8/2018	1,636.00 -	1,636.00	123.17	08/2020 -	08/2020
134	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	4/2018	206.63 -	206.63	0.12	02/2020 -	02/2020
135	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310	3/2018	3,380.00 -	3,380.00	1,151.10	09/2019 -	09/2019
136	KHARAGPUR LPG BOTTLING PLANT - [N16000300	4/2017	163.02 -	163.02	32.69	04/2020 -	04/2020
137	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322	5/2018	2,934.40 -	2,934.40	738.18	09/2019 -	09/2019
138	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333	3/2018	676.00 -	676.00	3.41	12/2021 -	12/2021
139	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338	4/2018	4,807.08 -	4,807.08	24.09	07/2021 -	07/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
140	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00 171.00	170.70	124.25	03/2019 03/2019	03/2019
141	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
142	BSVI UPGRADATION - [N16000257	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
143	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
144	GAMJI REDEVELOPMENT PROJECT - [N16000202	5/2015	1,671.22 -	567.22	449.95	11/2019 -	11/2019
145	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	7/2016	249.85 250.00	244.70	98.10	05/2020 05/2020	05/2020
146	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	1,162.56	285.28	03/2026 03/2026	03/2026
147	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297	2/2017	4,006.83 -	4,006.83	1,226.29	05/2021 05/2021	05/2021
148	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290	1/2017	474.15 -	474.15	299.26	05/2019 05/2019	05/2019
149	DEVELOPMENT OF BSE-11 BLOCK - [N16000293	2/2017	511.30 -	511.30	167.64	11/2019 11/2019	11/2019
150	DEVELOPMENT OF B-147 FIELD - [N16000292	2/2017	546.15 -	546.15	191.39	11/2019 11/2019	11/2019
151	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294	2/2017	968.61 -	968.61	502.40	11/2019 11/2019	11/2019
152	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335	4/2018	766.37 -	766.37	-	12/2019 -	12/2019
	<u>Oil India Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
153	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	42.33	12/2019 -	12/2019
154	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	23.61	10/2020 -	10/2020
155	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	1.65	02/2020 -	02/2020
	Total		1,08,401.41 -	1,05,241.87	20,871.05		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
156	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,293.72	11/2019 -	11/2019
157	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	6,135.72	09/2019 -	09/2019
	<u>Power Grid Corporation Of India Limited</u>						
158	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	55.10	02/2020 -	02/2020
159	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]	3/2017	162.31 -	162.31	22.42	03/2019 -	03/2019
160	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	354.00	04/2019 -	04/2019
161	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	21.82	12/2019 -	12/2019
162	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	103.28	02/2019 -	02/2019
163	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	20.09	06/2019 -	06/2019
164	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	97.53	11/2018 -	11/2018
165	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	552.21	04/2020 -	04/2020
166	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	303.70	04/2019 -	04/2019
167	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	197.76	02/2019 -	02/2019
168	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	321.99	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
169	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	50.27	07/2019 -	07/2019
170	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,798.00	04/2019 -	04/2019
171	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	597.00	07/2020 -	07/2020
172	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	191.76	02/2019 -	02/2019
173	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	79.31	06/2019 -	06/2019
174	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
175	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	76.98	02/2019 -	02/2019
176	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	26.40	03/2019 -	03/2019
177	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	743.82	01/2019 -	01/2019
178	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	89.17	09/2019 -	09/2019
179	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	502.54	06/2019 -	06/2019
180	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	375.34	11/2018 -	11/2018
181	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	16.10	06/2019 -	06/2019
182	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	2.50	06/2019 -	06/2019
183	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	25.85	11/2019 -	11/2019
184	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,861.40	05/2019 -	05/2019
185	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	194.26	12/2018 -	12/2018
186	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	3,710.05	11/2019 -	11/2019
187	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	250.73	03/2019 -	03/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
188	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	131.82	12/2021 -	12/2021
	<u>Thdc India Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
189	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	65.37	09/2020 -	09/2020
	Total		58,003.27 -	59,281.79	21,268.01		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
190	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	272.78	03/2021 -	03/2021
191	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
192	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	1.27	03/2023 -	03/2023
193	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	-	03/2024 -	03/2024
194	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
195	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	1,870.67	03/2021 -	03/2021
196	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	3,627.47	309.54	03/2024 -	03/2024
197	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	26.63	03/2023 -	03/2023
198	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	87.60	03/2023 -	03/2023
199	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	298.70	240.89	03/2019 -	03/2019
200	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	156.10	03/2022 -	03/2022
201	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	132.09	03/2022 -	03/2022
202	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	979.05	03/2023 -	03/2023
	<u>Container Corporation Of India</u>						
203	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	272.72	03/2019 -	03/2019
204	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	253.28	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
205	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
206	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
207	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
208	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
209	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	571.51	03/2020 -	03/2020
210	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	81.06	03/2022 -	03/2022
211	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
212	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	189.40	03/2022 -	03/2022
213	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	183.68	03/2022 -	03/2022
<u>Eastern Railways</u>							
214	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	4/2000	1,188.91 -	1,620.01	843.85	03/2019 12/2009	03/2019
215	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	319.21	03/2022 -	03/2022
216	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]	4/2010	157.94 -	157.94	50.69	11/2018 -	11/2018
217	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	303.58	03/2020 -	03/2020
<u>North Central Railway</u>							
218	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
219	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
220	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021
221	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
<u>North East Frontier Railway</u>							
222	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	163.08	03/2021 -	03/2021
223	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	64.09	03/2020 -	03/2020
224	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	123.11	03/2020 -	03/2020
225	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	264.69	03/2019 -	03/2019
226	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	457.51	03/2019 -	03/2019
227	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
228	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	551.00	595.01	03/2019 -	03/2019
229	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	259.43	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
230	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
231	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	366.71	0.45	01/2022 -	01/2022
232	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>North Western Railway</u>						
233	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	206.88	11/2019 -	11/2019
234	PHULERA - DIGANA DOUBLING - [N22000326]	5/2015	600.00 -	685.99	3.51	03/2020 -	03/2020
235	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	795.01	450.57	02/2019 -	02/2019
236	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	-	08/2022 -	08/2022
	<u>Northern Railway</u>						
237	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
238	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	899.56	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
239	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
240	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,127.00	1,161.88	03/2023 -	03/2023
241	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,750.00	1,563.47	03/2020 -	03/2020
242	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	975.62	623.78	12/2021 -	12/2021
243	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	835.70	12/2021 -	12/2021
244	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	300.05	12/2024 -	12/2024
245	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	758.09	849.72	03/2020 -	03/2020
246	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	354.55	12/2026 -	12/2026
247	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	970.00	975.36	03/2020 -	03/2020
248	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	101.07	03/2021 -	03/2021
249	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	249.33	12/2023 -	12/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
250	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,485.85	867.07	12/2020 -	12/2020
251	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	773.94 -	773.94	219.80	12/2024 -	12/2024
	<u>South Central Railway</u>						
252	KAZIPET-BALHRSHA - [N22000367	4/2015	2,063.03 -	2,063.03	368.22	03/2021 -	03/2021
253	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	704.31	119.69	03/2020 03/2020	03/2020
254	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>South East Central Railway</u>						
255	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
256	GEVRA ROAD PENDRA ROAD - [N22000488	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
257	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
258	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
259	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
260	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
261	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
262	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
263	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	4/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019
	<u>South Eastern Railway</u>						
264	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491	4/1998	1,027.40 -	2,373.00	481.65	03/2022 -	03/2022
265	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	1/1991	1,013.45 -	1,428.00	484.48	12/2021 12/2021	12/2021
	<u>South Western Railway</u>						
266	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	578.00	448.98	03/2020 03/2020	03/2020
267	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	860.43	490.28	03/2020 03/2020	03/2020
	<u>Southern Railway</u>						
268	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
269	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	4/2011	120.70 -	1,800.00	112.10	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
270	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019
271	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
272	ATTIPPATTU PUTTUR - [N22000184]	4/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019
	<u>West Central Railway</u>						
273	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
274	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
275	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
	<u>Western Railway</u>						
276	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	700.00	11.19	06/2020 -	06/2020
277	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	691.84	15.31	03/2020 -	03/2020
278	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	551.51	257.05	03/2019 -	03/2019
279	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	385.60	500.42	03/2020 03/2020	03/2020
280	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	1,030.29	1,081.52	03/2022 03/2019	03/2022
281	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	606.41	03/2022 03/2019	03/2022
282	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	603.75	03/2022 03/2019	03/2022
	Total		2,51,693.55 -	3,15,213.03	51,601.56		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
283	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019
284	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
286	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	-	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
287	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019
288	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000820	11/2017	237.80 -	238.00	-	11/2019 -	11/2019
289	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
290	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
291	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019
292	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	45.92	06/2019 -	06/2019
293	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	74.52	02/2020 -	02/2020
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
294	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
295	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
296	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
297	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
298	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
299	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
	<u>National Highways Authority Of India</u>						
300	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
301	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
302	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	1,388.34	206.87	09/2019 -	09/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
303	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	886.98	03/2020 -	03/2020
304	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
305	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
306	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	7/2015	2,128.72 -	2,128.72	218.51	04/2019 -	04/2019
307	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	1,945.00	01/2019 -	01/2019
308	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]	6/2015	1,583.79 -	1,583.79	496.70	01/2019 -	01/2019
309	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]	1/2017	244.90 -	244.90	77.00	05/2019 -	05/2019
310	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	351.90	04/2019 -	04/2019
311	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
312	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
313	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	2/2016	997.15 -	997.15	328.14	03/2019 -	03/2019
314	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]	7/2015	1,885.74 -	1,885.74	1,622.44	05/2019 -	05/2019
315	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
316	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	950.69	388.34	08/2019 -	08/2019
317	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
318	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	784.53	06/2019 -	06/2019
319	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
320	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]	11/2016	400.25 -	400.25	38.57	03/2019 -	03/2019
321	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	21.98	03/2020 -	03/2020
322	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	270.31	04/2020 -	04/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
323	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442	12/2015	649.50 -	649.50	80.89	03/2019 -	03/2019
324	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	237.07	07/2019 -	07/2019
325	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540	1/2016	701.12 -	701.12	842.34	05/2019 -	05/2019
326	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604	8/2016	320.30 -	320.30	193.54	01/2019 -	01/2019
327	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545	1/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018
328	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	87.19	07/2019 -	07/2019
329	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	1,167.42	191.05	03/2019 -	03/2019
330	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
331	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	5.00	03/2020 -	03/2020
332	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA - [N24000553	3/2016	229.37 -	229.37	6.39	11/2018 -	11/2018
333	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
334	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	3/2016	1,587.49 -	1,587.49	145.81	04/2019 -	04/2019
335	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605	8/2016	227.49 -	227.49	15.03	01/2019 -	01/2019
336	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	409.11	04/2019 -	04/2019
337	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546	2/2016	273.20 -	273.20	32.98	02/2019 -	02/2019
338	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	1,041.10	159.02	04/2019 -	04/2019
	Total		46,052.89 -	46,536.60	10,699.40		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
339	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	Total		818.00 -	818.00	31.60		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(November 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
340	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
341	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	4.44	11/2019 -	11/2019
342	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	9.96	03/2020 -	03/2020
343	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	209.00	52.00	10/2019 -	10/2019
344	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	3.36	05/2020 -	05/2020
345	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020
346	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	85.71	06/2019 -	06/2019
347	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]	1/2018	206.58 -	206.58	0.02	03/2019 -	03/2019
	<u>Lucknow Metro Rail Corporation Limited</u>						
348	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
349	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	1,881.14	11/2021 -	11/2021
	<u>National Building Construcion Corporation Ltd</u>						
350	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,581.53	11/2019 -	11/2019
	Total		24,257.89 -	24,433.12	8,157.51		
	Grand Total		5,69,773.70	6,32,344.31	1,27,718.90		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

Costing Rs.150 Crore and above							
						(November 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
	Total		14,951.00 -	22,680.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
10	JAGANNATHPORA OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
11	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
12	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
	Total		19,342.27 -	20,637.06			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
13	CONSTRUCTION WORKS PHASE 4 - [N39000001	12/2016	167.69 168.00	170.37	05/2018 -	01/2019	1.60
14	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	291.29	08/2020 -	08/2020	1.87
	Total		453.64 -	461.66			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
16	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	-	13.31
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
18	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014	07/2016	312.99 -	322.00	08/2018 -	-	2.88
	Total		987.47 -	1,036.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
19	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
20	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33
	<u>Hindustan Petroleum Corporation Limited</u>						
21	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50
22	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
23	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
24	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
25	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	10/2018	45.67
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
27	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
28	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
29	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,577.15	05/2013 -	03/2019	83.01
30	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
31	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
32	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						
33	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47
34	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		19,129.74 -	24,806.72			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
35	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69
36	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
37	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
38	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
39	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	12/2018	86.27
40	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
41	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
42	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
43	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
44	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65
45	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
46	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
47	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
48	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
49	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	12/2016	7.41
	<u>North East Electric Power Corporation</u>						
50	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51
51	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
52	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59
53	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14
54	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
55	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88 -	12/2012 -	-	36.79
56	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41 -	04/2016 -	12/2018	38.61
57	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18 -	11/2016 -	06/2019	5.34
58	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42 -	03/2016 -	-	32.69
59	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28 -	02/2016 -	-	14.60
60	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	01/2015	268.80 -	340.88 -	03/2018 -	-	26.82
61	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03 -	07/2017 -	06/2019	27.92
62	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10 -	11/2012 -	-	36.01
63	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65 -	09/2014 -	-	39.30
64	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46 -	06/2014 -	12/2018	31.17
65	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02 -	08/2014 -	12/2018	79.61
66	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,534.00 -	11/2008 -	12/2018	42.42
67	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27 -	12/2015 -	-	26.86
68	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71 -	09/2017 -	-	30.49
69	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30 -	06/2019 -	06/2019	.02
70	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97 -	12/2018 -	12/2019	92.28
71	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57 -	12/2018 -	12/2019	30.15
72	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00 -	12/2015 -	12/2018	42.83
73	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]	08/2008	771.00 -	1,624.00 -	02/2013 -	-	110.64
	<u>Satluj Jal Vidyut Nigam Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
74	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68	602.44	12/2016	12/2018	37.96
	<u>Thdc India Limited</u>						
75	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42	294.60	02/2014	03/2019	50.75
76	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	4,105.30	06/2013	12/2021	64.77
77	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	4,401.90	02/2016	05/2021	165.65
	Total		1,77,202.39	2,42,540.13			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
78	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06	298.70	03/2019	03/2019	62.28
79	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50	3,712.50	03/2021	03/2021	63.44
80	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999	-	29.55
81	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00	5,341.68	03/2024	03/2024	120.28
82	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00	3,438.51	03/2024	03/2024	25.04
83	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00	2,081.27	03/2023	03/2023	10.94
	<u>Container Corporation Of India</u>						
84	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50	235.00	03/2019	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
85	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	-	143.17
86	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020	03/2020	207.99
	<u>East Central Railways</u>						
87	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07	3,020.94	-	03/2021	192.42
88	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65	2,066.77	-	03/2023	290.95
89	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012	03/2020	56.73
90	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73	1,156.41	03/2012	03/2020	256.11

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
91	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
92	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
93	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	-	323.32
94	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
95	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
96	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	- -	03/2021	296.21
97	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
98	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
99	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
100	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
101	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
102	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
103	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	- -	12/2018	192.15
104	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	- -	12/2021	71.96
	<u>East Coast Railway</u>						
105	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
106	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96
107	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43
108	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2020	.07
109	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
110	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	-	542.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
111	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
112	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	-	818.15
113	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	- -	03/2021	124.59
114	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	- -	03/2022	590.61
115	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
116	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2019	36.26
117	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	607.91	02/2013 -	-	.14
118	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.59	02/2012 -	-	105.61
119	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	-	44.46
120	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242]	04/2003	337.96 -	355.44	- -	-	5.17
121	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	665.75	02/2012 -	-	33.16
122	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL [N22000244]	04/2009	257.42 -	258.73	03/2014 -	-	.51
123	MONIGRAM- NIMITTA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
124	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
125	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	193.08 -	612.45	12/2011 -	-	217.20
126	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	544.72	03/2006 -	-	33.84
127	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	-	51.19
128	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
129	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]	04/2010	174.56 -	175.99	- -	-	.82
	<u>Metropolitan Rapid Transport Projects</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
130	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
131	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
132	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
133	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
134	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
135	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
136	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
137	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
	<u>North East Frontier Railway</u>						
138	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
139	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
140	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56
141	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	3,230.02 -	5,820.00	04/2008 12/2011	06/2018	80.18
142	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59
143	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
144	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
145	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
146	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
147	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	1,142.00 -	3,374.00	03/2014 -	03/2019	195.45
148	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	03/2020	7.86

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
149	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69 -	12/2015 -	03/2020	204.95
150	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00 -	- -	03/2020	71.62
151	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,733.20 -	03/2007 -	04/2016	93.65
152	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00 -	03/2020 -	10/2022	14.11
153	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	451.00 -	03/2019 -	03/2019	59.05
154	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00 -	03/2021 -	03/2021	561.92
155	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00 -	03/2020 -	03/2020	94.45
156	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28 -	- -	-	63.25
157	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00 -	03/2020 -	03/2020	59.34
158	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00 -	- -	-	128.39
159	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00 -	03/2019 -	03/2019	75.48
160	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93 -	03/2019 -	03/2019	62.12
161	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00 -	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
162	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56 -	06/2018 -	10/2018	89.54
163	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40 -	- -	-	60.34
164	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08 -	12/2022 -	05/2019	234.77
165	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79 -	- -	-	51.31
166	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73 -	- -	-	8.10
167	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00 -	- -	-	.33
168	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00 -	12/2021 -	-	267.13
169	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	435.00 -	- -	03/2018	122.35

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
170	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	08/2018	35.17
171	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	02/2019	61.80
172	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
173	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
174	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16
175	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	12/2018	196.84
176	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
177	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	03/2019	70.85
178	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	02/2019	93.87
179	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	03/2020	14.33
180	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
181	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55
182	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2019	41.64
183	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97	- -	-	38.23
184	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2018	24.47
185	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
186	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
187	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35
188	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	12/2018	19.86
189	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	03/2019	44.16
	<u>Northern Railway</u>						
190	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
191	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
192	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	12/2011 -	-	117.77
193	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
194	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
195	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
196	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96
197	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
198	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
199	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
200	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
201	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	06/2019	55.57
202	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	188.58
203	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,850.00	03/2008 -	03/2020	152.45
204	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
205	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
206	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70
207	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
208	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
209	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
210	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
211	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
212	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48	1,750.00	03/2020	03/2020	145.28
213	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04	970.00	03/2020	03/2020	2.32
	<u>Railway Electrification</u>						
214	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10	275.08	03/2012	-	60.77
	<u>South Central Railway</u>						
215	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20	2,120.16	03/2009	03/2023	102.85
216	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00	2,911.84	-	-	161.86
217	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95	2,200.00	03/2023	03/2024	18.47
218	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23	1,787.00	-	-	93.56
219	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00	1,599.39	-	-	92.93
220	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36	1,050.00	02/2009	-	538.84
221	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25	458.26	-	-	.00
222	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43	1,025.00	-	03/2017	723.76
223	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022	03/2022	54.49
	<u>South East Central Railway</u>						
224	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	1,101.16	-	-	186.92
225	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86	1,756.00	04/2020	04/2020	243.06
226	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51	2,686.63	03/2023	03/2023	40.77
227	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93	1,420.39	02/2019	02/2019	142.42
228	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	403.00	12/2021	12/2021	75.98
229	CHHINDWARA-MANDLA FORT GC - [N22000481]	03/2011	556.54	1,342.46	03/2012	03/2020	141.22
230	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00	1,279.00	12/2019	12/2019	46.67

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
231	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,919.00 -	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
232	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00 -	- -	12/2024	114.37
233	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00 -	- -	03/2030	53.96
234	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00 -	03/2007 03/2007	-	160.76
235	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69 -	06/2005 -	-	155.02
236	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00 -	12/2016 -	12/2018	153.41
237	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00 -	- -	03/2025	131.89
238	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00 -	03/2015 -	03/2024	54.99
239	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00 -	- -	-	162.39
240	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00 -	03/2015 -	-	53.44
241	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81 -	12/2015 -	12/2018	69.92
242	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00 -	- -	12/2018	41.36
243	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88 -	- -	-	278.13
244	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,151.81 -	03/2020 -	06/2020	18.76
245	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00 -	12/2021 -	12/2021	40.90
246	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00 -	12/2021 -	12/2024	79.05
247	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00 -	03/2003 -	03/2030	130.97
248	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	04/1998	1,027.40 -	2,373.00 -	03/2022 -	03/2022	130.97
	<u>South Western Railway</u>						
249	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91 -	- -	12/2023	651.97
250	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43 -	- -	12/2023	24.09

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
251	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
252	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
253	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
254	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
255	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
256	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
257	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
258	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2019	185.98
259	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
260	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
261	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
262	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
263	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	02/2019	627.74
264	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
265	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
266	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
267	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
268	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
269	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
270	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
271	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	369.83	- -	-	92.90
272	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	03/2019	1,391.30
273	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
274	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	302.02	03/2005 -	-	12.33
275	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
276	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55 -	330.32	03/2009 -	-	65.53
277	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
278	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
279	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
280	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
<u>Western Railway</u>							
281	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
282	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
283	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,69,908.33 -	3,95,407.52			
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
<u>Ministry Of Road Transport And Highways</u>							
284	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
285	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
286	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	-	.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
287	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	-	.11
288	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	-	.04
289	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	-	.06
290	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	-	.02
291	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	-	.30
292	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	11/2019 -	11/2019	.17
293	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06
294	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
295	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
296	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
297	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
298	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
299	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
300	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99
301	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
302	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
303	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
304	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58
305	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
306	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
307	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
308	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
309	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83
310	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_ NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
311	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
312	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
313	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
314	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
315	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
316	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
317	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
318	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
319	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
320	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
321	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
322	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
323	SIX LAINING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
324	SIX LAINING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
325	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
326	TWO LAINING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
327	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
328	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
329	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24
330	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	31.78
331	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	-	10.82
332	TWO LAINING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		29,654.32 -	44,654.88			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
333	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
	<u>Mumbai Port Trust</u>						
334	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
335	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
336	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	-	42.39
	Total		343.00 -	488.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
337	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
338	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	04/2014	332.72 -	342.00	09/2016 -	-	2.79
339	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
340	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
341	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	<u>Chennai Metro Rail Ltd</u>						
342	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
343	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
344	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
345	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
346	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>National Building Construction Corporation Ltd</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
347	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		22,323.08 -	27,919.21			
	Grand Total		4,70,620.53	8,11,319.47			

Details of Delayed Projects w.r.t. Original Schedule

Annexure – VI

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044] BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,100.00	5,687.52	09/2010 -	03/2019	102	74.68	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010] NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	12,707.00	12/2015 11/2016	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027] NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,937.00	12/2016 03/2017	12/2020	48	0	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028] NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	10,632.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	74,849.00	38,963.52					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073] AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
	Total		314.61 -	441.33	85.79					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
6	MOONIDIH XV SEAM UG - [N06000098] BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	325.14	04/2015 -	04/2019	48	0	
	<u>Central Coal Fields Limited</u>									
7	NORTH URIMARI OCP (3.0 MTY) - [N06000084] CCL, JHARKHAND	12/2007	179.87 -	179.87	174.69	03/2012 -	03/2019	84	0	
8	TAPIN OCP (2.5 MTY) - [N06000086] CCL, JHARKHAND	08/2008	264.68 -	264.68	176.72	03/2012 -	03/2019	84	0	
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087] CCL, JHARKHAND	12/2009	510.85 -	510.85	340.06	03/2016 -	03/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
10	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.21	03/2014 -	03/2019	60	0	
11	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	103.27	03/2011 -	03/2020	108	0	
12	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	184.20	07/2012 -	03/2021	104	0	
	<u>Eastern Coal Fields Limited</u>									
13	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	382.14	03/2018 -	03/2020	24	0	1. Rehabilitation of PAFs- Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	<u>Mahanadi Coal Fields Limited</u>									
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	387.94	03/2017 -	03/2020	36	0	
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	583.96	03/2013 -	03/2020	84	0	
16	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	266.97	03/2010 -	03/2020	120	0	
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	251.75	03/2013 -	03/2020	84	0	
18	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	27.48	03/2018 -	03/2020	24	0	
19	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	234.29	03/2012 -	03/2021	108	0	
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	60.36	03/2019 -	03/2021	24	0	
21	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	116.85	03/2019 -	03/2024	60	0	
	<u>Neyveli Lignite Corporation</u>									
22	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,770.46	12/2015 12/2018	03/2019	39	0	
23	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	391.20	06/2015 09/2019	09/2019	51	-51.37	
	<u>Northern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
24	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	572.40	03/2018 -	03/2019	12	0	
	<u>Singareni Colliers Company Limited</u>									
25	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48	0	
26	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45	0	
27	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36	-3.5	
28	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
29	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44	-7.91	
30	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72	-32.3	
31	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72	114.6	
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72	-2.14	
33	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	16.86	
34	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	186.91	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
35	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.50	03/2016 -	03/2019	36	0	
36	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	163.85	03/2016 -	03/2019	36	0	
37	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	172.27	03/2015 03/2020	03/2020	60	201.44	
38	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
39	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50	321.50	202.68	03/2014	03/2020	72	0	
	<u>Western Coal Fields Limited</u>									
40	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65	313.34	6.12	03/2021	03/2024	36	12.85	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
	Total		20,438.89	20,353.64	12,856.30					
	<u>FERTILISERS</u>									
41	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85	482.85	413.00	12/2017	12/2018	12	0	
42	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79	209.44	126.30	11/2016	04/2019	29	5.89	
	Total		680.64	692.29	539.30					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
43	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00	15,525.00	14,485.63	05/2015	06/2019	49	0	
	<u>Rastriya Ispat Nigam Limited</u>									
44	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85	465.85	244.25	07/2018	01/2019	6	0	No
45	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66	320.66	115.36	08/2018	02/2019	6	0	No
46	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85	1,682.85	802.10	09/2018	03/2019	6	0	No
47	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00	2,500.00	1,013.76	12/2017	09/2019	21	-12.53	No

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
48	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	239.65	10/2016 -	03/2019	29	42.39	No
	<u>Steel Authority Of India Limited (SAIL)</u>									
49	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,509.89	04/2018 -	05/2019	13	0	
50	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	855.62	12/2017 -	06/2019	18	0	
51	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	362.48	10/2017 -	06/2020	32	0	
52	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	76.61	06/2019 -	06/2020	12	0	
	Total		26,773.72 -	26,561.12	20,705.35					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
53	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 1,097.54	694.00	507.96	10/2018 12/2018	12/2018	2	0	
54	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	2,420.04	08/2018 05/2019	05/2019	9	14.33	
55	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	360.27	02/2020 10/2020	10/2020	8	-73	
	<u>Gas Authority Of India Limited</u>									
56	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	110.98	04/2018 -	12/2018	8	-38.98	
57	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 3,030.00	2,915.00	1,965.67	12/2012 02/2019	06/2019	78	0	
	<u>Hindustan Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
58	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	586.10	10/2014 02/2019	02/2019	52	133.5	
	<u>Indian Oil Corporation Limited</u>									
59	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,443.76	09/2017 12/2018	12/2018	15	0	
60	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	341.79	10/2017 -	03/2019	17	17.66	
61	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	169.70	07/2018 10/2020	10/2020	27	0	
62	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	4,497.00	302.17	12/2018 -	12/2020	24	0	
63	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	1.18	10/2020 -	05/2021	7	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
64	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,504.61	2,119.15	05/2017 12/2018	12/2018	19	-13.63	
65	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 207.80	207.80	27.54	09/2018 02/2019	02/2019	5	-50.61	
66	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,107.69	03/2013 03/2019	03/2019	72	-3.5	
67	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,577.15	1,577.15	1,195.62	05/2013 03/2019	03/2019	70	83.01	
68	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 4,619.94	4,619.94	3,931.91	12/2017 03/2019	03/2019	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
69	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	172.79	03/2019 -	04/2019	1	0	
70	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,102.45	04/2018 05/2019	05/2019	13	1.77	
71	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,449.66	05/2019 10/2019	10/2019	5	-4.01	
72	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	60.44	01/2014 11/2019	11/2019	70	62.78	
73	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 12/2019	12/2019	57	29.42	
74	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	1,687.43	03/2019 05/2020	05/2020	14	0	
75	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	1,450.26	06/2020 08/2021	08/2021	14	0	
	<u>Oil India Limited</u>									
76	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	196.39	03/2017 06/2019	06/2019	27	24.47	
77	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
	Total		82,289.24 -	83,969.10	30,555.43					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
78	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	982.71	04/2020 -	10/2023	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>National Hydro-Electric Power Corporation</u>									
79	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,394.80	7,121.50	09/2009 -	12/2021	147	139.69	
	<u>National Thermal Power Corporation</u>									
80	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,186.04	09/2011 06/2018	12/2018	87	86.27	
81	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,911.13	11/2016 03/2019	03/2019	28	0	
82	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 -	05/2019	60	49.41	
83	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	10,490.56	06/2017 06/2019	06/2019	24	7.55	
84	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	9,958.55	09/2017 06/2019	06/2019	21	10.55	
85	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	8,122.05	08/2018 06/2019	06/2019	10	9.64	
86	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,789.00	12/2016 -	08/2019	32	0	
87	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	5,195.95	03/2019 09/2019	09/2019	6	0	
88	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	12,079.00	01/2018 -	05/2020	28	5.91	
89	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	7,673.86	02/2019 10/2020	10/2020	20	5.55	
90	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	2,701.10	07/2020 10/2020	10/2020	3	0	
91	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,690.33	03/2013 12/2020	12/2020	93	29.14	
92	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	15,031.14	01/2011 04/2021	04/2021	123	73.65	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
93	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	376.58	09/2019 02/2022	02/2022	29	0	
	<u>North East Electric Power Corporation</u>									
94	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,838.94	12/2009 03/2019	03/2019	111	147.51	
	<u>Power Grid Corporation Of India Limited</u>									
95	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL, MULTI STATE	02/2010	2,144.00 -	2,932.88	2,654.96	12/2012 -	11/2018	71	36.79	
96	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL, MULTI STATE	03/2013	2,514.88 -	3,190.27	2,281.28	12/2015 -	11/2018	35	26.86	
97	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE	03/2014	155.57 -	206.42	145.22	03/2016 -	11/2018	32	32.69	
98	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL, MULTI STATE	02/2014	196.58 -	225.28	148.92	02/2016 -	11/2018	33	14.6	
99	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL, MULTI STATE	01/2015	268.80 -	340.88	229.40	03/2018 -	11/2018	8	26.82	
100	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24 -	1,071.24	630.56	09/2017 -	11/2018	14	0	
101	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	307.18	206.21	11/2017 -	11/2018	12	0	
102	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 -	305.04	215.81	03/2017 -	11/2018	20	0	
103	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU	05/2005	1,779.29 -	2,534.00	2,051.63	11/2008 -	12/2018	121	42.42	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
104	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	738.48	669.46	09/2010 -	12/2018	99	54.59	
105	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	499.90	06/2014 -	12/2018	54	31.17	
106	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	534.02	426.98	08/2014 -	12/2018	52	79.61	
107	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,202.20	04/2016 -	12/2018	32	38.61	
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	419.63	06/2016 -	12/2018	30	0	
109	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITION - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	74.71	03/2018 -	12/2018	9	0	
110	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,518.90	04/2018 -	12/2018	8	0	
111	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	1,420.89	07/2018 -	12/2018	5	0	
112	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	287.99	161.82	06/2018 -	12/2018	6	0	
113	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	1,364.00	1,237.00	12/2015 -	12/2018	36	42.83	
114	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	1,750.00	1,324.00	06/2018 -	12/2018	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,538.37	10/2012 -	02/2019	76	5.14	
116	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	2,716.40	03/2018 -	03/2019	12	0	
117	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	332.96	01/2018 -	03/2019	14	0	
118	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	139.34	01/2019 -	03/2019	2	0	
119	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	550.18	433.43	11/2016 -	06/2019	31	5.34	
120	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	181.16	07/2017 -	06/2019	23	27.92	
121	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	191.64	05/2017 -	06/2019	25	0	
122	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	52.14	09/2018 -	06/2019	9	0	
123	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	407.22	10/2017 -	09/2019	23	0	
124	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	238.92	04/2018 -	11/2019	19	0	
125	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	840.87	12/2018 -	12/2019	12	92.28	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
126	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,652.57	802.18	12/2018 -	12/2019	12	30.15	
127	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	.80	09/2019 -	02/2020	5	0	
128	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	13,762.80	12,714.20	08/2013 -	03/2022	103	23.65	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
129	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	506.97	12/2016 -	12/2018	24	37.96	
130	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	309.64	11/2017 -	12/2018	13	0	
	<u>Thdc India Limited</u>									
131	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	215.93	02/2014 02/2018	03/2019	61	50.75	IInd stage forest clearance of 1.39 Ha. land for compensatory afforestation in lieu of 1.39 Ha. forest land for power evacuation is pending.
132	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,672.04	02/2016 12/2020	05/2021	63	165.65	Decision on renewal of 3.0 Ha land and compensatory afforestation of identified 10 Ha. land is to be expedited.
133	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,105.30	1,583.40	06/2013 -	12/2021	102	64.77	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Regular support of Distt. Administration is required.
	Total		2,01,764.40 -	2,46,979.62	1,69,674.25					
	<u>HEAVY INDUSTRY</u>									
	<u>Indira Gandhi Centre For Atomic Research</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
134	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37	0	
	Total		1,554.00 -	1,554.00	161.86					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Hospital Services Consultancy Corporation Ltd</u>									
135	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	58.52	02/2018 -	12/2018	10	0	
136	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	71.00	05/2018 -	08/2019	15	0	
	Total		516.94 -	516.94	129.52					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
137	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	1,035.16	18.99	03/2022 -	03/2023	12	0	
	<u>Container Corporation Of India</u>									
138	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	139.04	03/2019 -	08/2019	5	0	
139	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	410.89	03/2018 -	12/2019	21	0	
140	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	289.08	03/2019 -	12/2019	9	0	
141	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	2.98	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
142	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	15.79	03/2019 -	12/2019	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
143	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96	256.11	
144	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	56.73	
145	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	0	
146	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	256.36	03/2020 -	03/2021	12	0	
147	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	468.48	
148	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	0	
149	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	0	
150	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	63.37	
151	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	62.06	
	<u>East Coast Railway</u>									
152	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	765.60	02/2019 -	03/2021	25	38.43	
153	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	81.26	10/2020 -	03/2021	5	0	
154	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28	15.45	
155	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27	0	
156	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147	29.96	
157	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	574.98	06/2021 -	03/2023	21	137.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Railways</u>									
158	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	1,125.89	2,007.32	03/2016 -	03/2020	48	0	Acquisition by State Govt. is awaited
159	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.52	137.85	03/2016 -	03/2020	48	-3.88	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
	<u>Metropolitan Rapid Transport Projects</u>									
160	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 495.74	734.01	445.91	06/2013 03/2019	03/2019	69	48.06	
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	
162	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,329.00	03/2004 -	03/2020	192	259.68	
	<u>North East Frontier Railway</u>									
163	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	03/2019	123	157.59	
164	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019	60	195.45	
165	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	267.93	03/2019 -	03/2020	12	106.51	
166	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2020	108	210.02	
167	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020	12	297.72	
168	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2020	12	302.54	
169	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
170	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 2,393.48	4,968.00	2,318.33	03/2014 12/2020	12/2020	81	107.56	
171	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 2,446.57	3,000.00	655.38	03/2015 10/2021	10/2021	79	28.95	
172	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	14.11	
	<u>North Eastern Railway</u>									
173	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,805.26	04/1999 -	12/2018	236	196.84	
174	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	181.09	01/2019 -	02/2019	1	61.8	
175	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	.60	03/2014 -	04/2021	85	-12.65	
176	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	.55	04/2016 -	01/2022	69	.16	
177	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
178	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
179	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	22.53	04/2017 -	10/2022	66	-31.45	
	<u>North Western Railway</u>									
180	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	346.35	295.70	11/2018 -	12/2018	1	19.86	
181	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	1,116.00	795.27	03/2014 03/2019	03/2019	60	70.85	
182	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	349.00	278.89	02/2019 -	03/2019	1	44.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
183	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	712.13	03/2015 -	03/2020	60	46.55	
	<u>Northern Railway</u>									
184	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	16,834.42	11/2002 03/2021	03/2021	220	1017.96	
	<u>Rail Vikas Nigam Ltd.</u>									
185	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	373.73	03/2009 03/2009	12/2018	117	188.58	
186	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,367.66	12/2017 -	06/2019	18	55.57	
187	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	383.54 -	555.00	575.93	03/2010 -	12/2019	117	44.7	
188	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	1,850.00	1,972.23	03/2008 -	03/2020	144	152.45	
189	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	977.00	978.21	03/2019 -	03/2020	12	5.39	
190	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	595.33	03/2016 03/2017	12/2020	57	29.06	
191	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	942.95	887.88	03/2019 -	03/2021	24	0	
192	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	894.91	12/2020 -	03/2021	3	0	
193	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 245.00	1,202.70	631.11	02/2015 -	12/2021	82	0	
194	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	631.78 632.00	1,195.00	653.64	12/2012 -	03/2022	111	89.15	
195	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	931.68	03/2020 -	03/2022	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
196	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	943.60	122.70	03/2022 -	12/2024	33	0	
197	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	335.37	03/2023 -	12/2024	21	0	
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,866.83	03/2016 -	03/2025	108	7.78	
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	768.02	03/2016 -	03/2025	108	0	
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	
201	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,081.06	12/2024 -	03/2026	15	0	
	<u>South Central Railway</u>									
202	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	645.00	725.63	03/2000 03/2019	03/2019	228	-62.57	
203	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.47	111.36	03/2010 03/2022	03/2022	144	0	
204	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	375.28	03/2021 03/2022	03/2022	12	0	
205	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	289.91	03/2009 03/2023	03/2023	168	102.85	
206	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	216.07	03/2014 03/2023	03/2023	108	0	
207	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	124.49	03/2022 03/2023	03/2023	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
208	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 1,856.95	2,200.00	227.19	03/2023 03/2024	03/2024	12	18.47	
	<u>South East Central Railway</u>									
209	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	141.22	
	<u>South Eastern Railway</u>									
210	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	525.81	495.14	12/2015 12/2018	12/2018	36	69.92	
211	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	152.45	12/2016 08/2018	12/2018	24	153.41	
212	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,151.81	375.59	03/2020 03/2020	06/2020	3	18.76	
213	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	175.49	03/2021 03/2021	12/2021	9	0	
214	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108	54.99	
215	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024	36	79.05	
216	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	484.85	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
217	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	433.36	03/2017 -	03/2020	36	37.96	
218	HUBLI- CHIKAJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,156.94	1,156.94	680.39	03/2020 03/2020	03/2021	12	0	
219	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,614.59	1,614.59	696.73	03/2019 03/2021	03/2021	24	0	
220	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	285.06	03/2016 12/2023	12/2023	93	0	
221	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	8.66	03/2016 12/2023	12/2023	93	0	
222	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
223	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96	0	
224	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	27.34	12/2018 12/2024	12/2024	72	0	
	<u>Southern Railway</u>									
225	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71	23.72	
226	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
227	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	0	
228	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	<u>Western Railway</u>									
229	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	83.53	03/2012 -	03/2019	84	1.06	
230	RAJKOT-VERAVAL,WANSJALIA TO JATASAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	858.96	549.56	03/2019 03/2019	03/2022	36	167.87	
	Total		1,20,697.25 -	1,96,761.58	73,988.75					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
231	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
232	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
233	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
234	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
235	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
236	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	<u>National Highways Authority Of India</u>									
237	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67	2.65	
238	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27	0	
239	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	247.91	10/2018 -	11/2018	1	0	
240	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	174.34	214.88	03/2008 -	12/2018	129	-28.84	
241	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	884.12	02/2013 -	12/2018	70	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
242	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018	60	0	
243	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	975.23	07/2013 -	12/2018	65	0	
244	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	0	
245	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	0	
246	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	0	
247	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	564.35	11/2013 -	12/2018	61	0	
248	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	351.24	09/2017 -	12/2018	15	0	
249	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	53.70	03/2018 -	12/2018	9	0	
250	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	604.80	10/2017 -	12/2018	14	0	
251	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	54.89	06/2016 -	12/2018	30	0	
252	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,302.51	07/2017 -	12/2018	17	0	
253	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	12/2018	86	0	
254	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	12/2018	37	51.83	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
255	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	1,871.34	2,304.41	01/2018 -	12/2018	11	0	
256	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018	78	0	
257	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	400.35	04/2018 -	12/2018	8	0	
258	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	678.87	01/2014 -	01/2019	60	0	
259	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	167.98	198.82	05/2008 -	02/2019	129	4.99	
260	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	297.81	04/2008 -	03/2019	131	10.58	
261	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9	0	
262	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2019	79	0	
263	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,615.69	07/2015 -	03/2019	44	0	
264	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	0	
265	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	210.66	05/2018 -	03/2019	10	-12	
266	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	688.00	04/2018 -	03/2019	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
267	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	73.66	07/2018 -	03/2019	8	0	
268	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31	0	
269	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	934.46	104.98	03/2018 -	03/2019	12	0	
270	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36	0	
271	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	14.31	05/2018 -	03/2019	10	0	
272	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130	0	
273	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	360.84	389.08	04/2010 -	04/2019	108	65.82	
274	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29	0	
275	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	45.11	05/2018 -	04/2019	11	0	
276	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	194.09	05/2018 -	04/2019	11	0	
277	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	846.58	08/2018 -	04/2019	8	0	
278	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	31.96	12/2017 -	04/2019	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
279	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	21.80	06/2018 -	04/2019	10	0	
280	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	0	
281	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	895.57	11/2017 -	05/2019	18	0	
282	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12	0	
283	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	105.70	06/2018 -	05/2019	11	0	
284	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,871.89	11/2011 -	06/2019	91	106.5	
285	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,058.04	03/2013 -	06/2019	75	0	
286	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	831.33	07/2013 -	06/2019	71	0	
287	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	396.59	06/2014 -	06/2019	60	0	
288	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019	64	0	
289	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,410.94	09/2016 -	06/2019	33	21.9	
290	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
291	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	473.93	11/2016 -	06/2019	31	0	
292	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	25.84	05/2018 -	06/2019	13	0	
293	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	50.67	04/2018 -	06/2019	14	0	
294	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	180.17	08/2018 -	06/2019	10	0	
295	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	0	
296	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-11	
297	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	502.66	11/2018 -	07/2019	8	0	
298	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	22.02	03/2019 -	07/2019	4	0	
299	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	17.07	05/2019 -	08/2019	3	0	
300	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	0	
301	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	0	
302	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	65.48	12/2018 -	10/2019	10	0	
303	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	142.41	04/2019 -	10/2019	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
304	FOUR LANNING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	167.09	06/2019 -	11/2019	5	0	
305	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,580.02	04/2019 -	11/2019	7	0	
306	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	2.42	03/2019 -	11/2019	8	0	
307	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,141.90	03/2014 -	12/2019	69	0	
308	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	0	
309	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2019	68	0	
310	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	23.98	10/2017 -	01/2020	27	0	
311	FOUR LANNING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	57.86	04/2018 -	04/2020	24	0	
312	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	-	03/2020 -	04/2020	1	.23	
313	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	155.12	02/2020 -	05/2020	3	0	
314	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	303.24	03/2020 -	05/2020	2	3.4	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
315	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	0	
316	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2	13.97	
317	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	121.00	03/2020 -	06/2020	3	41.54	
318	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	325.34	03/2020 -	06/2020	3	44.39	
319	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	-	09/2017 -	06/2020	33	0	
320	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	0	
321	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	-	03/2020 -	08/2020	5	10.58	
322	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	289.99	03/2020 -	08/2020	5	5.56	
323	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	177.05	03/2020 -	08/2020	5	5.7	
324	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	211.17	06/2020 -	08/2020	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
325	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	9.12	03/2019 -	11/2020	20	0	
326	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	-	03/2020 -	11/2020	8	0	
327	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	86.58	03/2017 -	11/2020	44	1.06	
328	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	0	
329	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	-	06/2019 -	12/2020	18	0	
	<u>Public Works Dept Of State</u>									
330	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	231.56	09/2017 -	11/2018	14	36.24	
	Total		86,085.99 -	89,553.86	53,591.27					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
331	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-57.02	
	<u>Mumbai Port Trust</u>									
332	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	82.72	
	Total		966.39 -	927.36	412.57					
	<u>TELECOMMUNICATIONS</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>Bharat Sanchar Nigam Limited</u>									
333	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 -	159.30	60.27	04/2018 12/2018	12/2018	8	0	
334	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 -	167.68	32.44	04/2018 12/2018	12/2018	8	0	
335	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 214.10	214.10	33.46	05/2018 12/2018	12/2018	7	-56	
336	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 -	231.80	77.65	10/2018 12/2018	12/2018	2	0	
	<u>Department Of Telecommunication</u>									
337	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	
	Total		14,108.08 -	25,436.88	8,600.82					
	<u>URBAN DEVELOPMENT</u>									
	<u>Bangalore Metro Rail Corporation Limited</u>									
338	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
339	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	163.97	11/2014 -	02/2019	51	0	
340	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	146.31	08/2016 -	03/2019	31	0	
341	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	0	
342	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	391.23	05/2017 08/2018	03/2019	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
343	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	89.94	04/2018 -	07/2019	15	0	
344	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	127.86	04/2019 06/2019	09/2019	5	0	
345	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
346	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	540.42	197.12	07/2019 -	10/2019	3	-1.62	
347	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2019	56	0	
348	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	331.12	10/2019 -	03/2020	5	30.58	
349	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.28	03/2016 -	04/2020	49	0	
350	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	10.14	04/2019 06/2020	06/2020	14	0	
351	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	34.09	06/2017 07/2017	06/2020	36	.57	
352	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	29.78	02/2020 09/2020	09/2020	7	0	
353	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	4.00	07/2020 09/2018	09/2020	2	0	
	Hindustan Steelwork Construction Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above										
(November 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
354	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
355	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
356	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
357	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
358	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
359	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 8,680.00	8,680.00	4,631.87	03/2018 12/2019	12/2019	21	0	
	Total		70,169.58 -	70,688.03	9,644.68					
	<u>DEFENCE PRODUCTION</u>									
	<u>Goa Shipyard Limited</u>									
360	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA	12/2016	167.69 168.00	170.37	86.93	05/2018 01/2019	01/2019	8	1.6	
	Total		167.69 -	170.37	86.93					
	Grand Total		6,93,647.42	8,39,455.12	4,19,996.34					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

Costing Rs.150 Crore and above								
						Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69	102
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
	Total		14,951.00 -	22,680.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>Singareni Colliers Company Limited</u>							
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
7	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							
8	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
	Total		1,260.84 -	2,060.59				
	<u>DEFENCE PRODUCTION</u>							
	<u>Goa Shipyard Limited</u>							
9	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	170.37	05/2018 -	01/2019	1.60	8
	Total		167.69 -	170.37				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29
	Total		197.79 -	209.44				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
11	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33	9
	<u>Hindustan Petroleum Corporation Limited</u>							
12	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
13	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
	<u>Oil & Natural Gas Corporation Limited</u>							
14	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,577.15	05/2013 -	03/2019	83.01	70
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42	57
17	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77	13
	<u>Oil India Limited</u>							
18	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47	27
	Total		12,172.77 -	14,942.79				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
19	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69	147
	<u>National Thermal Power Corporation</u>							
20	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above								
(November 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
21	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41	60
22	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	12/2018	86.27	87
23	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
24	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
25	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91	28
26	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
27	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
28	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
	<u>North East Electric Power Corporation</u>							
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51	111
	<u>Power Grid Corporation Of India Limited</u>							
30	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	-	32.69	32
31	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	-	14.60	33
32	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92	23
33	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	-	26.82	8
34	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	12/2018	79.61	52
35	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34	31
36	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17	54
37	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59	99
38	TRANSMISSION SYSTEM ASSOCIATED WITH IPSPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	12/2018	42.83	36
39	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61	32
40	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,534.00	11/2008 -	12/2018	42.42	121

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above								
(November 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
41	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	-	36.79	71
42	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	-	26.86	35
43	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14	76
44	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15	12
45	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28	12
46	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
47	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96	24
	<u>Thdc India Limited</u>							
48	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75	61
49	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77	102
50	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65	63
	Total		1,33,131.92 -	1,78,347.14				
	<u>RAILWAYS</u>							
	<u>Container Corporation Of India</u>							
51	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73	96
53	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11	96
54	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
55	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
56	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48	61
	<u>East Coast Railway</u>							
57	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
58	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43	25
59	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
60	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96	147
	<u>Metropolitan Rapid Transport Projects</u>							
61	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06	69
62	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
63	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	<u>North East Frontier Railway</u>							
64	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
65	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11	31
66	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
67	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
68	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
69	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59	123
70	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,374.00	03/2014 -	03/2019	195.45	60
71	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
72	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56	81
73	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02	108
	<u>North Eastern Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
74	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16	69
75	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	02/2019	61.80	1
76	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	12/2018	196.84	236
	<u>North Western Railway</u>							
77	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	12/2018	19.86	1
78	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	03/2019	44.16	1
79	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	03/2019	70.85	60
80	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55	60
	<u>Northern Railway</u>							
81	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96	220
	<u>Rail Vikas Nigam Ltd.</u>							
82	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	188.58	117
83	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70	117
84	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
85	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39	12
86	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15	111
87	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	06/2019	55.57	18
88	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,850.00	03/2008 -	03/2020	152.45	144
89	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							
91	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168
92	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>South East Central Railway</u>							
93	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22	96
	<u>South Eastern Railway</u>							
94	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41	24
95	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	12/2018	69.92	36
96	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05	36
97	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99	108
98	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76	3
99	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
100	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96	36
	<u>Southern Railway</u>							
101	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72	71
	<u>West Central Railway</u>							
102	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
103	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
104	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
	Total		54,913.26 -	1,32,411.14				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
105	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above								
(November 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
106	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99	129
107	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58	131
108	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82	108
109	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
110	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
111	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
112	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
113	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
114	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54	3
115	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
116	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
117	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
118	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
119	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
120	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83	37
121	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
	<u>Public Works Dept Of State</u>							
122	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	14
	Total		14,567.07 -	18,106.92				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs.150 Crore and above								
(November 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>SHIPPING AND PORTS</u>							
	<u>Mumbai Port Trust</u>							
123	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		366.39 -	669.46				
	<u>STEEL</u>							
	<u>Rastriya Ispat Nigam Limited</u>							
124	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	-	42.39	29
	Total		343.00 -	488.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
125	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
126	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
127	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36
128	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	Total		1,829.65 -	2,356.99				
	Grand Total		2,47,549.99	3,97,548.57				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs.150 Crore and above					
				(November 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	05/2014 -	04/2018
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2018
3	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	10/2018
4	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
5	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	-
	<u>Mahanadi Coal Fields Limited</u>				
6	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	03/2010 -	03/2018
	<u>Northern Coal Fields Limited</u>				
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	03/2012 -	-
	<u>Singareni Colliers Company Limited</u>				
8	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
9	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	-
	<u>South-Eastern Coal Fields Limited</u>				
10	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	03/2018 -	03/2018
	<u>Western Coal Fields Limited</u>				
11	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018
	Total		3,842.14 -		
	<u>STEEL</u>				
	<u>Steel Authority Of India Limited (SAIL)</u>				
12	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
13	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		4,937.93 -		

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
14	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	<u>Chennai Petroleum Corporation Limited</u>				
15	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Gas Authority Of India Limited</u>				
16	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT	07/2014	199.95 -	03/2018 -	03/2018
	<u>Hindustan Petroleum Corporation Limited</u>				
17	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
18	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	09/2017 06/2018	06/2018
19	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	06/2018 -	10/2018
20	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
21	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 -	-
22	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-
23	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	- -	-
24	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	- -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
26	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	-
	<u>Oil India Limited</u>				
27	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		14,470.27 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Thermal Power Corporation</u>				
30	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016
31	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	01/2017 -	-
32	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
33	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
34	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
	<u>North East Electric Power Corporation</u>				
35	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	07/2013 -	-
	<u>Power Grid Corporation Of India Limited</u>				
36	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018
37	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	11/2012 -	10/2018
38	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	09/2014 -	10/2018
39	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	10/2018
40	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	10/2018 -	10/2018
41	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	10/2018
42	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	07/2018 -	10/2018
43	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE	08/2008	771.00 -	02/2013 -	10/2018
	Total		47,455.84 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
44	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation</u>				
45	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
46	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	-
47	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	-
48	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	-
49	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
50	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-
51	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
52	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	-
53	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	-
54	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	-
55	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	-
56	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA	07/2016	312.99 -	08/2018 -	-
57	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-
58	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	-
	Total		4,829.65 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
59	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Container Corporation Of India</u>				
60	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
61	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
62	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
63	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
64	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
65	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
66	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
67	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
68	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
69	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
70	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
71	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
72	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
73	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
74	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>East Coast Railway</u>				
75	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
76	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
77	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
	<u>Eastern Railways</u>				
78	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	06/2016
79	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
80	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 -	02/2012 -	-
81	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	193.08 -	12/2011 -	-
82	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	-
83	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
84	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
85	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
86	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	-
88	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	-
89	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
90	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-
91	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
92	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
93	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
94	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
95	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	-
96	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
97	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
98	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	-
99	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	-
100	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
101	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
102	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
103	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
104	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
105	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
107	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
108	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
109	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
110	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
111	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				
112	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	03/2018
113	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 4,118.00	03/2007 -	04/2016
114	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	3,230.02 4,857.00	04/2008 12/2011	06/2018
115	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	792.46 -	12/2010 -	-
116	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
	<u>North Eastern Railway</u>				
117	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018
118	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	08/2018
119	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	10/2018
120	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	- -	-
121	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
122	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
123	KAPILVASTU-BASTI VIA BANSI SIDHARTH NAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
124	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
125	GONDA - BAHRAICH (60 KMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-
126	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
127	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
128	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NR,MULTI STATE	03/2007	243.78 -	12/2021 -	-
	<u>North Western Railway</u>				
129	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2018
130	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
131	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
132	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
133	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
134	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
135	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
136	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-
138	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
139	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
140	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
141	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
142	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
143	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-
144	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
145	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
146	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
147	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
148	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
149	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
150	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
151	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-
152	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
153	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
154	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
155	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
156	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
157	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	10/2018
158	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017
159	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
160	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 2,911.84	- -	-
161	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
162	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
163	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
164	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
165	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
166	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
167	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00 -	09/2018 -	-
	<u>South Eastern Railway</u>				
168	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
169	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
170	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
171	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
172	ARA-BHABHUA ROAD (NL) - [N22000166]SR,BIHAR	04/2008	633.87 -	- -	-
	<u>Southern Railway</u>				
173	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018
174	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
175	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
176	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-
177	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
178	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
179	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
180	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
181	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
182	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
183	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
184	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
185	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 346.15	- -	-
186	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
187	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
188	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 342.85	- -	-
189	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
190	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
191	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
192	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-
193	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-
194	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
195	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
196	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-
197	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-
198	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-
199	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-
	<u>Western Railway</u>				
200	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
201	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
202	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
203	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
204	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
205	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		91,405.49 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
206	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
207	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
208	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
209	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
210	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
211	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
213	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
214	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
215	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
216	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
217	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
218	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
219	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
220	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
221	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
222	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
223	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
224	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
225	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
226	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
227	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
228	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
229	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
233	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
234	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
237	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-
238	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
239	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
240	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
241	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
242	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
243	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
244	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
245	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
246	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
247	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
248	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
249	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
250	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
251	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
252	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
253	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
254	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
255	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
256	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
257	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
258	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
259	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
260	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
261	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-
262	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-
263	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
264	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
265	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-
266	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-
267	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
268	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	-
269	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	-
270	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	06/2018 -	-
271	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-
272	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	-
273	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
274	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
275	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	-
276	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH	03/2015	235.08 -	05/2018 -	-
277	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
278	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
279	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	-
280	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
281	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
282	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	-
283	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
284	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
285	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
286	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
287	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
288	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
289	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
290	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
291	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
292	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
293	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
294	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
295	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
296	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
297	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
298	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
299	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
300	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
301	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
302	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
303	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
304	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
305	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
306	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
307	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-
309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	-
310	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
311	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
312	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
313	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
314	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
315	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
317	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
318	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
319	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
320	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
321	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
322	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
323	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
324	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA- NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
325	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	-
326	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
	<u>National Highways Authority Of India</u>				
327	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	07/2018
328	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	09/2018
329	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015
330	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	07/2018
331	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018
332	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	08/2018

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
333	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	08/2018
334	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	08/2018
335	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	09/2018
336	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	09/2018
337	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018
338	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	04/2009 -	10/2018
339	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	10/2018
340	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	-
341	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 -	-
342	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	-
343	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	-
344	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
345	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
346	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
347	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
348	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
349	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
350	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-
351	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	-
352	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
353	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-
354	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
355	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-
356	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
357	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	-
358	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	-
359	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
360	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
361	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-
362	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
363	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
364	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
365	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
366	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	-
367	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	-
368	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
369	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
370	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
371	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
372	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
373	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
374	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
375	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	-
376	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-
377	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	-
378	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
379	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
380	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
381	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
382	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
383	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-
384	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
385	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
386	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
387	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
388	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
389	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
390	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
391	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
392	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
393	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
394	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	-
395	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-
396	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
397	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
398	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
399	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
400	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
401	REHABILITATION AND UPGRADE TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
402	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
403	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
404	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
405	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-
406	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
407	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-
408	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
409	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
410	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
411	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
412	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
413	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
414	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
415	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
416	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
417	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-
418	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
419	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
420	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
421	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
422	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
423	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
424	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
425	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
426	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
427	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
428	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
429	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
430	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
431	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
432	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
433	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-
434	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
435	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-
436	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
437	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
438	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-
439	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
440	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
441	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-
442	REHABILITATION AND UPGRADE OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-
443	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	- -	-
444	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 -	- -	-
445	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
446	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-
447	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-
448	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU	02/2018	1,166.26 -	- -	-
449	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 -	- -	-
450	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI, KARNATAKA	02/2018	1,995.34 -	- -	-
451	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI, KARNATAKA	02/2018	2,177.80 -	- -	-
452	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	- -	-
453	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB	02/2018	261.76 -	- -	-
454	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI, UTTAR PRADESH	03/2018	809.07 -	- -	-
455	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI, UTTAR PRADESH	03/2018	925.40 -	- -	-
456	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	-
457	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
458	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI, UTTAR PRADESH	03/2018	1,117.84 -	- -	-
459	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
460	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	- -	-
461	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI, ANDHRA PRADESH	02/2018	1,959.00 -	- -	-
462	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI, UTTAR PRADESH	03/2018	1,120.57 -	- -	-
463	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- -	-
464	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	-
465	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	-
466	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
467	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI, UTTAR PRADESH	02/2018	972.77 -	- -	-
468	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI, ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
469	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI, ANDHRA PRADESH	03/2018	1,550.98 -	- -	-
470	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	- -	-
471	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI, ANDHRA PRADESH	03/2018	314.43 -	- -	-
472	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI, ANDHRA PRADESH	03/2018	557.30 -	- -	-
473	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-
474	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	- -	-
475	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	- -	-
476	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
477	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
478	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
479	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI, TAMIL NADU	03/2018	505.35 -	- -	-
480	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI, TAMIL NADU	03/2018	628.71 -	- -	-
481	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
482	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI, TAMIL NADU	03/2018	1,016.92 -	- -	-
483	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
484	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
485	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
486	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	- -	-
487	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
488	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- -	-
489	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-
490	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI, HARYANA	03/2018	307.79 -	- -	-
491	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
492	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- -	-
493	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
494	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-
495	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
496	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
497	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
498	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	-
499	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
500	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	-
501	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
502	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	-
503	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	-
504	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
505	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-
<u>National Highways Development Project</u>					
506	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	-
507	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
508	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
509	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
510	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	-
511	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-
512	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
513	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-
514	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
515	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
516	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
517	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-
518	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-
519	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-
520	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
521	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-
522	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-
523	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-
524	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
525	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-
526	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
527	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-
528	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-
529	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-
	<u>Public Works Dept Of State</u>				
530	REHABILITATION AND UPGRADE OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
531	REHABILITATION AND UPGRADE OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
532	YAN TO NIRMAL SEREHALITATION AND UPGRADE OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
533	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD, TELANGANA	01/2014	340.00 -	03/2016 -	-
534	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD, TELANGANA	01/2014	270.00 -	03/2016 -	-
535	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD, TELANGANA	10/2014	244.30 -	12/2016 -	-
536	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD, TELANGANA	10/2014	295.47 -	02/2017 -	-
537	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	-
538	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD, TELANGANA	03/2011	218.31 -	12/2015 -	-
539	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD, MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
540	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA	01/2014	267.16 352.00	11/2017 -	-
541	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD, ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	-
542	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-
543	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD, ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
544	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	-
545	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
546	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD, ANDHRA PRADESH	03/2015	175.03 -	- -	-
547	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD, ANDHRA PRADESH	02/2015	266.00 -	- -	-
548	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
549	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD, CHHATISGARH	10/2014	213.47 -	03/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
550	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
551	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
552	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
553	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
554	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
555	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	-
556	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
557	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
558	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
559	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
560	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
561	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
562	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	-
563	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	-
564	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-
565	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
566	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	-
567	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
568	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
569	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
570	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
571	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
572	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
573	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
574	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
575	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
576	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
577	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
578	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
579	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
580	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
581	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
582	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
583	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
584	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
585	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
586	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
587	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
588	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
589	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
590	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-
591	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
592	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
593	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
594	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-
595	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-
596	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-
597	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
598	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-
599	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
600	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
601	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
602	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
603	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
604	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-
605	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
606	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
607	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
608	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-
609	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
610	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
611	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
612	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
613	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
	Total		2,44,123.64 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
614	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	-
	<u>Port Trust</u>				
615	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
616	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
	Total		2,821.90 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
617	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
618	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
619	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	09/2018 -	09/2018
620	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	-
621	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
622	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
623	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-
624	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-
625	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-
626	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
	<u>Chennai Metro Rail Ltd</u>				
627	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
628	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
629	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
630	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
631	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
632	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
633	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
634	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
635	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
636	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
637	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
638	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
639	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
640	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
641	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Maharashtra Metro Rail Corporation Ltd.</u>				
642	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>National Building Construcion Corporation Ltd</u>				
643	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-
	Total		66,138.60 -		
	Grand Total		4,84,272.89		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs.150 Crore and above									
								(November 2018)	
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
1	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82	528.26	462.75	-	12/2018	-	0/0
2	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07	3,020.94	-	-	03/2021	-	0/0
3	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14	1,474.47	338.44	-	03/2021	-	0/0
4	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39	566.41	759.20	-	12/2021	-	0/0
5	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87	589.15	183.72	-	03/2022	-	0/0
6	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65	2,066.77	330.82	-	03/2023	-	0/0
7	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17	1,605.17	.19	-	03/2023	-	0/0
	<u>East Coast Railway</u>								
8	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00	729.92	253.10	-	03/2021	-	0/0
9	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56	2,614.36	111.71	-	03/2022	-	0/0
	<u>North Central Railway</u>								
10	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50	2,030.50	10.34	-	12/2022	-	0/0
	<u>North East Frontier Railway</u>								
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76	360.00	4.11	-	03/2020	-	0/0
12	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42	380.00	97.55	-	03/2020	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
13	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30	2,062.20	674.76	-	03/2022	-	0/2
	<u>South Eastern Railway</u>								
14	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20	365.00	184.85	-	12/2018	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	0(R3)	0/0
16	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	0(R3)	0/0
17	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	426.00	-	- 03/2030	03/2030	0(R3)	0/0
	<u>South Western Railway</u>								
18	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	1,190.92	190.63	- 03/2021	03/2021	0(R3)	0/0
19	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,801.01	12.54	- 12/2023	12/2023	0(R3)	0/0
20	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	1,350.91	913.65	- -	12/2023	-	0/1
21	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	692.43	-	- 12/2023	12/2023	0(R3)	0/0
22	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- 12/2023	12/2023	0(R3)	0/0
23	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- 12/2023	12/2023	0(R3)	0/0
24	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	0(R3)	0/0
25	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	0(R3)	0/0
26	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	2,135.00	144.75	- 12/2024	12/2024	0(R3)	0/0
	<u>Southern Railway</u>								
27	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	83.15	- -	03/2020	-	0/0
	<u>Western Railway</u>								
28	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WJR,GUJARAT	04/2011	844.10 -	844.10	61.85	- 03/2022	03/2022	12(R3)	0/0
	Total		19,643.41 -	30,254.29	4,860.72				0/3
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
29	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	795.76	131.52	- -	12/2018	-	0/0
30	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	794.30	117.99	- -	12/2018	-	0/0
31	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	195.21	- -	12/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
32	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	111.65	- -	12/2018	-	0/0
33	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	242.51	- -	12/2018	-	0/0
34	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	392.14	- -	03/2019	-	0/0
35	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	545.46	- -	03/2019	-	0/0
36	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	425.60	-	- -	03/2019	-	0/0
37	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	108.06	- -	04/2019	-	0/0
38	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	28.90	- -	04/2019	-	0/0
39	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	290.73	57.93	- -	05/2019	-	0/0
40	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	199.22	- -	08/2019	-	0/0
41	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	133.37	- -	08/2019	-	0/0
42	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	216.34	- -	09/2019	-	0/0
43	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	417.19	35.80	- -	09/2019	-	0/0
44	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	181.70	- -	10/2019	-	0/0
45	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	834.64	137.94	- -	10/2019	-	0/0
46	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
47	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	688.70	470.78	- -	11/2019	-	0/0
48	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	447.75	37.26	- -	11/2019	-	0/0
49	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	12/2019	-	0/0
50	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,167.45	28.96	- -	12/2019	-	0/0
51	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	364.56	76.83	- -	12/2019	-	0/0
52	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,100.19	610.00	- -	12/2019	-	0/0
53	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	814.04	229.41	- -	01/2020	-	0/0
54	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	60.20	- -	01/2020	-	0/0
55	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	196.05	21.93	- -	01/2020	-	0/0
56	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	122.72	- -	02/2020	-	0/0
57	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	297.13	- -	02/2020	-	0/0
58	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	85.00	- -	02/2020	-	0/0
59	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	50.71	- -	04/2020	-	0/0
60	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	1,169.61	481.60	- -	04/2020	-	0/0
61	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	475.69	- -	05/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	1,232.21	637.48	- -	05/2020	-	0/0
63	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	-	- -	07/2020	-	0/0
64	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	- -	07/2020	-	0/0
65	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-- [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
66	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	-	- -	09/2020	-	0/0
67	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	-	- -	10/2020	-	0/0
	Total		33,625.30 -	33,625.30	6,888.44				0/0
	Grand Total		53,268.71	63,879.59	11,749.16				0/3

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Antici Pated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
3	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>South-Eastern Coal Fields Limited</u>					
5	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH	05/2018	410.26 -	03/2026 -	03/2026	0/0
	<u>Western Coal Fields Limited</u>					
6	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
7	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
8	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
9	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	06/2019	0/0
10	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
11	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
12	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
13	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
14	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
15	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	12/2021 -	12/2021	0/0
16	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
17	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	181.20 -	07/2022 -	07/2022	0/0
18	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
19	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
20	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
21	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	06/2020 -	06/2020	0/0
22	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	06/2020 -	06/2020	0/0
23	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	04/2021	0/0
	<u>Indian Oil Corporation Limited</u>					
24	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	02/2020 -	02/2020	0/0
25	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	02/2020 -	02/2020	0/0
26	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	02/2020 -	02/2020	0/0
27	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
28	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	06/2020	0/0
29	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0
30	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT	08/2017	1,342.00 -	08/2020 -	08/2020	0/0
31	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	08/2020 -	08/2020	0/0
32	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	08/2020 -	08/2020	0/0
33	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	10/2020 -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
34	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
35	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
36	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
37	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
38	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
39	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL, BIHAR	07/2018	189.00 -	01/2021 -	01/2021	0/0
40	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
41	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
42	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL, BIHAR	04/2018	522.00 -	03/2021 -	03/2021	0/0
43	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2021	0/0
44	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	04/2021	0/0
45	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	10/2020 -	05/2021	0/0
46	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL, WEST BENGAL	03/2018	3,712.00 -	09/2022 -	06/2021	0/0
47	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL, ODISHA	04/2018	4,807.08 -	07/2021 -	07/2021	0/0
48	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH	08/2017	318.80 -	08/2021 -	08/2021	0/0
49	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL, ODISHA	08/2017	315.00 -	12/2021 -	12/2021	0/0
50	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL, UTTAR PRADESH	03/2018	676.00 -	12/2021 -	12/2021	0/0
51	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL, ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	04/2022	0/0
52	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT	10/2014	279.00 -	08/2018 -	-	0/0
<u>Indian Strategic Petroleum Reserves Ltd</u>						
53	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
<u>Mangalore Refinery And Petrochemicals Limited</u>						
54	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN, KARNATAKA	11/2017	581.00 -	03/2020 -	03/2020	0/0
<u>Oil India Limited</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
55	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
56	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
57	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	10/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
58	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					
59	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016	0/0
60	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
	<u>Power Grid Corporation Of India Limited</u>					
61	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
62	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	10/2018	0/0
63	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0
64	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	10/2018	0/0
65	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	07/2018 -	10/2018	0/0
66	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE	08/2008	771.00 -	02/2013 -	10/2018	0/0
67	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	11/2018	0/0
68	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2018	0/0
69	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 -	11/2018	0/0
70	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
71	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
72	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	12/2018	0/0
73	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
74	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	12/2018	0/0
75	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
76	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	12/2015 -	12/2018	0/0
77	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	12/2018	0/0
78	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
79	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
80	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
81	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
82	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
83	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 -	03/2019	0/0
84	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
85	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
86	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	03/2019	0/0
87	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
88	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
89	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
90	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
91	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
92	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
93	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
94	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
95	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
96	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
97	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 -	06/2019	0/0
98	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0
99	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL, MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
100	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 -	11/2019	0/0
101	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
102	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
103	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
104	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL, MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
105	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
106	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL, MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
107	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
108	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 -	02/2020	0/0
109	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
110	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
111	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Indira Gandhi Centre For Atomic Research</u>					
112	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR, DELHI	08/2016	1,554.00 -	08/2016 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
113	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES, UTTAR PRADESH	07/2016	785.00 -	04/2020 -	04/2020	0/0
114	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES, PUNJAB	07/2016	703.00 -	06/2020 -	06/2020	0/0
115	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES, ASSAM	05/2017	875.00 -	05/2021 -	05/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
116	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
117	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	-	0/0
118	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	-	0/0
119	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	-	0/0
120	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	-	0/0
121	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
122	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0
123	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0
124	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	08/2019	0/0
125	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0
126	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
127	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-	0/0
128	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
129	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 -	03/2019	0/0
130	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 2,271.50	03/2021 -	03/2021	0/0
131	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 792.89	03/2021 -	03/2021	0/0
132	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 540.02	03/2022 -	03/2022	0/0
133	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 1,272.19	03/2022 -	03/2022	0/0
134	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 3,168.29	03/2023 -	03/2023	0/0
135	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 2,449.91	03/2023 -	03/2023	0/0
136	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
137	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	03/2022 -	03/2023	0/0
138	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 637.95	03/2023 -	03/2023	0/0
139	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
140	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
141	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
142	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.47	03/2024 -	03/2024	0/0
143	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
	<u>Container Corporation Of India</u>					
144	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
145	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
146	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	08/2019	0/0
147	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	12/2019	0/0
148	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
149	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
150	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
151	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
152	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
153	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
154	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	12/2018	0/0
155	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
156	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	03/2012 -	03/2020	0/0
157	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
158	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	03/2012 -	03/2020	0/0
159	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2020	0/0
160	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
161	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 -	- -	03/2021	0/0
162	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	03/2021	0/0
163	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
164	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	02/2016 -	03/2021	0/0
165	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	- -	12/2021	0/0
166	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	03/2022	0/0
167	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2022	0/0
168	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	03/2021 -	03/2022	0/0
169	HAJIPUR-SAGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
170	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
171	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
172	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
173	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
174	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
175	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
176	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
177	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
178	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
179	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
180	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
181	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
182	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
	<u>East Coast Railway</u>					
183	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
184	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
185	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
186	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 -	03/2021	0/0
187	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 -	03/2021	0/0
188	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2021	0/0
189	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2021	0/0
190	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	06/2021	0/0
191	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
192	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 -	03/2022	0/0
193	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2022 -	03/2022	0/0
194	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 -	03/2022	0/0
195	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 -	03/2023	0/0
196	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
197	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
198	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
	<u>Eastern Railways</u>					
199	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	06/2016	0/0
200	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	11/2018	0/0
201	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2019	0/0
202	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	03/2016 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
203	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2020	0/0
204	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
205	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2022	0/0
206	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	02/2012 -	-	0/0
207	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	193.08 -	12/2011 -	-	0/0
208	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	-	0/0
209	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
210	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
211	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
212	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
213	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	-	0/0
214	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	-	0/0
215	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
216	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-	0/0
217	BARIAPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
218	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
219	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
220	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
221	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	-	0/0
222	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
223	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
224	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	-	0/0
225	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
226	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
227	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
228	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
229	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
230	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
231	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
232	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
233	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
234	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
235	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0
236	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
237	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	03/2021 -	03/2021	0/0
238	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	03/2022 -	03/2022	0/0
239	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	12/2022	0/0
240	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
241	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
242	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
243	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
	<u>North East Frontier Railway</u>					
244	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	03/2018	0/0
245	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 4,118.00	03/2007 -	04/2016	0/0
246	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	3,230.02 4,857.00	04/2008 12/2011	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
247	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 -	12/2008 -	03/2019	0/0
248	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	1,142.00 1,942.00	03/2014 12/2019	03/2019	0/0
249	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019	0/0
250	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	03/2019 -	03/2019	0/0
251	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 -	03/2019 -	03/2019	0/0
252	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	03/2019 -	03/2019	0/0
253	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0
254	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	03/2020	0/0
255	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2020	0/0
256	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 -	03/2019 -	03/2020	0/0
257	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	03/2020	0/0
258	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
259	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
260	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
261	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
262	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
263	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
264	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
265	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 2,393.48	03/2014 12/2020	12/2020	0/0
266	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
267	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
268	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 2,446.57	03/2015 10/2021	10/2021	0/0
269	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	792.46 -	12/2010 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
270	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
	<u>North Eastern Railway</u>					
271	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
272	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	08/2018	0/0
273	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	10/2018	0/0
274	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	04/1999 -	12/2018	0/0
275	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2019	0/0
276	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	02/2019	0/0
277	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	05/2019	0/0
278	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	03/2014 -	04/2021	0/0
279	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	01/2022	0/0
280	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
281	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2022	0/0
282	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
283	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
284	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	10/2022	0/0
285	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
286	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
287	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
288	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
289	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-	0/0
290	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
291	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
292	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>North Western Railway</u>					
293	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2018	0/0
294	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	11/2018 -	12/2018	0/0
295	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	02/2019	0/0
296	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 03/2019	03/2019	0/0
297	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	03/2019	0/0
298	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2019	0/0
299	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	11/2019	0/0
300	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 295.02	03/2020 -	12/2019	0/0
301	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2020	0/0
302	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	03/2020	0/0
303	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	08/2022	0/0
304	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
305	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
306	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 03/2021	03/2021	0/0
307	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
308	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
309	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
310	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
311	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-	0/0
312	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
313	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
314	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
316	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
317	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-	0/0
318	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
319	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
320	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
321	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
322	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
323	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
324	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
325	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-	0/0
326	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
327	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
328	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-	0/0
<u>National High Speed Rail Corporation Limited</u>						
329	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
<u>Rail India Technical And Economic Service</u>						
330	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
<u>Rail Vikas Nigam Ltd.</u>						
331	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	06/2019	0/0
332	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	03/2008 -	03/2020	0/0
333	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
334	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
335	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
336	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	03/2020 -	03/2020	0/0
337	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	03/2016 03/2017	12/2020	0/0
338	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
339	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
340	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
341	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
342	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 245.00	02/2015 -	12/2021	0/0
343	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
344	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
345	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	631.78 632.00	12/2012 -	03/2022	0/0
346	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
347	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
348	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
349	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
350	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
351	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 2,335.67	12/2024 -	12/2024	0/0
352	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
353	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	03/2016 -	03/2025	0/0
354	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
355	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
356	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2026	0/0
357	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2026	0/0
<u>Railway Electrification</u>						
358	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>South Central Railway</u>					
359	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	10/2018	0/0
360	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017	0/0
361	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 03/2019	03/2019	0/0
362	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2021	0/0
363	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
364	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 03/2023	03/2023	0/0
365	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 03/2023	03/2023	0/0
366	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 1,856.95	03/2023 03/2024	03/2024	0/0
367	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
368	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
369	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
	<u>South East Central Railway</u>					
370	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	02/2019 -	02/2019	0/0
371	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	12/2019	0/0
372	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	03/2012 -	03/2020	0/0
373	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	04/2020 -	04/2020	0/0
374	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	03/2021 -	03/2021	0/0
375	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	12/2021 -	12/2021	0/0
376	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 -	12/2021	0/0
377	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH	04/2011	1,471.93 -	03/2022 -	03/2022	0/0
378	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH	02/2014	2,288.00 -	03/2022 -	03/2022	0/0
379	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	03/2023 -	03/2023	0/0
380	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
381	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00 -	09/2018 -	-	0/0
	<u>South Eastern Railway</u>					
382	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 12/2018	12/2018	0/0
383	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- 12/2018	12/2018	0/0
384	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 08/2018	12/2018	0/0
385	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 03/2020	06/2020	0/0
386	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	03/2021 03/2021	12/2021	0/0
387	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	1,013.45 1,013.45	12/2021 12/2021	12/2021	0/0
388	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]SER,WEST BENGAL	04/1998	1,027.40 -	03/2022 -	03/2022	0/0
389	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 03/2024	03/2024	0/0
390	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	- 12/2024	12/2024	0/0
391	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 12/2024	12/2024	0/0
392	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
393	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	- 03/2030	03/2030	0/0
394	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
395	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
396	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
397	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
398	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
399	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	633.87 -	- -	-	0/0
	<u>South Western Railway</u>					
400	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	03/2020 03/2020	03/2020	0/0
401	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2020	0/0
402	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- 03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Antici Pated	
1	2	3	4	5	6	7
403	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,614.59	03/2019 03/2021	03/2021	0/0
404	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- 12/2023	12/2023	0/0
405	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- 12/2023	12/2023	0/0
406	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- 12/2023	12/2023	0/0
407	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- 12/2023	12/2023	0/0
408	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	- 12/2023	12/2023	0/0
409	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- 12/2023	12/2023	0/0
410	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	03/2016 12/2023	12/2023	0/0
411	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	03/2002 03/2024	03/2024	0/0
412	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 03/2024	03/2024	0/0
413	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- 12/2024	12/2024	0/0
414	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	12/2018 12/2024	12/2024	0/0
	<u>Southern Railway</u>					
415	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018	0/0
416	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2019	0/0
417	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	02/2019	0/0
418	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	03/2019	0/0
419	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
420	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
421	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	03/2020	0/0
422	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
423	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
424	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
425	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
426	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-	0/0
427	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
428	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
429	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
430	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
431	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
432	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
433	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
434	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 346.15	- -	-	0/0
435	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
436	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
437	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 342.85	- -	-	0/0
438	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
439	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
440	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
441	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-	0/0
442	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-	0/0
443	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
444	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
445	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-	0/0
446	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-	0/0
447	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-	0/0
448	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-	0/0
	<u>West Central Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
449	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	03/2021 -	03/2021	0/0
	<u>Western Railway</u>					
450	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
451	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 -	03/2019 -	03/2019	0/0
452	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 416.86	03/2020 03/2020	03/2020	0/0
453	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	03/2021 03/2019	03/2020	0/0
454	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 -	03/2020 -	03/2020	0/0
455	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 -	06/2020 -	06/2020	0/0
456	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 2,473.40	03/2022 03/2019	03/2022	0/0
457	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	03/2022 03/2019	03/2022	0/0
458	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	03/2022 03/2019	03/2022	0/0
459	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	03/2019 03/2019	03/2022	0/0
460	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	- 03/2022	03/2023	0/0
461	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
462	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
463	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
464	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
465	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
466	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
467	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
468	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
469	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	06/2019	0/0
470	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
471	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
472	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
473	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000820]MORTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
474	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
475	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
476	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
477	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
478	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
479	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
480	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	-	-	0/0
481	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	-	-	0/0
482	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	-	-	0/0
483	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	-	-	0/0
484	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	-	-	0/0
485	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	-	-	0/0
486	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
487	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
488	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
489	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
490	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
491	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
492	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
493	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
494	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
495	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
496	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-	0/0
497	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
498	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
499	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-	0/0
500	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000339]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-	0/0
501	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
502	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
503	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
504	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
505	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
506	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
507	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-	0/0
508	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
509	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
510	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
511	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
512	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
513	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
514	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
515	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
516	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
517	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
518	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
519	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
520	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
521	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
522	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
523	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
524	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
525	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
526	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
527	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
528	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
529	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
530	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
531	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
532	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0
533	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
534	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
535	WIDENING AND STRENGTHENING OF EXISTING SL. IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH, ODISHA	03/2014	162.51 163.00	05/2016 -	-	0/0
536	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH, UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
537	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH, UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
538	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
539	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
540	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
541	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
542	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
543	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	-	0/0
544	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-	0/0
545	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-	0/0
546	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
547	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL - [N24000618]NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
548	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
549	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
550	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
551	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
552	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL, ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
553	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
554	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
555	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
556	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
557	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL, NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
558	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
559	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL, SIKKIM	04/2017	388.00 -	10/2017 -	-	0/0
560	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL, A & N ISLANDS	03/2015	262.97 -	10/2018 -	-	0/0
561	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	09/2018 -	-	0/0
562	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL, NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
563	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 -	09/2018 -	-	0/0
564	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	09/2018 -	-	0/0
565	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68 -	09/2018 -	-	0/0
566	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	09/2018 -	-	0/0
567	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	09/2018 -	-	0/0
568	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM 19.9 - [N24000759]NHIDCL, NAGALAND	03/2018	237.72 -	09/2018 -	-	0/0
569	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM 40.0 - [N24000760]NHIDCL, NAGALAND	03/2018	251.97 -	09/2018 -	-	0/0
570	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM 65. - [N24000761]NHIDCL, NAGALAND	03/2018	282.98 -	09/2018 -	-	0/0
571	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	03/2018	215.12 -	09/2018 -	-	0/0
572	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	09/2018 -	-	0/0
573	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL, NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
574	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL, NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
575	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWAY TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL, SIKKIM	04/2017	318.42 -	11/2017 -	-	0/0
576	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL, SIKKIM	03/2017	375.80 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
577	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-	0/0
578	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-	0/0
579	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
580	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL, MEGHALAYA	04/2017	553.51 -	- -	-	0/0
581	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	01/2016 -	-	0/0
<u>National Highways Authority Of India</u>						
582	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	- -	07/2018	0/0
583	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	09/2018	0/0
584	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
585	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	07/2018	0/0
586	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018	0/0
587	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	08/2018 -	08/2018	0/0
588	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	08/2018	0/0
589	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	09/2018	0/0
590	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	09/2018	0/0
591	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018	0/0
592	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	04/2009 -	10/2018	0/0
593	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	10/2018	0/0
594	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	11/2018	0/0
595	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	11/2018	0/0
596	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	11/2018	0/0
597	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	11/2018	0/0
598	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	11/2018	0/0
599	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 174.34	03/2008 -	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
600	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	12/2018	0/0
601	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
602	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	12/2018	0/0
603	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018	0/0
604	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
605	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018	0/0
606	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	12/2018	0/0
607	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	12/2018	0/0
608	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN	09/2015	567.51 -	03/2018 -	12/2018	0/0
609	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	12/2018	0/0
610	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	12/2018	0/0
611	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	12/2018	0/0
612	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	12/2018	0/0
613	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	12/2018	0/0
614	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 09/2017	12/2018	0/0
615	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	12/2018	0/0
616	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018	0/0
617	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	12/2018	0/0
618	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	12/2018	0/0
619	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	12/2018	0/0
620	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	12/2018	0/0
621	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	12/2018	0/0
622	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	01/2014 -	01/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
623	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019	0/0
624	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	01/2019	0/0
625	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	01/2019	0/0
626	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	01/2019	0/0
627	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	02/2019	0/0
628	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	02/2019	0/0
629	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2019	0/0
630	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2019	0/0
631	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
632	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019	0/0
633	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 -	03/2019	0/0
634	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 -	03/2019	0/0
635	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2019	0/0
636	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	03/2019	0/0
637	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	03/2019	0/0
638	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2019	0/0
639	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2019	0/0
640	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
641	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	03/2019	0/0
642	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	03/2019	0/0
643	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	03/2019	0/0
644	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	03/2019	0/0
645	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
646	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	03/2019	0/0
647	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	04/2019	0/0
648	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	04/2019	0/0
649	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019	0/0
650	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	04/2019	0/0
651	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019	0/0
652	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	04/2019	0/0
653	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	04/2019	0/0
654	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	04/2019	0/0
655	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019	0/0
656	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	04/2019	0/0
657	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
658	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019	0/0
659	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019	0/0
660	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	04/2019	0/0
661	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	04/2019	0/0
662	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	04/2019	0/0
663	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	05/2019	0/0
664	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019	0/0
665	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	05/2019	0/0
666	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019	0/0
667	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	05/2019	0/0
668	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	05/2019 -	05/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
669	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019	0/0
670	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2019	0/0
671	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	05/2019	0/0
672	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
673	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2019	0/0
674	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	06/2019	0/0
675	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	06/2019	0/0
676	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	06/2019	0/0
677	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	06/2019	0/0
678	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2019	0/0
679	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	06/2019	0/0
680	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	06/2019	0/0
681	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	06/2019	0/0
682	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	06/2019	0/0
683	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	06/2019	0/0
684	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2019	0/0
685	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	06/2019	0/0
686	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	06/2019	0/0
687	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2019	0/0
688	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	07/2019	0/0
689	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	07/2019	0/0
690	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	07/2019	0/0
691	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
692	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	08/2019	0/0
693	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	08/2019	0/0
694	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	05/2019 -	08/2019	0/0
695	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
696	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	08/2019 -	08/2019	0/0
697	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
698	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGOUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
699	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
700	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	09/2019	0/0
701	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
702	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	10/2019	0/0
703	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0
704	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	10/2019	0/0
705	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
706	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	11/2019	0/0
707	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019	0/0
708	4/2 LANNING WITH PS DAUSA-LALSOT-KAUNTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	11/2019	0/0
709	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
710	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	11/2019	0/0
711	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	11/2019	0/0
712	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0
713	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0
714	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
715	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2019	0/0
716	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	12/2019	0/0
717	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
718	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
719	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0
720	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
721	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
722	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
723	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	01/2020	0/0
724	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
725	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	02/2020	0/0
726	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
727	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
728	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
729	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
730	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
731	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
732	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
733	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
734	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
735	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
736	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
737	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
738	4 LANNING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
739	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
740	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
741	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	05/2020	0/0
742	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
743	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
744	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	05/2020	0/0
745	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
746	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	05/2020	0/0
747	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2020	0/0
748	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
749	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
750	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
751	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
752	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
753	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0
754	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
755	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	08/2020	0/0
756	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
757	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
758	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0
759	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
760	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
761	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
762	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020	0/0
763	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
764	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	11/2020	0/0
765	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
766	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 -	03/2021	0/0
767	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
768	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
769	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
770	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
771	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
772	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
773	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
774	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
775	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
776	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
777	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
778	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
779	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
780	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
781	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
782	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
783	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
784	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	-	0/0
785	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
786	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
787	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-	0/0
788	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
789	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
790	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
791	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
792	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	-	0/0
793	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
794	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
795	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
796	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
797	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
798	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
799	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
800	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	-	0/0
801	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-	0/0
802	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
803	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
804	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
805	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
806	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
807	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
808	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
809	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
810	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
811	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
812	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
813	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
814	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
815	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
816	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
817	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
818	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
819	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	-	0/0
820	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-	0/0
821	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
822	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
823	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
824	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
825	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
826	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
827	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
828	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
829	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
830	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
831	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0
832	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-	0/0
833	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
834	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
835	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
836	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
837	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
838	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
839	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	-	-	0/0
840	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	-	-	0/0
841	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	-	-	0/0
842	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	-	-	0/0
843	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	-	-	0/0
844	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	-	-	0/0
845	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	-	-	0/0
846	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	-	-	0/0
847	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	-	-	0/0
848	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	-	-	0/0
849	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	-	-	0/0
850	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	-	-	0/0
851	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	-	-	0/0
852	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
853	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
854	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
855	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
856	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0
857	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
858	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
859	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-	0/0
860	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
861	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
862	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
863	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0
864	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
865	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
866	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
867	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
868	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
869	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
870	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
871	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
872	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
873	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-	0/0
874	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
875	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
876	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
877	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
878	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	-	0/0
879	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
880	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
881	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-	0/0
882	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
883	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-	0/0
884	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
885	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
886	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-	0/0
887	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
888	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-	0/0
889	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
890	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
891	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
892	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
893	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
894	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	-	0/0
895	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-	0/0
896	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	-	0/0
897	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
898	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
899	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-	0/0
900	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	- -	-	0/0
901	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-	0/0
902	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-	0/0
903	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-	0/0
904	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI, TAMIL NADU	03/2018	505.35 -	- -	-	0/0
905	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI, TAMIL NADU	03/2018	628.71 -	- -	-	0/0
906	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-	0/0
907	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI, TAMIL NADU	03/2018	1,016.92 -	- -	-	0/0
908	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
909	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
910	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-	0/0
911	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	- -	-	0/0
912	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-	0/0
913	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- -	-	0/0
914	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-	0/0
915	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI, HARYANA	03/2018	307.79 -	- -	-	0/0
916	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-	0/0
917	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- -	-	0/0
918	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
919	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I - [N24000841]NHAI, HARYANA	03/2018	795.50 -	- -	-	0/0
920	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-	0/0
921	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
922	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
923	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	-	0/0
924	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
925	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	-	0/0
926	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
927	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	-	0/0
928	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	-	0/0
929	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
930	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-	0/0
<u>National Highways Development Project</u>						
931	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-	0/0
932	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
933	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-	0/0
934	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
935	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
936	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
937	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-	0/0
938	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-	0/0
939	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-	0/0
940	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
941	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-	0/0
942	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-	0/0
943	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
944	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
945	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-	0/0
946	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
947	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-	0/0
948	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-	0/0
949	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-	0/0
Public Works Dept Of State						
950	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	11/2018	0/0
951	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
952	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-	0/0
953	REHABILITATION AND UPGRADE OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-	0/0
954	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
955	REHABILITATION AND UPGRADE OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
956	REHABILITATION AND UPGRADE OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
957	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
958	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
959	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
960	REHABILITATION AND UPGRADE OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
961	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
962	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
963	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
964	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
965	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-	0/0
966	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
967	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
968	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
969	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
970	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
971	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
972	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
973	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
974	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
975	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
976	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
977	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
978	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
979	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
980	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
981	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
982	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
983	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
984	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
985	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
986	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
987	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
988	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above						
(November 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
989	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
990	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-	0/0
991	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
992	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
993	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
994	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-	0/0
995	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
996	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
997	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
998	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-	0/0
999	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
1000	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
1001	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
1002	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
1003	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
1004	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-	0/0
1005	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
1006	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
1007	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
1008	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
1009	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
1010	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1011	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
1012	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
1013	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Kamarajar Port Limited</u>					
1014	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]JKPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	05/2020	0/0
	<u>Mumbai Port Trust</u>					
1015	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
	<u>Port Trust</u>					
1016	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
1017	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1018	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 -	04/2018 12/2018	12/2018	0/0
1019	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 -	04/2018 12/2018	12/2018	0/0
1020	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 214.10	05/2018 12/2018	12/2018	0/0
1021	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 -	10/2018 12/2018	12/2018	0/0
	<u>Department Of Telecommunication</u>					
1022	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
1023	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Bangalore Metro Rail Corporation Limited</u>					
1024	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1025	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
1026	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1027	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	10/2019	0/0
1028	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0
1029	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0
1030	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1031	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 07/2017	06/2020	0/0
1032	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 09/2020	09/2020	0/0
1033	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	-	0/0
1034	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
1035	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-	0/0
1036	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-	0/0
1037	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-	0/0
1038	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
Chennai Metro Rail Ltd						
1039	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-	0/0
Hindustan Steelwork Construction Limited						
1040	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
1041	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
1042	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1043	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1044	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1045	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1046	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above

(November 2018)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1047	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1048	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1049	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1050	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1051	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1052	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1053	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1054	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
<u>Jawahar Lal Nehru National Urban Renewal Mission</u>						
1055	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
<u>Kochi Metro Rail Corporation Ltd</u>						
1056	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
<u>Lucknow Metro Rail Corporation Limited</u>						
1057	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
<u>Maharashtra Metro Rail Corporation Ltd.</u>						
1058	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	11/2021	0/0
1059	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
<u>Mumbai Metro Rail Corporation Ltd</u>						
1060	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
<u>Nagpur Metro Rail Corporation Ltd</u>						
1061	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA	08/2014	8,680.00 8,680.00	03/2018 12/2019	12/2019	0/0
<u>National Building Construcion Corporation Ltd</u>						
1062	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
Total			11,60,169.89 -			0/0
Grand Total			11,60,169.89			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(November 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271	7/2015	2,881.40 -	2,000.00	774.62	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 -	2,321.00	619.33	12/2020 -	08/2020
4	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195	2/2015	890.00 -	887.00	516.56	10/2019 -	03/2019
5	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216	1/2016	247.52	247.52	139.42	02/2019 -	12/2018
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226	2/2016	356.00	356.00	194.38	05/2019 -	12/2018
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,712.00	6.28	09/2022 -	06/2021
8	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	664.00	385.61	12/2020 -	02/2020
	Total		15,270.92 -	14,386.52	2,831.17		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
9	GARHWA ROAD-RAMNA - [N22000465	3/2015	348.23 -	348.23	100.63	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
10	AGARTALA SABROOM, NL, NEFR - [N22000099	4/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019
11	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	4/2015	2,232.32 -	2,182.00	193.12	03/2022 -	03/2020
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	4/2016	602.27 -	612.00	18.38	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
13	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	770.08	274.48	12/2022 -	05/2019

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
14	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	99.33	03/2022 -	02/2019
	<u>North Western Railway</u>						
15	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	127.14	12/2019 -	06/2019
16	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR [N22000152]	4/2013	420.18 295.02	420.18	81.44	03/2020 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
17	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.22	12/2025 -	03/2025
	Total		7,240.31 -	10,074.24	3,910.72		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
18	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	86.95	03/2020 -	05/2019
19	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	41.21	03/2020 -	06/2019
20	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	10.57	03/2020 -	06/2019
21	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	15.00	04/2020 -	11/2019
	Total		1,995.48 -	1,873.06	153.73		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
22	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020
	Total		150.29 -	150.29	2.58		
	Grand Total		24,657.00	26,484.11	6,898.20		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs.150 Crore and above						(November 2018)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	184.43	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	296.64	03/2022 -	03/2022
4	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	174.04	08/2019 -	08/2019
5	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.45	03/2022 -	03/2022
6	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
	<u>Mahanadi Coal Fields Limited</u>						
7	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	689.19	03/2026 -	03/2026
8	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	435.69	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
9	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	391.20	06/2015 09/2019	09/2019
10	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	173.06	12/2019 -	12/2019
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	3,716.05	11/2021 -	11/2021
12	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	8.71	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
13	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	207.63	03/2021 -	03/2021
14	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
15	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 -	03/2019
16	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
17	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
	<u>South-Eastern Coal Fields Limited</u>						
18	JAGANNATHPOR OCP (3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	172.27	03/2015 03/2020	03/2020
19	PELMA OCP (15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.13	03/2023 -	03/2023
20	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	103.85	03/2023 03/2021	03/2021
21	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	4.06	03/2023 -	03/2023
22	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
23	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
24	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.53	03/2021 -	03/2021
25	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,842.98	03/2023 -	03/2023
26	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,902.85	03/2023 -	03/2023
27	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.81	03/2023 -	03/2023
28	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	56.54	03/2020 -	03/2020
29	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
30	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.51	03/2021 -	03/2021
31	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.19	03/2021 -	03/2021
32	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
33	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	58.15	03/2020 -	03/2020
34	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
35	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	74.81	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
36	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	52.87	03/2020 -	03/2020
37	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	391.37	03/2020 -	03/2020
38	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	88.46	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
40	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
41	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	16.21	03/2022 -	03/2022
42	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	129.39	03/2019 -	03/2019
43	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
44	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	184.45	03/2020 -	03/2020
45	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
46	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	236.66	03/2025 -	03/2025
47	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	83.52	03/2021 -	03/2021
48	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	102.75	03/2020 -	03/2020
49	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
50	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.29	03/2021 -	03/2021
51	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	257.36	03/2020 -	03/2020
	Total		71,425.61 -	70,046.87	14,178.69		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
52	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	170.37	86.93	05/2018 01/2019	01/2019
53	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	51.87	08/2020 -	08/2020
	Total		453.64 -	461.66	138.80		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	27.20	11/2019 -	11/2019
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	23.79	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	28.60	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
57	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	126.30	11/2016 04/2019	04/2019
58	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	413.00	12/2017 12/2018	12/2018
59	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	38.65	04/2020 -	04/2020
	Total		1,781.92 -	1,793.57	657.54		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
60	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
61	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
62	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
	<u>Hospital Services Consultancy Corporation</u>						
63	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	76.88	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
64	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	122.66	03/2019 -	03/2019
65	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	71.50	03/2019 -	03/2019
	Total		3,264.53 -	3,264.53	756.39		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
66	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
67	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	166.62	125.00	06/2019 06/2019	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
68	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
69	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
70	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	302.19	01/2020 01/2020	01/2020
	Total		7,078.62 -	7,078.62	556.09		
	PETROLEUM						
	<u>Bharat Petroleum Corporation Limited</u>						
71	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	507.96	10/2018 12/2018	12/2018
72	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	2,420.04	08/2018 05/2019	05/2019
73	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	115.17	12/2019 -	12/2019
74	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
75	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	19.99	12/2020 -	12/2020
76	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	56.69	08/2020 -	08/2020
77	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	360.27	02/2020 10/2020	10/2020
78	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	135.68	02/2020 -	02/2020
	<u>Chennai Petroleum Corporation Limited</u>						
79	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	575.65	12/2019 -	12/2019
80	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	16.73	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
81	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	2,313.08	12/2018 -	12/2018
82	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	733.62	02/2020 -	02/2020
83	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1.66	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
84	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	21.92	10/2022 -	10/2022
85	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	22.11	10/2022 -	10/2022
86	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	14.06	07/2022 -	07/2022
87	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	28.18	10/2022 -	10/2022
88	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	29.39	07/2022 -	07/2022
89	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	99.03	04/2022 -	04/2022
90	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	21.02	12/2020 -	12/2020
91	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	663.13	12/2020 -	12/2020
92	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	776.24	12/2020 -	12/2020
93	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	652.51	12/2020 -	12/2020
94	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	800.00	600.58	12/2018 -	12/2018
	<u>Hindustan Petroleum Corporation Limited</u>						
95	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	586.10	10/2014 02/2019	02/2019
96	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
97	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
98	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	4.33	11/2020 -	11/2020
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	241.80	09/2019 -	09/2019
100	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	961.58	06/2020 -	06/2020
101	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	110.04	02/2019 -	02/2019
102	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
103	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	9/2017	2,677.00 -	2,677.00	49.88	03/2021 -	03/2021
104	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
	<u>Indian Oil Corporation Limited</u>						
105	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
106	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00 -	690.00	169.70	07/2018 10/2020	10/2020
107	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254	9/2015	324.00 -	324.00	78.63	06/2020 -	06/2020
108	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
109	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250	2/2016	151.00 -	151.00	99.30	09/2019 -	09/2019
110	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249	5/2016	1,945.00 -	1,945.00	499.85	08/2021 -	08/2021
111	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248	7/2015	822.66 -	822.66	809.78	11/2018 -	11/2018
112	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243	2/2016	2,582.00 -	2,582.00	1,208.92	11/2019 -	11/2019
113	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	6/2016	423.00 -	423.00	208.63	08/2019 -	08/2019
114	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	1,823.00	569.04	12/2020 -	12/2020
115	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308	8/2017	315.00 -	315.00	2.56	12/2021 -	12/2021
116	BS-VI PROJECT AT MATHURA REFINERY - [N16000306	1/2018	666.64 -	666.64	200.89	09/2019 -	09/2019
117	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	8/2017	236.00 -	236.00	11.66	06/2020 -	06/2020
118	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303	8/2017	318.80 -	318.80	12.65	08/2021 -	08/2021
119	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302	8/2017	384.58 -	384.58	38.79	04/2021 -	04/2021
120	KHARAGPUR LPG BOTTLING PLANT - [N16000300	4/2017	163.02 -	163.02	32.69	04/2020 -	04/2020
121	AUGMENTATION OF CTMPL - [N16000286	12/2016	228.00 -	228.00	.17	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
122	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	67.71	07/2020 -	07/2020
123	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	33.81	12/2019 -	12/2019
124	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]	4/2018	355.00 -	355.00	-	04/2022 -	04/2022
125	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]	8/2018	466.00 -	466.00	1.12	04/2021 -	04/2021
126	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	123.17	08/2020 -	08/2020
127	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	69.88	02/2020 -	02/2020
128	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	4,807.08 -	4,807.08	24.09	07/2021 -	07/2021
129	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	3.64	01/2021 -	01/2021
130	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	3.41	12/2021 -	12/2021
131	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020
132	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	857.95	07/2019 -	07/2019
133	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	1.88	03/2021 -	03/2021
134	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
135	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	-	08/2020 -	08/2020
136	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	738.18	09/2019 -	09/2019
137	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	.12	02/2020 -	02/2020
138	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	268.88	09/2019 -	09/2019
139	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
140	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,151.10	09/2019 -	09/2019
141	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.67	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
142	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	25.56	02/2020 -	02/2020
143	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY [N16000277]	5/2016	429.00 -	429.00	256.93	01/2019 -	01/2019
144	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	8.48	01/2021 -	01/2021
145	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
146	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
147	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	8.48	01/2021 -	01/2021
148	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR- SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	14.11	01/2021 -	01/2021
149	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	2,443.76	09/2017 12/2018	12/2018
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
150	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
151	BSVI UPGRADEATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
152	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
153	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	124.25	03/2019 03/2019	03/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
154	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,107.69	03/2013 03/2019	03/2019
155	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	449.95	11/2019 -	11/2019
156	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	6/2010	202.94 -	330.35	60.44	01/2014 11/2019	11/2019
157	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,842.42	03/2015 12/2019	12/2019
158	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	87.79	03/2023 03/2022	03/2022
159	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	-	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
160	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	1,226.29	05/2021 05/2021	05/2021
161	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	502.40	11/2019 11/2019	11/2019
162	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	167.64	11/2019 11/2019	11/2019
163	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	191.39	11/2019 11/2019	11/2019
164	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	299.26	05/2019 05/2019	05/2019
165	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	207.80	27.54	09/2018 02/2019	02/2019
166	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	285.28	03/2026 03/2026	03/2026
167	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	98.10	05/2020 05/2020	05/2020
168	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	1,450.26	06/2020 08/2021	08/2021
169	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,102.45	04/2018 05/2019	05/2019
170	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	3,931.91	12/2017 03/2019	03/2019
171	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,577.15	1,195.62	05/2013 03/2019	03/2019
172	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	1,687.43	03/2019 05/2020	05/2020
173	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,504.61	2,119.15	05/2017 12/2018	12/2018
174	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,449.66	05/2019 10/2019	10/2019
175	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,559.88	04/2019 03/2019	03/2019
Oil India Limited							
176	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	438.84	196.39	03/2017 06/2019	06/2019
177	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	1.65	02/2020 -	02/2020
178	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAN SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	42.33	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
179	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	23.61	10/2020 -	10/2020
	Total		1,84,982.88 -	1,83,884.93	52,402.89		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
180	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	9,958.55	09/2017 06/2019	06/2019
181	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,690.33	03/2013 12/2020	12/2020
182	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	5,195.95	03/2019 09/2019	09/2019
183	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	376.58	09/2019 02/2022	02/2022
184	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	8,911.13	11/2016 03/2019	03/2019
185	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	6,135.72	09/2019 -	09/2019
186	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	2,701.10	07/2020 10/2020	10/2020
187	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10,490.56	06/2017 06/2019	06/2019
188	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,293.72	11/2019 -	11/2019
189	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	15,031.14	01/2011 04/2021	04/2021
190	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	7,673.86	02/2019 10/2020	10/2020
191	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	8,122.05	08/2018 06/2019	06/2019
	<u>North East Electric Power Corporation</u>						
192	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,838.94	12/2009 03/2019	03/2019
	<u>Power Grid Corporation Of India Limited</u>						
193	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	375.34	11/2018 -	11/2018
194	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	743.82	01/2019 -	01/2019
195	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	250.73	03/2019 -	03/2019
196	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	76.98	02/2019 -	02/2019
197	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	16.10	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
198	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	552.21	04/2020 -	04/2020
199	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	89.17	09/2019 -	09/2019
200	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	21.82	12/2019 -	12/2019
201	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	20.09	06/2019 -	06/2019
202	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	22.42	03/2019 -	03/2019
203	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	103.28	02/2019 -	02/2019
204	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	55.10	02/2020 -	02/2020
205	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	354.00	04/2019 -	04/2019
206	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	25.85	11/2019 -	11/2019
207	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	79.31	06/2019 -	06/2019
208	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	26.40	03/2019 -	03/2019
209	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	2.50	06/2019 -	06/2019
210	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
211	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	321.99	02/2020 -	02/2020
212	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	197.76	02/2019 -	02/2019
213	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	50.27	07/2019 -	07/2019
214	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	597.00	07/2020 -	07/2020
215	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,798.00	04/2019 -	04/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
216	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	191.76	02/2019 -	02/2019
217	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	194.26	12/2018 -	12/2018
218	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	97.53	11/2018 -	11/2018
219	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	3,710.05	11/2019 -	11/2019
220	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS [N18000222]	4/2016	790.13 -	790.30	502.54	06/2019 -	06/2019
221	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	303.70	04/2019 -	04/2019
222	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,861.40	05/2019 -	05/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
223	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	131.82	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
224	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	65.37	09/2020 -	09/2020
	Total		1,53,120.17 -	1,69,479.02	1,00,258.20		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
225	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	979.05	03/2023 -	03/2023
226	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	26.63	03/2023 -	03/2023
227	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	1.27	03/2023 -	03/2023
228	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	3,627.47	309.54	03/2024 -	03/2024
229	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	87.60	03/2023 -	03/2023
230	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	132.09	03/2022 -	03/2022
231	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
232	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
233	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	-	03/2024 -	03/2024
234	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	298.70	240.89	03/2019 -	03/2019
235	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	1,870.67	03/2021 -	03/2021
236	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	156.10	03/2022 -	03/2022
237	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	272.78	03/2021 -	03/2021
	<u>Container Corporation Of India</u>						
238	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	253.28	03/2019 -	03/2019
239	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	272.72	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
240	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
241	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
242	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
243	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	571.51	03/2020 -	03/2020
244	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	189.40	03/2022 -	03/2022
245	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	183.68	03/2022 -	03/2022
246	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
247	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	81.06	03/2022 -	03/2022
248	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
249	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) [N22000230]	4/2010	157.94 -	157.94	50.69	11/2018 -	11/2018
250	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	319.21	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
251	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	303.58	03/2020 -	03/2020
	<u>Metropolitan Rapid Transport Projects</u>						
252	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	734.01	445.91	06/2013 03/2019	03/2019
	<u>North Central Railway</u>						
253	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
254	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
255	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021
256	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
257	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	4,968.00	2,318.33	03/2014 12/2020	12/2020
258	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
259	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	259.43	03/2021 -	03/2021
260	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	123.11	03/2020 -	03/2020
261	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	264.69	03/2019 -	03/2019
262	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	163.08	03/2021 -	03/2021
263	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	551.00	595.01	03/2019 -	03/2019
264	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	64.09	03/2020 -	03/2020
265	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	457.51	03/2019 -	03/2019
266	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
267	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	2,326.52 -	3,000.00	655.38	03/2015 10/2021	10/2021
	<u>North Eastern Railway</u>						
268	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
269	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	366.71	.45	01/2022 -	01/2022
	<u>North Western Railway</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
270	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	1,116.00	795.27	03/2014 03/2019	03/2019
271	PHULERA - DIGANA DOUBLING - [N22000326]	5/2015	600.00 -	685.99	3.51	03/2020 -	03/2020
272	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	206.88	11/2019 -	11/2019
273	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	-	08/2022 -	08/2022
274	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	795.01	450.57	02/2019 -	02/2019
<u>Northern Railway</u>							
275	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	27,949.00	16,834.42	11/2002 03/2021	03/2021
276	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
<u>National High Speed Rail Corporation Limited</u>							
277	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	899.56	12/2023 12/2023	12/2023
<u>Rail India Technical And Economic Service</u>							
278	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
<u>Rail Vikas Nigam Ltd.</u>							
279	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	354.55	12/2026 -	12/2026
280	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	101.07	03/2021 -	03/2021
281	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,750.00	1,563.47	03/2020 -	03/2020
282	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	970.00	975.36	03/2020 -	03/2020
283	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	867.07	12/2020 -	12/2020
284	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	758.09	849.72	03/2020 -	03/2020
285	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	300.05	12/2024 -	12/2024
286	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	219.80	12/2024 -	12/2024
287	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	249.33	12/2023 -	12/2023
288	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	835.70	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
289	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,127.00	1,161.88	03/2023 -	03/2023
290	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	975.62	623.78	12/2021 -	12/2021
	<u>South Central Railway</u>						
291	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	289.91	03/2009 03/2023	03/2023
292	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	368.22	03/2021 -	03/2021
293	GUNTUR-GUNTAKAL - [N22000368]	4/2016	3,631.00 -	3,631.00	124.49	03/2022 03/2023	03/2023
294	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	1,723.00 1.00	645.00	725.63	03/2000 03/2019	03/2019
295	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	4/2008	2,132.77 -	2,132.77	216.07	03/2014 03/2023	03/2023
296	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	4/2006	1,160.48 -	1,160.47	111.36	03/2010 03/2022	03/2022
297	NADIKUDE-SRI KALAHASTI - [N22000286]	4/2011	2,288.70 -	2,288.70	375.28	03/2021 03/2022	03/2022
298	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	119.69	03/2020 03/2020	03/2020
299	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	4/2012	1,856.95 -	2,200.00	227.19	03/2023 03/2024	03/2024
300	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>South East Central Railway</u>						
301	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
302	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
303	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
304	JHARSUGUDA-BILASPU 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
305	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
306	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
307	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
308	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
309	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	4/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019
	<u>South Eastern Railway</u>						
310	MM FROM BURAMARA-CHAKULIA - [N22000305]	4/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024
311	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024
312	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	4/1998	1,027.40 -	2,373.00	481.65	03/2022 -	03/2022
313	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	525.81	495.14	12/2015 12/2018	12/2018
314	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024
315	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	4/1998	1,027.40 -	2,373.00	484.85	03/2003 03/2030	03/2030
316	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.48	12/2021 12/2021	12/2021
317	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	4/2012	258.20 -	365.00	184.85	- 12/2018	12/2018
318	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.77	- 03/2025	03/2025
319	MM FROM PANSKURA-GHATAL NL - [N22000309]	4/2011	276.69 -	426.00	-	- 03/2030	03/2030
	<u>South Western Railway</u>						
320	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	4/2011	1,801.01 -	1,801.01	12.54	- 12/2023	12/2023
321	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,614.59	696.73	03/2019 03/2021	03/2021
322	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	448.98	03/2020 03/2020	03/2020
323	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	490.28	03/2020 03/2020	03/2020
324	MIRAJ-LONDA - [N22000327]	3/2015	1,830.00 -	1,190.92	190.63	- 03/2021	03/2021
325	HUBLI-ANKOLA(NL),SWR - [220100193]	4/1997	2,315.00 -	2,135.00	144.75	- 12/2024	12/2024
326	MARIKUPPAM - KUPPAM - [N22000308]	4/2012	279.54 -	279.54	8.66	03/2016 12/2023	12/2023
327	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	4/2013	327.25 -	367.77	.31	- 12/2023	12/2023
328	GADAG-WADI NL - [N22000299]	4/2013	2,841.84 -	2,841.84	27.34	12/2018 12/2024	12/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
329	TORANAGALLU-RANJITPURA DL - [N22000298	4/2011	146.75 -	167.50	.34	- 12/2023	12/2023
330	BAGALKOT-KUDACHI NL - [N22000258	4/2010	986.30 -	986.30	285.06	03/2016 12/2023	12/2023
331	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	4/2013	558.00 -	692.43	-	- 12/2023	12/2023
332	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	4/2013	296.00 -	466.65	-	- 12/2023	12/2023
333	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	4/1996	1,382.78 -	1,382.78	7.35	03/2002 03/2024	03/2024
334	WHITE FIELD-KOLAR NL - [N22000280	4/2011	348.85 -	348.85	.36	- 12/2023	12/2023
335	SHIMOGA-HARIHAR NL - [N22000278	4/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024
	<u>Southern Railway</u>						
336	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079	9/2007	724.69 -	2,072.50	1,169.07	02/2019 -	02/2019
337	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	4/2011	120.70 -	1,800.00	112.10	03/2019 -	03/2019
338	ATTIPPATTU PUTTUR - [N22000184	4/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019
339	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
340	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
	<u>West Central Railway</u>						
341	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
342	KATNI-BINA 3RD LINE (263 KM) - [N22000415	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
343	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
	<u>Western Railway</u>						
344	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	385.60	500.42	03/2020 03/2020	03/2020
345	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494	4/2017	691.84 -	691.84	15.31	03/2020 -	03/2020
346	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493	4/2016	700.00 -	700.00	11.19	06/2020 -	06/2020
347	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	2/1991	551.51 -	551.51	257.05	03/2019 -	03/2019
	Total		2,85,562.06 -	3,83,886.00	74,358.77		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
348	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
349	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019
350	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	74.52	02/2020 -	02/2020
351	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
352	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000820	11/2017	237.80 -	238.00	-	11/2019 -	11/2019
353	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
354	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019
355	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019
356	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019
357	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
358	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	45.92	06/2019 -	06/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
359	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
360	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
361	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
362	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
363	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
364	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
<u>National Highways Authority Of India</u>							
365	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
366	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439	7/2015	1,885.74 -	1,885.74	1,622.44	05/2019 -	05/2019
367	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	218.51	04/2019 -	04/2019
368	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	1,041.10	159.02	04/2019 -	04/2019
369	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
370	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	950.69	388.34	08/2019 -	08/2019
371	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
372	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604	8/2016	320.30 -	320.30	193.54	01/2019 -	01/2019
373	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	1,167.42	191.05	03/2019 -	03/2019
374	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605	8/2016	227.49 -	227.49	15.03	01/2019 -	01/2019
375	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	270.31	04/2020 -	04/2020
376	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	1,388.34	206.87	09/2019 -	09/2019
377	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553	3/2016	229.37 -	229.37	6.39	11/2018 -	11/2018
378	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	21.98	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
379	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
380	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
381	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
382	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
383	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
384	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	5.00	03/2020 -	03/2020
385	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]	1/2017	244.90 -	244.90	77.00	05/2019 -	05/2019
386	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]	11/2016	400.25 -	400.25	38.57	03/2019 -	03/2019
387	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
388	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	886.98	03/2020 -	03/2020
389	REHABILITATION AND UPGRADATION BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
390	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	145.81	04/2019 -	04/2019
391	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	2/2016	997.15 -	997.15	328.14	03/2019 -	03/2019
392	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	32.98	02/2019 -	02/2019
393	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]	1/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018
394	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	409.11	04/2019 -	04/2019
395	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	784.53	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
396	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540	1/2016	701.12 -	701.12	842.34	05/2019 -	05/2019
397	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505	6/2015	1,583.79 -	1,583.79	496.70	01/2019 -	01/2019
398	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
399	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	237.07	07/2019 -	07/2019
400	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	87.19	07/2019 -	07/2019
401	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	351.90	04/2019 -	04/2019
402	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	1,945.00	01/2019 -	01/2019
403	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442	12/2015	649.50 -	649.50	80.89	03/2019 -	03/2019
	Total		46,052.89 -	46,536.60	10,699.40		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
404	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	15,525.00	14,485.63	05/2015 06/2019	06/2019
405	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	Total		16,343.00 -	16,343.00	14,517.23		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
406	MAHARASHTRA NODAL (LOT 1) - [N26000107	8/2017	159.30 -	159.30	60.27	04/2018 12/2018	12/2018
407	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	1/2018	231.80 -	231.80	77.65	10/2018 12/2018	12/2018
408	MADHYA PRADESH ACCESS (LOT1) - [N26000110	8/2017	215.30 -	214.10	33.46	05/2018 12/2018	12/2018
409	MAHARASHTRA CORE (LOT1) - [N26000108	8/2017	167.68 -	167.68	32.44	04/2018 12/2018	12/2018
	Total		774.08 -	772.88	203.82		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
410	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	6/2015	197.33 -	197.33	10.14	04/2019 06/2020	06/2020
411	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098	10/2016	209.84 -	209.84	9.96	03/2020 -	03/2020
412	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103	12/2016	246.31 -	246.31	29.78	02/2020 09/2020	09/2020
413	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107	12/2017	188.00 -	188.00	85.71	06/2019 -	06/2019
414	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 -	271.90	4.44	11/2019 -	11/2019
415	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
416	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108	1/2018	206.58 -	206.58	.02	03/2019 -	03/2019
417	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	3.36	05/2020 -	05/2020
418	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089	12/2015	209.00 -	209.00	52.00	10/2019 -	10/2019
	<u>Lucknow Metro Rail Corporation Limited</u>						
419	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
420	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	1,881.14	11/2021 -	11/2021
	<u>Nagpur Metro Rail Corporation Ltd</u>						
421	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	4,631.87	03/2018 12/2019	12/2019
	<u>National Building Construction Corporation Ltd</u>						
422	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,581.53	11/2019 -	11/2019
	Total		33,231.24 -	33,406.47	12,826.72		
	Grand Total		8,04,070.64	9,16,954.15	2,81,554.54		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs.150 Crore and above							
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
3	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
7	KAKATYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	Total		18,724.25 -	19,454.55			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
9	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	170.37	05/2018 -	01/2019	1.41

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	291.29	08/2020 -	08/2020	1.85
	Total		453.64 -	461.66			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
11	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	-	13.31
12	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
13	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014	07/2016	312.99 -	322.00	08/2018 -	-	2.88
	Total		987.47 -	1,036.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
16	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
18	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU [N16000255	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	<u>Oil & Natural Gas Corporation Limited</u>						
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
	<u>Oil India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	06/2019	24.47
21	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		6,548.66 -	7,870.53			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
22	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
24	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
25	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
26	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
27	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
28	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
29	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
30	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
31	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
33	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
	<u>North East Electric Power Corporation</u>						
34	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
35	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59
36	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65
38	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	-	36.79
39	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61
40	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34
41	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	-	32.69
42	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	-	14.60
43	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	-	26.82
44	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92
45	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	-	36.01
46	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	-	39.30
47	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17
48	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	12/2018	79.61
49	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,534.00	11/2008 -	12/2018	42.42
50	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	-	26.86
51	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	-	30.49
52	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
53	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
54	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15
55	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	12/2018	42.83
56	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]	08/2008	771.00 -	1,624.00	02/2013 -	-	110.64

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Satluj Jal Vidyut Nigam Limited</u>						
57	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
58	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77
59	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,57,203.79 -	2,08,267.90			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
60	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	298.70	03/2019 -	03/2019	62.28
61	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44
62	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	389.99
63	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
64	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
	<u>Container Corporation Of India</u>						
65	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
66	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	-	03/2021	192.42
67	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	-	03/2023	290.95
68	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	163.78
69	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
70	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	-	03/2022	261.73
71	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
72	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	-	-	323.32
73	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	-	338.91

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
75	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	-	03/2021	296.21
76	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
77	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
78	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
79	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
80	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
81	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
82	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	-	12/2018	192.15
83	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	-	12/2021	71.96
<u>East Coast Railway</u>							
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96
85	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
86	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	-	-	542.46
87	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
88	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	-	-	818.15
89	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	-	03/2021	124.59
90	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	-	03/2022	590.61
91	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
<u>Eastern Railways</u>							
92	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2019	36.26

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
93	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	607.91	02/2013 -	-	.14
94	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116	04/2009	259.51 -	533.59	02/2012 -	-	105.61
95	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	- -	-	44.46
96	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON- PORAMAHESHTALA AND CHA - [N22000242	04/2003	337.96 -	355.44	- -	-	5.17
97	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	665.75	02/2012 -	-	33.16
98	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL [N22000244	04/2009	257.42 -	258.73	03/2014 -	-	.51
99	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	259.23	- -	-	3.31
100	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	-	6.48
101	GHUTIASHARIF-CANNING (ER) - [N22000117	04/2009	193.08 -	612.45	12/2011 -	-	217.20
102	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	544.72	03/2006 -	-	33.84
103	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	- -	-	51.19
104	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	332.14	- -	-	27.07
105	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227	04/2010	174.56 -	175.99	- -	-	.82
	<u>Metropolitan Rapid Transport Projects</u>						
106	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
107	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
108	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
109	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
110	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
111	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
112	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
	<u>North East Frontier Railway</u>						
113	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
114	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
115	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56
116	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	3,230.02 -	5,820.00	04/2008 12/2011	06/2018	80.18
117	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	03/2019	157.59
118	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
119	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
120	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
121	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
122	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,374.00	03/2014 -	03/2019	195.45
123	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2020	7.86
124	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
125	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
126	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11
127	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	451.00	03/2019 -	03/2019	59.05
128	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
129	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
130	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
131	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
132	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	- -	-	128.39
133	AMBARA FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	551.00	03/2019 -	03/2019	75.48
134	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12
135	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
136	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	413.56	06/2018 -	10/2018	89.54
137	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34
138	HATHUA-BHATNI (N L) (NER) - [220100319	04/2005	230.03 -	770.08	12/2022 -	05/2019	234.77
139	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	744.71 -	1,126.79	- -	-	51.31
140	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
141	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130	03/2013	307.00 -	308.00	- -	-	.33
142	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	895.00	12/2021 -	-	267.13
143	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132	03/2008	195.64 -	435.00	- -	03/2018	122.35
144	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133	03/2012	199.75 -	270.00	08/2018 -	08/2018	35.17
145	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	01/2019 -	02/2019	61.80
146	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00 -	644.00	- -	-	.16
147	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455	04/1997	233.00 -	318.42	04/1999 -	-	36.66
148	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16
149	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458	04/1997	609.04 1,063.00	1,807.88	04/1999 -	12/2018	70.07
150	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
151	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	1,116.00	03/2014 -	03/2019	70.85

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
152	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	795.01	02/2019 -	02/2019	93.87
153	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	685.99	03/2020 -	03/2020	14.33
154	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330	05/2015	873.71 -	1,103.04	- -	-	26.25
155	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55
156	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137	04/2012	246.08 -	348.55	12/2019 -	06/2019	41.64
157	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	2,878.97	- -	-	38.23
158	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	294.90	10/2018 -	10/2018	24.47
159	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150	04/2013	822.00 -	1,099.54	- -	-	33.76
160	PUSHKAR-MERTA - [N22000151	04/2013	323.00 -	432.22	- -	-	33.81
161	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152	04/2013	420.18 -	420.18	03/2020 -	12/2019	.00
162	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35
163	RANI-MARWAR JN. PATCH DOUBLING - [N22000156	04/2012	288.97 -	346.35	11/2018 -	12/2018	19.86
164	ALWAR-BANDIKUI DOUBLING - [N22000157	04/2013	242.09 -	349.00	02/2019 -	03/2019	44.16
<u>Northern Railway</u>							
165	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	-	210.19
166	GRADE SEPERATOR AT DAYABASTI - [N22000269	04/1999	156.65 -	197.17	- -	-	25.87
167	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	625.00	12/2011 -	-	117.77
168	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	346.63	- -	-	57.68
169	CHANDIGARH-BADDI NL - [N22000296	04/2007	328.14 -	1,540.00	- -	-	369.31
170	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
171	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
172	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
174	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
175	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	06/2019	55.57
176	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	1,202.70	02/2015 -	12/2021	.00
177	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	85.99
178	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,850.00	03/2008 -	03/2020	152.45
179	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
180	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
181	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70
182	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
184	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
185	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
186	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39
187	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,750.00	03/2020 -	03/2020	145.28
188	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	970.00	03/2020 -	03/2020	2.32
	<u>Railway Electrification</u>						
189	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
190	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
191	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
192	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	-	-	93.56
193	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	-	-	92.93
194	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
195	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	645.00	03/2000 -	03/2019	64,400.00
196	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	-	-	.00
197	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,025.00	-	03/2017	723.76
	<u>South East Central Railway</u>						
198	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	-	-	186.92
199	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	04/2020 -	04/2020	243.06
200	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
201	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,420.39	02/2019 -	02/2019	142.42
202	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	403.00	12/2021 -	12/2021	75.98
203	CHHINDWARA-MANDLA FORT GC - [N22000481]	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22
204	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,279.00	12/2019 -	12/2019	46.67
205	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,919.00	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
206	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00	-	12/2024	114.37
207	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	-	03/2030	53.96
208	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
209	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
210	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41
211	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	-	03/2025	131.89
212	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
213	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
214	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
215	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81	12/2015 -	12/2018	69.92
216	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2018	41.36
217	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	- -	-	278.13
218	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76
219	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
220	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
221	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
222	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	04/1998	1,027.40 -	2,373.00	03/2022 -	03/2022	130.97
	<u>South Western Railway</u>						
223	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
224	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
225	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
226	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
227	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
228	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2019	185.98
229	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
230	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
231	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
232	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	-	-	79.80
233	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	1,105.00	02/2019 -	02/2019	627.74
234	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,350.00	- -	-	348.88
235	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
236	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
237	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1998	271.24 -	520.00	- -	-	91.71
238	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	- -	-	69.20
239	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05
240	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	03/2020	173.71
241	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	369.83	- -	-	92.90
242	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	1,800.00	03/2019 -	03/2019	1,391.30
243	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
244	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	302.02	03/2005 -	-	12.33
245	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
246	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450	02/2003	199.55 -	330.32	03/2009 -	-	65.53
247	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
248	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
249	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
250	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
<u>Western Railway</u>							

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
251	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
252	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
	Total		1,33,459.96 -	2,73,685.39			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
253	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
	<u>Ministry Of Road Transport And Highways</u>						
254	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
255	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	11/2019 -	11/2019	.17
256	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06
257	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
258	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
259	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
260	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
261	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
262	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	02/2019	4.99
263	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
264	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
265	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	04/2019	65.82

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
266	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2019	10.58
267	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
268	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
269	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
270	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
271	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83
272	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_ NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
273	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
274	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
275	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
276	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
277	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
278	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
279	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
280	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
281	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
282	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
283	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
284	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
285	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
286	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
287	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
288	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
289	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	.12
290	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	.01
291	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		27,118.65 -	41,914.00			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
292	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Mumbai Port Trust</u>						
293	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
294	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
295	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	-	42.39
	Total		343.00 -	488.40			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above							
(November 2018)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
296	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
297	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	04/2014	332.72 -	342.00	09/2016 -	-	2.79
298	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
299	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.60
	<u>Chennai Metro Rail Ltd</u>						
300	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
301	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
302	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>National Building Construcion Corporation Ltd</u>						
303	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		21,830.72 -	27,219.50			
	Grand Total		3,86,289.64	6,16,976.38			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs.150 Crore and above									
								(November 2018)	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,100.00	5,687.52	09/2010 -	03/2019	102	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	12,707.00	12/2015 11/2016	06/2020	54	43
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,937.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	10,632.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	74,849.00	38,963.52				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	85.79				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	325.14	04/2015 -	04/2019	48	-
	<u>Central Coal Fields Limited</u>								
7	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	174.69	03/2012 -	03/2019	84	-
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	176.72	03/2012 -	03/2019	84	-
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	340.06	03/2016 -	03/2019	36	-
10	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.21	03/2014 -	03/2019	60	-
11	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	103.27	03/2011 -	03/2020	108	-
12	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	184.20	07/2012 -	03/2021	104	-
	<u>Eastern Coal Fields Limited</u>								
13	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N060000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	382.14	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	387.94	03/2017 -	03/2020	36	-
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	583.96	03/2013 -	03/2020	84	-
16	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	266.97	03/2010 -	03/2020	120	-
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	251.75	03/2013 -	03/2020	84	-
18	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	27.48	03/2018 -	03/2020	24	-
19	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	234.29	03/2012 -	03/2021	108	-
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	60.36	03/2019 -	03/2021	24	-
21	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	116.85	03/2019 -	03/2024	60	-
	<u>Neyveli Lignite Corporation</u>								
22	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,770.46	12/2015 12/2018	03/2019	39	3
	<u>Northern Coal Fields Limited</u>								
23	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	572.40	03/2018 -	03/2019	12	-
	<u>Singareni Colliers Company Limited</u>								
24	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48	-
25	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45	-
26	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36	-
27	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
28	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44	-
29	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72	-
30	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72	-
31	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72	-
32	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	-
33	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	186.91	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
34	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.50	03/2016 -	03/2019	36	-
35	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	163.85	03/2016 -	03/2019	36	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
36	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
37	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	202.68	03/2014 -	03/2020	72	-
	<u>Western Coal Fields Limited</u>								
38	BHANEGAON OC - [N06000121]WCL, MAHARASHTRA	02/2015	187.94 409.68	409.68	95.81	03/2023 02/2017	03/2023	0	73
39	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 313.34	313.34	6.12	03/2021 09/2018	03/2024	36	66
	Total		19,016.23 -	19,594.77	12,388.64				
	<u>STEEL</u>								
	<u>Rastriya Ispat Nigam Limited</u>								
40	ADDITIONAL WATER STORAGE RESERVOIR (KBR-II) - [N12000120]RINL, ANDHRA PRADESH	07/2015	465.85 -	465.85	244.25	07/2018 -	01/2019	6	-
41	CENTRAL DISPATCH YARD - [N12000119]RINL, ANDHRA PRADESH	08/2015	320.66 -	320.66	115.36	08/2018 -	02/2019	6	-
42	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	802.10	09/2018 -	03/2019	6	-
43	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,013.76	12/2017 -	09/2019	21	-
44	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	239.65	10/2016 -	03/2019	29	-
	<u>Steel Authority Of India Limited (SAIL)</u>								
45	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	2,509.89	04/2018 -	05/2019	13	-
46	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	855.62	12/2017 -	06/2019	18	-
47	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	362.48	10/2017 -	06/2020	32	-
48	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	76.61	06/2019 -	06/2020	12	-
	Total		11,248.72 -	11,036.12	6,219.72				
	<u>PETROLEUM</u>								
	<u>Gas Authority Of India Limited</u>								
49	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	200.00	110.98	04/2018 -	12/2018	8	-
50	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 3,030.00	2,915.00	1,965.67	12/2012 02/2019	06/2019	78	4
	<u>Indian Oil Corporation Limited</u>								
51	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	10/2015	607.06 -	714.25	341.79	10/2017 -	03/2019	17	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
52	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	4,497.00	302.17	12/2018 -	12/2020	24	-
53	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	1.18	10/2020 -	05/2021	7	-
	<u>Oil & Natural Gas Corporation Limited</u>								
54	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	172.79	03/2019 -	04/2019	1	-
	<u>Oil India Limited</u>								
55	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
	Total		9,553.79 -	9,533.20	2,896.64				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
56	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	982.71	04/2020 -	10/2023	42	-
	<u>National Hydro-Electric Power Corporation</u>								
57	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,394.80	7,121.50	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
58	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,186.04	09/2011 06/2018	12/2018	87	6
59	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 -	05/2019	60	-
60	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,789.00	12/2016 -	08/2019	32	-
61	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	12,079.00	01/2018 -	05/2020	28	-
	<u>Power Grid Corporation Of India Limited</u>								
62	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,932.88	2,654.96	12/2012 -	11/2018	71	-
63	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	3,190.27	2,281.28	12/2015 -	11/2018	35	-
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	206.42	145.22	03/2016 -	11/2018	32	-
65	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	225.28	148.92	02/2016 -	11/2018	33	-
66	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	340.88	229.40	03/2018 -	11/2018	8	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
67	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	630.56	09/2017 -	11/2018	14	-
68	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	206.21	11/2017 -	11/2018	12	-
69	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	215.81	03/2017 -	11/2018	20	-
70	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 -	2,534.00	2,051.63	11/2008 -	12/2018	121	-
71	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	738.48	669.46	09/2010 -	12/2018	99	-
72	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	499.90	06/2014 -	12/2018	54	-
73	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	534.02	426.98	08/2014 -	12/2018	52	-
74	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,202.20	04/2016 -	12/2018	32	-
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	419.63	06/2016 -	12/2018	30	-
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	74.71	03/2018 -	12/2018	9	-
77	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,518.90	04/2018 -	12/2018	8	-
78	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	1,420.89	07/2018 -	12/2018	5	-
79	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	287.99	161.82	06/2018 -	12/2018	6	-
80	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	1,364.00	1,237.00	12/2015 -	12/2018	36	-
81	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	1,750.00	1,324.00	06/2018 -	12/2018	6	-
82	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,538.37	10/2012 -	02/2019	76	-
83	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	2,716.40	03/2018 -	03/2019	12	-
84	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	332.96	01/2018 -	03/2019	14	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
85	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	139.34	01/2019 -	03/2019	2	-
86	EASTERN REGION STRENGTHENING SCHEME- XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	550.18	433.43	11/2016 -	06/2019	31	-
87	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	181.16	07/2017 -	06/2019	23	-
88	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	191.64	05/2017 -	06/2019	25	-
89	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	52.14	09/2018 -	06/2019	9	-
90	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	407.22	10/2017 -	09/2019	23	-
91	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	238.92	04/2018 -	11/2019	19	-
92	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	840.87	12/2018 -	12/2019	12	-
93	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,652.57	802.18	12/2018 -	12/2019	12	-
94	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	.80	09/2019 -	02/2020	5	-
95	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	13,762.80	12,714.20	08/2013 -	03/2022	103	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
96	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	506.97	12/2016 -	12/2018	24	-
97	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	309.64	11/2017 -	12/2018	13	-
	<u>Thdc India Limited</u>								
98	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	215.93	02/2014 02/2018	03/2019	61	13
99	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,672.04	02/2016 12/2020	05/2021	63	5
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,105.30	1,583.40	06/2013 -	12/2021	102	-
	Total		1,06,647.50 -	1,36,782.39	90,684.06				
	<u>HEAVY INDUSTRY</u>								

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Indira Gandhi Centre For Atomic Research</u>								
101	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37	-
	Total		1,554.00 -	1,554.00	161.86				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
102	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	58.52	02/2018 -	12/2018	10	-
103	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	71.00	05/2018 -	08/2019	15	-
	Total		516.94 -	516.94	129.52				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
104	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	1,035.16	18.99	03/2022 -	03/2023	12	-
	<u>Container Corporation Of India</u>								
105	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	139.04	03/2019 -	08/2019	5	-
106	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	410.89	03/2018 -	12/2019	21	-
107	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	289.08	03/2019 -	12/2019	9	-
108	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	2.98	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
109	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	15.79	03/2019 -	12/2019	9	-
110	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96	-
111	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	-
112	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	-
113	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	256.36	03/2020 -	03/2021	12	-
114	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	-
115	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	-
116	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
117	SAGULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	-
118	MUZAFFARPUR SAGULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	-
	<u>East Coast Railway</u>								
119	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	765.60	02/2019 -	03/2021	25	-
120	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	81.26	10/2020 -	03/2021	5	-
121	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28	-
122	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27	-
123	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147	-
124	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	574.98	06/2021 -	03/2023	21	-
	<u>Eastern Railways</u>								
125	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,620.01	843.85	03/2019 12/2009	03/2019	0	111
126	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	1,125.89	2,007.32	03/2016 -	03/2020	48	-
127	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.52	137.85	03/2016 -	03/2020	48	-
	<u>Metropolitan Rapid Transport Projects</u>								
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
129	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,329.00	03/2004 -	03/2020	192	-
	<u>North East Frontier Railway</u>								
130	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	03/2019	123	-
131	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	614.00	267.93	03/2019 -	03/2020	12	-
132	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2020	108	-
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020	12	-
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2020	12	-
135	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
136	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	-
	<u>North Eastern Railway</u>								

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
137	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,805.26	04/1999 -	12/2018	236	-
138	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	181.09	01/2019 -	02/2019	1	-
139	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	.60	03/2014 -	04/2021	85	-
140	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	.55	04/2016 -	01/2022	69	-
141	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
142	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
143	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	22.53	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
144	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	346.35	295.70	11/2018 -	12/2018	1	-
145	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	349.00	278.89	02/2019 -	03/2019	1	-
146	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	712.13	03/2015 -	03/2020	60	-
	<u>Rail Vikas Nigam Ltd.</u>								
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	373.73	03/2009 03/2009	12/2018	117	117
148	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,367.66	12/2017 -	06/2019	18	-
149	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	383.54 -	555.00	575.93	03/2010 -	12/2019	117	-
150	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	1,850.00	1,972.23	03/2008 -	03/2020	144	-
151	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	977.00	978.21	03/2019 -	03/2020	12	-
152	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	595.33	03/2016 03/2017	12/2020	57	45
153	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	942.95	887.88	03/2019 -	03/2021	24	-
154	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	894.91	12/2020 -	03/2021	3	-
155	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 245.00	1,202.70	631.11	02/2015 -	12/2021	82	-
156	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	631.78 632.00	1,195.00	653.64	12/2012 -	03/2022	111	-
157	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	931.68	03/2020 -	03/2022	24	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
158	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	943.60	122.70	03/2022 -	12/2024	33	-
159	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	335.37	03/2023 -	12/2024	21	-
160	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,866.83	03/2016 -	03/2025	108	-
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	768.02	03/2016 -	03/2025	108	-
162	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
163	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,081.06	12/2024 -	03/2026	15	-
	<u>South East Central Railway</u>								
164	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	-
	<u>South Eastern Railway</u>								
165	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	152.45	12/2016 08/2018	12/2018	24	4
166	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,151.81	375.59	03/2020 03/2020	06/2020	3	3
167	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	175.49	03/2021 03/2021	12/2021	9	9
	<u>South Western Railway</u>								
168	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	433.36	03/2017 -	03/2020	36	-
169	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,156.94	1,156.94	680.39	03/2020 03/2020	03/2021	12	12
	<u>Southern Railway</u>								
170	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71	-
171	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
172	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	-
173	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	<u>Western Railway</u>								
174	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	83.53	03/2012 -	03/2019	84	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
175	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	232.37	03/2021 03/2019	03/2020	-12	12
176	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 2,473.40	1,030.29	1,081.52	03/2022 03/2019	03/2022	0	36
177	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	606.41	03/2022 03/2019	03/2022	0	36
178	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	603.75	03/2022 03/2019	03/2022	0	36
179	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	858.96	549.56	03/2019 03/2019	03/2022	36	36
180	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	844.10	61.85	- 03/2022	03/2023	-	12
	Total		96,424.83 -	1,36,142.23	49,085.16				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
181	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
182	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
183	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
184	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
185	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
186	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
187	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67	-
188	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
189	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	247.91	10/2018 -	11/2018	1	-
190	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	174.34	214.88	03/2008 -	12/2018	129	-
191	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	884.12	02/2013 -	12/2018	70	-
192	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018	60	-
193	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	975.23	07/2013 -	12/2018	65	-
194	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	-
195	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	-
196	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	-
197	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	564.35	11/2013 -	12/2018	61	-
198	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	351.24	09/2017 -	12/2018	15	-
199	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	53.70	03/2018 -	12/2018	9	-
200	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	604.80	10/2017 -	12/2018	14	-
201	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	54.89	06/2016 -	12/2018	30	-
202	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,302.51	07/2017 -	12/2018	17	-
203	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	12/2018	86	15
204	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	12/2018	37	-
205	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	1,871.34	2,304.41	01/2018 -	12/2018	11	-
206	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018	78	-
207	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	400.35	04/2018 -	12/2018	8	-
208	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	678.87	01/2014 -	01/2019	60	-
209	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	167.98	198.82	05/2008 -	02/2019	129	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
210	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	297.81	04/2008 -	03/2019	131	-
211	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9	-
212	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2019	79	-
213	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,615.69	07/2015 -	03/2019	44	-
214	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	-
215	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	210.66	05/2018 -	03/2019	10	-
216	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	688.00	04/2018 -	03/2019	11	-
217	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	73.66	07/2018 -	03/2019	8	-
218	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31	-
219	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	934.46	104.98	03/2018 -	03/2019	12	-
220	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36	-
221	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	14.31	05/2018 -	03/2019	10	-
222	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130	-
223	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	360.84	389.08	04/2010 -	04/2019	108	-
224	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29	-
225	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	45.11	05/2018 -	04/2019	11	-
226	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	194.09	05/2018 -	04/2019	11	-
227	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	846.58	08/2018 -	04/2019	8	-
228	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	31.96	12/2017 -	04/2019	16	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
229	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	21.80	06/2018 -	04/2019	10	-
230	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	-
231	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	895.57	11/2017 -	05/2019	18	-
232	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12	-
233	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	105.70	06/2018 -	05/2019	11	-
234	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,871.89	11/2011 -	06/2019	91	-
235	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,058.04	03/2013 -	06/2019	75	-
236	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	831.33	07/2013 -	06/2019	71	-
237	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	396.59	06/2014 -	06/2019	60	-
238	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019	64	-
239	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,410.94	09/2016 -	06/2019	33	-
240	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18	-
241	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	473.93	11/2016 -	06/2019	31	-
242	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	25.84	05/2018 -	06/2019	13	-
243	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	50.67	04/2018 -	06/2019	14	-
244	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	180.17	08/2018 -	06/2019	10	-
245	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	-
246	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-
247	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	502.66	11/2018 -	07/2019	8	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
248	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	22.02	03/2019 -	07/2019	4	-
249	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	17.07	05/2019 -	08/2019	3	-
250	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	-
251	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
252	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	65.48	12/2018 -	10/2019	10	-
253	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	142.41	04/2019 -	10/2019	6	-
254	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	167.09	06/2019 -	11/2019	5	-
255	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,580.02	04/2019 -	11/2019	7	-
256	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	2.42	03/2019 -	11/2019	8	-
257	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,141.90	03/2014 -	12/2019	69	-
258	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	-
259	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2019	68	-
260	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	23.98	10/2017 -	01/2020	27	-
261	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	57.86	04/2018 -	04/2020	24	-
262	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	-	03/2020 -	04/2020	1	-
263	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	155.12	02/2020 -	05/2020	3	-
264	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	303.24	03/2020 -	05/2020	2	-
265	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	842.34	03/2020 -	05/2020	2	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
266	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2	-
267	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	121.00	03/2020 -	06/2020	3	-
268	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	325.34	03/2020 -	06/2020	3	-
269	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	-	09/2017 -	06/2020	33	-
270	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
271	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	-	03/2020 -	08/2020	5	-
272	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	289.99	03/2020 -	08/2020	5	-
273	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	177.05	03/2020 -	08/2020	5	-
274	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	211.17	06/2020 -	08/2020	2	-
275	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	9.12	03/2019 -	11/2020	20	-
276	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	-	03/2020 -	11/2020	8	-
277	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	86.58	03/2017 -	11/2020	44	-
278	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	-
279	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	-	06/2019 -	12/2020	18	-
	<u>Public Works Dept Of State</u>								
280	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	231.56	09/2017 -	11/2018	14	-
	Total		86,085.99 -	89,553.86	53,591.27				
	<u>SHIPPING AND PORTS</u>								

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Kamarajar Port Limited</u>								
281	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-
	<u>Mumbai Port Trust</u>								
282	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	-
	Total		966.39 -	927.36	412.57				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
283	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Bangalore Metro Rail Corporation Limited</u>								
284	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
285	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	163.97	11/2014 -	02/2019	51	-
286	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	146.31	08/2016 -	03/2019	31	-
287	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	-
288	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	391.23	05/2017 08/2018	03/2019	22	7
289	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	89.94	04/2018 -	07/2019	15	-
290	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	127.86	04/2019 06/2019	09/2019	5	3
291	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
292	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	540.42	197.12	07/2019 -	10/2019	3	-
293	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2019	56	-

Costing Rs.150 Crore and above

(November 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
294	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	331.12	10/2019 -	03/2020	5	-
295	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.28	03/2016 -	04/2020	49	-
296	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	34.09	06/2017 07/2017	06/2020	36	35
297	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	4.00	07/2020 09/2018	09/2020	2	24
	<u>Hindustan Steelwork Construction Limited</u>								
298	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
299	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
300	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
301	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
302	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	Total		61,045.94 -	61,564.39	4,972.89				
	Grand Total		4,73,828.94	5,67,159.59	2,67,988.64				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	03/2019	3492	102
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2019	430.45	36
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2019	365.01	45
9	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
10	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
11	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2019	258.56	36
12	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2020	172.08	120
13	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL)	NCL	06/2011	03/2018	03/2019	1131.28	12
14	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2019	510.85	36
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2020	457.77	84
16	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.5	72
17	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
18	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
19	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2020	479.53	84
20	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2019	209.78	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
22	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	36
23	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
24	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
25	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
27	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2021	337.66	24
28	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
29	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
30	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
31	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
32	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
33	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
34	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
35	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
36	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
37	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
38	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
39	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
40	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	03/2019	5907.11	39

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
41	CONSTRUCTION WORKS PHASE 4	GSL	12/2016	05/2018	01/2019	167.69	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
42	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	RCF	02/2016	12/2017	12/2018	482.85	12
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
45	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	12/2018	152.95	10

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	IGCAR	08/2016	08/2016	09/2019	1554	37

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	05/2021	466.43	7
48	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
49	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2019	352.56	27
50	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
51	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
52	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
53	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	12/2018	2899.93	19
54	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
55	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
56	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2019	861.79	70
57	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
58	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
59	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2019	3190.69	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	06/2019	2915	78
61	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2019	2465.15	72
62	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	52
63	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	12/2018	327.78	8
64	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9
65	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
66	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	12/2020	4497	24
67	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
68	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
69	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
70	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	12/2018	955	36
71	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	99
72	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2019	4824.12	76
73	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	21
74	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
75	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	11/2018	2144	71
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	12/2018	539.82	30
77	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	06/2019	522.29	31
78	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	11/2018	155.57	32
79	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
80	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	12/2018	4375.35	87

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2019	5151.37	12
82	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	11/2018	196.58	33
83	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	10/2023	8112.12	42
84	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2018	1779.29	121
85	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	32
86	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	123
87	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	28
88	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	11846	24
89	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	11/2018	2514.88	35
90	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	11/2018	305.04	20
91	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
92	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	11/2019	454.11	19
93	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	PGCIL	04/2016	06/2018	12/2018	287.99	6
94	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V	PGCIL	02/2015	06/2018	12/2018	1750	6
95	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	06/2019	175.64	9
96	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	12964.6	28
97	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	08/2019	9750.89	32
98	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
99	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
100	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	10
101	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	20
102	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
103	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	11/2018	268.8	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
105	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	23
106	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2018	197.4	9
107	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	11/2018	1071.24	14
108	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
109	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	61
110	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353	60
111	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	24
112	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	PGCIL	04/2015	04/2018	12/2018	3705.61	8
113	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	11/2018	307.18	12
114	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	102
115	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.9	111
116	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657	63
117	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	54
118	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2018	297.33	52
119	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	12/2018	330	13

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
120	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
121	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	96
122	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	61
123	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
124	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
125	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	03/2014	04/2021	1177.96	85
126	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
127	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
128	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
129	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	06/2019	1185.64	18
130	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
131	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2018	133.41	117
132	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21
133	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	81
134	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
135	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2022	1160.48	144
136	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	732.81	144
137	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
138	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
139	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2020	277.28	48
140	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
141	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
142	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
143	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2022	2288.7	12
144	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2023	2132.77	108
145	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
146	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
147	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	03/2016	03/2020	1125.89	48
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
150	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	04/1997	03/2012	03/2020	324.73	96
151	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	1180.19	123
152	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	147
153	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108
154	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2019	495.74	69
155	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
156	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
158	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2019	5300	60
159	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2019	1142	60
160	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
161	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	03/2021	2500	220
162	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RVNL	04/1995	12/2012	03/2022	631.78	111
163	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	383.54	117
164	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
166	MUNEERABAD-MAHABOONNAGAR(NL),SCR	SCR	04/1997	03/2000	03/2019	1723	228
167	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
168	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
169	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
170	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2021	1111.99	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
171	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2018	148.77	24
172	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
173	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
174	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
175	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	03/2026	16216	15
176	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
177	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
178	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
179	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	12/2019	493.17	21
180	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
181	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
182	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651	108
183	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	12/2018	309.44	36
184	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	10/2022	569.63	31
185	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
186	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2021	1763.93	19
187	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2023	1035.16	12
188	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
189	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
190	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	28
191	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2021	1172.92	27
192	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
193	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA	SER	04/1995	12/2021	12/2024	524.43	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AND EXTENSION OF LINE FRO						
194	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
195	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
196	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
197	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	03/2020	678.54	12
198	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2020	829.74	60
199	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
200	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	10/2021	1491.47	19
201	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
202	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	10/2022	622.5	66
203	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
204	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	12/2018	609.04	236
205	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	01/2022	213	69
206	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
207	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
208	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
209	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	04/2019	641.17	33
210	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	11/2020	476.56	40
211	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	01/2020	639.97	27
212	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
213	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	MORTH	02/2015	03/2015	06/2019	383.4	51
214	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	11/2018	255.75	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
215	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
216	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
217	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2018	671.3	70
218	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2018	374	67
219	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2018	485	64
220	JORBAT - BARAPANI	NHAI	01/2011	01/2014	01/2019	536	60
221	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	06/2019	575	71
222	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2018	511.54	61
223	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	12/2019	624	68
224	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108	91
225	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	06/2019	1348.2	64
226	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2019	617	79
227	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	06/2019	1724.55	75
228	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	04/2019	1916.79	29
229	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.6	33
230	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	11/2018	1175	67
231	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2018	1250	60
232	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	12/2018	953.88	65
233	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2018	571	62
234	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
235	MUZZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
236	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	11/2018	530.07	27
237	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND	NHAI	08/2014	04/2018	03/2019	822.9	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	TWO-LANE PAVED SHOULDER FROM						
238	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	12/2018	972.5	17
239	4-LANING OF SOLAPUR - MAHARASHTRA/KARNATKA SECTION	NHAI	06/2014	11/2016	06/2019	923.04	31
240	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2019	1655.01	31
241	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	12/2018	1673.7	86
242	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	04/2019	1388	8
243	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	12/2018	1055	37
244	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	12/2018	1871.34	11
245	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	02/2019	160	129
246	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2019	478.51	69
247	PANVEL-INDAPUR	NHAI	12/2011	06/2014	06/2019	942.69	60
248	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	12/2018	709	15
249	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	03/2019	425.19	30
250	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	05/2019	1387.11	18
251	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2019	563.92	18
252	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	NHAI	09/2015	03/2018	12/2018	567.51	9
253	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	12/2018	597	14
254	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	03/2019	414.51	10
255	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	05/2019	531.13	12
256	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	04/2019	593.26	11
257	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	12/2018	602.95	30
258	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	03/2019	574.28	8
259	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	04/2019	505	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
260	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	12/2018	1170.52	78
261	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	06/2019	726.67	14
262	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	03/2019	479.2	10
263	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
264	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	12/2018	516.13	8
265	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
266	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	06/2019	707.82	10
267	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	04/2019	804.97	10
268	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	NHAI	05/2015	05/2017	06/2019	581.84	25
269	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	12/2018	245	129
270	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2019	217.61	108
271	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2019	208	131
272	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2019	225	130
273	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	03/2019	946	9
274	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	05/2019	1083	11
275	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
276	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2019	934.46	12
277	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	07/2019	1423.96	8
278	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	10/2019	2136.97	10
279	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	06/2019	596.67	13
280	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
281	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
282	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
283	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
284	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	11/2019	446.17	8
285	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
286	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
287	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
288	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
289	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29
290	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
291	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	RINL	07/2015	07/2018	01/2019	465.85	6
292	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	06/2019	15525	49
293	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343	29
294	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	05/2019	3127.3	13
295	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
296	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	06/2019	1154.18	18
297	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	02/2019	320.66	6
298	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	09/2019	2858	21
299	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12
300	FORGED WHEEL PLANT	RINL	04/2014	09/2018	03/2019	1682.85	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
301	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
302	MADHYA PRADESH ACCESS (LOT1)	BSNL	08/2017	05/2018	12/2018	215.3	7
303	MAHARASHTRA NODAL (LOT 1)	BSNL	08/2017	04/2018	12/2018	159.3	8
304	MAHARASHTRA CORE (LOT1)	BSNL	08/2017	04/2018	12/2018	167.68	8

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
306	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
307	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
308	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	04/2020	171.86	49
309	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	03/2019	156.57	31
310	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
311	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
312	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2019	216.69	56
313	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15
314	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
315	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	12/2018	151.33	15
316	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSCL	02/2014	12/2016	12/2018	787.29	24
317	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	03/2019	388	22
318	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	02/2019	270.83	51
319	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2019	165.23	77
320	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
321	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
322	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
8	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
12	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
13	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE
(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1577.15	715.36
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9394.8	5475.21
22	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
23	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
25	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37
26	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
27	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
28	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2534	754.71
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	534.02	236.69
32	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
33	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4401.9	2744.9
34	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
35	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
36	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
37	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
38	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47
40	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09
41	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
42	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
43	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
44	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9141.97	4387.55
45	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
46	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
47	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
48	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	2514.88	3190.27	675.39
49	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
50	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
51	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
52	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4105.3	1613.72
53	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	PGCIL	08/2008	02/2013	771	1624	853
54	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
55	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6652.57	1541.24
56	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
57	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
58	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	297.32	614	316.68
59	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
60	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	920	764.45

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3020.94	1987.87
62	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	792.46	1320	527.54
63	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
64	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
65	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
66	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
67	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
68	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
69	HATHUA-BHATNI (N L) (NER)	NER	04/2005	12/2022	230.03	770.08	540.05
70	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	245.39	125.39
71	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	06/2018	218.19	413.56	195.37
72	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2713.09	2288.49
73	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	732.81	1850	1117.19
74	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	749	271.12
75	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.77	1538.12
76	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	4968	2574.53
77	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
78	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
79	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
80	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
82	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1156.41	831.68

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
84	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	3230.02	5820	2589.98
85	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
86	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
87	MM FROM PANSKURA-GHATAL NL	SER	04/2011	N.A.	276.69	426	149.31
88	MM FROM BURAMARA-CHAKULIA	SER	04/2008	N.A.	466.48	1000	533.52
89	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
90	MUZAFFARPUR SGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
91	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
92	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
93	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
94	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
95	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	609.04	1807.88	1198.84
96	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
97	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	SR	02/2003	03/2009	199.55	330.32	130.77
98	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1420.39	834.46
99	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
100	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1260.61	678.48
101	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1750	1036.52
102	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
103	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
104	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	1013.45	1428	414.55
105	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1151.81	181.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
107	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
108	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
109	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
110	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
111	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
112	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
113	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	544.72	137.73
114	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
115	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
116	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	246.07	398.93	152.86
117	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	551	237
118	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
119	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
120	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
121	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
122	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
123	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	369.83	178.11
124	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
125	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
126	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	283.55	451	167.45
127	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1733.2	838.2
128	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
130	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
131	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
132	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
133	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
134	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
135	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
136	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	785.87	237.87
137	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1474.47	1102.33
138	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
139	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
140	CHHAPRA-MUZAFFARPUR (NL)	ECOR	04/2006	N.A.	378.56	2614.36	2235.8
141	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	325	729.92	404.92
142	BIHTA-AURANGABAD (NL)	ECOR	04/2008	N.A.	326.2	2995.01	2668.81
143	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
144	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECOR	04/2008	N.A.	445.25	2860.55	2415.3
145	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	620.57	2626.98	2006.41
146	ARA-BHABHUA ROAD (NL)	SER	04/2008	N.A.	633.87	2396.88	1763.01
147	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
148	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	525.81	216.37
149	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
150	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
151	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	349	106.91
153	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
154	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
155	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
156	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2878.97	796.22
157	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
158	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
159	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
160	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	435	239.36
161	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
162	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
163	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	845.58	220.58
164	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24.	SER	04/1998	03/2022	1027.4	2373	1345.6
165	GEVRA ROAD PENDRA ROAD	SECR	02/2014	03/2022	2288	4919	2631
166	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
167	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1279	407
168	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	556.54	1342.46	785.92
169	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	403	174
170	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	566.41	237.02
171	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	528.26	347.44
172	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	624.47	3550	2925.53
173	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
174	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	795.01	384.93
176	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
177	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
178	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	1142	3374	2232
179	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
180	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
181	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
182	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.96	195.95
183	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1025	900.57
184	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1216	386.26
185	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1103.04	229.33
186	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
187	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
188	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
189	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
190	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
191	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
193	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
194	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	383.54	555	171.46
195	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	631.78	1195	563.22
196	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	369.9	1581.53	1211.63
197	GHUTIASHARIF-CANNING (ER)	ER	04/2009	12/2011	193.08	612.45	419.37

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
199	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
200	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
201	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	13809	9354.83
202	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3798.8	875.67
203	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	3040	1859.81
204	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	589.15	426.28
205	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
206	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
207	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
208	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
209	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
210	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	625	338
211	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
212	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
213	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
214	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
215	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	298.7	114.64
216	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	665.75	165.79
217	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
218	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	ER	04/2009	02/2012	259.51	533.59	274.08
219	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	1116	462.81
220	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
221	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1620.01	431.1
222	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
223	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
224	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
225	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
226	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
227	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
228	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
229	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
230	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
231	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
232	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
233	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
234	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
235	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
236	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
237	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
238	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
239	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
240	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
241	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
242	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(NOVEMBER 2018)

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
SHIPPING AND PORTS							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
243	ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
244	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
245	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
246	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
247	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
248	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
249	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
250	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
251	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(NOVEMBER 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	03/2019	3492.00	6100.00	2608	102

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	5245.96	657.67	9
8	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	723.40	413.59	52
9	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
10	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
11	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2019	861.79	1577.15	715.36	70

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(NOVEMBER 2018)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	6652.57	1541.24	12
14	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	1,1846.00	1,2739.82	893.82	24
15	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	11/2018	2514.88	3190.27	675.39	35
16	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2018	1779.29	2534.00	754.71	121
17	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	1,2532.44	1,3740.53	1208.09	10
18	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	1,4366.58	1,5164.05	797.47	20
19	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353.00	7998.00	2645	60
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	602.44	165.76	24
21	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	4105.30	1613.72	102
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.90	6179.96	3683.06	111
23	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657.00	4401.90	2744.9	63
24	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	639.46	151.97	54
25	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2018	297.33	534.02	236.69	52
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9394.80	5475.21	147
27	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	738.48	260.79	99
28	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2019	4824.12	5071.94	247.82	76
29	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	1,1638.55	1,2865.92	1227.37	21
30	NORTH- EAST NORTH WESTERN	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,3762.80	2632.61	103

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	INTERCONNECTOR I PROJECT								
31	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	11/2018	2144.00	2932.88	788.88	71
32	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	1891.41	526.89	32
33	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	867.82	93
34	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	12/2018	4375.35	8150.00	3774.65	87
35	TRANSMISSION SYSTEM ASSOCIATED WITH IPDS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	12/2018	955.00	1364.00	409	36
36	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	1,2964.60	1,3731.26	766.66	28
37	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	1,5095.67	6402.7	123
38	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9141.97	4387.55	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
39	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
40	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	1342.46	785.92	96
41	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	3550.00	2925.53	61
42	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	939.00	414.57	36
43	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
44	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651.00	1009.00	358	108
45	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
46	LALITPUR-SATNA-REWA-SINGRULI	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	NL, (NCR)								
47	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1156.41	831.68	96
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	1180.19	3040.00	1859.81	123
49	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	3798.80	875.67	147
50	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	1,3809.00	9354.83	108
51	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTP	04/2006	06/2013	03/2019	495.74	734.01	238.27	69
52	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
53	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
54	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
55	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
56	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	06/2019	1185.64	1844.47	658.83	18
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2018	133.41	385.00	251.59	117
58	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
59	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	4968.00	2574.53	81
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	749.00	271.12	96
61	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	732.81	1850.00	1117.19	144
62	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	1116.00	462.81	60
63	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	3000.00	673.48	79
65	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
66	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2019	1142.00	3374.00	2232	60
67	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
68	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	03/2021	2500.00	2,7949.00	25449	220
69	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	1195.00	563.22	111
70	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	383.54	555.00	171.46	117
71	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
72	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
73	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2021	1111.99	1539.28	427.29	25
74	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2018	148.77	377.00	228.23	24
75	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2020	829.74	1216.00	386.26	60
76	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
77	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	12/2018	309.44	525.81	216.37	36
78	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	810.02	108.41	28
79	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
80	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(NOVEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
81	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
82	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	12/2018	609.04	1807.88	1198.84	236

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
83	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2019	217.61	360.84	143.23	108
84	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	12/2018	1055.00	1601.77	546.77	37
85	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108.00	2288.00	1180	91
86	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.60	1544.00	277.4	33

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
87	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
88	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343.00	488.40	145.4	29

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
89	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
90	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs.150 Crore and above								
(November 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2018	.00	56
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2018	.00	67
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	10/2018	.00	101
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2018	.00	61
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	11/2018	.00	27
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	01/2019	.00	60
11	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2018	.00	62
12	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2018	.00	54
13	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	06/2019	.00	71
14	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
15	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	03/2019	.00	79
16	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	12/2019	.00	68
17	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	-	.00	0
19	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	12/2018	.00	70
20	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	-	.00	0
21	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
22	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
23	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	03/2019	.00	11
24	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	06/2019	.00	31
25	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	12/2018	.00	65
26	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	12/2018	.00	17
27	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	-	.00	0
28	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	60
29	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
30	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	-	.00	0
31	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
32	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
33	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
34	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2018	.00	60
35	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	06/2019	.00	64
36	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	04/2019	.00	8
37	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	-	.00	0
38	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	10/2015	.00	13

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above								
(November 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	-	.00	0
40	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
41	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	06/2019	21.90	33
42	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
43	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	01/2019	.00	0
44	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	-	.00	0
45	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	12/2018	51.83	37
46	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	03/2019	.00	31
47	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	01/2019	.00	0
48	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	-	.00	0
49	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	12/2018	.00	86
50	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
51	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	06/2019	.00	75
52	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
53	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	12/2018	.00	11
54	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	04/2019	.00	29
55	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	03/2019	.00	44
56	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
57	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	04/2019	.00	0
58	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,159.00	06/2015	-	.00	0
59	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	06/2019	106.50	91

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above

(November 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	05/2019	.00	0
61	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
62	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	12/2019	.00	69
63	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
64	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56	71
	Total		76,530.12 -	81,310.94				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
65	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88	0
	<u>Mumbai Port Trust</u>							
66	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		610.89 -	945.44				
	Grand Total		77,141.01	82,256.38				

Sector-Wise Ongoing Project's Details

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.11.2018)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	0.00 (0.00) [0]
3	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	0.00 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
5	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	0.00 (0.20) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	0.00 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	0.00 (0.00) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
9	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [0/0]	601.02 (-) [601.02]	36.93 (0.00) [0]
10	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2019]	272.19 (-) [272.19]	76.88 (0.00) [0]
	<u>Petroleum</u>				
11	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [4/2021]	466.00 (-) [466.00]	1.12 (0.00) [0]
13	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2021]	384.58 (-) [384.58]	38.79 (0.00) [0]
14	FIELD DEVELOPMENT OF NLP BLOCK KG-ONN-2003,	4/2017	9/2018	420.76	27.54

	NAGAYALANKA-KG		(2/2019) [2/2019]	(207.80) [207.80]	(-212.96) [5]
15	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (8/2021) [8/2021]	34,012.00 (-) [34,012.00]	1,450.26 (0.00) [14]
16	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [4/2022]	355.00 (-) [355.00]	0.00 (0.00) [0]
17	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
18	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	540.49 (0.00) [0]
19	VVSPCL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	241.80 (0.00) [0]
	<u>Railways</u>				
20	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
21	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.07 (0.00) [0]
22	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
23	GUNTUR-GUNTAKAL	4/2016	3/2022 (3/2023) [3/2023]	3,631.00 (-) [3,631.00]	124.49 (0.00) [12]
24	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (3/2023) [3/2023]	1,045.20 (-) [2,120.16]	289.91 (1,074.96) [168]
25	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (2,499.71) [2,499.71]	183.68 (0.00) [0]
26	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	2.98 (0.50) [21]
27	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
28	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (3/2022) [3/2022]	2,288.70 (-) [2,288.70]	375.28 (0.00) [12]
29	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [10/2018]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
30	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	7/2006	3/2008 (-) [3/2020]	732.81 (-) [1,850.00]	1,972.23 (1,117.19) [144]
31	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	249.33 (302.41) [0]
32	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	931.68 (0.00) [24]
	<u>Road Transport And Highways</u>				
33	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	0.00 (0.00) [0]

34	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
35	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	0.00 (0.00) [0]
36	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
37	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	5/2013 (-) [0/0]	1,585.00 (-) [1,585.00]	2,159.63 (0.00) [0]
38	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
39	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	0.00 (0.00) [0]
40	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
41	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [3/2021]	1,532.62 (-) [1,532.62]	0.00 (0.00) [0]
42	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [0/0]	648.33 (-) [648.33]	0.00 (0.00) [0]
43	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [11/2018]	1,134.97 (-) [1,134.97]	16.31 (0.00) [0]
44	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	/ (-) [0/0]	480.21 (-) [480.21]	0.00 (0.00) [0]
45	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR	7/2015	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
46	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A	12/2014	2/2015 (-) [0/0]	201.12 (201.00) [201.12]	0.00 (0.00) [0]
47	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	1/2014	7/2014 (-) [0/0]	361.30 (-) [207.40]	44.08 (-153.90) [0]
48	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	5/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
49	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	11/2014 (-) [0/0]	170.21 (-) [170.21]	5.65 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [0/0]	565.09 (-) [565.09]	0.00 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	/ (-) [0/0]	175.03 (-) [175.00]	0.00 (-0.03) [0]
53	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	2/2015	2/2017 (-) [0/0]	241.61 (-) [241.61]	7.71 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF NH-167 FROM	2/2015	4/2015	224.83	0.00

	KM 70		(-) [0/0]	(-) [224.83]	(0.00) [0]
55	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [0/0]	271.45 (-) [271.45]	0.00 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [503.10]	15.10 (-145.22) [0]
57	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	/ (-) [0/0]	266.00 (-) [266.00]	0.00 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	3/2015	9/2015 (-) [0/0]	309.01 (-) [309.01]	0.00 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	2/2014	7/2014 (-) [0/0]	258.99 (-) [258.99]	16.54 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	2/2014	6/2014 (-) [0/0]	417.61 (-) [417.61]	0.00 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	11/2014	2/2017 (-) [0/0]	297.78 (330.00) [330.00]	0.00 (32.22) [0]
62	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
63	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [0/0]	1,959.00 (-) [1,959.00]	0.00 (0.00) [0]
64	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [0/0]	1,323.15 (-) [1,323.15]	0.00 (0.00) [0]
65	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [0/0]	1,550.98 (-) [1,550.98]	0.00 (0.00) [0]
66	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	2,993.77 (0.00) [0]
67	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	5.37 (145.48) [2]
68	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [12/2018]	571.00 (-) [571.00]	582.52 (0.00) [62]
69	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
70	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018 (-) [1/2019]	465.85 (-) [465.85]	244.25 (0.00) [6]
71	CENTRAL DISPATCH YARD	8/2015	8/2018 (-) [2/2019]	320.66 (-) [320.66]	115.36 (0.00) [6]
72	COKE OVEN BATTERY-5	12/2011	12/2017 (-) [9/2019]	2,858.00 (-) [2,500.00]	1,013.76 (-358.00) [21]
73	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016 (-) [3/2019]	343.00 (-) [488.40]	239.65 (145.40) [29]
	<u>Urban Development</u>				

74	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [3/2019]	206.58 (-) [206.58]	0.02 (0.00) [0]
75	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
76	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [157.84]	134.62 (0.00) [0]
77	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
<u>ARUNACHAL PRADESH</u>					
<u>Petroleum</u>					
78	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019 (-) [12/2018]	247.52 (-) [247.52]	139.42 (0.00) [-2]
<u>Power</u>					
79	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (3/2019) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,838.94 (3,683.06) [111]
80	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,385.81 (13,211.01) [0]
<u>Road Transport And Highways</u>					
81	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
82	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
83	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
84	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
85	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
86	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
87	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
88	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
89	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	38.50 (0.00) [0]
90	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
91	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
92	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]

93	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
94	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
95	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
96	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
97	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
98	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
99	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
100	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
101	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
102	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
103	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]
104	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
105	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
106	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
107	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
108	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
109	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
110	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
111	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (3/2019) [3/2019]	2,465.15 (-) [2,378.86]	2,107.69 (-86.29) [72]
112	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	69.88

			(-) [2/2020]	(-) [557.00]	(0.00) [0]
113	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	268.88 (0.00) [0]
114	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
115	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	60.44 (127.41) [70]
116	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	208.63 (0.00) [0]
117	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	1.65 (0.00) [0]
118	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,208.92 (0.00) [0]
119	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	98.10 (-5.15) [0]
120	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Power</u>				
121	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [12/2018]	4,375.35 (8,150.00) [8,150.00]	7,186.04 (3,774.65) [87]
	<u>Railways</u>				
122	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (-) [551.00]	595.01 (237.00) [0]
123	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	193.12 (-50.32) [-24]
124	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [6/2018]	3,230.02 (4,857.00) [5,820.00]	5,224.22 (2,589.98) [0]
125	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	163.08 (-49.96) [0]
126	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (-) [398.93]	264.69 (152.86) [0]
127	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	538.17 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
128	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
129	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
130	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]
131	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-)	223.30 (-)	0.00 (0.00)

			[0/0]	[223.30]	[0]
132	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
133	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
134	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2018]	289.99 (-) [289.99]	0.00 (0.00) [0]
135	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
136	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
137	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
138	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2019]	217.61 (-) [360.84]	389.08 (143.23) [108]
139	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [2/2019]	160.00 (-) [167.98]	198.82 (7.98) [129]
140	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
141	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
142	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
143	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	0.00 (0.00) [0]
144	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
145	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [361.00]	410.32 (81.00) [0]
146	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
147	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
148	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [385.13]	209.80 (185.32) [0]
149	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [0]
150	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	245.83 (0.00) [0]
151	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2019]	208.00 (-) [230.00]	297.81 (22.00) [131]

152	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [4/2019]	225.00 (-) [225.00]	312.79 (0.00) [130]
153	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [12/2018]	245.00 (174.34) [174.34]	214.88 (-70.66) [129]
154	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
155	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>BIHAR</u>				
	<u>Petroleum</u>				
156	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	385.61 (0.00) [-10]
157	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	28.18 (0.00) [0]
158	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	1.88 (0.00) [0]
159	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	0.00 (0.00) [0]
160	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [11/2018]	822.66 (-) [822.66]	809.78 (0.00) [0]
161	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	3.64 (0.00) [0]
162	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	0.00 (0.00) [0]
163	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [6/2020]	324.00 (-) [324.00]	78.63 (0.00) [0]
	<u>Power</u>				
164	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	4/2016	6/2019 (-) [6/2019]	790.13 (-) [790.30]	502.54 (0.17) [0]
165	BARH STPP(3X660MW) NTPC	2/2005	1/2011 (4/2021) [4/2021]	8,692.97 (15,095.67) [15,095.67]	15,031.14 (6,402.70) [123]
166	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	5/2014 (-) [5/2019]	5,353.00 (-) [7,998.00]	7,128.72 (2,645.00) [60]
167	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	1/2018 (-) [5/2020]	12,964.60 (-) [13,731.26]	12,079.00 (766.66) [28]
168	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	12/2016 (-) [12/2018]	436.68 (-) [602.44]	506.97 (165.76) [24]
	<u>Railways</u>				
169	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [2,396.88]	0.39 (1,763.01) [0]
170	ARARIA-SUPAUL (NL)	4/2008	/ (-) [3/2023]	1,605.17 (-) [1,605.17]	0.19 (0.00) [-]

171	BIHTA-AURANGABAD (NL)	4/2008	/	326.20	1.68
			(-)	(-)	(2,668.81)
			[0/0]	[2,995.01]	[0]
172	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	378.56	111.71
			(-)	(-)	(2,235.80)
			[3/2022]	[2,614.36]	[-]
173	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00
			(-)	(-)	(-67.92)
			[0/0]	[339.00]	[0]
174	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-)	(-)	(0.00)
			[0/0]	[205.00]	[0]
175	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/	329.39	759.20
			(-)	(-)	(237.02)
			[12/2021]	[566.41]	[-]
176	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	0.00
			(-)	(-)	(2,415.30)
			[0/0]	[2,860.55]	[0]
177	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	13.00
			(-)	(-)	(154.16)
			[0/0]	[367.17]	[0]
178	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	330.82
			(-)	(-)	(1,538.12)
			[3/2023]	[2,066.77]	[-]
179	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	876.49
			(-)	(-)	(831.68)
			[3/2020]	[1,156.41]	[96]
180	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	40.00
			(-)	(-)	(237.87)
			[3/2020]	[785.87]	[0]
181	KATIHAR - JOGBANI (GC)(NEFR)	9/2001	12/2010	792.46	928.50
			(-)	(-)	(527.54)
			[0/0]	[1,320.00]	[0]
182	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	183.72
			(-)	(-)	(426.28)
			[3/2022]	[589.15]	[-]
183	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	4.11
			(-)	(-)	(26.24)
			[3/2020]	[360.00]	[-]
184	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	0.00
			(-)	(-)	(0.00)
			[10/2021]	[1,200.20]	[19]
185	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	640.78
			(-)	(-)	(16.61)
			[3/2020]	[516.02]	[0]
186	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.38
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
187	MAHARAJGANJ-MASRAKH (NL) - NER	4/2003	6/2018	218.19	364.21
			(-)	(-)	(195.37)
			[10/2018]	[413.56]	[0]
188	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	495.40
			(-)	(283.95)	(271.12)
			[3/2020]	[749.00]	[96]
189	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.41
			(-)	(-)	(715.09)
			[0/0]	[926.09]	[0]
190	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	0.00
			(-)	(-)	(454.09)
			[3/2022]	[1,185.73]	[12]
191	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.58

			(-) [0/0]	(-) [281.30]	(0.00) [0]
192	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.52
			(-) [0/0]	(-) [228.05]	(0.00) [0]
193	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	538.21
			(-) [0/0]	(-) [559.91]	(227.76) [0]
194	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.00
			(-) [0/0]	(-) [2,626.98]	(2,006.41) [0]
195	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	928.89
			(-) [3/2020]	(-) [2,145.00]	(1,612.13) [12]
196	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	11/2001	2/2016	624.47	97.63
			(-) [3/2021]	(-) [3,550.00]	(2,925.53) [61]
197	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	462.75
			(-) [12/2018]	(-) [528.26]	(347.44) [-]
198	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	0.00
			(-) [10/2021]	(-) [1,491.47]	(0.00) [19]
199	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	1.81
			(-) [3/2022]	(-) [1,215.54]	(471.50) [12]
200	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	253.10
			(-) [3/2021]	(-) [729.92]	(404.92) [-]
201	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	338.44
			(-) [3/2021]	(-) [1,474.47]	(1,102.33) [-]
202	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	0.00
			(-) [0/0]	(-) [380.00]	(0.00) [0]
203	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.17
			(-) [0/0]	(-) [2,393.23]	(1,714.61) [0]
	Road Transport And Highways				
204	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013	351.54	351.23
			(-) [0/0]	(-) [351.54]	(0.00) [0]
205	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	564.35
			(-) [12/2018]	(-) [511.54]	(0.00) [61]
206	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-) [0/0]	(-) [375.09]	(0.00) [0]
207	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	831.33
			(-) [6/2019]	(-) [575.00]	(0.00) [71]
208	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	77.43
			(-) [6/2019]	(-) [581.84]	(0.00) [25]
209	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	0.00
			(-) [0/0]	(-) [288.24]	(0.00) [0]
210	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-) [0/0]	(-) [2,598.00]	(0.00) [0]
211	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-	3/2017	3/2020	235.48	0.00

	ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE		(-) [3/2020]	(-) [227.77]	(-7.71) [0]
212	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	0.00
			(-) [0/0]	(-) [496.20]	(0.00) [0]
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016	683.83	0.00
			(-) [0/0]	(-) [683.83]	(0.00) [0]
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016	369.77	0.00
			(-) [0/0]	(-) [369.77]	(0.00) [0]
215	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	553.30	0.00
			(-) [0/0]	(-) [553.30]	(0.00) [0]
216	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	178.85	0.00
			(-) [0/0]	(-) [178.85]	(0.00) [0]
217	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45	28.96
			(-) [12/2019]	(-) [1,167.45]	(0.00) [-]
218	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41	0.00
			(-) [10/2020]	(-) [642.41]	(0.00) [-]
219	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018	322.09	57.86
			(-) [4/2020]	(-) [322.09]	(0.00) [24]
220	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016	1,408.85	0.00
			(-) [0/0]	(-) [1,408.85]	(0.00) [0]
221	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/	814.04	229.41
			(-) [1/2020]	(-) [814.04]	(0.00) [-]
222	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07	0.00
			(-) [0/0]	(-) [556.07]	(0.00) [0]
223	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019	1,041.10	159.02
			(-) [4/2019]	(-) [1,041.10]	(0.00) [0]
224	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014	574.00	768.62
			(-) [9/2018]	(-) [574.00]	(0.00) [0]
225	PATNA-MUZZAFFARPUR	8/2010	2/2013	671.30	884.12
			(-) [12/2018]	(-) [671.30]	(0.00) [70]
226	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016	1,742.01	0.00
			(-) [0/0]	(-) [1,742.01]	(0.00) [0]
227	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/	573.70	0.00
			(-) [0/0]	(-) [573.70]	(0.00) [0]
228	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	3/2014	377.64	0.00
			(-) [0/0]	(-) [377.64]	(0.00) [0]
229	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014	278.39	0.00
			(-) [0/0]	(-) [278.39]	(0.00) [0]
230	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/	478.35	0.00
			(-) [0/0]	(-) [478.35]	(0.00) [0]
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-	1/1991	/	319.68	0.00
			(-)	(-)	(0.00)

	104		[0/0]	[319.68]	[0]
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
233	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [282.41]	67.52 (0.00) [0]
234	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [358.22]	188.71 (0.00) [0]
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/2013	8/2014 (-) [0/0]	322.01 (-) [322.01]	0.00 (0.00) [0]
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	0.00 (0.00) [0]
237	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
238	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
239	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [0/0]	950.64 (-) [950.64]	0.00 (0.00) [0]
240	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	0.00 (0.00) [0]
241	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [10/2019]	399.54 (-) [399.54]	142.41 (0.00) [6]
242	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [3/2019]	854.80 (-) [854.80]	545.46 (0.00) [-]
243	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [12/2018]	516.13 (-) [516.13]	400.35 (0.00) [8]
244	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
	<u>Urban Development</u>				
245	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (7/2017) [6/2020]	496.18 (496.00) [498.99]	34.09 (2.81) [36]
246	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
247	AMERA OC RCE	2/2015	3/2018 (-) [3/2018]	335.97 (-) [335.97]	52.39 (0.00) [0]
248	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	56.54 (0.00) [0]
249	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016 (-) [3/2019]	198.59 (-) [198.59]	169.50 (0.00) [36]
250	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2019]	258.56 (-) [258.56]	163.85 (0.00) [36]

251	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	58.15 (0.00) [0]
252	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	74.81 (0.00) [0]
253	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	3.81 (0.00) [0]
254	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,842.98 (0.00) [0]
255	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2020]	152.43 (459.49) [459.49]	172.27 (307.06) [60]
256	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	5.16 (0.00) [72]
257	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	1,902.85 (0.00) [0]
258	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
259	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
260	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2020]	321.50 (-) [321.50]	202.68 (0.00) [72]
261	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.13 (0.00) [0]
262	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
263	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	0.00 (0.00) [0]
	<u>Power</u>				
264	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	6/2017 (6/2019) [6/2019]	11,846.00 (-) [12,739.82]	10,490.56 (893.82) [24]
265	TALAIPELLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,293.72 (0.00) [0]
	<u>Railways</u>				
266	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (-) [12/2019]	872.00 (-) [1,279.00]	0.00 (407.00) [0]
267	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	4/1995	12/2012 (-) [3/2022]	631.78 (632.00) [1,195.00]	653.64 (563.22) [111]
268	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [3/2022]	2,288.00 (-) [4,919.00]	67.00 (2,631.00) [0]
269	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [3/2021]	1,973.00 (-) [1,973.00]	78.00 (0.00) [0]
270	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM	4/2011	3/2022	1,471.93	0.00

			(-) [3/2022]	(-) [543.00]	(-928.93) [0]
271	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [0/0]	3,055.00 (-) [3,055.00]	600.00 (0.00) [0]
272	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2020]	1,160.00 (1,160.83) [1,160.83]	571.51 (0.83) [0]
273	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
274	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [3/2020]	1,402.02 (-) [758.09]	849.72 (-643.93) [0]
275	SALKA ROAD -ANUPNAGAR LINE DOUBLING	9/2006	3/2010 (-) [12/2019]	383.54 (-) [555.00]	575.93 (171.46) [117]
	<u>Road Transport And Highways</u>				
276	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [0/0]	1,029.96 (-) [1,029.96]	0.00 (0.00) [0]
277	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	12/2010	12/2012 (-) [0/0]	169.26 (-) [169.26]	0.00 (0.00) [0]
278	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [6/2019]	726.67 (-) [726.67]	50.67 (0.00) [14]
279	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	7.21 (0.00) [0]
280	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [6/2019]	596.67 (-) [596.67]	25.84 (0.00) [13]
281	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.	10/2014	3/2015 (-) [0/0]	213.47 (-) [213.47]	0.00 (0.00) [0]
282	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	0.00 (0.00) [0]
283	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.	12/2014	/ (-) [0/0]	394.20 (-) [394.20]	0.00 (0.00) [0]
284	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	0.00 (0.00) [0]
285	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV	10/2014	3/2015 (-) [0/0]	298.34 (-) [298.34]	0.00 (0.00) [0]
286	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	3/2015 (-) [0/0]	262.54 (-) [262.54]	0.00 (0.00) [0]
287	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	/ (-) [0/0]	422.34 (-) [422.34]	22.25 (0.00) [0]
	<u>Steel</u>				
288	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020 (-) [6/2020]	818.00 (-) [818.00]	31.60 (0.00) [0]
289	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015 (-) [0/0]	188.93 (-) [188.93]	124.84 (0.00) [0]

290	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (6/2019) [6/2019]	15,525.00 (-) [15,525.00]	14,485.63 (0.00) [49]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
291	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,449.66 (-243.77) [5]
	<u>DELHI</u>				
	<u>Health And Family Welfare</u>				
292	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [0/0]	204.44 (-) [204.44]	237.80 (0.00) [0]
293	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [0/0]	293.65 (-) [293.65]	237.86 (0.00) [0]
294	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [0/0]	156.56 (-) [156.56]	22.59 (0.00) [0]
295	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [0/0]	414.11 (-) [414.11]	141.00 (0.00) [0]
	<u>Heavy Industry</u>				
296	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	8/2016 (-) [9/2019]	1,554.00 (-) [1,554.00]	161.86 (0.00) [37]
	<u>Power</u>				
297	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (-) [6/2019]	1,394.52 (-) [1,394.52]	191.64 (0.00) [25]
298	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)	5/2015	10/2018 (-) [10/2018]	780.33 (-) [780.33]	516.25 (0.00) [0]
	<u>Railways</u>				
299	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [0/0]	295.68 (-) [295.68]	1.20 (0.00) [0]
300	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [0/0]	156.65 (-) [197.17]	56.10 (40.52) [0]
	<u>Road Transport And Highways</u>				
301	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [7/2018]	771.18 (-) [7,558.00]	261.77 (6,786.82) [0]
	<u>Telecommunications</u>				
302	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	172.30 (0.00) [0]
	<u>Urban Development</u>				
303	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2020) [6/2020]	197.33 (-) [197.33]	10.14 (0.00) [14]
304	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	647.07 (0.00) [0]
305	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [11/2019]	271.90 (-) [271.90]	4.44 (0.00) [0]
306	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [6/2019]	188.00 (-) [188.00]	85.71 (0.00) [0]

307	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,270.32 (0.00) [0]
308	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2020]	1,219.21 (-) [1,592.00]	331.12 (372.79) [5]
309	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	3.36 (0.00) [0]
310	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,439.23]	3,581.53 (175.23) [0]
311	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/ (-) [0/0]	392.00 (-) [392.00]	0.00 (0.00) [0]
312	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (-) [0/0]	422.00 (-) [422.00]	0.00 (0.00) [0]
313	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]
314	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (-) [0/0]	248.20 (-) [248.20]	1.21 (0.00) [0]
	<u>GOA</u>				
	<u>Defence Production</u>				
315	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020 (-) [8/2020]	285.95 (286.00) [291.29]	51.87 (5.34) [0]
316	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018 (1/2019) [1/2019]	167.69 (168.00) [170.37]	86.93 (2.68) [8]
	<u>Health And Family Welfare</u>				
317	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [0/0]	249.01 (-) [249.01]	17.00 (0.00) [0]
	<u>Road Transport And Highways</u>				
318	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [280.16]	16.06 (0.00) [0]
319	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	10.72 (0.00) [0]
320	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM- MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	0.00 (0.00) [0]
321	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	16.10 (0.00) [0]
322	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	38.33 (0.00) [0]
323	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	0.00 (0.00) [0]
324	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	0.00 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
325	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11,459.00	12,707.00

			(11/2016) [6/2020]	(16,580.00) [16,580.00]	(5,121.00) [54]
	<u>Petroleum</u>				
326	ANKLESHWAR BARODA PIPELINE PROJECT	7/2014	3/2018 (-) [3/2018]	199.95 (-) [199.95]	156.83 (0.00) [0]
327	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [0/0]	588.20 (-) [588.20]	0.00 (0.00) [0]
328	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [9/2019]	3,380.00 (-) [3,380.00]	1,151.10 (0.00) [0]
329	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [12/2018]	327.78 (-) [200.00]	110.98 (-127.78) [8]
330	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	3.67 (0.00) [0]
331	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [2/2020]	906.00 (-) [906.00]	12.74 (0.00) [0]
332	GAMJI REDEVELOPMENT PROJECT	5/2015	11/2019 (-) [11/2019]	1,671.22 (567.22) [567.22]	449.95 (-1,104.00) [0]
333	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	67.71 (0.00) [0]
334	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (3/2026) [3/2026]	1,162.56 (1,162.56) [1,162.56]	285.28 (0.00) [0]
335	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [0/0]	279.00 (-) [279.00]	200.05 (0.00) [0]
	<u>Power</u>				
336	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [6/2019]	193.14 (-) [193.14]	2.50 (0.00) [0]
337	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (-) [6/2019]	175.64 (-) [175.64]	52.14 (0.00) [9]
338	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)	7/2016	12/2018 (-) [12/2018]	300.94 (-) [300.94]	194.26 (0.00) [0]
339	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [12/2018]	330.00 (-) [330.00]	309.64 (0.00) [13]
	<u>Railways</u>				
340	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [975.62]	623.78 (0.00) [0]
341	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2020) [3/2020]	829.74 (416.86) [385.60]	500.42 (-444.14) [0]
342	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [203.00]	202.29 (85.64) [0]
343	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (-) [3/2019]	551.51 (-) [551.51]	257.05 (0.00) [0]
344	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-)	318.24 (-)	83.53 (3.38)

			[3/2019]	[321.62]	[84]
345	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (-) [3/2020]	691.84 (-) [691.84]	15.31 (0.00) [0]
346	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	101.07 (0.00) [0]
347	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
348	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2022) [3/2023]	844.10 (-) [844.10]	61.85 (0.00) [-]
349	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	289.08 (0.00) [9]
350	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
351	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,548.66 (-) [1,548.66]	835.70 (0.00) [0]
352	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2019) [3/2022]	320.66 (1,378.12) [858.96]	549.56 (538.30) [36]
353	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2019) [3/2020]	1,002.39 (-) [1,002.39]	232.37 (0.00) [-12]
354	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	<u>Road Transport And Highways</u>				
355	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	35.80 (0.00) [-]
356	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	60.20 (0.00) [-]
357	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [8/2020]	1,958.88 (-) [1,958.88]	211.17 (0.00) [2]
358	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,659.71 (0.00) [0]
359	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2019]	364.56 (-) [364.56]	76.83 (0.00) [-]
360	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
361	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [0/0]	1,437.64 (-) [1,437.64]	0.00 (0.00) [0]
362	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [0/0]	2,702.05 (-) [2,702.05]	0.00 (0.00) [0]
363	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [8/2019]	998.18 (-) [998.18]	199.22 (0.00) [-]
364	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE	5/2016	/ (-)	723.64 (-)	216.34 (0.00)

	ST		[9/2019]	[723.64]	[-]
365	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [10/2019]	834.64 (-) [834.64]	137.94 (0.00) [-]
366	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [8/2019]	763.08 (-) [763.08]	133.37 (0.00) [-]
367	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [8/2018]	1,509.10 (-) [3,237.87]	3,176.22 (1,728.77) [0]
368	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
369	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [12/2018]	953.88 (-) [953.88]	975.23 (0.00) [65]
370	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [0/0]	1,052.21 (-) [1,052.21]	0.00 (0.00) [0]
371	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	0.00 (0.00) [0]
372	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [3/2019]	425.60 (-) [425.60]	0.00 (0.00) [-]
373	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	346.60 (0.00) [0]
	<u>Urban Development</u>				
374	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
375	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	27.20 (0.00) [0]
	<u>Health And Family Welfare</u>				
376	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	355.00 (17.42) [0]
377	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	7/2016	8/2018 (-) [0/0]	312.99 (-) [322.00]	469.00 (9.01) [0]
	<u>Petroleum</u>				
378	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [7/2019]	3,529.00 (-) [3,529.00]	857.95 (0.00) [0]
379	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	0.12 (0.00) [0]
380	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	4.33 (0.00) [0]
381	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	123.17 (0.00) [0]
	<u>Railways</u>				
382	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/ (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]

383	JIND-SONEPAT (NL),NR	1/2004	3/2012 (-) [0/0]	238.56 (-) [740.00]	722.65 (501.44) [0]
384	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2019]	346.32 (-) [300.00]	272.72 (-46.32) [0]
385	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [0/0]	287.00 (-) [625.00]	4.38 (338.00) [0]
	Road Transport And Highways				
386	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [12/2018]	602.95 (-) [602.95]	54.89 (0.00) [30]
387	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [3/2019]	574.28 (-) [574.28]	73.66 (0.00) [8]
388	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [6/2019]	639.79 (-) [552.90]	41.21 (-86.89) [-9]
389	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [4/2019]	2,128.72 (-) [2,128.72]	218.51 (0.00) [0]
390	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [8/2019]	248.97 (-) [248.97]	17.07 (0.00) [3]
391	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [0/0]	1,484.30 (-) [1,484.30]	0.00 (0.00) [0]
392	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [5/2019]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
393	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [10/2018]	486.00 (-) [486.00]	475.57 (0.00) [0]
394	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
395	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
396	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [6/2019]	1,108.00 (-) [2,288.00]	3,871.89 (1,180.00) [91]
397	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [0/0]	551.58 (-) [551.58]	0.00 (0.00) [0]
398	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	0.00 (0.00) [0]
399	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI	3/2018	/ (-) [0/0]	307.79 (-) [307.79]	0.00 (0.00) [0]
400	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	0.00 (0.00) [0]
401	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [0/0]	198.05 (-) [198.05]	0.00 (0.00) [0]
402	ROHTAK-BAWAL	5/2011	11/2013 (-) [0/0]	650.00 (-) [650.00]	832.39 (0.00) [0]

403	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I	3/2018	/ (-) [0/0]	795.50 (-) [795.50]	0.00 (0.00) [0]
404	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [0/0]	634.70 (-) [634.70]	0.00 (0.00) [0]
	HIMACHAL PRADESH				
	Petroleum				
405	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [9/2019]	151.00 (-) [151.00]	99.30 (0.00) [0]
406	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP	2/2016	5/2019 (-) [12/2018]	356.00 (-) [356.00]	194.38 (0.00) [-5]
	Power				
407	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,394.80]	7,121.50 (5,475.21) [147]
	Railways				
408	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2026]	2,966.99 (-) [7,000.00]	354.55 (4,033.01) [0]
	Road Transport And Highways				
409	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [2/2019]	273.20 (-) [273.20]	32.98 (0.00) [0]
410	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [6/2020]	2,485.93 (-) [2,485.93]	0.00 (0.00) [0]
411	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [4/2019]	1,916.79 (-) [1,916.79]	1,737.91 (0.00) [29]
412	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2019]	934.46 (-) [934.46]	104.98 (0.00) [12]
413	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [0/0]	478.74 (-) [478.74]	0.00 (0.00) [0]
414	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (-) [1,273.71]	0.00 (0.00) [-]
415	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (-) [447.75]	37.26 (0.00) [-]
416	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (-) [1,583.18]	0.00 (0.00) [-]
	Urban Development				
417	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [2/2019]	270.83 (-) [270.83]	163.97 (0.00) [51]
	JAMMU AND KASHMIR				
	Power				
418	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [10/2023]	8,112.12 (-) [8,112.12]	982.71 (0.00) [42]
419	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT	1/2014	9/2017 (-) [9/2018]	1,788.41 (-) [2,333.71]	1,528.12 (545.30) [0]
	Railways				
420	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002	2,500.00	16,834.42

			(3/2021) [3/2021]	(27,949.00) [27,949.00]	(25,449.00) [220]
	<u>Road Transport And Highways</u>				
421	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [0/0]	1,471.75 (-) [1,471.75]	0.00 (0.00) [0]
422	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	0.00 (0.00) [18]
423	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [10/2019]	2,136.97 (-) [2,136.97]	65.48 (0.00) [10]
424	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
425	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
426	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [3/2019]	1,987.00 (-) [1,987.00]	1,615.69 (0.00) [44]
427	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [0/0]	1,100.70 (-) [1,100.70]	1,246.47 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
428	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	184.43 (0.00) [0]
429	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2020]	163.51 (-) [163.51]	103.27 (0.00) [108]
430	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	42.45 (0.00) [0]
431	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
432	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2019]	162.46 (-) [162.46]	89.21 (0.00) [60]
433	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	194.20 (0.00) [0]
434	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2021]	706.40 (-) [706.40]	184.20 (0.00) [104]
435	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	325.14 (0.00) [48]
436	MURAIIDH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [0]
437	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	4.57 (0.00) [0]
438	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [3/2019]	179.87 (-) [179.87]	174.69 (0.00) [84]
439	PATHERDIH NLW WASHERY	10/2012	4/2014 (-)	269.82 (-)	178.53 (0.00)

			[4/2018]	[269.82]	[0]
440	RAJMAHAL OC EXP.	9/2009	3/2014 (-) [0/0]	153.82 (-) [153.82]	131.07 (0.00) [0]
441	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2019]	510.85 (-) [510.85]	340.06 (0.00) [36]
442	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2019]	264.68 (-) [264.68]	176.72 (0.00) [84]
	<u>Petroleum</u>				
443	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]
444	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	21.92 (0.00) [0]
445	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	22.11 (0.00) [0]
446	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	658.62 (910.23) [910.23]	87.79 (251.61) [-12]
447	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	176.28 (0.00) [0]
	<u>Power</u>				
448	NORTH KARANPURA STPP (3X660 MW)	2/2014	2/2019 (10/2020) [10/2020]	14,366.58 (-) [15,164.05]	7,673.86 (797.47) [20]
449	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [12/2016]	4,237.96 (4,552.00) [4,552.00]	2,922.12 (314.04) [0]
	<u>Railways</u>				
450	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2021]	1,724.20 (1,724.20) [1,724.20]	175.49 (0.00) [9]
451	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	4/2010	12/2015 (12/2018) [12/2018]	309.44 (-) [525.81]	495.14 (216.37) [36]
452	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	100.63 (0.00) [-3]
453	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (-) [3,020.94]	0.00 (1,987.87) [-]
454	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [0/0]	459.91 (-) [459.91]	221.54 (0.00) [0]
455	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	4/1995	3/2016 (-) [3/2020]	1,125.89 (-) [1,125.89]	2,007.32 (0.00) [48]
456	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (12/2018) [12/2018]	258.20 (-) [365.00]	184.85 (106.80) [-]
457	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [12/2018]	148.77 (-) [377.00]	152.45 (228.23) [24]
	<u>Road Transport And Highways</u>				
458	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-)	239.68 (-)	21.98 (-3.78)

			[3/2020]	[235.90]	[0]
459	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [6/2019]	165.50 (-) [172.16]	10.57 (6.66) [-9]
460	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [0/0]	1,005.08 (-) [1,005.08]	0.00 (0.00) [0]
461	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [3/2019]	997.15 (-) [997.15]	328.14 (0.00) [0]
462	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
463	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [8/2018]	323.72 (-) [323.72]	37.20 (0.00) [0]
464	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
465	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
466	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [458.03]	0.00 (0.00) [0]
	<u>Steel</u>				
467	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	9/2017 (-) [0/0]	4,749.00 (-) [4,749.00]	106.59 (0.00) [0]
468	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (-) [6/2019]	1,154.18 (-) [1,154.18]	855.62 (0.00) [18]
469	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (-) [6/2020]	1,034.01 (-) [1,034.01]	362.48 (0.00) [32]
470	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (-) [6/2020]	262.87 (-) [262.87]	76.61 (0.00) [12]
	<u>Urban Development</u>				
471	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [4/2020]	171.86 (-) [171.86]	41.28 (0.00) [49]
472	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
473	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
474	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [12/2018]	787.29 (-) [787.29]	285.30 (0.00) [24]
475	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
476	BSVI UPGRADATION	9/2016	12/2019 (-) [12/2019]	1,810.00 (1,810.00) [1,810.00]	130.79 (0.00) [0]
477	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-)	224.00 (207.00)	99.99 (-16.75)

			[4/2019]	[207.25]	[0]
478	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [749.00]	733.62 (0.00) [0]
479	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (3/2019) [3/2019]	135.00 (170.70) [170.70]	124.25 (35.70) [0]
480	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [3/2020]	581.00 (-) [581.00]	0.00 (0.00) [0]
481	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
482	KUDGI STPP STAGE 1	1/2012	1/2017 (-) [0/0]	15,166.19 (-) [16,934.65]	15,364.00 (1,768.46) [0]
483	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [2/2019]	445.89 (-) [445.89]	197.76 (0.00) [0]
	<u>Railways</u>				
484	ARSIKERE-TUMKUR	3/2015	3/2020 (3/2020) [3/2020]	578.00 (578.00) [578.00]	448.98 (0.00) [0]
485	BAGALKOT-KUDACHI NL	4/2010	3/2016 (12/2023) [12/2023]	986.30 (986.30) [986.30]	285.06 (0.00) [93]
486	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (3/2024) [3/2024]	1,382.78 (1,382.78) [1,382.78]	7.35 (0.00) [264]
487	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (12/2023) [12/2023]	327.25 (367.77) [367.77]	0.31 (40.52) [-]
488	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (12/2023) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
489	GADAG-WADI NL	4/2013	12/2018 (12/2024) [12/2024]	2,841.84 (2,841.84) [2,841.84]	27.34 (0.00) [72]
490	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,127.00]	1,161.88 (0.00) [0]
491	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2020) [3/2021]	1,156.94 (1,156.94) [1,156.94]	680.39 (0.00) [12]
492	HUBLI-ANKOLA(NL),SWR	4/1997	/ (12/2024) [12/2024]	2,315.00 (-) [2,135.00]	144.75 (-180.00) [-]
493	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (-) [889.52]	433.36 (244.74) [36]
494	MARIKUPPAM - KUPPAM	4/2012	3/2016 (12/2023) [12/2023]	279.54 (279.54) [279.54]	8.66 (0.00) [93]
495	MUNIRABAD (GINGERA) -RAICHUR NL	4/2007	/ (-) [12/2023]	179.65 (1,350.91) [1,350.91]	913.65 (1,171.26) [-]
496	SHIMOGA-HARIHAR NL	4/2011	3/2016 (3/2024) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
497	TORANAGALLU-RANJITPURA DL	4/2011	/	146.75	0.34

			(12/2023) [12/2023]	(167.50) [167.50]	(20.75) [-]
498	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/	1,801.01	12.54
			(12/2023) [12/2023]	(-) [1,801.01]	(0.00) [-]
499	WHITE FIELD-KOLAR NL	4/2011	/	348.85	0.36
			(12/2023) [12/2023]	(-) [348.85]	(0.00) [-]
	<u>Road Transport And Highways</u>				
500	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [3/2019]	1,167.42 (-) [1,167.42]	191.05 (0.00) [0]
501	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/	486.78	0.00
			(-) [0/0]	(-) [486.78]	(0.00) [0]
502	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [3/2019]	1,655.01 (-) [1,655.01]	1,515.16 (0.00) [31]
503	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/	720.69	99.03
			(-) [0/0]	(-) [720.69]	(0.00) [0]
504	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [7/2019]	701.40 (-) [701.40]	22.02 (0.00) [4]
505	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	9.12 (0.00) [20]
506	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [4/2019]	1,388.00 (-) [1,388.00]	846.58 (0.00) [8]
507	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	270.31 (0.00) [0]
508	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [3/2019]	946.00 (-) [946.00]	818.53 (0.00) [9]
509	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
510	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	325.34 (440.84) [3]
511	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [6/2020]	831.58 (-) [1,177.00]	121.00 (345.42) [3]
512	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/	2,177.80	0.00
			(-) [0/0]	(-) [2,177.80]	(0.00) [0]
513	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/	1,995.34	0.00
			(-) [0/0]	(-) [1,995.34]	(0.00) [0]
514	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
515	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
516	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [12/2018]	709.00 (-) [709.00]	351.24 (0.00) [15]
517	TWO/FOUR LANNING OF BRT TIGER RESERVE	9/2016	8/2019	950.69	388.34

	BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM		(-) [8/2019]	(-) [950.69]	(0.00) [0]
	<u>Urban Development</u>				
518	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	2,391.46 (0.00) [13]
519	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
520	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
521	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (9/2020) [9/2020]	246.31 (-) [246.31]	29.78 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
522	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [6/2019]	1,112.00 (-) [1,112.00]	108.79 (0.00) [0]
523	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [3/2019]	607.06 (-) [714.25]	341.79 (107.19) [17]
524	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	360.27 (-24.04) [8]
525	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (5/2019) [5/2019]	4,588.29 (5,245.96) [5,245.96]	2,420.04 (657.67) [9]
	<u>Railways</u>				
526	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (1,566.00) [2,815.62]	254.53 (1,249.62) [0]
527	CHENGANNUR-CHINGAVANAM	4/2006	/ (-) [0/0]	191.72 (342.85) [369.83]	432.50 (178.11) [0]
528	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (-) [189.24]	6.70 (0.00) [0]
529	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (-) [252.96]	8.50 (0.00) [0]
530	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	2/2005	3/2014 (-) [0/0]	241.00 (-) [241.00]	294.63 (0.00) [0]
531	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
532	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [0/0]	1,431.90 (-) [1,431.90]	23.84 (0.00) [0]
533	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (-) [828.50]	0.08 (-171.50) [0]
	<u>Road Transport And Highways</u>				
534	4 LANNING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [4/2019]	845.24 (-) [845.24]	108.06 (0.00) [-]
535	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [4/2019]	804.97 (-) [804.97]	21.80 (0.00) [10]

536	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,124.11]	0.00 (0.00) [33]
537	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/	1,424.77 (-) [1,424.77]	0.00 (0.00) [0]
538	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	11/2017 (-) [0/0]	267.16 (352.00) [352.05]	201.35 (84.89) [0]
539	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [11/2018]	255.75 (348.00) [348.43]	231.56 (92.68) [14]
540	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [3/2019]	617.00 (-) [617.00]	245.89 (0.00) [79]
	<u>Urban Development</u>				
541	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (6/2020) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
542	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2019]	165.23 (-) [165.23]	58.85 (0.00) [77]
543	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,181.79]	0.00 (0.00) [29]
	<u>MADHYA PRADESH</u>				
	<u>Coal</u>				
544	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	111.53 (0.00) [0]
545	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
546	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
547	BATURA OCP (2.0 MTY)	8/2015	3/2023 (3/2021) [3/2021]	1,186.64 (203.82) [203.82]	103.85 (-982.82) [-24]
548	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	16.21 (0.00) [0]
549	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	94.68 (0.00) [0]
550	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	207.63 (0.00) [0]
551	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	41.51 (0.00) [0]
552	MALACHUA OPENCASE PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	4.06 (0.00) [0]
553	NIGAHU OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	3/2012 (-) [0/0]	259.40 (-) [486.57]	266.38 (227.17) [0]
554	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	113.19 (0.00) [0]
	<u>Petroleum</u>				

555	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [6/2020]	236.00 (-) [236.00]	11.66 (0.00) [0]
	Power				
556	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [2,104.21]	65.37 (0.00) [0]
557	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	9/2017 (6/2019) [6/2019]	11,638.55 (-) [12,865.92]	9,958.55 (1,227.37) [21]
558	KHARGONE STPP STAGE I (1320 MW)	3/2015	9/2019 (-) [9/2019]	9,870.51 (-) [11,148.86]	6,135.72 (1,278.35) [0]
559	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	4/2016	6/2018 (-) [12/2018]	287.99 (-) [287.99]	161.82 (0.00) [6]
560	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	1/2016	3/2017 (-) [11/2018]	305.04 (-) [305.04]	215.81 (0.00) [20]
561	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V	2/2015	6/2018 (-) [12/2018]	1,750.00 (-) [1,750.00]	1,324.00 (0.00) [6]
	Railways				
562	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2021]	1,370.00 (-) [1,370.00]	101.00 (0.00) [0]
563	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	867.07 (0.00) [0]
564	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,101.16]	194.91 (717.37) [0]
565	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [2/2019]	585.93 (-) [1,420.39]	104.10 (834.46) [0]
566	CHHINDWARA-MANDLA FORT GC	3/2011	3/2012 (-) [3/2020]	556.54 (-) [1,342.46]	396.00 (785.92) [96]
567	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (-) [6/2020]	700.00 (-) [700.00]	11.19 (0.00) [0]
568	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,763.93 (-) [1,763.93]	0.00 (0.00) [19]
569	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2022]	582.13 (-) [1,260.61]	0.00 (678.48) [0]
570	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2022]	2,478.23 (-) [2,478.23]	112.07 (0.00) [0]
571	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [8/2019]	174.00 (-) [174.00]	139.04 (0.00) [5]
572	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2021]	424.60 (-) [2,713.09]	898.83 (2,288.49) [0]
573	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2019) [3/2022]	3,503.69 (2,473.40) [1,030.29]	1,081.52 (-2,473.40) [0]
	Road Transport And Highways				
574	BALANCE WORK FOR FOUR LANING OF ITARSI TO	12/2017	/	950.27	0.00

	BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN		(-) [0/0]	(-) [950.27]	(0.00) [0]
575	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [1/2019]	227.49 (-) [227.49]	15.03 (0.00) [0]
576	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]
577	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	0.00 (0.00) [0]
578	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
579	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [0/0]	390.51 (-) [390.51]	43.25 (0.00) [0]
580	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	2/2015 (-) [0/0]	670.82 (-) [670.82]	590.00 (0.00) [0]
581	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015 (-) [0/0]	704.26 (-) [704.26]	0.00 (0.00) [0]
582	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	2/2016 (-) [0/0]	257.80 (-) [257.80]	59.30 (0.00) [0]
583	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [1/2019]	1,583.79 (-) [1,583.79]	496.70 (0.00) [0]
584	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [0/0]	960.24 (-) [960.24]	0.00 (0.00) [0]
585	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [3/2019]	1,012.90 (-) [1,012.90]	439.07 (0.00) [36]
586	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [12/2018]	1,055.00 (-) [1,601.77]	1,328.85 (546.77) [37]
587	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [12/2018]	928.83 (-) [928.83]	195.21 (0.00) [-]
588	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [12/2018]	794.30 (-) [794.30]	117.99 (0.00) [-]
589	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [12/2018]	795.76 (-) [795.76]	131.52 (0.00) [-]
590	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [12/2018]	810.22 (-) [810.22]	111.65 (0.00) [-]
591	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	23.98 (0.00) [27]
592	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
593	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	6/2018 (-) [0/0]	927.54 (-) [927.54]	29.17 (0.00) [0]
594	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-)	497.05 (-)	0.00 (0.00)

			[0/0]	[497.05]	[0]
595	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
596	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [11/2018]	1,175.00 (-) [1,206.10]	1,209.67 (31.10) [67]
597	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	3/2018 (-) [0/0]	628.45 (-) [628.45]	20.74 (0.00) [0]
598	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	5/2017 (-) [0/0]	327.32 (-) [327.32]	142.73 (0.00) [0]
599	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	7/2017 (-) [0/0]	377.83 (-) [377.83]	57.42 (0.00) [0]
600	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	12/2017 (-) [0/0]	641.02 (-) [641.02]	89.88 (0.00) [0]
601	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	381.86 (-) [381.86]	252.03 (0.00) [0]
602	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
603	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	5/2017 (-) [0/0]	532.49 (-) [532.49]	137.08 (0.00) [0]
604	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [0/0]	871.15 (-) [871.15]	332.25 (0.00) [0]
605	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [0/0]	511.83 (-) [511.83]	40.87 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Coal</u>				
606	ADASA UG TO OC	8/2015	3/2023 (-) [3/2023]	288.90 (-) [288.90]	0.00 (0.00) [0]
607	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2019]	198.68 (-) [198.68]	254.72 (0.00) [0]
608	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	83.52 (0.00) [0]
609	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	236.66 (0.00) [0]
610	BHANEGAON OC	2/2015	3/2023 (2/2017) [3/2023]	187.94 (409.68) [409.68]	95.81 (221.74) [0]
611	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2019]	304.52 (-) [304.52]	129.39 (0.00) [0]
612	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	391.37 (0.00) [0]
613	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	207.74 (0.00) [0]
614	KAMPTEE DEEP OC MINE	11/2015	3/2021	277.65	6.12

			(9/2018) [3/2024]	(313.34) [313.34]	(35.69) [36]
615	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	257.36 (0.00) [0]
616	MAKARDHOKRA I OC	9/2014	3/2021 (-) [3/2021]	266.23 (-) [266.23]	143.29 (0.00) [0]
617	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	52.87 (0.00) [0]
618	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	88.13 (0.00) [0]
619	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	184.45 (0.00) [0]
620	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	102.75 (0.00) [0]
	<u>Fertilisers</u>				
621	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	38.65 (0.00) [0]
622	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	2/2016	12/2017 (12/2018) [12/2018]	482.85 (482.85) [482.85]	413.00 (0.00) [12]
623	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (4/2019) [4/2019]	197.79 (209.44) [209.44]	126.30 (11.65) [29]
	<u>Health And Family Welfare</u>				
624	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [0/0]	582.99 (-) [582.99]	4.80 (0.00) [0]
625	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2019]	274.19 (-) [274.19]	122.66 (0.00) [0]
	<u>Petroleum</u>				
626	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
627	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (11/2019) [11/2019]	968.61 (968.61) [968.61]	502.40 (0.00) [0]
628	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	8.48 (0.00) [0]
629	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	212.00 (-) [212.00]	14.11 (0.00) [0]
630	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	348.00 (-) [348.00]	8.48 (0.00) [0]
631	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (3/2019) [3/2019]	861.79 (1,577.15) [1,577.15]	1,195.62 (715.36) [70]
632	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (11/2019) [11/2019]	546.15 (546.15) [546.15]	191.39 (0.00) [0]
633	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (11/2019)	511.30 (511.30)	167.64 (0.00)

			[11/2019]	[511.30]	[0]
634	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,006.83) [4,006.83]	1,226.29 (0.00) [0]
635	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2019) [3/2019]	4,619.94 (4,619.94) [4,619.94]	3,931.91 (0.00) [15]
636	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	135.68 (0.00) [0]
637	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,842.42 (606.02) [57]
638	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	499.85 (0.00) [0]
639	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2019) [5/2019]	3,190.69 (-) [3,247.19]	2,102.45 (56.50) [13]
640	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	115.17 (0.00) [0]
641	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (3/2019) [3/2019]	6,068.80 (6,068.80) [5,296.93]	4,559.88 (-771.87) [-1]
642	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [7/2019]	4,199.00 (-) [4,199.00]	194.97 (0.00) [-8]
643	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	1,687.43 (0.00) [14]
644	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY	1/2017	5/2019 (5/2019) [5/2019]	474.15 (474.15) [474.15]	299.26 (0.00) [0]
645	PIPELINE REPLACEMENT PROJECT -4	2/2015	5/2017 (12/2018) [12/2018]	2,899.93 (-) [2,504.61]	2,119.15 (-395.32) [19]
646	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	0.00 (0.00) [0]
647	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	56.69 (0.00) [0]
	<u>Power</u>				
648	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
649	SOLAPUR STPP	3/2012	11/2016 (3/2019) [3/2019]	9,395.18 (-) [9,395.18]	8,911.13 (0.00) [28]
650	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	9/2010 (-) [12/2018]	477.69 (-) [738.48]	669.46 (260.79) [99]
	<u>Railways</u>				
651	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [3/2019]	184.06 (199.12) [298.70]	240.89 (114.64) [0]
652	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2021]	2,271.50 (2,271.50) [3,712.50]	1,870.67 (1,441.00) [0]
653	AMRAVATI-NARKHER NL(CR)	6/1994	6/1999	663.01	716.67

			(-) [0/0]	(668.34) [858.96]	(195.95) [0]
654	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2020]	495.44 (1,781.98) [1,781.98]	1,329.00 (1,286.54) [192]
655	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (2,081.27) [2,081.27]	1.27 (205.27) [0]
656	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,750.00]	1,563.47 (1,036.52) [0]
657	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.22 (0.00) [-9]
658	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [8,857.98]	0.00 (-1,110.02) [0]
659	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (2,449.91) [2,449.91]	87.60 (0.00) [0]
660	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2021]	792.89 (792.89) [792.89]	272.78 (0.00) [0]
661	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2023]	1,035.16 (1,035.16) [1,035.16]	18.99 (0.00) [12]
662	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [3/2019]	305.00 (-) [305.00]	253.28 (0.00) [0]
663	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
664	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2019]	5,300.00 (-) [7,986.04]	2,423.55 (2,686.04) [60]
665	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2024]	3,627.47 (3,627.47) [3,627.47]	309.54 (0.00) [0]
666	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
667	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (-) [3/2023]	1,908.51 (-) [2,686.63]	0.00 (778.12) [0]
668	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
669	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
670	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
671	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2021]	229.00 (-) [403.00]	36.28 (174.00) [0]
672	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2023]	637.95 (637.95) [637.95]	26.63 (0.00) [0]
673	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-)	1,272.19 (1,272.19)	132.09 (0.00)

			[3/2022]	[1,272.19]	[0]
674	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (3,168.29) [3,168.29]	979.05 (0.00) [0]
675	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2022]	540.02 (540.02) [540.02]	156.10 (0.00) [0]
	Road Transport And Highways				
676	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]
677	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [5/2019]	1,885.74 (-) [1,885.74]	1,622.44 (0.00) [0]
678	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [12/2018]	972.50 (-) [972.50]	1,302.51 (0.00) [17]
679	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [0/0]	607.00 (-) [607.00]	0.00 (0.00) [0]
680	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	0.00 (0.00) [0]
681	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [6/2019]	923.04 (-) [923.04]	473.93 (0.00) [31]
682	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
683	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [0/0]	1,071.61 (-) [1,071.61]	0.00 (0.00) [0]
684	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [11/2019]	446.17 (-) [446.17]	2.42 (0.00) [8]
685	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	177.05 (62.58) [5]
686	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	0.00 (0.00) [0]
687	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]
688	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [3/2019]	400.25 (-) [400.25]	38.57 (0.00) [0]
689	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [0/0]	1,064.88 (-) [1,064.88]	0.00 (0.00) [0]
690	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	86.58 (11.27) [44]
691	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	303.24 (35.07) [2]
692	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	289.99 (54.94) [5]
693	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (-)	505.00 (-)	194.09 (0.00)

			[4/2019]	[505.00]	[11]
694	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [7/2018]	197.69 (-) [197.69]	0.00 (0.00) [0]
695	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60	3/2016	7/2018 (-) [0/0]	244.00 (-) [244.00]	0.00 (0.00) [0]
696	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [0/0]	1,162.92 (-) [1,162.92]	0.00 (0.00) [0]
697	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (-) [3/2019]	649.50 (-) [649.50]	80.89 (0.00) [0]
698	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [0/0]	291.53 (-) [291.53]	0.00 (0.00) [0]
699	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [5/2019]	244.90 (-) [244.90]	77.00 (0.00) [0]
700	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [0/0]	289.21 (-) [289.21]	0.00 (0.00) [0]
701	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [4/2019]	593.26 (-) [593.26]	45.11 (0.00) [11]
702	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [156.26]	65.16 (0.00) [0]
703	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	/ (-) [0/0]	185.82 (292.00) [185.82]	205.97 (0.00) [0]
704	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [5/2019]	531.13 (-) [531.13]	163.10 (0.00) [12]
705	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	13.43 (0.00) [0]
706	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	57.60 (0.00) [0]
707	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [3/2020]	247.02 (-) [157.49]	0.00 (-89.53) [0]
708	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (-) [3/2019]	414.51 (-) [414.00]	210.66 (-0.51) [10]
709	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [5/2019]	296.19 (-) [254.00]	86.95 (-42.19) [-10]
710	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [12/2018]	1,170.52 (-) [1,170.52]	2,056.03 (0.00) [78]
711	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [642.13]	0.00 (0.00) [0]
712	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [12/2018]	1,871.34 (-) [1,871.34]	2,304.41 (0.00) [11]
713	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [5/2020]	904.16 (-) [904.16]	155.12 (0.00) [3]

714	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	279.92 (0.00) [0]
715	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [7/2019]	546.00 (-) [546.00]	87.19 (0.00) [0]
716	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [7/2019]	591.66 (-) [591.66]	237.07 (0.00) [0]
717	PANVEL-INDAPUR	12/2011	6/2014 (-) [6/2019]	942.69 (-) [942.69]	396.59 (0.00) [60]
718	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [6/2019]	1,724.55 (-) [1,724.55]	2,058.04 (0.00) [75]
719	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	12/2013	11/2016 (-) [0/0]	220.72 (-) [220.72]	95.02 (0.00) [0]
720	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	11/2016 (-) [0/0]	260.39 (-) [260.39]	87.43 (0.00) [0]
721	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	87.62 (0.00) [0]
722	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	11/2014 (-) [0/0]	292.98 (-) [292.98]	95.60 (0.00) [0]
723	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	6.50 (0.00) [0]
724	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [0/0]	404.94 (-) [404.94]	0.00 (0.00) [0]
725	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [5/2019]	290.73 (-) [290.73]	57.93 (0.00) [-]
726	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	0.00 (0.00) [0]
727	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [6/2019]	1,348.20 (-) [1,348.20]	3,386.77 (0.00) [64]
	Shipping And Ports				
728	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	1/2007	12/2010 (-) [12/2018]	366.39 (-) [669.46]	411.12 (303.07) [96]
	Telecommunications				
729	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (12/2018) [12/2018]	215.30 (214.10) [214.10]	33.46 (-1.20) [7]
730	MAHARASHTRA CORE (LOT1)	8/2017	4/2018 (12/2018) [12/2018]	167.68 (-) [167.68]	32.44 (0.00) [8]
731	MAHARASHTRA NODAL (LOT 1)	8/2017	4/2018 (12/2018) [12/2018]	159.30 (-) [159.30]	60.27 (0.00) [8]
732	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (12/2018) [12/2018]	231.80 (-) [231.80]	77.65 (0.00) [2]
	Urban Development				
733	CONSTRUCTION OF IITB RESEARCH PARK AT IIT	1/2018	7/2020	223.37	4.00

	BOMBAY, POWAI, MUMBAI		(9/2018) [9/2020]	(-) [223.37]	(0.00) [2]
734	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
735	NAGPUR METRO RAIL	8/2014	3/2018 (12/2019) [12/2019]	8,680.00 (8,680.00) [8,680.00]	4,631.87 (0.00) [21]
736	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	1,881.14 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
737	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	7,919.05 (9,354.83) [108]
	<u>Urban Development</u>				
738	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2019]	216.69 (-) [216.69]	52.00 (0.00) [56]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
739	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [8/2019]	363.99 (-) [363.99]	71.00 (0.00) [15]
	<u>Railways</u>				
740	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	259.43 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
741	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
742	JORBAT - BARAPANI	1/2011	1/2014 (-) [1/2019]	536.00 (-) [536.00]	678.87 (0.00) [60]
743	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [3/2019]	479.20 (-) [479.20]	14.31 (0.00) [10]
744	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	<u>Urban Development</u>				
745	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	<u>MIZORAM</u>				
	<u>Railways</u>				
746	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,968.00]	2,318.33 (2,574.53) [81]
	<u>Road Transport And Highways</u>				
747	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
748	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
749	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]

	<u>MULTI STATE</u>				
	<u>Coal</u>				
750	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	16.00 (0.00) [0]
751	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	88.46 (0.00) [0]
752	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	58.04 (0.00) [0]
	<u>Heavy Industry</u>				
753	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (-) [0/0]	1,718.00 (-) [3,827.30]	2,289.00 (2,109.30) [0]
	<u>Petroleum</u>				
754	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
755	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (-) [1,823.00]	569.04 (0.00) [0]
756	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	42.33 (0.00) [0]
757	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	1.66 (0.00) [0]
758	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	663.13 (0.00) [0]
759	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	9/2011 (-) [0/0]	736.65 (-) [571.47]	543.05 (-165.18) [0]
760	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	776.24 (0.00) [0]
761	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	49.88 (0.00) [0]
762	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [3/2019]	890.00 (-) [887.00]	516.56 (-3.00) [-7]
763	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2019) [6/2019]	2,915.00 (3,030.00) [2,915.00]	1,965.67 (0.00) [78]
764	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2019 (12/2020) [12/2019]	2,881.40 (-) [2,000.00]	774.62 (-881.40) [0]
765	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	961.58 (0.00) [0]
766	PARADIP HALDIA DURGAPUR LPG PIPELINE	2/2011	6/2018 (-) [10/2018]	913.00 (1,330.00) [1,330.00]	1,308.86 (417.00) [0]
767	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (-) [2,321.00]	619.33 (0.00) [-4]
768	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (10/2020) [10/2020]	690.00 (-) [690.00]	169.70 (0.00) [27]

769	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
770	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [12/2018]	3,957.00 (3,561.00) [3,397.00]	2,313.08 (-560.00) [0]
771	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	23.61 (0.00) [0]
772	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)	11/2016	2/2019 (-) [2/2019]	230.00 (-) [230.00]	110.04 (0.00) [0]
773	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (6/2019) [6/2019]	352.56 (-) [438.84]	196.39 (86.28) [27]
774	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (2/2019) [2/2019]	309.81 (723.40) [723.40]	586.10 (413.59) [52]
	<u>Power</u>				
775	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [2/2020]	198.49 (-) [198.49]	0.80 (0.00) [5]
776	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	8/2008	2/2013 (-) [10/2018]	771.00 (-) [1,624.00]	1,429.45 (853.00) [0]
777	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	3/2014	3/2016 (-) [11/2018]	155.57 (-) [206.42]	145.22 (50.85) [32]
778	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	3/2013	12/2015 (-) [11/2018]	2,514.88 (-) [3,190.27]	2,281.28 (675.39) [35]
779	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2019]	4,754.42 (-) [9,141.97]	840.87 (4,387.55) [12]
780	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	0.00 (0.00) [0]
781	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (-) [11/2018]	196.58 (-) [225.28]	148.92 (28.70) [33]
782	EASTERN REGION STRENGTHENING SCHEME XI	5/2016	11/2018 (-) [11/2018]	766.21 (-) [766.21]	375.34 (0.00) [0]
783	EASTERN REGION STRENGTHENING SCHEME XIV	5/2016	11/2018 (-) [11/2018]	167.01 (-) [167.01]	97.53 (0.00) [0]
784	EASTERN REGION STRENGTHENING SCHEME-III	7/2010	11/2012 (-) [10/2018]	1,272.80 (-) [1,731.10]	1,461.65 (458.30) [0]
785	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (-) [12/2018]	1,364.52 (-) [1,891.41]	1,202.20 (526.89) [32]
786	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (-) [6/2019]	522.29 (-) [550.18]	433.43 (27.89) [31]
787	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	597.00 (0.00) [0]
788	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [6/2019]	235.53 (-) [235.53]	20.09 (0.00) [0]

789	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [2/2019]	322.30 (-) [322.30]	103.28 (0.00) [0]
790	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2018]	197.40 (-) [197.40]	74.71 (0.00) [9]
791	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	5/2016	5/2019 (-) [5/2019]	3,519.59 (-) [3,519.59]	1,861.40 (0.00) [0]
792	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	4/2015	4/2018 (-) [12/2018]	3,705.61 (-) [3,705.61]	2,518.90 (0.00) [8]
793	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C	7/2015	7/2018 (-) [12/2018]	2,247.37 (-) [2,247.37]	1,420.89 (0.00) [5]
794	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	552.21 (0.00) [0]
795	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	3,710.05 (0.00) [0]
796	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	321.99 (0.00) [0]
797	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	79.31 (0.00) [0]
798	INSTALLATION OF STATCOMS IN WESTERN REGION	3/2015	9/2017 (-) [11/2018]	1,071.24 (-) [1,071.24]	630.56 (0.00) [14]
799	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2019]	5,111.33 (-) [6,652.57]	802.18 (1,541.24) [12]
800	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (-) [3/2022]	11,130.19 (-) [13,762.80]	12,714.20 (2,632.61) [103]
801	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	6/2016 (-) [12/2018]	539.82 (-) [539.82]	419.63 (0.00) [30]
802	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA	3/2017	3/2019 (-) [3/2019]	162.31 (-) [162.31]	22.42 (0.00) [0]
803	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN	7/2016	3/2019 (-) [3/2019]	333.17 (-) [333.17]	250.73 (0.00) [0]
804	PROVISION OF SERIES REACTORS IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	177.52 (-) [177.52]	76.98 (0.00) [0]
805	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	431.89 (-) [431.89]	191.76 (0.00) [0]
806	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	25.85 (0.00) [0]
807	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [3/2019]	562.25 (-) [562.25]	26.40 (0.00) [0]
808	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [4/2019]	3,654.00 (-) [3,654.00]	2,798.00 (0.00) [0]
809	SUB STATION WORK ASSOCIATED WITH	10/2016	4/2019	608.24	354.00

	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI		(-) [4/2019]	(-) [608.24]	(0.00) [0]
810	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [6/2019]	203.28 (-) [260.03]	181.16 (56.75) [23]
811	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [12/2019]	379.95 (-) [379.95]	21.82 (0.00) [0]
812	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [6/2019]	337.75 (-) [337.75]	16.10 (0.00) [0]
813	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	1/2016	7/2018 (-) [10/2018]	1,455.47 (-) [1,455.47]	1,028.69 (0.00) [0]
814	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	8/2014 (-) [12/2018]	297.33 (-) [534.02]	426.98 (236.69) [52]
815	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [12/2018]	487.49 (-) [639.46]	499.90 (151.97) [54]
816	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (-) [2/2019]	4,824.12 (-) [5,071.94]	4,538.37 (247.82) [76]
817	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	3/2015	12/2015 (-) [12/2018]	955.00 (-) [1,364.00]	1,237.00 (409.00) [36]
818	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (-) [11/2018]	268.80 (-) [340.88]	229.40 (72.08) [8]
819	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	2/2010	12/2012 (-) [11/2018]	2,144.00 (-) [2,932.88]	2,654.96 (788.88) [71]
820	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (-) [9/2019]	871.62 (-) [871.62]	407.22 (0.00) [23]
821	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [3/2019]	408.46 (-) [408.46]	139.34 (0.00) [2]
822	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [3/2019]	5,151.37 (-) [5,151.37]	2,716.40 (0.00) [12]
823	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (-) [3/2019]	808.63 (-) [808.63]	332.96 (0.00) [14]
824	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (-) [10/2018]	374.63 (-) [374.63]	187.24 (0.00) [0]
825	WESTERN REGION STRENGTHENING SCHEME-XVI	7/2016	7/2018 (-) [10/2018]	150.99 (-) [150.99]	88.66 (0.00) [0]
826	WESTERN REGION STRENGTHENING SCHEME XVII	2/2017	9/2019 (-) [9/2019]	204.12 (-) [204.12]	89.17 (0.00) [0]
827	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (-) [2/2020]	195.05 (-) [195.05]	55.10 (0.00) [0]
	<u>Railways</u>				
828	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	899.56 (0.00) [0]
829	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF	4/2010	/	338.54	212.64

	DHAPPER-CHANDIGARH		(-) [0/0]	(-) [338.54]	(0.00) [0]
830	BANDEL-BOINCHI 3RD LINE	4/2011	/	288.35	273.54
			(-) [0/0]	(-) [238.36]	(-49.99) [0]
831	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/	450.55	19.82
			(-) [0/0]	(-) [250.55]	(-200.00) [0]
832	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (704.31) [704.31]	119.69 (0.00) [0]
833	BHADRACHALAM-KOVVUR	4/2012	/	923.23	2.46
			(-) [0/0]	(-) [1,787.00]	(863.77) [0]
834	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/	175.80	139.80
			(-) [0/0]	(-) [173.91]	(-1.89) [0]
835	CALICUT-MANGALORE (DL) (SR)	2/1996	/	240.00	537.30
			(-) [0/0]	(-) [579.37]	(339.37) [0]
836	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	229.95 (1,211.86) [0]
837	CHANDIGARH-BADDI NL	4/2007	/	328.14	45.20
			(-) [0/0]	(-) [1,540.00]	(1,211.86) [0]
838	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/	337.96	72.84
			(-) [0/0]	(-) [355.44]	(17.48) [0]
839	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/	523.52	2.27
			(-) [0/0]	(-) [2,350.00]	(1,826.48) [0]
840	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2019]	295.00 (-) [477.31]	181.09 (182.31) [1]
841	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [0/0]	243.78 (-) [895.00]	97.92 (651.22) [0]
842	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [0/0]	595.51 (-) [538.37]	108.62 (-57.14) [0]
843	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2019) [3/2022]	1,347.26 (-) [1,347.26]	606.41 (0.00) [0]
844	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2019) [3/2022]	1,640.04 (-) [1,640.04]	603.75 (0.00) [0]
845	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [0/0]	365.17 (-) [296.43]	118.48 (-68.74) [0]
846	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR	4/2013	/	1,239.00	0.00
			(-) [0/0]	(-) [1,239.00]	(0.00) [0]
847	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/	336.91	143.18
			(-) [0/0]	(-) [336.91]	(0.00) [0]
848	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [6/2016]	607.09 (-) [607.91]	1,067.93 (0.82) [0]
849	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-	4/2010	/	2,030.50	10.34
			(-)	(-)	(0.00)

	BANSI PAHARPUR		[12/2022]	[2,030.50]	[-]
850	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (3/2024) [3/2024]	651.00 (-) [1,009.00]	7.96 (358.00) [108]
851	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/	11,589.00	0.00
			(-) [0/0]	(30,357.00) [28,181.00]	(16,592.00) [0]
852	GAYA-CHATRA (NL)	4/2008	/	415.67	14.62
			(-) [0/0]	(-) [549.75]	(134.08) [0]
853	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020	511.86	967.96
			(-) [4/2020]	(-) [1,756.00]	(1,244.14) [0]
854	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/	636.38	0.00
			(-) [0/0]	(-) [636.38]	(0.00) [0]
855	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	4/1986	3/1994	158.77	629.43
			(-) [0/0]	(274.56) [634.48]	(475.71) [0]
856	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022	2,912.96	1.92
			(-) [3/2022]	(-) [3,845.60]	(932.64) [0]
857	HAJIPUR - BACHAWARA	5/2015	3/2019	678.54	0.00
			(-) [3/2020]	(-) [678.54]	(0.00) [12]
858	HANSDIHA-GODDA NL	4/2011	3/2020	542.18	303.58
			(-) [3/2020]	(-) [542.18]	(0.00) [0]
859	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	10.84
			(-) [0/0]	(-) [260.10]	(88.07) [0]
860	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022	230.03	274.48
			(-) [5/2019]	(-) [770.08]	(540.05) [-43]
861	HOTGI-KUDGI-GADAG	3/2015	3/2019	1,614.59	696.73
			(3/2021) [3/2021]	(1,614.59) [1,614.59]	(0.00) [24]
862	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018	157.94	50.69
			(-) [11/2018]	(-) [157.94]	(0.00) [0]
863	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	246.00
			(-) [0/0]	(-) [166.89]	(0.00) [0]
864	JAKHAL-MANSA DOUBLING ON SPR SECTION	4/2008	/	162.96	153.31
			(-) [0/0]	(-) [162.96]	(0.00) [0]
865	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016	625.00	0.00
			(-) [0/0]	(-) [845.58]	(220.58) [0]
866	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	3/2002	6/2007	625.30	841.57
			(-) [0/0]	(408.76) [876.10]	(250.80) [0]
867	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014	2,132.77	216.07
			(3/2023) [3/2023]	(-) [2,132.77]	(0.00) [108]
868	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016	923.52	335.88
			(-) [0/0]	(-) [792.27]	(-131.25) [0]
869	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	57.51
			(-) [0/0]	(-) [175.99]	(1.43) [0]

870	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	4/1999	/ (-) [0/0]	744.71 (-) [1,126.79]	751.05 (382.08) [0]
871	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2021]	2,063.03 (-) [2,063.03]	368.22 (0.00) [0]
872	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (3/2024) [3/2024]	1,856.95 (1,856.95) [2,200.00]	227.19 (343.05) [12]
873	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (346.15) [457.08]	317.14 (186.94) [0]
874	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [0/0]	406.99 (-) [544.72]	147.26 (137.73) [0]
875	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	972.82 (5,845.65) [178]
876	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [0/0]	257.42 (-) [258.73]	113.51 (1.31) [0]
877	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [3/2019]	120.70 (-) [1,800.00]	112.10 (1,679.30) [0]
878	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [0/0]	499.96 (-) [665.75]	148.88 (165.79) [0]
879	MIRAJ-LONDA	3/2015	/ (3/2021) [3/2021]	1,830.00 (1,190.92) [1,190.92]	190.63 (-639.08) [-]
880	MM FROM BURAMARA-CHAKULIA	4/2008	0/0 (12/2024) [12/2024]	466.48 (-) [1,000.00]	0.83 (533.52) [-]
881	MONIGRAM- NIMTITA	4/2012	/ (-) [0/0]	250.93 (-) [259.23]	199.46 (8.30) [0]
882	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (3/2019) [3/2019]	1,723.00 (1.00) [645.00]	725.63 (-1,078.00) [228]
883	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	123.11 (246.16) [0]
884	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [0/0]	450.00 (-) [2,100.00]	484.14 (1,650.00) [0]
885	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [0/0]	494.54 (-) [492.68]	32.00 (-1.86) [0]
886	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	64.09 (228.78) [0]
887	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [0/0]	241.52 (-) [394.28]	148.33 (152.76) [0]
888	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2019]	1,798.00 (-) [1,798.00]	0.00 (0.00) [0]
889	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [3/2018]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
890	NEW MAYNAGURI TO JOGIGHOPA VIA	4/2000	12/2008	1,180.19	3,036.52

	CHANGRABANDHA (NL),NEFR		(-) [3/2019]	(-) [3,040.00]	(1,859.81) [123]
891	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [3/2020]	600.00 (-) [685.99]	3.51 (85.99) [0]
892	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [0/0]	261.38 (-) [332.14]	360.58 (70.76) [0]
893	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2022]	915.98 (-) [915.96]	319.21 (-0.02) [0]
894	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [0/0]	299.60 (-) [269.60]	1.12 (-30.00) [0]
895	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	3/1998	/ (-) [0/0]	280.00 (-) [1,122.00]	834.87 (842.00) [0]
896	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [2,878.97]	183.63 (796.22) [0]
897	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (-) [2,062.20]	674.76 (-0.10) [-]
898	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE	4/2010	/ (-) [0/0]	268.52 (-) [268.52]	78.81 (0.00) [0]
899	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [0/0]	297.47 (-) [153.02]	52.10 (-144.45) [0]
900	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2020]	277.28 (-) [266.52]	137.85 (-10.76) [48]
901	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (12/2023) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
902	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [0/0]	450.00 (-) [288.85]	9.31 (-161.15) [0]
903	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [0/0]	365.17 (-) [527.54]	1.73 (162.37) [0]
904	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
905	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/ (-) [0/0]	876.00 (-) [876.00]	0.00 (0.00) [0]
906	YELAHANKA-PENUKONDA	5/2015	3/2020 (3/2020) [3/2020]	860.43 (860.43) [860.43]	490.28 (0.00) [0]
	<u>Road Transport And Highways</u>				
907	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,489.54 (0.00) [0]
908	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	2,335.94 (1,016.78) [0]
909	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
910	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM	3/2018	/	1,294.47	0.00

	SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.		(-) [0/0]	(-) [1,294.47]	(0.00) [0]
911	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/	998.70	0.00
			(-) [0/0]	(-) [998.70]	(0.00) [0]
912	GWALIOR-JHANSI, NH-75	12/2003	12/2009	604.00	423.83
			(-) [8/2020]	(-) [604.00]	(0.00) [128]
913	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013	754.00	1,363.43
			(-) [12/2019]	(-) [754.00]	(0.00) [81]
914	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/	1,244.10	85.00
			(-) [2/2020]	(-) [1,244.10]	(0.00) [-]
915	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011	1,693.75	2,675.28
			(-) [0/0]	(-) [1,693.75]	(0.00) [0]
916	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014	2,848.00	1,141.90
			(-) [12/2019]	(-) [2,848.00]	(0.00) [69]
917	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	/	789.83	109.77
			(-) [0/0]	(-) [789.83]	(0.00) [0]
	<u>Telecommunications</u>				
918	NETWORK FOR SPECTRUM	3/2012	7/2015	13,334.00	8,397.00
			(-) [5/2020]	(-) [24,664.00]	(11,330.00) [58]
919	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014	2,111.17	253.90
			(-) [0/0]	(-) [2,011.17]	(-100.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
920	DIMAPUR-TIZIT NL	4/2013	3/2020	4,274.00	0.00
			(-) [3/2020]	(-) [4,274.00]	(0.00) [0]
921	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015	2,326.52	655.38
			(10/2021) [10/2021]	(2,446.57) [3,000.00]	(673.48) [79]
	<u>Road Transport And Highways</u>				
922	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018	239.30	0.00
			(-) [0/0]	(-) [239.30]	(0.00) [0]
923	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018	285.68	0.00
			(-) [0/0]	(-) [285.68]	(0.00) [0]
924	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018	282.98	0.00
			(-) [0/0]	(-) [282.98]	(0.00) [0]
925	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018	387.00	0.00
			(-) [0/0]	(-) [387.00]	(0.00) [0]
926	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018	500.09	0.00
			(-) [0/0]	(-) [500.09]	(0.00) [0]
927	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017	507.68	0.00
			(-) [0/0]	(-) [507.68]	(0.00) [0]
928	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018	339.57	0.00
			(-) [0/0]	(-) [339.57]	(0.00) [0]
929	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS	3/2018	9/2018	315.03	0.00

	OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO		(-) [0/0]	(-) [315.03]	(0.00) [0]
930	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
931	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	0.00 (0.00) [0]
932	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
933	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
934	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
935	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	0.00 (0.00) [0]
936	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	0.00 (0.00) [0]
937	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
938	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
939	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
940	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	ODISHA				
	Coal				
941	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	234.29 (0.00) [108]
942	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2020]	172.08 (-) [172.08]	266.97 (0.00) [120]
943	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	116.85 (0.00) [60]
944	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	387.94 (0.00) [36]
945	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	435.69 (0.00) [0]
946	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2020]	479.53 (-) [479.53]	251.75 (0.00) [84]
947	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2021]	337.66 (-) [337.66]	60.36 (0.00) [24]
948	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2020]	457.77 (-) [457.77]	583.96 (0.00) [84]

949	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	27.48 (0.00) [24]
950	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2018]	302.96 (-) [302.96]	302.96 (0.00) [0]
951	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	689.19 (0.00) [0]
	<u>Mines</u>				
952	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	96.98 (0.00) [0]
953	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
954	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.00 (0.00) [0]
955	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	302.19 (0.00) [0]
	<u>Petroleum</u>				
956	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	19.99 (0.00) [0]
957	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	2.56 (0.00) [0]
958	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (243.53) [243.53]	29.39 (0.00) [0]
959	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	181.20 (-) [181.20]	14.06 (0.00) [0]
960	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	652.51 (0.00) [0]
961	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	7/2021 (-) [7/2021]	4,807.08 (-) [4,807.08]	24.09 (0.00) [0]
962	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [1/2019]	429.00 (-) [429.00]	256.93 (0.00) [0]
963	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	33.81 (0.00) [0]
964	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (12/2018) [12/2018]	3,150.00 (-) [3,150.00]	2,443.76 (0.00) [15]
	<u>Power</u>				
965	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	8/2018 (6/2019) [6/2019]	12,532.44 (-) [13,740.53]	8,122.05 (1,208.09) [10]
966	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [4/2019]	844.64 (-) [844.64]	303.70 (0.00) [0]
	<u>Railways</u>				
967	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [942.95]	887.88 (0.00) [24]

968	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2021]	843.04 (843.04) [843.04]	81.26 (0.00) [5]
969	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2021]	1,172.92 (-) [1,172.92]	245.16 (0.00) [27]
970	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
971	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2020]	5,200.00 (-) [5,200.00]	0.00 (0.00) [0]
972	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [6/2019]	1,185.64 (-) [1,844.47]	1,367.66 (658.83) [18]
973	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	1,547.38 (1,547.38) [1,547.38]	189.40 (0.00) [0]
974	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2021]	701.61 (-) [810.02]	88.04 (108.41) [28]
975	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2018]	133.41 (207.00) [385.00]	373.73 (251.59) [117]
976	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2021]	2,923.13 (-) [3,798.80]	1,123.73 (875.67) [147]
977	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2022]	2,361.74 (2,361.74) [2,361.74]	81.06 (0.00) [0]
978	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [6/2020]	969.83 (-) [1,151.81]	375.59 (181.98) [3]
979	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	4/1995	12/2021 (12/2024) [12/2024]	524.43 (-) [939.00]	184.09 (414.57) [36]
980	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	180.78 (82.22) [0]
981	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2020]	948.04 (-) [970.00]	975.36 (21.96) [0]
982	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2021]	1,111.99 (1,539.28) [1,539.28]	765.60 (427.29) [25]
983	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (245.00) [1,202.70]	631.11 (0.00) [82]
984	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (1,928.07) [1,928.07]	574.98 (1,117.29) [21]
985	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (2,335.67) [2,335.67]	300.05 (0.00) [0]
	<u>Road Transport And Highways</u>				
986	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [0/0]	1,282.94 (-) [1,282.94]	0.00 (0.00) [0]
987	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [0]

988	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
989	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [0/0]	319.80 (320.00) [320.00]	0.00 (0.20) [0]
990	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [0/0]	319.80 (-) [319.80]	0.00 (0.00) [0]
991	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [0/0]	1,069.65 (-) [1,069.65]	0.00 (0.00) [0]
992	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [10/2015]	1,410.00 (-) [1,410.00]	1,555.96 (0.00) [0]
993	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [0/0]	1,008.96 (-) [1,008.96]	0.00 (0.00) [0]
994	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPASS	1/2018	/ (-) [0/0]	564.66 (-) [564.66]	0.00 (0.00) [0]
995	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [11/2020]	476.56 (-) [476.56]	0.00 (0.00) [40]
996	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
997	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [0/0]	953.09 (-) [953.09]	0.00 (0.00) [0]
998	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [0/0]	668.86 (-) [668.86]	0.00 (0.00) [0]
999	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [0/0]	614.48 (-) [614.48]	0.00 (0.00) [0]
1000	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	0.00 (0.00) [0]
1001	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
1002	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [0/0]	503.88 (-) [503.88]	0.00 (0.00) [0]
1003	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2020]	1,288.07 (-) [1,420.00]	0.00 (131.93) [0]
1004	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
1005	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
1006	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
1007	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	0.00 (-0.05) [0]
1008	REHABILITATION AND UPGRADATION OF SIX LANING OF	1/2018	/	999.00	0.00

	BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141		(-) [0/0]	(-) [999.00]	(0.00) [0]
1009	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	0.00 (0.04) [0]
1010	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1011	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1012	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,613.62 (0.00) [0]
1013	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [0/0]	806.11 (-) [806.11]	0.00 (0.00) [0]
1014	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	3/2014	5/2016 (-) [0/0]	162.51 (163.00) [163.00]	0.00 (0.49) [0]
1015	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	0.00 (0.50) [0]
1016	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [240.00]	0.00 (0.09) [0]
1017	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [327.00]	0.00 (0.37) [0]
1018	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [11/2018]	157.30 (157.00) [157.00]	0.00 (-0.30) [5]
1019	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	0.00 (0.00) [0]
1020	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	0.00 (0.00) [0]
1021	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [0/0]	226.31 (226.00) [226.00]	0.00 (-0.31) [0]
	<u>Steel</u>				
1022	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (-) [5/2019]	3,127.30 (-) [3,127.30]	2,509.89 (0.00) [13]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1023	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	23.79 (0.00) [0]
1024	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	28.60 (0.00) [0]
	<u>Health And Family Welfare</u>				
1025	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [6/2020]	703.00 (-) [703.00]	272.00 (0.00) [0]
1026	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [12/2018]	152.95 (-) [152.95]	58.52 (0.00) [10]
	<u>Railways</u>				

1027	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	4/2009	/ (-) [0/0]	396.04 (-) [369.00]	186.27 (-27.04) [0]
1028	QADIAN-BEAS	4/2011	/ (-) [0/0]	205.22 (-) [205.22]	3.18 (0.00) [0]
	Road Transport And Highways				
1029	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	/ (-) [0/0]	573.96 (605.00) [605.00]	209.74 (31.04) [0]
1030	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	/ (-) [0/0]	486.74 (-) [486.74]	189.39 (0.00) [0]
1031	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (-) [1,169.61]	481.60 (0.00) [-]
1032	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	/ (-) [0/0]	463.65 (546.00) [463.65]	280.16 (0.00) [0]
1033	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	/ (-) [0/0]	483.38 (-) [483.38]	65.76 (0.00) [0]
1034	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	/ (-) [0/0]	616.36 (-) [616.36]	68.58 (0.00) [0]
1035	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	299.81 (0.00) [0]
1036	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [889.24]	389.64 (0.00) [0]
1037	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [9/2019]	1,388.34 (-) [1,388.34]	206.87 (0.00) [0]
1038	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	/ (-) [0/0]	312.79 (-) [312.79]	17.57 (0.00) [0]
1039	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	7/2014	/ (-) [0/0]	319.80 (-) [319.80]	102.55 (0.00) [0]
1040	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	0.00 (1.73) [1]
1041	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	99.86 (0.00) [0]
1042	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	/ (-) [0/0]	578.38 (-) [578.38]	128.53 (0.00) [0]
1043	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [4/2019]	447.29 (-) [447.29]	31.96 (0.00) [16]
1044	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [0/0]	261.76 (-) [261.76]	0.00 (0.00) [0]
1045	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2019]	479.00 (-) [479.00]	392.14 (0.00) [-]
1046	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	/ (-) [4/2019]	273.06 (-) [273.06]	28.90 (0.00) [-]

1047	JALANDHAR - AMRITSAR	1/2014	1/2016 (-) [0/0]	523.85 (-) [523.85]	170.68 (0.00) [0]
1048	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [1/2020]	196.05 (-) [196.05]	21.93 (0.00) [-]
1049	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	0.00 (0.00) [0]
1050	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	/ (-) [0/0]	435.90 (-) [435.90]	31.02 (0.00) [0]
1051	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	/ (-) [0/0]	279.68 (-) [279.68]	25.28 (0.00) [0]
1052	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	/ (-) [0/0]	899.21 (-) [899.21]	25.08 (0.00) [0]
1053	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	26.92 (0.00) [0]
	<u>Urban Development</u>				
1054	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (8/2018) [3/2019]	388.00 (-) [388.00]	391.23 (0.00) [22]
1055	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	9/2018 (-) [9/2018]	430.00 (-) [430.00]	25.49 (0.00) [0]
1056	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (6/2019) [9/2019]	294.00 (-) [294.00]	127.86 (0.00) [5]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1057	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (3/2017) [12/2020]	12,320.00 (-) [12,320.00]	9,937.00 (0.00) [48]
	<u>Coal</u>				
1058	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	173.06 (0.00) [0]
1059	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	8.71 (0.00) [0]
	<u>Petroleum</u>				
1060	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1061	LPG BP PROJECT JODHPUR	3/2018	/ (-) [0/0]	229.80 (-) [229.80]	69.04 (0.00) [0]
	<u>Power</u>				
1062	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [1/2019]	1,429.38 (-) [1,429.38]	743.82 (0.00) [0]
1063	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	7/2015	11/2017 (-) [11/2018]	307.18 (-) [307.18]	206.21 (0.00) [12]
	<u>Railways</u>				
1064	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,103.04]	2.32 (229.33) [0]

1065	AJMER-BANGURGRAM	4/2011	11/2019 (-) [11/2019]	213.39 (-) [244.02]	206.88 (30.63) [0]
1066	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/	822.00	0.00
			(-) [0/0]	(-) [1,099.54]	(277.54) [0]
1067	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [3/2019]	242.09 (-) [349.00]	278.89 (106.91) [1]
1068	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2019]	246.08 (-) [348.55]	127.14 (102.47) [-6]
1069	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [2/2019]	410.08 (780.98) [795.01]	450.57 (384.93) [0]
1070	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	4/2008	3/2015 (-) [3/2020]	829.74 (-) [1,216.00]	712.13 (386.26) [60]
1071	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	4/2008	3/2014 (3/2019) [3/2019]	653.19 (-) [1,116.00]	795.27 (462.81) [60]
1072	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [8/2022]	808.85 (-) [808.85]	0.00 (0.00) [0]
1073	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	4/2013	3/2020 (-) [12/2019]	420.18 (295.02) [420.18]	81.44 (0.00) [-3]
1074	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [12/2019]	493.17 (-) [493.17]	410.89 (0.00) [21]
1075	PUSHKAR-MERTA	4/2013	/	323.00	0.00
			(-) [0/0]	(-) [432.22]	(109.22) [0]
1076	RANI-MARWAR JN. PATCH DOUBLING	4/2012	11/2018 (-) [12/2018]	288.97 (-) [346.35]	295.70 (57.38) [1]
1077	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [10/2018]	236.93 (-) [294.90]	162.66 (57.97) [0]
	<u>Road Transport And Highways</u>				
1078	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [12/2018]	597.00 (-) [597.00]	604.80 (0.00) [14]
1079	2-LANE WITH PAVED SHOULDER TONK- SAWAIMADHOPUR	8/2016	1/2019 (-) [1/2019]	320.30 (-) [320.30]	193.54 (0.00) [0]
1080	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA	11/2012	8/2016 (-) [11/2018]	530.07 (-) [530.07]	556.02 (0.00) [27]
1081	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/	688.70	470.78
			(-) [11/2019]	(-) [688.70]	(0.00) [-]
1082	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/	1,031.95	367.00
			(-) [8/2020]	(-) [1,031.95]	(0.00) [-]
1083	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [3/2019]	822.90 (-) [822.90]	688.00 (0.00) [11]
1084	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)- TANOT FROM	3/2018	/	1,158.35	0.00
			(-) [0/0]	(-) [1,158.35]	(0.00) [0]

1085	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	0.00 (0.00) [0]
1086	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1087	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	0.00 (0.00) [0]
1088	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	167.09 (0.00) [5]
1089	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	0.00 (0.00) [3]
1090	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	0.00 (0.00) [0]
1091	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (9/2017) [12/2018]	1,673.70 (-) [1,673.70]	3,079.44 (0.00) [86]
1092	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1093	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1094	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	9/2015	3/2018 (-) [12/2018]	567.51 (-) [567.51]	53.70 (0.00) [9]
1095	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1096	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	1/1991	5/2016 (-) [0/0]	208.87 (-) [208.87]	206.78 (0.00) [0]
1097	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	10/2016 (-) [0/0]	269.26 (-) [269.26]	212.72 (0.00) [0]
1098	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1099	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	610.00 (0.00) [-]
1100	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	475.69 (0.00) [-]
1101	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [894.00]	15.00 (0.00) [-5]
1102	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR	9/2014	9/2016 (-) [3/2019]	425.19 (-) [425.19]	274.20 (0.00) [30]
1103	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [12/2018]	275.90 (-) [275.90]	242.51 (0.00) [-]
1104	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [11/2018]	331.46 (-) [331.46]	247.91 (0.00) [1]
1105	TWO LANNING WITH PAVED SHOULDER OF SALASAR-	6/2016	6/2019	637.18	571.06

	NAGAU		(-) [9/2019]	(-) [637.18]	(0.00) [3]
1106	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/	874.25	0.00
			(-) [0/0]	(-) [874.25]	(0.00) [0]
1107	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/	1,103.88	0.00
			(-) [0/0]	(-) [1,103.88]	(0.00) [0]
1108	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015	257.09	14.80
			(-) [0/0]	(-) [257.09]	(0.00) [0]
1109	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015	383.40	224.68
			(-) [6/2019]	(-) [383.40]	(0.00) [51]
1110	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015	269.22	33.24
			(-) [0/0]	(-) [269.22]	(0.00) [0]
1111	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018	621.43	0.00
			(-) [0/0]	(-) [621.43]	(0.00) [0]
	<u>Urban Development</u>				
1112	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017	189.00	0.00
			(-) [0/0]	(-) [189.00]	(0.00) [0]
1113	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019	549.31	197.12
			(-) [10/2019]	(-) [540.42]	(-8.89) [3]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1114	SEVOK RANGPO, NEFR	4/2008	12/2015	1,339.48	383.92
			(-) [3/2020]	(-) [4,084.69]	(2,745.21) [51]
	<u>Road Transport And Highways</u>				
1115	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013	182.28	24.36
			(-) [0/0]	(-) [182.00]	(-0.28) [0]
1116	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013	151.59	0.00
			(-) [0/0]	(-) [151.59]	(0.00) [0]
1117	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013	166.27	0.00
			(-) [0/0]	(-) [166.27]	(0.00) [0]
1118	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/	375.80	0.00
			(-) [0/0]	(-) [375.80]	(0.00) [0]
1119	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017	290.05	18.12
			(-) [0/0]	(-) [290.05]	(0.00) [0]
1120	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017	318.42	7.50
			(-) [0/0]	(-) [318.42]	(0.00) [0]
1121	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018	264.84	0.00
			(-) [0/0]	(-) [264.84]	(0.00) [0]
1122	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017	388.00	0.00
			(-) [0/0]	(-) [447.37]	(59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1123	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020	39,849.00	10,632.00
			(-)	(-)	(0.00)

			[11/2023]	[39,849.00]	[36]
1124	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [3/2019]	3,492.00 (-) [6,100.00]	5,687.52 (2,608.00) [102]
	<u>Coal</u>				
1125	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (9/2019) [9/2019]	1,458.17 (709.06) [709.06]	391.20 (-749.11) [51]
1126	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (12/2018) [3/2019]	5,907.11 (-) [5,907.11]	5,770.46 (0.00) [39]
	<u>Mines</u>				
1127	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (6/2019) [6/2019]	166.62 (166.62) [166.62]	125.00 (0.00) [0]
	<u>Petroleum</u>				
1128	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	0.17 (0.00) [0]
1129	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	575.65 (0.00) [0]
1130	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [5/2021]	466.43 (-) [466.43]	1.18 (0.00) [7]
1131	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [12/2020]	4,497.00 (-) [4,497.00]	302.17 (0.00) [24]
1132	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1133	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [4/2019]	390.52 (390.52) [390.52]	172.79 (0.00) [1]
1134	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [0/0]	678.00 (-) [678.00]	5.12 (0.00) [0]
1135	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	16.73 (0.00) [0]
1136	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.42 (0.00) [0]
	<u>Power</u>				
1137	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	9/2011	9/2014 (-) [10/2018]	1,940.13 (-) [2,702.65]	2,529.92 (762.52) [0]
1138	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (-) [12/2018]	1,779.29 (-) [2,534.00]	2,051.63 (754.71) [121]
1139	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [7/2019]	186.17 (-) [186.17]	50.27 (0.00) [0]
	<u>Railways</u>				
1140	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [3/2018]	257.00 (257.00) [257.00]	0.00 (0.00) [0]
1141	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [2/2019]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1142	CHENNAI BEACH-TAMBARAM-CHENGALPATTU	4/1998	/	271.24	468.18

	SUBURBAN GC		(-) [0/0]	(-) [520.00]	(248.76) [0]
1143	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/	198.68	303.72
			(-) [0/0]	(-) [556.64]	(357.96) [0]
1144	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	9/2006	/	343.17	1,049.68
			(-) [0/0]	(-) [1,065.00]	(721.83) [0]
1145	ERODE-PALANI	4/2008	/	288.57	1.63
			(-) [0/0]	(-) [1,140.00]	(851.43) [0]
1146	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (3/2019) [3/2019]	495.74 (495.74) [734.01]	445.91 (238.27) [69]
1147	KARUR-SALEM(NL),SR	2/1997	/	155.55	856.94
			(-) [0/0]	(-) [920.00]	(764.45) [0]
1148	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020	760.00	0.00
			(-) [3/2020]	(-) [1,182.31]	(422.31) [0]
1149	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION	2/1997	3/2015	458.63	0.92
			(-) [0/0]	(-) [458.63]	(0.00) [0]
1150	MADURAI-BODINAYAKKANUR	4/2008	/	164.41	83.15
			(-) [3/2020]	(-) [450.00]	(285.59) [-]
1151	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	2/2003	3/2009	199.55	2.12
			(-) [0/0]	(-) [330.32]	(130.77) [0]
1152	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.	2/2006	3/2012	208.00	3.58
			(-) [0/0]	(-) [208.00]	(0.00) [0]
1153	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022	1,700.00	0.00
			(-) [3/2022]	(-) [1,700.00]	(0.00) [0]
1154	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019	724.69	1,169.07
			(-) [2/2019]	(-) [2,072.50]	(1,347.81) [0]
1155	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014	187.26	7.62
			(-) [3/2020]	(-) [231.67]	(44.41) [71]
1156	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/	839.00	0.61
			(-) [0/0]	(-) [1,500.00]	(661.00) [0]
1157	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005	268.87	304.07
			(-) [0/0]	(-) [302.02]	(33.15) [0]
1158	TIDIVANAM-NAGARI (NL)	9/2006	/	582.83	237.73
			(-) [0/0]	(-) [2,300.00]	(1,717.17) [0]
1159	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/	227.40	61.97
			(-) [0/0]	(-) [900.00]	(672.60) [0]
1160	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024	1,567.00	0.00
			(-) [3/2026]	(-) [1,567.00]	(0.00) [24]
1161	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	2/2000	3/2014	200.84	394.26
			(-) [0/0]	(-) [200.84]	(0.00) [0]
1162	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	2/2005	3/2010	600.00	671.00
			(-)	(600.00)	(45.54)

			[0/0]	[645.54]	[0]
	Road Transport And Highways				
1163	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [12/2018]	485.00 (-) [485.00]	406.68 (0.00) [64]
1164	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [12/2019]	624.00 (-) [624.00]	350.79 (0.00) [68]
1165	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	0.00 (0.00) [0]
1166	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [0/0]	1,227.87 (-) [1,227.87]	0.00 (0.00) [0]
1167	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1168	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1169	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [0/0]	600.00 (-) [600.00]	325.55 (0.00) [0]
1170	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [0/0]	1,016.92 (-) [1,016.92]	0.00 (0.00) [0]
1171	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [5/2019]	1,387.11 (-) [1,387.11]	895.57 (0.00) [18]
1172	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [0/0]	628.71 (-) [628.71]	0.00 (0.00) [0]
1173	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,065.96]	0.00 (0.00) [0]
1174	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [0/0]	1,166.26 (-) [1,166.26]	0.00 (0.00) [0]
1175	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [4/2019]	641.17 (-) [641.17]	244.33 (0.00) [33]
1176	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [0/0]	505.35 (-) [505.35]	0.00 (0.00) [0]
1177	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [0/0]	1,176.37 (-) [1,176.37]	0.00 (0.00) [0]
1178	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [6/2019]	707.82 (-) [707.82]	180.17 (0.00) [10]
1179	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	5.00 (0.00) [0]
1180	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [0/0]	641.17 (-) [641.17]	204.31 (0.00) [0]
1181	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1182	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-)	379.90 (-)	0.00 (0.00)

			[0/0]	[379.90]	[0]
1183	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [12/2018]	1,250.00 (-) [1,250.00]	1,329.17 (0.00) [60]
1184	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	11/2014	11/2016 (-) [0/0]	563.92 (-) [563.92]	186.50 (0.00) [0]
1185	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1186	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	627.37 (0.00) [0]
1187	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [12/2018]	374.00 (-) [374.00]	237.00 (0.00) [67]
1188	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [633.55]	0.00 (0.00) [0]
1189	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [6/2019]	563.92 (-) [563.92]	96.48 (0.00) [18]
	<u>Shipping And Ports</u>				
1190	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (-) [5/2020]	600.00 (258.00) [257.90]	1.45 (-342.10) [29]
1191	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (-) [0/0]	244.50 (258.00) [275.98]	275.98 (31.48) [0]
1192	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (-) [0/0]	150.00 (-) [600.00]	139.80 (450.00) [0]
1193	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]
	<u>Urban Development</u>				
1194	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE- IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [10/2019]	209.00 (-) [209.00]	52.00 (0.00) [0]
1195	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1196	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.77 (4,458.00) [0]
1197	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [0/0]	348.77 (-) [348.77]	0.00 (0.00) [0]
1198	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	4/2014	9/2016 (-) [0/0]	332.72 (-) [342.00]	321.13 (9.28) [0]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1199	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	0.00 (0.00) [0]
1200	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2019]	426.79 (-) [426.79]	0.00 (0.00) [12]
1201	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-)	447.06 (-)	353.61 (-9.55)

			[3/2021]	[437.51]	[72]
1202	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1203	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2019]	413.84 (-) [413.84]	0.00 (0.00) [0]
1204	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2019]	397.09 (-) [442.42]	79.96 (45.33) [0]
1205	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	146.45 (-33.01) [44]
1206	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	12.69 (-78.25) [72]
1207	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	159.87 (0.00) [0]
1208	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	477.74 (70.65) [132]
1209	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	1.31 (186.52) [72]
1210	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2019]	430.45 (-) [415.37]	160.45 (-15.08) [36]
1211	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [3/2019]	365.01 (-) [365.01]	204.26 (0.00) [45]
1212	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2019]	209.78 (-) [209.78]	154.21 (0.00) [48]
1213	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	186.91 (199.83) [144]
	<u>Power</u>				
1214	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	7/2020 (10/2020) [10/2020]	10,598.98 (-) [10,598.98]	2,701.10 (0.00) [3]
	<u>Railways</u>				
1215	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (3/2017) [12/2020]	632.68 (-) [816.55]	595.33 (183.87) [57]
1216	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	169.16 (0.00) [0]
1217	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	723.00 (-) [616.08]	0.00 (-106.92) [0]
1218	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (-) [458.26]	3.69 (0.01) [0]
1219	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	0.00 (65.24) [0]
1220	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (3/2022) [3/2022]	1,160.48 (-) [1,160.47]	111.36 (-0.01) [144]
1221	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92

			(-) [0/0]	(2,911.84) [2,911.84]	(1,799.84) [0]
1222	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	/ (3/2017) [3/2017]	124.43 (926.23) [1,025.00]	1,021.82 (900.57) [0]
1223	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	219.80 (0.00) [0]
	<u>Road Transport And Highways</u>				
1224	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	3/2016 (-) [0/0]	340.00 (-) [340.00]	0.00 (0.00) [0]
1225	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [6/2019]	1,266.60 (-) [1,544.00]	1,410.94 (277.40) [33]
1226	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	3/2011	12/2015 (-) [0/0]	218.31 (-) [339.82]	208.28 (121.51) [0]
1227	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	0.00 (0.00) [0]
1228	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1229	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (3/2018) (-) [0/0]	857.62 (-) [857.62]	0.00 (0.00) [0]
1230	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (3/2018) (-) [0/0]	802.65 (-) [802.65]	0.00 (0.00) [0]
1231	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (3/2018) (-) [0/0]	950.63 (-) [950.63]	0.00 (0.00) [0]
1232	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (3/2018) (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1233	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (-) [7/2019]	1,423.96 (-) [1,423.96]	502.66 (0.00) [8]
1234	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO	12/2013	3/2016 (-) [0/0]	158.65 (-) [158.65]	103.50 (0.00) [0]
1235	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	3/2016 (-) [0/0]	177.18 (-) [177.18]	40.51 (0.00) [0]
1236	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1237	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [313.27]	0.00 (17.80) [0]
1238	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	12/2016 (-) [0/0]	244.30 (-) [156.09]	0.00 (-88.21) [0]
1239	YAN TO NIRMAL SERE HABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW	12/2013	3/2016 (-) [0/0]	244.08 (-) [244.08]	38.32 (0.00) [0]
	<u>Urban Development</u>				
1240	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (-) [209.84]	9.96 (0.00) [0]

	<u>TRIPURA</u>				
	<u>Power</u>				
1241	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
1242	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (1,942.00) [3,374.00]	3,015.98 (2,232.00) [60]
1243	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
1244	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (4,118.00) [1,733.20]	1,543.99 (838.20) [0]
	<u>Road Transport And Highways</u>				
1245	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	246.46 (0.00) [0]
1246	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				
1247	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1248	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1249	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Coal</u>				
1250	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	3/2018 (-) [3/2019]	1,131.28 (-) [1,131.28]	572.40 (0.00) [12]
1251	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	3,716.05 (0.80) [0]
	<u>Health And Family Welfare</u>				
1252	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [4/2020]	785.00 (-) [785.00]	39.35 (0.00) [0]
1253	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [0/0]	268.84 (-) [268.84]	18.50 (0.00) [0]
	<u>Petroleum</u>				
1254	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	3.41 (0.00) [0]
1255	AURAIYA PHULPUR PIPELINE PROJECT	7/2015	12/2018 (-) [12/2018]	1,427.94 (-) [800.00]	600.58 (-627.94) [0]
1256	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	200.89 (0.00) [0]
1257	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	99.03 (0.00) [0]
1258	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK	8/2017	8/2020	255.40	0.00

	IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY		(-) [8/2020]	(-) [255.40]	(0.00) [0]
1259	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [8/2021]	318.80 (-) [318.80]	12.65 (0.00) [0]
	<u>Power</u>				
1260	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (2/2018) [3/2019]	195.42 (294.60) [294.60]	215.93 (99.18) [61]
1261	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW)	7/2013	12/2016 (-) [0/0]	3,363.12 (-) [3,363.12]	2,244.00 (0.00) [0]
1262	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	12/2016 (-) [8/2019]	9,750.89 (-) [9,750.89]	8,789.00 (0.00) [32]
1263	TANDA TPP STAGE-II (2X660 MW)	9/2014	3/2019 (9/2019) [9/2019]	9,188.98 (-) [9,188.98]	5,195.95 (0.00) [6]
	<u>Railways</u>				
1264	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	4/1999	12/2009 (-) [0/0]	108.00 (-) [432.72]	446.52 (324.72) [0]
1265	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [308.00]	0.00 (1.00) [0]
1266	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [366.71]	0.45 (-233.29) [0]
1267	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	8/2018 (-) [8/2018]	199.75 (-) [270.00]	265.14 (70.25) [0]
1268	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1269	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	894.91 (0.00) [3]
1270	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	/ (-) [3/2018]	195.64 (-) [435.00]	447.20 (239.36) [0]
1271	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	0.00 (111.84) [0]
1272	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1273	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1274	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [245.39]	210.67 (125.39) [0]
1275	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	4/2013	/ (-) [0/0]	654.00 (-) [654.00]	0.00 (0.00) [0]
1276	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1277	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	4/1997	4/1999 (-) [0/0]	233.00 (-) [318.42]	334.60 (85.42) [0]

1278	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [1/2022]	213.00 (-) [213.35]	0.55 (0.35) [69]
1279	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	0.00 (0.00) [0]
1280	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	0.00 (0.00) [0]
1281	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1282	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	15.79 (0.00) [9]
1283	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [977.00]	978.21 (49.99) [12]
1284	MANDHANA - BRAHMAWART NEW LINE PROJECT.	4/1997	4/1999 (-) [12/2018]	609.04 (1,063.00) [1,807.88]	1,805.26 (1,198.84) [236]
1285	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	668.70 (668.00) [668.00]	0.00 (-0.70) [0]
1286	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	335.37 (0.00) [21]
1287	MEERUT-MUZAFARNAGAR PATCH DL	4/2012	/ (-) [0/0]	377.44 (-) [377.44]	182.85 (0.00) [0]
1288	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1289	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,343.00]	0.00 (0.00) [0]
1290	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [10/2022]	622.50 (427.00) [426.74]	22.53 (-195.76) [66]
1291	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	256.36 (0.00) [12]
1292	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [2/2019]	1,295.42 (-) [1,295.42]	99.33 (0.00) [-37]
1293	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	3/2014 (-) [4/2021]	1,177.96 (-) [1,028.95]	0.60 (-149.01) [85]
1294	UNCHAHAR-AMETHI	4/2012	/ (-) [0/0]	1,229.00 (-) [380.00]	4.12 (-849.00) [0]
1295	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	4/2006	3/2010 (-) [0/0]	369.90 (-) [1,581.53]	618.19 (1,211.63) [0]
1296	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [943.60]	122.70 (0.00) [33]
Road Transport And Highways					
1297	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	232.93 (0.00) [0]

1298	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1299	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	425.99 (0.00) [0]
1300	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	603.13 (0.00) [0]
1301	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [9/2018]	291.36 (-) [291.36]	430.61 (0.00) [0]
1302	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	191.48 (0.00) [0]
1303	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,580.02 (0.00) [7]
1304	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,120.57]	0.00 (0.00) [0]
1305	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [2/2020]	1,668.00 (-) [1,668.00]	297.13 (0.00) [-]
1306	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	681.34 (0.00) [0]
1307	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	0.00 (0.00) [-]
1308	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	50.71 (0.00) [-]
1309	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	193.08 (0.00) [0]
1310	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [4/2019]	1,587.49 (-) [1,587.49]	145.81 (0.00) [0]
1311	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	135.54 (0.00) [0]
1312	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [1/2019]	1,657.20 (-) [1,657.20]	1,945.00 (0.00) [0]
1313	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	886.98 (382.01) [0]
1314	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1315	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [4/2019]	676.73 (-) [676.73]	409.11 (0.00) [0]
1316	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	3/2018 (-) [0/0]	774.57 (-) [774.57]	0.00 (0.00) [0]
1317	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	1/2014	10/2016 (-) [0/0]	397.04 (-) [397.04]	0.00 (0.00) [0]
1318	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL	10/2013	3/2017	317.76	15.47

	SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43		(-) [0/0]	(-) [317.76]	(0.00) [0]
1319	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [9/2018]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1320	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	/ (-) [0/0]	629.74 (-) [629.74]	0.00 (0.00) [0]
1321	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	0.00 (0.00) [0]
1322	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [534.55]	211.60 (0.00) [0]
1323	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1324	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [0/0]	1,117.84 (-) [1,117.84]	0.00 (0.00) [0]
1325	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	314.70 (0.00) [0]
1326	CONSTRUCTION OF RING ROAD FOR RAE BARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	0.00 (0.00) [0]
1327	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	1/2016	5/2019 (-) [5/2019]	701.12 (-) [701.12]	842.34 (0.00) [0]
1328	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [6/2019]	1,081.57 (-) [1,081.57]	784.53 (0.00) [0]
1329	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [5/2020]	1,232.21 (-) [1,232.21]	637.48 (0.00) [-]
1330	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [5/2020]	1,989.00 (-) [1,989.00]	842.34 (0.00) [2]
1331	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018 (-) [0/0]	785.78 (-) [785.78]	839.63 (0.00) [0]
1332	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,998.25 (0.00) [0]
1333	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	0.00 (0.00) [0]
1334	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	0.00 (0.00) [0]
1335	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [925.40]	0.00 (0.00) [0]
1336	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	439.40 (0.00) [0]
1337	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	372.80 (0.00) [0]
1338	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-)	1,027.53 (-)	433.51 (0.00)

			[0/0]	[1,027.53]	[0]
1339	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	328.63 (0.00) [0]
1340	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1341	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	0.00 (0.00) [8]
1342	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [8/2020]	1,184.71 (-) [1,310.00]	0.00 (125.29) [5]
1343	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [4/2019]	899.00 (-) [899.00]	351.90 (0.00) [0]
1344	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,948.72 (0.00) [0]
1345	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	10/2016 (-) [0/0]	283.45 (-) [283.45]	0.00 (0.00) [0]
1346	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	531.60 (0.00) [0]
1347	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [1,025.80]	0.00 (0.00) [0]
1348	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [1,115.28]	0.00 (0.00) [0]
1349	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [445.89]	0.00 (0.00) [0]
1350	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1351	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	3/2017 (-) [0/0]	493.94 (-) [493.94]	0.00 (0.00) [0]
1352	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	10/2016 (-) [0/0]	227.74 (-) [227.74]	0.00 (0.00) [0]
1353	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1354	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1355	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1356	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	0.00 (0.00) [0]
	<u>Steel</u>				
1357	FORGED WHEEL PLANT	4/2014	9/2018 (-) [3/2019]	1,682.85 (-) [1,682.85]	802.10 (0.00) [6]
	<u>Urban Development</u>				
1358	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT	11/2017	3/2020	171.72	0.00

	KANPUR		(-) [3/2020]	(-) [171.72]	(0.00) [0]
1359	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Petroleum</u>				
1360	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [2/2020]	160.10 (-) [160.10]	25.56 (0.00) [0]
	<u>Power</u>				
1361	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	151.99 (274.07) [0]
1362	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	131.82 (0.00) [0]
1363	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (-) [3,846.30]	3,690.33 (867.82) [93]
1364	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (12/2020) [5/2021]	1,657.00 (2,978.86) [4,401.90]	2,672.04 (2,744.90) [63]
1365	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2021]	2,491.58 (-) [4,105.30]	1,583.40 (1,613.72) [102]
	<u>Railways</u>				
1366	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	38.33 (126.80) [0]
1367	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1368	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2026]	16,216.00 (-) [16,216.00]	1,081.06 (0.00) [15]
	<u>Road Transport And Highways</u>				
1369	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	0.00 (0.00) [0]
1370	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	0.00 (0.00) [0]
1371	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [7/2018]	605.84 (-) [605.84]	722.46 (0.00) [0]
1372	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	122.72 (0.00) [-]
1373	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	0.00 (0.00) [0]
1374	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1375	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [10/2019]	720.00 (-) [720.00]	181.70 (0.00) [-]
1376	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [7/2019]	478.51 (-) [478.00]	409.17 (-0.51) [69]

1377	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	40.04 (0.00) [0]
1378	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [284.00]	86.43 (0.49) [0]
1379	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	0.00 (0.00) [0]
1380	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [6/2019]	282.08 (-) [282.08]	45.92 (0.00) [0]
1381	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	35.76 (0.00) [0]
1382	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	74.52 (0.00) [0]
1383	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	78.85 (0.00) [0]
1384	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	0.14 (0.00) [0]
1385	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.74 (0.27) [0]
1386	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.01 (0.00) [0]
	<u>Urban Development</u>				
1387	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Coal</u>				
1388	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	296.64 (0.00) [0]
1389	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2019]	2,661.73 (-) [2,661.73]	174.04 (0.00) [0]
1390	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1391	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	382.14 (0.00) [24]
	<u>Health And Family Welfare</u>				
1392	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [0/0]	244.00 (-) [244.00]	214.62 (0.00) [0]
1393	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [0/0]	168.90 (-) [191.38]	191.38 (22.48) [0]
1394	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [0/0]	651.99 (-) [651.99]	19.50 (0.00) [0]
1395	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2019]	355.15 (-) [355.15]	71.50 (0.00) [0]

	<u>Petroleum</u>				
1396	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,712.00]	6.28 (0.00) [-15]
1397	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [9/2019]	2,934.40 (-) [2,934.40]	738.18 (0.00) [0]
1398	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	3/2014	9/2017 (6/2018) [6/2018]	3,076.00 (4,190.00) [4,190.00]	3,184.09 (1,114.00) [0]
1399	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	21.02 (0.00) [0]
1400	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1401	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (12/2018) [12/2018]	694.00 (1,097.54) [694.00]	507.96 (0.00) [2]
1402	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [4/2020]	163.02 (-) [163.02]	32.69 (0.00) [0]
	<u>Power</u>				
1403	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (-) [11/2019]	454.11 (-) [454.11]	238.92 (0.00) [19]
1404	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,381.84]	376.58 (0.00) [29]
	<u>Railways</u>				
1405	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (1,966.70) [2,373.00]	484.85 (1,345.60) [324]
1406	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24.	4/1998	3/2022 (-) [3/2022]	1,027.40 (-) [2,373.00]	481.65 (1,345.60) [0]
1407	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [0/0]	1,106.62 (-) [1,092.20]	620.73 (-14.42) [0]
1408	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [0/0]	255.64 (-) [272.20]	88.25 (16.56) [0]
1409	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/ (-) [0/0]	289.64 (-) [760.00]	0.13 (470.36) [0]
1410	BOWAICHANDI-ARAMBAGH	4/2010	/ (3/2025) [3/2025]	267.37 (-) [620.00]	40.77 (352.63) [-]
1411	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [0/0]	573.78 (-) [268.52]	0.67 (-305.26) [0]
1412	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	4/2009	2/2012 (-) [0/0]	259.51 (-) [533.59]	144.46 (274.08) [0]
1413	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [4,874.58]	1,881.65 (0.00) [0]
1414	GHUTIASHARIF-CANNING (ER)	4/2009	12/2011 (-) [0/0]	193.08 (-) [612.45]	150.70 (419.37) [0]
1415	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007	393.46	182.49

			(3/2007) [0/0]	(154.30) [1,026.00]	(632.54) [0]
1416	MM FROM PANSKURA-GHATAL NL	4/2011	0/0 (3/2030) [3/2030]	276.69 (-) [426.00]	0.00 (149.31) [-]
1417	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [3/2020]	221.42 (-) [380.00]	97.55 (158.58) [-]
1418	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (-) [614.00]	267.93 (316.68) [12]
1419	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	283.55 (-) [451.00]	457.51 (167.45) [0]
1420	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	18.38 (9.73) [-21]
1421	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1422	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (4,200.00) [2,913.50]	768.02 (-0.01) [108]
1423	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1424	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	1,866.83 (307.50) [108]
1425	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (12/2021) [12/2021]	1,013.45 (1,013.45) [1,428.00]	484.48 (414.55) [0]
1426	TAMLUK DIGHA,LINE DOUBLING (SER)	3/1984	6/2005 (-) [0/0]	293.97 (-) [749.69]	0.00 (455.72) [0]
1427	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2019]	1,188.91 (-) [1,620.01]	843.85 (431.10) [0]
1428	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,544.30 (2,355.23) [0]
	Road Transport And Highways				
1429	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [5/2019]	1,083.00 (-) [1,083.00]	105.70 (0.00) [11]
1430	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [0/0]	998.79 (-) [998.79]	1,822.70 (0.00) [0]
1431	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [0/0]	1,078.84 (-) [1,078.84]	2,310.60 (0.00) [0]
1432	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,614.84 (0.00) [0]
1433	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [12/2019]	361.15 (-) [361.15]	0.00 (0.00) [-]
1434	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	0.00 (0.00) [0]
1435	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK,	3/2016	11/2018	229.37	6.39

	HALDIA		(-) [11/2018]	(-) [229.37]	(0.00) [0]
1436	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [8/2018]	767.03 (-) [767.03]	123.31 (0.00) [0]
1437	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [0/0]	702.16 (-) [702.16]	441.57 (0.00) [0]
1438	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1439	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1440	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [1,665.00]	1,836.44 (0.00) [0]
	<u>Urban Development</u>				
1441	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [3/2019]	156.57 (-) [156.57]	146.31 (0.00) [31]
1442	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1443	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	89.94 (0.00) [15]
	Total			18,30,362.48 (3,51,180.50) [21,51,136.69]	7,97,496.44 (3,20,774.21)

North East Project Detail's

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on 30.11.2018)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
1	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUMKH	1/2016	2/2019 (-) [12/2018]	247.52 (-) [247.52]	139.42 (0.00) [-2]
	<u>Power</u>				
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (3/2019) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,838.94 (3,683.06) [111]
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,385.81 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
6	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59)	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
7	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM.583.450)	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
9	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
10	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	38.50 (0.00) [0]
13	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
14	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
15	CONSTRUCTION OF TWOLANE WITH PAVED	2/2017	4/2017	216.71	0.00

	SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS		(-) [0/0]	(-) [216.71]	(0.00) [0]
16	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
17	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/	264.16	0.00
			(-) [0/0]	(-) [264.16]	(0.00) [0]
18	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016	334.22	0.00
			(-) [0/0]	(-) [334.22]	(0.00) [0]
19	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	0.00
			(-) [0/0]	(-) [434.06]	(0.00) [0]
20	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	0.00
			(-) [0/0]	(-) [284.09]	(0.00) [0]
21	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	0.00
			(-) [0/0]	(-) [195.23]	(0.00) [0]
22	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	0.00
			(-) [0/0]	(-) [203.36]	(0.00) [0]
23	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	0.00
			(-) [0/0]	(-) [194.66]	(0.00) [0]
24	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	0.00
			(-) [0/0]	(-) [198.22]	(0.00) [0]
25	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012	207.03	0.00
			(-) [0/0]	(-) [207.03]	(0.00) [0]
26	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010	165.00	0.00
			(-) [0/0]	(-) [165.00]	(0.00) [0]
27	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017	180.57	0.00
			(-) [0/0]	(-) [180.57]	(0.00) [0]
28	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017	168.32	0.00
			(-) [0/0]	(-) [168.32]	(0.00) [0]
29	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012	156.63	132.21
			(-) [0/0]	(276.00) [276.00]	(119.37) [0]
30	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011	305.49	0.00
			(-) [0/0]	(-) [305.49]	(0.00) [0]
31	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010	104.00	0.00
			(-) [0/0]	(-) [201.00]	(97.00) [0]
	ASSAM				
	Health And Family Welfare				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	174.00
			(-) [5/2021]	(-) [875.00]	(0.00) [0]
33	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	113.50
			(-) [0/0]	(-) [175.57]	(0.00) [0]
	Petroleum				
34	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (3/2019)	2,465.15 (-)	2,107.69 (-86.29)

			[3/2019]	[2,378.86]	[72]
35	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	69.88 (0.00) [0]
36	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	268.88 (0.00) [0]
37	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
38	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	60.44 (127.41) [70]
39	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	208.63 (0.00) [0]
40	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	1.65 (0.00) [0]
41	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,208.92 (0.00) [0]
42	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	98.10 (-5.15) [0]
43	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Power</u>				
44	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [12/2018]	4,375.35 (8,150.00) [8,150.00]	7,186.04 (3,774.65) [87]
	<u>Railways</u>				
45	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (-) [551.00]	595.01 (237.00) [0]
46	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	193.12 (-50.32) [-24]
47	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [6/2018]	3,230.02 (4,857.00) [5,820.00]	5,224.22 (2,589.98) [0]
48	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	163.08 (-49.96) [0]
49	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (-) [398.93]	264.69 (152.86) [0]
50	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	538.17 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
51	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
52	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
53	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]

54	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
55	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/	520.01 (-) [520.01]	0.00 (0.00) [0]
56	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
57	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2018]	289.99 (-) [289.99]	0.00 (0.00) [0]
58	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
59	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
60	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
61	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2019]	217.61 (-) [360.84]	389.08 (143.23) [108]
62	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [2/2019]	160.00 (-) [167.98]	198.82 (7.98) [129]
63	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
64	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
65	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
66	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	0.00 (0.00) [0]
67	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
68	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [361.00]	410.32 (81.00) [0]
69	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
70	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
71	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [385.13]	209.80 (185.32) [0]
72	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [0]
73	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	245.83 (0.00) [0]
74	NALBARI T BIJNI (AS-7)	12/2003	4/2008	208.00	297.81

			(-) [3/2019]	(-) [230.00]	(22.00) [131]
75	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [4/2019]	225.00 (-) [225.00]	312.79 (0.00) [130]
76	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [12/2018]	245.00 (174.34) [174.34]	214.88 (-70.66) [129]
77	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
78	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	MANIPUR				
	<u>Railways</u>				
79	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	7,919.05 (9,354.83) [108]
	Urban Development				
80	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2019]	216.69 (-) [216.69]	52.00 (0.00) [56]
	MEGHALAYA				
	<u>Health And Family Welfare</u>				
81	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [8/2019]	363.99 (-) [363.99]	71.00 (0.00) [15]
	<u>Railways</u>				
82	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	259.43 (5,093.54) [0]
	Road Transport And Highways				
83	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
84	JORBAT - BARAPANI	1/2011	1/2014 (-) [1/2019]	536.00 (-) [536.00]	678.87 (0.00) [60]
85	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [3/2019]	479.20 (-) [479.20]	14.31 (0.00) [10]
86	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	Urban Development				
87	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	MIZORAM				
	<u>Railways</u>				
88	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,968.00]	2,318.33 (2,574.53) [81]
	Road Transport And Highways				
89	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
90	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]

91	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
92	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
93	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [10/2021]	2,326.52 (2,446.57) [3,000.00]	655.38 (673.48) [79]
	<u>Road Transport And Highways</u>				
94	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
95	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
96	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	0.00 (0.00) [0]
97	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	0.00 (0.00) [0]
98	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
99	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
100	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
101	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
102	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
103	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	0.00 (0.00) [0]
104	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
105	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
106	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
107	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	0.00 (0.00) [0]
108	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	0.00 (0.00) [0]
109	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
110	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM	3/2016	8/2016	396.52	0.00

	DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1		(-) [8/2019]	(-) [396.52]	(0.00) [36]
111	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
112	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
113	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
114	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
115	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
116	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
117	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
118	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	18.12 (0.00) [0]
119	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
120	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
121	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
122	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
123	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (1,942.00) [3,374.00]	3,015.98 (2,232.00) [60]
124	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
125	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (4,118.00) [1,733.20]	1,543.99 (838.20) [0]
	<u>Road Transport And Highways</u>				
126	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	246.46 (0.00) [0]
127	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				

128	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
129	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
130	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			81,727.82 (31,890.61) [1,31,973.70]	59,019.47 (50,245.88)
