

**432th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
October, 2021**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for October 2021 contains information on the status of the 1680 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, out of 1680 projects, 16 projects are added and 9 projects are completed. 539 projects are delayed with respect to their original schedules and 64 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 64 projects, 18 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)


S.No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report
1	ROAD TRANSPORT AND HIGHWAYS	887	130	3
2	RAILWAYS	287	142	5
3	PETROLEUM	151	85	5
4	COAL	107	57	1
5	POWER	62	44	1
6	WATER RESOURCES	43	8	0
7	HEALTH AND FAMILY WELFARE	29	6	0
8	URBAN DEVELOPMENT	28	14	0
9	DEPARTMENT OF HIGHER EDUCATION	23	13	0
10	CIVIL AVIATION	20	18	1
11	STEEL	8	5	1
12	MINES	6	3	1
13	HOME AFFAIRS	6	3	0
14	ATOMIC ENERGY	4	4	0
15	FERTILISERS	4	2	0
16	TELECOMMUNICATIONS	3	3	0
17	FINANCE	2	0	0
18	HEAVY INDUSTRY	2	0	0
19	DPIIT	2	1	0
20	SHIPPING AND PORTS	1	0	0
21	DEFENCE PRODUCTION	1	1	0
22	COMMERCE	1	0	0
23	RURAL DEVELOPMENT	1	0	0
24	DONER	1	0	0
25	RENEWABLE ENERGY	1	0	0
		1680	539	18

3. Total original cost of implementation of the 1680 projects was ₹21,74,182.86 crore and their anticipated completion cost is likely to be ₹26,08,330.02 crore, which reflects overall cost overruns of ₹4,34,147.16 crore (19.97% of original cost). The expenditure incurred on these projects till October 2021 is ₹12,64,545.31 crore, which is 48.48% of the anticipated cost of the projects. The information can be viewed graphically as:

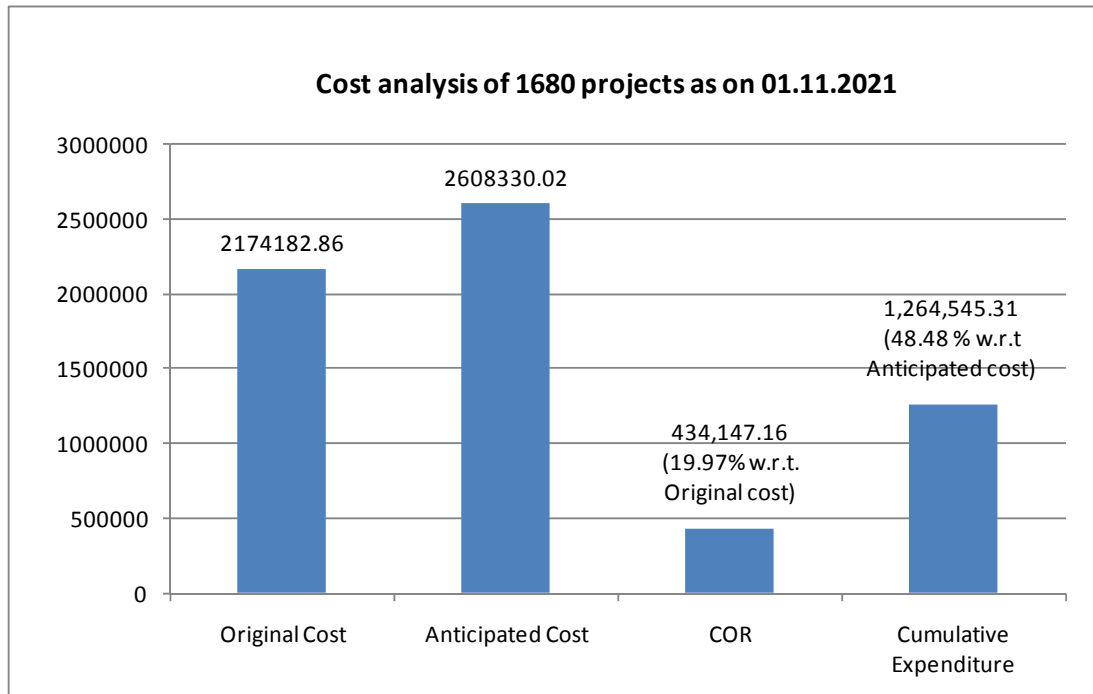


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.


5. Out of the 1680 projects, 12 projects are ahead of schedule, 292 are on schedule, 539 are delayed, 438 projects reported cost overrun and 211 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 377 if delay is calculated on the basis of latest schedule of completion. Further, for 837 projects neither the year of commissioning nor the tentative gestation period has been reported.

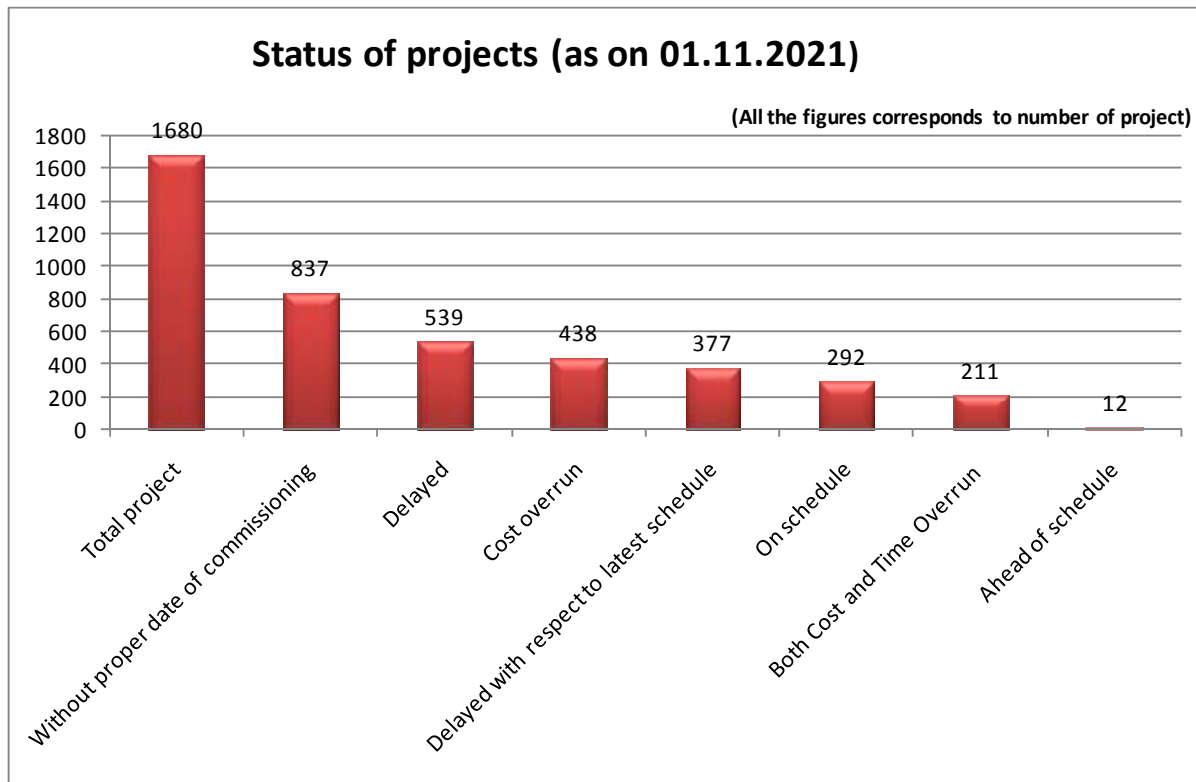

6. Out of 539 delayed projects, 98 (18.18%) projects have overall delay in the range of 1 to 12 months, 109 (20.22%) projects have delay in the range of 13 to 24 months, 211 (39.15%) projects have delay in the range of 25 to 60 months and 121 (22.45%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

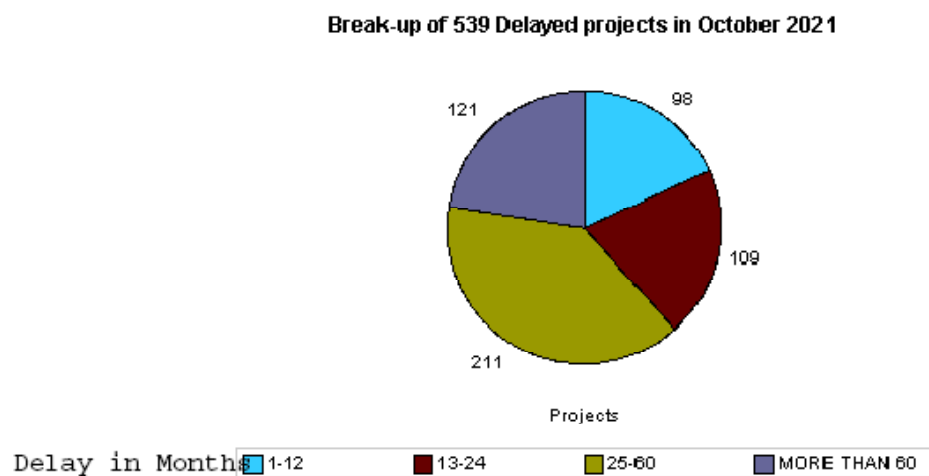

7. The status of online reporting of projects can be viewed month wise as:

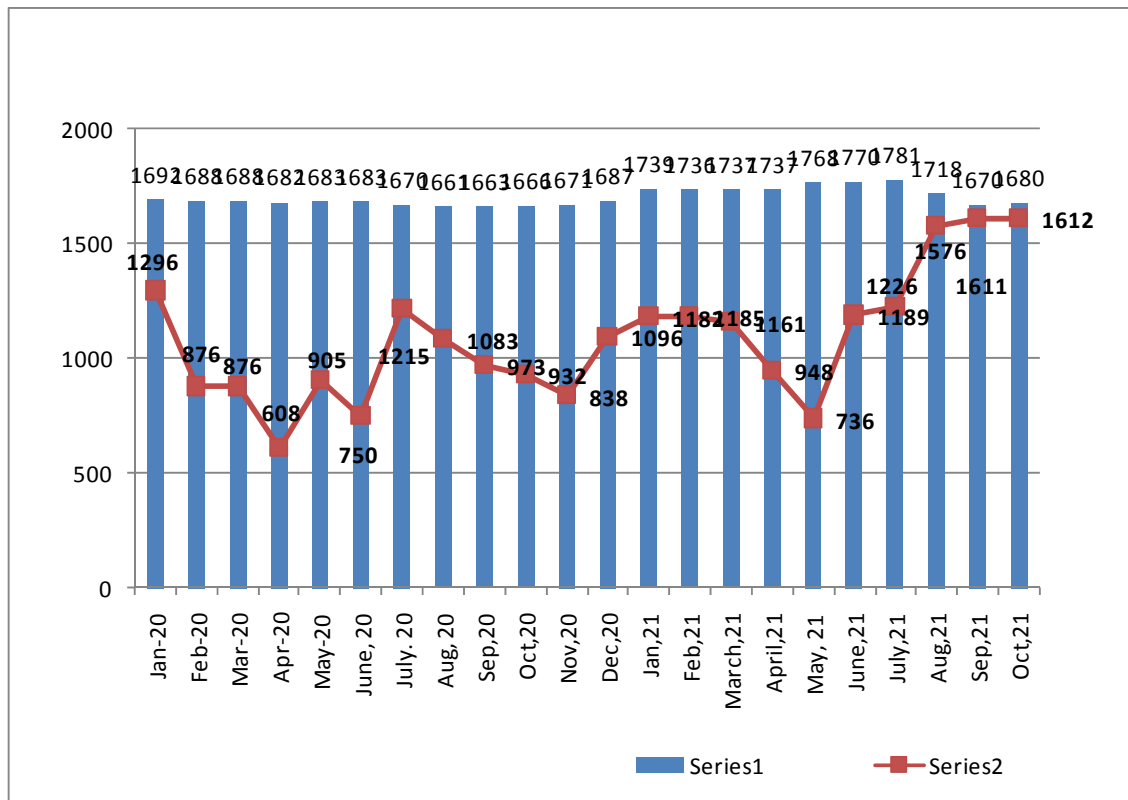

The average time overrun in these 539 delayed projects is 47.16 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. These sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

FLASH REPORT

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-11-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	69.63
5	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1383.00	1983.00	43.38
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
COAL					
8	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
9	BHANEGAON OC	02/2015	187.94	409.68	117.98
10	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
11	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
12	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	708.55	47.76
DEPARTMENT OF HIGHER EDUCATION					
13	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
16	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
DPIIT					
17	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
19	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	41.63
20	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
21	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	190.34	21.58
22	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
23	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
HEAVY INDUSTRY					
24	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3727.30	116.96
HOME AFFAIRS					
25	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
26	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
27	NSG AT KOLKATA	10/2014	162.88	238.00	46.12

28	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	4.68
PETROLEUM					
29	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.34	132.23
30	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
31	LPG TERMINAL AT KOCHI	10/2015	607.06	1236.00	103.60
32	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
33	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
POWER					
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
35	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4825.60	191.23
36	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
37	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
38	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	126.58
RAILWAYS					
39	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
40	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	04/2011	120.70	2172.16	1699.64
41	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
42	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
43	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
ROAD TRANSPORT AND HIGHWAYS					
44	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
45	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
46	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
47	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	612.58	118.78
48	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
STEEL					
49	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
50	FORGED WHEEL PLANT	04/2014	1682.85	2100.00	24.79
TELECOMMUNICATIONS					
51	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
52	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
53	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	25.89
54	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
55	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
56	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	16.25
WATER RESOURCES					
57	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
58	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	76.68
59	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	62.63
60	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	22.24
61	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	17.91

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)

(as on 01-11-2021)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1383.00	1983.00	600.00
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	290.50
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
COAL					
8	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
9	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
10	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
11	MAGADH EXPANSION OC(51 MTY)	08/2008	6964.33	7254.37	290.04
12	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	708.55	229.02
DEPARTMENT OF HIGHER EDUCATION					
13	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
16	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
DPIIT					
17	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
HEALTH AND FAMILY WELFARE					
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
20	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	172.39
21	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
22	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
23	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
HEAVY INDUSTRY					
24	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3727.30	2009.30
HOME AFFAIRS					
25	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
26	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74
27	NSG AT KOLKATA	10/2014	162.88	238.00	75.12
28	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	12.98
PETROLEUM					
29	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	01/2019	12366.00	18968.00	6602.00
30	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00

31	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
32	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
33	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
POWER					
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
35	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
36	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
37	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
38	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9129.32	4374.90
RAILWAYS					
39	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
40	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
41	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
42	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
43	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12264.15	7809.98
ROAD TRANSPORT AND HIGHWAYS					
44	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
45	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
46	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
47	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	03/2018	1532.62	2499.00	966.38
48	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	1083.00	1827.15	744.15
STEEL					
49	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
50	FORGED WHEEL PLANT	04/2014	1682.85	2100.00	417.15
TELECOMMUNICATIONS					
51	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
52	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
53	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	4289.98
54	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	3780.00
55	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
56	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
WATER RESOURCES					
57	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
58	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	173.13
59	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	159.16
60	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	50.14
61	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	47.50

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)

(as on 01-11-2021)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	02/2022	74
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2022	45
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	11/2021	29
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	05/2022	27
8	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	09/2021	12/2023	27
9	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	06/2022	26
COAL					
10	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	03/2010	03/2029	228
11	MAGADH EXPANSION OC(51 MTY)	08/2008	07/2012	03/2028	188
12	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	03/2013	03/2028	180
13	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	03/2017	03/2031	168
14	KARTALI (EAST) OCP (2.50 MTY)	07/2008	03/2014	03/2026	144
DEFENCE PRODUCTION					
15	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	02/2020	12/2021	22
DEPARTMENT OF HIGHER EDUCATION					
16	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	11/2021	84
17	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	03/2022	57
18	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	09/2020	11/2022	26
19	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	01/2018	05/2020	06/2022	25
20	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	07/2019	03/2021	02/2023	23
DPIIT					
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	05/2022	29
FERTILISERS					
22	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	10/2021	23
23	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	10/2021	18
HEALTH AND FAMILY WELFARE					
24	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	03/2022	46
25	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	10/2021	31
26	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	09/2017	03/2020	12/2021	21
27	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	03/2018	09/2020	04/2022	19
28	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	06/2021	05/2022	11
HOME AFFAIRS					
29	NSG AT KOLKATA	10/2014	04/2018	12/2021	44
30	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	03/2022	29

31	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	07/2022	10/2022	3
	MINES				
32	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	12/2023	37
33	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	01/2024	33
34	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	04/2021	12/2023	32
	PETROLEUM				
35	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	05/2022	108
37	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
38	LPG TERMINAL AT KOCHI	10/2015	10/2017	09/2022	59
39	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	04/2018	05/2022	49
	POWER				
40	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2023	162
41	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
42	BARH STPP(3X660MW) NTPC	02/2005	10/2011	07/2023	141
43	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	09/2024	138
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2024	138
	RAILWAYS				
45	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
46	MUNEERABAD-MAHABOONNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
47	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
48	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
49	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
	ROAD TRANSPORT AND HIGHWAYS				
50	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	12/2021	134
51	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	06/2023	118
52	PUNE-SATARA(NH-4)	10/2010	03/2013	03/2022	108
53	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	05/2010	05/2013	02/2022	105
54	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
	STEEL				
55	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	01/2022	80
56	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	11/2022	61
57	COKE OVEN BATTERY-5	12/2011	12/2017	07/2022	55
58	FORGED WHEEL PLANT	04/2014	09/2018	11/2021	38
59	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	12/2021	30
	TELECOMMUNICATIONS				
60	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2022	80
61	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	03/2018	12/2021	45
62	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	11/2021	5
	URBAN DEVELOPMENT				
63	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2019	03/2025	73
64	NAGPUR METRO RAIL	08/2014	03/2018	12/2021	45
65	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
66	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	03/2020	03/2023	36
67	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	06/2015	04/2019	02/2022	34
	WATER RESOURCES				
68	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	04/2022	25
69	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	12/2021	24

70	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	05/2016	12/2021	12/2022	12
71	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	03/2019	07/2021	06/2022	11
72	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	05/2016	02/2022	12/2022	10

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-11-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	303.80	303.80	189.25	04/2020	06/2022
2	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	02/2019	645.63	645.63	0.00	08/2022	11/2022
COAL							
3	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	93.05	09/2020	N.A.
4	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
5	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	143.95	09/2020	N.A.
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
7	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	24.86	04/2018	10/2022
COMMERCE							
8	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	30.00	10/2020	N.A.
DEPARTMENT OF HIGHER EDUCATION							
9	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	N.A.
10	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	110.13	03/2020	12/2021
11	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	213.47	04/2023	04/2023
12	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	09/2018	392.51	392.51	57.47	06/2022	06/2022
13	PERMANENT CAMPUS FOR IIM	09/2018	375.00	375.00	110.13	09/2020	11/2022

	BODH GAYA						
	DPIIT						
14	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9574.07	09/2019	07/2021
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	3013.69	12/2019	05/2022
	HEALTH AND FAMILY WELFARE						
16	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
17	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	573.94	11/2013	09/2021
18	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	538.20	06/2020	N.A.
19	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	591.61	04/2020	N.A.
20	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
	HEAVY INDUSTRY						
21	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	900.00	815.00	09/2019	N.A.
	HOME AFFAIRS						
22	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
23	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI	05/2019	199.31	199.31	20.53	01/2022	01/2020
24	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	27.25	07/2022	10/2022
25	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	166.98	166.98	0.00	10/2023	10/2023
	MINES						
26	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	04/2019	255.37	255.37	0.86	04/2022	04/2022
	PETROLEUM						
27	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	19.44	02/2017	08/2022
28	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
29	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	769.00	06/2019	02/2022
30	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	05/2016	261.00	261.00 ¹³	183.60	01/2021	09/2021

31	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	212.00	212.00	172.42	01/2021	09/2021
POWER							
32	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	156.99	06/2006	N.A.
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	14458.38	09/2010	08/2023
34	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3824.26	10/2017	N.A.
35	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	252.99	04/2016	12/2021
36	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	2083.10	04/2020	07/2025
RAILWAYS							
37	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
38	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2017.96	878.49	07/2012	11/2024
39	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.06	03/2019	N.A.
40	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.31	03/2006	03/2025
41	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	560.09	07/2014	N.A.
RENEWABLE ENERGY							
42	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.90	271.90	90.99	11/2019	N.A.
ROAD TRANSPORT AND HIGHWAYS							
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	319.07	N.A.	N.A.
44	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	675.00	675.00	379.73	N.A.	N.A.
45	GWALIOR-JHANSI, NH-75	12/2003	604.00	364.59	360.15	12/2009	09/2020
46	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	612.58	612.58	02/2009	N.A.
47	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	655.17	07/2009	N.A.
STEEL							
48	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	70.05	12/2023	12/2023
TELECOMMUNICATIONS							

49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	20545.00	07/2015	03/2022
50	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	422.87	46.37	06/2021	11/2021
URBAN DEVELOPMENT							
51	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6059.17	07/2017	09/2020
52	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	19493.96	03/2020	03/2023
53	NAGPUR METRO RAIL	08/2014	8680.00	8680.00	8427.24	03/2018	12/2021
54	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	6928.00	6928.00	6928.00	03/2019	03/2019
55	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	1128.00	1128.00	30.00	03/2022	06/2023
WATER RESOURCES							
56	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	260.12	12/2019	01/2021
57	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	220.08	12/2019	N.A.
58	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	291.32	03/2020	03/2021
59	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	248.86	04/2020	03/2021
60	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	326.75	01/2021	N.A.

N.A.: Not Available.

Table-E

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-11-2021)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	17298.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	13709.00
COAL					
3	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	0.00	729.73
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	293.69
HEALTH AND FAMILY WELFARE					
5	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	573.94
6	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	249.24
7	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	158.90	0.00	169.51

	PETROLEUM				
10	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	423.00	0.00	444.35
11	PIPELINE REPLACEMENT PROJECT (PRP-VI)	05/2019	763.92	0.00	791.49
	POWER				
12	NAITWAR MORI HEP	10/2017	648.33	0.00	704.97
	RAILWAYS				
13	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	560.09
14	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	803.11	1218.49
15	TIRUCHIRAPPALI-NAGORE-KARAIKAL(SR)(GC)	09/1995	303.98	0.00	705.52
16	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	920.91
17	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	495.44	0.00	1866.85
	ROAD TRANSPORT AND HIGHWAYS				
18	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
19	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
20	TRICHY - KARUR	03/2007	516.00	0.00	886.96
21	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	1673.70	0.00	3326.93
22	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2848.49
	STEEL				
23	FORGED WHEEL PLANT	04/2014	1682.85	0.00	1736.92
	URBAN DEVELOPMENT				
24	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39486.58
	WATER RESOURCES				
25	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	291.32
26	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	326.75

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-11-2021)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	COAL				
1	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	N.A.	03/2021
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
3	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
4	RFR OF MANUGURU OC PROJECT	11/2012	03/2016	N.A.	09/2021
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
	COMMERCE				
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT	06/2018	10/2020	N.A. ¹⁶	N.A.

	MAIDAN GARHI, NEW DELHI				
DEPARTMENT OF HIGHER EDUCATION					
7	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
8	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	N.A.	N.A.
9	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	N.A.	N.A.
10	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	07/2019	N.A.	N.A.
11	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	02/2019	06/2020	N.A.	N.A.
DONER					
12	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	N.A.	08/2021
DPIIT					
13	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	01/2014	07/2021
FERTILISERS					
14	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	05/2021	N.A.
15	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	05/2021	N.A.
FINANCE					
16	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	N.A.	07/2021
HEALTH AND FAMILY WELFARE					
17	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
18	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	09/2021
19	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	03/2021
20	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
21	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
HEAVY INDUSTRY					
22	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	17 03/2021	03/2021

23	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	N.A.	N.A.
HOME AFFAIRS					
24	CONSTRUCTION OF ITBP ROAD TO INDO- CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
MINES					
25	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
PETROLEUM					
26	ENNORE-TRICHY- MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
27	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	03/2019	09/2021	09/2021
28	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR- SOLAPUR PIPELI	05/2016	01/2021	N.A.	09/2021
29	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR- SOLAPUR PIPELINE	05/2016	01/2021	N.A.	09/2021
30	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	08/2019	06/2021	05/2021
POWER					
31	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
32	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
33	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
34	TALAIPELLI COAL MINING PROJECT	09/2015	11/2019	N.A.	N.A.
35	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	03/2016	01/2018	07/2021	06/2021
RAILWAYS					
36	HOWRAH-AMTA- CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
37	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL).NEFR	04/1983	03/2019	N.A.	N.A.
38	MUZAFFARPUR- SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
39	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	09/2021
40	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	04/1996	03/2012	18 09/2021	09/2021

RENEWABLE ENERGY					
41	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	N.A.	N.A.	N.A.
44	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	N.A.	N.A.	N.A.
45	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	N.A.	N.A.
46	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	N.A.	N.A.
RURAL DEVELOPMENT					
47	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	07/2021	N.A.	N.A.
48	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	02/2019	02/2019
49	DELHI MRTS PHASE-III	09/2011	03/2016	08/2021	N.A.
50	KOCHI METRO RAIL PROJECT	07/2012	07/2017	09/2020	09/2020
51	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	03/2019	N.A.	03/2019
WATER RESOURCES					
52	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	N.A.	N.A.
53	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	N.A.	01/2021
54	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	05/2021	N.A.
55	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	03/2020	N.A.	03/2021
56	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	04/2020	N.A.	03/2021

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	887	15
2	RAILWAYS	287	10
3	PETROLEUM	151	24
4	COAL	107	2
5	POWER	62	4
6	WATER RESOURCES	43	0
7	HEALTH AND FAMILY WELFARE	29	1
8	URBAN DEVELOPMENT	28	0
9	DEPARTMENT OF HIGHER EDUCATION	23	0
10	CIVIL AVIATION	20	3
11	STEEL	8	2
12	MINES	6	3
13	HOME AFFAIRS	6	0
14	ATOMIC ENERGY	4	0
15	FERTILISERS	4	0
16	TELECOMMUNICATIONS	3	0
17	FINANCE	2	0
18	HEAVY INDUSTRY	2	0
19	DPIIT	2	0
20	SHIPPING AND PORTS	1	0
21	DEFENCE PRODUCTION	1	0
22	COMMERCE	1	0
23	RURAL DEVELOPMENT	1	0
24	DONER	1	0
25	RENEWABLE ENERGY	1	0
	Total	1680	64

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2021			
	<u>PETROLEUM</u>			
1	MMPL PIPELINE REROUTING PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000261]	449.58	12/2019	396.13
2	PUNE POL STORAGE DEPOT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000313]	282.64	08/2020	194.26
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000664]	639.79	03/2020	597.77
4	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000930]	378.24	01/2018	315.42
5	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001183]	251.55	02/2015	7.74
	June,2021			
	<u>PETROLEUM</u>			
6	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
7	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	<u>WATER RESOURCES</u>			
8	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI (Uttarakhand Pey Jal Nigam) - [N30000003]	273.37	08/2019	84.55
9	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR (Bihar Urban Infrastructure Development Corporation Ltd) - [N300000038]	184.93	04/2020	163.36
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000287]	485.44	12/2015	447.13

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000617]	198.00	10/2016	184.62
12	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001220]	491.52	09/2016	474.76
	August,2021			
	<u>PETROLEUM</u>			
13	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN (OIL INDIA LIMITED) - [N16000167]	352.56	03/2017	455.00
14	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
15	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000312]	255.00	11/2020	275.68
	<u>POWER</u>			
16	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
17	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
18	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
19	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
20	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
21	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
22	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
23	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000273]	587.44	09/2020	463.48
24	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000274]	349.00	11/2020	313.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
25	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000251]	297.00	04/2018	290.64
26	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000276]	156.26	-	141.35

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
27	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000294]	269.22	01/2015	33.24
28	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000295]	257.09	01/2015	14.18
29	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000297]	376.52	04/2014	171.16
30	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000298]	383.40	03/2015	244.68
31	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000311]	207.03	05/2012	308.09
32	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000317]	157.18	07/2015	148.24
33	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000318]	154.14	08/2015	142.06
34	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000333]	621.43	06/2018	387.22
35	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000371]	445.89	03/2017	464.05
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000376]	219.40	01/2018	0.10
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000379]	218.63	10/2017	29.27
38	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000385]	766.36	-	685.36
39	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000388]	497.05	05/2017	754.27
40	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000389]	847.02	-	795.00
41	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000397]	322.00	03/2018	56.41

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000402]	358.22	10/2016	339.86
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000414]	229.41	05/2018	6.65
44	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000417]	342.05	01/2017	258.91
45	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000467]	511.00	10/2013	2,323.04
46	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000470]	511.00	10/2013	492.00
47	FOUR LANING OF CHANDIGARH - KHARAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000503]	447.29	12/2017	346.39
48	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000523]	159.39	11/2017	210.29
49	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000524]	892.17	-	648.44
50	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000537]	278.39	08/2014	22.18
51	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
52	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000580]	206.80	07/2016	74.04
53	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000581]	288.24	11/2015	287.37
54	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000608]	248.97	05/2019	270.65
55	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000625]	1,004.67	05/2019	577.21
56	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000640]	326.63	04/2018	249.26
57	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000641]	239.91	10/2017	147.25
58	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000644]	342.05	01/2017	258.91

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
59	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000646]	157.30	06/2018	97.29
60	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000727]	960.24	-	738.74
61	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000871]	600.87	11/2017	682.36
62	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000873]	823.20	11/2017	807.99
63	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000878]	235.91	02/2018	176.23
64	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000879]	202.69	11/2019	148.21
65	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000884]	191.21	11/2019	127.13
66	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000895]	287.34	01/2019	194.85
67	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000905]	322.48	07/2020	291.93
68	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000906]	173.24	06/2020	56.66
69	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000908]	276.01	03/2019	187.39
70	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000911]	165.06	12/2016	92.59
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000936]	244.95	08/2018	136.22
72	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 ((MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000938]	297.12	07/2018	373.98
73	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000942]	208.50	11/2019	165.82
74	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000962]	178.23	09/2018	122.99
75	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000999]	230.34	10/2019	201.82

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
76	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001001]	199.98	08/2016	163.16
77	MAJALGAON TO KAIJ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001036]	413.99	07/2019	299.72
78	AKKALKOT TO DHUDHNI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001120]	211.42	02/2019	131.85
79	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001131]	212.99	06/2020	156.72
80	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001139]	218.94	03/2020	120.69
81	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001143]	176.94	10/2018	141.11
82	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001147]	239.63	02/2019	212.53
83	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001148]	599.34	01/2020	492.15
84	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001153]	197.37	02/2014	89.36
85	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001155]	175.20	01/2017	142.48
86	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001184]	269.69	09/2019	0.01
87	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001202]	388.83	12/2019	304.70
88	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001205]	209.10	10/2019	201.70
89	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001223]	179.89	03/2013	242.23
90	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001225]	169.26	01/2019	270.11
91	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001237]	162.72	09/2016	136.59
92	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001238]	307.70	01/2017	313.06
	URBAN DEVELOPMENT			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
93	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000079]	884.30	12/2015	874.29
94	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000123]	218.72	11/2020	175.63
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
95	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000102]	294.00	04/2019	289.13
	September,2021			
	<u>STEEL</u>			
96	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000121]	263.36	09/2020	253.46
	<u>POWER</u>			
97	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000061]	4,824.12	10/2012	4,612.66
98	SYSTEM STRENGTHENING XIII OF SR GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000109]	487.49	06/2014	590.30
99	EASTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000155]	1,364.52	04/2016	1,290.03
100	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000168]	5,151.37	03/2018	3,269.93
101	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000181]	871.62	10/2017	628.13
102	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000182]	203.28	07/2017	200.16
103	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000218]	3,519.59	05/2019	2,562.41
104	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000238]	283.72	11/2019	196.10
105	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000239]	408.46	01/2019	369.27
106	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000240]	608.24	04/2019	425.04
107	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000257]	3,654.00	04/2019	3,508.04

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
108	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000261]	175.64	09/2018	115.43
109	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000263]	445.89	02/2019	372.58
110	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000267]	198.49	09/2019	132.15
111	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000269]	193.14	06/2019	108.80
	<u>RAILWAYS</u>			
112	GONDIA-JABALPUR(GC),(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100186]	511.86	04/2020	1,867.16
113	NANDYAL-YERRAGUNTLA(NL),SCR (SOUTH CENTRAL RAILWAY) - [220100192]	164.36	02/2009	1,148.67
114	HARIDASPUR-PARADEEP(NL) (RAIL VIKAS NIGAM LTD.) - [220100285]	1,185.64	12/2017	2,129.37
115	ETAWAH-MAINPURI (NL),NCR (NORTH CENTRAL RAILWAY) - [220100318]	120.00	12/2008	345.51
116	CHHINDWARA - NAGPUR (GC)(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100324]	383.79	-	1,448.56
117	BARDHAMAN-KATWA (GC) (EASTERN RAILWAYS) - [N22000091]	1,106.62	12/2010	1,003.78
118	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) (WESTERN RAILWAY) - [N22000125]	117.36	03/2011	809.40
119	BANGURGRAM-GURIYA PATCH DOUBLING (NORTH WESTERN RAILWAY) - [N22000137]	246.08	12/2019	366.92
120	THIYAT HAMIRA-SANU (NORTH WESTERN RAILWAY) - [N22000149]	236.93	10/2018	287.42
121	AJMER-BANGURGRAM (NORTH WESTERN RAILWAY) - [N22000155]	213.39	11/2019	361.83
122	ALWAR-BANDIKUI DOUBLING (NORTH WESTERN RAILWAY) - [N22000157]	242.09	02/2019	476.34
123	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000165]	258.20	12/2018	318.44
124	HAJIPUR-RAMDAYALUNAGAR DOUBLING (EAST CENTRAL RAILWAYS) - [N22000182]	213.01	-	498.44
125	CUDDALORE-SALEM VIA VRIDDHACHALAM GC (SOUTHERN RAILWAY) - [N22000187]	198.68	-	273.57
126	AMBARI FALAKATA TO NEW MAYNAGURI (NORTH EAST FRONTIER RAILWAY) - [N22000210]	314.00	03/2019	831.65
127	PIRPAINTI-BHAGALPUR (EASTERN RAILWAYS) - [N22000222]	261.38	-	553.59
128	HANSDIHA-GODDA NL (EASTERN RAILWAYS) - [N22000236]	542.18	03/2020	545.97
129	HARIDWAR-LAKSAR (NORTHERN RAILWAY) - [N22000289]	219.83	-	204.53
130	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND (SOUTH EASTERN RAILWAY) - [N22000323]	148.77	12/2016	206.49

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
131	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM (SOUTHERN RAILWAY) - [N22000373]	187.26	04/2014	276.82
132	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO (WESTERN RAILWAY) - [N22000433]	243.60	-	423.00
133	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000444]	257.00	03/2018	153.84
134	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION (NORTH EASTERN RAILWAY) - [N22000461]	622.50	04/2017	521.88
135	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR (EAST CENTRAL RAILWAYS) - [N22000475]	180.82	-	546.29
136	CHAMPA-JHARSUGUDA 3RD LINE (SOUTH EAST CENTRAL RAILWAY) - [N22000483]	872.00	12/2019	1,156.06
137	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION (WESTERN RAILWAY) - [N22000487]	551.51	03/2019	773.12
138	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM (WESTERN RAILWAY) - [N22000494]	691.84	03/2020	812.08
	ROAD TRANSPORT AND HIGHWAYS			
139	SONAPUR TO GUWAHTI (AS-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000044]	245.00	03/2008	240.36
140	NALBARI TO BIJNI (AS-6) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000047]	225.00	06/2008	390.72
141	NALBARI T BIJNI (AS-7) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000048]	208.00	04/2008	370.56
142	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000049]	160.00	05/2008	270.97
143	BRAHMPUTRA BRIDGE,NH NO-31 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000063]	217.61	04/2010	489.84
144	VADODARA-SURAT SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000361]	503.16	08/2016	389.50
145	FOUR LANING OF AURANGABAD - YEDISHI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000508]	1,871.34	01/2018	3,443.43
146	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000518]	399.54	04/2019	259.67
147	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000541]	1,081.57	06/2019	480.25
148	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000542]	197.69	07/2018	151.11
149	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000545]	1,134.97	11/2018	809.71
150	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000621]	1,239.82	-	1,691.00
151	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000837]	307.79	-	197.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
152	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000850]	551.58	-	305.46
153	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000978]	172.75	-	134.38
154	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001174]	235.31	11/2020	195.72
155	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001257]	159.85	10/2022	2.80
	<u>URBAN DEVELOPMENT</u>			
156	REDEVELOPMENT OF EAST KIDWAI NAGAR (NATIONAL BUILDING CONSTRUCTION CORPORATION LTD) - [N28000080]	4,264.00	11/2019	4,683.08
	<u>WATER RESOURCES</u>			
157	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS (Uttar Pradesh Jal Nigam) - [N30000007]	904.00	09/2021	148.55
158	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR (Uttar Pradesh Jal Nigam) - [N30000009]	370.40	08/2020	396.14
159	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA (Uttar Pradesh Jal Nigam) - [N30000011]	161.31	11/2019	91.38
160	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA (Bihar Urban Infrastructure Development Corporation Ltd) - [N30000041]	184.86	05/2021	168.85
	October,2021			
	<u>CIVIL AVIATION</u>			
161	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNAI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000040]	535.00	06/2010	331.8
	<u>COAL</u>			
162	SINGHORI OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000130]	205.49	03/2020	138.58
163	AMALGAMATED PAUNI-II III OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000131]	483.69	03/2021	253.70
164	AMALGAMATED GONDEGAON GHATROHAN OC (WESTERN COAL FIELDS LIMITED) - [N06000149]	198.68	03/2019	272.90
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
165	GAIL GAS LTD BENGALURU CGD PROJECT Central Sector Projects(GAS AUTHORITY OF INDIA LIMITED) - [N16000210]	749.00	02/2020	1,043.56
166	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000227]	4,588.29	08/2018	5,376.50
167	BS-VI PROJECTS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000295]	1,858.00	12/2019	1,528.75
	<u>RAILWAYS</u>			
168	GHAZIPUR - AUNRIHAR (40 KM) (NORTH EASTERN RAILWAY) - [N22000321]	182.92	-	0.01
	<u>URBAN DEVELOPMENT</u>			
169	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000143]	532.00	11/2020	541.00

FLASH REPORT

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000321]	829.00	01/2019	350.14
2	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000430]	223.30	06/2018	111.16
3	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000618]	434.06	-	306.05
4	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000676]	138.93	01/2017	124.76
5	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
6	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000681]	194.66	04/2017	117.61
7	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000689]	507.68	04/2017	129.13
8	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000766]	318.42	11/2017	66.63
	August,2021			
9	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
10	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000274]	333.21	12/2015	256.11
11	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000296]	278.87	05/2014	0.00
12	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000302]	333.21	12/2015	256.11

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000307]	156.63	02/2012	0.00
14	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000309]	305.49	03/2011	131.08
15	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
16	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000335]	159.12	11/2015	0.00
17	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000373]	305.49	03/2017	0.00
18	SATANA-BELA SECTION OF NH-75(4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000375]	320.48	08/2015	189.49
19	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000395]	257.80	-	12.38
20	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000396]	470.20	02/2011	569.40
21	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000398]	282.41	08/2016	327.21
22	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
23	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000407]	333.21	11/2015	256.11
24	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
25	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
26	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000519]	478.35	-	516.69
27	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000530]	154.62	-	0.00
28	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000575]	665.50	07/2016	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
29	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000577]	369.77	06/2016	0.00
30	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000927]	293.64	08/2020	28.24
31	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001144]	445.89	03/2017	469.64
32	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001145]	164.54	08/2015	141.33
33	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001154]	367.44	01/2017	61.95
34	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001167]	165.67	01/2016	87.63
35	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001170]	471.16	08/2014	201.64
36	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001230]	281.45	12/2020	112.70
	September, 2021			
	<u>RAILWAYS</u>			
37	DANIAWAN-BIHARSARIF (NL), ECR (EAST CENTRAL RAILWAYS) - [220100311]	406.92	-	200.00
38	GOOTY-DHARMAVARAM-BANGLORE (RAIL INDIA TECHNICAL AND ECONOMIC SERVICE) - [N22000370]	636.38	-	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
39	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000253]	187.79	07/2016	82.95
40	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000275]	289.60	-	160.70
41	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000439]	1,885.74	05/2019	1,636.02
42	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000650]	244.90	05/2019	251.87

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	<u>RURAL DEVELOPMENT</u>			
43	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V (HSCL FOR RURAL) - [N12000098]	149.73	12/2015	144.95
44	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI (HSCL FOR RURAL) - [N12000099]	202.61	12/2016	190.22
45	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII (HSCL FOR RURAL) - [N12000100]	175.49	12/2016	124.87
	October,2021			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
46	STUDY IN INDIA (EDCIL(India) Limited) - [N42000003]	150.00	04/2018	0.00
47	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION (Indian Institute of Technology, Kharagpur) - [N42000004]	418.00	03/2019	110.00
48	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES(CPWD OF HIGHER EDUCATION) - [N44000001]	127.26	10/2023	12.73
	<u>HOME AFFAIRS</u>			
49	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 (CPWD FOR MHA) - [N45000001]	166.98	05/2022	0.29

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1670
No of Projects Completed/Dropped/Frozen in Current Month	19
No of Projects Elevated in Current Month	13
No of Projects added in Current Month	16
No of Projects in Current Month	1680

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	539 (32.08%)	12 (.71%)	292 (17.38%)	108 (6.43%)	729 (43.39%)	1680
Latest Approved (Date)	377 (22.44%)	17 (1.01%)	475 (28.27%)	77 (4.58%)	734 (43.69%)	1680

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1353	16,49,802.44	17,88,688.96	7,88,223.73	44.10	1,38,886.52	8.40
Project with Revision in Cost	327	8,05,359.46	8,19,641.06	4,76,321.58	58.10	14,281.60	1.80
Total	1,680	24,55,161.90	26,08,330.02	12,64,545.31	48.48	1,53,168.12	6.24
Original Cost of All Projects							
Original Cost	1,680	21,74,182.86	26,08,330.02	12,64,545.31	48.48	4,34,147.16	19.97

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	539	9,06,492.37	12,02,897.68	6,95,028.04	57.80	2,96,405.31	32.70
Latest Approved (RCE)	377	6,40,109.10	7,26,164.52	4,09,243.07	56.40	86,055.42	13.44

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	64	54,305.49	71,955.60	49,832.72	69.30	17,650.11	32.50
Total	64	54,305.49	71,955.60	49,832.72	69.25	17,650.11	32.50

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	20	14,431.97	15,510.25	7.47	4	3,288.50	4,403.06	33.89
3	COAL	107	1,49,691.71	1,54,295.46	3.08	20	38,151.12	44,429.38	16.46
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	6	7,333.99	7,330.54	-0.05	0	0.00	0.00	0.00
7	STEEL	8	25,189.15	32,021.30	27.12	2	17,207.85	24,040.00	39.70
8	PETROLEUM	151	3,41,221.64	3,52,793.57	3.39	29	66,399.38	90,818.23	36.78
9	POWER	62	2,07,257.24	2,68,103.37	29.36	22	1,03,919.23	1,66,878.72	60.59
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	1	1,718.00	3,727.30	116.96
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	12	5,589.39	6,374.57	14.05
12	RAILWAYS	287	4,54,260.58	6,93,056.85	52.57	202	2,37,744.15	4,83,777.42	103.49
13	ROAD TRANSPORT AND HIGHWAYS	887	5,35,763.35	5,50,414.28	2.73	117	86,912.44	1,07,895.52	24.14
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	28	2,76,487.00	2,98,377.53	7.92	7	93,659.03	1,15,628.76	23.46
17	WATER RESOURCES	43	24,702.19	70,243.27	184.36	8	12,236.47	58,101.66	374.82
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	23	10,311.33	10,416.24	1.02	4	1,715.81	1,889.72	10.14
21	HOME AFFAIRS	6	2,139.99	3,160.62	47.69	4	1,773.70	2,794.33	57.54

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	RURAL DEVELOPMENT	1	361.60	361.60	0.00	0	0.00	0.00	0.00
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0.00
Total		1680	21,74,182.86	26,08,330.02	19.97	438	7,28,272.16	11,94,911.97	64.07

^ - Cost Overrun = Anticipated Cost minus Original Cost

FLASH REPORT

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	72	1,22,941.96	1,69,556.60	37.92	14	46,781.75	1,02,318.39	118.71
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	5	8,861.14	22,797.48	157.27
3	ASSAM	49	49,143.47	58,539.90	19.12	14	19,479.81	30,200.19	55.03
4	BIHAR	98	1,23,227.91	1,59,156.00	29.16	34	54,885.85	92,399.07	68.35
5	GOA	10	5,332.77	5,343.26	0.20	2	529.17	539.66	1.98
6	GUJARAT	59	1,07,424.00	1,18,232.87	10.06	18	34,751.43	46,539.39	33.92
7	HARYANA	36	61,492.56	63,819.18	3.78	7	3,823.83	6,282.82	64.31
8	HIMACHAL PRADESH	19	21,918.19	31,775.79	44.97	3	8,237.58	18,122.01	119.99
9	JAMMU AND KASHMIR	30	48,180.49	74,107.74	53.81	3	6,236.00	32,296.00	417.90
10	KARNATAKA	55	70,566.39	82,854.38	17.41	20	46,634.93	59,256.65	27.06
11	KERALA	22	30,240.60	35,331.06	16.83	11	13,558.92	18,649.40	37.54
12	MADHYA PRADESH	77	68,456.96	77,078.88	12.59	17	16,204.94	25,822.52	59.35
13	MAHARASHTRA	232	2,07,667.20	2,30,622.84	11.05	39	64,167.67	92,399.80	44.00
14	MANIPUR	26	12,108.58	20,557.35	69.78	2	5,032.79	13,575.20	169.74
15	MEGHALAYA	13	5,269.68	8,588.18	62.97	2	1,390.78	4,709.28	238.61
16	MIZORAM	24	11,957.35	15,906.05	33.02	5	3,593.57	7,542.27	109.88
17	NAGALAND	35	15,989.03	20,357.79	27.32	3	3,035.84	7,404.60	143.91
18	ODISHA	79	1,14,487.57	1,22,542.27	7.04	18	16,773.01	24,827.71	48.02
19	PUNJAB	28	18,344.99	20,091.84	9.52	6	4,559.90	6,549.20	43.63
20	RAJASTHAN	55	51,403.28	58,056.27	12.94	7	16,567.47	23,268.78	40.45
21	SIKKIM	18	7,278.84	14,598.73	100.56	2	1,727.48	9,047.37	423.73
22	TAMIL NADU	67	1,20,992.20	1,40,426.27	16.06	21	39,380.30	60,463.05	53.54
23	TRIPURA	19	5,084.45	5,259.05	3.43	2	767.30	978.18	27.48
24	UTTAR PRADESH	114	1,51,266.95	1,55,023.25	2.48	31	39,713.76	47,349.82	19.23
25	WEST BENGAL	71	62,791.47	80,666.39	28.47	30	29,474.39	47,676.14	61.75
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	44.38
27	DELHI	31	84,554.41	85,648.40	1.29	10	7,987.98	9,815.17	22.87
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	46	78,726.75	89,025.67	13.08	11	27,508.38	37,926.65	37.87
30	JHARKHAND	38	68,190.29	71,740.96	5.21	11	29,531.56	35,412.49	19.91
31	UTTARAKHAND	31	35,703.09	50,557.17	41.60	10	26,841.67	41,696.26	55.34
32	TELANGANA	52	38,726.46	41,766.05	7.85	11	17,090.29	20,624.10	20.68
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	38.72
34	MULTI STATE	113	3,45,091.51	4,57,134.61	32.47	66	1,32,141.37	2,46,996.26	86.92
Total		1680	21,74,182.86	26,08,330.02	19.97	438	7,28,272.16	11,94,911.97	64.07

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	20	14,431.97	15,510.25	7.47	18	13,466.56	14,544.84	3 - 45
3	COAL	107	1,49,691.71	1,54,295.46	3.08	57	76,766.38	79,761.61	12 - 228
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	4	1,101.28	1,101.28	0.00	2	642.64	642.64	18 - 23
6	MINES	6	7,333.99	7,330.54	-0.05	3	6,378.00	6,378.00	32 - 37
7	STEEL	8	25,189.15	32,021.30	27.12	5	21,362.73	28,194.88	30 - 80
8	PETROLEUM	151	3,41,221.64	3,52,793.57	3.39	85	1,46,121.16	1,52,701.43	1 - 110
9	POWER	62	2,07,257.24	2,68,103.37	29.36	44	1,70,020.67	2,29,586.27	1 - 162
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	6	2,675.43	2,795.43	9 - 46
12	RAILWAYS	287	4,54,260.58	6,93,056.85	52.57	142	1,92,054.49	3,22,695.21	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	887	5,35,763.35	5,50,414.28	2.73	130	67,133.82	68,156.72	5 - 134
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	3	14,013.36	25,335.07	5 - 80
16	URBAN DEVELOPMENT	28	2,76,487.00	2,98,377.53	7.92	14	1,03,728.10	1,20,242.55	12 - 73
17	WATER RESOURCES	43	24,702.19	70,243.27	184.36	8	11,797.25	57,131.86	4 - 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	1	246.31	210.00	22 - 22
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	23	10,311.33	10,416.24	1.02	13	6,533.03	6,466.84	3 - 84
21	HOME AFFAIRS	6	2,139.99	3,160.62	47.69	3	1,659.44	2,528.33	3 - 44
22	RURAL DEVELOPMENT	1	361.60	361.60	0.00	0	0.00	0.00	-
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	-
Total		1680	21,74,182.86	26,08,330.02	19.97	539	9,06,492.37	12,02,897.68	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	72	1,22,941.96	1,69,556.60	37.92	22	82,929.98	1,27,990.84	4 - 180
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	6	7,811.86	21,690.30	3 - 155
3	ASSAM	49	49,143.47	58,539.90	19.12	19	10,412.34	13,124.56	5 - 74
4	BIHAR	98	1,23,227.91	1,59,156.00	29.16	19	37,044.29	62,782.64	4 - 141
5	GOA	10	5,332.77	5,343.26	0.20	0	0.00	0.00	-
6	GUJARAT	59	1,07,424.00	1,18,232.87	10.06	17	32,311.26	42,393.46	1 - 139
7	HARYANA	36	61,492.56	63,819.18	3.78	11	8,352.20	8,526.92	2 - 29
8	HIMACHAL PRADESH	19	21,918.19	31,775.79	44.97	4	5,801.42	11,872.59	9 - 162
9	JAMMU AND KASHMIR	30	48,180.49	74,107.74	53.81	3	11,037.05	36,486.05	3 - 241
10	KARNATAKA	55	70,566.39	82,854.38	17.41	18	41,251.18	47,569.61	4 - 264
11	KERALA	22	30,240.60	35,331.06	16.83	6	3,831.57	4,855.75	6 - 59
12	MADHYA PRADESH	77	68,456.96	77,078.88	12.59	45	33,986.62	41,445.00	12 - 64
13	MAHARASHTRA	232	2,07,667.20	2,30,622.84	11.05	43	81,521.31	1,04,273.10	3 - 219
14	MANIPUR	26	12,108.58	20,557.35	69.78	2	4,971.74	12,688.08	36 - 153
15	MEGHALAYA	13	5,269.68	8,588.18	62.97	2	670.27	670.27	34 - 46
16	MIZORAM	24	11,957.35	15,906.05	33.02	12	7,144.12	10,541.61	10 - 134
17	NAGALAND	35	15,989.03	20,357.79	27.32	14	6,110.30	10,431.42	38 - 132
18	ODISHA	79	1,14,487.57	1,22,542.27	7.04	35	64,662.22	72,504.35	3 - 228
19	PUNJAB	28	18,344.99	20,091.84	9.52	4	1,936.78	1,896.34	5 - 108
20	RAJASTHAN	55	51,403.28	58,056.27	12.94	9	21,012.13	26,256.78	3 - 75
21	SIKKIM	18	7,278.84	14,598.73	100.56	2	1,629.53	8,890.05	49 - 96
22	TAMIL NADU	67	1,20,992.20	1,40,426.27	16.06	30	69,820.16	79,087.57	1 - 145
23	TRIPURA	19	5,084.45	5,259.05	3.43	3	1,179.81	1,315.90	15 - 29
24	UTTAR PRADESH	114	1,51,266.95	1,55,023.25	2.48	35	79,909.27	81,376.94	2 - 73
25	WEST BENGAL	71	62,791.47	80,666.39	28.47	27	31,549.05	38,659.97	4 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	7	2,230.29	2,520.99	23 - 54
27	DELHI	31	84,554.41	85,648.40	1.29	14	12,224.87	13,364.11	3 - 55
28	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
29	CHHATISGARH	46	78,726.75	89,025.67	13.08	24	34,481.96	44,179.94	3 - 144
30	JHARKHAND	38	68,190.29	71,740.96	5.21	19	54,051.80	53,941.72	3 - 188
31	UTTARAKHAND	31	35,703.09	50,557.17	41.60	14	28,222.96	42,565.52	3 - 138
32	TELANGANA	52	38,726.46	41,766.05	7.85	13	17,328.34	18,107.16	6 - 168
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	15 - 15
34	MULTI STATE	113	3,45,091.51	4,57,134.61	32.47	58	1,10,524.42	1,60,212.81	5 - 276
Total		1680	21,74,182.86	26,08,330.02	19.97	539	9,06,492.37	12,02,897.68	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	3	63,628.00	73,508.00	36 - 75
2	CIVIL AVIATION	20	15,324.88	15,510.25	1.21	14	12,423.16	12,608.53	3 - 29
3	COAL	107	1,52,152.82	1,54,295.46	1.41	40	40,477.27	43,408.44	0 - 168
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	4	1,101.28	1,101.28	0.00	1	215.92	215.92	23 - 23
6	MINES	6	8,226.44	7,330.54	-10.89	1	355.00	355.00	37 - 37
7	STEEL	8	31,604.15	32,021.30	1.32	2	1,296.88	1,296.88	30 - 61
8	PETROLEUM	151	3,64,602.32	3,52,793.57	-3.24	48	29,661.89	28,437.34	-1 - 59
9	POWER	62	2,67,295.21	2,68,103.37	0.30	23	1,29,087.57	1,29,048.41	11 - 138
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	6	2,675.43	2,795.43	9 - 46
12	RAILWAYS	287	5,64,471.78	6,93,056.85	22.78	110	1,85,724.03	2,57,409.39	0 - 324
13	ROAD TRANSPORT AND HIGHWAYS	887	5,41,776.54	5,50,414.28	1.59	102	53,643.28	53,404.90	0 - 118
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	2	24,912.20	24,912.20	45 - 80
16	URBAN DEVELOPMENT	28	2,85,533.80	2,98,377.53	4.50	4	31,357.10	33,371.10	12 - 44
17	WATER RESOURCES	43	70,134.44	70,243.27	0.16	8	57,131.86	57,131.86	4 - 25
18	DEFENCE PRODUCTION	1	210.00	210.00	0.00	1	210.00	210.00	22 - 22
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	23	10,359.62	10,416.24	0.55	11	6,090.30	6,051.12	3 - 57
21	HOME AFFAIRS	6	2,379.85	3,160.62	32.81	1	1,219.21	2,000.00	29 - 29
22	RURAL DEVELOPMENT	1	361.60	361.60	0.00	0	0.00	0.00	-
23	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	-
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	-
Total		1680	24,55,161.90	26,08,330.02	6.24	377	6,40,109.10	7,26,164.52	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	41.55
2	CIVIL AVIATION	20	15,324.88	15,510.25	1.21	3	3,426.27	3,695.33	7.85
3	COAL	107	1,52,152.82	1,54,295.46	1.41	8	22,093.43	25,136.67	13.77
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	6	8,226.44	7,330.54	-10.89	0	0.00	0.00	0.00
7	STEEL	8	31,604.15	32,021.30	1.32	1	1,682.85	2,100.00	24.79
8	PETROLEUM	151	3,64,602.32	3,52,793.57	-3.24	3	4,946.46	5,575.34	12.71
9	POWER	62	2,67,295.21	2,68,103.37	0.30	5	24,279.91	26,684.38	9.90
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	12	5,589.39	6,374.57	14.05
12	RAILWAYS	287	5,64,471.78	6,93,056.85	22.78	167	1,95,131.24	3,33,189.11	70.75
13	ROAD TRANSPORT AND HIGHWAYS	887	5,41,776.54	5,50,414.28	1.59	143	95,479.17	1,12,893.82	18.24
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	28	2,85,533.80	2,98,377.53	4.50	3	47,274.77	60,118.50	27.17
17	WATER RESOURCES	43	70,134.44	70,243.27	0.16	4	1,393.47	1,736.93	24.65
18	DEFENCE PRODUCTION	1	210.00	210.00	0.00	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	23	10,359.62	10,416.24	0.55	5	1,863.63	2,061.44	10.61
21	HOME AFFAIRS	6	2,379.85	3,160.62	32.81	1	1,219.21	2,000.00	64.04
22	RURAL DEVELOPMENT	1	361.60	361.60	0.00	0	0.00	0.00	0.00
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0.00
Total		1680	24,55,161.90	26,08,330.02	6.24	359	4,45,510.89	6,34,215.39	42.36

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	74- 75
2	CIVIL AVIATION	20	15,324.88	15,510.25	1.21	3	3,426.27	3,695.33	15- 27
3	COAL	107	1,52,152.82	1,54,295.46	1.41	6	4,567.14	7,609.57	36- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	6	8,226.44	7,330.54	-10.89	0	0.00	0.00	0- 0
7	STEEL	8	31,604.15	32,021.30	1.32	0	0.00	0.00	0- 0
8	PETROLEUM	151	3,64,602.32	3,52,793.57	-3.24	0	0.00	0.00	0- 0
9	POWER	62	2,67,295.21	2,68,103.37	0.30	2	17,866.58	19,383.42	19- 51
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	1	1,351.00	1,471.00	9- 9
12	RAILWAYS	287	5,64,471.78	6,93,056.85	22.78	68	1,01,507.30	1,73,654.57	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	887	5,41,776.54	5,50,414.28	1.59	7	5,310.57	6,060.07	23- 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	28	2,85,533.80	2,98,377.53	4.50	1	10,773.00	12,787.00	44- 44
17	WATER RESOURCES	43	70,134.44	70,243.27	0.16	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	210.00	210.00	0.00	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	23	10,359.62	10,416.24	0.55	1	496.00	498.99	57- 57
21	HOME AFFAIRS	6	2,379.85	3,160.62	32.81	1	1,219.21	2,000.00	29- 29
22	RURAL DEVELOPMENT	1	361.60	361.60	0.00	0	0.00	0.00	0- 0
23	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	0- 0
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0- 0
Total		1680	24,55,161.90	26,08,330.02	6.24	92	1,70,296.07	2,60,818.95	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	20	14,431.97	15,510.25	7.47	4	3,288.50	4,403.06	15- 45
3	COAL	107	1,49,691.71	1,54,295.46	3.08	16	31,009.03	34,889.43	12- 188
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	6	7,333.99	7,330.54	-0.05	0	0.00	0.00	0- 0
7	STEEL	8	25,189.15	32,021.30	27.12	2	17,207.85	24,040.00	38- 80
8	PETROLEUM	151	3,41,221.64	3,52,793.57	3.39	24	51,911.42	69,135.09	6- 110
9	POWER	62	2,07,257.24	2,68,103.37	29.36	19	97,575.65	1,59,214.60	6- 162
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,715.78	2.90	1	1,351.00	1,471.00	9- 9
12	RAILWAYS	287	4,54,260.58	6,93,056.85	52.57	107	1,41,191.78	2,73,293.02	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	887	5,35,763.35	5,50,414.28	2.73	23	11,034.82	13,062.93	23- 134
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	1	13,334.00	24,664.00	80- 80
16	URBAN DEVELOPMENT	28	2,76,487.00	2,98,377.53	7.92	4	60,511.47	77,105.12	34- 73
17	WATER RESOURCES	43	24,702.19	70,243.27	184.36	2	10,349.47	55,773.56	4- 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	23	10,311.33	10,416.24	1.02	1	496.18	498.99	57- 57
21	HOME AFFAIRS	6	2,139.99	3,160.62	47.69	3	1,659.44	2,528.33	3- 44
22	RURAL DEVELOPMENT	1	361.60	361.60	0.00	0	0.00	0.00	0- 0
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
25	RENEWABLE ENERGY	1	271.90	271.90	0.00	0	0.00	0.00	0- 0
Total		1680	21,74,182.86	26,08,330.02	19.97	211	4,72,964.61	7,85,756.13	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Project	DOA	Original		Now anticipated		Final Expenditure
			Cost	DOC	Cost	DOC	
	<u>CIVIL AVIATION</u>						
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNAI AIRPORT	01/2008	535.00	06/2010	535.00	N.A.	0.01
	<u>COAL</u>						
2	SINGHORI OC MINE	06/2015	205.49	03/2020	205.49	10/2021	138.58
3	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	03/2019	325.18	10/2021	272.90
4	AMALGAMATED PAUNI-II III OC MINE	06/2015	483.69	03/2021	499.00	10/2021	253.70
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
5	STUDY IN INDIA	03/2018	150.00	04/2018	150.00	N.A.	0.00
6	DEVELOPMENT OF PERMANENT CAMPUS OF IIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES PPP BOT (Hybrid Annuity)	03/2021	127.26	10/2023	188.88	10/2023	12.73
7	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	03/2019	418.00	N.A.	110.00
	<u>HOME AFFAIRS</u>						
8	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE-C/O 336 NOS. TYPE- II QTRS , 96	01/2020	166.98	05/2022	166.98	05/2022	0.29
	<u>PETROLEUM</u>						
9	GAIL GAS LTD BENGALURU CGD PROJECT Central Sector Projects	02/2015	749.00	02/2020	749.00	N.A.	1,043.56
10	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4,588.29	08/2018	5,575.00	09/2021	5,376.50
11	BS-VI PROJECTS	09/2017	1,858.00	12/2019	1,858.00	10/2021	1,528.75
	<u>RAILWAYS</u>						
12	GHAZIPUR - AUNRIHAR (40 KM)	04/2014	182.92	N.A.	197.73	N.A.	0.01
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
13	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH EPC	07/2015	197.16	10/2018	197.16	N.A.	91.25
14	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-	03/2018	323.98	09/2018	323.98	11/2022	50.13

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	TAMLU-MON ROAD FROM EXISTING KM 60.345 TO						
15	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	01/2017	256.66	N.A.	256.66	03/2021	16.42
16	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D EPC	08/2020	232.29	04/2022	232.29	04/2022	4.98
17	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	02/2017	167.28	04/2017	167.28	08/2020	22.06
18	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	03/2016	429.52	08/2016	429.52	02/2021	238.28
	<u>URBAN DEVELOPMENT</u>						
19	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	02/2020	532.00	11/2020	532.00	09/2021	541.00

TABLE-14

List of projects added Rs. 150 Crore and above					(October 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	645.63	8/2022	645.63	11/2022
	<u>COAL</u>					
2	DHUPTALA OC(SASTI UG TO OC)	2/2019	720.87	3/2028	720.87	3/2028
	<u>POWER</u>					
3	SHIYAL SOLAR POWER PROJECT	5/2021	296.20	10/2022	296.20	10/2022
4	PARASAN SOLAR POWER PROJECT	8/2021	313.58	12/2022	313.58	12/2022
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
5	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. EPC	7/2020	319.09	9/2021	319.09	9/2021
6	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II EPC	8/2020	216.72	12/2020	216.72	-
7	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. EPC	12/2020	379.23	10/2021	379.23	10/2021
8	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 & KM 158.419 TO KM 173.300 PKG-II. EPC	12/2020	339.65	10/2021	339.65	10/2021
9	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- EPC	2/2021	240.99	11/2021	240.99	11/2021
10	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 EPC	12/2020	733.00	1/2024	733.00	1/2024
11	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO EPC	12/2020	881.00	4/2024	881.00	4/2024
12	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI EPC	12/2020	989.66	1/2024	989.66	1/2024
13	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO EPC	12/2020	1,234.40	4/2024	1,234.40	4/2024
14	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO EPC	12/2020	1,094.46	4/2024	1,094.46	4/2024

List of projects added Rs. 150 Crore and above					(October 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
15	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- EPC	2/2021	1,269.96	4/2024	1,269.96	4/2024
16	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- EPC	2/2021	853.66	4/2024	853.66	4/2024

TABLE-15

Milestones (Cumulative due & achieved)		Rs. 150 Crore and above
Total		5961
Achieved up to month		2987

TABLE-16

List of projects reporting additional delayed Rs. 150 Crore and above							(October 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT AAI	438.28	402.00	06/2019	10/2021	11/2021	1
2	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI AAI	951.28	951.28	10/2021	07/2022	10/2022	3
3	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT AAI	1,405.00	1,405.00	08/2022	12/2022	03/2023	3
	<u>COAL</u>						
4	MADHUBAND NLW WASHERY BCCL	289.45	289.45	05/2014	10/2021	12/2021	2
5	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL	1,055.05	1,055.05	03/2018	10/2021	03/2029	89
	<u>MINES</u>						
6	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN NALCO Central Sector Projects	483.00	483.00	04/2021	03/2023	12/2023	9
7	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT NALCO	5,540.00	5,540.00	04/2021	12/2022	01/2024	13
8	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND NALCO Central Sector Projects	355.00	355.00	11/2020	02/2021	12/2023	34
	<u>STEEL</u>						
9	FORGED WHEEL PLANT RINL	1,682.85	2,100.00	09/2018	10/2021	11/2021	1
10	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL SAIL	262.87	262.87	06/2019	10/2021	12/2021	2
	<u>PETROLEUM</u>						
11	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	10/2021	11/2021	1
12	AUGMENTATION OF CTMPL IOCL Central Sector Projects	228.00	228.00	11/2021	11/2021	12/2021	1
13	RE-LIQUIFIED NATURAL GAS CPCL	421.00	305.00	08/2020	11/2021	12/2021	1

List of projects reporting additional delayed Rs. 150 Crore and above							(October 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
14	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY IOCL	315.00	315.00	12/2021	10/2021	11/2021	1
15	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY IOCL	189.00	189.00	01/2021	11/2021	12/2021	1
16	RESITEMENT OF RAICHUR DEPOT TO GULBARGA BPCL	206.26	206.26	03/2021	10/2021	11/2021	1
17	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI IOCL	921.00	921.00	09/2023	12/2023	02/2024	2
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	2,001.34	05/2013	02/2022	05/2022	3
19	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR IOCL	1,823.00	3,027.90	03/2021	12/2021	03/2022	3
20	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN OIL	224.75	198.00	08/2020	09/2021	12/2021	3
21	SULPHUR FORMING UNIT IN SRU HPCL EPC	210.94	210.94	08/2021	12/2021	03/2022	3
22	SWRO II WITH LLPH FACILITIES HPCL	196.26	196.26	07/2020	09/2021	01/2022	4
23	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU HPCL	380.00	380.00	11/2021	11/2021	03/2022	4
24	PARADIP LPG IMPORT FACILITY IOCL	690.00	690.00	07/2018	10/2021	03/2022	5
25	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE IOCL	906.00	906.00	02/2020	10/2021	03/2022	5
26	DEVANGONTHI MARKETING TERMINAL MANGALORE REFIN	200.00	304.00	06/2023	08/2023	01/2024	5
27	LPG TERMINAL AT KOCHI IOCL	607.06	1,236.00	10/2017	03/2022	09/2022	6
28	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA HPCL	249.26	249.26	06/2020	09/2021	03/2022	6
29	LPG BP PROJECT CHITTOOR IOCL	167.00	167.00	07/2022	07/2022	01/2023	6
30	LPG BP PROJECT KHORDHA IOCL Central Sector Projects	161.59	161.59	12/2019	03/2022	10/2022	7
31	LPG BP PROJECT JODHPUR IOCL	229.80	229.80	N.A.	05/2022	12/2022	7
32	SITARGANJ LPG PROJECT IOCL Central Sector Projects	160.10	160.10	02/2020	10/2021	06/2022	8

List of projects reporting additional delayed Rs. 150 Crore and above (October 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
33	KHARAGPUR LPG BOTTLING PLANT IOCL	163.02	207.36	04/2020	10/2021	07/2022	9
34	ETHYLENE GLYCOL PROJECT AT PARADIP IOCL	5,654.00	5,654.00	10/2021	10/2021	07/2022	9
	<u>POWER</u>						
35	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	10,566.00	07/2012	10/2021	11/2021	1
36	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	11/2021	12/2021	1
37	EASTERN REGION STRENGTHENING SCHEME XX PGCIL	358.83	358.83	05/2020	11/2021	12/2021	1
38	KAWAS SOLAR 56 MW NTPC EPC	261.80	261.80	10/2021	10/2021	11/2021	1
	<u>HEALTH AND FAMILY WELFARE</u>						
39	HOSPITAL AND TEACHING- AIIMS GUNTUR HSCC Central Sector Projects	601.02	601.02	N.A.	11/2021	12/2021	1
	<u>RAILWAYS</u>						
40	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	10/2021	11/2021	1
41	ARSIKERE-TUMKUR SWR	578.00	760.00	03/2020	11/2021	12/2021	1
42	ROURKELA JHARSUGUDA THIRD LINE 101 KM SER	969.83	1,312.96	03/2020	02/2022	03/2022	1
43	MADURAI-BODINAYAKKANUR SR	164.41	608.13	N.A.	12/2021	02/2022	2
44	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) MRTPT	495.44	2,980.41	03/2004	03/2022	06/2022	3
45	AGARTALA-AKHAURA NL NFR	569.63	742.00	03/2020	03/2022	06/2022	3
46	BHADRACHALAM ROAD-SATTUPALLI SCR	704.31	927.94	03/2020	11/2021	02/2022	3
47	NANGALDAM-TALWARA(NL),NR NR	450.00	2,017.96	07/2012	03/2024	11/2024	8
48	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,122.00	N.A.	09/2021	12/2022	15
49	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC ECR	548.00	819.01	03/2020	03/2023	12/2024	21

List of projects reporting additional delayed Rs. 150 Crore and above							(October 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
50	4-LANING OF FARAKA-RAIGANJ NHAJ PPP (BOT)	1,078.84	1,078.84	08/2013	10/2021	11/2021	1
51	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C MoRTH	171.90	171.90	08/2020	10/2021	11/2021	1
52	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 MoRTH EPC	957.54	957.54	02/2020	09/2021	11/2021	2
53	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS MoRTH	162.56	162.56	03/2018	10/2021	12/2021	2
54	2L+PS OF THIKRI ANJAD SECTION OF NH-347B MoRTH	249.05	249.05	07/2018	10/2021	12/2021	2
55	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A MoRTH	373.82	373.82	09/2019	10/2021	12/2021	2
56	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. MoRTH	392.33	428.55	03/2018	10/2021	12/2021	2
57	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS MoRTH	296.50	296.50	09/2020	09/2021	11/2021	2
58	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 MoRTH	306.59	306.59	N.A.	09/2021	11/2021	2
59	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM NHAJ PPP (BOT)	822.90	822.90	04/2018	09/2021	12/2021	3
60	HOSPET-BELLARY-KARNATAKA AP BORDER NHAJ	1,167.42	870.00	03/2019	09/2022	12/2022	3
61	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV NHAJ	894.00	929.32	04/2020	12/2021	03/2022	3
62	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAJ	1,532.62	2,499.00	03/2021	04/2021	07/2021	3
63	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 MoRTH	263.89	242.05	04/2020	12/2021	03/2022	3
64	PUNE-SATARA(NH-4) NHAJ PPP (BOT)	1,724.55	1,724.55	03/2013	09/2021	03/2022	6

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	704,68.00	80,348.00	62,664.37
CIVIL AVIATION	20	14,431.97	153,24.88	15,510.25	5,187.07
COAL	107	1,49,691.71	1,521,52.82	1,54,295.46	53,610.91
FINANCE	2	557.77	5,57.77	557.73	394.75
FERTILISERS	4	1,101.28	11,01.28	1,101.28	886.72
MINES	6	7,333.99	82,26.44	7,330.54	1,618.41
STEEL	8	25,189.15	316,04.15	32,021.30	24,076.03
PETROLEUM	151	3,41,221.64	3,646,02.32	3,52,793.57	1,19,873.17
POWER	62	2,07,257.24	2,672,95.21	2,68,103.37	1,74,646.26
HEAVY INDUSTRY	2	3,272.00	52,81.30	4,627.30	4,337.74
HEALTH AND FAMILY WELFARE	29	15,273.26	152,73.26	15,715.78	9,026.70
RAILWAYS	287	4,54,260.58	5,644,71.78	6,93,056.85	2,66,992.14
ROAD TRANSPORT AND HIGHWAYS	887	5,35,763.35	5,417,76.54	5,50,414.28	3,28,536.82
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,940.64
TELECOMMUNICATIONS	3	14,013.36	253,35.07	25,335.07	20,736.63
URBAN DEVELOPMENT	28	2,76,487.00	2,855,33.80	2,98,377.53	1,49,823.10
WATER RESOURCES	43	24,702.19	701,34.44	70,243.27	22,642.34
DEFENCE PRODUCTION	1	246.31	2,10.00	210.00	149.80
COMMERCE	1	302.64	3,02.64	302.64	30.00
DEPARTMENT OF HIGHER EDUCATION	23	10,311.33	103,59.62	10,416.24	3,303.35
HOME AFFAIRS	6	2,139.99	23,79.85	3,160.62	1,227.84
RURAL DEVELOPMENT	1	361.60	3,61.60	361.60	12.44
DPIIT	2	17,352.09	173,52.09	18,990.30	12,587.76
DONER	1	151.33	1,51.33	151.33	149.33
RENEWABLE ENERGY	1	271.90	2,71.90	271.90	90.99
Grand total	1680	21,74,182.86	24,55,161.90	26,08,330.02	12,64,545.31

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	72	1,22,941.96	1,69,556.60	37.92	6	39,547.65	93,530.51	24 - 180
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	4	6,882.14	20,760.58	59 - 155
3	ASSAM	49	49,143.47	58,539.90	19.12	7	5,692.32	8,431.29	12 - 60
4	BIHAR	98	1,23,227.91	1,59,156.00	29.16	9	30,388.03	56,126.38	36 - 141
5	GOA	10	5,332.77	5,343.26	0.20	0	0.00	0.00	-
6	GUJARAT	59	1,07,424.00	1,18,232.87	10.06	10	28,158.76	38,368.74	3 - 139
7	HARYANA	36	61,492.56	63,819.18	3.78	2	493.05	667.77	16 - 29
8	HIMACHAL PRADESH	19	21,918.19	31,775.79	44.97	2	5,270.59	11,368.59	9 - 162
9	JAMMU AND KASHMIR	30	48,180.49	74,107.74	53.81	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	55	70,566.39	82,854.38	17.41	8	31,934.94	38,587.10	7 - 264
11	KERALA	22	30,240.60	35,331.06	16.83	2	1,719.06	2,743.24	32 - 59
12	MADHYA PRADESH	77	68,456.96	77,078.88	12.59	12	13,206.12	21,277.86	12 - 48
13	MAHARASHTRA	232	2,07,667.20	2,30,622.84	11.05	19	44,485.10	67,380.50	8 - 219
14	MANIPUR	26	12,108.58	20,557.35	69.78	1	4,454.17	12,264.15	153 - 153
15	MEGHALAYA	13	5,269.68	8,588.18	62.97	0	0.00	0.00	-
16	MIZORAM	24	11,957.35	15,906.05	33.02	3	2,774.12	6,171.61	87 - 134
17	NAGALAND	35	15,989.03	20,357.79	27.32	1	2,326.52	6,647.64	132 - 132
18	ODISHA	79	1,14,487.57	1,22,542.27	7.04	14	14,971.58	22,813.71	6 - 204
19	PUNJAB	28	18,344.99	20,091.84	9.52	1	754.54	756.27	30 - 30
20	RAJASTHAN	55	51,403.28	58,056.27	12.94	3	13,624.08	18,868.73	23 - 75
21	SIKKIM	18	7,278.84	14,598.73	100.56	1	1,339.48	8,600.00	96 - 96
22	TAMIL NADU	67	1,20,992.20	1,40,426.27	16.06	9	11,289.42	22,024.04	27 - 145
23	TRIPURA	19	5,084.45	5,259.05	3.43	1	569.63	742.00	27 - 27
24	UTTAR PRADESH	114	1,51,266.95	1,55,023.25	2.48	10	24,670.82	27,100.77	12 - 73
25	WEST BENGAL	71	62,791.47	80,666.39	28.47	14	16,068.31	23,184.80	4 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	23 - 45
27	DELHI	31	84,554.41	85,648.40	1.29	4	6,466.89	7,685.33	3 - 34
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATISGARH	46	78,726.75	89,025.67	13.08	9	25,751.75	35,569.08	18 - 84
30	JHARKHAND	38	68,190.29	71,740.96	5.21	4	21,922.14	23,368.06	12 - 188
31	UTTARAKHAND	31	35,703.09	50,557.17	41.60	6	24,597.23	38,939.79	3 - 138
32	TELANGANA	52	38,726.46	41,766.05	7.85	7	13,818.02	15,075.98	23 - 168
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	15 - 15
34	MULTI STATE	113	3,45,091.51	4,57,134.61	32.47	38	76,286.85	1,27,326.55	12 - 276
Total		1680	21,74,182.86	26,08,330.02	19.97	211	4,72,964.61	7,85,756.13	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	152	5
2	ROAD TRANSPORT AND HIGHWAYS	150	3
3	PETROLEUM	59	5
4	POWER	37	1
5	COAL	31	1
6	URBAN DEVELOPMENT	22	0
7	CIVIL AVIATION	5	1
8	STEEL	5	1
9	ATOMIC ENERGY	4	0
10	HEALTH AND FAMILY WELFARE	4	0
11	DPIIT	2	0
12	MINES	1	1
13	HEAVY INDUSTRY	1	0
14	SHIPPING AND PORTS	1	0
15	TELECOMMUNICATIONS	1	0
16	WATER RESOURCES	1	0
17	HOME AFFAIRS	1	0
	Total	477	18

FLASH REPORT

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	June,2021			
	<u>PETROLEUM</u>			
1	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	August,2021			
	<u>PETROLEUM</u>			
3	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
	<u>POWER</u>			
4	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
5	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
6	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
7	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
8	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
9	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
10	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
	September,2021			
	<u>POWER</u>			
12	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000061]	4,824.12	10/2012	4,612.66

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	EASTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000155]	1,364.52	04/2016	1,290.03
14	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000168]	5,151.37	03/2018	3,269.93
15	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000218]	3,519.59	05/2019	2,562.41
16	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000257]	3,654.00	04/2019	3,508.04
	<u>RAILWAYS</u>			
17	GONDIA-JABALPUR(GC),(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100186]	511.86	04/2020	1,867.16
18	NANDYAL-YERRAGUNTALA(NL),SCR (SOUTH CENTRAL RAILWAY) - [220100192]	164.36	02/2009	1,148.67
19	HARIDASPUR-PARADEEP(NL) (RAIL VIKAS NIGAM LTD.) - [220100285]	1,185.64	12/2017	2,129.37
20	CHHINDWARA - NAGPUR (GC)(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100324]	383.79	-	1,448.56
21	BARDHAMAN-KATWA (GC) (EASTERN RAILWAYS) - [N22000091]	1,106.62	12/2010	1,003.78
22	CHAMPA-JHARSUGUDA 3RD LINE (SOUTH EAST CENTRAL RAILWAY) - [N22000483]	872.00	12/2019	1,156.06
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
23	FOUR LANING OF AURANGABAD - YEDISHI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000508]	1,871.34	01/2018	3,443.43
24	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000541]	1,081.57	06/2019	480.25
25	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000545]	1,134.97	11/2018	809.71
26	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000621]	1,239.82	-	1,691.00
	<u>URBAN DEVELOPMENT</u>			
27	REDEVELOPMENT OF EAST KIDWAI NAGAR (NATIONAL BUILDING CONSTRUCTION CORPORATION LTD) - [N28000080]	4,264.00	11/2019	4,683.08
	October,2021			
	<u>PETROLEUM</u>			
28	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000227]	4,588.29	08/2018	5,376.50

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
29	BS-VI PROJECTS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000295]	1,858.00	12/2019	1,528.75

FLASH REPORT

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
	August,2021			
2	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
3	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
4	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
5	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
6	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
	September,2021			
7	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000439]	1,885.74	05/2019	1,636.02

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	475
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects Elevated in Current Month	1
No of Projects added in Current Month	3
No of Projects in Current Month	477

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	212 (44.44%)	9 (1.89%)	65 (13.63%)	31 (6.50%)	160 (33.54%)	477
Latest Approved (Date)	133 (27.88%)	11 (2.31%)	151 (31.66%)	22 (4.61%)	160 (33.54%)	477

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	354	12,24,118.90	13,54,906.25	5,82,970.89	43.00	1,30,787.35	10.70
Project with Revision in Cost	123	7,22,353.53	7,35,470.74	4,29,443.40	58.40	13,117.21	1.80
Total	477	19,46,472.43	20,90,376.99	10,12,414.29	48.43	1,43,904.56	7.39
Original Cost of All Projects							
Original Cost	477	16,70,459.77	20,90,376.99	10,12,414.29	48.43	4,19,917.22	25.14

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	212	7,69,716.92	10,59,555.42	6,19,132.94	58.40	2,89,838.50	37.66
Latest Approved (RCE)	133	5,38,905.82	6,21,800.55	3,55,428.84	57.20	82,894.73	15.38

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	18	35,226.60	51,862.39	36,811.37	71.00	16,635.79	47.20
Total	18	35,226.60	51,862.39	36,811.37	70.98	16,635.79	47.23

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.90	8,303.90	9.06	2	2,525.00	3,215.00	27.33
3	COAL	31	1,15,154.25	1,20,003.52	4.21	4	32,770.17	37,619.44	14.80
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	5	24,006.86	30,839.01	28.46	2	17,207.85	24,040.00	39.70
6	PETROLEUM	59	3,03,883.67	3,14,979.30	3.65	15	61,689.32	85,050.89	37.87
7	POWER	37	1,95,373.11	2,55,798.01	30.93	18	1,02,032.76	1,64,531.01	61.25
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
10	RAILWAYS	152	3,92,533.76	6,21,279.34	58.27	121	2,07,780.97	4,37,795.52	110.70
11	ROAD TRANSPORT AND HIGHWAYS	150	2,29,558.56	2,40,947.63	4.96	42	56,087.90	70,020.24	24.84
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,74,372.14	2,96,243.00	7.97	6	93,461.70	1,15,411.76	23.49
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		477	16,70,459.77	20,90,376.99	25.14	221	6,47,529.01	10,86,412.33	67.78

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						1000	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	21	1,02,371.04	1,48,846.18	45.40	9	45,368.15	1,00,765.29	122.11
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	2	8,264.33	22,029.33	166.56
3	ASSAM	8	33,271.03	41,170.76	23.74	5	16,996.48	26,066.21	53.36
4	BIHAR	29	91,524.56	1,25,846.81	37.50	16	46,877.81	81,835.56	74.57
5	GUJARAT	23	87,132.33	97,557.24	11.96	11	32,208.42	43,292.38	34.41
6	HARYANA	13	51,125.78	52,305.78	2.31	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	8,237.58	18,122.01	119.99
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	3	6,236.00	32,296.00	417.90
9	KARNATAKA	18	54,648.17	66,583.30	21.84	12	43,122.74	55,057.87	27.68
10	KERALA	9	24,577.63	28,764.08	17.03	7	12,015.73	16,202.18	34.84
11	MADHYA PRADESH	20	40,080.22	48,043.50	19.87	9	13,249.36	21,729.69	64.01
12	MAHARASHTRA	45	1,30,458.47	1,56,360.61	19.85	20	56,156.86	82,765.93	47.38
13	MANIPUR	2	5,032.79	13,575.20	169.74	2	5,032.79	13,575.20	169.74
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	130.69
16	NAGALAND	2	6,600.52	10,921.64	65.47	1	2,326.52	6,647.64	185.73
17	ODISHA	36	95,620.70	1,02,819.52	7.53	10	14,418.29	21,617.11	49.93
18	PUNJAB	7	8,647.82	9,958.16	15.15	2	2,557.95	3,868.29	51.23
19	RAJASTHAN	14	31,155.16	37,300.84	19.73	3	14,293.90	20,439.58	43.00
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	27	1,01,563.30	1,20,154.29	18.30	13	36,726.73	55,712.72	51.70
22	UTTAR PRADESH	42	1,16,619.62	1,21,373.57	4.08	14	33,185.29	39,391.89	18.70
23	WEST BENGAL	24	46,173.48	62,979.44	36.40	14	25,352.53	42,174.79	66.35
24	DELHI	8	75,922.38	77,028.97	1.46	2	5,992.21	7,178.00	19.79
25	CHHATISGARH	17	65,860.61	75,619.96	14.82	7	25,757.63	35,619.00	38.29
26	JHARKHAND	14	59,480.43	63,628.76	6.97	6	27,885.12	33,589.45	20.46
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	5	24,870.06	39,070.51	57.10
28	TELANGANA	6	19,991.02	22,312.36	11.61	4	14,138.06	16,827.28	19.02
29	MULTI STATE	56	3,20,940.13	4,28,221.25	33.43	37	1,20,511.06	2,30,045.95	90.89
Total		477	16,70,459.77	20,90,376.99	25.14	221	6,47,529.01	10,86,412.33	67.78

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	8,303.90	9.06	5	7,613.90	8,303.90	7 - 27
3	COAL	31	1,15,154.25	1,20,003.52	4.21	17	60,862.87	63,638.46	12 - 228
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	33 - 33
5	STEEL	5	24,006.86	30,839.01	28.46	4	21,099.86	27,932.01	38 - 80
6	PETROLEUM	59	3,03,883.67	3,14,979.30	3.65	30	1,25,411.75	1,31,575.65	2 - 110
7	POWER	37	1,95,373.11	2,55,798.01	30.93	28	1,63,196.43	2,22,300.79	4 - 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	152	3,92,533.76	6,21,279.34	58.27	99	1,70,653.75	2,97,006.28	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	150	2,29,558.56	2,40,947.63	4.96	10	15,211.87	15,375.44	21 - 108
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	22	2,74,372.14	2,96,243.00	7.97	9	1,02,178.24	1,18,673.02	12 - 73
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29 - 29
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
Total		477	16,70,459.77	20,90,376.99	25.14	212	7,69,716.92	10,59,555.42	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	1,02,371.04	1,48,846.18	45.40	9	78,917.36	1,23,978.22	24 - 180
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	41,170.76	23.74	4	4,630.48	7,098.21	12 - 48
4	BIHAR	29	91,524.56	1,25,846.81	37.50	10	33,252.42	58,716.95	14 - 141
5	GUJARAT	23	87,132.33	97,557.24	11.96	8	28,375.60	38,331.57	3 - 74
6	HARYANA	13	51,125.78	52,305.78	2.31	3	5,172.94	5,172.94	2 - 20
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	2	10,612.12	36,061.12	63 - 241
9	KARNATAKA	18	54,648.17	66,583.30	21.84	6	34,583.00	40,805.05	26 - 264
10	KERALA	9	24,577.63	28,764.08	17.03	2	1,719.06	2,743.24	32 - 59
11	MADHYA PRADESH	20	40,080.22	48,043.50	19.87	13	19,570.47	26,986.98	12 - 48
12	MAHARASHTRA	45	1,30,458.47	1,56,360.61	19.85	19	70,547.41	92,816.24	7 - 219
13	MANIPUR	2	5,032.79	13,575.20	169.74	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	120 - 120
16	NAGALAND	2	6,600.52	10,921.64	65.47	1	2,326.52	6,647.64	132 - 132
17	ODISHA	36	95,620.70	1,02,819.52	7.53	23	59,245.99	66,312.88	5 - 228
18	PUNJAB	7	8,647.82	9,958.16	15.15	0	0.00	0.00	-
19	RAJASTHAN	14	31,155.16	37,300.84	19.73	4	17,374.02	22,133.02	4 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	27	1,01,563.30	1,20,154.29	18.30	13	59,759.13	69,451.46	3 - 145
22	UTTAR PRADESH	42	1,16,619.62	1,21,373.57	4.08	17	72,880.51	74,446.66	5 - 48
23	WEST BENGAL	24	46,173.48	62,979.44	36.40	12	26,338.00	33,067.05	5 - 324
24	DELHI	8	75,922.38	77,028.97	1.46	5	9,694.73	10,801.32	15 - 55
25	CHHATISGARH	17	65,860.61	75,619.96	14.82	7	27,278.34	36,436.75	18 - 80
26	JHARKHAND	14	59,480.43	63,628.76	6.97	8	50,765.98	50,522.86	13 - 188
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	5	24,726.84	38,653.22	3 - 138
28	TELANGANA	6	19,991.02	22,312.36	11.61	3	13,183.42	13,427.52	23 - 168
29	MULTI STATE	56	3,20,940.13	4,28,221.25	33.43	32	99,019.54	1,47,197.90	11 - 276
Total		477	16,70,459.77	20,90,376.99	25.14	212	7,69,716.92	10,59,555.42	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	3	63,628.00	73,508.00	36 - 75
2	CIVIL AVIATION	5	8,168.90	8,303.90	1.65	5	8,168.90	8,303.90	7 - 27
3	COAL	31	1,17,517.97	1,20,003.52	2.12	11	29,179.51	31,664.26	0 - 168
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	5	30,421.86	30,839.01	1.37	1	1,034.01	1,034.01	61 - 61
6	PETROLEUM	59	3,26,275.11	3,14,979.30	-3.46	8	14,622.04	13,740.64	2 - 59
7	POWER	37	2,55,249.40	2,55,798.01	0.21	15	1,26,365.47	1,26,326.31	11 - 138
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	152	5,00,535.26	6,21,279.34	24.12	73	1,67,929.12	2,36,166.30	0 - 324
11	ROAD TRANSPORT AND HIGHWAYS	150	2,34,695.48	2,40,947.63	2.66	9	13,838.59	14,002.16	24 - 108
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	1	24,664.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	22	2,83,399.27	2,96,243.00	4.53	4	31,357.10	33,371.10	12 - 44
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29 - 29
17	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	-
Total		477	19,46,472.43	20,90,376.99	7.39	133	5,38,905.82	6,21,800.55	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	41.55
2	CIVIL AVIATION	5	8,168.90	8,303.90	1.65	2	3,080.00	3,215.00	4.38
3	COAL	31	1,17,517.97	1,20,003.52	2.12	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	5	30,421.86	30,839.01	1.37	1	1,682.85	2,100.00	24.79
6	PETROLEUM	59	3,26,275.11	3,14,979.30	-3.46	2	4,523.46	5,073.34	12.16
7	POWER	37	2,55,249.40	2,55,798.01	0.21	4	23,631.58	25,736.49	8.91
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
10	RAILWAYS	152	5,00,535.26	6,21,279.34	24.12	98	1,69,243.48	2,93,432.53	73.38
11	ROAD TRANSPORT AND HIGHWAYS	150	2,34,695.48	2,40,947.63	2.66	39	54,031.84	64,553.99	19.47
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	22	2,83,399.27	2,96,243.00	4.53	3	47,274.77	60,118.50	27.17
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		477	19,46,472.43	20,90,376.99	7.39	158	3,68,645.01	5,34,562.43	45.01

[^] - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	74- 75
2	CIVIL AVIATION	5	8,168.90	8,303.90	1.65	2	3,080.00	3,215.00	24- 27
3	COAL	31	1,17,517.97	1,20,003.52	2.12	1	2,661.73	5,146.48	60- 60
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	5	30,421.86	30,839.01	1.37	0	0.00	0.00	0- 0
6	PETROLEUM	59	3,26,275.11	3,14,979.30	-3.46	0	0.00	0.00	0- 0
7	POWER	37	2,55,249.40	2,55,798.01	0.21	2	17,866.58	19,383.42	19- 51
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	152	5,00,535.26	6,21,279.34	24.12	50	93,260.80	1,62,427.92	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	150	2,34,695.48	2,40,947.63	2.66	1	2,848.00	3,379.45	105- 105
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	22	2,83,399.27	2,96,243.00	4.53	1	10,773.00	12,787.00	44- 44
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29- 29
17	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	0- 0
Total		477	19,46,472.43	20,90,376.99	7.39	61	1,56,839.32	2,43,469.27	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	8,303.90	9.06	2	2,525.00	3,215.00	24- 27
3	COAL	31	1,15,154.25	1,20,003.52	4.21	3	26,863.06	29,638.65	12- 188
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	5	24,006.86	30,839.01	28.46	2	17,207.85	24,040.00	38- 80
6	PETROLEUM	59	3,03,883.67	3,14,979.30	3.65	13	48,500.05	64,945.10	8- 110
7	POWER	37	1,95,373.11	2,55,798.01	30.93	15	95,689.18	1,56,866.89	19- 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	152	3,92,533.76	6,21,279.34	58.27	79	1,27,964.51	2,55,437.00	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	150	2,29,558.56	2,40,947.63	4.96	1	2,848.00	3,379.45	105- 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80- 80
14	URBAN DEVELOPMENT	22	2,74,372.14	2,96,243.00	7.97	3	60,314.14	76,888.12	36- 73
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29- 29
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
Total		477	16,70,459.77	20,90,376.99	25.14	126	4,40,011.04	7,43,771.08	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>							
Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4,588.29	08/2018	5,575.00	09/2021	5,376.50
2	BS-VI PROJECTS	09/2017	1,858.00	12/2019	1,858.00	10/2021	1,528.75

FLASH REPORT

TABLE-32

List of projects added Rs. 1000 Crore and above					(October 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
1	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO EPC	12/2020	1,234.40	4/2024	1,234.40	4/2024
2	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO EPC	12/2020	1,094.46	4/2024	1,094.46	4/2024
3	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- EPC	2/2021	1,269.96	4/2024	1,269.96	4/2024

FLASH REPORT

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2578	
Achieved up to month	1635	

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(October 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT AAI	1,405.00	1,405.00	08/2022	12/2022	03/2023	3
	<u>COAL</u>						
2	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL	1,055.05	1,055.05	03/2018	10/2021	03/2029	89
	<u>MINES</u>						
3	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT NALCO	5,540.00	5,540.00	04/2021	12/2022	01/2024	13
	<u>STEEL</u>						
4	FORGED WHEEL PLANT RINL	1,682.85	2,100.00	09/2018	10/2021	11/2021	1
	<u>PETROLEUM</u>						
5	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	10/2021	11/2021	1
6	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	2,001.34	05/2013	02/2022	05/2022	3
7	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR IOCL	1,823.00	3,027.90	03/2021	12/2021	03/2022	3
8	LPG TERMINAL AT KOCHI IOCL	607.06	1,236.00	10/2017	03/2022	09/2022	6
9	ETHYLENE GLYCOL PROJECT AT PARADIP IOCL	5,654.00	5,654.00	10/2021	10/2021	07/2022	9
	<u>POWER</u>						
10	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	10,566.00	07/2012	10/2021	11/2021	1
	<u>RAILWAYS</u>						
11	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	10/2021	11/2021	1

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above							(October 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
12	ROURKELA JHARSUGUDA THIRD LINE 101 KM SER	969.83	1,312.96	03/2020	02/2022	03/2022	1
13	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) MRTD	495.44	2,980.41	03/2004	03/2022	06/2022	3
14	NANGALDAM-TALWARA(NL),NR NR	450.00	2,017.96	07/2012	03/2024	11/2024	8
15	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,122.00	N.A.	09/2021	12/2022	15
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
16	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	10/2021	11/2021	1
17	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAI	1,532.62	2,499.00	03/2021	04/2021	07/2021	3
18	PUNE-SATARA(NH-4) NHAI PPP (BOT)	1,724.55	1,724.55	03/2013	09/2021	03/2022	6

TABLE-35

Sector wise analysis of projects Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	704,68.00	80,348.00	62,664.37
CIVIL AVIATION	5	7,613.90	81,68.90	8,303.90	2,232.59
COAL	31	1,15,154.25	1,175,17.97	1,20,003.52	43,342.62
MINES	1	5,540.00	64,35.90	5,540.00	988.67
STEEL	5	24,006.86	304,21.86	30,839.01	23,754.50
PETROLEUM	59	3,03,883.67	3,262,75.11	3,14,979.30	1,01,628.54
POWER	37	1,95,373.11	2,552,49.40	2,55,798.01	1,68,491.64
HEAVY INDUSTRY	1	1,718.00	37,27.30	3,727.30	3,522.74
HEALTH AND FAMILY WELFARE	4	6,160.00	61,60.00	6,531.00	1,405.62
RAILWAYS	152	3,92,533.76	5,005,35.26	6,21,279.34	2,37,278.02
ROAD TRANSPORT AND HIGHWAYS	150	2,29,558.56	2,346,95.48	2,40,947.63	1,64,039.69
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,940.64
TELECOMMUNICATIONS	1	13,334.00	246,64.00	24,664.00	20,545.00
URBAN DEVELOPMENT	22	2,74,372.14	2,833,99.27	2,96,243.00	1,48,666.05
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	18,317.91
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	1,007.93
DPIIT	2	17,352.09	173,52.09	18,990.30	12,587.76
Grand total	477	16,70,459.77	19,46,472.43	20,90,376.99	10,12,414.29


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	1,02,371.04	1,48,846.18	45.40	6	39,547.65	93,530.51	24 - 180
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	41,170.76	23.74	4	4,630.48	7,098.21	12 - 48
4	BIHAR	29	91,524.56	1,25,846.81	37.50	7	29,343.85	54,808.38	36 - 141
5	GUJARAT	23	87,132.33	97,557.24	11.96	7	26,970.60	36,926.57	3 - 74
6	HARYANA	13	51,125.78	52,305.78	2.31	0	0.00	0.00	-
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	18	54,648.17	66,583.30	21.84	4	29,931.16	36,153.21	36 - 264
10	KERALA	9	24,577.63	28,764.08	17.03	2	1,719.06	2,743.24	32 - 59
11	MADHYA PRADESH	20	40,080.22	48,043.50	19.87	8	12,194.36	20,127.92	12 - 48
12	MAHARASHTRA	45	1,30,458.47	1,56,360.61	19.85	12	41,761.00	64,118.58	8 - 219
13	MANIPUR	2	5,032.79	13,575.20	169.74	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	120 - 120
16	NAGALAND	2	6,600.52	10,921.64	65.47	1	2,326.52	6,647.64	132 - 132
17	ODISHA	36	95,620.70	1,02,819.52	7.53	9	13,130.22	20,197.11	21 - 204
18	PUNJAB	7	8,647.82	9,958.16	15.15	0	0.00	0.00	-
19	RAJASTHAN	14	31,155.16	37,300.84	19.73	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	27	1,01,563.30	1,20,154.29	18.30	6	10,455.67	20,543.00	27 - 145
22	UTTAR PRADESH	42	1,16,619.62	1,21,373.57	4.08	6	23,356.71	25,545.80	12 - 39
23	WEST BENGAL	24	46,173.48	62,979.44	36.40	6	14,041.95	20,771.30	60 - 324
24	DELHI	8	75,922.38	77,028.97	1.46	2	5,992.21	7,178.00	29 - 29
25	CHHATISGARH	17	65,860.61	75,619.96	14.82	5	24,001.00	33,261.43	18 - 80
26	JHARKHAND	14	59,480.43	63,628.76	6.97	2	21,330.91	22,643.79	51 - 188
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	4	23,343.06	37,269.44	3 - 138
28	TELANGANA	6	19,991.02	22,312.36	11.61	2	11,759.46	12,371.44	23 - 168
29	MULTI STATE	56	3,20,940.13	4,28,221.25	33.43	25	69,612.13	1,19,060.89	12 - 276
Total		477	16,70,459.77	20,90,376.99	25.14	126	4,40,011.04	7,43,771.08	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

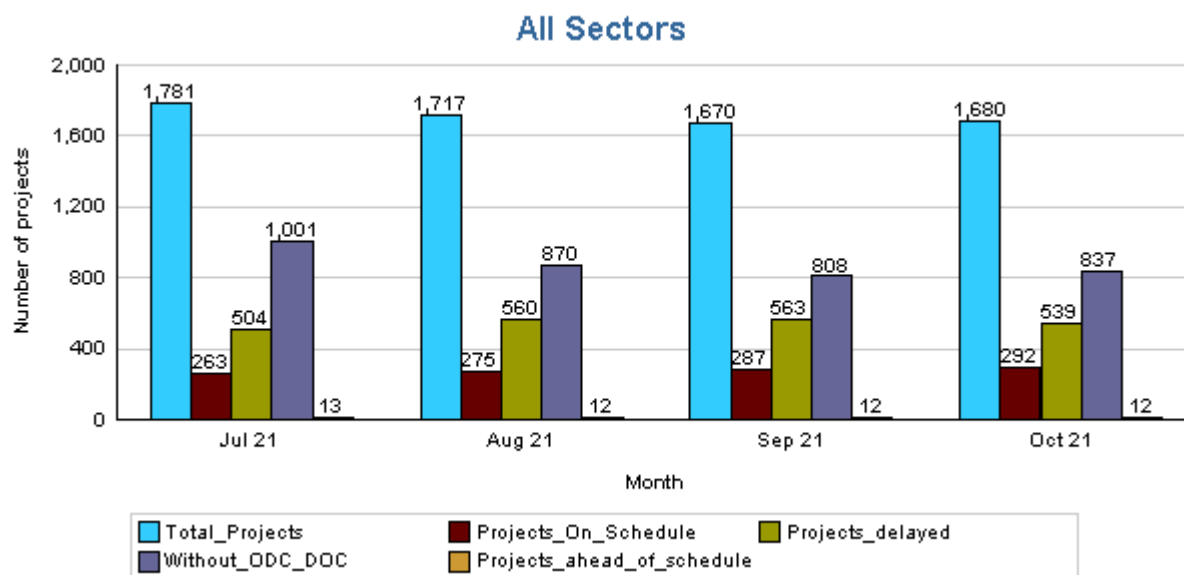

Break-up of 539 Delayed projects in October 2021

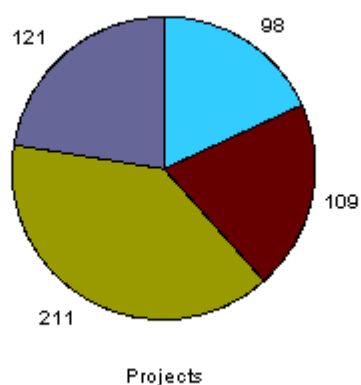


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of ATOMIC ENERGY Sector

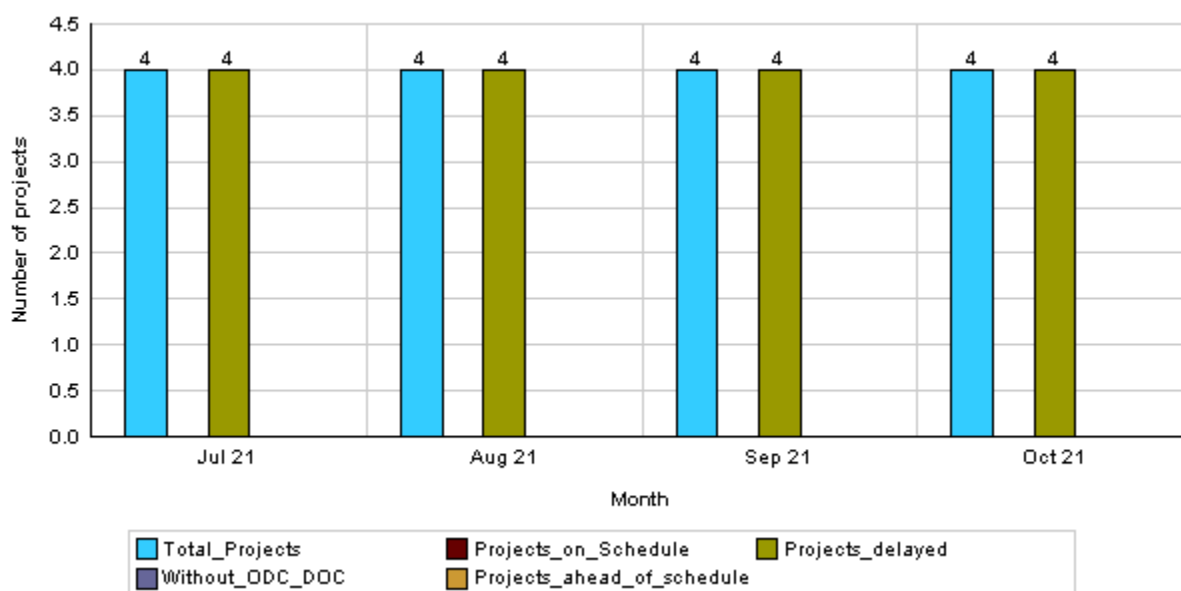


Break-up of 4 Delayed projects in October 2021

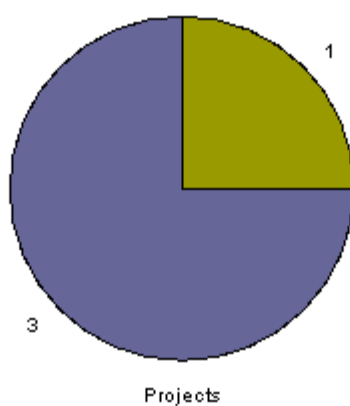


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	0	1	3

Graphical Presentation of HOME AFFAIRS Sector

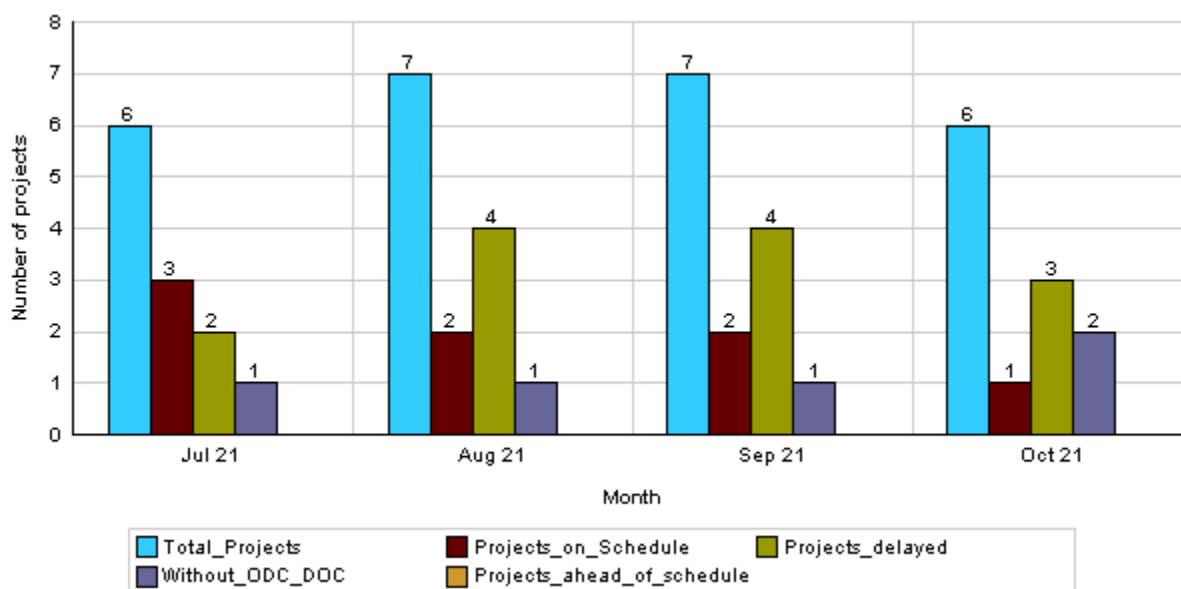


Break-up of 3 Delayed projects in October 2021

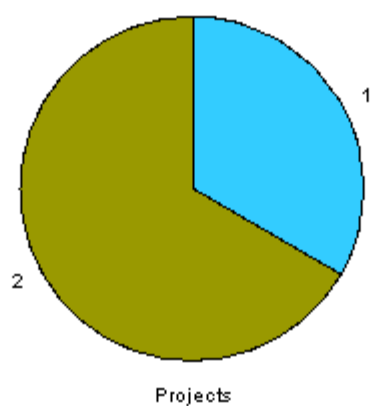


Delay in Months

Graphical Presentation of DEPARTMENT OF HIGHER EDUCATION Sector

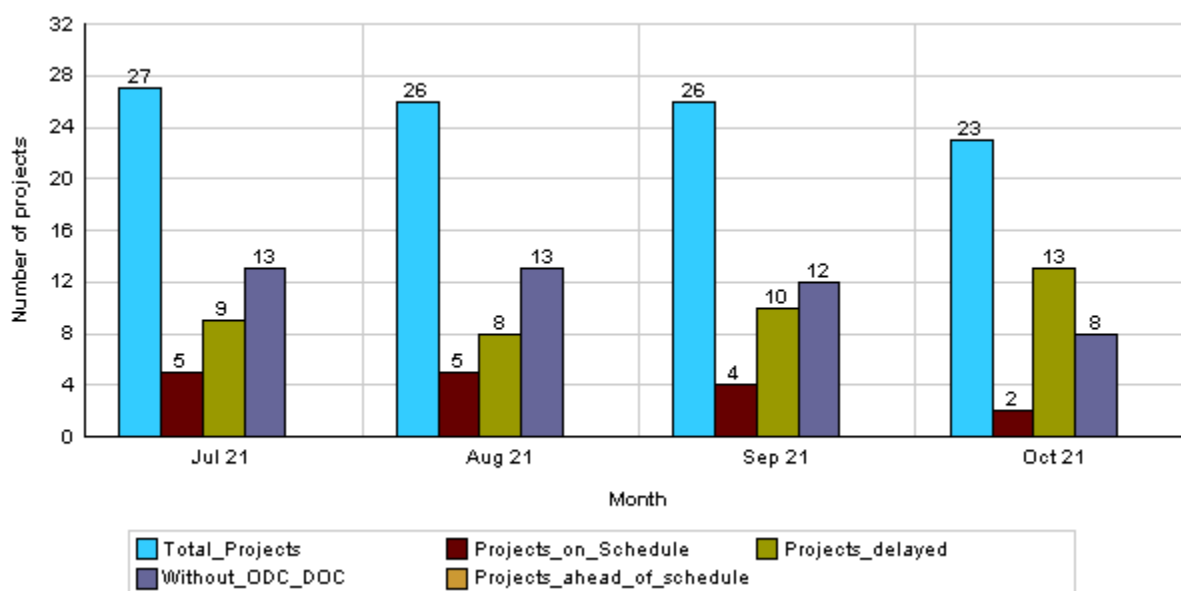


Break-up of 13 Delayed projects in October 2021

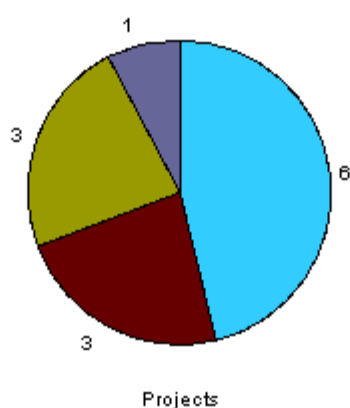

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

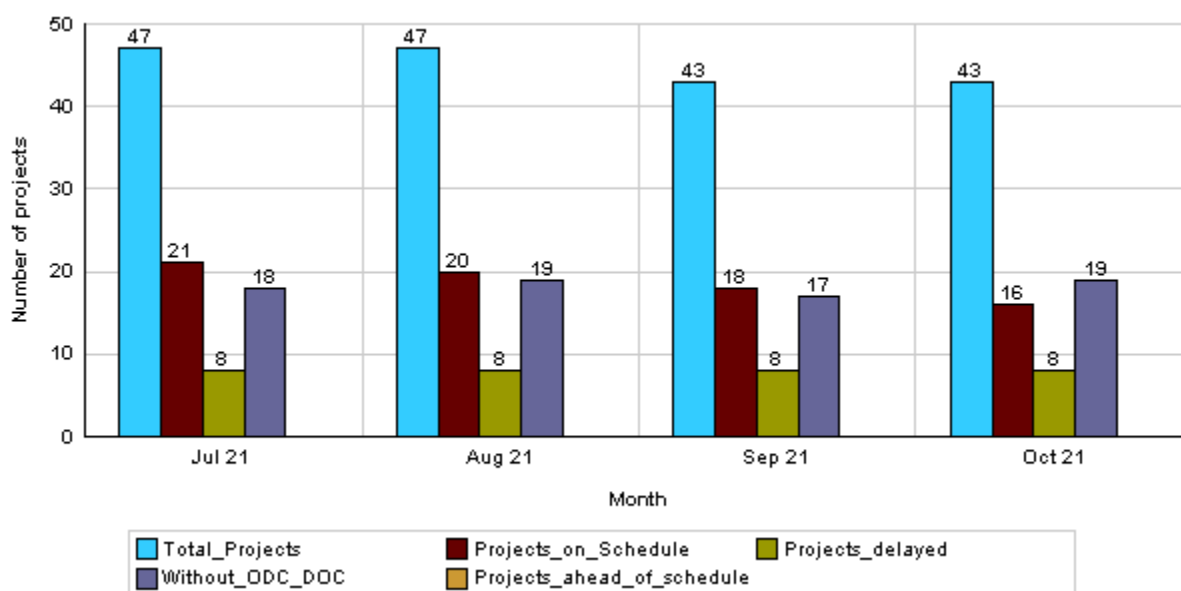


Break-up of 8 Delayed projects in October 2021




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	6	1	1	0

Graphical Presentation of URBAN DEVELOPMENT Sector

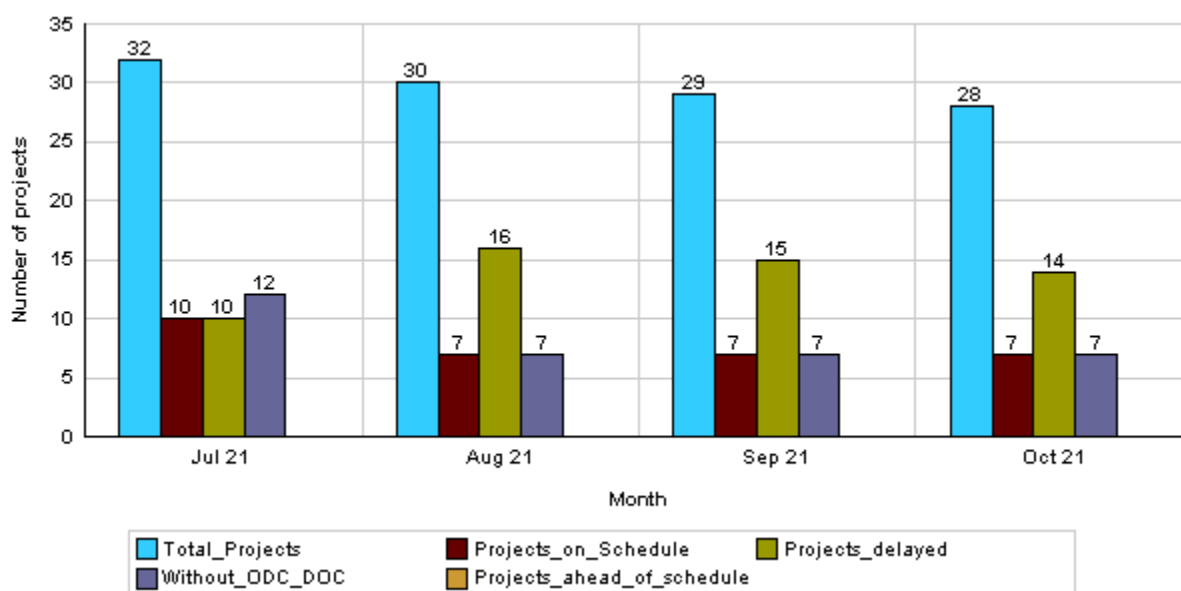


Break-up of 14 Delayed projects in October 2021

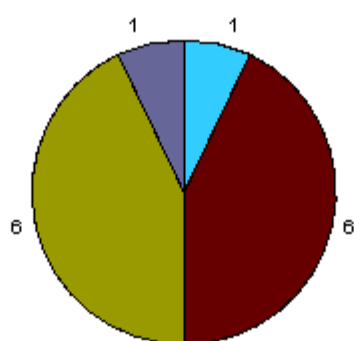


Projects

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of TELECOMMUNICATIONS Sector

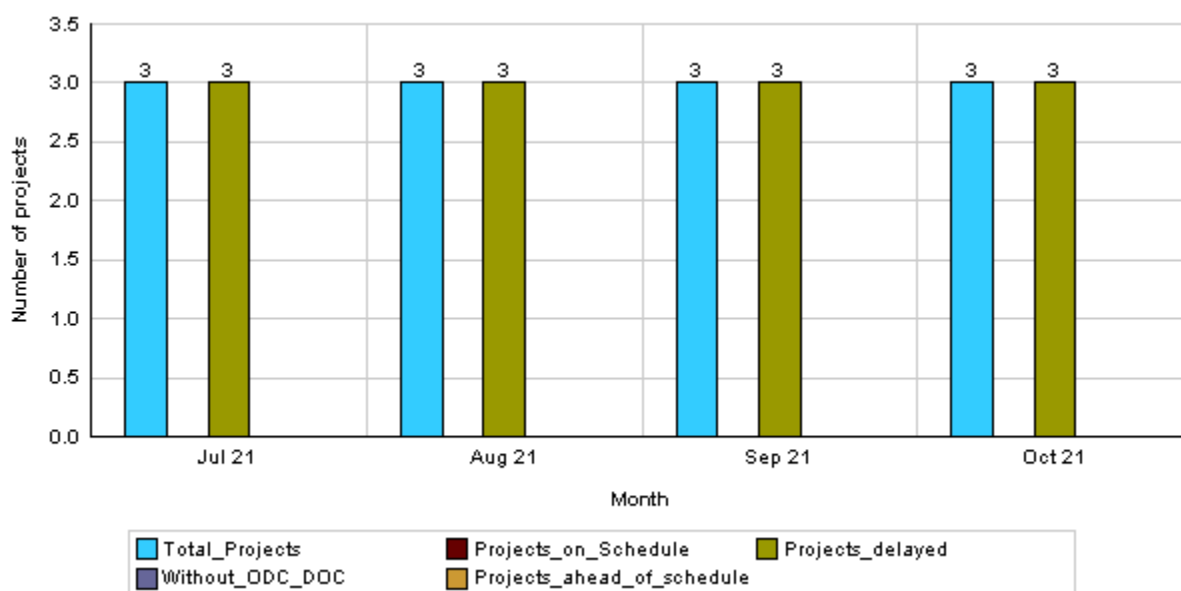


Break-up of 3 Delayed projects in October 2021

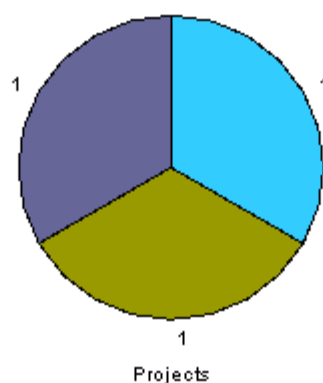


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

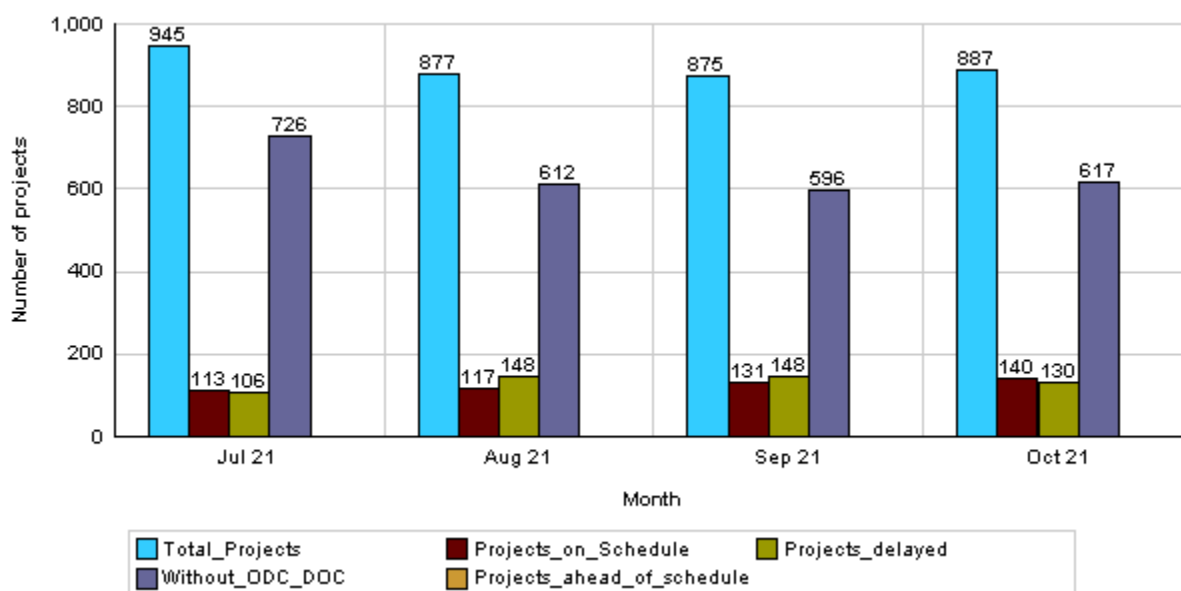


Break-up of 130 Delayed projects in October 2021

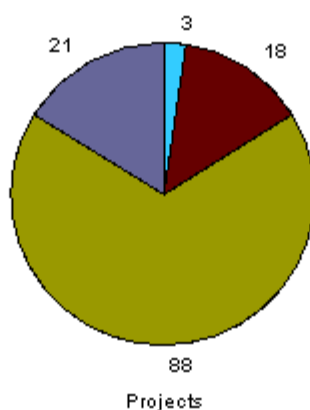


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

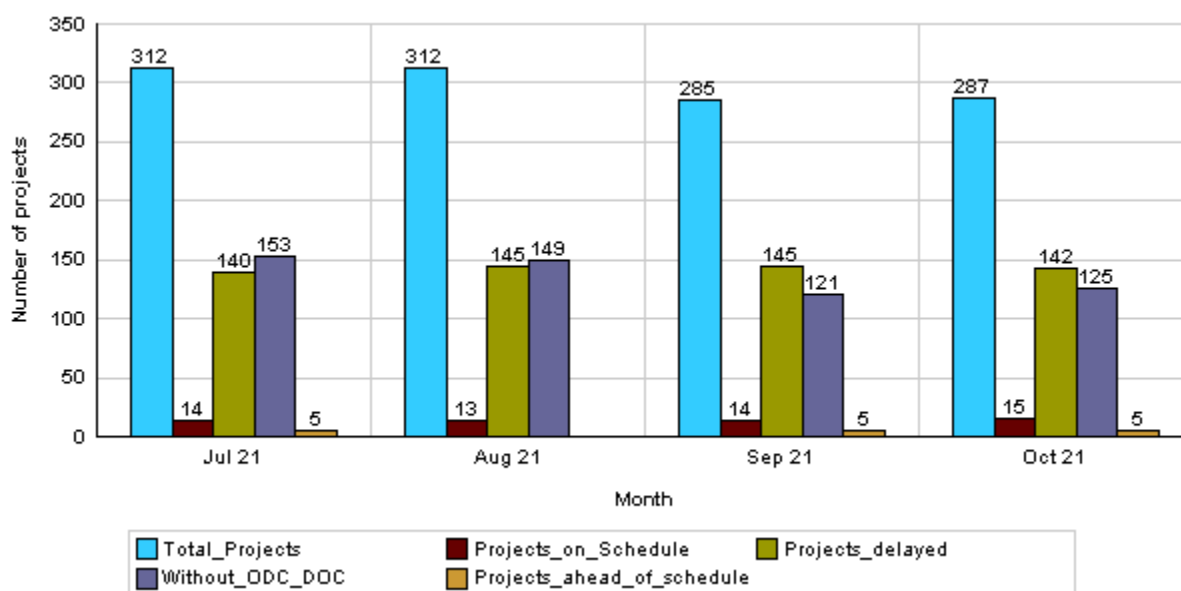


Break-up of 142 Delayed projects in October 2021

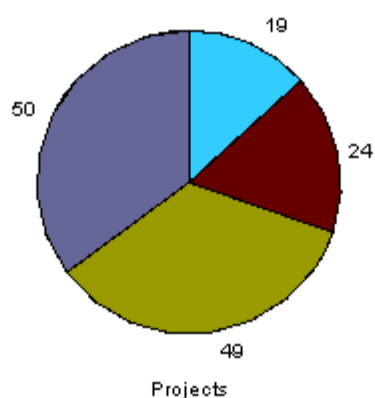


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

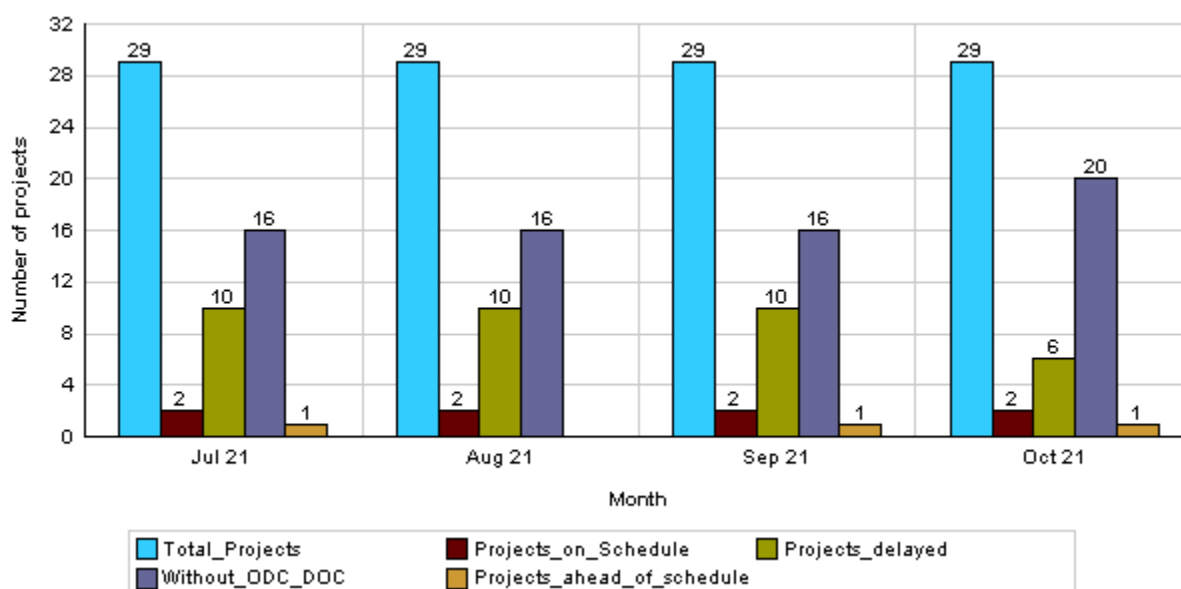


Break-up of 6 Delayed projects in October 2021

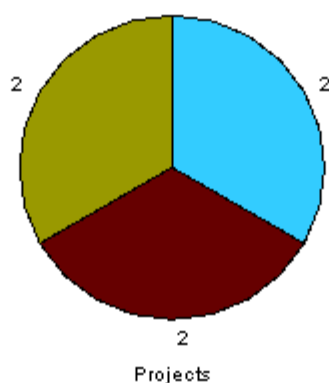


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

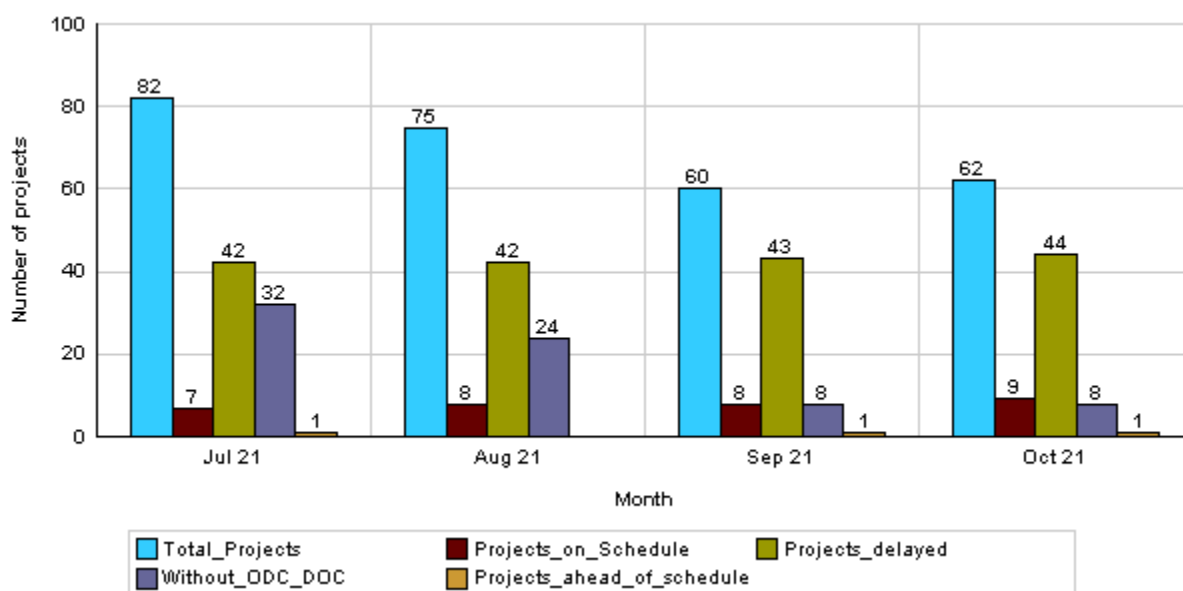


Break-up of 44 Delayed projects in October 2021

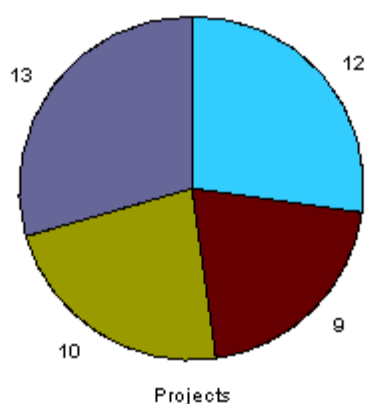


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

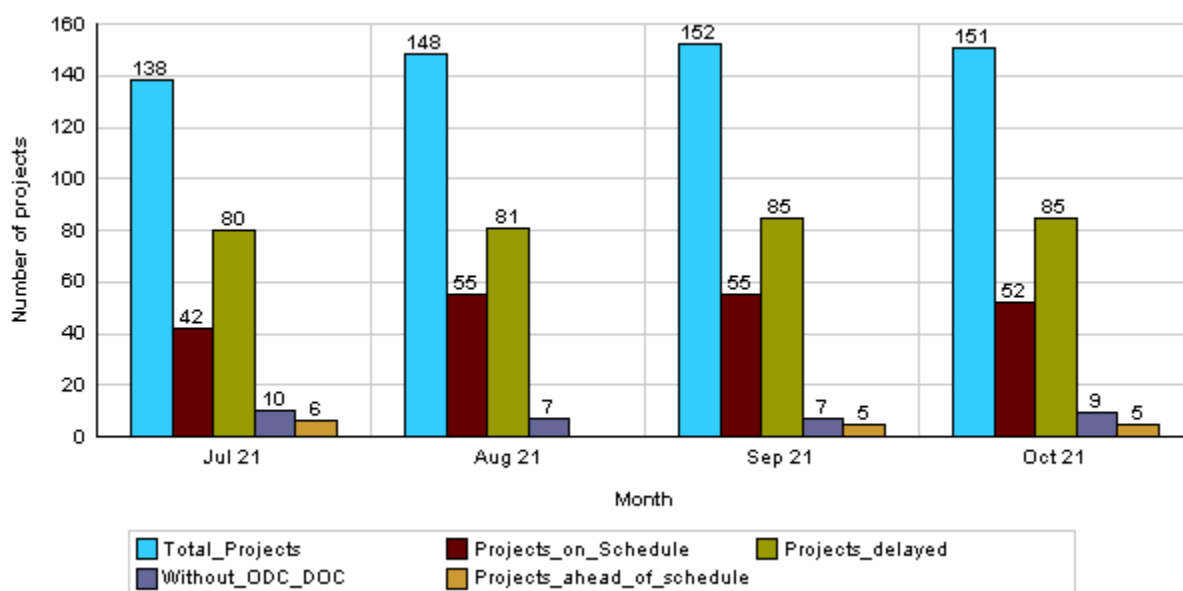


Break-up of 85 Delayed projects in October 2021

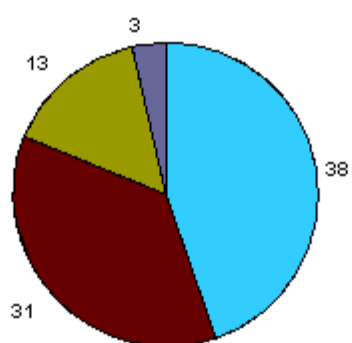


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	38			
13-24		31		
25-60			13	
MORE THAN 60				3

Graphical Presentation of STEEL Sector

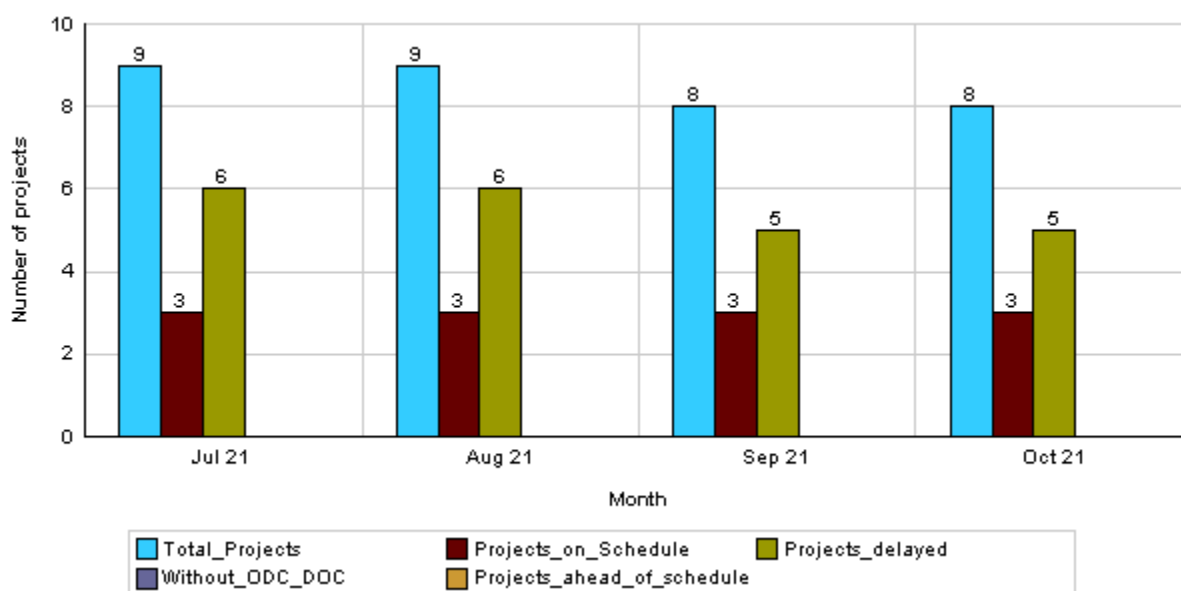


Break-up of 5 Delayed projects in October 2021

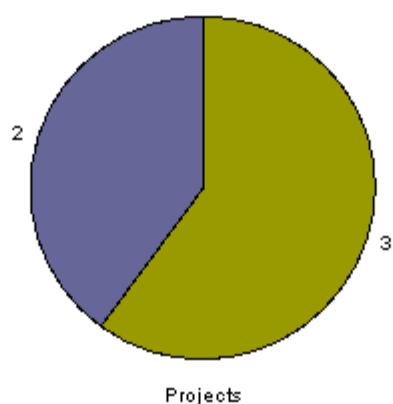

Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Dark Blue)

Graphical Presentation of MINES Sector

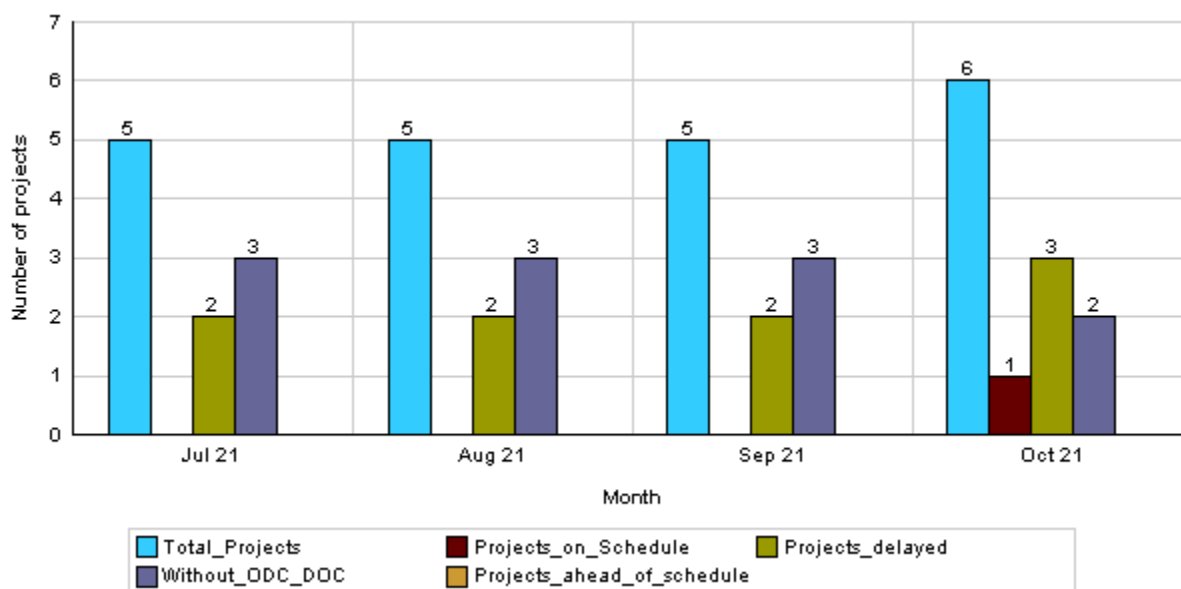


Break-up of 3 Delayed projects in October 2021




Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of FERTILISERS Sector

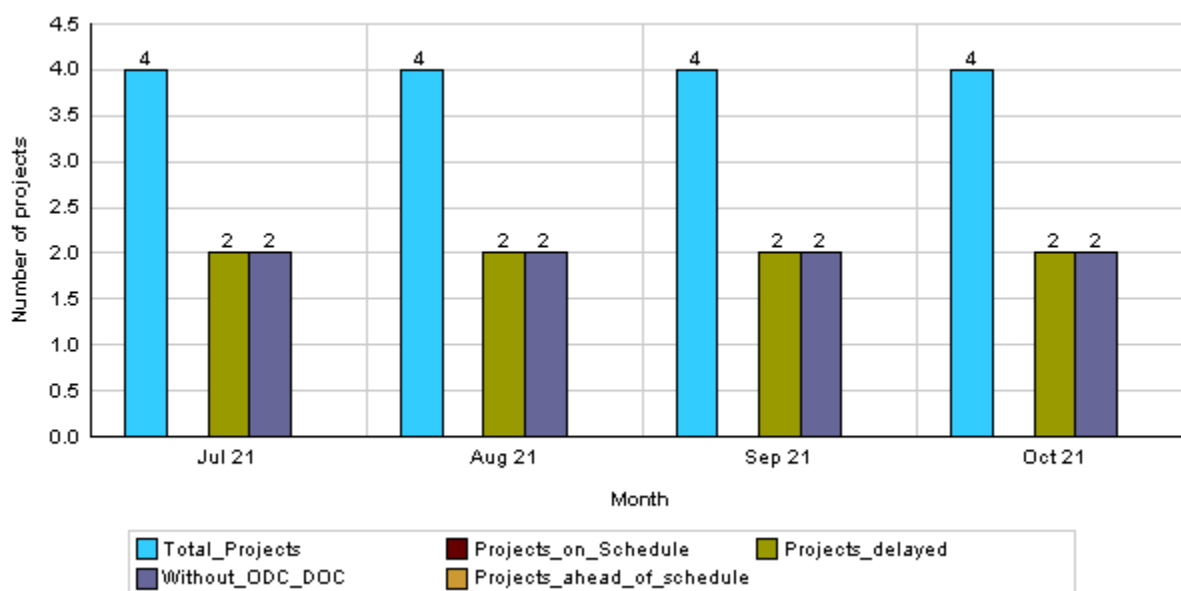


Break-up of 2 Delayed projects in October 2021

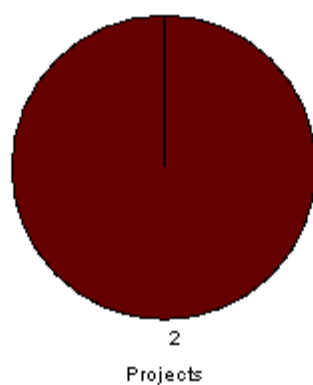


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	1	0	0

Graphical Presentation of COAL Sector

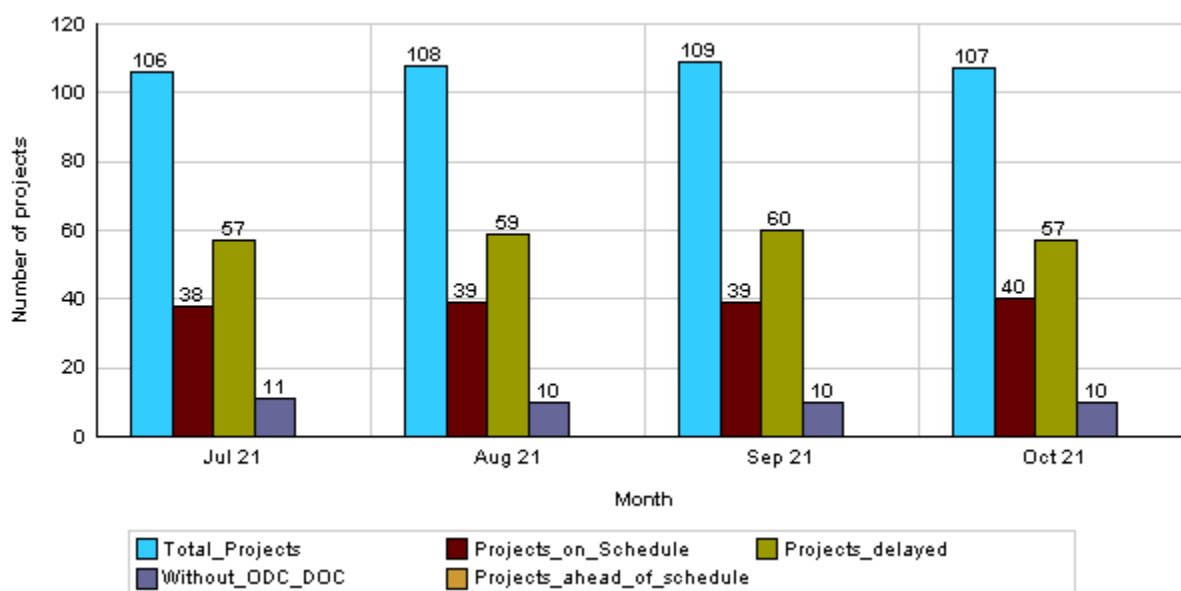


Break-up of 57 Delayed projects in October 2021

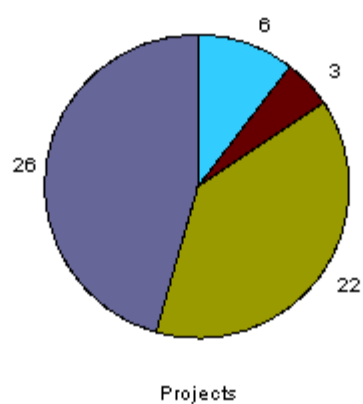


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

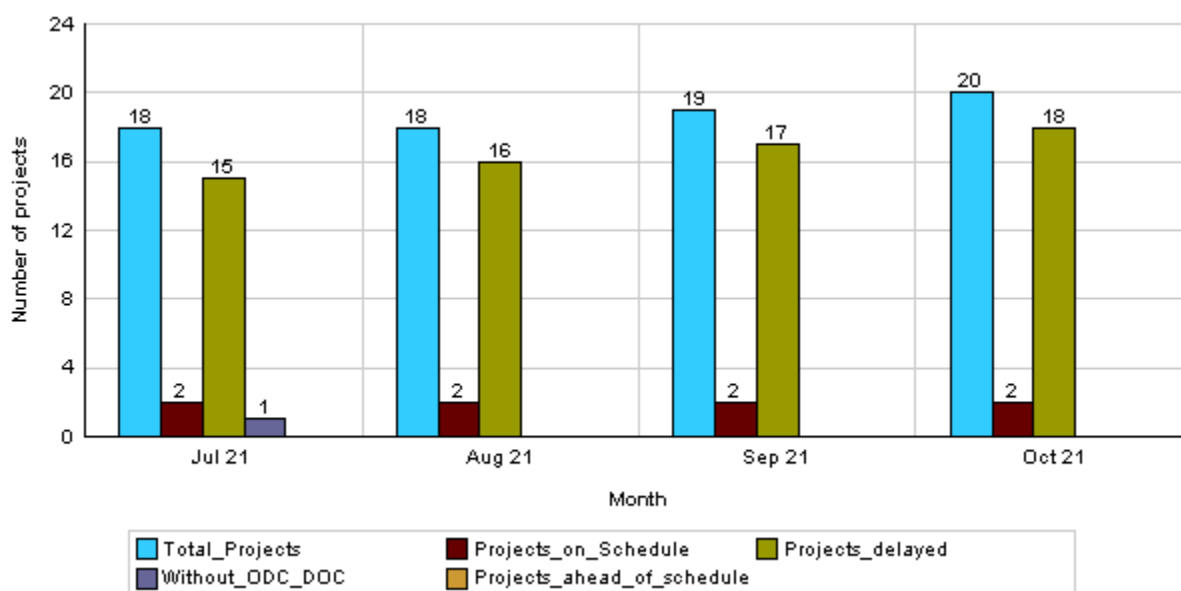

Break-up of 18 Delayed projects in October 2021

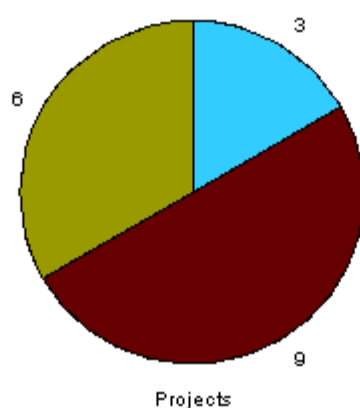

Delay in Months

Legend: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00	16,580.00	17,298.00	12/2015	02/2022	74(O)	63/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00	17,079.00	13,709.00	12/2016	03/2023	75(O)	52/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00	6,840.00	6,054.37	09/2010	10/2022	145(O)	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT- 3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00	39,849.00	25,603.00	11/2020	11/2023	36(O)	28/76
	Total		67,120.00	80,348.00	62,664.37				226/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23	707.73	476.54	09/2018	06/2022	45(O)	0/6
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10	177.10	104.49	02/2020	05/2022	27(O)	1/4
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80	611.80	52.08	03/2023	03/2023	0(O)	4/14
8	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH ,	02/2019	645.63	645.63	.00	08/2022	11/2022	3(O)	0/0
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00	1,232.00	371.33	03/2021	03/2023	24(O)	0/1
10	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90	1,216.90	229.22	10/2022	12/2023	14(O)	0/3
11	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80	303.80	189.25	04/2020	06/2022	26(O)	0/0
12	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00	1,405.00	368.21	08/2022	03/2023	7(O)	1/15
13	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH ,	07/2018	346.27	480.33	114.59	09/2021	12/2022	15(O)	2/4
14	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24	412.24	212.35	06/2021	12/2022	18(O)	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	169.84	04/2021 -	08/2022	16(O) -	3/10
16	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	728.99	02/2022 -	12/2023	22(O) -	0/12
17	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	477.10	10/2021 -	10/2022	12(O) -	3/14
18	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	15.41	03/2022 12/2023	12/2023	21(O) 0	3/14
19	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	81.41	05/2022 -	05/2022	0(O) -	0/4
20	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	402.00	390.15	06/2019 10/2021	11/2021	29(O) 1	0/1
21	CCS INTERNATIONAL AIRPORT -LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 1,938.00	1,988.00	534.84	09/2021 -	12/2023	27(O) -	0/2
22	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	314.79	09/2020 -	09/2022	24(O) -	1/1
23	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	157.18	03/2020 06/2022	04/2022	25(O) -2	0/2
24	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	199.30	11/2021 01/2023	01/2023	14(O) 0	0/2
	Total		14,431.97 -	15,510.25	5,187.07				18/110
	<u>COAL</u>								
25	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,639.30	03/2023 03/2016	03/2023	0(O) 0	15/21
26	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	3,118.22	03/2023 -	03/2023	0(O) -	13/22
27	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023	0(O) -	1/12
28	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	199.99	03/2015 03/2020	03/2022	84(O) 0	9/11
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	11.37	03/2014 -	03/2026	144(O) -	3/9
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	210.73	03/2014 -	03/2023	108(O) -	5/6
31	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	160.43	03/2022 -	03/2022	0(O) -	4/11
32	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60(O) -	1/7
33	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	146.27	03/2020 -	03/2023	36(O) -	3/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
34	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36(O) -	2/12
35	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2027	36(O) -	2/6
36	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	76.12	03/2026 -	03/2026	0(O) -	2/2
37	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	40.57	03/2026 -	03/2026	0(O) -	2/4
38	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	3/5
39	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	314.88	03/2029 -	03/2029	0(O) -	0/0
40	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	185.35	03/2024 -	03/2024	0(O) -	0/0
41	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
42	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	2,025.60	03/2029 -	03/2029	0(O) -	0/0
43	MAGADH EXPANSION OC(51 MTY) - [N06000015]JCLL,JHARKHAND ,	08/2008	6,964.33 7,254.37	7,254.37	729.50	07/2012 03/2028	03/2028	188(O) 0	7/7
44	CHURI BENTI UG (0.81 MTY) - [N06000083]JCLL,JHARKHAND ,	08/2007	163.51 -	163.51	124.85	03/2011 -	03/2022	132(O) -	7/7
45	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCLL,JHARKHAND ,	12/2009	510.85 -	510.85	497.97	03/2016 -	03/2022	72(O) -	7/7
46	KARMA OCP (1.0MTY) - [N06000088]JCLL,JHARKHAND ,	06/2009	162.46 -	162.46	89.46	03/2014 -	03/2022	96(O) -	7/7
47	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	69.37	04/2014 -	04/2023	108(O) -	4/7
48	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	501.39	04/2015 -	02/2023	94(O) -	2/6
49	RECAST EPR AMRAPALI OC - [N06000103]JCLL,JHARKHAND ,	02/2012	4,983.58 4,983.58	4,983.58	360.01	03/2020 03/2028	03/2028	96(O) 0	8/8
50	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2022	12(O) -	0/2
51	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	285.81	05/2014 -	12/2021	91(O) -	0/8
52	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	211.94	04/2014 -	04/2020	-	0/10
53	HURA - C OC (3 MTY) - [N06000143]JCLL,JHARKHAND ,	10/2015	359.69 -	359.69	257.70	03/2022 -	03/2022	0(O) -	4/22
54	CHITRA EAST (RCE) OCP - [N06000169]JCLL,JHARKHAND ,	08/2018	513.98 -	513.98	159.28	03/2024 -	03/2024	0(O) -	0/17
55	NORTH URIMARI EXPANSION OCP - [N06000182]JCLL,JHARKHAND ,	03/2019	1,553.06 -	778.80	349.76	03/2023 -	03/2023	0(O) -	2/2
56	TETARIAKHAR EXPANSION OCP - [N06000186]JCLL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	37.16	03/2023 -	03/2023	0(O) -	1/1
57	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	37.13	08/2022 -	09/2023	13(O) -	5/11
58	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	24.86	04/2018 -	10/2022	54(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
59	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	1,186.64	234.04	03/2023 -	03/2026	36(O) -	6/11
60	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2027	48(O) -	3/10
61	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.65	03/2021 04/2024	04/2024	37(O) 0	4/10
62	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	66.57	03/2021 -	03/2024	36(O) -	5/9
63	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	1.78	03/2022 -	03/2025	36(O) -	1/10
64	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	127.49	03/2021 -	03/2022	12(O) -	4/6
65	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	281.25 -	281.25	18.24	03/2022 03/2026	03/2026	48(O) 0	0/4
66	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	825.70	03/2021 -	03/2022	12(O) -	4/9
67	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	316.50	03/2022 -	03/2023	12(O) -	4/9
68	SEMARIA OPENCASST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
69	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
70	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	1.00	03/2026 -	03/2026	0(O) -	1/7
71	BLOCK-B EXPANSION OPENCASST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	1/7
72	NIGAHU EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
73	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL,MADHYA PRADESH ,	03/2021	496.28 -	496.28	.00	03/2028 -	03/2028	0(O) -	0/0
74	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA ,	11/2014	1,184.33 -	1,184.33	392.88	03/2020 03/2027	03/2027	84(O) 0	5/13
75	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	86.90	03/2023 -	03/2023	0(O) -	7/11
76	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 299.67	299.67	164.36	03/2019 03/2022	03/2022	36(O) 0	10/13
77	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 745.03	745.03	390.11	03/2025 -	03/2025	0(O) -	9/13
78	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 333.43	333.43	145.08	03/2023 -	03/2024	12(O) -	4/10
79	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA ,	11/2015	313.34 -	313.34	149.32	03/2021 03/2024	03/2024	36(O) 0	5/6
80	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA ,	11/2015	851.60 826.80	826.80	233.76	03/2020 03/2026	03/2026	72(O) 0	2/6
81	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 327.41	327.41	160.84	03/2019 -	03/2022	36(O) -	6/8
82	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 402.90	402.90	336.00	03/2020 09/2022	09/2022	30(O) 0	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
83	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	217.47	03/2021 09/2022	09/2022	18(O) 0	1/4
84	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	103.38	03/2021 09/2022	09/2022	18(O) 0	0/3
85	GHONSA EXPANSION DEEP OC - [N06000205]WCL,MAHARASHTRA ,	03/2021	241.72 -	241.72	57.00	03/2028 -	03/2028	0(O) -	0/7
86	SASTI EXPANSION OC - [N06000206]WCL,MAHARASHTRA ,	08/2020	371.59 -	371.59	52.55	03/2026 -	03/2026	0(O) -	0/7
87	DHUPTALA OC(SASTI UG TO OC) - [N06000209]WCL,MAHARASHTRA ,	02/2019	720.87 -	720.87	9.86	03/2028 -	03/2028	0(O) -	0/0
88	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 404.45	404.45	246.02	03/2022 -	03/2022	0(O) -	0/3
89	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	289.29 -	289.30	36.10	03/2022 03/2025	03/2025	36(O) 0	2/12
90	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	296.56	03/2021 09/2023	09/2023	30(O) 0	4/6
91	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
92	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	3,145.45 -	3,145.45	637.17	03/2017 -	03/2031	168(O) -	11/12
93	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	8,416.19 8,416.19	8,416.19	941.90	03/2013 03/2028	03/2028	180(O) 0	8/10
94	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA ,	12/2007	3,504.21 3,504.21	3,504.21	589.86	03/2010 03/2029	03/2029	228(O) 0	3/5
95	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	204.33	03/2012 -	03/2021	-	5/7
96	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	708.55	729.73	03/2013 -	03/2024	132(O) -	6/9
97	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	240.64	03/2019 -	03/2024	60(O) -	3/9
98	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	2,558.11	03/2026 -	03/2026	0(O) -	9/15
99	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	659.30	03/2021 -	09/2025	54(O) -	9/10
100	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	598.36	03/2027 -	03/2027	0(O) -	3/12
101	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,282.18	03/2029 -	03/2029	0(O) -	1/9
102	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	898.53	07/2020 -	04/2020	-	18/22
103	NAINI COAL MINE - [N06000203]SCCL,ODISHA ,	03/2020	494.30 -	494.30	76.43	03/2024 -	03/2024	0(O) -	0/7
104	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
105	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
106	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	93.05	09/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	143.95	09/2020 -	-	-	0/0
108	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,417.83	12/2015 -	02/2021	-	35/35
109	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	496.17	06/2015 03/2025	03/2025	117(O) 0	5/7
110	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
111	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84(O) -	4/5
112	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	293.69	03/2015 -	03/2022	84(O) -	14/29
113	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	183.12	03/2015 -	03/2023	96(O) -	10/13
114	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	135.30	07/2016 -	03/2022	68(O) -	26/28
115	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	213.44	03/2016 -	09/2021	-	38/39
116	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	112.99	03/2019 -	03/2022	36(O) -	17/18
117	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	206.41	03/2019 -	03/2022	36(O) -	6/11
118	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	- -	03/2022	- -	2/6
119	GODAVARIKHANI COAL MINE - [N06000202]SCCL,TELANGANA ,	07/2019	438.98 -	438.98	80.04	03/2023 -	03/2023	0(O) -	0/11
120	VENKATESH KHANI COAL MINE - [N06000204]SCCL,TELANGANA ,	10/2020	484.51 -	484.51	25.43	03/2023 -	03/2023	0(O) -	0/8
121	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	12,656.73	11/2021 11/2022	11/2022	12(O) 0	18/48
122	KHADIA EXPANSION OCP - [N06000208]NCL,UTTAR PRADESH ,	06/2021	491.67 -	491.67	.00	03/2025 -	03/2025	0(O) -	0/5
123	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	1,210.12 -	1,210.12	49.04	03/2022 03/2029	03/2029	84(O) 0	9/13
124	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	690.16	03/2018 -	03/2029	132(O) -	12/16
125	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	622.22	08/2019 -	08/2024	60(O) -	1/19
126	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.75	03/2026 -	03/2026	0(O) -	4/22
127	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	18.15	03/2029 -	03/2029	0(O) -	2/22
128	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	2.70	03/2027 -	03/2027	0(O) -	2/27
129	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.19	03/2027 -	03/2027	0(O) -	0/22
130	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	6.82	03/2025 -	03/2025	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	73.17	03/2017 -	10/2022	67(O) -	0/0
	Total		1,49,691.71 -	1,54,295.46	53,610.91				490/1030
	<u>FINANCE</u>								
132	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU ,	12/2015	209.00 -	208.96	205.75	10/2019 -	07/2021	-	1/6
133	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU ,	11/2017	348.77 -	348.77	189.00	11/2021 -	11/2021	0(O) -	3/8
	Total		557.77 -	557.73	394.75				4/14
	<u>FERTILISERS</u>								
134	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	172.93	11/2019 06/2021	10/2021	23(O) 0	0/2
135	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	314.91	04/2020 10/2021	10/2021	18(O) 0	14/14
136	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	194.79	11/2019 05/2021	-	-	1/2
137	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	204.09	11/2019 05/2021	-	-	1/2
	Total		1,101.28 -	1,101.28	886.72				16/20
	<u>MINES</u>								
138	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	988.67	04/2021 01/2024	01/2024	33(O) 13	4/4
139	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	391.52	01/2020 -	-	-	3/3
140	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	95.45	11/2020 -	12/2023	37(O) -	3/3
141	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	6.91	04/2021 12/2023	12/2023	32(O) 9	2/2
142	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2021	12/2020	-	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
143	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART DG GSI AT SECTOR-V SA - [N1000015]CPWD,WEST BENGAL , EPC	04/2019	255.37 -	255.37	.86	04/2022 -	04/2022	0(O) -	0/0
	Total		7,333.99 -	7,330.54	1,618.41				13/13
	<u>STEEL</u>								
144	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,858.00	2,004.81	12/2017 07/2022	07/2022	55(O) 0	5/6
145	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	19,016.02	05/2015 01/2022	01/2022	80(O) 0	71/86
146	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	70.05	12/2023 -	12/2023	0(O) -	0/0
147	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	439.00	06/2023 -	06/2023	0(O) -	1/8
148	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	557.75	10/2017 12/2021	11/2022	61(O) 0	0/2
149	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	207.19	06/2019 10/2021	12/2021	30(O) 2	1/1
150	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	44.29	05/2023 -	05/2023	0(O) -	0/1
151	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	2,100.00	1,736.92	09/2018 11/2021	11/2021	38(O) 1	5/5
	Total		25,189.15 -	32,021.30	24,076.03				83/109
	<u>PETROLEUM</u>								
152	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	16,536.13	07/2020 07/2022	07/2022	24(O) 0	95/111
153	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	14,210.03	06/2020 06/2022	06/2022	24(O) 0	15/20
154	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	291.62	04/2021 03/2021	03/2021	-	0/0
155	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	290.69	04/2021 -	12/2021	8(O) -	0/0
156	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	124.99	04/2022 -	02/2023	10(O) -	0/0
157	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	130.90	10/2021 03/2022	03/2022	5(O) 0	0/0
158	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	242.18	02/2021 -	03/2023	25(O) -	0/16
159	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	104.54	07/2020 -	01/2022	18(O) -	1/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
160	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	10.81	07/2022 -	01/2023	6(O) -	0/0
161	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	28.57	11/2022 -	11/2022	0(O) -	0/0
162	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	216.34	03/2021 -	10/2021	7(O) -	0/0
163	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	125.01	08/2021 -	03/2022	7(O) -	0/0
164	CGD PROJECT AT SRIKAKULAM VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH ,	06/2019	2,880.00 -	2,880.00	104.89	08/2027 -	08/2027	0(O) -	0/0
165	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	502.00	444.35	08/2019 06/2021	05/2021	-	11/13
166	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 303.75	303.75	222.27	05/2020 08/2021	11/2021	18(O) 0	4/5
167	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 652.10	638.60	395.08	02/2020	12/2021	22(O) -	1/14
168	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	556.96	02/2020 06/2021	11/2021	21(O) 0	5/5
169	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 222.21	198.00	183.20	08/2020 09/2021	12/2021	16(O) 3	0/0
170	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 18,968.00	18,968.00	648.35	10/2024 -	10/2024	0(O) -	0/0
171	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 9,058.00	9,058.00	526.70	10/2024 -	10/2024	0(O) -	0/0
172	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]IOCL,ASSAM ,	05/2021	412.00 -	412.00	25.15	10/2023 -	10/2023	0(O) -	0/0
173	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	157.79	03/2021 09/2021	01/2022	10(O) 0	21/26
174	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	72.98	10/2020 08/2022	08/2022	22(O) 0	2/2
175	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	181.07	10/2022 -	10/2022	0(O) -	10/10
176	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	171.59	01/2021 06/2021	12/2021	11(O) 1	7/8
177	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	376.88	03/2021 12/2021	12/2021	9(O) 0	0/0
178	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	1,620.50	04/2023 -	04/2023	0(O) -	2/2
179	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR ,	06/2020	403.00 -	403.00	94.90	08/2022 -	08/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
180	CGD PROJECT AT AURANGABAD KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR ,	10/2018	176.00 -	176.00	77.52	08/2027 -	08/2027	0(0) -	0/0
181	CGD PROJECT AT ARARIA PURNIA KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR ,	06/2019	988.00 -	988.00	41.60	12/2029 -	12/2029	0(0) -	0/0
182	CGD PROJECT AT ARWAL JEHANABAD BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR ,	06/2019	439.00 -	439.00	119.54	02/2028 -	02/2028	0(0) -	0/0
183	CGD PROJECT AT KHAGARIA SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR ,	06/2019	163.00 -	163.00	24.46	12/2029 -	12/2029	0(0) -	0/0
184	CGD PROJECT AT LAKHISARAI MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR ,	06/2019	347.00 -	347.00	94.78	02/2028 -	02/2028	0(0) -	0/0
185	CGD PROJECT AT MUZAFFARPUR VAISHALI SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR ,	06/2019	2,996.00 -	2,996.00	283.56	02/2028 -	02/2028	0(0) -	0/0
186	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]HPCL,CHHATISGARH , EPC	03/2021	456.00 -	456.00	13.22	03/2024 -	03/2024	0(0) -	4/64
187	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	197.30	04/2018 -	12/2021	44(0) -	19/20
188	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	970.30	947.93	03/2026 -	03/2026	0(0) -	9/10
189	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	345.08	02/2020 10/2021	03/2022	25(0) 5	7/8
190	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 730.20	730.20	157.01	- 05/2023	05/2023	- 0	12/17
191	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 247.90	247.90	47.78	02/2021 -	08/2022	18(0) -	6/8
192	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]ONGC,GUJARAT ,	10/2018	156.67 -	156.67	62.93	03/2021 05/2022	05/2022	14(0) 0	4/6
193	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	181.90	12/2021 -	04/2022	4(0) -	9/11
194	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	552.22	05/2023 -	05/2023	0(0) -	6/11
195	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	166.08	12/2022 -	12/2022	0(0) -	0/0
196	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	115.83	08/2022 -	08/2022	0(0) -	5/6
197	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	796.97	09/2024 -	08/2024	-1(0) -	0/0
198	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT ,	10/2020	1,614.00 -	1,614.00	1.12	08/2023 -	08/2023	0(0) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
199	REDEVELOPMENT OF LINCH FIELD - [N16000428]ONGC,GUJARAT , EPC	04/2021	631.03 -	631.03	217.38	03/2025 -	03/2025	0(O) -	0/2
200	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 340.76	340.76	145.36	02/2020 07/2022	07/2022	29(O) 0	6/7
201	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	924.60	08/2020 04/2022	04/2022	20(O) 0	6/7
202	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	466.82	01/2021 03/2022	03/2022	14(O) 0	3/6
203	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	419.33	02/2020 02/2022	02/2022	24(O) 0	4/5
204	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	223.50	08/2020 05/2021	12/2021	16(O) 0	14/16
205	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	100.38	06/2021 07/2022	07/2022	13(O) 0	3/3
206	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 3,199.60	2,281.94	553.94	12/2022 07/2023	07/2023	7(O) 0	0/0
207	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	298.37	10/2021 -	12/2021	2(O) -	0/0
208	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	16.46	07/2021 03/2022	03/2022	8(O) 0	0/0
209	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	155.75	09/2026 02/2027	02/2027	5(O) 0	38/52
210	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]IOCL,HARYANA ,	02/2021	34,627.00 -	34,627.00	466.97	09/2024 -	09/2024	0(O) -	0/0
211	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	730.57	03/2023 03/2022	03/2022	-12(O) 0	9/10
212	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	111.34	06/2020 -	03/2022	21(O) -	5/12
213	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	133.18	10/2022 -	10/2022	0(O) -	19/19
214	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	136.91	06/2022 -	09/2022	3(O) -	0/0
215	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	105.20	10/2022 -	10/2022	0(O) -	9/9
216	CGD PROJECT AT BOKARO HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND ,	10/2018	613.00 -	613.00	157.77	12/2029 -	12/2029	0(O) -	0/0
217	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,766.26	12/2019 04/2021	02/2022	26(O) 0	9/12
218	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	534.34	03/2020 11/2020	11/2021	20(O) 0	2/3
219	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	155.99	03/2021 -	11/2021	8(O) -	0/15

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
220	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	1,334.00	06/2022 -	06/2022	0(O) -	13/18
221	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	179.41	12/2022 -	12/2022	0(O) -	14/19
222	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	306.50	11/2021 -	03/2022	4(O) -	15/19
223	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 304.00	304.00	2.56	06/2023 01/2024	01/2024	7(O) 5	3/6
224	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 1,236.00	1,236.00	500.28	10/2017 03/2022	09/2022	59(O) 6	44/52
225	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	769.00	06/2019 -	02/2022	32(O) -	0/0
226	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023	0(O) -	0/0
227	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 319.61	319.61	219.15	06/2020 12/2021	12/2021	18(O) 0	0/0
228	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH ,	10/2018	177.00 -	177.00	62.90	02/2027 -	02/2027	0(O) -	0/0
229	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,846.46	2,001.34	1,599.60	05/2013 05/2022	05/2022	108(O) 3	5/8
230	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,884.63	04/2018 05/2022	05/2022	49(O) 0	13/15
231	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,566.92	02/2022 -	02/2022	0(O) -	5/5
232	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	172.42	01/2021 -	09/2021	-	0/0
233	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 437.00	437.00	179.80	01/2021 -	08/2022	19(O) -	0/0
234	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	183.60	01/2021 -	09/2021	-	0/0
235	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,520.44	05/2021 05/2021	05/2021	-	14/15
236	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	183.21	06/2020 -	03/2022	21(O) -	4/12
237	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	2,121.13	05/2021 12/2021	12/2021	7(O) 0	4/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
238	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	1,463.48	03/2022 05/2023	05/2023	14(O) 0	4/6
239	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	3,032.38	05/2021 01/2022	01/2022	8(O) 0	4/6
240	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	06/2019	2,494.68	2,354.72	1,694.11	03/2022 -	03/2022	0(O) -	4/6
241	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	733.86	791.49	12/2020 12/2021	12/2021	12(O) 0	4/5
242	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA ,	07/2020	640.00 -	640.00	357.57	12/2021 -	03/2022	3(O) -	0/0
243	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA ,	08/2020	697.00 -	697.00	256.43	03/2023 -	03/2023	0(O) -	0/0
244	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]GAIL,MAHARASHTRA ,	05/2019	8,797.00 -	8,797.00	228.35	04/2025 -	04/2025	0(O) -	0/0
245	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	2,163.26	03/2021 12/2021	03/2022	12(O) 3	5/5
246	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	3,071.72	12/2020 03/2022	03/2022	15(O) 0	5/5
247	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	596.34	07/2018 05/2021	03/2022	44(O) 5	27/36
248	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	281.34	10/2020 -	03/2022	17(O) -	6/12
249	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	510.00	485.08	12/2019 -	12/2021	24(O) -	6/22
250	LAYING OF VIJAPUR-AURAIYA PIPELINE SECTION OF VIJAPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,652.70	12/2020 -	11/2021	11(O) -	21/24
251	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,166.20	12/2020 12/2021	12/2021	12(O) 0	21/24
252	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	2,129.90	12/2020 12/2021	12/2021	12(O) 0	21/24
253	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,773.40	12/2012 02/2022	02/2022	110(O) 0	26/42
254	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	3,072.00	2,574.63	06/2021 08/2022	07/2022	13(O) 0	18/26
255	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	2,496.20	12/2021 -	12/2021	0(O) -	17/20
256	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	368.60	11/2022 -	11/2022	0(O) -	12/20
257	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	402.90	07/2022 -	07/2022	0(O) -	11/14

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
258	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	337.20	11/2022 -	11/2022	0(O) -	9/12
259	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	1,616.30	05/2023 -	05/2023	0(O) -	12/29
260	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE ,	06/2019	169.00 -	169.00	37.29	12/2029 -	12/2029	0(O) -	0/0
261	CGD PROJECT AT SHEIKHPURA JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE ,	06/2019	303.00 -	303.00	118.98	02/2028 -	02/2028	0(O) -	0/0
262	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,484.70	12/2020 12/2021	12/2021	12(O) 0	20/24
263	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	56.21	12/2019 03/2022	10/2022	34(O) 7	18/26
264	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	151.09	07/2022 -	07/2022	0(O) -	10/10
265	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	223.98	12/2021 08/2021	11/2021	-1(O) 1	3/3
266	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	91.81	07/2022 -	07/2022	0(O) -	9/9
267	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	3,485.97	10/2021 07/2022	07/2022	9(O) 9	9/10
268	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	823.08	10/2021 -	03/2022	5(O) -	1/1
269	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	107.63	09/2021 06/2022	06/2022	9(O) 0	1/5
270	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	2,039.85	08/2021 09/2022	09/2022	13(O) 0	7/11
271	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 427.00	427.00	28.69	09/2022 03/2023	03/2023	6(O) 0	3/8
272	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	283.87	08/2022 -	06/2023	10(O) -	0/21
273	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	28.71	07/2022 -	07/2022	0(O) -	0/0
274	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	373.13	01/2024 -	01/2024	0(O) -	0/0
275	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,421.46	171.55	02/2023 -	02/2023	0(O) -	11/22
276	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	90.20	- 05/2022	12/2022	- 7	17/26
277	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
278	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66(O) 0	0/0
279	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	455.52	03/2019 09/2021	09/2021	-	4/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	4,049.27	12/2018 02/2022	02/2022	38(O) 0	5/5
281	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	156.18	11/2021 -	12/2021	1(O) -	5/5
282	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	305.00	288.20	08/2020 -	12/2021	16(O) -	0/0
283	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	258.36	10/2020 01/2022	01/2022	15(O) 0	0/0
284	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	5.29	09/2023 -	02/2024	5(O) -	0/0
285	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	116.76	12/2023 -	10/2023	-2(O) -	0/0
286	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU ,	10/2018	2,998.00 -	2,998.00	191.16	03/2030 -	03/2030	0(O) -	0/0
287	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU ,	10/2018	1,304.00 -	1,304.00	39.09	03/2030 -	03/2030	0(O) -	0/0
288	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	96.02	04/2022 -	08/2023	16(O) -	0/0
289	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 345.15	345.15	246.25	04/2022 -	04/2022	0(O) -	44/53
290	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	173.55	08/2021 -	11/2022	15(O) -	0/0
291	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	109.97	08/2020 03/2022	03/2022	19(O) 0	1/1
292	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	490.71	08/2022 -	08/2022	0(O) -	3/3
293	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	998.48	12/2021 -	12/2021	0(O) -	0/21
294	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	369.06	03/2029 08/2029	08/2029	5(O) 0	28/64
295	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 217.92	217.92	101.80	04/2021 -	03/2022	11(O) -	12/14
296	60 KTA POLYPROPYLENE PROJECT - [N16000429]GAIL,UTTAR PRADESH ,	03/2019	910.56 -	910.56	105.31	04/2024 -	04/2024	0(O) -	0/0
297	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	104.05	02/2020 06/2021	06/2022	28(O) 8	19/26
298	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	939.30	12/2020 12/2021	12/2021	12(O) 0	13/24

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
299	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL ,	04/2017	163.02 207.36	207.36	126.85	04/2020 10/2021	07/2022	27(O) 9	19/26
300	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL, WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	2,292.73	09/2022 03/2022	03/2022	-6(O) 0	3/3
301	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	136.39	03/2031 08/2031	08/2031	5(O) 0	24/50
302	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL, WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	103.42	01/2023 -	01/2023	0(O) -	1/6
	Total		3,41,221.64 -	3,52,793.57	1,19,873.17				1039/1571
	<u>POWER</u>								
303	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	14,458.38	09/2010 08/2023	08/2023	155(O) 0	0/0
304	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	19,311.93	10/2011 07/2023	07/2023	141(O) 0	34/48
305	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR ,	01/2007	5,353.00 10,566.00	10,566.00	8,993.63	07/2012 06/2020	11/2021	112(O) 1	24/25
306	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	16,371.88	05/2018 -	02/2022	45(O) -	43/45
307	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN, BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	3,509.49	01/2024 -	01/2024	0(O) -	16/27
308	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,343.71	11/2019 -	-	-	0/0
309	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL, DELHI ,	03/2015	1,394.52 -	1,394.52	561.71	05/2017 12/2021	12/2021	55(O) 0	4/9
310	KAWAS SOLAR 56 MW - [N18000283]NTPC, GUJARAT , EPC	08/2020	261.80 -	261.80	87.43	10/2021 01/2022	11/2021	1(O) 1	0/0
311	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC, GUJARAT , EPC	01/2021	842.27 -	842.27	92.08	07/2022 -	06/2022	-1(O) -	0/0
312	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI MESANKA AND RADHANPUR) - [N18000296]NTPC, GUJARAT , EPC	05/2021	674.92 -	674.92	76.00	09/2022 -	09/2022	0(O) -	0/0
313	SHIYAL SOLAR POWER PROJECT - [N18000297]SJVN, GUJARAT ,	05/2021	296.20 -	296.20	.00	10/2022 -	10/2022	0(O) -	0/0
314	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	9,279.64	09/2009 03/2023	03/2023	162(O) 0	5/5
315	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN, HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	532.10	01/2026 -	01/2026	0(O) -	0/0
316	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN, HIMACHAL PRADESH ,	10/2020	687.97 -	687.97	182.27	11/2025 -	11/2025	0(O) -	0/0
317	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	2,083.10	04/2020 07/2025	07/2025	63(O) 0	0/0
318	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL, JAMMU AND KASHMIR ,	03/2019	4,287.59 -	4,287.59	597.82	- 08/2024	08/2024	- 0	0/0
319	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND ,	02/2014	14,366.58 -	15,389.42	12,291.69	06/2019 10/2022	09/2023	51(O) 0	29/39

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
320	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,824.26	10/2017 -	-	-	0/0
321	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	17,112.00	4,391.63	03/2023 -	02/2025	23(O) -	3/14
322	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	116.32	06/2021 12/2021	12/2021	6(O) 0	0/0
323	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 1,587.16	1,587.16	629.21	09/2020 08/2022	08/2022	23(O) 0	13/16
324	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 1,311.05	1,311.05	156.99	06/2006 -	-	-	0/0
325	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,979.18	08/2013 11/2022	08/2022	108(O) 0	23/26
326	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	252.99	04/2016 12/2017	12/2021	68(O) 0	0/0
327	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	480.66	11/2016 12/2021	12/2021	61(O) 0	10/12
328	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	90.75	03/2018 -	12/2021	45(O) -	0/0
329	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	688.55	01/2018 07/2021	06/2021	-	0/0
330	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,683.96	11/2019 07/2021	10/2021	23(O) 0	0/0
331	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	204.37	02/2019 09/2021	02/2022	36(O) 0	0/0
332	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	156.95	06/2019 11/2021	12/2021	30(O) 1	0/0
333	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	235.98	12/2019 09/2021	12/2021	24(O) 0	0/0
334	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	4,223.07	04/2020 09/2021	06/2021	-	0/0
335	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 9,129.32	9,129.32	2,697.96	12/2018 03/2024	03/2024	63(O) 0	0/0
336	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 6,700.00	6,700.00	3,207.16	12/2018 12/2021	03/2022	39(O) 0	0/0
337	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	3,096.25	07/2020 12/2020	02/2022	19(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
338	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,807.75	02/2020 09/2021	10/2021	20(O) 0	0/0
339	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	260.80	05/2020 08/2021	12/2021	19(O) 1	0/0
340	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 2,311.89	2,311.89	1,922.67	12/2018 -	12/2021	36(O) -	0/0
341	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	996.32	09/2021 10/2022	01/2022	4(O) 0	0/0
342	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	672.69	09/2021 07/2022	09/2022	12(O) 0	0/0
343	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	539.41	03/2021 11/2021	11/2021	8(O) 0	0/0
344	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	1,277.87	09/2021 02/2022	02/2022	5(O) 0	0/0
345	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN , EPC	01/2021	382.22 -	382.22	.00	03/2022 -	03/2022	0(O) -	0/0
346	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN , EPC	01/2021	1,221.73 -	1,221.73	137.36	07/2022 -	07/2022	0(O) -	0/0
347	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN , EPC	02/2021	599.99 -	559.98	60.85	07/2022 -	07/2022	0(O) -	0/0
348	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	167.22	07/2019 07/2021	12/2021	29(O) 0	0/0
349	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	687.97	09/2021 02/2022	02/2022	5(O) 0	0/0
350	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 10,997.70	10,997.70	8,866.73	11/2020 07/2022	10/2022	23(O) 0	27/32
351	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	401.90	180.67	04/2021 10/2021	10/2021	6(O) 0	0/0
352	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	2,822.96	09/2023 -	08/2024	11(O) -	1/11
353	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	501.29	342.98	09/2021 02/2022	02/2022	5(O) 0	0/0
354	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	798.24	415.99	09/2021 02/2022	02/2022	5(O) 0	0/0
355	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,722.14	436.25	09/2021 07/2022	01/2023	16(O) 0	0/0
356	PARASAN SOLAR POWER PROJECT - [N18000298]SJVN,UTTAR PRADESH ,	08/2021	313.58 -	313.58	.00	12/2022 -	12/2022	0(O) -	0/0
357	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 4,825.60	4,825.60	4,266.10	02/2016 -	06/2023	88(O) -	26/30
358	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	5,187.12	03/2013 12/2021	09/2024	138(O) 0	8/15
359	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 3,860.35	3,860.35	2,313.83	06/2013 12/2024	12/2024	138(O) 0	11/17
360	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.93	08/2017 -	-	-	0/15

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
361	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	947.89	704.97	12/2021 06/2022	06/2022	6(O) 0	11/32
362	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.54	721.34	09/2019 12/2024	12/2024	63(O) 0	6/10
363	EASTERN REGION STRENGTHENING SCHEME- XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	345.15	04/2018 03/2021	06/2021	-	0/0
364	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 633.80	633.80	472.23	11/2018 -	02/2022	39(O) -	0/0
	Total		2,07,257.24 -	2,68,103.37	1,74,646.26				294/428
	HEAVY INDUSTRY								
365	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	900.00	815.00	09/2019 -	-	-	0/0
366	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	3,727.30	3,522.74	09/2011 03/2021	03/2021	-	24/25
	Total		3,272.00 -	4,627.30	4,337.74				24/25
	HEALTH AND FAMILY WELFARE								
367	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	268.55	03/2019 -	03/2021	-	0/0
368	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	487.74	- -	12/2021	- -	0/0
369	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0
370	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	417.16	05/2021 -	-	-	0/0
371	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	586.50	573.94	11/2013 -	09/2021	-	0/0
372	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021	-	2/2
373	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	5/5
374	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	190.34	176.66	- -	11/2021	- -	0/0
375	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	231.05	- -	01/2021	-	0/0
376	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	2/2
377	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	9(O) -	2/4
378	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
379	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	333.02	09/2023 -	09/2023	0(O) -	0/0
380	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
381	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	201.80	09/2025 -	05/2024	-16(O) -	0/0
382	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD FOR HEALTH,KERALA ,	09/2017	150.29 -	150.29	64.32	03/2020 -	12/2021	21(O) -	2/7
383	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	259.46	03/2019 -	01/2021	-	0/0
384	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	541.38	-	10/2021	-	0/0
385	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	253.84	05/2018 -	03/2022	46(O) -	0/0
386	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
387	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	-	1/1
388	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	538.20	06/2020 -	-	-	0/0
389	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA ,	10/2016	209.84 -	209.84	164.40	03/2020 -	05/2021	-	1/5
390	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	243.92	-	03/2021	-	0/0
391	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	591.61	04/2020 -	-	-	0/0
392	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
393	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
394	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	317.45	03/2019 -	10/2021	31(O) -	0/0
395	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	591.68	-	10/2021	-	0/0
	Total		15,273.26 -	15,715.78	9,026.70				18/62

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
396	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	1,035.50	03/2009 -	03/2024	180(O) -	0/0
397	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
398	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	- -	-	-	1/1
399	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 2,333.00	2,333.00	1,290.39	03/2021 -	03/2024	36(O) -	0/1
400	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	3,126.39	03/2020 -	03/2022	24(O) -	0/0
401	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
402	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,365.73	03/2022 -	03/2024	24(O) -	0/0
403	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	3,082.97	12/2023 -	12/2023	0(O) -	0/0
404	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	737.43	03/2022 03/2024	03/2026	48(O) 0	0/0
405	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	487.13	434.63	03/2018 -	-	-	0/0
406	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	-	-	0/0
407	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,043.00	873.80	03/2019 -	03/2023	48(O) -	0/0
408	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,950.00	1,842.95	03/2022 -	03/2023	12(O) -	0/0
409	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	1,873.21	1,498.64	03/2021 -	03/2022	12(O) -	0/0
410	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 898.53	1,080.00	1,077.28	03/2012 11/2022	11/2022	128(O) 0	0/0
411	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 614.45	614.45	352.46	- -	12/2023	-	0/0
412	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,590.10	- 03/2023	03/2023	- 0	0/0
413	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 516.02	516.02	459.05	03/2020 -	-	-	0/0
414	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 751.55	751.55	719.65	03/2012 09/2021	09/2021	-	0/0
415	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	1,021.19	03/2019 -	03/2024	60(O) -	0/0
416	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	- -	-	-	0/0
417	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	-	-	0/0
418	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	- -	-	-	0/0
419	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
420	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	- -	0/0
421	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	389.43	- -	03/2021	-	0/0
422	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	- -	0/0
423	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
424	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	- -	-	-	0/0
425	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	- -	-	-	0/0
426	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	- -	03/2024	- -	0/0
427	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	147.56	- 03/2023	03/2023	- 0	0/0
428	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	-	-	0/0
429	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	- -	-	-	0/0
430	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	1,436.01	- -	03/2023	-	0/0
431	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	541.64	03/2020 03/2023	12/2024	57(O) 21	0/0
432	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	309.90	- -	03/2025	- -	0/0
433	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	971.03	03/2020 -	03/2023	36(O) -	0/1
434	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	552.33	03/2020 03/2023	03/2023	36(O) 0	1/1
435	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	546.71	560.09	07/2014 -	-	-	0/0
436	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 1,215.54	1,215.54	513.54	03/2021 03/2024	03/2024	36(O) 0	0/0
437	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 1,185.73	1,185.73	383.26	03/2021 03/2024	03/2024	36(O) 0	0/0
438	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 803.11	1,483.14	1,218.49	- 03/2022	03/2022	- 0	0/0
439	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	1,010.84	03/2020 03/2023	03/2023	36(O) 0	1/1
440	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,347.35	03/2020 -	12/2021	21(O) -	0/0
441	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
442	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 2,135.34	2,135.34	700.69	03/2021 12/2023	12/2023	33(O) 0	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
443	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	18(O) -	0/1
444	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	45(O) -	0/1
445	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	339.31	03/2020 -	-	-	1/2
446	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	116.87	- -	03/2024	- -	0/0
447	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	160.79	- -	09/2023	- -	0/0
448	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,246.59	1,886.76	1,875.42	03/2020 03/2024	03/2024	48(O) 0	0/0
449	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	126.36	03/2012 10/2023	10/2023	139(O) 0	0/0
450	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,650.00	1,689.43	12/2021 -	12/2021	0(O) -	0/0
451	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	937.77	03/2021 -	12/2021	9(O) -	0/0
452	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	254.99	- 03/2024	03/2024	- 0	0/0
453	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.96	1,378.11	558.66	03/2019 03/2023	03/2023	48(O) 0	0/0
454	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	2,128.65	12/2021 -	03/2022	3(O) -	0/0
455	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,125.53	1,383.69	1,199.84	03/2021 12/2022	12/2022	21(O) 0	0/0
456	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,042.12	730.07	03/2021 12/2022	12/2022	21(O) 0	0/0
457	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
458	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 528.49	528.49	123.75	- 12/2022	-	-	0/0
459	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 154.15	154.15	103.45	- 12/2021	-	-	0/0
460	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT ,	04/2017	692.25 -	692.25	.77	03/2020 -	03/2023	36(O) -	0/0
461	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT ,	04/2018	537.31 -	537.31	.64	03/2024 -	03/2024	0(O) -	0/0
462	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	717.17	12/2011 -	06/2021	-	0/0
463	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	320.28	03/2019 -	-	-	0/0
464	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	1,809.22	12/2026 -	12/2025	-12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
465	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	25,828.58	11/2002 -	12/2022	241(O) -	0/0
466	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,630.00	3,630.96	- 03/2022	03/2022	- 0	0/0
467	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	904.73	- 03/2023	03/2023	- 0	0/0
468	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	1,028.57	03/2021 -	12/2023	33(O) -	0/0
469	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	390.00	386.59	03/2021 -	03/2022	12(O) -	0/0
470	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	5,174.30	158.11	- -	12/2024	- -	0/0
471	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	264(O) -	0/0
472	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	2,161.36	82.47	- -	12/2023	- -	0/0
473	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	1,530.09	316.23	03/2016 -	12/2026	129(O) -	1/1
474	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	- -	12/2023	- -	0/0
475	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
476	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	- -	12/2025	- -	0/0
477	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	2,400.15	03/2023 -	12/2022	-3(O) -	0/1
478	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	373.87	12/2018 -	06/2025	78(O) -	0/0
479	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	- -	12/2023	- -	0/0
480	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	36.97	03/2016 -	12/2023	93(O) -	0/0
481	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,968.00	1,174.76	03/2020 -	03/2023	36(O) -	1/5
482	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	760.00	642.52	03/2020 12/2021	12/2021	21(O) 1	1/2
483	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 889.00	732.89	469.70	03/2017 -	03/2025	96(O) -	0/0
484	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 1,566.00	2,815.62	264.50	- -	-	- -	0/0
485	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 369.55	709.69	8.50	- -	03/2025	- -	0/0
486	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 275.21	448.10	6.73	- -	03/2025	- -	0/0
487	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	492.74	- -	03/2024	- -	0/0
488	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 1,246.00	1,339.00	.82	- -	03/2025	- -	0/0
489	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	- -	0/0
490	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 2,909.99	2,909.99	1,378.97	03/2021 03/2024	03/2024	36(O) 0	4/15

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
491	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,839.02	6,171.08	2,327.60	03/2022 03/2023	03/2023	12(O) 0	0/0
492	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	2,449.00	1,293.48	03/2020 -	03/2024	48(O) -	1/1
493	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	1,972.62	12/2020 -	12/2021	12(O) -	0/0
494	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 2,875.12	2,875.12	1,035.16	03/2022 06/2023	06/2023	15(O) -9	4/17
495	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	508.67	03/2022 -	03/2023	12(O) -	1/1
496	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
497	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 1,268.32	1,268.32	1,082.34	02/2019 12/2021	12/2021	34(O) 0	0/1
498	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.94	1,370.94	712.76	12/2021 12/2023	12/2023	24(O) 0	0/0
499	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	314.13	06/2020 03/2023	03/2023	33(O) 0	0/0
500	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH ,	04/2017	495.18 -	495.18	.33	03/2022 -	03/2024	24(O) -	0/0
501	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,866.85	03/2004 06/2022	06/2022	219(O) 3	0/0
502	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,794.60	2,905.60	03/2021 -	03/2023	24(O) -	0/0
503	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	-	-	0/0
504	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
505	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,445.48	1,418.05	03/2023 -	03/2023	0(O) -	0/0
506	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,387.52	357.95	03/2021 -	03/2023	24(O) -	0/0
507	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 -	325.00	325.01	03/2019 -	-	-	0/0
508	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	354.61	03/2022 -	03/2024	24(O) -	0/0
509	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
510	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
511	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.49	.00	03/2024 -	-	-	0/0
512	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	515.13	03/2022 -	03/2023	12(O) -	0/0
513	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	466.67	03/2023 -	03/2024	12(O) -	0/0
514	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,721.84	03/2024 -	03/2023	-12(O) -	0/0
515	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	630.94	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
516	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	314.37	03/2022 -	03/2024	24(O) -	0/0
517	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	237.71	03/2023 -	03/2024	12(O) -	0/0
518	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,900.00	2,831.13	03/2020 -	12/2021	21(O) -	0/0
519	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
520	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 3,176.60	3,176.60	1,417.20	03/2023 12/2023	12/2023	9(O) 0	0/1
521	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	269.73	03/2019 -	-	-	0/0
522	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 311.36	311.36	.00	- -	-	-	0/0
523	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 393.62	393.62	152.98	- 12/2022	-	-	0/0
524	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 852.50	1,096.00	40.47	12/2021 12/2024	12/2024	36(O) 0	0/1
525	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	12,264.15	11,504.51	03/2011 -	12/2023	153(O) -	0/0
526	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	4,083.02	264.34	03/2021 -	-	-	0/0
527	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 5,021.45	5,521.45	4,232.46	03/2014 -	03/2024	120(O) -	0/0
528	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 2,017.96	2,017.96	878.49	07/2012 -	11/2024	148(O) -	0/0
529	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	2,004.42	03/2000 -	03/2023	276(O) -	0/0
530	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202(O) -	1/9
531	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	4,541.38	3,881.59	12/2008 -	11/2021	155(O) -	0/0
532	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	638.28	02/2013 -	03/2024	133(O) -	0/0
533	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
534	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	116.24	12/2021 -	12/2021	0(O) -	0/0
535	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	610.00	580.83	01/2019 -	02/2022	37(O) -	0/0
536	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,524.68	1,524.68	974.69	03/2022 03/2023	03/2023	12(O) 0	0/0
537	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,873.10	1,873.10	869.58	03/2022 03/2025	03/2025	36(O) 0	0/0
538	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	191.39	- -	-	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
539	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	329.61	03/2022 12/2024	12/2024	33(O) 0	0/3
540	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	.00	- 04/2010	12/2021	- 0	0/0
541	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
542	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.58	- -	-	-	0/0
543	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,042.51	2,042.51	328.75	03/2019 -	12/2023	57(O) -	0/0
544	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	- -	0/0
545	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 457.08	749.40	550.86	- 12/2021	01/2022	- 0	0/0
546	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	76.57	03/2020 -	-	-	0/0
547	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	333.46	- 12/2021	03/2022	- 0	0/0
548	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	750.00	157.19	03/2020 -	-	-	0/0
549	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23	1,090.60	1,089.12	- -	-	-	0/0
550	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	285.53	03/2019 -	12/2027	105(O) -	0/0
551	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228(O) -	0/0
552	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
553	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	11.77	- -	03/2025	- -	0/0
554	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	439.23	03/2022 -	03/2025	36(O) -	0/0
555	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	517.25	- -	03/2021	-	0/0
556	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	614.87	03/2016 -	03/2025	108(O) -	0/0
557	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96(O) -	0/0
558	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	- -	0/0
559	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	199.72	03/2016 -	03/2025	108(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
560	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	480.96	03/2017 -	03/2025	96(O) -	0/0
561	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	-	0/0
562	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.11	- -	03/2025	- -	0/0
563	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
564	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	313.03	- -	03/2022	- -	0/0
565	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
566	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240(O) -	0/0
567	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	36.13	- -	03/2025	- -	0/0
568	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	40.65	- -	03/2025	- -	0/0
569	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	157(O) -	0/0
570	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	109.51	03/2014 -	03/2025	132(O) -	0/0
571	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
572	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	714.51	03/2023 -	03/2024	12(O) -	0/0
573	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	2.39	- -	-	-	1/1
574	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	791.39	597.99	- -	09/2023	-	0/0
575	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- -	12/2023	-	0/0
576	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,404.03	1,087.98	- -	12/2025	-	2/2
577	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 927.94	927.94	680.25	03/2020 -	02/2022	23(O) -	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
578	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	156(O) -	1/1
579	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	383.74	- -	03/2024	- -	0/0
580	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	313.14	03/2020 -	10/2022	31(O) -	0/0
581	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,104.00	966.68	03/2020 -	09/2021	-	0/0
582	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,877.81	1,878.00	1,488.87	03/2019 -	03/2024	60(O) -	0/0
583	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	929.86	926.80	03/2019 12/2021	12/2021	33(O) 0	0/38
584	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
585	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,582.36	03/2021 -	03/2024	36(O) -	0/0
586	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	17,009.45	12/2023 -	12/2023	0(O) -	0/0
587	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
588	CHANDIGARH-BADDI - [N22000467]JNR,MULTI STATE ,	04/2007	328.14 -	1,540.13	242.55	03/2023 -	03/2023	0(O) -	0/0
589	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]JNR,MULTI STATE ,	03/2002	625.00 781.00	839.00	839.36	03/2016 -	-	-	0/0
590	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,647.64	1,369.40	03/2015 -	03/2026	132(O) -	0/0
591	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
592	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,649.76	03/2009 03/2026	03/2026	204(O) 0	0/0
593	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,842.99	02/2015 -	06/2022	88(O) -	0/0
594	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	433.00	405.83	03/2009 12/2022	12/2022	165(O) 0	1/1
595	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	909.17	06/2021 03/2025	03/2025	45(O) 0	0/0
596	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
597	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	1,195.24	02/2019 03/2022	03/2022	37(O) 0	0/0
598	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	269.52	10/2020 03/2024	03/2024	41(O) 0	0/0
599	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	223.69	03/2020 -	03/2022	24(O) -	0/0
600	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	696.10	03/2022 03/2023	03/2023	12(O) 0	0/0
601	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	493.76	03/2022 03/2026	03/2026	48(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
602	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	193.71	11/2018 03/2024	03/2024	64(O) 0	0/0
603	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	692.35	12/2018 03/2024	03/2024	63(O) 0	0/0
604	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,312.96	1,071.24	03/2020 -	03/2022	24(O) -	0/0
605	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	1,887.58	12/2024 -	12/2026	24(O) -	0/0
606	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	2,119.84	03/2020 -	12/2021	21(O) -	0/0
607	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,233.58	03/2019 -	06/2022	39(O) -	0/0
608	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 -	5,200.00	101.77	03/2020 -	03/2025	60(O) -	0/0
609	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
610	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108(O) -	0/0
611	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	759.31	02/2019 -	06/2022	40(O) -	0/0
612	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	821.64	.00	- -	-	-	0/1
613	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	322.98	.00	- -	-	-	0/0
614	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	480.00	378.63	03/2020 -	09/2021	-	0/0
615	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	2,215.27	4.60	- -	-	-	0/0
616	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	464.53	03/2018 -	-	-	0/0
617	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	356.84	08/2022 -	11/2022	3(O) -	0/0
618	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 4,084.69	8,600.00	1,656.78	12/2015 12/2023	12/2023	96(O) 0	0/0
619	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,720.00	705.52	03/2020 -	03/2025	60(O) -	0/0
620	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	478.72	06/2013 07/2022	07/2022	109(O) 0	1/4
621	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,950.00	1,667.29	02/2019 -	03/2025	73(O) -	0/0
622	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	227.40	65.02	- -	03/2030	- -	0/0
623	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	3,150.00	239.53	- -	12/2025	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
624	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	133(O) -	0/0
625	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	839.01	.63	- -	03/2030	- -	0/0
626	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	603.23	1.63	- -	03/2030	- -	0/0
627	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	608.13	399.75	- 12/2021	02/2022	- 2	0/0
628	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	1,122.00	989.62	- 09/2021	12/2022	- 15	0/0
629	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	920.91	03/2005 -	09/2021	-	0/0
630	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
631	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	1,056.49	03/2022 -	06/2022	3(O) -	0/0
632	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,409.57	03/2020 -	06/2022	27(O) -	0/0
633	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.25	3.69	- -	-	-	0/0
634	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,373.74	646.34	03/2010 -	03/2024	168(O) -	1/1
635	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	836.26	03/2016 -	12/2021	69(O) -	0/0
636	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
637	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 -	723.00	.00	- -	-	-	0/1
638	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	634.20	03/2021 -	-	-	3/3
639	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	925.02	12/2024 -	12/2024	0(O) -	0/0
640	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 176.18	242.28	67.24	03/2022 03/2022	03/2022	0(O) 0	0/0
641	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 90.00	742.00	561.03	03/2020 06/2022	06/2022	27(O) 3	2/3
642	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
643	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
644	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
645	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	489.64	105.51	- -	03/2023	- -	0/0
646	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,824.00	1,373.75	03/2022 -	03/2022	0(O) -	0/0
647	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	4.00	03/2020 -	12/2021	21(O) -	4/6
648	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	945.85	03/2022 -	12/2024	33(O) -	0/0
649	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,429.50	03/2019 -	06/2022	39(O) -	0/0
650	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	1,054.05	03/2023 -	12/2024	21(O) -	0/0
651	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,710.66	12/2020 -	12/2022	24(O) -	0/0
652	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,367.09	03/2020 -	03/2024	48(O) -	0/0
653	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	236.91	03/2019 -	03/2022	36(O) -	0/0
654	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	69.01	04/2016 -	12/2021	68(O) -	0/0
655	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
656	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	341.66	.00	04/2017 -	10/2022	66(O) -	0/0
657	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	-	-	0/0
658	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
659	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	800.00	128.90	- -	12/2023	- -	0/0
660	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	315.05	01/2022 -	03/2022	2(O) -	0/0
661	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	346.17	12/2019 -	04/2021	-	0/0
662	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	71.56	03/2023 -	06/2025	27(O) -	0/0
663	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	980.08	03/2021 12/2022	12/2023	33(O) 0	1/6
664	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	2,261.21	12/2023 -	12/2023	0(O) -	0/0
665	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
666	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	4,874.57	12/2024 -	03/2025	3(O) -	0/0
667	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	275.06	03/2019 -	-	-	0/0
668	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
669	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268]MRTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
670	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [N220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	908.35	03/2019 12/2009	03/2025	72(O) 0	0/0
671	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
672	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0
673	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	3,033.55	03/2016 -	03/2025	108(O) -	0/0
674	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	1,422.91	03/2016 -	03/2025	108(O) -	0/0
675	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	-	0/0
676	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	41.78	-	03/2025	-	0/0
677	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.20	-	-	-	0/0
678	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
679	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	299.01	-	03/2022	-	0/0
680	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	1,167.00	1,028.89	12/2021 -	10/2021	-2(O) -	0/0
681	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
682	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	-	0/0
	Total		4,54,260.58 -	6,93,056.85	2,66,992.14				37/139
	DEPARTMENT OF HIGHER EDUCATION								
683	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD EDUCATION, ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	-	3/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
684	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH ,	02/2019	655.34 -	655.34	125.17	06/2020 -	-	-	0/110
685	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRIC - [N42000007]CPWD EDUCATION,ANDHRA PRADESH ,	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4(O) -	0/0
686	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR ,	02/2016	496.18 496.00	498.99	292.81	06/2017 -	03/2022	57(O) -	2/6
687	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR ,	09/2018	375.00 -	375.00	110.13	09/2020 -	11/2022	26(O) -	0/0
688	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH ,	03/2020	808.62 -	808.62	249.81	07/2022 -	10/2022	3(O) -	0/0
689	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD EDUCATION,GOA ,	05/2019	303.90 -	303.90	37.80	03/2020 -	-	-	1/8
690	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH ,	11/2012	270.83 -	244.00	241.67	11/2014 11/2021	11/2021	84(O) 0	7/8
691	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	57.47	06/2022 -	06/2022	0(O) -	0/0
692	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR ,	03/2019	424.93 -	424.93	55.00	07/2022 -	10/2022	3(O) -	0/0
693	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD EDUCATION,JAMMU AND KASHMIR ,	01/2018	676.00 748.19	676.00	213.47	04/2023 -	04/2023	0(O) -	0/0
694	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND ,	09/2012	171.86 -	171.86	111.29	03/2016 -	-	-	1/6
695	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6(O) -	0/12
696	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	1/8
697	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	177.82	03/2021 -	02/2023	23(O) -	2/11
698	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA ,	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	17(O) -	4/14
699	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
700	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA ,	01/2019	790.79 -	790.79	230.59	03/2022 -	06/2022	3(O) -	0/5
701	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB ,	01/2018	430.00 -	387.83	228.61	05/2020 -	06/2022	25(O) -	3/5
702	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB ,	10/2019	348.24 -	348.24	24.91	05/2022 -	10/2022	5(O) -	1/7
703	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN ,	12/2016	549.31 -	559.47	458.38	07/2019 -	-	-	3/6
704	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD EDUCATION,UTTAR PRADESH ,	11/2017	171.72 135.00	171.72	110.13	03/2020 12/2021	12/2021	21(O) 0	0/0
705	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL , EPC	03/2020	193.83 -	193.83	170.60	06/2020 -	-	-	0/0
	Total		10,311.33 -	10,416.24	3,303.35				28/213
	HOME AFFAIRS								
706	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI ,	10/2013	1,219.21 -	2,000.00	1,007.93	10/2019 -	03/2022	29(O) -	1/7
707	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI , EPC	06/2019	277.35 290.33	290.33	27.25	07/2022 10/2022	10/2022	3(O) 0	0/0
708	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD FOR MHA,HARYANA , EPC	01/2020	166.98 167.00	166.98	.00	10/2023 -	10/2023	0(O) -	0/0
709	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD FOR MHA,UTTAR PRADESH ,	05/2019	199.31 -	199.31	20.53	01/2022 02/2022	01/2020	-	0/0
710	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD FOR MHA,UTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
711	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL , Central Sector Projects	10/2014	162.88 238.00	238.00	172.13	04/2018 12/2021	12/2021	44(O) 0	5/6
	Total		2,139.99 -	3,160.62	1,227.84				6/13
	RURAL DEVELOPMENT								
712	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD FOR RURAL,DELHI ,	11/2018	361.60 -	361.60	12.44	07/2021 -	-	-	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		361.60 -	361.60	12.44				0/2
	<u>DPIIT</u>								
713	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI ,	11/2017	4,773.00 -	5,178.00	3,013.69	12/2019 05/2022	05/2022	29(O) 0	0/0
714	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	9,574.07	09/2019 01/2014	07/2021	-	0/0
	Total		17,352.09 -	18,990.30	12,587.76				0/0
	<u>DONER</u>								
715	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA ,	04/2014	151.33 -	151.33	149.33	09/2017 -	08/2021	-	12/15
	Total		151.33 -	151.33	149.33				12/15
	<u>RENEWABLE ENERGY</u>								
716	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI ,	10/2017	271.90 -	271.90	90.99	11/2019 -	-	-	0/0
	Total		271.90 -	271.90	90.99				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
717	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022	39(O) 0	1/4
718	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51(O) 0	2/4
719	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	54(O) 0	3/4
720	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41(O) -	1/4
721	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41(O) 0	2/4
722	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 237.80	238.00	121.78	11/2019 10/2021	10/2021	23(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
723	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	214.90	11/2019 06/2021	06/2021	-	0/0
724	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	229.32	07/2019 -	-	-	0/4
725	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
726	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,283.85	05/2014 -	-	-	0/0
727	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
728	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	243.29	10/2015 06/2021	-	-	4/4
729	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	.00	02/2017 -	-	-	0/0
730	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	966.71	03/2020 -	-	-	0/0
731	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	266.63	- -	-	-	0/0
732	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	1,187.87	- -	-	-	0/0
733	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
734	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,314.63	- -	10/2021	-	0/0
735	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	1,009.18	03/2021 07/2021	07/2021	-	4/4
736	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,633.66	- -	09/2021	-	0/0
737	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	654.33	- -	02/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
738	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	85.61	- -	06/2022	- -	0/0
739	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	433.20	- -	-	-	0/0
740	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	353.43	333.09	12/2015 -	-	-	3/3
741	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 309.37	372.68	256.21	02/2017 10/2021	-	-	3/4
742	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	142.33	05/2017 10/2021	-	-	3/4
743	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	203.81	08/2017 02/2022	-	-	3/4
744	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 373.05	429.43	325.31	11/2017 01/2022	-	-	3/4
745	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 202.83	228.32	140.06	08/2018 12/2021	-	-	3/4
746	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 274.73	289.67	208.86	08/2018 11/2021	-	-	3/4
747	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 556.13	504.19	469.14	11/2018 07/2021	-	-	3/4
748	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	561.45	05/2016 09/2021	-	-	3/4
749	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 381.75	418.03	324.42	08/2018 10/2021	-	-	3/4
750	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	324.69	01/2017 12/2021	-	-	3/4
751	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 316.06	386.09	214.31	05/2016 11/2021	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
752	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	231.08	08/2016 12/2021	07/2021	-	3/4
753	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	349.19	09/2016 08/2021	-	-	3/4
754	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	314.18	08/2017 12/2021	-	-	3/4
755	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 381.75	263.45	116.24	09/2017 05/2022	-	-	1/4
756	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 596.38	576.48	388.43	01/2018 04/2022	-	-	2/4
757	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 -	597.67	216.39	01/2020	-	-	0/0
758	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 -	617.41	526.54	02/2019	-	-	0/0
759	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 -	1,226.88	211.90	02/2021 -	-	-	0/0
760	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	13.51	02/2021 -	-	-	0/0
761	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH , EPC	03/2020	207.79 -	207.79	102.76	03/2021 -	04/2022	13(O) -	2/4
762	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH , EPC	06/2020	221.40 -	221.40	16.24	05/2021 -	12/2022	19(O) -	0/4
763	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH , EPC	08/2020	222.61 -	222.61	6.94	03/2021 -	03/2023	24(O) -	0/4
764	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	390.07	06/2018 -	03/2021	-	3/3
765	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	- 0	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
766	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	167.81	04/2017 03/2021	03/2022	59(O) 0	2/4
767	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	142.18	04/2017 -	03/2022	59(O) -	2/4
768	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	148.30	04/2017 -	03/2022	59(O) -	2/4
769	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	61.40	04/2017 -	02/2021	-	1/4
770	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	252.05	152.53	04/2017 -	03/2022	59(O) -	3/4
771	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
772	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	125.91	- 08/2021	12/2021	- 0	3/4
773	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022	- 0	2/4
774	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	310.07	- 11/2021	03/2022	- 0	0/0
775	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	104.07	- 03/2021	03/2022	- 0	3/4
776	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	90.86	- 04/2022	04/2022	- 0	3/4
777	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	76.96	- 04/2022	04/2022	- 0	2/4
778	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 -	210.50	145.76	- -	10/2021	- -	4/4
779	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,242.74	- 03/2020	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
780	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	217.60	- -	09/2020	-	0/0
781	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	25.63	04/2022 -	04/2022	0(0) -	0/4
782	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	20.81	05/2022 -	05/2022	0(0) -	0/4
783	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	64.64	02/2020 -	-	-	0/0
784	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	167.73	02/2020 -	-	-	0/0
785	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	50.14	11/2020 -	-	-	0/0
786	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	119.81	11/2020 -	-	-	0/0
787	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	83.55	10/2020 -	-	-	0/0
788	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	172.41	02/2020 -	-	-	0/0
789	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	95.49	09/2020 -	-	-	0/0
790	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	35.37	10/2020 -	-	-	0/0
791	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	37.16	11/2020 -	-	-	0/0
792	TADADEGE - HENKAR - [N24001315]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	550.45 -	550.45	13.03	03/2023 -	03/2023	0(0) -	0/4
793	LADDA - BASAI - [N24001316]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	445.96 -	445.96	.00	04/2023 -	04/2023	0(0) -	0/4
794	DOGINALA - GAU - [N24001320]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	242.30 -	242.30	.00	09/2022 -	09/2022	0(0) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
795	DEMBUEN - BRUNI - [N24001321]NHIDCL, ARUNACHAL PRADESH , EPC	12/2020	606.63 -	606.63	.00	03/2023 -	03/2023	0(0) -	0/4
796	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]MoRTH, ARUNACHAL PRADESH , EPC	02/2021	588.09 -	588.09	83.83	03/2024 -	03/2024	0(0) -	0/0
797	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]MoRTH, ARUNACHAL PRADESH , EPC	01/2020	358.26 -	358.26	1.15	02/2024 -	02/2024	0(0) -	0/0
798	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH, ARUNACHAL PRADESH , EPC	06/2020	437.60 -	437.60	.00	08/2021 -	-	-	0/0
799	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH, ARUNACHAL PRADESH , EPC	06/2020	496.47 -	496.47	.00	08/2021 -	-	-	0/0
800	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH, ARUNACHAL PRADESH , EPC	03/2021	182.55 -	182.55	.00	09/2021 -	09/2021	-	0/0
801	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]NHIDCL, ARUNACHAL PRADESH ,	08/2020	228.71 -	228.71	27.48	04/2022 -	04/2022	0(0) -	1/4
802	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]NHIDCL, ARUNACHAL PRADESH , EPC	08/2020	294.04 -	294.04	56.85	04/2022 -	04/2022	0(0) -	2/4
803	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]NHIDCL, ARUNACHAL PRADESH , EPC	08/2020	199.03 -	199.03	39.84	04/2022 -	04/2022	0(0) -	2/4
804	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]NHIDCL, ARUNACHAL PRADESH , EPC	08/2020	184.88 -	184.88	32.58	04/2022 -	04/2022	0(0) -	1/4
805	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM ,	12/2003	280.00 -	612.58	612.58	02/2009 -	-	-	0/0
806	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM ,	12/2003	199.81 -	340.14	.00	04/2009 -	-	-	0/0
807	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI, ASSAM ,	12/2003	167.64 -	435.78	.00	11/2008 -	-	-	0/0
808	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM ,	12/2003	155.04 -	255.23	.00	11/2008 -	-	-	0/0
809	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI, ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
810	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM , EPC	05/2015	454.89 -	454.89	346.86	05/2018 -	03/2022	46(0) -	3/4
811	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM , EPC	06/2015	437.39 -	437.39	105.09	06/2018 -	12/2021	42(0) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
812	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM , EPC	06/2015	463.49 -	463.49	165.06	06/2018 -	12/2021	42(O) -	2/4
813	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM , EPC	03/2015	168.39 -	168.39	148.91	11/2018 -	11/2021	36(O) -	4/4
814	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM , EPC	10/2014	588.95 -	588.95	504.10	11/2018 -	02/2022	39(O) -	3/4
815	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH- 52B(EXTN) IN ASSAM - [N24000392]MoRTH, ASSAM , EPC	11/2010	268.08 -	390.73	326.56	05/2017 05/2022	05/2022	60(O) 0	0/0
816	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM , EPC	01/1991	520.01 -	520.01	199.64	- -	12/2021	- -	3/4
817	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM , EPC	12/2015	289.99 -	289.99	95.89	12/2018 -	12/2021	36(O) -	1/4
818	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM , EPC	01/2016	294.17 -	294.17	219.83	01/2016 -	03/2022	74(O) -	3/4
819	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM , EPC	01/2016	252.00 -	252.00	136.10	01/2016 -	03/2022	74(O) -	2/4
820	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM ,	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74(O) -	2/3
821	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM ,	10/2017	818.00 -	818.00	215.66	- -	03/2023	- -	1/4
822	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH, ASSAM ,	09/2018	160.00 -	160.00	124.58	09/2021 -	02/2022	5(O) -	0/0
823	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL, ASSAM ,	03/2017	1,049.51 -	1,049.51	155.61	- -	12/2021	- -	2/4
824	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH, ASSAM ,	03/2020	166.94 -	166.94	32.27	12/2020 12/2022	-	-	0/0
825	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL, ASSAM , EPC	03/2020	220.20 -	220.20	27.79	12/2022 -	12/2022	0(O) -	1/4
826	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL, ASSAM , EPC	08/2020	208.84 -	208.84	17.93	04/2022 -	04/2022	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
827	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	103.50	03/2022 -	03/2022	0(0) -	1/4
828	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	40.09	03/2022 -	03/2022	0(0) -	1/4
829	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]NHIDCL,ASSAM , EPC	11/2020	4,997.04 -	4,997.04	532.08	09/2028 -	09/2028	0(0) -	0/4
830	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]NHIDCL,ASSAM , EPC	12/2020	804.00 -	804.00	7.04	08/2023 -	08/2023	0(0) -	0/4
831	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL,ASSAM , EPC	03/2020	261.13 -	261.13	23.56	06/2022 -	06/2022	0(0) -	0/4
832	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]NHIDCL,ASSAM , EPC	03/2020	217.50 -	217.50	34.17	06/2022 -	06/2022	0(0) -	0/4
833	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]NHIDCL,ASSAM , EPC	09/2019	761.54 -	761.54	116.54	05/2023 -	05/2023	0(0) -	1/4
834	DABOKA KATHKATI PACKAGE-2 - [N24001364]NHIDCL,ASSAM , EPC	03/2021	335.88 -	335.88	11.78	01/2024 -	01/2024	0(0) -	0/4
835	DABOKA KATHKATI PACKAGE-4 - [N24001365]NHIDCL,ASSAM , EPC	02/2021	260.07 -	260.07	67.70	12/2023 -	12/2023	0(0) -	0/4
836	DABOKA KATHKATI PACKAGE-5 - [N24001366]NHIDCL,ASSAM , EPC	03/2021	288.85 -	288.85	.00	01/2023 -	01/2023	0(0) -	0/4
837	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM , EPC	03/2021	636.42 -	636.42	.00	12/2022 -	12/2022	0(0) -	0/4
838	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]NHIDCL,ASSAM , EPC	03/2021	286.72 -	286.72	.00	01/2024 -	01/2024	0(0) -	0/4
839	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]MoRTH,ASSAM , EPC	02/2021	925.47 -	925.47	.00	07/2025 -	07/2025	0(0) -	0/0
840	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,197.27	02/2013 -	-	-	3/4
841	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.92	03/2014 -	-	-	0/0
842	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
843	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	503.83	07/2013 12/2021	-	-	2/3
844	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	591.00	578.00	11/2013 -	-	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 780.77	675.00	379.73	- -	-	-	0/0
846	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
847	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	414.67	04/2019 -	-	-	0/0
848	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	799.07	-	10/2021	-	2/4
849	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	.00	04/2018 -	-	-	0/0
850	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	503.71	-	-	-	1/4
851	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	272.27	-	-	-	0/0
852	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,023.88	-	-	-	3/4
853	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	648.77	04/2018 -	-	-	4/4
854	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	319.07	-	-	-	0/0
855	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 683.82	560.70	694.71	07/2016 -	-	-	0/0
856	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	140.55	05/2016 -	-	-	0/0
857	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	527.97	05/2016 -	-	-	0/0
858	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 2,138.16	925.87	1,209.93	10/2016 -	-	-	0/0
859	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	.00	05/2017 -	-	-	0/0
860	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,729.05	12/2016 -	-	-	0/0
861	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	75.90	03/2020 -	-	-	0/0
862	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	-	0/0
863	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	311.03	08/2017 -	02/2022	54(O) -	0/0
864	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 1,962.50	1,962.50	235.00	- 01/2021	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
865	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	82.47	- -	-	-	0/0
866	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
867	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	64.82	- -	-	-	0/0
868	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	79.35	- -	-	-	0/0
869	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	86.31	- -	-	-	0/0
870	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	218.52	- -	-	-	0/0
871	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	44.00	12/2020 -	-	-	0/0
872	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	-	-	0/0
873	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	.00	11/2020 -	-	-	0/0
874	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR , EPC	10/2019	1,101.99 -	1,101.99	193.26	02/2020 -	-	-	0/4
875	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	238.67	- 10/2021	10/2021	- 0	0/0
876	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
877	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
878	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 1,096.52	1,096.52	518.73	04/2018 -	-	-	0/0
879	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	402.95	- -	03/2021	-	0/0
880	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 572.66	572.66	284.62	08/2016 06/2022	06/2022	70(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
881	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	279.60	06/2017 12/2021	12/2021	54(O) 0	0/0
882	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	400.86	09/2016 12/2021	12/2021	63(O) 0	0/0
883	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	470.70	10/2016 12/2021	12/2021	62(O) 0	0/0
884	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	112.86	07/2016 12/2022	12/2022	77(O) 0	0/0
885	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	295.71	01/2018 12/2021	12/2021	47(O) 0	0/0
886	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	250.97	03/2015 03/2022	03/2022	84(O) 0	0/0
887	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	90.41	05/2019 12/2021	12/2021	31(O) 0	0/0
888	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	322.96	11/2017 11/2021	11/2021	48(O) 0	0/0
889	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	325.55	- -	-	-	0/4
890	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	118.37	- -	-	-	2/4
891	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	244.36	- -	-	-	3/4
892	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	520.09	- -	-	-	0/0
893	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	394.63	- -	-	-	0/0
894	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	362.15	- -	-	-	0/0
895	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	292.34	05/2020 -	-	-	1/4
896	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 -	852.67	190.09	12/2019 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
897	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-	-	2/3
898	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	.00	07/2013 -	-	-	0/0
899	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	439.91	12/2015 -	-	-	3/3
900	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	737.67	- -	-	-	2/2
901	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	203.40	- -	-	-	1/1
902	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	505.33	- -	-	-	2/2
903	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	414.25	- -	-	-	2/2
904	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	-	-	0/0
905	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	392.00	353.42	- -	04/2021	-	0/0
906	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	235.85	- -	-	-	0/0
907	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	199.86	- -	-	-	0/3
908	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 1,361.00	1,361.00	449.41	- 01/2019	-	-	2/4
909	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	-	3/3
910	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
911	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,361.00	449.41	- 01/2019	-	-	2/4
912	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,043.00	1,888.51	- -	-	-	0/0
913	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	564.11	- -	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
914	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
915	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH, GUJARAT , EPC	12/2017	867.97 -	867.97	602.77	11/2018 -	-	-	2/4
916	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH, GUJARAT , EPC	03/2018	464.07 -	464.07	314.18	11/2018 -	-	-	4/4
917	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH, GUJARAT , EPC	10/2018	400.76 -	400.76	175.16	05/2019 -	-	-	2/4
918	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH, GUJARAT , EPC	08/2017	962.43 -	962.43	301.45	03/2018 -	-	-	1/4
919	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH, GUJARAT ,	03/2018	351.00 -	351.00	172.78	06/2021 -	06/2021	-	2/4
920	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
921	PANIPAT -JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 3,485.00	2,288.00	3,450.00	11/2011 -	-	-	0/0
922	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 -	507.70	.00	06/2016 -	-	-	0/0
923	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 -	537.16	.00	07/2018 -	-	-	0/0
924	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,577.44	04/2019 -	09/2021	-	0/0
925	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA ,	03/2018	1,484.30 -	1,484.30	275.72	- 06/2021	12/2020	-	0/0
926	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA ,	03/2018	275.12 -	275.12	172.62	- -	-	-	0/0
927	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA ,	03/2018	634.70 -	925.96	341.09	- 02/2018	02/2018	-	0/0
928	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA ,	03/2018	795.50 906.65	922.64	387.49	- 02/2018	02/2018	-	0/0
929	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA ,	03/2018	198.05 -	198.05	136.17	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
930	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	129.84	- -	-	-	0/0
931	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	179.30	03/2019 -	-	-	0/0
932	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	870.68	- -	-	-	0/0
933	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	905.59	- -	-	-	0/0
934	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	978.00	- -	-	-	0/0
935	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	898.54	- -	-	-	0/0
936	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	985.75	- -	-	-	0/0
937	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	692.40	- -	-	-	0/0
938	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	804.31	- -	-	-	0/0
939	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	1,000.97	- -	-	-	0/0
940	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
941	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	1,299.17	03/2018 03/2021	-	-	0/0
942	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	669.49	02/2019 -	-	-	0/0
943	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	-	-	0/0
944	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	860.13	- -	-	-	0/0
945	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,340.40	- -	-	-	0/0
946	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	1,025.14	06/2020 -	09/2021	-	0/0
947	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	727.92	- 11/2021	-	-	0/0
948	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH , EPC	08/2020	272.98 -	272.98	11.86	04/2021 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
949	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MORTH,HIMACHAL PRADESH , EPC	08/2020	242.80 -	242.80	10.23	03/2021 -	-	-	0/0
950	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MORTH,HIMACHAL PRADESH , EPC	08/2020	349.20 -	349.20	17.99	04/2021 -	-	-	0/0
951	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	09/2020	-	0/0
952	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	-	0/0
953	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,653.88	07/2013 -	-	-	0/0
954	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,933.30	06/2014 -	10/2020	-	0/0
955	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	1,158.40	06/2019 -	-	-	0/0
956	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,763.58	12/2018 -	-	-	0/0
957	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	953.12	- -	01/2021	-	2/3
958	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	222.70	08/2018 -	-	-	2/4
959	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	112.12	11/2018 -	-	-	1/4
960	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	85.34	07/2019 -	-	-	0/4
961	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023	0(0) -	1/4
962	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	275.00	09/2026 -	09/2026	0(0) -	0/6
963	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	17.68	04/2022 -	04/2022	0(0) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
964	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	17.58	04/2022 -	04/2022	0(0) -	1/4
965	KHELLANI-KHANABAL PKG-1 - [N24001323]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	486.45 -	486.45	36.09	09/2022 -	09/2022	0(0) -	1/4
966	KHELLANI-KHANABAL PKG-6 - [N24001324]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	285.28 -	285.28	18.65	09/2022 -	09/2022	0(0) -	0/4
967	KHELLANI-KHANABAL PKG-3 - [N24001341]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	398.51 -	398.51	.00	12/2022 -	12/2022	0(0) -	0/4
968	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	260.40 -	260.40	.00	12/2022 -	12/2022	0(0) -	0/4
969	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	512.43 -	512.43	.00	02/2023 -	02/2023	0(0) -	0/0
970	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	859.67 -	859.67	.00	08/2023 -	08/2023	0(0) -	0/0
971	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	497.09 -	497.09	.00	02/2023 -	02/2023	0(0) -	0/0
972	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	431.28 -	431.28	4.14	03/2023 -	03/2023	0(0) -	0/0
973	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	486.00	406.73	-	-	-	0/0
974	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	316.60	08/2018 -	-	-	0/0
975	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	109.40	-	-	-	0/0
976	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	498.07	-	-	-	0/0
977	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2021	-	-	0/0
978	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	109.08	09/2021 -	09/2021	-	0/4
979	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
980	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	116.49	11/2015 -	-	-	0/0
981	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	541.35	09/2017 -	09/2019	-	0/0
982	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
983	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,311.10	08/2018 -	-	-	0/0
984	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36(O) -	0/0
985	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
986	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	1,158.53	04/2020 -	12/2020	-	0/0
987	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	348.00	03/2019 01/2021	12/2022	45(O) 3	0/0
988	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,918.36	1,108.00	1,462.67	08/2019 -	-	-	0/0
989	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	-	0/0
990	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,311.37	03/2020 -	-	-	0/0
991	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	171.98	- -	-	-	0/0
992	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,378.36	- -	11/2021	- -	0/0
993	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,498.34	- -	-	-	0/0
994	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	184.91	09/2017 -	-	-	0/0
995	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	162.88	02/2017 -	-	-	0/0
996	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	61.80	06/2019 -	-	-	0/0
997	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	116.36	07/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
998	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	110.75	10/2018 -	-	-	0/0
999	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	318.28	181.43	01/2019 -	-	-	0/0
1000	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	386.41	345.82	10/2018 -	-	-	0/0
1001	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	238.12	02/2017 -	-	-	0/0
1002	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	290.17	03/2017 -	-	-	0/0
1003	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	212.86	03/2017 -	-	-	0/0
1004	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	125.81	01/2016 -	-	-	0/0
1005	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	80.28	05/2018 -	-	-	0/0
1006	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	221.32	08/2017 -	-	-	0/0
1007	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.28	05/2019 -	-	-	0/0
1008	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA , EPC	01/2017	264.34 -	264.34	184.91	09/2017 -	-	-	0/0
1009	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA , EPC	03/2019	423.15 -	423.15	140.05	12/2019 -	-	-	0/0
1010	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	.00	08/2012 -	-	-	0/0
1011	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	314.12	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1012	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	902.51	- 01/2020	01/2020	-	0/0
1013	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	594.02	06/2018 10/2021	10/2021	40(O) -2	0/0
1014	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	629.21	09/2017 -	-	-	0/0
1015	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1016	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA , EPC	02/2017	294.28 -	294.26	138.25	08/2017 -	-	-	0/0
1017	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA , EPC	02/2017	380.76 -	380.76	242.85	09/2017 -	-	-	0/0
1018	KARGIL-ZANSKR PACKAGE-5 - [N24001330]NHIDCL,LADAKH , EPC	08/2020	169.79 -	169.79	40.96	12/2023 -	12/2023	0(O) -	0/4
1019	KARGIL-ZANSKR PACKAGE-1 - [N24001343]NHIDCL,LADAKH , EPC	03/2021	384.23 -	384.23	7.11	01/2023 -	01/2023	0(O) -	0/4
1020	KARGIL-ZANSKR PACKAGE-2 - [N24001344]NHIDCL,LADAKH , EPC	03/2021	404.89 -	404.89	.00	01/2023 -	01/2023	0(O) -	0/4
1021	KARGIL-ZANSKR PACKAGE-3 - [N24001345]NHIDCL,LADAKH , EPC	08/2020	381.01 -	381.01	.00	01/2023 -	01/2023	0(O) -	0/4
1022	KARGIL-ZANSKR PACKAGE-6 - [N24001346]NHIDCL,LADAKH , EPC	01/2021	239.81 -	239.81	31.14	05/2024 -	05/2024	0(O) -	1/4
1023	KARGIL-ZANSKR PACKAGE-7 - [N24001347]NHIDCL,LADAKH , EPC	01/2021	308.86 -	308.86	31.14	06/2024 -	06/2024	0(O) -	1/4
1024	KARGIL-ZANSKR PACKAGE-8 - [N24001348]NHIDCL,LADAKH , EPC	03/2021	398.37 -	398.37	3.39	01/2023 -	01/2023	0(O) -	0/4
1025	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1026	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1027	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	281.69	- 03/2021	03/2022	- 0	0/0
1028	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	392.42	04/2015 -	-	-	0/0
1029	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	686.13	669.94	- -	-	-	0/0
1030	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	691.38	669.35	- -	-	-	0/0
1031	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	448.61	01/2020 06/2021	11/2021	22(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1032	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	773.30	02/2020 08/2021	11/2021	21(O) 2	0/0
1033	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	867.83	- -	-	-	0/0
1034	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1035	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1036	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	742.47	- -	-	-	0/0
1037	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	403.23	08/2017 06/2021	12/2022	64(O) 0	0/0
1038	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	193.99	01/2019 -	-	-	4/4
1039	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	485.73	10/2017 -	-	-	4/4
1040	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	316.97	09/2017 -	-	-	4/4
1041	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	719.29	09/2017 11/2021	11/2021	50(O) 0	3/4
1042	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	282.63	- -	03/2022	- -	3/4
1043	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	415.50	- -	-	-	0/0
1044	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	12/2021	45(O) 2	0/0
1045	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 174.90	174.90	154.26	08/2018 08/2021	12/2021	40(O) 0	0/0
1046	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	61.20	03/2018 04/2021	04/2022	49(O) 0	0/0
1047	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	125.42	02/2018 09/2021	12/2021	46(O) 0	0/0
1048	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	129.31	03/2017 06/2021	12/2021	57(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1049	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	80.06	03/2018 09/2021	06/2022	51(O) 0	0/0
1050	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	226.88	182.97	08/2018 09/2021	12/2021	40(O) 0	0/0
1051	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	166.48	03/2018 10/2021	12/2021	45(O) 0	0/0
1052	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	198.83	07/2018 08/2021	12/2021	41(O) 2	0/0
1053	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	183.37	02/2018 03/2022	03/2022	49(O) 0	0/0
1054	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	223.22	03/2018 11/2021	11/2021	44(O) 0	0/0
1055	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	238.57	09/2019 06/2021	12/2021	27(O) 2	0/0
1056	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	615.21	07/2018 05/2021	12/2021	41(O) 0	0/0
1057	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	743.57	06/2019 04/2021	12/2021	30(O) 0	0/0
1058	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	322.21	06/2019 -	-	-	0/4
1059	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	390.40	03/2018 06/2021	12/2021	45(O) 2	0/0
1060	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	139.54	03/2021 11/2021	03/2022	12(O) 0	0/0
1061	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	429.00	- -	12/2021	- -	2/3
1062	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	297.00	- -	11/2022	- -	2/4
1063	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	827.00	- -	02/2022	- -	2/4
1064	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	486.00	- -	10/2022	- -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1065	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	718.00	12/2019 -	12/2021	24(O) -	2/3
1066	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	556.00	03/2020 -	04/2022	25(O) -	2/3
1067	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	538.00	05/2020 -	05/2022	24(O) -	2/3
1068	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	601.00	03/2020 -	-	-	2/3
1069	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	716.00 -	716.00	.00	07/2021 -	-	-	0/0
1070	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,633.18	03/2013 -	03/2022	108(O) -	0/0
1071	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1072	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	106.56	- -	-	-	0/4
1073	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	303.72	- -	-	-	3/4
1074	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	107.34	- -	-	-	0/0
1075	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	410.01	05/2018 11/2020	11/2020	-	1/1
1076	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	744.73	694.42	05/2018 03/2022	03/2022	46(O) 0	0/0
1077	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 717.24	716.78	622.88	05/2018 03/2022	03/2022	46(O) 0	0/1
1078	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	233.12	03/2019 12/2021	06/2022	39(O) 0	0/0
1079	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	444.50	05/2018 04/2019	06/2021	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1080	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
1081	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	867.59	11/2016 -	-	-	0/0
1082	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1083	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29(O) -	0/0
1084	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29(O) -	0/0
1085	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	978.04	- -	-	-	0/0
1086	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	334.55	- -	-	-	0/0
1087	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	1,154.03	- 10/2021	07/2021	-	3/4
1088	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	435.76	- 01/2022	07/2021	-	2/4
1089	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	167.14	03/2019 -	-	-	0/0
1090	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	128.88	03/2019 -	-	-	0/0
1091	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	315.00	246.70	- 12/2016	05/2017	-	3/4
1092	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 911.07	904.16	.00	02/2020 03/2021	-	-	0/0
1093	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	31.97	03/2020 -	-	-	0/0
1094	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1095	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	.00	03/2020 -	-	-	0/3
1096	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	.00	03/2020 -	-	-	3/3
1097	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1098	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0
1099	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	.00	03/2020 -	-	-	0/3
1100	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 495.24	448.18	481.97	- 05/2021	09/2021	-	0/0
1101	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	510.71	- -	08/2021	-	0/1
1102	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	595.00	- -	-	-	2/3
1103	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	220.18	- -	02/2022	-	0/0
1104	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	224.45	- -	01/2022	-	0/0
1105	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	61.31	- -	07/2021	-	0/0
1106	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	716.34	- -	-	-	0/0
1107	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	183.00	07/2019 -	-	-	0/4
1108	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	98.37	06/2019 -	-	-	0/4
1109	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	219.50	06/2019 -	-	-	0/4
1110	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	160.15	05/2019 -	-	-	0/0
1111	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	314.20	05/2019 -	-	-	0/4
1112	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	230.03	05/2019 -	-	-	0/4
1113	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	401.46	06/2019 -	-	-	0/4
1114	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	237.84	06/2019 -	-	-	0/0
1115	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	258.29	06/2019 -	-	-	0/0
1116	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	231.19	06/2019 -	-	-	0/0
1117	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	321.02	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1118	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	154.69	06/2019 -	-	-	3/4
1119	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	274.75	06/2019 -	-	-	0/0
1120	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	260.43	06/2019 -	-	-	0/4
1121	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	280.56	06/2019 -	-	-	3/4
1122	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	60.66	09/2019 -	-	-	1/4
1123	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	261.86	06/2019 -	-	-	0/4
1124	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4
1125	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	269.58	07/2019 -	-	-	3/4
1126	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	82.35	05/2019 -	-	-	1/4
1127	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	59.88	12/2019 -	-	-	1/4
1128	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	121.71	12/2019 -	-	-	0/4
1129	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	224.47	08/2019 -	-	-	2/4
1130	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	292.53	08/2019 -	-	-	2/4
1131	MANJUSUMBHA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	159.32	08/2019 -	-	-	2/4
1132	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	268.44	05/2019 -	-	-	0/4
1133	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	304.27	07/2019 -	-	-	2/4
1134	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	269.24	07/2019 -	-	-	2/4
1135	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	263.13	12/2019 -	-	-	0/4
1136	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	302.14	07/2019 -	-	-	2/4
1137	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	9.66	05/2020 -	-	-	0/4
1138	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	125.61	- -	-	-	0/4
1139	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	324.19	11/2019 -	-	-	2/4
1140	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	130.63	07/2019 -	-	-	2/4
1141	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	262.66	12/2019 -	-	-	0/4
1142	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	188.65	05/2020 -	-	-	0/4
1143	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	467.78	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1144	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	204.36	11/2019 -	-	-	0/4
1145	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	210.81	07/2019 -	-	-	0/4
1146	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	204.49	11/2019 -	-	-	0/0
1147	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	151.60	07/2019 -	-	-	0/0
1148	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	220.46	12/2019 -	-	-	0/4
1149	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	128.89	12/2019 -	-	-	0/4
1150	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	143.39	12/2019 -	-	-	0/4
1151	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	166.31	12/2019 -	-	-	0/4
1152	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	197.17	06/2019 -	-	-	0/4
1153	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.30	11/2019 -	-	-	0/4
1154	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	223.81	07/2019 -	-	-	0/4
1155	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	302.13	07/2019 -	-	-	0/0
1156	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	194.17	06/2019 -	-	-	0/4
1157	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	136.94	12/2019 -	-	-	0/4
1158	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	-	-	0/4
1159	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	138.05	12/2019 -	-	-	0/4
1160	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	107.85	12/2019 -	-	-	0/4
1161	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	215.00	12/2019 -	-	-	0/4
1162	WADIGODRI TO DHANGRIIMPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	111.20	02/2020 -	-	-	0/4
1163	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	137.57	02/2020 -	-	-	0/4
1164	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	177.80	12/2019 -	-	-	0/4
1165	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	203.39	12/2019 -	-	-	0/4
1166	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	218.03	12/2019 -	-	-	0/4
1167	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	133.93	12/2019 -	-	-	1/4
1168	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	228.09	09/2019 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1169	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	137.99	12/2019 -	-	-	2/4
1170	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	169.59	08/2020 -	-	-	0/4
1171	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	137.37	12/2019 -	-	-	0/4
1172	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	159.42	08/2020 -	-	-	0/0
1173	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	-	-	0/0
1174	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	142.00	08/2020 -	-	-	0/4
1175	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	146.73	12/2019 -	-	-	0/0
1176	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	199.34	12/2019 -	-	-	2/4
1177	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	88.39	12/2019 -	-	-	0/0
1178	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	197.37	06/2020 -	-	-	1/4
1179	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	174.63	12/2019 -	-	-	0/0
1180	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	132.39	12/2019 -	-	-	1/4
1181	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	52.22	12/2019 -	-	-	0/0
1182	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	240.73	12/2019 -	-	-	2/4
1183	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	159.96	05/2020 -	-	-	0/4
1184	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	237.50	06/2019 -	-	-	0/4
1185	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	159.96	07/2019 -	-	-	0/4
1186	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	156.87	11/2019 -	-	-	0/4
1187	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1188	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	193.15	12/2019 -	-	-	0/4
1189	KOLDE TO KHEIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	257.83	07/2019 -	-	-	0/4
1190	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	552.29	12/2019 12/2021	12/2021	24(O) 0	0/0
1191	SATARA TO MHSWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	284.02	07/2019 -	-	-	0/4
1192	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	192.24	12/2019 -	-	-	0/0
1193	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	170.33	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1194	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	199.61	- -	-	-	0/0
1195	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	173.14	03/2019 -	-	-	0/0
1196	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	25.96	05/2020 -	-	-	0/4
1197	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	148.93	12/2019 -	-	-	1/4
1198	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	233.89	07/2019 -	-	-	0/4
1199	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	470.17	08/2019 -	-	-	0/4
1200	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	-	-	0/4
1201	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	170.80	07/2019 -	-	-	0/4
1202	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	174.16	07/2019 -	-	-	0/4
1203	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	191.12	06/2019 -	-	-	2/4
1204	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	170.22	03/2019 -	-	-	0/4
1205	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	80.25	03/2018 -	-	-	0/4
1206	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	9.66	05/2020 -	-	-	0/4
1207	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	145.87	12/2019 -	-	-	0/4
1208	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	154.68	12/2019 -	-	-	0/4
1209	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	167.95	04/2020 -	-	-	1/4
1210	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	74.00	04/2019 -	-	-	0/4
1211	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	172.47	09/2019 -	-	-	2/4
1212	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	135.85	09/2018 -	-	-	0/4
1213	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	791.90	12/2019 -	-	-	1/4
1214	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	1,026.75	11/2019 -	-	-	1/4
1215	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	333.22	06/2019 -	-	-	2/4
1216	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	48.40	07/2019 -	-	-	1/4
1217	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	155.76	06/2019 -	-	-	0/4
1218	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.40	07/2019 -	-	-	0/4
1219	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	210.10	11/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1220	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	155.96	06/2019 -	-	-	0/4
1221	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	186.62	06/2019 -	-	-	0/4
1222	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	330.00	06/2019 -	-	-	0/4
1223	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	232.56	06/2019 -	-	-	0/4
1224	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	310.14	06/2019 -	-	-	0/4
1225	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.64	06/2019 -	-	-	0/0
1226	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	169.64	07/2019 -	-	-	0/4
1227	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	290.00	06/2021 -	-	-	1/4
1228	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	725.27	12/2019 -	-	-	1/4
1229	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	631.68	11/2019 -	-	-	1/4
1230	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	840.10	02/2019 -	-	-	0/0
1231	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-	-	2/4
1232	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-	-	3/5
1233	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	80.76	06/2019 -	-	-	1/4
1234	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	238.22	12/2019 -	-	-	0/0
1235	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	186.55	04/2020 -	-	-	0/4
1236	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA , EPC	02/2019	731.89 731.89	732.34	279.40	11/2019 -	-	-	0/0
1237	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA , EPC	02/2019	362.46 362.46	362.46	201.85	11/2019 -	-	-	0/0
1238	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA , EPC	02/2019	594.75 594.75	606.75	167.02	11/2019 -	-	-	0/0
1239	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	36(O) -	4/4
1240	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL,MANIPUR , EPC	03/2019	471.00 -	471.00	154.09	07/2022 -	07/2022	0(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1241	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR , EPC	03/2020	292.24 -	292.24	36.80	06/2022 -	06/2022	0(0) -	1/4
1242	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR , EPC	06/2020	365.53 -	365.53	42.84	08/2022 -	08/2022	0(0) -	1/4
1243	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	28.20	06/2022 -	06/2022	0(0) -	1/4
1244	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR , EPC	07/2020	177.76 -	177.76	25.18	08/2022 -	08/2022	0(0) -	1/4
1245	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL,MANIPUR , EPC	08/2020	379.39 -	379.39	5.07	04/2022 -	04/2022	0(0) -	0/4
1246	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(0) -	0/4
1247	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(0) -	0/4
1248	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	46.68	06/2022 -	06/2022	0(0) -	1/4
1249	MARIAM - PEREN PKG-1A - [N24001349]NHIDCL,MANIPUR , EPC	02/2021	226.32 -	226.32	.00	12/2022 -	12/2022	0(0) -	0/4
1250	MARIAM - PEREN (PKG 1B) - [N24001350]NHIDCL,MANIPUR , EPC	02/2021	188.36 -	188.36	.00	12/2022 -	12/2022	0(0) -	0/4
1251	MARIAM - PEREN PKG-2B - [N24001351]NHIDCL,MANIPUR , EPC	02/2021	232.26 -	232.26	.00	12/2022 -	12/2022	0(0) -	0/4
1252	IMPHAL – MOREH PACKAGE- 3 - [N24001352]NHIDCL,MANIPUR , EPC	03/2021	259.31 -	259.31	25.85	12/2022 -	12/2022	0(0) -	1/4
1253	IMPHAL - KHONGSANG PKG-2 - [N24001353]NHIDCL,MANIPUR , EPC	03/2021	195.14 -	195.14	.00	12/2022 -	12/2022	0(0) -	0/4
1254	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL,MANIPUR , EPC	03/2021	234.08 -	234.08	.00	12/2022 -	12/2022	0(0) -	0/4
1255	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR , EPC	07/2021	204.58 -	204.58	.00	03/2023 -	03/2023	0(0) -	0/0
1256	IMPHAL – MOREH (PACKAGE 4) - [N24001399]NHIDCL,MANIPUR , EPC	03/2021	277.99 -	277.99	.00	01/2023 -	01/2023	0(0) -	0/0
1257	SENAPATI- IMPHAL PKG-5B - [N24001400]NHIDCL,MANIPUR , EPC	03/2021	211.70 -	211.70	.00	01/2023 -	01/2023	0(0) -	0/4
1258	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR , EPC	07/2021	467.00 -	467.00	.00	03/2023 -	03/2023	0(0) -	0/0
1259	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR , EPC	07/2021	185.80 -	185.80	.00	03/2023 -	03/2023	0(0) -	0/0
1260	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL,MANIPUR , EPC	07/2021	483.87 -	483.87	.00	03/2023 -	03/2023	0(0) -	0/0
1261	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL,MANIPUR , EPC	07/2021	198.77 -	198.77	.00	03/2023 -	03/2023	0(0) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1262	CHURACHANPUR TUIVAI PKG-3 - [N24001405]NHIDCL,MANIPUR , EPC	07/2021	673.27 -	673.27	.00	10/2023 -	10/2023	0(O) -	0/0
1263	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1264	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	197.23	- 09/2021	09/2021	-	2/4
1265	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	133.81	05/2019 -	03/2022	34(O) -	2/4
1266	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]NHIDCL,MEGHALAYA , EPC	11/2020	351.12 -	351.12	171.37	12/2023 -	12/2023	0(O) -	0/4
1267	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]NHIDCL,MEGHALAYA , EPC	11/2020	525.68 -	525.68	288.84	12/2023 -	12/2023	0(O) -	0/4
1268	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]NHIDCL,MEGHALAYA , EPC	11/2020	445.51 -	445.51	173.17	12/2023 -	12/2023	0(O) -	0/4
1269	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]NHIDCL,MEGHALAYA , EPC	11/2020	284.21 -	284.21	40.21	12/2023 -	12/2023	0(O) -	0/4
1270	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL,MEGHALAYA , EPC	10/2020	157.86 -	157.86	53.58	04/2022 -	04/2022	0(O) -	1/4
1271	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]NHIDCL,MEGHALAYA , EPC	03/2021	260.21 -	260.21	38.58	12/2022 -	12/2022	0(O) -	0/4
1272	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	978.43	03/2011 12/2021	-	-	0/0
1273	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021	134(O) 0	0/0
1274	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	368.39	10/2010 12/2021	-	-	0/0
1275	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	83.73	09/2019 -	04/2023	43(O) -	1/4
1276	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	94.28	09/2019 06/2023	07/2023	46(O) 0	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1277	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	106.57	09/2019 04/2023	06/2023	45(O) 0	1/4
1278	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	118.96	09/2019 04/2023	04/2023	43(O) 0	1/4
1279	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	129.40	09/2019 06/2023	04/2023	43(O) 0	1/4
1280	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	126.61	09/2019 04/2023	06/2023	45(O) 0	1/4
1281	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	41.29	09/2019 03/2024	04/2024	55(O) 0	0/4
1282	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	82.60	09/2019 09/2023	09/2023	48(O) 0	1/4
1283	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	308.85	09/2014 12/2021	12/2021	87(O) 0	0/0
1284	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM ,	01/2017	205.95 -	205.95	108.58	01/2021 -	11/2021	10(O) -	0/0
1285	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	24.56	10/2022 -	10/2022	0(O) -	1/4
1286	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	30.06	07/2022 -	07/2022	0(O) -	1/4
1287	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	53.72	07/2022 -	07/2022	0(O) -	1/4
1288	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	49.59	07/2022 -	07/2022	0(O) -	0/4
1289	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	92.39	07/2022 -	07/2022	0(O) -	2/4
1290	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]NHIDCL,MIZORAM , EPC	03/2021	374.39 -	374.39	23.26	12/2022 -	12/2022	0(O) -	0/4
1291	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]NHIDCL,MIZORAM , EPC	03/2021	233.25 -	233.25	.00	12/2022 -	12/2022	0(O) -	0/4
1292	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]NHIDCL,MIZORAM , EPC	03/2021	674.71 -	674.71	12.16	06/2023 -	06/2023	0(O) -	0/4
1293	TLABUNG - LUNGLEI PKG-A - [N24001358]NHIDCL,MIZORAM , EPC	03/2021	698.44 -	698.44	.00	12/2022 -	12/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1294	TLABUNG - LUNGLEI PKG-B - [N24001359]NHIDCL,MIZORAM , EPC	03/2021	740.58 -	740.58	.00	01/2023 -	01/2023	0(O) -	0/4
1295	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	360.15	12/2009 09/2020	09/2020	-	0/0
1296	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1297	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1298	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105(O) -	0/0
1299	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	-	-	0/0
1300	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 1,928.22	1,928.22	1,890.04	04/2015 01/2021	12/2021	80(O) 0	3/4
1301	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,665.00	- -	-	-	0/0
1302	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	11/2021	- -	0/0
1303	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	11/2018	-	0/0
1304	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	342.06	08/2016 -	05/2021	-	3/4
1305	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	304.39	08/2016 -	05/2021	-	3/4
1306	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	315.99	09/2018 -	03/2022	42(O) -	3/4
1307	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	115.32	09/2018 -	11/2022	50(O) -	2/4
1308	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	169.77	09/2018 -	07/2022	46(O) -	2/4
1309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	116.27	09/2018 -	05/2022	44(O) -	2/4
1310	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	89.53	09/2018 -	09/2022	48(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1311	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	115.77	09/2018 -	12/2021	39(O) -	0/4
1312	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	121.06	09/2018 -	12/2021	39(O) -	0/4
1313	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	126.19	09/2018 -	11/2021	38(O) -	3/4
1314	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	146.10	09/2018 -	11/2021	38(O) -	3/4
1315	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	161.15	09/2018 -	11/2021	38(O) -	2/4
1316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	108.86	09/2018 -	11/2021	38(O) -	1/4
1317	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	77.59	09/2018 -	12/2021	39(O) -	1/4
1318	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	63.44	09/2018 -	10/2022	49(O) -	0/4
1319	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	118.61	12/2020 09/2021	-	-	0/0
1320	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	132.43	12/2020 09/2021	-	-	0/0
1321	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	369.96	322.13	09/2019 -	-	-	0/0
1322	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	104.81	11/2020 08/2021	-	-	0/0
1323	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	96.49	12/2022 -	12/2022	0(O) -	0/0
1324	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 177.00	277.44	32.33	10/2022 -	10/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1325	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 -	202.36	3.90	04/2022 -	04/2022	0(0) -	0/4
1326	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 -	315.63	7.80	04/2022 -	04/2022	0(0) -	0/4
1327	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	40.94	04/2022 -	04/2022	0(0) -	1/4
1328	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	39.60	06/2022 -	06/2022	0(0) -	1/4
1329	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	58.14	06/2022 -	06/2022	0(0) -	1/4
1330	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	32.21	06/2022 -	06/2022	0(0) -	1/4
1331	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	54.27	12/2021 -	12/2021	0(0) -	1/4
1332	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	79.89	06/2022 -	06/2022	0(0) -	2/4
1333	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	38.65	12/2021 -	12/2021	0(0) -	1/4
1334	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]NHIDCL,NAGALAND , EPC	03/2020	206.53 -	206.53	81.84	06/2022 -	06/2022	0(0) -	2/4
1335	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL,NAGALAND , EPC	07/2021	258.52 -	258.52	8.04	03/2023 -	03/2023	0(0) -	0/0
1336	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL,NAGALAND , EPC	02/2021	207.33 -	207.33	8.04	03/2023 -	03/2023	0(0) -	0/0
1337	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	14.80	09/2014 -	-	-	0/0
1338	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,873.47	06/2014 -	-	-	0/0
1339	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	720.08	-	-	-	0/0
1340	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	281.06	-	03/2022	-	0/1
1341	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	182.41	08/2015 -	-	-	0/0
1342	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	836.93	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1343	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	633.26	08/2019 -	-	-	0/0
1344	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	1,125.65	- -	-	-	0/0
1345	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	-	0/0
1346	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	100.67	06/2016 -	-	-	0/0
1347	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	1,033.61	03/2020 -	-	-	0/0
1348	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	212.64	07/2017 -	-	-	0/0
1349	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	290.00	- -	-	-	0/0
1350	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	246.25	- -	-	-	0/0
1351	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	468.85	- -	03/2022	-	0/0
1352	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	413.00	- -	-	-	0/0
1353	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	165.60	- -	-	-	0/1
1354	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	309.98	- -	08/2021	-	0/0
1355	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	387.54	- -	-	-	0/1
1356	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	254.00	- -	-	-	0/0
1357	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	512.80	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA ,	01/2018	999.00 -	999.00	178.93	- -	-	-	0/0
1359	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA ,	01/2018	503.88 -	503.88	130.36	- -	-	-	0/0
1360	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA , EPC	03/2018	806.11 -	806.11	362.39	- -	-	-	0/0
1361	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH, ODISHA ,	08/2016	287.70 -	287.70	213.19	02/2017 -	-	-	0/0
1362	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH, ODISHA ,	09/2016	295.67 -	295.67	207.20	02/2017 -	-	-	0/0
1363	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH, ODISHA ,	12/2016	223.50 -	223.50	143.52	08/2018 -	-	-	0/0
1364	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH, ODISHA ,	12/2016	206.88 -	206.88	126.02	04/2018 -	-	-	0/0
1365	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH, ODISHA ,	03/2018	214.23 -	214.23	112.86	08/2018 -	-	-	0/0
1366	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH, ODISHA ,	03/2018	199.16 -	199.16	124.19	08/2018 -	-	-	0/0
1367	4-LANING OF MOGA- TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH, PUNJAB , EPC	11/2015	889.24 -	904.82	851.32	- -	-	-	0/0
1368	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	03/2022	-	0/0
1369	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB ,	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	-	0/0
1370	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB ,	08/2016	1,169.61 - 1,367.00	2,280.00	1,367.00	- -	-	-	0/0
1371	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB ,	03/2017	754.54 -	756.27	443.91	03/2020 -	09/2022	30(O) -	0/0
1372	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB ,	02/2018	261.76 -	207.00	205.00	- -	11/2021	-	0/0
1373	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1374	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1375	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	183.87	08/2020 -	-	-	0/0
1376	JALANDHAR-HOSHIARPUR SECTION OF NH-70 (NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	734.04	10/2019 -	08/2021	-	0/0
1377	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 -	170.57	70.83	11/2020 -	-	-	0/0
1378	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	261.09	08/2020 -	-	-	0/0
1379	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414]NHAI,PUNJAB , EPC	12/2020	733.00 -	733.00	.00	01/2024 -	01/2024	0(O) -	0/0
1380	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB , EPC	12/2020	881.00 -	881.00	.00	04/2024 -	04/2024	0(O) -	0/0
1381	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB , EPC	12/2020	989.66 -	989.66	.00	01/2024 -	01/2024	0(O) -	0/0
1382	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB , EPC	12/2020	1,234.40 -	1,234.40	.00	04/2024 -	04/2024	0(O) -	0/0
1383	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB , EPC	12/2020	1,094.46 -	1,094.46	.00	04/2024 -	04/2024	0(O) -	0/0
1384	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB , EPC	02/2021	1,269.96 -	1,269.96	.00	04/2024 -	04/2024	0(O) -	0/0
1385	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - - [N24001420]NHAI,PUNJAB , EPC	02/2021	853.66 -	853.66	.00	04/2024 -	04/2024	0(O) -	0/0
1386	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1387	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	.00	10/2017 -	-	-	3/4
1388	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1389	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	12/2021	44(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1390	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1391	TWO LANNING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	- -	-	-	0/0
1392	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1393	FOUR LANNING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1394	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	677.75	06/2019 -	-	-	0/0
1395	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	870.48	- -	-	-	0/0
1396	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1397	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,355.00	- -	-	-	0/0
1398	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	1,505.00	- -	03/2022	-	0/0
1399	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	23(O) -	0/0
1400	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	927.72	10/2017 -	-	-	0/0
1401	FOUR LANNING OF DANGIARAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	- -	-	-	0/0
1402	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	708.45	- -	-	-	0/0
1403	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	302.58	- -	-	-	0/0
1404	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	687.07	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1405	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 866.55	866.55	864.82	- 10/2021	10/2021	- 0	0/0
1406	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	496.04	- -	-	-	0/0
1407	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	136.22	04/2018 -	-	-	3/4
1408	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	116.47	04/2018 -	07/2020	-	4/4
1409	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	317.79	06/2018 -	-	-	3/4
1410	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	242.52	05/2018 -	-	-	3/4
1411	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	160.90	- -	-	-	4/4
1412	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	196.71	08/2022 -	08/2022	0(0) -	0/4
1413	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	62.45	08/2020 -	-	-	0/4
1414	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	34.51	11/2020 -	-	-	1/4
1415	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN , EPC	07/2020	319.09 -	319.09	.00	09/2021 -	09/2021	-	0/0
1416	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN , EPC	08/2020	216.72 -	216.72	.00	12/2020 -	-	-	0/0
1417	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN , EPC	12/2020	379.23 -	379.23	.00	10/2021 -	10/2021	0(0) -	0/0
1418	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 & KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN , EPC	12/2020	339.65 -	339.65	.00	10/2021 -	10/2021	0(0) -	0/0
1419	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN , EPC	02/2021	240.99 -	240.99	.00	11/2021 -	11/2021	0(0) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1420	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	295.14	10/2017 -	-	-	3/4
1421	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	69.32	- -	-	-	2/4
1422	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	154.83	11/2017 -	12/2021	49(O) -	2/4
1423	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	63.83	06/2018 -	-	-	1/4
1424	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	56.40	04/2022 -	04/2022	0(O) -	1/4
1425	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	27.06	04/2023 -	04/2023	0(O) -	0/4
1426	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	32.98	06/2022 -	06/2022	0(O) -	0/4
1427	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	21.62	04/2023 -	04/2023	0(O) -	0/4
1428	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	74.52	04/2023 -	04/2023	0(O) -	0/4
1429	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM , EPC	09/2020	183.31 -	183.31	75.61	05/2022 -	05/2022	0(O) -	0/4
1430	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL,SIKKIM , EPC	09/2020	262.84 -	262.84	118.63	05/2023 -	05/2023	0(O) -	0/4
1431	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM , EPC	08/2020	292.80 -	292.80	27.45	05/2022 -	05/2022	0(O) -	0/4
1432	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]NHIDCL,SIKKIM , EPC	08/2020	230.45 -	230.45	2.58	04/2023 -	04/2023	0(O) -	0/4
1433	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL,SIKKIM , EPC	10/2020	493.42 -	493.42	.00	11/2023 -	11/2023	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1434	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]NHIDCL,SIKKIM , EPC	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023	0(O) -	0/4
1435	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]NHIDCL,SIKKIM , EPC	01/2021	332.20 -	332.20	.00	09/2023 -	09/2023	0(O) -	0/4
1436	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]NHIDCL,SIKKIM , EPC	12/2020	410.60 -	410.60	.00	02/2024 -	02/2024	0(O) -	0/4
1437	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-	-	0/0
1438	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	6.35	06/2013 -	09/2021	-	0/0
1439	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	77.82	05/2013 -	02/2022	105(O) -	0/0
1440	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	264.10	08/2013 -	-	-	0/0
1441	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	90.50	04/2014 -	01/2022	93(O) -	0/0
1442	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 - 273.27	268.92	229.77	08/2015 -	-	-	0/4
1443	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1444	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	32.96	12/2017 -	05/2023	65(O) -	0/0
1445	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1446	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1447	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	429.86	08/2018 -	01/2022	41(O) -	0/0
1448	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	398.58	07/2018 -	12/2021	41(O) -	0/0
1449	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	243.59	03/2020 -	12/2021	21(O) -	0/0
1450	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	398.58	07/2016 -	12/2021	65(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1451	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59(O) -	0/0
1452	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	178.41	09/2017 -	-	-	0/0
1453	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	770.94	09/2017 -	07/2022	58(O) -	0/0
1454	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	242.86	- -	03/2021	-	0/0
1455	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,296.93	346.17	- -	01/2022	-	0/0
1456	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
1457	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	382.61	- -	03/2022	-	0/0
1458	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1459	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	309.05	- -	01/2022	-	0/0
1460	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	12/2021	-	0/0
1461	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU ,	03/2019	297.55 -	297.55	210.16	11/2019 -	-	-	3/4
1462	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 204.73	240.38	129.04	06/2019 -	-	-	3/4
1463	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	3,426.00	.00	12/2021 -	12/2021	0(O) -	0/0
1464	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU , EPC	08/2020	302.62 -	302.62	51.88	02/2021 -	-	-	0/4
1465	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1466	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	.00	03/2016 -	-	-	1/4
1467	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA , EPC	10/2014	295.47 -	295.47	207.71	02/2017 -	-	-	0/1
1468	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0
1469	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	1,003.47	11/2018 -	10/2021	35(O) -	0/0
1470	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1471	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	456.99	- -	-	-	0/0
1472	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	673.91	- -	-	-	0/0
1473	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	305.87	- -	-	-	0/0
1474	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1475	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	121.09	02/2019 -	-	-	0/0
1476	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	124.12	03/2019 -	-	-	0/0
1477	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	165.50	05/2019 -	-	-	0/0
1478	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	115.95	10/2019 -	-	-	0/0
1479	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	242.66	12/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1480	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	301.86	05/2019 -	-	-	0/0
1481	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	205.58	05/2019 -	-	-	0/0
1482	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	138.84	05/2020 -	-	-	0/0
1483	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	209.06	12/2019 -	-	-	0/0
1484	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA ,	02/2018	206.13 -	206.13	174.09	06/2020 -	-	-	0/0
1485	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA ,	02/2018	294.13 -	294.13	147.88	11/2019 -	-	-	0/0
1486	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA ,	02/2018	220.28 -	220.28	148.95	11/2019 -	-	-	0/0
1487	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA ,	02/2018	426.52 -	426.52	391.57	04/2020 -	-	-	0/0
1488	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	192.25	09/2020 -	-	-	0/0
1489	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	207.51	07/2020 -	-	-	0/0
1490	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	407.38	10/2019 -	-	-	0/0
1491	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	164.44	07/2019 -	-	-	0/0
1492	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	100.34	- -	-	-	0/0
1493	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	358.78	03/2018 -	-	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1494	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	142.81	08/2020 -	11/2021	15(O) -	0/0
1495	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA , EPC	03/2020	247.76 -	247.76	19.60	01/2022 -	01/2022	0(O) -	1/4
1496	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA , EPC	06/2020	347.36 -	347.36	66.04	01/2022 -	01/2022	0(O) -	1/4
1497	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA , EPC	06/2020	277.50 -	277.50	103.62	01/2022 -	01/2022	0(O) -	1/4
1498	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA , EPC	03/2020	154.51 -	154.51	39.78	07/2022 -	07/2022	0(O) -	1/4
1499	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL,TRIPURA , EPC	03/2020	178.43 -	178.43	10.30	07/2022 -	07/2022	0(O) -	1/4
1500	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA , EPC	01/2017	197.67 -	236.18	33.22	12/2022 -	12/2022	0(O) -	0/0
1501	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]NHIDCL,TRIPURA , EPC	11/2020	332.14 -	332.14	10.88	07/2022 -	07/2022	0(O) -	1/4
1502	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]NHIDCL,TRIPURA , EPC	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022	0(O) -	0/4
1503	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]NHIDCL,TRIPURA , EPC	11/2020	280.91 -	280.91	59.89	07/2022 -	07/2022	0(O) -	1/4
1504	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]NHIDCL,TRIPURA , EPC	11/2020	206.78 -	206.78	52.08	07/2022 -	07/2022	0(O) -	1/4
1505	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA , EPC	06/2020	201.99 -	201.99	18.87	01/2022 -	01/2022	0(O) -	0/4
1506	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]NHIDCL,TRIPURA , EPC	09/2020	173.17 -	173.17	5.10	04/2022 -	04/2022	0(O) -	1/4
1507	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]NHIDCL,TRIPURA , EPC	06/2020	257.96 -	257.96	95.22	01/2022 -	01/2022	0(O) -	3/4
1508	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]NHIDCL,TRIPURA , EPC	03/2020	165.54 -	165.54	5.26	07/2022 -	07/2022	0(O) -	1/4
1509	MANU-SIMLUNG (PKG 4) - [N24001363]NHIDCL,TRIPURA , EPC	03/2021	354.79 -	354.79	.00	12/2022 -	12/2022	0(O) -	0/4
1510	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	-	-	0/0
1511	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	469.31	459.07	01/2014 -	-	-	0/0
1512	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-	-	0/0
1513	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 319.96	319.96	193.43	03/2016 04/2022	04/2022	73(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1514	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1515	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	417.68	433.68	01/2016 -	-	-	0/0
1516	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	242.67	09/2016 -	-	-	0/0
1517	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	627.93	633.24	01/2016 -	-	-	0/0
1518	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1519	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1520	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1521	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1522	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1523	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	141.33	08/2015 -	01/2021	-	0/0
1524	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	987.94	.00	-	-	-	0/2
1525	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	985.40	04/2019 -	-	-	0/0
1526	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	-	-	-	0/0
1527	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	-	-	-	0/0
1528	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1529	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	450.47	04/2019 10/2022	10/2022	42(O) 0	0/0
1530	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	-	-	-	0/0
1531	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 827.05	827.05	387.83	- 07/2022	07/2022	- 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1532	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 1,201.51	1,201.51	1,077.55	- 06/2021	09/2021	-	0/0
1533	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1534	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	-	-	0/0
1535	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1536	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	1,285.31	03/2020 12/2021	12/2021	21(O) 0	3/4
1537	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,294.21	03/2020 -	-	-	3/4
1538	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	766.64	03/2020 -	-	-	0/0
1539	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	-	0/0
1540	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	1,084.94	- -	-	-	0/0
1541	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1542	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1543	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1544	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	75.10	- -	-	-	0/0
1545	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	838.28	- -	-	-	0/0
1546	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,176.70	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1547	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	- -	0/0
1548	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,315.69	- -	-	-	0/0
1549	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,517.15	- -	-	-	0/0
1550	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	222.94	- -	-	-	0/0
1551	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	332.69	- -	-	-	0/0
1552	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1553	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	123.44	- -	12/2021	- -	0/0
1554	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	145.76	09/2019 -	10/2019	-	0/0
1555	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	-	0/0
1556	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	229.57	05/2019 -	04/2021	-	0/0
1557	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,650.78	01/2019 -	-	-	0/0
1558	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	147.70	03/2020 03/2020	03/2021	-	0/0
1559	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	183.54	10/2019 -	03/2021	-	0/0
1560	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	188.89	04/2020 -	03/2022	23(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1561	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.69	02/2020 -	01/2021	-	0/0
1562	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	192.35	08/2020 -	12/2021	16(O) -	0/0
1563	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	237.29	09/2020 -	11/2021	14(O) -	0/0
1564	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	195.15	- -	11/2021	- -	0/0
1565	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 319.96	319.96	115.07	- -	03/2022	- -	0/0
1566	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 720.81	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1567	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	-	-	0/0
1568	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	206.32	- 10/2022	-	-	0/0
1569	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	-	-	0/0
1570	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 02/2022	02/2022	43(O) 0	0/0
1571	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	126.90	05/2018 -	03/2022	46(O) -	3/4
1572	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	217.43	06/2018 -	03/2022	45(O) -	3/4
1573	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	265.48	05/2018 -	03/2022	46(O) -	3/4
1574	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	214.90	12/2019 07/2021	07/2021	-	0/0
1575	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	185.44	12/2019 07/2021	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1576	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	234.12	12/2019 08/2021	08/2021	-	0/0
1577	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	207.83	06/2019 12/2021	12/2021	30(O) 0	0/0
1578	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	171.22	11/2019 07/2021	07/2021	-	0/0
1579	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	259.90	11/2019 05/2021	05/2021	-	0/0
1580	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	186.16	11/2019 10/2020	10/2020	-	0/0
1581	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	287.56	02/2020 09/2021	09/2021	-	0/0
1582	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	183.73	- 10/2021	10/2021	- 0	0/0
1583	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021	19(O) 0	0/0
1584	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	116.25	- -	-	-	0/0
1585	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	280.16	07/2018 -	07/2022	48(O) -	2/5
1586	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	234.88	174.51	12/2017 12/2020	12/2020	-	0/0
1587	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	11/2021	99(O) -	3/4
1588	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023	118(O) -	3/4
1589	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	1,396.18	09/2014 -	-	-	0/0
1590	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 363.93	363.93	277.34	- -	-	-	0/0
1591	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 2,587.75	1,827.15	989.55	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1592	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,511.49	- -	-	-	0/0
1593	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	.00	11/2018 -	-	-	0/0
1594	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	696.60	08/2018 -	-	-	0/0
1595	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 2,145.96	1,952.20	97.16	- -	-	-	0/0
1596	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL ,	03/2016	271.17 291.20	291.20	120.51	11/2018 01/2021	03/2022	40(O) 0	0/0
1597	REHABILITATION AND UPGRADEATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021	25(O) 0	0/0
1598	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	254.43	09/2020 01/2022	01/2022	16(O) 0	0/0
1599	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	111.78	11/2020 04/2021	06/2021	-	0/0
1600	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO) - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	118.34	10/2020 03/2021	06/2021	-	0/0
1601	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	26.91	08/2019 -	11/2022	39(O) -	0/0
1602	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 263.26	263.26	77.57	08/2019 08/2022	08/2022	36(O) 0	0/0
1603	REHABILITATION AND UPGRADEATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.52	398.52	331.86	08/2017 -	02/2020	-	0/0
	Total		5,35,763.35 -	5,50,414.28	3,28,536.82				472/1510
	SHIPPING AND PORTS								
1604	JAL MARG VIKAS PROJECT - [N25000072]IWAJ, MULTI STATE ,	01/2018	5,369.18 4,633.81	4,633.81	1,940.64	03/2023 -	03/2023	0(O) -	1/7
	Total		5,369.18 -	4,633.81	1,940.64				1/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	TELECOMMUNICATIONS								
1605	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI ,	10/2014	248.20 -	248.20	145.26	03/2018 -	12/2021	45(O) -	3/5
1606	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 24,664.00	24,664.00	20,545.00	07/2015 05/2020	03/2022	80(O) 0	0/0
1607	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE , Central Sector Projects	03/2020	431.16 422.87	422.87	46.37	06/2021 11/2021	11/2021	5(O) 0	0/0
	Total		14,013.36 -	25,335.07	20,736.63				3/5
	URBAN DEVELOPMENT								
1608	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL,BIHAR ,	02/2019	13,365.77 -	13,925.50	302.95	06/2024 -	06/2024	0(O) -	0/0
1609	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH ,	05/2019	299.97 299.97	299.97	20.39	09/2020 01/2023	01/2023	28(O) 0	0/6
1610	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	39,486.58	03/2016 08/2021	-	-	1/1
1611	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 217.00	217.00	173.51	04/2019 02/2022	02/2022	34(O) 0	1/2
1612	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	896.32	- -	12/2022	- -	0/9
1613	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 238.56	238.56	208.13	05/2020 11/2021	11/2021	18(O) 0	2/2
1614	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 422.00	422.00	108.75	03/2021 06/2023	06/2023	27(O) 0	0/0
1615	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 392.00	392.00	161.81	08/2020 06/2022	06/2022	22(O) 0	1/5
1616	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 1,100.80	1,100.80	35.74	07/2021 06/2023	06/2023	23(O) 0	0/6
1617	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 1,128.00	1,128.00	30.00	03/2022 -	06/2023	15(O) -	0/0
1618	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	2,442.28	03/2025 -	03/2025	0(O) -	0/1
1619	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	484.46	12/2020 09/2021	-	-	1/1
1620	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	9,472.48	12/2018 -	08/2022	44(O) -	0/1
1621	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	247.58	03/2024 -	03/2024	0(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1622	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	208.21	03/2024 -	03/2024	0(O) -	0/1
1623	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 30,695.12	30,695.12	18,874.67	02/2019 03/2025	03/2025	73(O) 0	152/249
1624	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 6,218.14	6,218.14	6,059.17	07/2017 09/2020	09/2020	-	0/0
1625	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	248.29	02/2023 -	02/2023	0(O) -	0/0
1626	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	142.54	02/2023 -	02/2023	0(O) -	0/0
1627	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	8,427.24	03/2018 12/2021	12/2021	45(O) 0	0/0
1628	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	19,493.96	03/2020 03/2023	03/2023	36(O) 0	0/0
1629	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 11,420.00	11,420.00	7,187.19	11/2021 12/2022	12/2022	13(O) 0	0/0
1630	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	5,222.09	06/2025 -	06/2025	0(O) -	0/8
1631	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 18,380.00	18,380.00	17,619.68	12/2015 02/2019	02/2019	-	24/24
1632	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	2,996.83	03/2018 02/2021	02/2021	-	8/21
1633	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	6,928.00	03/2019 -	03/2019	-	0/0
1634	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	1,917.78	03/2024 -	03/2025	12(O) -	0/0
1635	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	426.47	03/2024 -	05/2025	14(O) -	0/0
	Total		2,76,487.00 -	2,98,377.53	1,49,823.10				190/338
	<u>WATER RESOURCES</u>								
1636	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	18,317.91	03/2020 11/2021	04/2022	25(O) 0	0/19
1637	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL FOR WATER,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	-	-	5/7
1638	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	90.99	07/2021 -	07/2021	-	0/0
1639	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	413.29	.05	09/2020 -	-	-	0/0
1640	I AND D AND STP AT CHAPPRRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	59.84	12/2020 06/2021	-	-	0/0
1641	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	28.31	08/2021 -	12/2021	4(O) -	0/0
1642	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1643	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	398.90	291.32	03/2020 -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1644	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	326.75	01/2021 -	-	-	0/0
1645	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	130.39	04/2021 -	04/2021	-	0/0
1646	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	64.43	11/2020 03/2021	-	-	0/0
1647	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	199.50	05/2021 -	05/2021	-	0/0
1648	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	42.75	06/2022 -	06/2022	0(0) -	0/0
1649	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	42.75	06/2022 -	06/2022	0(0) -	0/0
1650	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	230.58	12/2022 -	12/2022	0(0) -	0/0
1651	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	108.28	12/2021 -	12/2022	12(0) -	0/0
1652	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	149.02	02/2022 -	12/2022	10(0) -	0/0
1653	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	336.27	01/2021 -	06/2021	-	0/0
1654	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1655	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	148.83	12/2019 -	12/2021	24(0) -	0/0
1656	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	132.29	09/2021 -	09/2021	-	0/0
1657	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 261.12	261.12	.00	03/2022 -	03/2022	0(0) -	0/0
1658	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	65.24	09/2021 -	09/2021	-	0/0
1659	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	-	0/0
1660	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	248.16	12/2020 -	05/2021	-	0/0
1661	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 330.05	330.05	260.12	12/2019 -	01/2021	-	0/0
1662	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	14.63	12/2021 -	12/2021	0(0) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1663	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	53.62	10/2021 -	10/2021	0(0) -	0/0
1664	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	690.71	.00	06/2022 -	06/2022	0(0) -	0/0
1665	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 213.91	213.91	.00	07/2021 -	06/2022	11(0) -	0/0
1666	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	84.32	11/2019 03/2021	-	-	0/0
1667	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(0) -	0/0
1668	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(0) -	0/0
1669	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(0) -	0/0
1670	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 224.69	224.69	.00	02/2022 -	06/2022	4(0) -	0/0
1671	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(0) -	0/0
1672	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(0) -	0/0
1673	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 154.73	154.73	.00	02/2022 -	10/2022	8(0) -	0/0
1674	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	11.56	12/2021 -	12/2021	0(0) -	0/0
1675	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	220.08	12/2019 05/2021	-	-	0/0
1676	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	248.86	04/2020 -	03/2021	-	0/0
1677	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	11.56	12/2021 -	12/2021	0(0) -	0/0
1678	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	11.56	12/2021 -	12/2021	0(0) -	0/0
	Total		24,702.19 -	70,243.27	22,642.34				5/26
	DEFENCE PRODUCTION								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1679	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD FOR DEFENC,KARNATAKA ,	12/2016	246.31 210.00	210.00	149.80	02/2020 10/2021	12/2021	22(O) 0	8/10
	Total		246.31 -	210.00	149.80				8/10
	COMMERCE								
1980	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI ,	06/2018	302.64 302.64	302.64	30.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	30.00				0/0
	Grand Total		21,74,182.86	26,08,330.02	12,64,545.31				2987/5961

FLASH REPORT


Summary of projects in the Flash Report for the month of October, 2021

Project Implementation - Current Status:

Number of Projects in Previous Month	1670
Number of Projects completed/dropped/frozen in Current Month	19
Number of Projects elevated to the status of Major project during the current month	13
Number of Projects Added in Current Month	16
Number of Projects in Current Month	1680

Brief Analysis

Project Status with respect to Original Schedule: Out of 1680 projects, 12 projects are ahead of schedule, 292 projects are on schedule 539 projects are delayed. 729 projects do not have fixed dates of commissioning. 108 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

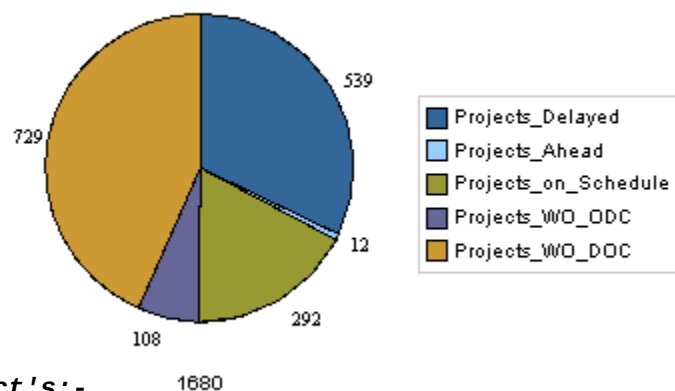


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1680 projects when sanctioned, was of the order of Rs. 2174182.86 crore but this was subsequently revised to Rs. 2608330.02 crore implying a cost overrun of 20%. The expenditure incurred on these projects till October, 2021 is Rs. 1264545.31 crore, which is 48.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

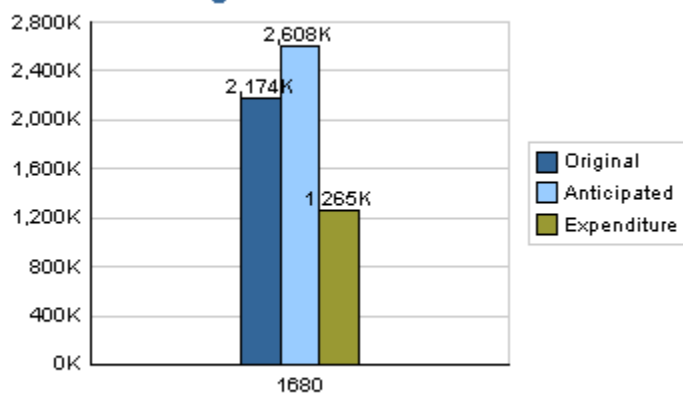

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

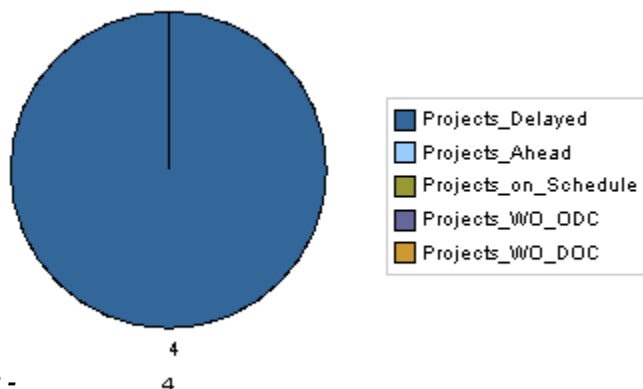

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till October, 2021 is Rs. 62664.37 crore, which is 78% of the anticipated cost of the projects.

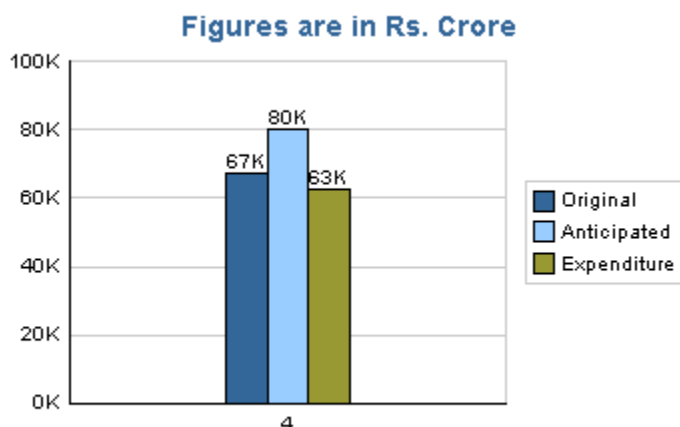

Sector wise current status of projects on the Flash Report

HOME AFFAIRS


Current Status:

Number of Projects	6
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 1 project is on schedule 3 projects are delayed. 2 projects do not have fixed dates of commissioning.

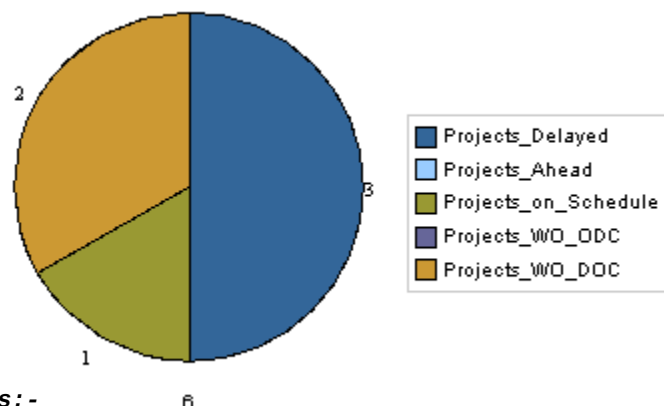


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 2139.99 crore but this was subsequently anticipated to Rs. 3160.62 crore implying a cost overrun of 47.7%. The expenditure incurred on these projects till October, 2021 is Rs. 1227.84 crore, which is 38.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

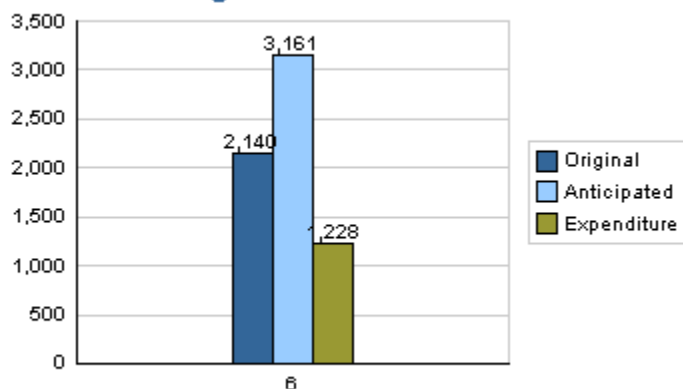

Sector wise current status of projects on the Flash Report

DEPARTMENT OF HIGHER EDUCATION


Current Status:

Number of Projects	23
Number of Projects On Schedule	2
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	8
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 23 projects, 2 projects are on schedule 13 projects are delayed. 8 projects do not have fixed dates of commissioning.

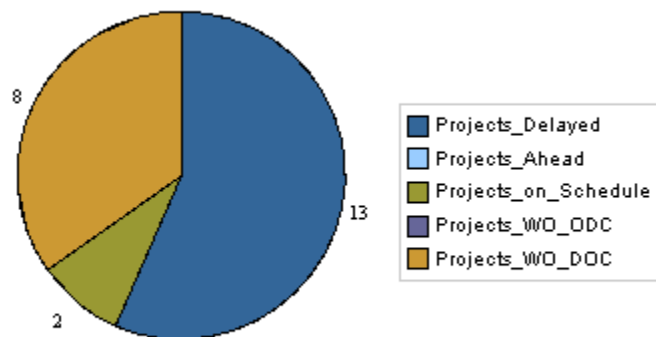


Total No Of Project's:-

23

Investment Scenario

Total original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 10311.33 crore but this was subsequently anticipated to Rs. 10416.24 crore implying a cost overrun of 1%. The expenditure incurred on these projects till October, 2021 is Rs. 3303.35 crore, which is 31.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

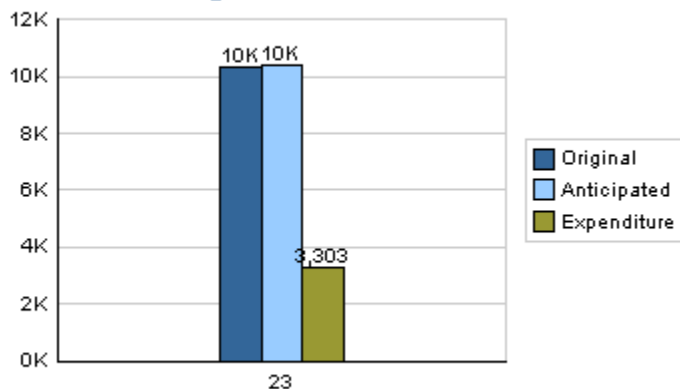

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	43
Number of Projects On Schedule	16
Number of Projects Delayed	8

Number of Projects Without Date Of Commissioning 19

Brief Analysis

Project Status with respect to Original Schedule: Out of 43 projects, 16 projects are on schedule 8 projects are delayed. 19 projects do not have fixed dates of commissioning.

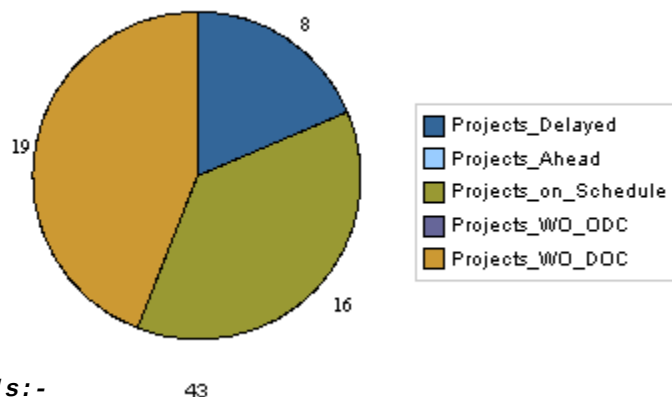


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 43 projects when sanctioned, was of the order of Rs. 24702.19 crore but this was subsequently anticipated to Rs. 70243.27 crore implying a cost overrun of 184.4%. The expenditure incurred on these projects till October, 2021 is Rs. 22642.34 crore, which is 32.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

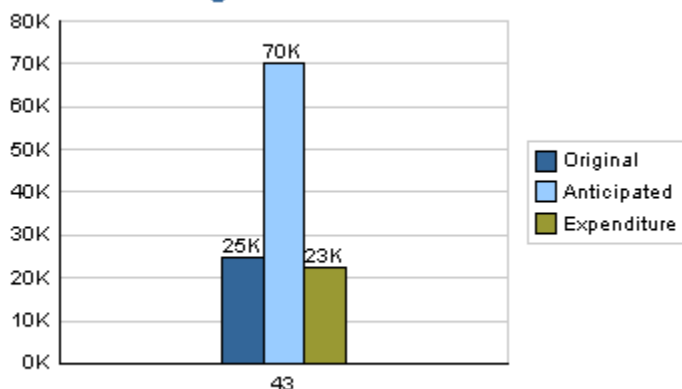

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	28
Number of Projects On Schedule	7
Number of Projects Delayed	14

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 7 projects are on schedule 14 projects are delayed. 6 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

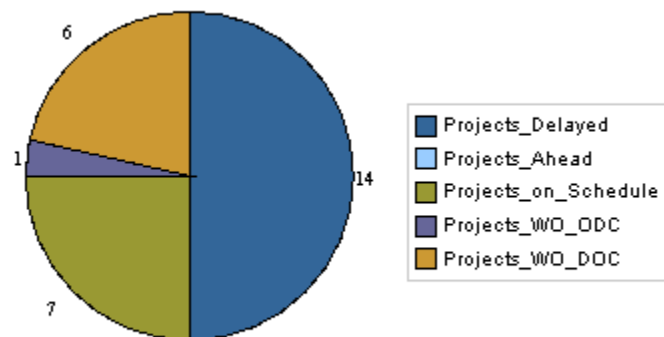


Total No Of Project's:-

28

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 276487 crore but this was subsequently anticipated to Rs. 298377.53 crore implying a cost overrun of 7.9%. The expenditure incurred on these projects till October, 2021 is Rs. 149823.1 crore, which is 50.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

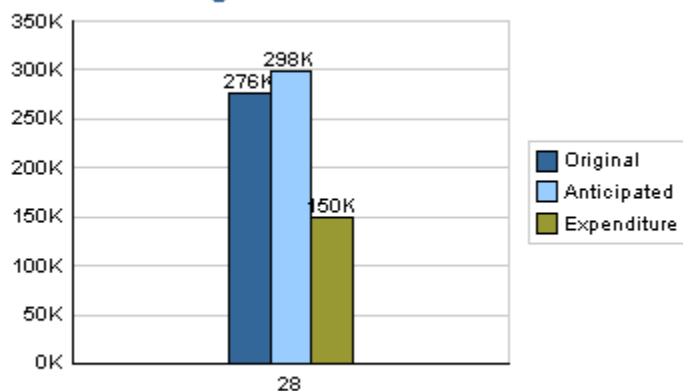

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed.

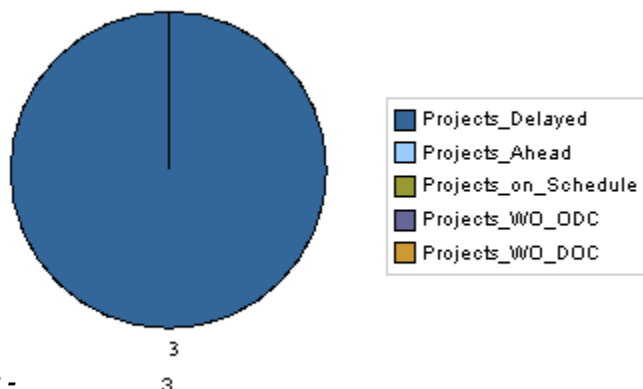


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 25335.07 crore implying a cost overrun of 80.8%. The expenditure incurred on these projects till October, 2021 is Rs. 20736.63 crore, which is 81.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

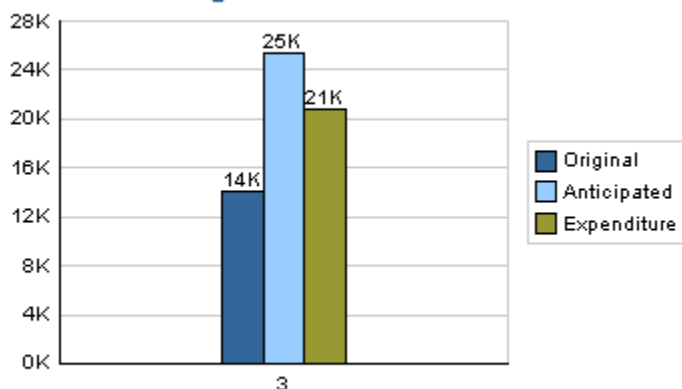

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	887
Number of Projects On Schedule	140
Number of Projects Delayed	130

Number of Projects Without Original Date of Commissioning	44
Number of Projects Without Date Of Commissioning	573

Brief Analysis

Project Status with respect to Original Schedule: Out of 887 projects, 140 projects are on schedule 130 projects are delayed. 573 projects do not have fixed dates of commissioning. 44 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

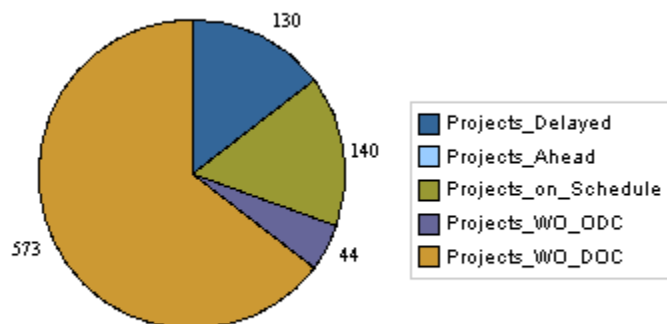


Total No Of Project's:-

887

Investment Scenario

Total original cost of implementation of 887 projects when sanctioned, was of the order of Rs. 535763.35 crore but this was subsequently anticipated to Rs. 550414.28 crore implying a cost overrun of 2.7%. The expenditure incurred on these projects till October, 2021 is Rs. 328536.82 crore, which is 59.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

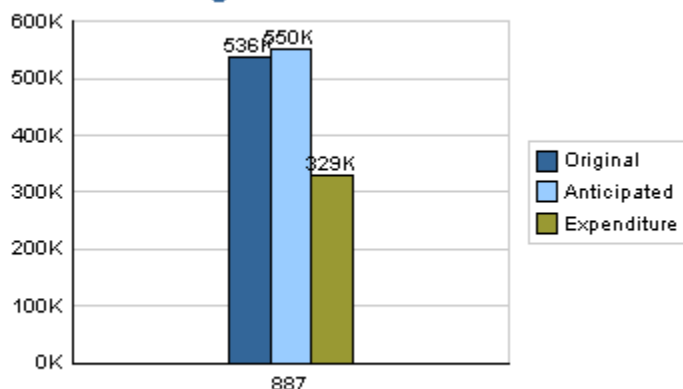

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	287
Number of Projects On Schedule	15
Number of Projects Delayed	142
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	55
Number of Projects Without Date Of Commissioning	70

Brief Analysis

Project Status with respect to Original Schedule: Out of 287 projects, 5 projects are ahead of schedule, 15 projects are on schedule 142 projects are delayed. 70 projects do not have fixed dates of commissioning. 55 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

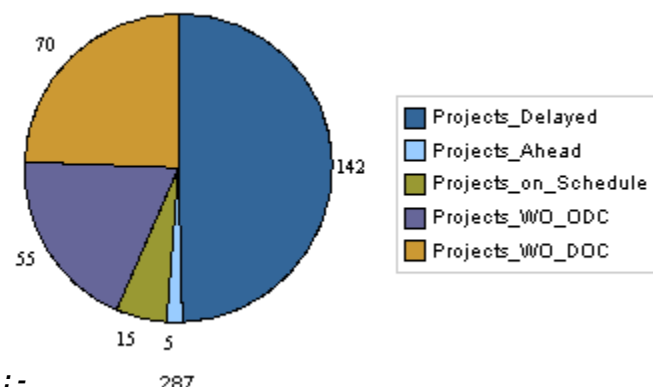


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 287 projects when sanctioned, was of the order of Rs. 454260.58 crore but this was subsequently anticipated to Rs. 693056.85 crore implying a cost overrun of 52.6%. The expenditure incurred on these projects till October, 2021 is Rs. 266992.14 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

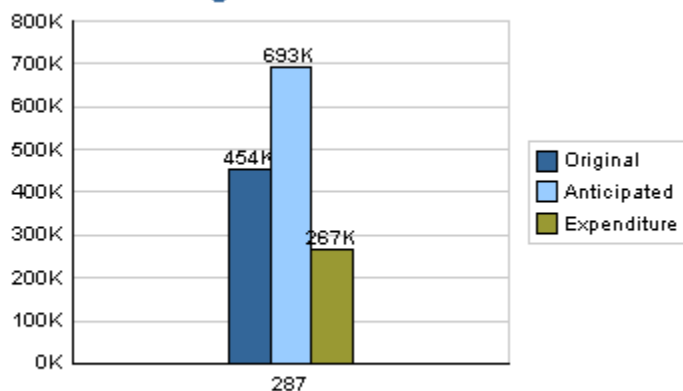

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	29
Number of Projects On Schedule	2
Number of Projects Delayed	6
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	16

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 1 project is ahead of schedule, 2 projects are on schedule 6 projects are delayed. 16 projects do not have fixed dates of commissioning. 4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

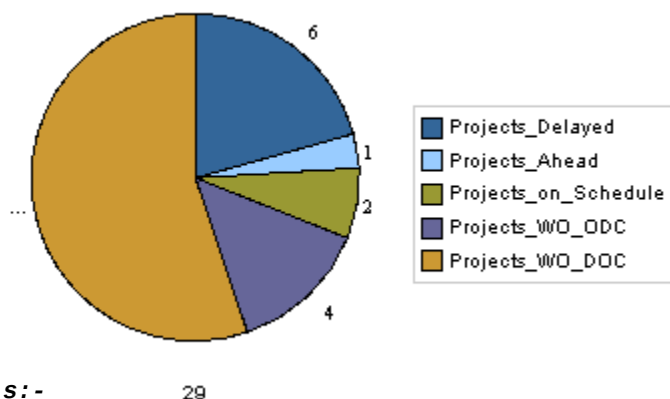


Total No Of Project's:-

29

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 15273.26 crore but this was subsequently anticipated to Rs. 15715.78 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till October, 2021 is Rs. 9026.7 crore, which is 57.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

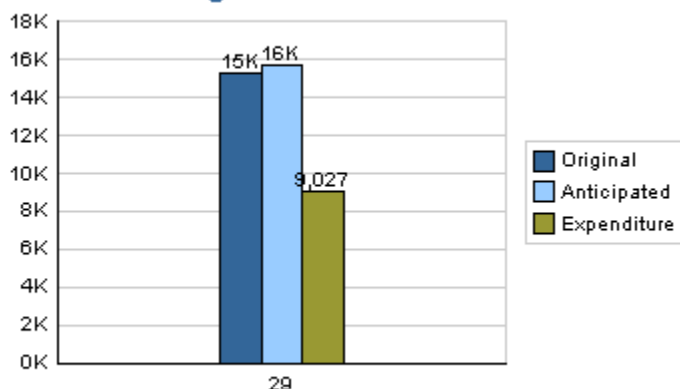

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	62
Number of Projects On Schedule	9
Number of Projects Delayed	44
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 62 projects, 1 project is ahead of schedule, 9 projects are on schedule 44 projects are delayed. 7 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

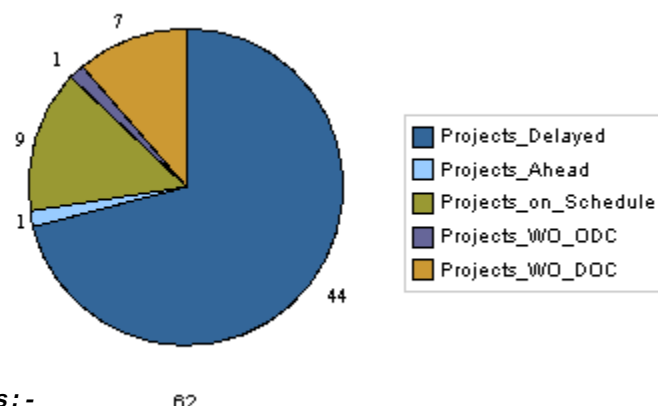


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 62 projects when sanctioned, was of the order of Rs. 207257.24 crore but this was subsequently anticipated to Rs. 268103.37 crore implying a cost overrun of 29.4%. The expenditure incurred on these projects till October, 2021 is Rs. 174646.26 crore, which is 65.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

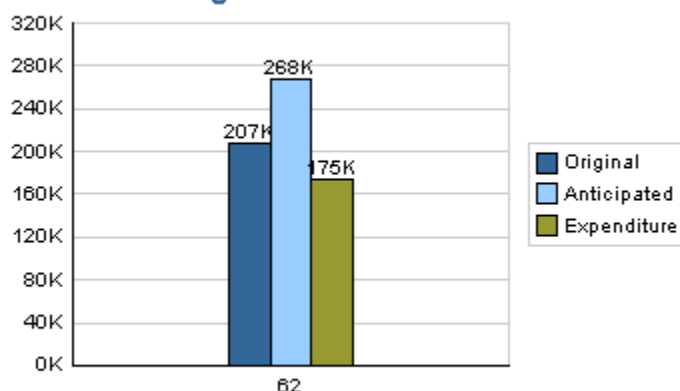

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	151
Number of Projects On Schedule	52
Number of Projects Delayed	85
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 151 projects, 5 projects are ahead of schedule, 52 projects are on schedule 85 projects are delayed. 7 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

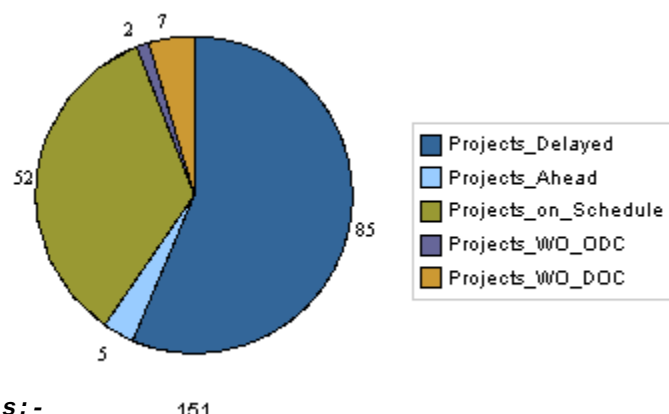


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 151 projects when sanctioned, was of the order of Rs. 341221.64 crore but this was subsequently anticipated to Rs. 352793.57 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till October, 2021 is Rs. 119873.17 crore, which is 34% of the anticipated cost of the projects.

Figures are in Rs. Crore

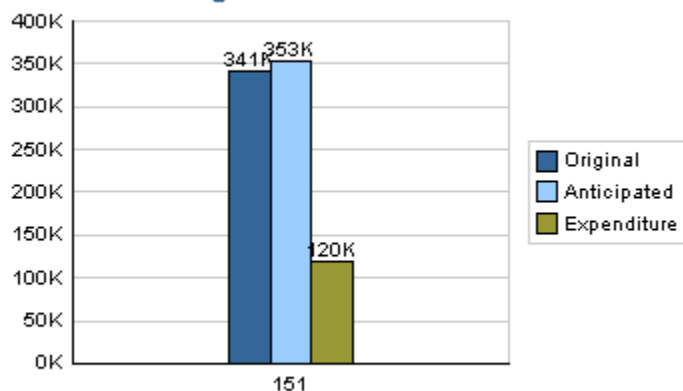

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	8
Number of Projects On Schedule	3
Number of Projects Delayed	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule 5 projects are delayed.

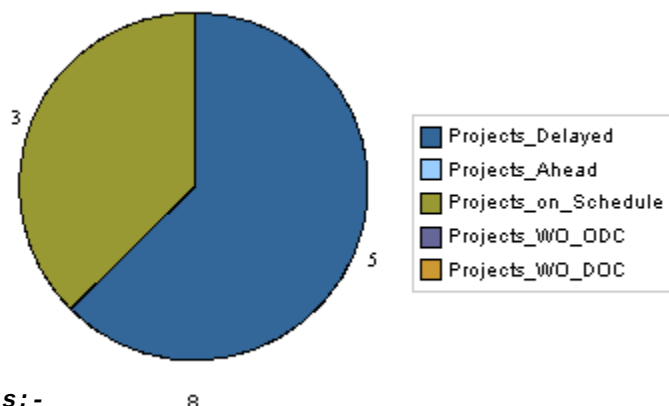


Total No Of Project's:-

8

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 25189.15 crore but this was subsequently anticipated to Rs. 32021.3 crore implying a cost overrun of 27.1%. The expenditure incurred on these projects till October, 2021 is Rs. 24076.03 crore, which is 75.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

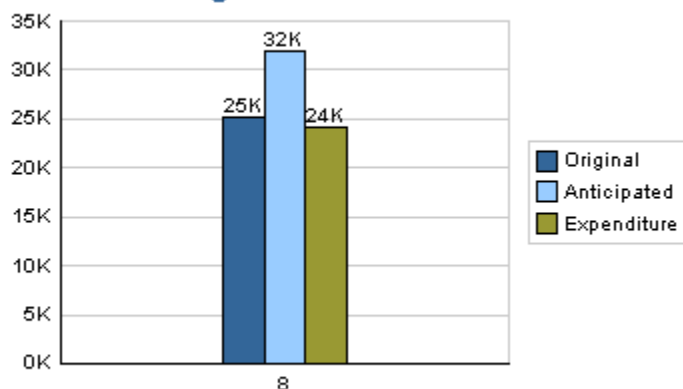

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	6
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 1 project is on schedule 3 projects are delayed. 2 projects do not have fixed dates of commissioning.

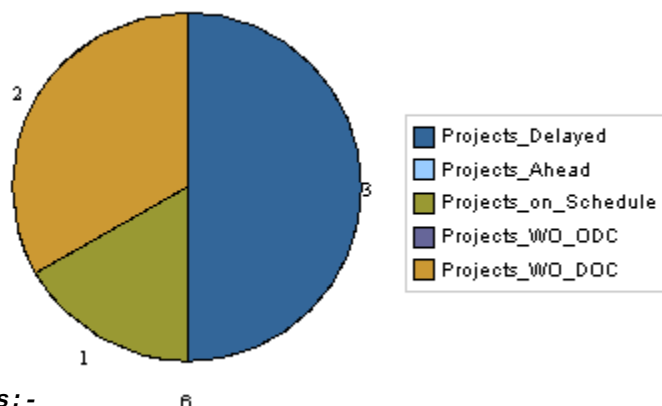


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 7333.99 crore but this was subsequently anticipated to Rs. 7330.54 crore. The expenditure incurred on these projects till October, 2021 is Rs. 1618.41 crore, which is 22.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

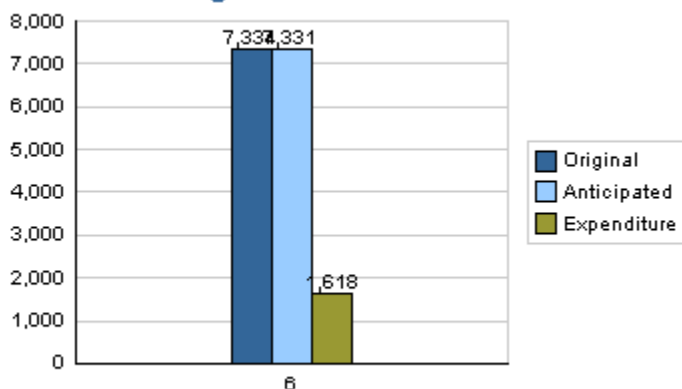

Sector wise current status of projects on the Flash Report

FERTILISERS

Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

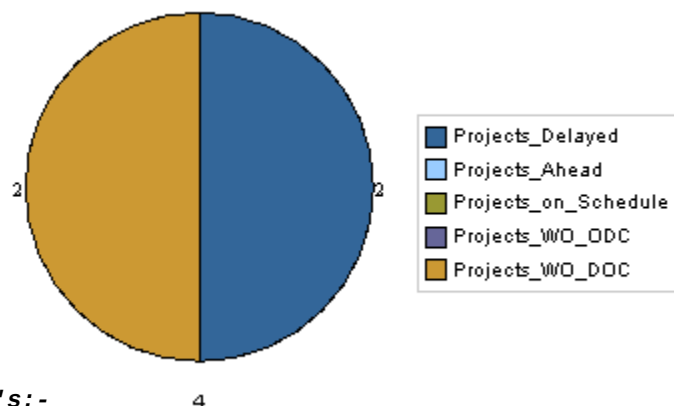

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till October, 2021 is Rs. 886.72 crore, which is 80.5% of the anticipated cost of the projects.

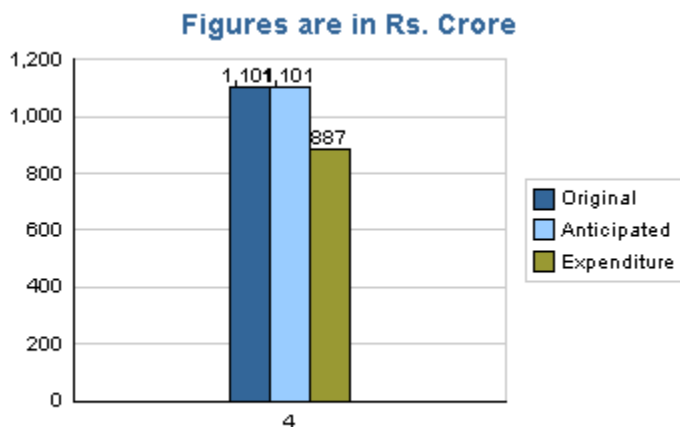

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	107
Number of Projects On Schedule	40
Number of Projects Delayed	57

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	9

Brief Analysis

Project Status with respect to Original Schedule: Out of 107 projects, 40 projects are on schedule 57 projects are delayed. 9 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

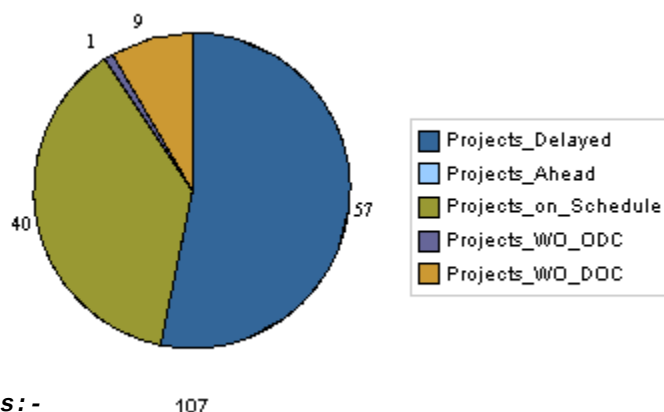


Total No Of Project's:-

107

Investment Scenario

Total original cost of implementation of 107 projects when sanctioned, was of the order of Rs. 149691.71 crore but this was subsequently anticipated to Rs. 154295.46 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till October, 2021 is Rs. 53610.91 crore, which is 34.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

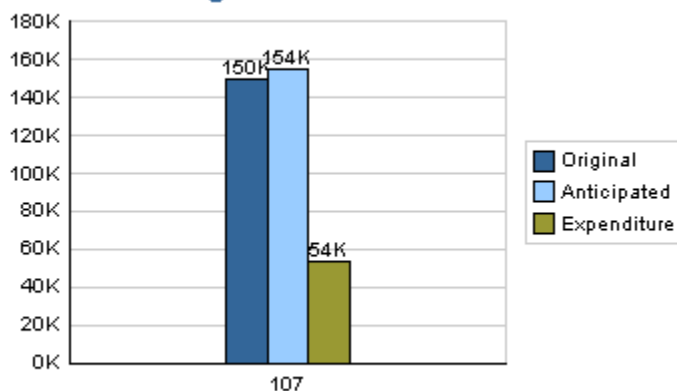

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	20
Number of Projects On Schedule	2
Number of Projects Delayed	18

Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 2 projects are on schedule 18 projects are delayed.

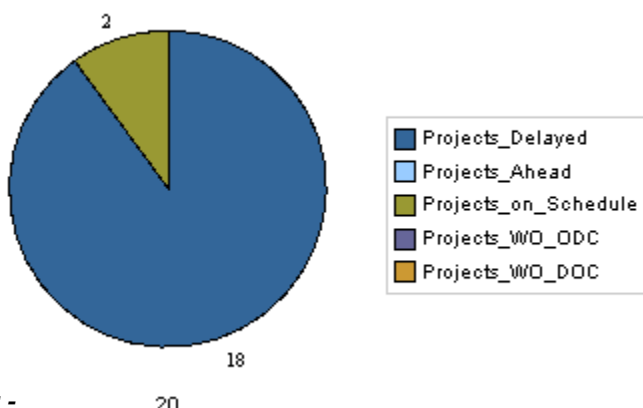


Total No Of Project's:-

20

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 14431.97 crore but this was subsequently anticipated to Rs. 15510.25 crore implying a cost overrun of 7.5%. The expenditure incurred on these projects till October, 2021 is Rs. 5187.07 crore, which is 33.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

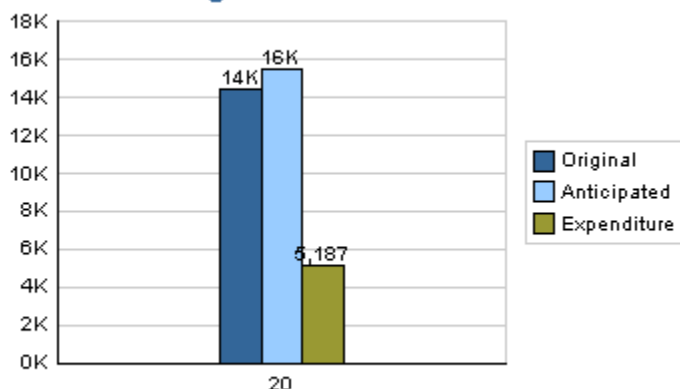

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (OCTOBER 2021)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	3,159.99	1,597.32
2	ANDHRA PRADESH	72	1,22,941.96	1,69,556.6	82,670.47
3	ARUNACHAL PRADESH	43	23,906.6	37,842.94	19,686.48
4	ASSAM	49	49,143.47	58,539.9	13,611.22
5	BIHAR	98	1,23,227.91	1,59,156	80,725.15
6	CHHATISGARH	46	78,726.75	89,025.67	44,085.02
7	DELHI	31	84,554.41	85,648.4	52,322.51
8	GOA	10	5,332.77	5,343.26	2,716.43
9	GUJARAT	59	1,07,424	1,18,232.87	54,400.91
10	HARYANA	36	61,492.56	63,819.18	19,824.74
11	HIMACHAL PRADESH	19	21,918.19	31,775.79	20,921.8
12	JAMMU AND KASHMIR	30	48,180.49	74,107.74	48,317.95
13	JHARKHAND	38	68,190.29	71,740.96	33,891.57
14	KARNATAKA	55	70,566.39	82,854.38	47,729.8
15	KERALA	22	30,240.6	35,331.06	11,839.17
16	LADAKH	8	2,633.23	2,767.29	228.33
17	MADHYA PRADESH	77	68,456.96	77,078.88	33,813.58
18	MAHARASHTRA	232	2,07,667.2	2,30,622.84	1,25,436.57
19	MANIPUR	26	12,108.58	20,557.35	12,459.14
20	MEGHALAYA	13	5,269.68	8,588.18	2,477.19
21	MIZORAM	24	11,957.35	15,906.05	7,389.12
22	MULTI STATE	113	3,45,091.51	4,57,134.61	1,91,361.07
23	NAGALAND	35	15,989.03	20,357.79	5,003.01
24	ODISHA	79	1,14,487.57	1,22,542.27	49,161.15
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	28	18,344.99	20,091.84	7,358.17
27	RAJASTHAN	55	51,403.28	58,056.27	37,433.76
28	SIKKIM	18	7,278.84	14,598.73	2,678.95
29	TAMIL NADU	67	1,20,992.2	1,40,426.27	85,595.96
30	TELANGANA	52	38,726.46	41,766.05	22,220.64
31	TRIPURA	19	5,084.45	5,259.05	1,980.35
32	UTTAR PRADESH	114	1,51,266.95	1,55,023.25	80,524.89
33	UTTARAKHAND	31	35,703.09	50,557.17	23,711.39
34	WEST BENGAL	71	62,791.47	80,666.39	41,355.09
TOTAL		1,680	21,74,182.86	26,08,330.02	12,64,545.31

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						Date of Commissioning	
						Original/ Revised	Anticipated
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)		
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	17,298.00	12/2015 -	02/2022
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,709.00	12/2016 -	03/2023
	Total		23,779.00 -	33,659.00	31,007.00		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
3	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	708.55	729.73	03/2013 -	03/2024
	<u>Singareni Colliers Company Limited</u>						
4	RCE OF INDARAM OCP(1,20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	293.69	03/2015	03/2022
	Total		642.29 -	1,057.83	1,023.42		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
5	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	586.50	573.94	11/2013 -	09/2021
6	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
8	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	164.17	02/2018 -	03/2021
9	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	176.66	- -	11/2021
10	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
11	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021
	Total		1,896.19 -	2,305.96	2,220.24		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
12	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	502.00	444.35	08/2019 06/2021	05/2021
	<u>Oil & Natural Gas Corporation Limited</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
13	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	791.49	12/2020 12/2021	12/2021
	Total		1,186.92 -	1,235.86	1,235.84		
	<u>POWER</u>						
	<u>Satlu Jal Vidyut Nigam Limited</u>						
14	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	704.97	12/2021 06/2022	06/2022
	Total		648.33 -	947.89	704.97		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
15	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	325.00	325.01	03/2019 -	-
16	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,794.60	2,905.60	03/2021 -	03/2023
	<u>Container Corporation Of India</u>						
17	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	487.13	434.63	03/2018 -	-
	<u>East Central Railways</u>						
18	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,630.00	3,630.96	- 03/2022	03/2022
19	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,218.49	- 03/2022	03/2022
20	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	390.00	386.59	03/2021 -	03/2022
21	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	546.71	560.09	07/2014 -	-
22	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	4/2006	378.56 -	1,858.75	386.36	- -	03/2023
23	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,080.00	1,077.28	03/2012 11/2022	11/2022
24	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	926.80	03/2019 12/2021	12/2021
	<u>Eastern Railways</u>						
25	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	1,425.44	638.28	02/2013 -	03/2024
26	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI- SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	4/2010	365.17 -	439.30	480.96	03/2017 -	03/2025
27	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	383.74	- -	03/2024
28	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	4/2012	255.64 -	272.20	299.01	- -	03/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
29	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	495.10	313.03	- -	03/2022
30	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	502.48	517.25	- -	03/2021
	<u>Metropolitan Rapid Transport Projects</u>						
31	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
32	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,866.85	03/2004 06/2022	06/2022
33	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-
	<u>North East Frontier Railway</u>						
34	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	1,180.19 -	4,541.38	3,881.59	12/2008 -	11/2021
35	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,043.00	873.80	03/2019 -	03/2023
36	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,090.60	1,089.12	- -	-
37	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	1,167.00	1,028.89	12/2021 -	10/2021
38	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	2/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-
39	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	1,873.21	1,498.64	03/2021 -	03/2022
40	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	373.87	333.46	- 12/2021	03/2022
41	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	12,264.15	11,504.51	03/2011 -	12/2023
	<u>North Eastern Railway</u>						
42	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
43	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,373.75	03/2022 -	03/2022
44	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	610.00	580.83	01/2019 -	02/2022
	<u>North Western Railway</u>						
45	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	860.41	759.31	02/2019 -	06/2022
	<u>Northern Railway</u>						
46	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	717.17	12/2011 -	06/2021
47	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	839.00	839.36	03/2016 -	-
48	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	4/2007	336.91 -	791.39	597.99	- -	09/2023
	<u>Rail Vikas Nigam Ltd.</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
49	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	1,202.70 -	2,440.53	1,842.99	02/2015 -	06/2022
50	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	3,000.00	2,400.15	03/2023 -	12/2022
51	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,650.00	1,689.43	12/2021 -	12/2021
52	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	433.00	405.83	03/2009 12/2022	12/2022
53	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	3/2012	1,503.71 -	3,377.00	3,126.39	03/2020 -	03/2022
54	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	872.65	937.77	03/2021 -	12/2021
55	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	1,868.89	2,128.65	12/2021 -	03/2022
56	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,536.00	1,409.57	03/2020 -	06/2022
57	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,835.83	1,972.62	12/2020 -	12/2021
58	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,825.00	1,710.66	12/2020 -	12/2022
59	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,536.00	1,233.58	03/2019 -	06/2022
60	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	2,009.00	2,119.84	03/2020 -	12/2021
61	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	2,900.00	2,831.13	03/2020 -	12/2021
62	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,400.00	1,429.50	03/2019 -	06/2022
63	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	773.94 -	850.00	925.02	12/2024 -	12/2024
64	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	4/2015	943.60 -	1,000.00	945.85	03/2022 -	12/2024
65	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	950.00	836.26	03/2016 -	12/2021
<u>South Central Railway</u>							
66	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	4/1997	1,723.00 1.00	3,421.35	2,004.42	03/2000 -	03/2023
<u>South Eastern Railway</u>							
67	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	1,071.24	03/2020 -	03/2022
<u>South Western Railway</u>							
68	HUBLI- CHIKJAJUR - [N22000325	3/2015	1,156.94 -	1,968.00	1,174.76	03/2020 -	03/2023
69	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	1,104.00	966.68	03/2020 -	09/2021
70	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	760.00	642.52	03/2020 12/2021	12/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Southern Railway</u>						
71	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,950.00	1,667.29	02/2019 -	03/2025
72	KURUPPANTHARA-CHINGAVANAM - [N22000190]	4/2007	270.14 -	749.40	550.86	- 12/2021	01/2022
73	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	608.13	399.75	- 12/2021	02/2022
74	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	2/1996	268.87 -	950.00	920.91	03/2005 -	09/2021
75	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	2,172.16	285.53	03/2019 -	12/2027
76	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	4/2007	931.98 -	1,122.00	989.62	- 09/2021	12/2022
77	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	1,720.00	705.52	03/2020 -	03/2025
	<u>West Central Railway</u>						
78	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025
	<u>Western Railway</u>						
79	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,886.76	1,875.42	03/2020 03/2024	03/2024
80	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,383.69	1,199.84	03/2021 12/2022	12/2022
	Total		54,678.00 -	1,23,263.65	97,834.10		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
81	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	978.43	03/2011 12/2021	-
82	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021
83	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	326.56	05/2017 05/2022	05/2022
84	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]	11/2013	683.83 -	560.70	694.71	07/2016 -	-
85	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-
86	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]	1/2017	166.67 -	166.67	184.91	09/2017 -	-
87	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	322.24	308.85	09/2014 12/2021	12/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
88	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	3/2018	325.86 -	386.41	345.82	10/2018 -	-
89	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-
90	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	552.29	12/2019 12/2021	12/2021
91	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	368.39	10/2010 12/2021	-
92	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257	3/2015	298.33 -	298.33	325.55	- -	-
National Highways Authority Of India							
93	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	612.58	612.58	02/2009 -	-
94	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-
95	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016	-
96	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
97	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 02/2022	02/2022
98	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636	12/2016	1,031.95 -	1,031.95	1,505.00	- -	03/2022
99	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634	10/2016	447.75 -	447.75	1,340.40	- -	-
100	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633	10/2016	1,008.96 -	1,008.96	1,125.65	- -	-
101	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627	11/2016	1,071.61 -	1,048.10	1,154.03	- 10/2021	07/2021
102	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,665.00	- -	-
103	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	9/2016	1,100.19 -	1,145.31	1,355.00	- -	-
104	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591	7/2016	688.70 -	688.70	870.48	- -	-
105	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	677.75	06/2019 -	-
106	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	486.00	- -	10/2022
107	ISMAILABAD-NARNAUL PKG-1 - [N24001193	1/2019	996.65 -	996.65	1,000.97	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	3/2018	642.13 -	807.00	716.34	- -	-
109	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]	3/2018	478.74 -	478.74	727.92	- 11/2021	-
110	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]	3/2018	565.09 -	565.09	654.33	- -	02/2021
111	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]	3/2018	1,550.98 -	1,550.98	1,633.66	- -	09/2021
112	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	3/2018	1,120.57 -	1,332.00	1,517.15	- -	-
113	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	3/2018	925.40 -	1,197.00	1,176.70	- -	-
114	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]	3/2018	809.07 -	809.07	838.28	- -	-
115	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	2/2018	2,177.80 -	2,450.00	2,498.34	- -	-
116	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	2/2018	1,995.34 -	2,400.00	3,378.36	- -	11/2021
117	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	3/2017	993.16 -	1,434.00	1,311.37	03/2020 -	-
118	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	3/2017	831.58 -	1,177.00	912.41	03/2020 -	-
119	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-
120	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	1,294.21	03/2020 -	-
121	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
122	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	669.49	02/2019 -	-
123	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	985.40	04/2019 -	-
124	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	886.96	07/2008 -	-
125	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	8/2015	516.13 -	649.27	648.77	04/2018 -	-
126	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	8/2015	854.80 -	1,038.56	1,023.88	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
127	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]	8/2015	275.90 -	275.90	289.13	- -	-
128	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]	12/2015	479.20 -	479.20	712.89	05/2018 -	-
129	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	2,360.65	4,511.49	- -	-
130	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
131	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
132	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	627.93	633.24	01/2016 -	-
133	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	417.68	433.68	01/2016 -	-
134	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-
135	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	469.31	459.07	01/2014 -	-
136	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,873.47	06/2014 -	-
137	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023
138	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	11/2021
139	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	-
140	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,933.30	06/2014 -	10/2020
141	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	591.00	578.00	11/2013 -	-
142	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
143	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.92	03/2014 -	-
144	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,283.85	05/2014 -	-
145	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022
146	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.53	10/2013 -	-
147	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-
148	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	-
149	PATNA-MUZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	1,197.27	02/2013 -	-
150	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,653.88	07/2013 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
151	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-
152	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	09/2020
153	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	1,299.17	03/2018 03/2021	-
154	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
155	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
156	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
157	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	902.51	- 01/2020	01/2020
158	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-
159	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	844.08	04/2018 -	12/2021
160	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	694.42	05/2018 03/2022	03/2022
161	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
162	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
163	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-
164	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-
165	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,633.18	03/2013 -	03/2022
166	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
167	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
168	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-
	Total		84,649.51 -	93,388.07	1,23,265.81		
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
169	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	2,100.00	1,736.92	09/2018 11/2021	11/2021
	Total		1,682.85 -	2,100.00	1,736.92		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>URBAN DEVELOPMENT</u>						
	<u>Delhi Metro Rail Corporation</u>						
170	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	39,486.58	03/2016 08/2021	-
	Total		38,585.00 -	38,585.00	39,486.58		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
171	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	291.32	03/2020 -	03/2021
172	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	326.75	01/2021 -	-
	Total		494.40 -	667.53	618.07		
	Grand Total		2,08,242.49	2,97,210.79	2,99,132.95		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	157.18	03/2020 06/2022	04/2022
	Total		458.00 -	458.00	157.18		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	201.80	09/2025	05/2024
	Total		1,828.00 -	1,828.00	201.80		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
3	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	3,072.00	2,574.63	06/2021 08/2022	07/2022
	<u>Indian Oil Corporation Limited</u>						
4	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00 -	1,398.00	116.76	12/2023 -	10/2023
5	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	796.97	09/2024 -	08/2024
	Total		23,011.00 -	23,406.00	3,488.36		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
6	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	87.43	10/2021 01/2022	11/2021
7	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71 -	1,522.71	996.32	09/2021 10/2022	01/2022
8	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]	1/2021	842.27 -	842.27	92.08	07/2022 -	06/2022
	<u>Power Grid Corporation Of India Limited</u>						
9	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 14,719.10	14,719.10	12,979.18	08/2013 11/2022	08/2022
	Total		13,756.97 -	17,345.88	14,155.01		
	<u>RAILWAYS</u>						

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Central Railways</u>						
10	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	1,721.84	03/2024 -	03/2023
	<u>North East Frontier Railway</u>						
11	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	1,167.00	1,028.89	12/2021 -	10/2021
	<u>Rail Vikas Nigam Ltd.</u>						
12	BHANUPALI-BILASPUK BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	1,809.22	12/2026 -	12/2025
13	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,400.15	03/2023 -	12/2022
14	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
	Total		10,047.51 -	15,271.67	6,960.29		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
15	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]	1/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
16	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	129.40	09/2019 06/2023	04/2023
17	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]	3/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022
	Total		2,653.27 -	2,653.27	920.79		
	Grand Total		51,754.75	60,962.82	25,883.43		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	81.41	05/2022 -	05/2022
2	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	52.08	03/2023 -	03/2023
	Total		965.41 -	965.41	133.49		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
3	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	778.80	349.76	03/2023 -	03/2023
4	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	37.16	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
5	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	2.70	03/2027 -	03/2027
6	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	257.70	03/2022 -	03/2022
7	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	6.82	03/2025 -	03/2025
8	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	18.15	03/2029 -	03/2029
9	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.75	03/2026 -	03/2026
10	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	159.28	03/2024 -	03/2024
11	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	0.19	03/2027 -	03/2027
	<u>Mahanadi Coal Fields Limited</u>						
12	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,282.18	03/2029 -	03/2029
13	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,558.11	03/2026 -	03/2026
14	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	598.36	03/2027 -	03/2027
	<u>Northern Coal Fields Limited</u>						
15	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
16	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
17	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
19	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
	<u>Singareni Colliers Company Limited</u>						
20	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	25.43	03/2023 -	03/2023
21	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	76.43	03/2024 -	03/2024
22	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	80.04	03/2023 -	03/2023
	<u>South-Eastern Coal Fields Limited</u>						
23	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,118.22	03/2023 -	03/2023
24	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	314.88	03/2029 -	03/2029
25	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	40.57	03/2026 -	03/2026
26	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023
27	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	2,025.60	03/2029 -	03/2029
28	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
29	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	4,639.30	03/2023 03/2016	03/2023
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	160.43	03/2022 -	03/2022
31	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
32	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	185.35	03/2024 -	03/2024
33	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	76.12	03/2026 -	03/2026
34	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
	<u>Western Coal Fields Limited</u>						
35	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
36	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.90	03/2023 -	03/2023
37	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	9.86	03/2028 -	03/2028
38	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	246.02	03/2022 -	03/2022
39	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	1.00	03/2026 -	03/2026
40	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
42	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	390.11	03/2025 -	03/2025
	Total		58,091.89 -	57,641.81	16,930.06		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
43	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	57.47	06/2022 -	06/2022
44	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	213.47	04/2023 -	04/2023
	Total		1,068.51 -	1,068.51	270.94		
	<u>FINANCE</u>						
	<u>Cpwd For Finance</u>						
45	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	189.00	11/2021 -	11/2021
	Total		348.77 -	348.77	189.00		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
46	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	333.02	09/2023 -	09/2023
47	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	Total		2,981.00 -	3,232.00	333.02		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
48	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		166.98 -	166.98	.00		
	<u>MINES</u>						
	<u>Central Public Works Department</u>						
49	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]	4/2019	255.37 -	255.37	0.86	04/2022 -	04/2022
	Total		255.37 -	255.37	.86		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
50	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410	8/2020	697.00 -	697.00	256.43	03/2023 -	03/2023
51	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365	12/2017	1,524.06 -	1,524.06	998.48	12/2021 -	12/2021
52	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023
	<u>Gas Authority Of India Limited</u>						
53	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329	10/2017	226.45 -	226.45	133.18	10/2022 -	10/2022
54	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388	9/2019	2,658.34 -	2,658.34	402.90	07/2022 -	07/2022
55	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	4/2017	287.49 -	345.15	246.25	04/2022 -	04/2022
56	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289	7/2017	243.53 -	243.53	151.09	07/2022 -	07/2022
57	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398	6/2020	7,844.25 -	7,844.25	1,616.30	05/2023 -	05/2023
58	60 KTA POLYPROPYLENE PROJECT - [N16000429	3/2019	910.56 -	910.56	105.31	04/2024 -	04/2024
59	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327	10/2017	359.25 -	359.25	181.07	10/2022 -	10/2022
60	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430	5/2019	8,797.00 -	8,797.00	228.35	04/2025 -	04/2025
61	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389	10/2017	221.45 -	221.45	105.20	10/2022 -	10/2022
62	BARAUNI-GUWAHATI PIPELINE - [N16000334	6/2018	3,308.00 -	3,060.00	2,496.20	12/2021 -	12/2021
63	DHAMRA HALDIA PIPELINE PROJECT - [N16000391	3/2020	1,030.65 -	1,030.65	337.20	11/2022 -	11/2022
64	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328	7/2017	182.20 -	182.20	91.81	07/2022 -	07/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
65	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367	6/2019	2,166.38 -	2,166.38	1,334.00	06/2022 -	06/2022
66	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369	12/2018	854.00 -	854.00	179.41	12/2022 -	12/2022
67	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413	3/2021	456.00 -	456.00	13.22	03/2024 -	03/2024
68	BARMER PALANPUR PIPELINE - [N16000384	11/2019	776.00 -	776.00	368.60	11/2022 -	11/2022
69	RUF PITCH LOADING GANTRY - [N16000406	10/2020	332.61 -	332.61	28.57	11/2022 -	11/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
70	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	171.55	02/2023 -	02/2023
	<u>Indian Oil Corporation Limited</u>						
71	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	490.71	08/2022 -	08/2022
72	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	191.16	03/2030 -	03/2030
73	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,566.92	02/2022 -	02/2022
74	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	94.90	08/2022 -	08/2022
75	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	283.56	02/2028 -	02/2028
76	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	24.46	12/2029 -	12/2029
77	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	39.09	03/2030 -	03/2030
78	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]	10/2018	613.00 -	613.00	157.77	12/2029 -	12/2029
79	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]	10/2018	176.00 -	176.00	77.52	08/2027 -	08/2027
80	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	1,620.50	04/2023 -	04/2023
81	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	118.98	02/2028 -	02/2028
82	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]	6/2019	2,880.00 -	2,880.00	104.89	08/2027 -	08/2027
83	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]	2/2021	34,627.00 -	34,627.00	466.97	09/2024 -	09/2024
84	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	103.42	01/2023 -	01/2023
85	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	94.78	02/2028 -	02/2028
86	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	1.12	08/2023 -	08/2023
87	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	552.22	05/2023 -	05/2023
88	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	37.29	12/2029 -	12/2029
89	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	41.60	12/2029 -	12/2029
90	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	166.08	12/2022 -	12/2022
91	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	25.15	10/2023 -	10/2023
92	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	62.90	02/2027 -	02/2027

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
93	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	373.13	01/2024 -	01/2024
94	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	28.71	07/2022 -	07/2022
95	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	119.54	02/2028 -	02/2028
	<u>Numaligarh Refinery Limited</u>						
96	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	18,968.00	648.35	10/2024 -	10/2024
97	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	526.70	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
98	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	947.93	03/2026	03/2026
99	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	115.83	08/2022 -	08/2022
100	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	217.38	03/2025 -	03/2025
101	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,694.11	03/2022 -	03/2022
	Total		1,62,448.98 -	1,67,358.42	20,864.09		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
102	CHHATTARGARH 150 MW - [N18000294]	2/2021	599.99 -	559.98	60.85	07/2022 -	07/2022
103	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]	5/2021	674.92 -	674.92	76.00	09/2022 -	09/2022
104	ANTA SOLAR 90 MW - [N18000292]	1/2021	382.22 -	382.22	-	03/2022 -	03/2022
105	BHENSARA 320 MW - [N18000293]	1/2021	1,221.73 -	1,221.73	137.36	07/2022 -	07/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
106	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	3,509.49	01/2024 -	01/2024
107	SHIYAL SOLAR POWER PROJECT - [N18000297]	5/2021	296.20 -	296.20	-	10/2022 -	10/2022
108	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	182.27	11/2025 -	11/2025
109	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	532.10	01/2026 -	01/2026
110	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	313.58 -	313.58	-	12/2022 -	12/2022
	Total		16,426.26 -	16,386.25	4,498.07		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
111	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
112	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,445.48	1,418.05	03/2023 -	03/2023
113	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	630.94	03/2023 -	03/2023
114	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
	<u>North Eastern Railway</u>						
115	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	116.24	12/2021 -	12/2021
116	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
117	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,373.75	03/2022	03/2022
	<u>Northern Railway</u>						
118	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.13	242.55	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
119	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	17,009.45	12/2023 -	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
120	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	2,261.21	12/2023 -	12/2023
121	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,650.00	1,689.43	12/2021 -	12/2021
122	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,082.97	12/2023 -	12/2023
123	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	925.02	12/2024 -	12/2024
	<u>South Central Railway</u>						
124	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	242.28	67.24	03/2022 03/2022	03/2022
	<u>Western Railway</u>						
125	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	4/2018	537.31 -	537.31	0.64	03/2024 -	03/2024
	Total		1,36,865.28 -	1,43,831.62	29,094.63		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
126	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - [N24001180]	3/2019	237.51 -	237.51	96.49	12/2022 -	12/2022
127	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDA-SAGWARA) SECTION OF NH-927A. PKG- - [N24001413]	2/2021	240.99 -	240.99	-	11/2021 -	11/2021
128	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]	2/2021	925.47 -	925.47	-	07/2025 -	07/2025
129	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 & KM 158.419 TO KM 173.300 PKG-II. - [N24001412]	12/2020	339.65 -	339.65	-	10/2021 -	10/2021
130	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	236.18	33.22	12/2022 -	12/2022
131	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]	12/2020	379.23 -	379.23	-	10/2021 -	10/2021
132	NAGOUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]	3/2020	370.36 -	370.36	196.71	08/2022 -	08/2022
133	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]	2/2021	588.09 -	588.09	83.83	03/2024 -	03/2024
134	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]	1/2020	358.26 -	358.26	1.15	02/2024 -	02/2024
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
135	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023
136	TAMENGLONG - MAHUR PKG-2 - [N24001403]	7/2021	483.87 -	483.87	-	03/2023 -	03/2023
137	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	7.80	04/2022 -	04/2022
138	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]	8/2020	278.46 -	278.46	103.50	03/2022 -	03/2022
139	CHURACHANPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	-	10/2023 -	10/2023
140	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]	6/2020	277.50 -	277.50	103.62	01/2022 -	01/2022
141	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24 -	292.24	49.59	07/2022 -	07/2022
142	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	31.14	06/2024 -	06/2024
143	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	173.17	12/2023 -	12/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
144	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	40.21	12/2023 -	12/2023
145	LADDA - BASAI - [N24001316]	2/2021	445.96 -	445.96	-	04/2023 -	04/2023
146	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	66.04	01/2022 -	01/2022
147	IMPHAL – MOREH (PACKAGE 4) - [N24001399]	3/2021	277.99 -	277.99	-	01/2023 -	01/2023
148	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	-	12/2022 -	12/2022
149	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]	9/2020	183.31 -	183.31	75.61	05/2022 -	05/2022
150	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53 -	361.53	32.21	06/2022 -	06/2022
151	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]	3/2019	402.94 -	402.94	56.40	04/2022 -	04/2022
152	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
153	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	27.06	04/2023 -	04/2023
154	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
155	PEREN-DIMAPUR PKG-5 - [N24001407]	2/2021	207.33 -	207.33	8.04	03/2023 -	03/2023
156	KHELLANI-KHANABAL PKG-6 - [N24001324]	2/2021	285.28 -	285.28	18.65	09/2022 -	09/2022
157	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]	9/2020	262.84 -	262.84	118.63	05/2023 -	05/2023
158	TAMENGLONG - MAHUR PKG-3 - [N24001354]	3/2021	234.08 -	234.08	-	12/2022 -	12/2022
159	DOGINALA - GAU - [N24001320]	12/2020	242.30 -	242.30	-	09/2022 -	09/2022
160	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]	3/2020	167.95 -	167.95	46.68	06/2022 -	06/2022
161	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]	3/2020	261.13 -	261.13	23.56	06/2022 -	06/2022
162	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	275.00	09/2026 -	09/2026
163	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
164	KHELLANI-KHANABAL PKG-4 - [N24001395]	7/2021	859.67 -	859.67	-	08/2023 -	08/2023
165	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	11.78	01/2024 -	01/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
166	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247	3/2020	247.76 -	247.76	19.60	01/2022 -	01/2022
167	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327	8/2020	292.80 -	292.80	27.45	05/2022 -	05/2022
168	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329	3/2020	165.54 -	165.54	5.26	07/2022 -	07/2022
169	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262	7/2020	345.38 -	345.38	74.52	04/2023 -	04/2023
170	MARIAM - PEREN (PKG 2A) - [N24001398	7/2021	204.58 -	204.58	-	03/2023 -	03/2023
171	KHELLANI-KHANABAL PKG-5 - [N24001396	7/2021	497.09 -	497.09	-	02/2023 -	02/2023
172	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	28.20	06/2022 -	06/2022
173	IMPHAL - KHONGSANG PKG-2 - [N24001353	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
174	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314	11/2020	525.68 -	525.68	288.84	12/2023 -	12/2023
175	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	42.84	08/2022 -	08/2022
176	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278	3/2020	206.88 -	206.88	30.06	07/2022 -	07/2022
177	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	10.30	07/2022 -	07/2022
178	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM 20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264	7/2020	228.39 -	228.39	17.68	04/2022 -	04/2022
179	TAMENGLONG - MAHUR PKG-1 - [N24001402	7/2021	185.80 -	185.80	-	03/2023 -	03/2023
180	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318	9/2020	173.17 -	173.17	5.10	04/2022 -	04/2022
181	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248	8/2020	208.84 -	208.84	17.93	04/2022 -	04/2022
182	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261	8/2020	311.00 -	311.00	21.62	04/2023 -	04/2023
183	KARGIL-ZANSKR PACKAGE-3 - [N24001345	8/2020	381.01 -	381.01	-	01/2023 -	01/2023
184	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260	9/2020	257.15 -	257.15	40.94	04/2022 -	04/2022
185	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	32.98	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
186	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]	11/2020	280.91 -	280.91	59.89	07/2022 -	07/2022
187	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
188	TAMENGLONG - MAHUR PKG-4 - [N24001404]	7/2021	198.77 -	198.77	-	03/2023 -	03/2023
189	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]	3/2019	471.00 -	471.00	154.09	07/2022 -	07/2022
190	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM D - [N24001255]	9/2020	277.44 -	277.44	32.33	10/2022 -	10/2022
191	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]	3/2020	220.20 -	220.20	27.79	12/2022 -	12/2022
192	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	39.60	06/2022 -	06/2022
193	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]	6/2020	201.99 -	201.99	18.87	01/2022 -	01/2022
194	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	532.08	09/2028 -	09/2028
195	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]	3/2020	278.95 -	278.95	79.89	06/2022 -	06/2022
196	KHELLANI-KHANABAL PKG-2 - [N24001394]	7/2021	512.43 -	512.43	-	02/2023 -	02/2023
197	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]	3/2020	330.78 -	330.78	54.27	12/2021 -	12/2021
198	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]	3/2020	154.51 -	154.51	39.78	07/2022 -	07/2022
199	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
200	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	36.09	09/2022 -	09/2022
201	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	-	01/2023 -	01/2023
202	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	12.16	06/2023 -	06/2023
203	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	58.14	06/2022 -	06/2022
204	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) [N24001279]	3/2020	216.49 -	216.49	53.72	07/2022 -	07/2022
205	JORAM - KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]	8/2020	199.03 -	199.03	39.84	04/2022 -	04/2022
206	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]	3/2020	216.49 -	216.49	40.09	03/2022 -	03/2022
207	IMPHAL - KHONGSANG PKG-3 - [N24001401]	7/2021	467.00 -	467.00	-	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
208	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	-	12/2022 -	12/2022
209	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]	3/2021	636.42 -	636.42	-	12/2022 -	12/2022
210	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]	3/2020	281.78 -	281.78	92.39	07/2022 -	07/2022
211	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	-	12/2022 -	12/2022
212	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	7.11	01/2023 -	01/2023
213	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	36.80	06/2022 -	06/2022
214	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
215	JORAM - KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]	8/2020	294.04 -	294.04	56.85	04/2022 -	04/2022
216	RANIKOR-MAHESKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	38.58	12/2022 -	12/2022
217	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	20.81	05/2022 -	05/2022
218	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
219	JORAM - KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]	8/2020	184.88 -	184.88	32.58	04/2022 -	04/2022
220	SENAPATI- IMPHAL PKG-5B - [N24001400]	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
221	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
222	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	23.26	12/2022 -	12/2022
223	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	3.39	01/2023 -	01/2023
224	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]	7/2021	258.52 -	258.52	8.04	03/2023 -	03/2023
225	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	25.63	04/2022 -	04/2022
226	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
227	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
228	STRENGTHENING OF CHURAIBARI - AGARTALA SECTION OF NH-08 - [N24001319]	6/2020	257.96 -	257.96	95.22	01/2022 -	01/2022
229	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]	9/2019	761.54 -	761.54	116.54	05/2023 -	05/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
230	TLABUNG - LUNGLEI PKG-A - [N24001358]	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
231	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	24.56	10/2022 -	10/2022
232	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]	7/2020	210.79 -	210.79	17.58	04/2022 -	04/2022
233	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]	11/2020	206.78 -	206.78	52.08	07/2022 -	07/2022
234	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]	12/2020	804.00 -	804.00	7.04	08/2023 -	08/2023
235	DABOKA KATHKATI PACKAGE-4 - [N24001365]	2/2021	260.07 -	260.07	67.70	12/2023 -	12/2023
236	GOHA-KHELLANI PKG-3 - [N24001397]	2/2021	431.28 -	431.28	4.14	03/2023 -	03/2023
237	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
238	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	31.14	05/2024 -	05/2024
239	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]	8/2020	230.45 -	230.45	2.58	04/2023 -	04/2023
240	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
241	IMPHAL – MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	25.85	12/2022 -	12/2022
242	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	-	12/2022 -	12/2022
243	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	40.96	12/2023 -	12/2023
244	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	25.18	08/2022 -	08/2022
245	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	-	12/2022 -	12/2022
246	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]	10/2020	157.86 -	157.86	53.58	04/2022 -	04/2022
247	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	-	12/2022 -	12/2022
248	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	5.07	04/2022 -	04/2022
249	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.37	12/2023 -	12/2023
250	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]	4/2020	330.80 -	330.80	38.65	12/2021 -	12/2021
251	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]	3/2020	206.53 -	206.53	81.84	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
252	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
253	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390	8/2020	228.71 -	228.71	27.48	04/2022 -	04/2022
254	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022
255	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308	11/2020	332.14 -	332.14	10.88	07/2022 -	07/2022
256	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	3.90	04/2022 -	04/2022
<u>National Highways Authority Of India</u>							
257	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
258	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416	12/2020	989.66 -	989.66	-	01/2024 -	01/2024
259	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
260	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
261	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
262	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
263	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 -	01/2024
264	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
265	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
	Total		68,209.44 -	68,247.95	5,805.94		
<u>SHIPPING AND PORTS</u>							
<u>Inland Waterways Authority Of India</u>							
266	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,940.64	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,940.64		
<u>STEEL</u>							

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Mineral Development Corporation (Nmdc)</u>						
267	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]	11/2015	2,907.00 -	2,907.00	439.00	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						
268	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]	11/2020	542.24 -	542.24	70.05	12/2023 -	12/2023
269	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	44.29	05/2023 -	05/2023
	Total		3,826.42 -	3,826.42	553.34		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
270	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	208.21	03/2024 -	03/2024
271	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	247.58	03/2024 -	03/2024
	<u>Delhi Metro Rail Corporation</u>						
272	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	2,442.28	03/2025 -	03/2025
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
273	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	248.29	02/2023 -	02/2023
274	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	142.54	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
275	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	5,222.09	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
276	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,925.50	302.95	06/2024 -	06/2024
	Total		1,00,435.11 -	1,00,994.84	8,813.94		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
277	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	42.75	06/2022 -	06/2022
278	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	42.75	06/2022 -	06/2022
279	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
	<u>Delhi Jal Board</u>						
280	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	230.58	12/2022 -	12/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Kolkata Metropolitan Development Authority</u>						
281	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	11.56	12/2021 -	12/2021
282	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
283	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
284	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	11.56	12/2021 -	12/2021
285	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
286	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
287	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	11.56	12/2021 -	12/2021
288	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
289	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	53.62	10/2021 -	10/2021
290	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	14.63	12/2021 -	12/2021
291	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
292	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
	Total		5,597.26 -	5,655.93	419.01		
	Grand Total		5,63,055.86	5,74,614.09	89,847.03		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,840.00	6,054.37	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00 -	16,580.00	17,298.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027	10/2009	12,320.00 -	17,079.00	13,709.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	40,499.00	37,061.37			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073	10/2013	417.23 -	707.73	476.54	09/2018 -	06/2022	69.63
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077	06/2018	1,383.00 -	1,983.00	534.84	09/2021 -	12/2023	43.38
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078	07/2018	346.27 -	480.33	114.59	09/2021 -	12/2022	38.72
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083	12/2016	1,142.00 -	1,232.00	371.33	03/2021 -	03/2023	7.88
	Total		3,288.50 -	4,403.06	1,497.30			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
8	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194	10/2015	243.00 -	334.27	24.86	04/2018 -	10/2022	37.56
9	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195	12/2015	304.13 -	341.22	73.17	03/2017 -	10/2022	12.20
	<u>Central Coal Fields Limited</u>							
10	MAGADH EXPANSION OC(51 MTY) - [N06000015	08/2008	6,964.33 6,964.33	7,254.37	729.50	07/2012 03/2028	03/2028	4.16
	<u>Eastern Coal Fields Limited</u>							
11	RANIGANJ MASTER PLAN - [N06000163	08/2009	2,661.73 -	5,146.48	622.22	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	708.55	729.73	03/2013 -	03/2024	47.76
	<u>Neyveli Lignite Corporation</u>							
13	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,417.83	12/2015 -	02/2021	35.10
14	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	12,656.73	11/2021 -	11/2022	.00
	<u>Singareni Colliers Company Limited</u>							
15	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86
16	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	112.99	03/2019 -	03/2022	11.42
17	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	183.12	03/2015 -	03/2023	5.85
18	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	293.69	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
19	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	199.99	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
20	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	86.90	03/2023 -	03/2023	117.98
21	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	299.67	164.36	03/2019 -	03/2022	1.39
22	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	08/2015	727.28 -	745.03	390.11	03/2025 -	03/2025	2.44
23	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	145.08	03/2023 -	03/2024	15.41
24	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	327.41	160.84	03/2019 -	03/2022	7.52
25	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 -	404.45	246.02	03/2022 -	03/2022	26.49
26	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	36.10	03/2022 -	03/2025	.00
27	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 -	402.90	336.00	03/2020 -	09/2022	11.07
	Total		38,151.12 -	44,429.38	25,025.31			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
28	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	292.81	06/2017 -	03/2022	.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
29	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	-	1.85
30	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	10.22
	<u>Rites Of Higher Education</u>							
31	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	-	09/2014 -	-	29.31
	Total		1,715.81 -	1,889.72	881.82			
	<u>DPIIT</u>							
	<u>Dmic For Dpiit</u>							
32	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	9,574.07	09/2019 -	07/2021	9.80
	<u>licc For Dpiit</u>							
33	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,013.69	12/2019 -	05/2022	8.49
	Total		17,352.09 -	18,990.30	12,587.76			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Cpwd For Health</u>							
34	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
35	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	586.50	573.94	11/2013 -	09/2021	41.63
36	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021	22.29
37	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
38	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
39	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
40	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	16.33
41	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
42	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	268.55	03/2019 -	03/2021	.13
43	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	190.34	176.66	- -	11/2021	21.58
44	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022	01/2018	249.01 -	249.07	231.05	- -	01/2021	.02
	<u>Nbcc For Health</u>							
45	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	8.88
	Total		5,589.39 -	6,374.57	3,815.56			
	<u>HEAVY INDUSTRY</u>							
	<u>Natrip Implementation Society</u>							
46	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,727.30	3,522.74	09/2011 -	03/2021	116.96
	Total		1,718.00 -	3,727.30	3,522.74			
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
47	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	1,007.93	10/2019 -	03/2022	64.04
48	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
49	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	238.00	172.13	04/2018 -	12/2021	46.12
50	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002	06/2019	277.35 -	290.33	27.25	07/2022 -	10/2022	4.68
	Total		1,773.70 -	2,794.33	1,207.31			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
51	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11
52	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	769.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
53	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,773.40	12/2012 -	02/2022	102.71
54	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	246.25	04/2022 -	04/2022	20.06
55	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	47.78	02/2021 -	08/2022	9.91
56	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	223.50	08/2020 -	12/2021	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
57	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00	26,264.00	16,536.13	07/2020 -	07/2022	25.50
58	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,574.63	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>							
59	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	500.28	10/2017 -	09/2022	103.60
60	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,163.26	03/2021 -	03/2022	66.09
61	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	3,071.72	12/2020 -	03/2022	43.82
62	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	444.35	08/2019 -	05/2021	18.68
63	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	4,049.27	12/2018 -	02/2022	33.98
64	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	05/2016	348.00 -	437.00	179.80	01/2021 -	08/2022	25.57
65	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	04/2017	163.02 -	207.36	126.85	04/2020 -	07/2022	27.20
66	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	319.61	219.15	06/2020 -	12/2021	35.43
67	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	04/2018	206.63 -	340.76	145.36	02/2020 -	07/2022	64.91
68	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	03/2018	588.20 -	730.20	157.01	- -	05/2023	24.14
69	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	06/2019	371.00 -	427.00	28.69	09/2022 -	03/2023	15.09
	<u>Mangalore Refinery And Petrochemicals Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
70	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	534.34	03/2020 -	11/2021	9.64
71	DEVANGONTHI MARKETING TERMINAL - [N16000401]	06/2020	200.00 -	304.00	2.56	06/2023 -	01/2024	52.00
	<u>Numaligarh Refinery Limited</u>							
72	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	01/2019	12,366.00 -	18,968.00	648.35	10/2024 -	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>							
73	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	1,599.60	05/2013 -	05/2022	132.23
74	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,884.63	04/2018 -	05/2022	5.80
75	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	730.57	03/2023 -	03/2022	38.20
76	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	222.27	05/2020 -	11/2021	21.57
77	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,463.48	03/2022 -	05/2023	23.16
78	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	3,032.38	05/2021 -	01/2022	2.17
	<u>Oil India Limited</u>							
79	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	395.08	02/2020 -	12/2021	17.41
	Total		66,399.38 -	90,818.23	46,789.13			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
80	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62 -	1,311.05	156.99	06/2006 -	-	126.58
81	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	9,279.64	09/2009 -	03/2023	152.52
82	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	14,458.38	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
83	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	5,187.12	03/2013 -	09/2024	96.99
84	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	12,291.69	06/2019 -	09/2023	7.12
85	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,993.63	07/2012 -	11/2021	97.38

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
86	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	16,371.88	05/2018 -	02/2022	33.47
87	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	19,311.93	10/2011 -	07/2023	145.16
88	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.93	08/2017 -	-	17.95
89	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,997.70	8,866.73	11/2020 -	10/2022	3.76
90	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,824.26	10/2017 -	-	7.41
91	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 -	2,311.89	1,922.67	12/2018 -	12/2021	22.64
92	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	633.80	472.23	11/2018 -	02/2022	19.66
	<u>Power Grid Corporation Of India Limited</u>							
93	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,979.18	08/2013 -	08/2022	32.24
94	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	480.66	11/2016 -	12/2021	4.61
95	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,697.96	12/2018 -	03/2024	92.02
96	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	3,207.16	12/2018 -	03/2022	31.08
97	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,096.25	07/2020 -	02/2022	14.11
98	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	167.22	07/2019 -	12/2021	17.99
	<u>Satluj Jal Vidyut Nigam Limited</u>							
99	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	704.97	12/2021 -	06/2022	46.20
	<u>Thdc India Limited</u>							
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,313.83	06/2013 -	12/2024	54.94
101	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,266.10	02/2016 -	06/2023	191.23
	Total		1,03,919.23 -	1,66,878.72	131,200.41			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
102	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,418.05	03/2023 -	03/2023	8.75

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
103	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	357.95	03/2021 -	03/2023	75.00
104	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	325.00	325.01	03/2019 -	-	76.57
105	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	2,905.60	03/2021 -	03/2023	111.08
106	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
107	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.49	-	03/2024 -	-	25.04
108	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	515.13	03/2022 -	03/2023	.89
109	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	630.94	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
110	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	-	25.65
111	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
112	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
113	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
114	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,630.00	3,630.96	- -	03/2022	251.38
115	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,590.10	- -	03/2023	290.95
116	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	719.65	03/2012 -	09/2021	57.27
117	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,080.00	1,077.28	03/2012 -	11/2022	232.58
118	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	352.46	- -	12/2023	277.26
119	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	459.05	03/2020 -	-	3.33
120	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	309.90	- -	03/2025	36.67
121	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	926.80	03/2019 -	12/2021	37.04
122	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	904.73	- -	03/2023	253.52
123	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	15.58	- -	-	32.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
124	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	818.15
125	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	389.43	- -	03/2021	126.22
126	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	391.01
127	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	24.16	- -	-	376.78
128	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	1,436.01	- -	03/2023	295.15
129	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	541.64	03/2020 -	12/2024	49.45
130	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	560.09	07/2014 -	-	64.60
131	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 -	390.00	386.59	03/2021 -	03/2022	11.99
132	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	513.54	03/2021 -	03/2024	63.37
133	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	383.26	03/2021 -	03/2024	62.06
134	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	1,218.49	- -	03/2022	350.27
	<u>East Coast Railway</u>							
135	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	909.17	06/2021 -	03/2025	137.80
136	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,649.76	03/2009 -	03/2026	29.71
137	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,195.24	02/2019 -	03/2022	38.43
138	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	1,010.84	03/2020 -	03/2023	.07
139	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	223.69	03/2020 -	03/2022	52.77
140	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	193.71	11/2018 -	03/2024	15.45
	<u>Eastern Railways</u>							
141	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	908.35	03/2019 12/2009	03/2025	36.22
142	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	638.28	02/2013 -	03/2024	134.80
143	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	480.96	03/2017 -	03/2025	20.30

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
144	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	1.76	- -	03/2025	44.46
145	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	313.03	- -	03/2022	181.63
146	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02
147	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	.01
148	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	36.13	- -	03/2025	.25
149	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	36.15
150	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	383.74	- -	03/2024	23.82
151	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	299.01	- -	03/2022	6.48
152	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	34.08
153	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	-	- -	03/2025	180.30
154	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	11.77	- -	03/2025	51.19
155	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	439.23	03/2022 -	03/2025	133.39
156	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	517.25	- -	03/2021	74.26
157	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	614.87	03/2016 -	03/2025	7.75
158	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>								
159	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	117.23
160	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	.00
<u>Metropolitan Rapid Transport Projects</u>								
161	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
162	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,866.85	03/2004 -	06/2022	501.57
163	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	478.72	06/2013 -	07/2022	48.06
164	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	75.91
	<u>North Central Railway</u>							
165	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	329.61	03/2022 -	12/2024	32.02
166	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	4.00	03/2020 -	12/2021	1.69
	<u>North East Frontier Railway</u>							
167	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	275.06	03/2019 -	-	106.51
168	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	4,282.46	03/2014 -	03/2024	130.69
169	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,881.59	12/2008 -	11/2021	284.80
170	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	11,504.51	03/2011 -	12/2023	175.34
171	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,043.00	873.80	03/2019 -	03/2023	170.77
172	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	1,021.19	03/2019 -	03/2024	302.54
173	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,647.64	1,369.40	03/2015 -	03/2026	185.73
174	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	6.74	- -	-	7.86
175	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	1,656.78	12/2015 -	12/2023	542.04
176	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,042.51	328.75	03/2019 -	12/2023	13.60
177	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	38.20	- -	-	71.62
178	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	561.03	03/2020 -	06/2022	30.26
179	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	264.34	03/2021 -	-	350.44
180	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	76.57	03/2020 -	-	94.45
181	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	333.46	- -	03/2022	54.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
182	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	157.19	03/2020 -	-	80.79
183	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,090.60	1,089.12	- -	-	33.13
184	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,842.95	03/2022 -	03/2023	32.15
185	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,498.64	03/2021 -	03/2022	115.07
186	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	1,167.00	1,028.89	12/2021 -	10/2021	93.77
187	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	186.55
	<u>North Eastern Railway</u>							
188	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	0.15	- -	-	60.34
189	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	-	358.99
190	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	116.24	12/2021 -	12/2021	267.13
191	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	610.00	580.83	01/2019 -	02/2022	106.78
192	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	-	.16
193	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,824.00	1,373.75	03/2022 -	03/2022	40.80
194	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	69.01	04/2016 -	12/2021	.16
195	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	127.77
196	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	-	01/2018 -	-	.15
197	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	128.90	- -	12/2023	32.78
	<u>North Western Railway</u>							
198	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	759.31	02/2019 -	06/2022	109.82
199	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	313.14	03/2020 -	10/2022	16.97
200	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	2,215.27	4.60	- -	-	153.55
201	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	191.39	- -	-	104.65

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
202	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18	480.00	378.63	03/2020	09/2021	14.24
	<u>Northern Railway</u>							
203	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65	359.00	116.87	-	03/2024	129.17
204	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00	893.45	717.17	12/2011	06/2021	211.31
205	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91	791.39	597.99	-	09/2023	134.90
206	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68	419.00	160.79	-	09/2023	41.71
207	QADIAN-BEAS - [N22000295]	04/2011	205.22	841.90	1.73	-	03/2024	310.24
208	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00	2,017.96	878.49	07/2012	11/2024	348.44
209	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	27,949.00	25,828.58	11/2002	12/2022	1,017.96
210	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14	1,540.13	242.55	03/2023	03/2023	369.35
211	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00	839.00	839.36	03/2016	-	34.24
	<u>Rail Vikas Nigam Ltd.</u>							
212	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70	2,440.53	1,842.99	02/2015	06/2022	102.92
213	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	405.83	03/2009 03/2009	12/2022	224.56
214	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51	4,639.00	1,422.91	03/2016	03/2025	59.22
215	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99	6,753.42	1,809.22	12/2026	12/2025	127.62
216	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00	3,000.00	2,400.15	03/2023	12/2022	41.04
217	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	3,033.55	03/2016	03/2025	7.78
218	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42	2,733.86	40.46	03/2014	12/2025	18.95
219	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71	3,377.00	3,126.39	03/2020	03/2022	124.58
220	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62	1,650.00	1,689.43	12/2021	12/2021	69.12
221	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38	872.65	937.77	03/2021	12/2021	35.42

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
222	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	2,128.65	12/2021 -	03/2022	20.68
223	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	836.26	03/2016 -	12/2021	50.15
224	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	3,082.97	12/2023 -	12/2023	9.32
225	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	945.85	03/2022 -	12/2024	5.98
226	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	925.02	12/2024 -	12/2024	9.83
227	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,429.50	03/2019 -	06/2022	51.02
228	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	4,874.57	12/2024 -	03/2025	40.08
229	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,900.00	2,831.13	03/2020 -	12/2021	306.46
230	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	1,887.58	12/2024 -	12/2026	42.47
231	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	2,119.84	03/2020 -	12/2021	111.91
232	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,233.58	03/2019 -	06/2022	62.89
233	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,710.66	12/2020 -	12/2022	54.24
234	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,972.62	12/2020 -	12/2021	23.55
235	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,409.57	03/2020 -	06/2022	102.11
	<u>Railway Electrification</u>							
236	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
237	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,035.50	03/2009 -	03/2024	102.85
238	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	1,373.74	646.34	03/2010 -	03/2024	18.38
239	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	-	-	161.86
240	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	714.51	03/2023 -	03/2024	5.16
241	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,333.00	1,290.39	03/2021 -	03/2024	1.94
242	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	680.25	03/2020 -	02/2022	31.75

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
243	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	42.44
244	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,421.35	2,004.42	03/2000 -	03/2023	98.57
245	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	1,365.73	03/2022 -	03/2024	7.06
246	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	242.28	67.24	03/2022 -	03/2022	102.36
	<u>South East Central Railway</u>							
247	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,176.60	1,417.20	03/2023 -	12/2023	66.44
248	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	04/2010	585.93 -	1,268.32	1,082.34	02/2019 -	12/2021	116.46
249	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	378.60
250	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 -	2,135.34	700.69	03/2021 -	12/2023	8.23
251	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	712.76	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
252	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
253	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	41.78	-	03/2025	131.89
254	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
255	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
256	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	1,071.24	03/2020 -	03/2022	35.38
257	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
258	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	1,801.01 -	2,161.36	82.47	-	12/2023	20.01
259	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 -	1,530.09	316.23	03/2016 -	12/2026	55.13
260	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	-	-	12/2023	24.09
261	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	-	-	12/2023	57.65
262	RAYADURGA-TUMKUR NL - [N22000279	04/2007	2,062.30 -	2,404.03	1,087.98	-	12/2025	16.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
263	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	-	-	12/2023	12.38
264	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	158.11	-	12/2024	123.51
265	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	41.74
266	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,968.00	1,174.76	03/2020 -	03/2023	70.10
267	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,104.00	966.68	03/2020 -	09/2021	28.31
268	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	642.52	03/2020 -	12/2021	31.49
269	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,488.87	03/2019 -	03/2024	16.31
270	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	732.89	469.70	03/2017 -	03/2025	13.67
	<u>Southern Railway</u>							
271	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,950.00	1,667.29	02/2019 -	03/2025	307.07
272	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,150.00	239.53	- -	12/2025	440.47
273	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	705.52	03/2020 -	03/2025	465.83
274	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	264.50	- -	-	79.80
275	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	247.32
276	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	130.17
277	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	0.63	- -	03/2030	.00
278	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	749.40	550.86	- -	01/2022	177.41
279	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	709.69	8.50	- -	03/2025	180.55
280	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.23	1.63	- -	03/2030	109.04
281	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	608.13	399.75	- -	02/2022	269.89
282	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,122.00	989.62	- -	12/2022	20.39
283	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	448.10	6.73	- -	03/2025	136.79

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
284	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	285.53	03/2019 -	12/2027	1,699.64
285	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	0.82	-	03/2025	33.90
286	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	920.91	03/2005 -	09/2021	253.33
	<u>West Central Railway</u>							
287	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,378.97	03/2021 -	03/2024	585.35
288	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	3,230.57
289	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,449.00	1,293.48	03/2020 -	03/2024	38.84
290	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	16.02
291	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	508.67	03/2022 -	03/2023	114.32
	<u>Western Railway</u>							
292	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	76.13
293	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	126.36	03/2012 -	10/2023	1.06
294	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,886.76	1,875.42	03/2020 -	03/2024	127.39
295	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	974.69	03/2022 -	03/2023	13.17
296	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	04/2007	1,640.04 -	1,873.10	869.58	03/2022 -	03/2025	14.21
297	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2023	329.77
298	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	33.41
299	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	3.96
300	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]	03/2010	265.88 -	311.36	-	-	-	17.11
301	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 -	393.62	152.98	-	-	81.07
302	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 -	528.49	123.75	-	-	112.88
303	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]	03/2012	153.83 -	154.15	103.45	-	-	.21

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	Total		2,37,744.15	4,83,777.42	224,456.45			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
304	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41	992.67	978.43	03/2011	-	58.98
305	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69	327.92	323.23	10/2010	12/2021	69.30
306	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97	268.92	229.77	08/2015	-	3.84
307	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	01/2014	282.41	319.96	193.43	03/2016	04/2022	13.30
308	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16	290.59	244.36	-	-	3.72
309	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	314.12	09/2017	-	36.24
310	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08	390.73	326.56	05/2017	05/2022	45.75
311	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24	904.82	851.32	-	-	1.75
312	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04	377.99	368.39	10/2010	-	93.80
313	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68	369.77	319.07	-	-	15.67
314	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	183.94	05/2016	-	.26
315	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	100.67	06/2016	-	.02
316	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73	461.00	116.25	-	-	.06
317	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80	238.00	121.78	11/2019	10/2021	.08
318	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21	174.90	154.26	08/2018	12/2021	5.23

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
319	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	120.51	11/2018 -	03/2022	7.39
320	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	26.91	08/2019 -	11/2022	33.51
321	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	77.57	08/2019 -	08/2022	11.18
322	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	331.86	08/2017 -	02/2020	42.48
323	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	182.97	08/2018 -	12/2021	4.45
324	FOUR LANEING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	333.09	12/2015 -	-	6.07
325	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	169.64	07/2019 -	-	.31
326	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	390.40	03/2018 -	12/2021	9.23
327	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 -	318.28	181.43	01/2019 -	-	7.06
328	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 -	386.41	345.82	10/2018 -	-	18.58
329	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	369.96	322.13	09/2019 -	-	10.03
330	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	308.85	09/2014 -	12/2021	72.36
331	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	1,242.74	- -	-	2.93
332	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 -	319.96	115.07	- -	03/2022	13.68
333	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	572.66	284.62	08/2016 -	06/2022	15.19
334	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	400.86	09/2016 -	12/2021	14.24
335	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	470.70	10/2016 -	12/2021	17.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
336	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 -	236.18	33.22	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
337	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	142.18	04/2017 -	03/2022	29.48
338	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	148.30	04/2017 -	03/2022	29.48
339	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	342.06	08/2016 -	05/2021	3.73
340	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	152.53	04/2017 -	03/2022	27.16
341	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	295.14	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>							
342	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	612.58	612.58	02/2009 -	-	118.78
343	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	-	04/2009 -	-	70.23
344	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	-	11/2008 -	-	159.95
345	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	-	11/2008 -	-	64.62
346	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
347	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	3,450.00	11/2011 -	-	106.50
348	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
349	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
350	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	16.67
351	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66
352	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	578.00	11/2013 -	-	15.53
353	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	07/2012	291.36 -	469.31	459.07	01/2014 -	-	61.08
354	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	04/2014	351.34 -	417.68	433.68	01/2016 -	-	18.88

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
355	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	-	26.66
356	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	694.42	05/2018 -	03/2022	40.22
357	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	277.34	- -	-	.77
358	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	716.78	622.88	05/2018 -	03/2022	20.82
359	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	902.51	- -	01/2020	11.33
360	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	989.55	06/2018 -	-	68.71
361	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	799.07	- -	10/2021	1.37
362	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
363	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	503.71	- -	-	6.11
364	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	272.27	- -	-	1.33
365	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 -	1,096.52	518.73	04/2018 -	-	50.90
366	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,511.49	- -	-	41.78
367	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,023.88	- -	-	21.50
368	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	648.77	04/2018 -	-	25.80
369	MEERUT-BULANDSHAHAHAR - [N24000539]	01/2016	683.24 -	987.94	-	- -	-	44.60
370	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
371	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	- -	04/2021	7.53
372	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 -	486.00	406.73	- -	-	6.11
373	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	14.40
374	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,367.00	- -	-	94.94

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
375	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	336.60	316.60	08/2018 -	-	3.98
376	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	1,462.67	08/2019 -	-	16.55
377	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	1,355.00	-	-	4.10
378	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	246.70	-	05/2017	8.35
379	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2022	19.25
380	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 -	1,361.00	449.41	-	-	8.78
381	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	1,294.21	03/2020 -	-	10.58
382	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88
383	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	-	03/2020 -	-	3.40
384	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	-	03/2020 -	-	5.56
385	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	1.06
386	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	-	03/2020 -	-	5.70
387	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	443.91	03/2020 -	09/2022	.23
388	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	75.90	03/2020 -	-	9.38
389	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	966.71	03/2020 -	-	13.97
390	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	1,033.61	03/2020 -	-	10.24
391	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	18.50
392	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	41.54

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
393	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	1,311.37	03/2020 -	-	44.39
394	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	3.95
395	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	1.78
396	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	629.21	09/2017 -	-	9.67
397	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	481.97	-	09/2021	10.68
398	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	109.40	-	-	.99
399	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09
400	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	346.17	-	01/2022	11.20
401	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	3,378.36	-	11/2021	20.28
402	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	2,498.34	-	-	12.50
403	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	97.16	-	-	54.69
404	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	1,176.70	-	-	29.35
405	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	1,517.15	-	-	18.87
406	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,361.00	449.41	-	-	29.35
407	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	1,009.18	03/2021 -	07/2021	63.05
408	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	64.82	-	-	8.26
409	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	402.95	-	03/2021	22.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
410	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	309.05	- -	01/2022	5.32
411	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	- -	12/2021	4.99
412	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	- -	11/2021	.12
413	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	925.96	341.09	- -	02/2018	45.89
414	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	922.64	387.49	- -	02/2018	15.98
415	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	716.34	- -	-	25.68
416	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	429.00	- -	12/2021	.00
417	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	297.00	- -	11/2022	27.86
418	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	486.00	- -	10/2022	305.58
419	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 -	732.34	279.40	11/2019 -	-	.06
420	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	167.02	11/2019 -	-	2.02
	Total		86,912.44 -	1,07,895.52	74,723.75			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
421	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	19,016.02	05/2015 -	01/2022	41.32
	<u>Ra triya Ispat Nigam Limited</u>							
422	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85 -	2,100.00	1,736.92	09/2018 -	11/2021	24.79
	Total		17,207.85 -	24,040.00	20,752.94			
	<u>TELECOMMUNICATIONS</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Department Of Telecommunication</u>							
423	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	84.97
	Total		13,334.00 -	24,664.00	20,545.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
424	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	9,472.48	12/2018 -	08/2022	18.69
	<u>Bangalore Metro Rail Corporation Limited</u>							
425	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	02/2014	26,405.14 -	30,695.12	18,874.67	02/2019 -	03/2025	16.25
	<u>Central Public Works Department</u>							
426	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	06/2015	197.33 -	217.00	173.51	04/2019 -	02/2022	9.97
	<u>Chennai Metro Rail Ltd</u>							
427	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	18,380.00	17,619.68	12/2015 -	02/2019	25.89
	<u>Kochi Metro Rail Corporation Ltd</u>							
428	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	09/2020	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>							
429	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	19,493.96	03/2020 -	03/2023	44.39
	<u>Patna Metro Rail Corporation</u>							
430	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 -	13,925.50	302.95	06/2024 -	06/2024	4.19
	Total		93,659.03 -	1,15,628.76	71,996.42			
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
431	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 -	413.29	0.05	09/2020 -	-	62.63
432	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	291.32	03/2020 -	03/2021	76.68
	<u>Kolkata Metropolitan Development Authority</u>							
433	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23
	<u>Polavaram Project Authority</u>							
434	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	18,317.91	03/2020 -	04/2022	447.22

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Uttar Pradesh Jal Nigam</u>							
435	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008	10/2017	213.62 -	261.12	-	03/2022 -	03/2022	22.24
436	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020	02/2011	279.91 -	330.05	260.12	12/2019 -	01/2021	17.91
437	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	14.63	12/2021 -	12/2021	.97
438	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 -	690.71	-	06/2022 -	06/2022	1.31
	Total		12,236.47 -	58,101.66	18,884.03			
	Grand Total		7,28,272.16	11,94,911.97	694,947.30			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 6,840.00	6,840.00	6,054.37	09/2010 10/2022	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	17,298.00	12/2015 -	02/2022	74	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,709.00	12/2016 -	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	25,603.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	62,664.37					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	402.00	390.15	06/2019 10/2021	11/2021	29	-8.28	NIL
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB I AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	458.00	157.18	03/2020 06/2022	04/2022	25	0	NIL

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	104.49	02/2020 12/2021	05/2022	27	0	1. A portion of the site measuring 3.42 acres is fouling in the Runway extension and Basic Strip due to which the work will be further delay 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men,materials & Machinery for the work.
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 707.73	707.73	476.54	09/2018 06/2022	06/2022	45	69.63	NIL
9	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	303.80	189.25	04/2020 -	06/2022	26	0	NIL
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	475.39	169.84	04/2021 -	08/2022	16	0	NIL
11	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	314.79	09/2020 -	09/2022	24	0	NIL
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	477.10	10/2021 -	10/2022	12	0	NIL
13	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63 -	645.63	-	08/2022 -	11/2022	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
14	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH	07/2018	346.27 -	480.33	114.59	09/2021 -	12/2022	15	38.72	NIL
15	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	412.24	212.35	06/2021 -	12/2022	18	0	Diversion of Road Crossing the runway is pending with state Govt. (Amount Deposited by AAI)
16	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI, WEST BENGAL	01/2019	389.71 -	389.71	199.30	11/2021 01/2023	01/2023	14	0	2
17	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	371.33	03/2021 03/2022	03/2023	24	7.88	
18	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	1,405.00	368.21	08/2022 -	03/2023	7	0	1) Doshaliguna & Lomakotadi Village road diversion. 2) Resolving land swapping of Doshaliguna village. 3) Removal of structures of Lomakotadi village coming inside operational area. 4) Relocation of Juna Hirasar village 5) Relocation of wind mills. 6) Land swapping for N.H. expansion & flyover construction.
19	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	2,467.00	728.99	02/2022 -	12/2023	22	0	NIL
20	CCS INTERNATIONAL AIRPORT, LUCKNOW - [N04000077]AAI, UTTAR PRADESH	06/2018	1,383.00 1,938.00	1,983.00	534.84	09/2021 -	12/2023	27	43.38	NIL
21	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI, BIHAR	05/2018	1,216.90 -	1,216.90	229.22	10/2022 -	12/2023	14	0	AUGUMENTATION OF STORM WATER DRAINAGE SYSTEM FOR CONNECTING NEW STORM WATER SYSTEM OF AIRPORT WITH ENLARGED CAPACITY.
22	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI, TAMIL NADU	06/2019	380.87 -	380.87	15.41	03/2022 12/2023	12/2023	21	0	NIL
	Total		13,466.56 -	14,544.84	5,053.58					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
23	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	285.81	05/2014 -	12/2021	91	0	
24	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2022	12	0	
25	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	24.86	04/2018 -	10/2022	54	37.56	
26	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	73.17	03/2017 -	10/2022	67	12.2	
27	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	501.39	04/2015 -	02/2023	94	0	
28	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	69.37	04/2014 -	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									
29	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	124.85	03/2011 -	03/2022	132	0	
30	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	497.97	03/2016 -	03/2022	72	0	
31	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.46	03/2014 -	03/2022	96	0	
32	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND	08/2008	6,964.33 7,254.37	7,254.37	729.50	07/2012 03/2028	03/2028	188	4.16	
33	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND	02/2012	4,983.58 4,983.58	4,983.58	360.01	03/2020 03/2028	03/2028	96	0	
	<u>Eastern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
34	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73	5,146.48	622.22	08/2019	08/2024	60	93.35	i). Publication of final figure of Demographic survey report for Non-ECL houses by ADDA. ii). Publication of valuation of immovable properties for LTH households by ADDA to assess the financial implications for payment of cash compensation to affected beneficiaries. iii). Identification and finalization of balance 33.69 Ha land in non-coal bearing areas for construction of remaining flats in connection with implementation of this rehabilitation project. iv). As per resolution of review meeting taken by Sec(coal), CMPDI, RI-1 has identified land areas both in non-coal bearing and deep-seated coal bearing measures and report was sent to ADDA for utilization in rehabilitation purpose. WB Govt. is examining the status of encumbrance free land areas. Communication in this regard is yet to be received from State authority. v). Furthermore, CMPDI has examined the stability status of 192.74 acres Govt. vested land out of the list submitted by CEO, ADDA. The report was communicated to ADDA to check the encumbrance free status of land areas. Out of this 192.74 acres, ADDA has accepted only 37.23 acres encumbrance free land areas belong to mouza Mahatadih for rehabilitation purpose. The examination of encumbrance free status of balance 155.51 acres vested land areas is under way by concerned Deptt. of WB Govt. However, no updated status on the matter has yet been received from ADDA. vi). Shifting of affected families (on the basis of priority list to be prepared as per vulnerability of

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
35	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL, WEST BENGAL	11/2015	1,210.12 -	1,210.12	49.04	03/2022 03/2029	03/2029	84	0	
36	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	690.16	03/2018 -	03/2029	132	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.
	<u>Mahanadi Coal Fields Limited</u>									
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	708.55	729.73	03/2013 -	03/2024	132	47.76	
38	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	240.64	03/2019 -	03/2024	60	0	
39	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38 -	1,375.38	659.30	03/2021 -	09/2025	54	0	
40	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL, ODISHA	12/2007	8,416.19 8,416.19	8,416.19	941.90	03/2013 03/2028	03/2028	180	0	
41	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL, ODISHA	12/2007	3,504.21 3,504.21	3,504.21	589.86	03/2010 03/2029	03/2029	228	0	
42	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL, ODISHA	12/2007	3,145.45 -	3,145.45	637.17	03/2017 -	03/2031	168	0	
	<u>Neyveli Lignite Corporation</u>									
43	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	12,656.73	11/2021 11/2022	11/2022	12	0	PPA
44	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC, JHARKHAND	07/2013	1,795.01 -	1,795.01	37.13	08/2022 -	09/2023	13	0	
45	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	709.06	496.17	06/2015 03/2025	03/2025	117	-51.37	
	<u>Northern Coal Fields Limited</u>									
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	825.70	03/2021 -	03/2022	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
47	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	316.50	03/2022 -	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
48	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84	-32.3	
49	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	293.69	03/2015 -	03/2022	84	114.6	
50	KALYANIKHANI OPENCAS T PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	135.30	07/2016 -	03/2022	68	-7.91	
51	KAKATIYAKHANI OPENCAS T-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	112.99	03/2019 -	03/2022	36	11.42	
52	KAKATIYAKHANI OPENCAS T III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	206.41	03/2019 -	03/2022	36	0	
53	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
54	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	183.12	03/2015 -	03/2023	96	5.85	
	<u>South-Eastern Coal Fields Limited</u>									
55	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	199.99	03/2015 03/2020	03/2022	84	201.44	
56	AMADAND OPENCAS T EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	127.49	03/2021 -	03/2022	12	0	
57	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	210.73	03/2014 -	03/2023	108	0	
58	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	0	
59	AMGAON OPENCAS T PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	146.27	03/2020 -	03/2023	36	0	
60	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	66.57	03/2021 -	03/2024	36	0	
61	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	100.65	03/2021 04/2024	04/2024	37	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
62	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	231.92	1.78	03/2022 -	03/2025	36	0	
63	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	08/2015	1,186.64 -	1,186.64	234.04	03/2023 -	03/2026	36	0	
64	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	11.37	03/2014 -	03/2026	144	0	
65	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	0	
66	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2027	48	0	
67	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	0	
	Western Coal Fields Limited									
68	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 299.67	299.67	164.36	03/2019 03/2022	03/2022	36	1.39	
69	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 327.41	327.41	160.84	03/2019 -	03/2022	36	7.52	
70	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 402.90	402.90	336.00	03/2020 09/2022	09/2022	30	11.07	
71	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	217.47	03/2021 09/2022	09/2022	18	0	
72	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	103.38	03/2021 09/2022	09/2022	18	0	
73	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	296.56	03/2021 09/2023	09/2023	30	0	
74	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	145.08	03/2023 -	03/2024	12	15.41	
75	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	149.32	03/2021 03/2024	03/2024	36	0	
76	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	36.10	03/2022 03/2025	03/2025	36	0	
77	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 826.80	826.80	233.76	03/2020 03/2026	03/2026	72	-2.91	
78	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	18.24	03/2022 03/2026	03/2026	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
79	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	392.88	03/2020 03/2027	03/2027	84	0	
	Total		76,766.38 -	79,761.61	27,158.85					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									
80	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N0800014]NFL,HARYANA	01/2018	215.92 -	215.92	172.93	11/2019 06/2021	10/2021	23	0	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
81	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N0800018]RCF,MAHARASHTRA	04/2018	426.72 -	426.72	314.91	04/2020 10/2021	10/2021	18	0	
	Total		642.64 -	642.64	487.84					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
82	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N1000012]NALCO,ODISHA	12/2015	355.00 -	355.00	95.45	11/2020 -	12/2023	37	0	
83	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N1000013]NALCO,ODISHA	11/2017	483.00 483.00	483.00	6.91	04/2021 12/2023	12/2023	32	0	
84	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N1000010]NALCO,ODISHA	12/2014	5,540.00 6,435.90	5,540.00	988.67	04/2021 01/2024	01/2024	33	0	
	Total		6,378.00 -	6,378.00	1,091.03					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
85	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	19,016.02	05/2015 01/2022	01/2022	80	41.32	
	<u>Rastriya Ispat Nigam Limited</u>									
86	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	2,100.00	1,736.92	09/2018 11/2021	11/2021	38	24.79	No
87	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,858.00	2,004.81	12/2017 07/2022	07/2022	55	0	No
	<u>Steel Authority Of India Limited (SAIL)</u>									
88	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	207.19	06/2019 10/2021	12/2021	30	0	
89	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	557.75	10/2017 12/2021	11/2022	61	0	
	Total		21,362.73 -	28,194.88	23,522.69					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
90	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL, KARNATAKA	10/2018	206.26 -	206.26	155.99	03/2021 -	11/2021	8	0	
91	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	1,507.24	769.00	06/2019 -	02/2022	32	35.54	
92	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	640.00	357.57	12/2021 -	03/2022	3	0	
93	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66	117.11	
94	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	248.55	136.91	06/2022 -	09/2022	3	0	
95	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	242.18	02/2021 -	03/2023	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
96	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA	08/2019	1,607.00	1,607.00	283.87	08/2022	06/2023	10	0	
	<u>Chennai Petroleum Corporation Limited</u>									
97	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00	305.00	288.20	08/2020	12/2021	16	-27.55	
	<u>Gas Authority Of India Limited</u>									
98	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40	2,000.00	1,652.70	12/2020	11/2021	11	-30.59	
99	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78	200.00	197.30	04/2018	12/2021	44	-38.98	
100	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00	1,933.00	1,484.70	12/2020	12/2021	12	0	
101	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00	2,433.00	2,166.20	12/2020	12/2021	12	0	
102	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00	3,048.00	2,129.90	12/2020	12/2021	12	-11.32	
103	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00	1,740.00	939.30	12/2020	12/2021	12	0	
104	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42	327.01	223.50	08/2020	12/2021	16	14.17	
105	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00	5,909.00	3,773.40	12/2012	02/2022	110	102.71	
106	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92	217.92	101.80	04/2021	03/2022	11	0	
107	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54	247.90	47.78	02/2021	08/2022	18	9.91	
	<u>Hindustan Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
108	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	303.40	216.34	03/2021 -	10/2021	7	0	
109	SWRO II WITH LLP FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	104.54	07/2020 -	01/2022	18	0	
110	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	183.21	06/2020 -	03/2022	21	0	
111	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	111.34	06/2020 -	03/2022	21	0	
112	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA	06/2018	380.00 -	380.00	306.50	11/2021 -	03/2022	4	0	
113	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	125.01	08/2021 -	03/2022	7	0	
114	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	16,536.13	07/2020 07/2022	07/2022	24	25.5	
115	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 -	3,072.00	2,574.63	06/2021 08/2022	07/2022	13	14.76	
116	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	155.75	09/2026 02/2027	02/2027	5	0	
117	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	369.06	03/2029 08/2029	08/2029	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
118	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL	03/2019	5,830.20 -	5,830.20	136.39	03/2031 08/2031	08/2031	5	0	1. Laying of Gas pipeline along across NH-2 Application made by company in August 2020 for laying of Gas pipeline along across NH-2 for 22 km in Hooghly District to National Highway Authority of India. Permission awaited from PD PIU Durgapur NHAI Complex, Durgapur, WB. Assistance is sought for expediting the issue of demand note permissions to lay the CGD pipeline along across NH-2
	<u>Indian Oil Corporation Limited</u>									
119	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL, ASSAM	08/2018	557.00 -	557.00	556.96	02/2020 06/2021	11/2021	21	0	
120	AUGMENTATION OF CTMPL - [N16000286]IOCL, TAMIL NADU	12/2016	228.00 -	228.00	156.18	11/2021 -	12/2021	1	0	
121	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 319.61	319.61	219.15	06/2020 12/2021	12/2021	18	35.43	
122	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL, BIHAR	07/2018	189.00 -	189.00	171.59	01/2021 06/2021	12/2021	11	0	
123	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	466.00	290.69	04/2021 -	12/2021	8	0	
124	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL, BIHAR	04/2018	522.00 -	522.00	376.88	03/2021 12/2021	12/2021	9	0	
125	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL, HARYANA	08/2019	1,255.00 -	1,255.00	298.37	10/2021 -	12/2021	2	0	
126	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	466.43	258.36	10/2020 01/2022	01/2022	15	0	
127	LPG BP PROJECT MOTIHARI - [N16000317]IOCL, BIHAR	05/2018	206.50 -	206.50	157.79	03/2021 09/2021	01/2022	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
128	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	4,049.27	12/2018 02/2022	02/2022	38	33.98	
129	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	419.33	02/2020 02/2022	02/2022	24	0	
130	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,163.26	03/2021 12/2021	03/2022	12	66.09	
131	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 3,338.00	3,338.00	3,071.72	12/2020 03/2022	03/2022	15	43.82	
132	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	596.34	07/2018 05/2021	03/2022	44	0	
133	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	109.97	08/2020 03/2022	03/2022	19	0	
134	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	345.08	02/2020 10/2021	03/2022	25	0	
135	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	823.08	10/2021 -	03/2022	5	0	
136	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	316.20	130.90	10/2021 03/2022	03/2022	5	0	
137	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	466.82	01/2021 03/2022	03/2022	14	0	
138	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	16.46	07/2021 03/2022	03/2022	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
139	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	924.60	08/2020 04/2022	04/2022	20	0	
140	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT	10/2019	403.00 -	403.00	181.90	12/2021 -	04/2022	4	0	
141	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	104.05	02/2020 06/2021	06/2022	28	0	
142	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	462.30	107.63	09/2021 06/2022	06/2022	9	0	
143	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 207.36	207.36	126.85	04/2020 10/2021	07/2022	27	27.2	
144	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 340.76	340.76	145.36	02/2020 07/2022	07/2022	29	64.91	
145	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	5,654.00 -	5,654.00	3,485.97	10/2021 07/2022	07/2022	9	0	
146	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	100.38	06/2021 07/2022	07/2022	13	0	
147	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	179.80	01/2021 -	08/2022	19	25.57	
148	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	72.98	10/2020 08/2022	08/2022	22	0	
149	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	500.28	10/2017 03/2022	09/2022	59	103.6	
150	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA	05/2019	3,361.00 -	3,361.00	2,039.85	08/2021 09/2022	09/2022	13	0	
151	LPG BP PROJECT KHANDA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	56.21	12/2019 03/2022	10/2022	34	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
152	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	173.55	08/2021 -	11/2022	15	0	
153	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	10.81	07/2022 -	01/2023	6	0	
154	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	124.99	04/2022 -	02/2023	10	0	
155	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 427.00	427.00	28.69	09/2022 03/2023	03/2023	6	15.09	
156	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,199.60	2,281.94	553.94	12/2022 07/2023	07/2023	7	0	
157	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	96.02	04/2022 -	08/2023	16	0	
158	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.29	09/2023 -	02/2024	5	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
159	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	534.34	03/2020 11/2020	11/2021	20	9.64	
160	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,766.26	12/2019 04/2021	02/2022	26	0	
161	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 304.00	304.00	2.56	06/2023 01/2024	01/2024	7	52	
	<u>Oil & Natural Gas Corporation Limited</u>									
162	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	222.27	05/2020 08/2021	11/2021	18	21.57	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
163	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	2,203.71	2,121.13	05/2021 12/2021	12/2021	7	-3.87	
164	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	791.49	12/2020 12/2021	12/2021	12	-3.93	
165	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	05/2019	3,660.71 3,740.05	3,740.05	3,032.38	05/2021 01/2022	01/2022	8	2.17	
166	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	2,001.34	1,599.60	05/2013 05/2022	05/2022	108	132.23	
167	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,884.63	04/2018 05/2022	05/2022	49	5.8	
168	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]ONGC,GUJARAT	10/2018	156.67 -	156.67	62.93	03/2021 05/2022	05/2022	14	0	
169	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	14,210.03	06/2020 06/2022	06/2022	24	-26.23	
170	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	1,463.48	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
171	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	510.00	485.08	12/2019 -	12/2021	24	-10.79	
172	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 652.10	638.60	395.08	02/2020 -	12/2021	22	17.41	
173	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 222.21	198.00	183.20	08/2020 09/2021	12/2021	16	-11.9	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
174	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	281.34	10/2020 -	03/2022	17	0	
	Total		1,46,121.16 -	1,52,701.43	89,521.79					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
175	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	2,083.10	04/2020 07/2025	07/2025	63	0	
	<u>National Hydro-Electric Power Corporation</u>									
176	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	9,279.64	09/2009 03/2023	03/2023	162	152.52	
177	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	14,458.38	09/2010 08/2023	08/2023	155	218.08	PPA is yet to be signed with Delhi DISCOMS for Power of 113 MW.
	<u>National Thermal Power Corporation</u>									
178	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	401.90	180.67	04/2021 10/2021	10/2021	6	0	
179	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,993.63	07/2012 06/2020	11/2021	112	97.38	Support of State Govt. required for early resolution of acquisition / possession of 39.94 Acres of critical land balance due to court cases, wrong payments in awarded land and ownership disputes in following areas: Main Plant: 20.66 acres Ash Dyke: 13.45 acres Township: 5.83 acres De-notification of 17.69 Acres GMM land for Ralyatikaran is critical as construction of Overflow Lagoon of Ash Dyke is held up. The proposal for de-notification is with Revenue Dept. GOB, since 05.02.2020. Report sent by Dist Authorities on 15.12.20.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
180	KAWAS SOLAR 56 MW - [N18000283]NTPC, GUJARAT	08/2020	261.80 -	261.80	87.43	10/2021 01/2022	11/2021	1	0	
181	JETSAR SOLAR 160 MW - [N18000287]NTPC, RAJASTHAN	12/2019	702.28 -	702.28	539.41	03/2021 11/2021	11/2021	8	0	
182	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 2,311.89	2,311.89	1,922.67	12/2018 -	12/2021	36	22.64	
183	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC, KERALA	09/2019	403.62 -	403.62	116.32	06/2021 12/2021	12/2021	6	0	
184	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC, RAJASTHAN	01/2020	1,522.71 -	1,522.71	996.32	09/2021 10/2022	01/2022	4	0	
185	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 17,304.00	17,304.00	16,371.88	05/2018 -	02/2022	45	33.47	
186	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 633.80	633.80	472.23	11/2018 -	02/2022	39	19.66	
187	DEVIKOT SOLAR 90MW - [N18000280]NTPC, UTTAR PRADESH	03/2020	501.29 -	501.29	342.98	09/2021 02/2022	02/2022	5	0	
188	DEVIKOT SOLAR 150MW - [N18000281]NTPC, UTTAR PRADESH	01/2020	798.24 -	798.24	415.99	09/2021 02/2022	02/2022	5	0	
189	FATEHGARH SOLAR 296MW - [N18000289]NTPC, RAJASTHAN	03/2020	1,749.31 -	1,749.31	1,277.87	09/2021 02/2022	02/2022	5	0	
190	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC, TAMIL NADU	03/2020	1,316.22 -	1,316.22	687.97	09/2021 02/2022	02/2022	5	0	
191	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC, RAJASTHAN	03/2020	1,782.00 -	1,782.00	672.69	09/2021 07/2022	09/2022	12	0	
192	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC, TELANGANA	01/2016	10,598.98 10,997.70	10,997.70	8,866.73	11/2020 07/2022	10/2022	23	3.76	
193	NOKHRA - [N18000282]NTPC, UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	436.25	09/2021 07/2022	01/2023	16	0	
194	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 21,312.11	21,312.11	19,311.93	10/2011 07/2023	07/2023	141	145.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
195	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58	15,389.42	12,291.69	06/2019 10/2022	09/2023	51	7.12	Support of State Govt of Jharkhand is required for following: 1.Maintaining Law & order and resolution of following issue: Agitation by villagers for compensation on already awarded land. Raiyats had stopped site works completely w.e.f. 23.02.2021 for demand of additional compensation for already acquired land, which continued till 30.03.2021. Work was started but the workforce strength is still very low, due to fear of another agitation. 2.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 3.Acquisition of Land by CCL for external CHP. 4.Early completion of Road Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD. The road diversion in project area needs to be completed on priority. 5.Repair of damaged bridge over Garhi River is critical for transportation of material for project. 6.Forest clearance in ATS lines.
196	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	5,187.12	03/2013 12/2021	09/2024	138	96.99	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
197	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.54	721.34	09/2019 12/2024	12/2024	63	-0.2	•All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSECL. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (11Nos + 01 School).
198	PATRATU STPP-I (3X800MW) - [N18000275]NTPC, JHARKHAND	11/2017	18,668.00 -	17,112.00	4,391.63	03/2023	02/2025	23	-8.34	
	Power Grid Corporation Of India Limited									
199	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	14,733.37	11,683.96	11/2019 07/2021	10/2021	23	0	
200	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	1,931.39	1,807.75	02/2020 09/2021	10/2021	20	0	
201	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	252.99	04/2016 12/2017	12/2021	68	0	
202	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE	05/2014	522.29 546.36	546.36	480.66	11/2016 12/2021	12/2021	61	4.61	
203	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	197.40	90.75	03/2018 -	12/2021	45	0	
204	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL, DELHI	03/2015	1,394.52 -	1,394.52	561.71	05/2017 12/2021	12/2021	55	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
205	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	156.95	06/2019 11/2021	12/2021	30	0	
206	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	235.98	12/2019 09/2021	12/2021	24	0	
207	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	167.22	07/2019 07/2021	12/2021	29	17.99	
208	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	260.80	05/2020 08/2021	12/2021	19	0	
209	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	204.37	02/2019 09/2021	02/2022	36	0	
210	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,096.25	07/2020 12/2020	02/2022	19	14.11	
211	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	3,207.16	12/2018 12/2021	03/2022	39	31.08	
212	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,979.18	08/2013 11/2022	08/2022	108	32.24	
213	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,697.96	12/2018 03/2024	03/2024	63	92.02	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
214	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	704.97	12/2021 06/2022	06/2022	6	46.2	1. Stay imposed by Hon'ble High Court of Uttarakhand on all construction activities within 200 m of the river. 2. Agitation by locals in project area. 3. Delay due to Covid-19 pandemic. 4. Geological challenges. 5. Change in Design and scope of work.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Thdc India Limited</u>									
215	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 1,587.16	1,587.16	629.21	09/2020 08/2022	08/2022	23	-24.57	1. Te nancy/Private land (337.35 Ha): 06 cases, out of total 53 cases of land losers are pending in Court of Collector, Singrauli due to which distribution of Compensation is delayed. 2. Govt. land of Coal Block (178.13 Ha): Collector, Singrauli to issue necessary direction to concerned department for compliance of conditions mentioned in order dtd 13.09.21. 3. Revenue land for R&R (53.13 Ha): Necessary direction for handing over of above land pending with District Collector, Singrauli. 4. Forest land (0.87 Ha) for CEC and RS: Issuance of FRA certificate by Collector, Singrauli is pending. Deposition of Rs. 5.45 lakh (NPV)+Rs. 24.27 lakh (compensatory afforestation)+ Rs. 2.43 lakh (supervision charges) i.e. Total Rs. 32.15 Lakh, as per demand of DFO, Singrauli is under process by THDCIL. 5. Govt. and Private Land for CEC and RS: Expeditious action is required from District Authorities for handing over of both Govt. and Private Land to start the work.
216	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 4,825.60	4,825.60	4,266.10	02/2016 -	06/2023	88	191.23	Pending signing of Lease Deed with GoUK for existing 3 Ha. Land at Asena Quarry after permission of extension of mining lease received on 19.04.21 from GoUK and Allotment of additional 4.916 Ha. Land for mining at Asena Quarry by GoUK.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
217	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	2,822.96	09/2023	08/2024	11	0	Continuous help of District administration is required for expeditious shifting of Nagla residents to newly identified land.
218	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	3,860.35	2,313.83	06/2013	12/2024	138	54.94	No any. Regular support on law & order issues is being provided by GoUK/ District Administration, Chamoli since Jun'21.
	Total		1,70,020.67	2,29,586.27	1,58,726.63					
	HEALTH AND FAMILY WELFARE									
	Cpwd For Health									
219	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29	150.29	64.32	03/2020	12/2021	21	0	
220	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00	195.00	16.41	09/2020	04/2022	19	0	
221	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00	260.00	25.38	06/2021	05/2022	11	0	
	Hospital Services Consultancy Corporation Ltd									
222	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15	355.15	317.45	03/2019	10/2021	31	0	
223	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99	363.99	253.84	05/2018	03/2022	46	0	
	Nbcc For Health									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
224	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH, HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	9	8.88	
	Total		2,675.43 -	2,795.43	1,548.20					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
225	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,905.60	03/2021 -	03/2023	24	111.08	
226	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	1,387.52	357.95	03/2021 -	03/2023	24	75	
227	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	1,283.49	515.13	03/2022 -	03/2023	12	.89	
228	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	540.02	354.61	03/2022 -	03/2024	24	0	
229	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,449.91 -	2,449.91	466.67	03/2023 -	03/2024	12	0	
230	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	1,035.16 -	1,035.16	314.37	03/2022 -	03/2024	24	0	
231	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	637.95 -	637.95	237.71	03/2023 -	03/2024	12	0	
	<u>East Central Railways</u>									
232	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 678.54	929.86	926.80	03/2019 12/2021	12/2021	33	37.04	
233	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	236.91	03/2019 -	03/2022	36	0	Land acquisition
234	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	390.00	386.59	03/2021 -	03/2022	12	11.99	
235	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 898.53	1,080.00	1,077.28	03/2012 11/2022	11/2022	128	232.58	
236	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR, BIHAR	12/2015	1,200.20 1,200.20	1,200.20	971.03	03/2020 -	03/2023	36	0	
237	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR, BIHAR	12/2015	1,491.47 -	1,491.47	552.33	03/2020 03/2023	03/2023	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
238	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,367.09	03/2020 -	03/2024	48	0	
239	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	513.54	03/2021 03/2024	03/2024	36	63.37	
240	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	383.26	03/2021 03/2024	03/2024	36	62.06	
241	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	541.64	03/2020 03/2023	12/2024	57	49.45	land acquisition
	<u>East Coast Railway</u>									
242	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	1,195.24	02/2019 03/2022	03/2022	37	38.43	
243	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	223.69	03/2020 -	03/2022	24	52.77	
244	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	1,010.84	03/2020 03/2023	03/2023	36	.07	
245	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	696.10	03/2022 03/2023	03/2023	12	0	
246	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	269.52	10/2020 03/2024	03/2024	41	0	
247	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	193.71	11/2018 03/2024	03/2024	64	15.45	
248	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	692.35	12/2018 03/2024	03/2024	63	0	
249	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	909.17	06/2021 03/2025	03/2025	45	137.8	
250	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,649.76	03/2009 03/2026	03/2026	204	29.71	
251	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	737.43	03/2022 03/2024	03/2026	48	0	
252	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	493.76	03/2022 03/2026	03/2026	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Railways</u>									
253	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	638.28	02/2013 -	03/2024	133	134.8	
254	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	908.35	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30 KM between Kamarpukur and Jairambati in Hooghly district is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
255	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
256	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98	2,137.81	439.23	03/2022	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
257	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52	995.10	614.87	03/2016	03/2025	108	7.75	
258	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51	769.40	97.40	03/2017	03/2025	96	29.2	Suri – Prantik New Line (33.90 Km). - The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
259	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28	266.32	199.72	03/2016	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
260	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17	439.30	480.96	03/2017	03/2025	96	20.3	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non-availability of land.
261	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54	494.59	30.12	03/2005	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bakrahahat (9.75 Km) New line-- Work could not be started due to non availability of land

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
262	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
263	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	109.51	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
264	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
265	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	45	0	
266	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	18	117.23	
267	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	5,200.00	101.77	03/2020 -	03/2025	60	0	
	<u>Metropolitan Rapid Transport Projects</u>									
268	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,866.85	03/2004 06/2022	06/2022	219	501.57	
269	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	478.72	06/2013 07/2022	07/2022	109	48.06	
	<u>North Central Railway</u>									
270	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	680.00	4.00	03/2020 -	12/2021	21	1.69	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
271	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	2,001.00	980.08	03/2021 12/2022	12/2023	33	0	NIL
272	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	329.61	03/2022 12/2024	12/2024	33	32.02	
273	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	71.56	03/2023 -	06/2025	27	0	Due follow up is in progress with U.P & M.P Govt. for land acquisition.
	<u>North East Frontier Railway</u>									
274	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,881.59	12/2008 -	11/2021	155	284.8	
275	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,498.64	03/2021 -	03/2022	12	115.07	
276	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 90.00	742.00	561.03	03/2020 06/2022	06/2022	27	30.26	
277	NEW B.G. LINE FROM TETELIA TO BYRNihat (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,043.00	873.80	03/2019 -	03/2023	48	170.77	
278	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,842.95	03/2022 -	03/2023	12	32.15	
279	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	11,504.51	03/2011 -	12/2023	153	175.34	
280	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	8,600.00	1,656.78	12/2015 12/2023	12/2023	96	542.04	
281	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	328.75	03/2019 -	12/2023	57	13.6	
282	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	1,021.19	03/2019 -	03/2024	60	302.54	
283	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	4,232.46	03/2014 -	03/2024	120	130.69	
284	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,647.64	1,369.40	03/2015 -	03/2026	132	185.73	
	<u>North Eastern Railway</u>									
285	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	69.01	04/2016 -	12/2021	68	.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
286	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	610.00	580.83	01/2019 -	02/2022	37	106.78	
287	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	315.05	01/2022 -	03/2022	2	-38.88	
288	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
289	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	127.77	
290	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									
291	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	759.31	02/2019 -	06/2022	40	109.82	
292	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	313.14	03/2020 -	10/2022	31	16.97	
293	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	356.84	08/2022 -	11/2022	3	0	
	<u>Northern Railway</u>									
294	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	25,828.58	11/2002 -	12/2022	241	1017.96	
295	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,017.96	2,017.96	878.49	07/2012 -	11/2024	148	348.44	
296	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	0	
	<u>Rail Vikas Nigam Ltd.</u>									
297	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	872.65	937.77	03/2021 -	12/2021	9	35.42	
298	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	836.26	03/2016 -	12/2021	69	50.15	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
299	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,900.00	2,831.13	03/2020 -	12/2021	21	306.46	
300	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	2,119.84	03/2020 -	12/2021	21	111.91	
301	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,347.35	03/2020 -	12/2021	21	-7.28	
302	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,972.62	12/2020 -	12/2021	12	23.55	
303	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	2,128.65	12/2021 -	03/2022	3	20.68	
304	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	3,126.39	03/2020 -	03/2022	24	124.58	
305	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,842.99	02/2015 -	06/2022	88	102.92	
306	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,429.50	03/2019 -	06/2022	39	51.02	
307	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,233.58	03/2019 -	06/2022	39	62.89	
308	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,056.49	03/2022 -	06/2022	3	-23.24	
309	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,409.57	03/2020 -	06/2022	27	102.11	
310	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	433.00	405.83	03/2009 12/2022	12/2022	165	224.56	
311	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,710.66	12/2020 -	12/2022	24	54.24	
312	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	945.85	03/2022 -	12/2024	33	5.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
313	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92	1,765.92	1,054.05	03/2023	12/2024	21	0	
314	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98	4,259.48	3,033.55	03/2016	03/2025	108	7.78	
315	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51	4,639.00	1,422.91	03/2016	03/2025	108	59.22	
316	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00	22,716.11	4,874.57	12/2024	03/2025	3	40.08	
317	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42	2,733.86	40.46	03/2014	12/2025	141	18.95	
318	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67	3,327.72	1,887.58	12/2024	12/2026	24	42.47	
<u>South Central Railway</u>										
319	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 927.94	927.94	680.25	03/2020	02/2022	23	31.75	
320	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,004.42	03/2000	03/2023	276	98.57	
321	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20	2,120.16	1,035.50	03/2009	03/2024	180	102.85	
322	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48	1,373.74	646.34	03/2010	03/2024	168	18.38	
323	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95	1,952.68	714.51	03/2023	03/2024	12	5.16	
324	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 2,333.00	2,333.00	1,290.39	03/2021	03/2024	36	1.94	
325	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03	2,063.03	1,582.36	03/2021	03/2024	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
326	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,365.73	03/2022 -	03/2024	24	7.06	
327	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	156	42.44	
	<u>South East Central Railway</u>									
328	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 1,268.32	1,268.32	1,082.34	02/2019 12/2021	12/2021	34	116.46	
329	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 3,176.60	3,176.60	1,417.20	03/2023 12/2023	12/2023	9	66.44	
330	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 2,135.34	2,135.34	700.69	03/2021 12/2023	12/2023	33	8.23	
331	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	1,370.94	712.76	12/2021 12/2023	12/2023	24	.07	
332	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 852.50	1,096.00	40.47	12/2021 12/2024	12/2024	36	378.6	
	<u>South Eastern Railway</u>									
333	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.96	1,071.24	03/2020 -	03/2022	24	35.38	
334	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,028.57	03/2021 -	12/2023	33	0	
335	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	
336	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
337	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	760.00	642.52	03/2020 12/2021	12/2021	21	31.49	
338	HUBLI- CHIKAJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,968.00	1,174.76	03/2020 -	03/2023	36	70.1	
339	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.97	03/2016 -	12/2023	93	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
340	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	264	41.74	
341	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
342	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	1,878.00	1,488.87	03/2019 -	03/2024	60	16.31	
343	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	732.89	469.70	03/2017 -	03/2025	96	13.67	
344	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	373.87	12/2018 -	06/2025	78	0	
345	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	1,530.09	316.23	03/2016 -	12/2026	129	55.13	
<u>Southern Railway</u>										
346	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	705.52	03/2020 -	03/2025	60	465.83	
347	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,950.00	1,667.29	02/2019 -	03/2025	73	307.07	
348	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
349	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	285.53	03/2019 -	12/2027	105	1699.64	
350	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	133	247.32	
<u>West Central Railway</u>										
351	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	508.67	03/2022 -	03/2023	12	114.32	
352	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 2,875.12	2,875.12	1,035.16	03/2022 06/2023	06/2023	15	16.02	
353	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 2,909.99	2,909.99	1,378.97	03/2021 03/2024	03/2024	36	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
354	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	2,449.00	1,293.48	03/2020	03/2024	48	38.84	Work is suffering badly on this Critical project due pending forest land clearance. The detail position is as under: ∴ Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. ∴ Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 17454 Nos trees cutting have been submitted on 18.08.2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
355	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202	3230.57	Nil
	<u>Western Railway</u>									
356	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,125.53	1,383.69	1,199.84	03/2021 12/2022	12/2022	21	33.41	
357	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	1,042.12	730.07	03/2021 12/2022	12/2022	21	3.96	
358	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	6,171.08	2,327.60	03/2022 03/2023	03/2023	12	76.13	
359	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,524.68	1,524.68	974.69	03/2022 03/2023	03/2023	12	13.17	
360	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.96	1,378.11	558.66	03/2019 03/2023	03/2023	48	329.77	
361	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	314.13	06/2020 03/2023	03/2023	33	-13.76	
362	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 -	692.25	.77	03/2020 -	03/2023	36	0	
363	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	126.36	03/2012 10/2023	10/2023	139	1.06	
364	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,246.59	1,886.76	1,875.42	03/2020 03/2024	03/2024	48	127.39	
365	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	495.18	.33	03/2022 -	03/2024	24	0	
366	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	1,873.10	869.58	03/2022 03/2025	03/2025	36	14.21	
	Total		1,92,054.49 -	3,22,695.21	1,66,681.71					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
367	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 237.80	238.00	121.78	11/2019 10/2021	10/2021	23	.08	
368	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021	25	0	
369	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	448.61	01/2020 06/2021	11/2021	22	0	
370	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	773.30	02/2020 08/2021	11/2021	21	0	
371	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	223.22	03/2018 11/2021	11/2021	44	0	
372	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	142.81	08/2020 -	11/2021	15	0	
373	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	205.95	108.58	01/2021 -	11/2021	10	0	
374	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	237.29	09/2020 -	11/2021	14	0	
375	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	322.96	11/2017 11/2021	11/2021	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
376	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021	134	69.3	
377	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	282.08	207.83	06/2019 12/2021	12/2021	30	0	
378	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021	19	0	
379	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	12/2021	45	0	
380	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 174.90	174.90	154.26	08/2018 08/2021	12/2021	40	5.23	
381	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	125.42	02/2018 09/2021	12/2021	46	0	
382	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	129.31	03/2017 06/2021	12/2021	57	0	
383	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	182.97	08/2018 09/2021	12/2021	40	4.45	
384	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	166.48	03/2018 10/2021	12/2021	45	0	
385	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	198.83	07/2018 08/2021	12/2021	41	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
386	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	238.57	09/2019 06/2021	12/2021	27	0	
387	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	615.21	07/2018 05/2021	12/2021	41	0	
388	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	743.57	06/2019 04/2021	12/2021	30	0	
389	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	536.65	552.29	12/2019 12/2021	12/2021	24	0	
390	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	390.40	03/2018 06/2021	12/2021	45	9.23	
391	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	322.24	308.85	09/2014 12/2021	12/2021	87	72.36	
392	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	192.35	08/2020 -	12/2021	16	0	
393	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	279.60	06/2017 12/2021	12/2021	54	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
394	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	400.86	09/2016 12/2021	12/2021	63	14.24	
395	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	470.70	10/2016 12/2021	12/2021	62	17.04	
396	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	295.71	01/2018 12/2021	12/2021	47	0	
397	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	90.41	05/2019 12/2021	12/2021	31	0	
398	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	254.43	09/2020 01/2022	01/2022	16	0	
399	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	160.00	124.58	09/2021 -	02/2022	5	0	
400	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.51	11/2018 01/2021	03/2022	40	7.39	
401	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	183.37	02/2018 03/2022	03/2022	49	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
402	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	139.54	03/2021 11/2021	03/2022	12	0	
403	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.89	04/2020 -	03/2022	23	-8.28	
404	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	250.97	03/2015 03/2022	03/2022	84	0	
405	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE - I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 319.96	319.96	193.43	03/2016 04/2022	04/2022	73	13.3	
406	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	61.20	03/2018 04/2021	04/2022	49	0	
407	REHABILITATION AND UPGRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	102.76	03/2021 -	04/2022	13	0	
408	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	390.73	326.56	05/2017 05/2022	05/2022	60	45.75	
409	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	80.06	03/2018 09/2021	06/2022	51	0	
410	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	572.66	284.62	08/2016 06/2022	06/2022	70	15.19	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
411	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	263.26	77.57	08/2019 08/2022	08/2022	36	11.18	
412	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	213.97	26.91	08/2019 -	11/2022	39	33.51	
413	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH, MADHYA PRADESH	03/2015	511.83 -	511.83	403.23	08/2017 06/2021	12/2022	64	0	
414	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH, CHHATISGARH	03/2016	452.94 435.61	435.61	112.86	07/2016 12/2022	12/2022	77	-3.83	
415	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH, ANDHRA PRADESH	06/2020	221.40 -	221.40	16.24	05/2021 -	12/2022	19	0	
416	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH, ANDHRA PRADESH	08/2020	222.61 -	222.61	6.94	03/2021 -	03/2023	24	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
417	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL, A & N ISLANDS	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	54	0	
418	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	36	-18.09	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
419	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM	03/2015	168.39	168.39	148.91	11/2018	11/2021	36	0	
420	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL, NAGALAND	03/2018	237.72	237.72	126.19	09/2018	11/2021	38	0	
421	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL, NAGALAND	03/2018	251.97	251.97	146.10	09/2018	11/2021	38	0	
422	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL, NAGALAND	03/2018	282.98	282.98	161.15	09/2018	11/2021	38	0	
423	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL, NAGALAND	03/2018	215.12	215.12	108.86	09/2018	11/2021	38	0	
424	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39	437.39	105.09	06/2018	12/2021	42	0	
425	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49	463.49	165.06	06/2018	12/2021	42	0	
426	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99	289.99	95.89	12/2018	12/2021	36	0	
427	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03	315.03	115.77	09/2018	12/2021	39	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
428	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	121.06	09/2018 -	12/2021	39	0	
429	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	77.59	09/2018 -	12/2021	39	0	
430	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	154.83	11/2017 -	12/2021	49	0	
431	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022	39	0	
432	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	588.95	504.10	11/2018 -	02/2022	39	0	
433	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	346.86	05/2018 -	03/2022	46	0	
434	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	219.83	01/2016 -	03/2022	74	0	
435	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	136.10	01/2016 -	03/2022	74	0	
436	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	167.81	04/2017 03/2021	03/2022	59	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
437	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	252.79	142.18	04/2017 -	03/2022	59	29.48	
438	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	263.31	148.30	04/2017 -	03/2022	59	29.48	
439	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	252.05	152.53	04/2017 -	03/2022	59	27.16	
440	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31 -	274.31	126.90	05/2018 -	03/2022	46	0	
441	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL, UTTARAKHAND	03/2018	403.36 -	403.36	217.43	06/2018 -	03/2022	45	0	
442	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL, UTTARAKHAND	03/2018	417.24 -	417.24	265.48	05/2018 -	03/2022	46	0	
443	2 LANE WITH HARD SHOULDER, REHABILITATION AND UPGRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51	0	
444	REHABILITATION AND UPGRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
445	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41	0	
446	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	387.00	315.99	09/2018 -	03/2022	42	0	
447	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	0	
448	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	133.81	05/2019 -	03/2022	34	0	
449	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	116.27	09/2018 -	05/2022	44	0	
450	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	169.77	09/2018 -	07/2022	46	0	
451	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	280.16	07/2018 -	07/2022	48	0	
452	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	89.53	09/2018 -	09/2022	48	0	
453	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	63.44	09/2018 -	10/2022	49	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
454	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	115.32	09/2018 -	11/2022	50	0	
455	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	83.73	09/2019 -	04/2023	43	0	
456	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	118.96	09/2019 04/2023	04/2023	43	0	
457	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	129.40	09/2019 06/2023	04/2023	43	0	
458	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	106.57	09/2019 04/2023	06/2023	45	0	
459	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	126.61	09/2019 04/2023	06/2023	45	0	
460	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	94.28	09/2019 06/2023	07/2023	46	0	
461	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	82.60	09/2019 09/2023	09/2023	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
462	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	41.29	09/2019 03/2024	04/2024	55	0	
	<u>National Highways Authority Of India</u>									
463	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	1,003.47	11/2018 -	10/2021	35	-25.83	
464	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	594.02	06/2018 10/2021	10/2021	40	0	
465	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	11/2021	99	0	
466	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	719.29	09/2017 11/2021	11/2021	50	0	
467	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 1,928.22	1,928.22	1,890.04	04/2015 01/2021	12/2021	80	0	
468	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	12/2021	44	0	
469	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	398.58	07/2018 -	12/2021	41	0	
470	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29	0	
471	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29	0	
472	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	243.59	03/2020 -	12/2021	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
473	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	1,285.31	03/2020 12/2021	12/2021	21	0	
474	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	398.58	07/2016 -	12/2021	65	0	
475	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	718.00	12/2019 -	12/2021	24	0	
476	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	90.50	04/2014 -	01/2022	93	0	
477	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	429.86	08/2018 -	01/2022	41	0	
478	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	77.82	05/2013 -	02/2022	105	-55.37	
479	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 02/2022	02/2022	43	19.25	
480	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	311.03	08/2017 -	02/2022	54	0	
481	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,633.18	03/2013 -	03/2022	108	0	
482	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	744.73	694.42	05/2018 03/2022	03/2022	46	40.22	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
483	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 717.24	716.78	622.88	05/2018 03/2022	03/2022	46	20.82	
484	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36	0	
485	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	23	3.95	
486	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	556.00	03/2020 -	04/2022	25	0	
487	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	538.00	05/2020 -	05/2022	24	0	
488	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	233.12	03/2019 12/2021	06/2022	39	0	
489	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59	0	
490	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	770.94	09/2017 -	07/2022	58	0	
491	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	443.91	03/2020 -	09/2022	30	.23	
492	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	450.47	04/2019 10/2022	10/2022	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
493	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	18.66	
494	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	348.00	03/2019 01/2021	12/2022	45	-25.48	
495	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	32.96	12/2017 -	05/2023	65	0	
496	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023	118	0	
	Total		67,133.82 -	68,156.72	46,293.43					
	TELECOMMUNICATIONS									
	Bharat Sanchar Nigam Limited									
497	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	422.87	46.37	06/2021 11/2021	11/2021	5	-1.92	
	Cpwd For Telecom									
498	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	145.26	03/2018 -	12/2021	45	0	
	Department Of Telecommunication									
499	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	20,545.00	07/2015 05/2020	03/2022	80	84.97	
	Total		14,013.36 -	25,335.07	20,736.63					
	URBAN DEVELOPMENT									
	Ahmedabad Metro Rail									
500	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	9,472.48	12/2018 -	08/2022	44	18.69	NA
	Bangalore Metro Rail Corporation Limited									
501	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	18,874.67	02/2019 03/2025	03/2025	73	16.25	NIL

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Central Public Works Department									
502	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 238.56	238.56	208.13	05/2020 11/2021	11/2021	18	0	
503	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 217.00	217.00	173.51	04/2019 02/2022	02/2022	34	9.97	Reason were mentioned during period of occurrence, available in previous months report.
504	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 392.00	392.00	161.81	08/2020 06/2022	06/2022	22	0	
505	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 299.97	299.97	20.39	09/2020 01/2023	01/2023	28	0	
506	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 422.00	422.00	108.75	03/2021 06/2023	06/2023	27	0	
507	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 1,100.80	1,100.80	35.74	07/2021 06/2023	06/2023	23	-6.71	
508	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	1,128.00	30.00	03/2022 -	06/2023	15	0	
	Lucknow Metro Rail Corporation Limited									
509	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	1,917.78	03/2024 -	03/2025	12	0	NO
510	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	426.47	03/2024 -	05/2025	14	0	NO
	Maharashtra Metro Rail Corporation Ltd.									
511	PUNE METRO RAIL PROJECT (PHASE I) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11,420.00	7,187.19	11/2021 12/2022	12/2022	13	0	•Delay in Land acquisition at Khadki •Delay in Slum R& R at Kamgar Putala & Rajiv Gandhi Nagar

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(October 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Mumbai Metro Rail Corporation Ltd</u>									
512	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00	33,406.00	19,493.96	03/2020 03/2023	03/2023	36	44.39	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
513	NAGPUR METRO RAIL - [N28000085]NMRC, MAHARASHTRA	08/2014	8,680.00	8,680.00	8,427.24	03/2018 12/2021	12/2021	45	0	NIL
	Total		1,03,728.10	1,20,242.55	66,538.12					
	<u>WATER RESOURCES</u>									
	<u>Brahmaputra Board</u>									
514	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB, MAHARASHTRA	03/2017	233.57	233.57	148.83	12/2019	12/2021	24	0	
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
515	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19	305.19	28.31	08/2021	12/2021	4	0	
	<u>Delhi Jal Board</u>									
516	REHABILITATION AND UPGRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79	211.79	108.28	12/2021	12/2022	12	0	
517	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11	239.11	149.02	02/2022	12/2022	10	0	
	<u>Kolkata Metropolitan Development Authority</u>									
518	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022	06/2022	4	13.23	
519	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022	10/2022	8	-3.29	
	<u>Polavaram Project Authority</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
520	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	18,317.91	03/2020 11/2021	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
521	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-28.25	
	Total		11,797.25 -	57,131.86	18,752.35					
	<u>DEFENCE PRODUCTION</u>									
	<u>Cpwd For Defence</u>									
522	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD FOR DEFENC,KARNATAKA	12/2016	246.31 210.00	210.00	149.80	02/2020 10/2021	12/2021	22	-14.74	
	Total		246.31 -	210.00	149.80					
	<u>DEPARTMENT OF HIGHER EDUCATION</u>									
	<u>Cpwd Of Higher Education</u>									
523	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH	11/2012	270.83 -	244.00	241.67	11/2014 11/2021	11/2021	84	-9.91	
524	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD EDUCATION,UTTAR PRADESH	11/2017	171.72 135.00	171.72	110.13	03/2020 12/2021	12/2021	21	0	
525	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	17	0	
526	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	498.99	292.81	06/2017 -	03/2022	57	.57	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
527	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB	01/2018	430.00 -	387.83	228.61	05/2020 -	06/2022	25	-9.81	
528	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA	01/2019	790.79 -	790.79	230.59	03/2022 -	06/2022	3	0	
529	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	0	
530	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	424.93	55.00	07/2022 -	10/2022	3	0	
531	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	249.81	07/2022 -	10/2022	3	0	
532	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	24.91	05/2022 -	10/2022	5	0	
533	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	110.13	09/2020 -	11/2022	26	0	
534	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	0	
535	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	177.82	03/2021 -	02/2023	23	0	
	Total		6,533.03 -	6,466.84	1,880.02					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (October 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	HOME AFFAIRS									
	Cpwd For Mha									
536	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL	10/2014	162.88 238.00	238.00	172.13	04/2018 12/2021	12/2021	44	46.12	
537	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 -	2,000.00	1,007.93	10/2019 -	03/2022	29	64.04	
538	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35 290.33	290.33	27.25	07/2022 10/2022	10/2022	3	4.68	
	Total		1,659.44 -	2,528.33	1,207.31					
	DPIIT									
	Iicc For Dpiit									
539	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,178.00	3,013.69	12/2019 05/2022	05/2022	29	8.49	
	Total		4,773.00 -	5,178.00	3,013.69					
	Grand Total		9,06,492.37	12,02,897.68	6,95,028.04					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(October 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	6,840.00	6,054.37	09/2010	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00	16,580.00	17,298.00	12/2015	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00	17,079.00	13,709.00	12/2016	03/2023	38.63	75
	Total		27,271.00	40,499.00	37,061.37				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27	480.33	114.59	09/2021	12/2022	38.72	15
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23	707.73	476.54	09/2018	06/2022	69.63	45
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	371.33	03/2021	03/2023	7.88	24
7	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00	1,983.00	534.84	09/2021	12/2023	43.38	27
	Total		3,288.50	4,403.06	1,497.30				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
8	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00	334.27	24.86	04/2018	10/2022	37.56	54
9	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13	341.22	73.17	03/2017	10/2022	12.20	67
	<u>Central Coal Fields Limited</u>								
10	MAGADH EXPANSION OC(51 MTY) - [N06000015]	08/2008	6,964.33	7,254.37	729.50	07/2012	03/2028	4.16	188
	<u>Eastern Coal Fields Limited</u>								
11	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	622.22	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	708.55	729.73	03/2013 -	03/2024	47.76	132
	<u>Neyveli Lignite Corporation</u>								
13	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	12,656.73	11/2021 -	11/2022	.00	12
	<u>Singareni Colliers Company Limited</u>								
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	293.69	03/2015 -	03/2022	114.60	84
15	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	112.99	03/2019 -	03/2022	11.42	36
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	183.12	03/2015 -	03/2023	5.85	96
17	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
18	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	199.99	03/2015 -	03/2022	201.44	84
	<u>Western Coal Fields Limited</u>								
19	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	36.10	03/2022 -	03/2025	.00	36
20	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	299.67	164.36	03/2019 -	03/2022	1.39	36
21	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	327.41	160.84	03/2019 -	03/2022	7.52	36
22	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	145.08	03/2023 -	03/2024	15.41	12
23	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 -	402.90	336.00	03/2020 -	09/2022	11.07	30
	Total		31,009.03 -	34,889.43	16,884.45				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
24	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	292.81	06/2017 -	03/2022	.57	57
	Total		496.18 -	498.99	292.81				
	<u>DPIIT</u>								
	<u>licc For Dpiit</u>								
25	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE [N40000002]	11/2017	4,773.00 -	5,178.00	3,013.69	12/2019 -	05/2022	8.49	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		4,773.00 -	5,178.00	3,013.69				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Nbcc For Health</u>								
26	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	8.88	9
	Total		1,351.00 -	1,471.00	870.80				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								
27	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	238.00	172.13	04/2018 -	12/2021	46.12	44
28	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002	06/2019	277.35 -	290.33	27.25	07/2022 -	10/2022	4.68	3
29	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	1,007.93	10/2019 -	03/2022	64.04	29
	Total		1,659.44 -	2,528.33	1,207.31				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
30	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11	66
31	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	769.00	06/2019 -	02/2022	35.54	32
	<u>Gas Authority Of India Limited</u>								
32	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	47.78	02/2021 -	08/2022	9.91	18
33	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	223.50	08/2020 -	12/2021	14.17	16
34	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,773.40	12/2012 -	02/2022	102.71	110
	<u>Hindustan Petroleum Corporation Limited</u>								
35	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	2,574.63	06/2021 -	07/2022	14.76	13
36	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	16,536.13	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
37	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	04/2017	163.02 -	207.36	126.85	04/2020 -	07/2022	27.20	27
38	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	319.61	219.15	06/2020 -	12/2021	35.43	18
39	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	04/2018	206.63 -	340.76	145.36	02/2020 -	07/2022	64.91	29
40	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	06/2019	371.00 -	427.00	28.69	09/2022 -	03/2023	15.09	6
41	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	05/2016	348.00 -	437.00	179.80	01/2021 -	08/2022	25.57	19
42	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	500.28	10/2017 -	09/2022	103.60	59
43	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,163.26	03/2021 -	03/2022	66.09	12
44	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	3,071.72	12/2020 -	03/2022	43.82	15
45	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	4,049.27	12/2018 -	02/2022	33.98	38
<u>Mangalore Refinery And Petrochemicals Limited</u>									
46	DEVANGONTHI MARKETING TERMINAL - [N16000401]	06/2020	200.00 -	304.00	2.56	06/2023 -	01/2024	52.00	7
47	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	534.34	03/2020 -	11/2021	9.64	20
<u>Oil & Natural Gas Corporation Limited</u>									
48	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	222.27	05/2020 -	11/2021	21.57	18
49	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	1,599.60	05/2013 -	05/2022	132.23	108
50	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,884.63	04/2018 -	05/2022	5.80	49
51	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	3,032.38	05/2021 -	01/2022	2.17	8
52	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,463.48	03/2022 -	05/2023	23.16	14
<u>Oil India Limited</u>									
53	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	395.08	02/2020 -	12/2021	17.41	22
	Total		51,911.42 -	69,135.09	44,562.60				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
54	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210	09/2002	3,919.59 -	9,897.59	9,279.64	09/2009 -	03/2023	152.52	162
55	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221	09/2003	6,285.33 -	19,992.43	14,458.38	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
56	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277	12/2016	529.68 -	633.80	472.23	11/2018 -	02/2022	19.66	39
57	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276	05/2016	1,885.13 -	2,311.89	1,922.67	12/2018 -	12/2021	22.64	36
58	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	5,867.38	5,187.12	03/2013 -	09/2024	96.99	138
59	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	10,566.00	8,993.63	07/2012 -	11/2021	97.38	112
60	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	01/2016	10,598.98 -	10,997.70	8,866.73	11/2020 -	10/2022	3.76	23
61	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,389.42	12,291.69	06/2019 -	09/2023	7.12	51
62	NGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	17,304.00	16,371.88	05/2018 -	02/2022	33.47	45
63	BARH STPP(3X660MW) NTPC - [N180100242	02/2005	8,692.97 -	21,312.11	19,311.93	10/2011 -	07/2023	145.16	141
	<u>Power Grid Corporation Of India Limited</u>								
64	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	05/2017	186.17 -	219.66	167.22	07/2019 -	12/2021	17.99	29
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	546.36	480.66	11/2016 -	12/2021	4.61	61
66	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	03/2017	3,500.00 3,500.00	3,994.00	3,096.25	07/2020 -	02/2022	14.11	19
67	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,700.00	3,207.16	12/2018 -	03/2022	31.08	39
68	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,129.32	2,697.96	12/2018 -	03/2024	92.02	63
69	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	14,719.10	12,979.18	08/2013 -	08/2022	32.24	108
	<u>Satluj Jal Vidyut Nigam Limited</u>								
70	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	947.89	704.97	12/2021 -	06/2022	46.20	6
	<u>Thdc India Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
71	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58	3,860.35	2,313.83	06/2013	12/2024	54.94	138
72	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	4,825.60	4,266.10	02/2016	06/2023	191.23	88
	Total		97,575.65	1,59,214.60	127,069.23				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
73	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19	1,283.49	515.13	03/2022	03/2023	.89	12
74	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89	1,387.52	357.95	03/2021	03/2023	75.00	24
75	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	2,271.50	4,794.60	2,905.60	03/2021	03/2023	111.08	24
	<u>East Central Railways</u>								
76	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23	390.00	386.59	03/2021	03/2022	11.99	12
77	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00	819.01	541.64	03/2020	12/2024	49.45	57
78	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54	929.86	926.80	03/2019	12/2021	37.04	33
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73	1,080.00	1,077.28	03/2012	11/2022	232.58	128
80	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64	1,185.73	383.26	03/2021	03/2024	62.06	36
81	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04	1,215.54	513.54	03/2021	03/2024	63.37	36
	<u>East Coast Railway</u>								
82	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81	238.03	223.69	03/2020	03/2022	52.77	24
83	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61	810.02	193.71	11/2018	03/2024	15.45	64
84	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00	1,160.83	1,010.84	03/2020	03/2023	.07	36
85	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99	1,539.28	1,195.24	02/2019	03/2022	38.43	37
86	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78	1,928.07	909.17	06/2021	03/2025	137.80	45
87	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13	3,791.66	1,649.76	03/2009	03/2026	29.71	204
	<u>Eastern Railways</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
88	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60	335.62	1.12	03/2017	03/2026	12.02	108
89	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17	439.30	480.96	03/2017	03/2025	20.30	96
90	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54	494.59	30.12	03/2005	03/2025	.01	240
91	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99	545.70	149.31	03/2006	03/2025	34.08	228
92	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96	680.68	141.76	02/2012	03/2025	36.15	157
93	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51	769.40	97.40	03/2017	03/2025	29.20	96
94	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52	995.10	614.87	03/2016	03/2025	7.75	108
95	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09	1,425.44	638.28	02/2013	03/2024	134.80	133
96	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91	1,619.48	908.35	03/2019 12/2009	03/2025	36.22	72
97	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98	2,137.81	439.23	03/2022	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
98	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00	3,055.15	2,707.85	09/2018	06/2022	.00	45
99	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00	4,970.11	953.27	03/2022	09/2023	117.23	18
	<u>Metropolitan Rapid Transport Projects</u>								
100	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74	734.01	478.72	06/2013	07/2022	48.06	109
101	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44	2,980.41	1,866.85	03/2004	06/2022	501.57	219
	<u>North Central Railway</u>								
102	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	4.00	03/2020	12/2021	1.69	21
103	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96	3,845.60	329.61	03/2022	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
104	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63	742.00	561.03	03/2020	06/2022	30.26	27

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
105	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20	1,043.00	873.80	03/2019	03/2023	170.77	48
106	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96	1,873.21	1,498.64	03/2021	03/2022	115.07	12
107	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING [N22000183]	04/2013	1,798.00	2,042.51	328.75	03/2019	12/2023	13.60	57
108	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87	2,145.00	1,021.19	03/2019	03/2024	302.54	60
109	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32	2,950.00	1,842.95	03/2022	03/2023	32.15	12
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	1,180.19	4,541.38	3,881.59	12/2008	11/2021	284.80	155
111	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47	5,521.45	4,232.46	03/2014	03/2024	130.69	120
112	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52	6,647.64	1,369.40	03/2015	03/2026	185.73	132
113	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48	8,600.00	1,656.78	12/2015	12/2023	542.04	96
114	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17	12,264.15	11,504.51	03/2011	12/2023	175.34	153
	<u>North Eastern Railway</u>								
115	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00	213.35	69.01	04/2016	12/2021	.16	68
116	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00	341.66	-	04/2017	10/2022	127.77	66
117	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00	610.00	580.83	01/2019	02/2022	106.78	37
	<u>North Western Railway</u>								
118	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00	701.81	313.14	03/2020	10/2022	16.97	31
119	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08	860.41	759.31	02/2019	06/2022	109.82	40
	<u>Northern Railway</u>								
120	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00	2,017.96	878.49	07/2012	11/2024	348.44	148
121	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	27,949.00	25,828.58	11/2002	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>								
122	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	405.83	03/2009 03/2009	12/2022	224.56	165
123	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38	872.65	937.77	03/2021	12/2021	35.42	9

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
124	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68	950.00	836.26	03/2016	12/2021	50.15	69
125	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60	1,000.00	945.85	03/2022	12/2024	5.98	33
126	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01	1,400.00	1,429.50	03/2019	06/2022	51.02	39
127	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00	1,536.00	1,409.57	03/2020	06/2022	102.11	27
128	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95	1,536.00	1,233.58	03/2019	06/2022	62.89	39
129	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25	1,825.00	1,710.66	12/2020	12/2022	54.24	24
130	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85	1,835.83	1,972.62	12/2020	12/2021	23.55	12
131	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66	1,868.89	2,128.65	12/2021	03/2022	20.68	3
132	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04	2,009.00	2,119.84	03/2020	12/2021	111.91	21
133	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70	2,440.53	1,842.99	02/2015	06/2022	102.92	88
134	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42	2,733.86	40.46	03/2014	12/2025	18.95	141
135	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48	2,900.00	2,831.13	03/2020	12/2021	306.46	21
136	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67	3,327.72	1,887.58	12/2024	12/2026	42.47	24
137	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71	3,377.00	3,126.39	03/2020	03/2022	124.58	24
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	3,033.55	03/2016	03/2025	7.78	108
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51	4,639.00	1,422.91	03/2016	03/2025	59.22	108
140	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00	22,716.11	4,874.57	12/2024	03/2025	40.08	3
<u>South Central Railway</u>									
141	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31	927.94	680.25	03/2020	02/2022	31.75	23
142	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48	1,373.74	646.34	03/2010	03/2024	18.38	168

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
143	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95	1,952.68	714.51	03/2023	03/2024	5.16	12
144	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20	2,120.16	1,035.50	03/2009	03/2024	102.85	180
145	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70	2,333.00	1,290.39	03/2021	03/2024	1.94	36
146	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77	3,037.95	347.10	03/2014	03/2027	42.44	156
147	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00	3,421.35	2,004.42	03/2000	03/2023	98.57	276
148	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00	3,887.48	1,365.73	03/2022	03/2024	7.06	24
<u>South East Central Railway</u>									
149	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00	1,096.00	40.47	12/2021	12/2024	378.60	36
150	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93	1,268.32	1,082.34	02/2019	12/2021	116.46	34
151	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00	1,370.94	712.76	12/2021	12/2023	.07	24
152	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00	2,135.34	700.69	03/2021	12/2023	8.23	33
153	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51	3,176.60	1,417.20	03/2023	12/2023	66.44	9
<u>South Eastern Railway</u>									
154	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00	1,009.00	7.96	03/2015	03/2025	54.99	120
155	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83	1,312.96	1,071.24	03/2020	03/2022	35.38	24
156	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40	2,373.00	485.04	03/2003	03/2030	130.97	324
<u>South Western Railway</u>									
157	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78	732.89	469.70	03/2017	03/2025	13.67	96
158	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00	760.00	642.52	03/2020	12/2021	31.49	21
159	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30	1,530.09	316.23	03/2016	12/2026	55.13	129
160	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59	1,878.00	1,488.87	03/2019	03/2024	16.31	60
161	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78	1,960.00	7.35	03/2002	03/2024	41.74	264
162	HUBLI- CHIKAJAJUR - [N22000325]	03/2015	1,156.94	1,968.00	1,174.76	03/2020	03/2023	70.10	36
<u>Southern Railway</u>									

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
163	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	247.32	133
164	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	705.52	03/2020 -	03/2025	465.83	60
165	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	285.53	03/2019 -	12/2027	1,699.64	105
166	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,950.00	1,667.29	02/2019 -	03/2025	307.07	73
	<u>West Central Railway</u>								
167	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	508.67	03/2022 -	03/2023	114.32	12
168	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,449.00	1,293.48	03/2020 -	03/2024	38.84	48
169	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	16.02	15
170	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]	04/2001	424.60 -	2,909.99	1,378.97	03/2021 -	03/2024	585.35	36
171	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
172	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	126.36	03/2012 -	10/2023	1.06	139
173	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,042.12	730.07	03/2021 -	12/2022	3.96	21
174	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2023	329.77	48
175	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	33.41	21
176	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	974.69	03/2022 -	03/2023	13.17	12
177	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	04/2007	1,640.04 -	1,873.10	869.58	03/2022 -	03/2025	14.21	36
178	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,886.76	1,875.42	03/2020 -	03/2024	127.39	48
179	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,171.08	2,327.60	03/2022 -	03/2023	76.13	12
	Total		1,41,191.78 -	2,73,293.02	150,171.47				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
180	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	174.90	154.26	08/2018 -	12/2021	5.23	40
181	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	26.91	08/2019 -	11/2022	33.51	39
182	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	182.97	08/2018 -	12/2021	4.45	40
183	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	121.78	11/2019 -	10/2021	.08	23
184	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	77.57	08/2019 -	08/2022	11.18	36
185	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	120.51	11/2018 -	03/2022	7.39	40
186	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]	01/2014	282.41 -	319.96	193.43	03/2016 -	04/2022	13.30	73
187	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	308.85	09/2014 -	12/2021	72.36	87
188	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	323.23	10/2010 -	12/2021	69.30	134
189	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	326.56	05/2017 -	05/2022	45.75	60
190	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	390.40	03/2018 -	12/2021	9.23	45
191	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	400.86	09/2016 -	12/2021	14.24	63
192	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	284.62	08/2016 -	06/2022	15.19	70
193	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	470.70	10/2016 -	12/2021	17.04	62
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
194	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 -	252.05	152.53	04/2017 -	03/2022	27.16	59
195	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	142.18	04/2017 -	03/2022	29.48	59

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
196	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36	263.31	148.30	04/2017	03/2022	29.48	59
	<u>National Highways Authority Of India</u>								
197	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26	716.78	622.88	05/2018	03/2022	20.82	46
198	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84	722.46	722.46	07/2018	02/2022	19.25	43
199	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13	744.73	694.42	05/2018	03/2022	40.22	46
200	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54	756.27	443.91	03/2020	09/2022	.23	30
201	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691	04/2017	894.00	929.32	810.00	04/2020	03/2022	3.95	23
202	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00	3,379.45	3,379.45	03/2014	12/2022	18.66	105
	Total		11,034.82	13,062.93	10,498.78				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
203	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00	21,940.00	19,016.02	05/2015	01/2022	41.32	80
	<u>Rastriya Ispat Nigam Limited</u>								
204	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85	2,100.00	1,736.92	09/2018	11/2021	24.79	38
	Total		17,207.85	24,040.00	20,752.94				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
205	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00	24,664.00	20,545.00	07/2015	03/2022	84.97	80
	Total		13,334.00	24,664.00	20,545.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
206	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00	12,787.00	9,472.48	12/2018	08/2022	18.69	44
	<u>Bangalore Metro Rail Corporation Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
207	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	02/2014	26,405.14 -	30,695.12	18,874.67	02/2019 -	03/2025	16.25	73
	<u>Central Public Works Department</u>								
208	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 -	217.00	173.51	04/2019 -	02/2022	9.97	34
	<u>Mumbai Metro Rail Corporation Ltd</u>								
209	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	19,493.96	03/2020 -	03/2023	44.39	36
	Total		60,511.47 -	77,105.12	48,014.62				
	<u>WATER RESOURCES</u>								
	<u>Kolkata Metropolitan Development Authority</u>								
210	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23	4
	<u>Polavaram Project Authority</u>								
211	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	18,317.91	03/2020 -	04/2022	447.22	25
	Total		10,349.47 -	55,773.56	18,317.91				
	Grand Total		4,72,964.61	7,85,756.13	500,760.28				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Mahanadi Coal Fields Limited</u>				
2	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	03/2021
	<u>Neyveli Lignite Corporation</u>				
3	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
4	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
5	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
9	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	09/2021
	Total		14,560.71 -		
	<u>FINANCE</u>				
	<u>Cpwd For Finance</u>				
10	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
	Total		209.00 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
11	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	11/2019 05/2021	-
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 05/2021	-
	Total		458.64 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
13	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 12/2021	12/2020
14	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		700.62 -		
	<u>PETROLEUM</u>				
	<u>Indian Oil Corporation Limited</u>				
15	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021
16	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	08/2019 06/2021	05/2021
17	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	09/2021
18	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	09/2021
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
20	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,475.92	05/2021 05/2021	05/2021
21	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	03/2019 09/2021	09/2021
	Total		6,649.23 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
24	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
25	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				
26	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021
27	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	06/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
28	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021
	Total		15,680.45 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
29	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-
	<u>Natrip Implementation Society</u>				
30	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 03/2021	03/2021
	Total		3,272.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
31	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
	<u>HII Infra Tech Services Limited</u>				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
33	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
34	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
35	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
36	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
37	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
38	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
39	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
40	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
41	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	-	01/2021
42	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	03/2021
43	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	03/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
44	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021
45	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021
46	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
	Total		5,796.27 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
47	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-
48	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
49	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
50	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	-
51	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
52	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
53	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	-
54	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
55	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
56	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
57	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
58	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
59	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021
61	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	-
62	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
63	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
64	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
65	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
66	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
67	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
68	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
69	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
70	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
71	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
<u>Eastern Railways</u>					
72	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
73	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
<u>Kolkata Metro Rail Corporation Limited</u>					
74	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
<u>Metropolitan Rapid Transport Projects</u>					
75	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
76	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
77	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
78	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
<u>North East Frontier Railway</u>					
79	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
80	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
81	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
82	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
83	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
84	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
86	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-
87	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
88	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
89	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
90	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
91	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
92	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
93	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	420.18 -	03/2020 -	09/2021
94	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
95	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
96	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
97	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
98	ROHTAK-MEHAM HANSI - [N22000272]NR, HARYANA	04/2012	287.00 -	12/2011 -	06/2021
99	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR, MULTI STATE	03/2002	625.00 781.00	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
100	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES, TELANGANA	03/2015	636.38 -	03/2021 -	-
101	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES, CHHATISGARH	02/2016	393.98 -	03/2020 -	-
	<u>Railway Electrification</u>				
102	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
103	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	458.25 -	- -	-
104	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
105	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
106	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
107	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
108	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
109	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South Eastern Railway</u>				
110	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
111	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>South Western Railway</u>				
112	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021
	<u>Southern Railway</u>				
113	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021
114	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-
115	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
116	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 311.36	- -	-
	Total		84,579.23 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
117	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	09/2021
118	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
119	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020
120	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
121	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
122	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020
123	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2020	12/2020
124	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021
125	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
126	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
127	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 03/2020	03/2021
128	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021
129	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	04/2021
130	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021
131	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 06/2021	06/2021
132	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021
133	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021
134	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021
135	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021
136	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021
137	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021
138	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 12/2021	07/2021
139	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
140	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021
141	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021
142	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021
143	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021
144	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
145	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	02/2017 -	-
146	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
147	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	-	-
148	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	-	-
149	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	-	-
150	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	-	-
151	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	-	-
152	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
153	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
154	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
155	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 12/2021	-
156	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 273.27	08/2015 -	-
157	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	-	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
158	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
159	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-
160	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
161	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
162	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
163	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
164	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
165	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCHI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
166	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
167	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-
168	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
169	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
170	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-
171	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
172	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
173	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
174	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
175	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	
1	2	3	4	5	6
176	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
177	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-
178	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
179	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	-
180	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
181	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
182	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
183	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
184	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
185	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
186	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
187	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
188	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
189	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
190	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
191	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU) - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 10/2021	-
192	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 10/2021	-
193	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 02/2022	-
194	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 01/2022	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
195	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 12/2021	-
196	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 274.73	08/2018 11/2021	-
197	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 556.13	11/2018 07/2021	-
198	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 09/2021	-
199	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
200	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
201	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
202	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
203	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
204	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 381.75	08/2018 10/2021	-
205	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2021	-
206	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 11/2021	-
207	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 08/2021	-
208	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 12/2021	-
209	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 381.75	09/2017 05/2022	-
210	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 596.38	01/2018 04/2022	-
211	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
212	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
213	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH, TELANGANA	01/2017	244.54 -	05/2019 -	-
214	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH, TELANGANA	01/2017	196.52 -	10/2019 -	-
215	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH, TELANGANA	01/2017	283.00 -	12/2019 -	-
216	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH, TELANGANA	01/2017	359.27 -	05/2019 -	-
217	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH, TELANGANA	01/2017	300.00 -	05/2019 -	-
218	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH, TELANGANA	01/2018	283.15 -	05/2020 -	-
219	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH, TELANGANA	01/2018	230.03 -	12/2019 -	-
220	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA	02/2018	206.13 -	06/2020 -	-
221	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA	02/2018	294.13 -	11/2019 -	-
222	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA	02/2018	220.28 -	11/2019 -	-
223	REHABILITATION AND UPGADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA	02/2018	426.52 -	04/2020 -	-
224	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA	03/2018	322.81 -	09/2020 -	-
225	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA	03/2018	626.76 -	07/2020 -	-
226	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA	01/2017	605.08 -	10/2019 -	-
227	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA	03/2018	192.67 -	07/2019 -	-
228	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA	01/2019	193.19 -	- -	-
229	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH, BIHAR	03/2018	153.24 -	- -	-
230	SARSAM TO KOTHARI - [N24001002]MoRTH, MAHARASHTRA	02/2016	545.64 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
232	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
233	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
234	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
235	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
236	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
237	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
238	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
239	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
240	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
241	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
242	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
243	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
244	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
245	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
246	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
247	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
248	AMDHI TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
249	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
250	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
251	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
252	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
253	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
254	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
255	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
257	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
258	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
259	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
260	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
261	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
262	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
263	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
264	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
265	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
266	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
267	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
268	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
269	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
270	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
271	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
272	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
273	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
274	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
275	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
276	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
277	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
278	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
279	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
280	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
281	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
282	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
283	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
284	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
285	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
286	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
287	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
288	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
289	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
290	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
291	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
292	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
293	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
294	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
295	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
296	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
297	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
298	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
299	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
300	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
301	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
302	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
303	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
304	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
305	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
306	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
307	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
308	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
309	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
310	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
311	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
312	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
313	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
314	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
315	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
316	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
317	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
318	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
319	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
320	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
321	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
322	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
323	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
324	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
325	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
326	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
327	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
328	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
329	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
330	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
331	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
332	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
333	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
334	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
335	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
336	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
337	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
338	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	-
339	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
340	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
341	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
342	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
343	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
344	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
345	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
346	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
347	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
348	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
349	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
350	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
351	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
352	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
353	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	06/2021 -	-
354	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
355	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
356	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
357	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
358	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
359	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
360	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
361	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
362	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
363	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
364	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
365	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
366	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
367	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
368	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
369	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
370	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
371	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
372	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
373	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
374	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
375	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-
376	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	-
377	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	-
378	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-
379	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 08/2021	-
380	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
381	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
382	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
383	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 204.73	06/2019 -	-
384	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
385	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
386	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
387	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
388	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
389	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
390	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
391	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
392	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
393	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
394	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
395	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
396	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	-
397	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	-
398	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
399	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
400	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
401	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
402	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-
403	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	-
404	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
405	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 12/2021	-
406	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
407	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
408	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
409	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
410	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	03/2021
411	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
412	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
413	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- 09/2021	09/2021
414	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
415	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
416	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
417	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
418	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
419	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
420	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
<u>National Highways Authority Of India</u>					
421	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- 12/2016	05/2017
422	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- 02/2018	02/2018
423	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- 02/2018	02/2018
424	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018
425	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
426	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
427	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
428	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
429	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020
430	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
431	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
432	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
433	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
434	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
435	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
436	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
437	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
438	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
439	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021
440	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
441	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	04/2021
442	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021
443	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	06/2021
444	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- 10/2021	07/2021
445	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- 01/2022	07/2021
446	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 07/2021	07/2021
447	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					Anticipated
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	
1	2	3	4	5	6
448	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021
449	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	08/2021
450	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021
451	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021
452	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021
453	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 1,201.51	- 06/2021	09/2021
454	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021
455	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.24	- 05/2021	09/2021
456	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021
457	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
458	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
459	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
460	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
461	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
462	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
463	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
464	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
465	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-
466	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
467	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
468	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
469	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
470	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
471	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
472	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
473	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
474	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
475	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
476	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
477	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
478	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
479	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
480	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
481	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 12/2021	-
482	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
483	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
484	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
485	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
486	6-LANNING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
487	2-LANNING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
488	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
489	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
490	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
491	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
492	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
493	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
494	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
495	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
496	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
497	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
498	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
499	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
500	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
501	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
502	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 363.93	- -	-
503	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
504	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
505	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
506	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
507	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
508	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-
509	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
510	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
511	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
512	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
513	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
514	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	-
515	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
516	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
517	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
518	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
519	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
520	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
521	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
522	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
523	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
524	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
525	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
526	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	-
527	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
528	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
529	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
530	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
531	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
532	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 1,096.52	04/2018 -	-
533	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
534	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
535	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
536	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
537	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
538	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
539	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
540	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
541	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
542	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
543	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
544	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-
545	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
546	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
547	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
548	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-
549	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
550	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-
551	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-
552	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-
553	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
554	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	-
555	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-
556	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-
557	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-
558	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
559	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-
560	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
561	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
562	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	-
563	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 1,367.00	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
564	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
565	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
566	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
567	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
568	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-
569	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
570	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-
571	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	-
572	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
573	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
574	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
575	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
576	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
577	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
578	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
579	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
580	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
581	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 1,361.00	- 01/2019	-
582	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-
583	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
584	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
585	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
586	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
587	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
588	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
589	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
590	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
591	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
592	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT - SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	-
593	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
594	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	03/2020 -	-
595	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
596	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
597	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
598	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	-
599	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
600	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
601	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
602	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
603	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
604	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
605	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
606	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
607	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
608	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-
609	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
610	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
611	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
612	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
613	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
614	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
615	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
616	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
617	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
618	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
619	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
620	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
621	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
622	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
623	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
624	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
625	REHABILITATION AND UPGRADE OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
626	REHABILITATION SIX LANING UPGRADE CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
627	REHABILITATION AND UPGRADE OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
628	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
629	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
630	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
631	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
632	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E., VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
633	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
634	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
635	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-
636	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
637	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
638	UPGRADE TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-
639	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
640	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
641	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
642	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
643	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- 01/2019	-
644	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	-
645	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	-
646	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
647	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI, UTTAR PRADESH	02/2018	972.77 -	- -	-
648	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI, ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
649	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI, ANDHRA PRADESH	03/2018	557.30 -	- -	-
650	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-
651	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	- -	-
652	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
653	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
654	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
655	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
656	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-
657	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-
658	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
659	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-
660	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
661	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
662	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
663	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
664	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
665	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-
666	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
667	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
668	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
669	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
670	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
671	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
672	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
673	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
674	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
675	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
676	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
677	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
678	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
679	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
680	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
681	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
682	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
683	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-
684	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
685	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 -	-
686	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	-
687	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	-
688	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
689	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
	Total		3,68,575.91 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
690	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 18,380.00	12/2015 02/2019	02/2019
691	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	02/2021
	<u>Delhi Metro Rail Corporation</u>				
692	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
693	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
694	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
695	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019
	Total		69,629.79 -		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
696	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021
697	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021
698	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021
699	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021
700	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
701	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	-
702	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-
703	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-
<u>Delhi Jal Board</u>					
704	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021
705	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
<u>Hscl For Water</u>					
706	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL FOR WATER,BIHAR	10/2005	956.00 -	03/2015 -	-
<u>Kolkata Metropolitan Development Authority</u>					
707	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021
708	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	-
<u>Uttar Pradesh Jal Nigam</u>					
709	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
710	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021
711	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021
712	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021
713	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021
<u>Uttarakhand Pey Jal Nigam</u>					
714	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-
Total			7,307.68 -		
<u>COMMERCE</u>					

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Nbcc For Commerce</u>				
715	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 302.64	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Cpwd Of Higher Education</u>				
716	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND	09/2012	171.86 -	03/2016 -	-
717	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	-
718	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN	12/2016	549.31 -	07/2019 -	-
719	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD EDUCATION,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
720	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
721	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90 -	03/2020 -	-
722	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Rites Of Higher Education</u>				
723	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		2,709.79 -		
	<u>HOME AFFAIRS</u>				
	<u>Cpwd For Mha</u>				
724	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	01/2022 02/2022	01/2020
725	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD FOR MHA,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
	Total		313.57 -		
	<u>RURAL DEVELOPMENT</u>				
	<u>Cpwd For Rural</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
726	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD FOR RURAL,DELHI	11/2018	361.60 -	07/2021 -	-
	Total		361.60 -		
	<u>DPIIT</u>				
	<u>Dmic For Dpiit</u>				
727	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021
	Total		12,579.09 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
728	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	08/2021
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
729	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		5,94,109.45		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (October 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75				2/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	90.20	-	12/2022	7(R3)	17/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20	730.20	157.01	-	05/2023	0(R3)	13/17
	Total		818.00	960.00	247.21				30/43
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
4	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL, JAMMU AND KASHMIR	03/2019	4,287.59	4,287.59	597.82	-	08/2024	0(R3)	0/0
	Total		4,287.59	4,287.59	597.82				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
5	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	541.38	-	10/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	591.68	-	10/2021	-	0/0
7	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	176.66	-	11/2021	-	0/0
8	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	487.74	-	12/2021	-	0/0
	Total		1,992.56	2,026.34	1,797.46				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
9	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	1,033.07 3,020.95	3,630.00	3,630.96	- 03/2022	03/2022	0(R3)	0/0
10	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476] ECR, BIHAR	04/1991	329.39 803.11	1,483.14	1,218.49	- 03/2022	03/2022	0(R3)	0/0
11	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303] ECR, BIHAR	04/2003	528.65 2,066.78	2,066.78	1,590.10	- 03/2023	03/2023	0(R3)	0/0
12	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, JHARKHAND	04/2002	459.91 1,625.87	1,625.87	904.73	- 03/2023	03/2023	0(R3)	0/0
13	CHHAPRA-MUZAFFARPUR (NL) - [N22000172] ECR, BIHAR	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	-	0/0
14	ARARIA-SUPAUL (NL) - [N22000177] ECR, BIHAR	04/2008	1,605.17 -	1,605.17	147.56	- 03/2023	03/2023	0(R3)	0/0
15	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180] ECR, BIHAR	04/2004	372.14 1,470.50	1,470.50	1,436.01	- -	03/2023	-	0/0
16	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, BIHAR	04/1997	162.87 614.45	614.45	352.46	- -	12/2023	-	0/0
17	BIHTA-AURANGABAD (NL) - [N22000170] ECR, BIHAR	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	-	0/0
18	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176] ECR, BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
19	SAMASTIPUR-DARBANGHA - [N22000329] ECR, BIHAR	05/2015	380.00 -	519.33	309.90	- -	03/2025	-	0/0
	<u>Eastern Railways</u>								
20	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238] ER, MULTI STATE	04/2011	175.80 -	495.10	313.03	- -	03/2022	-	0/0
21	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302] ER, WEST BENGAL	04/2012	255.64 -	272.20	299.01	- -	03/2022	-	0/0
22	MONIGRAM- NIMTITA - [N22000301] ER, MULTI STATE	04/2012	250.93 -	310.70	383.74	- -	03/2024	-	0/0
23	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217] ER, MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
24	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218] ER, MULTI STATE	04/2010	172.03 -	260.10	11.77	- -	03/2025	-	0/0
25	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227] ER, MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
26	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234] ER, MULTI STATE	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
27	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235] ER, MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
28	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241] ER, MULTI STATE	04/2000	297.47 -	298.22	36.13	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
29	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	40.65	- -	03/2025	-	0/0
30	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
31	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North Central Railway</u>								
32	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	-	- 04/2010	12/2021	140(R3)	0/0
	<u>North East Frontier Railway</u>								
33	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	333.46	- 12/2021	03/2022	3(R3)	0/0
	<u>North Eastern Railway</u>								
34	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50 -	800.00	128.90	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
35	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	597.99	-	09/2023	-	0/0
36	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	419.00	160.79	- -	09/2023	-	0/0
37	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	359.00	116.87	- -	03/2024	-	0/0
38	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
39	UNCHAHAH-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	1,229.00 -	489.64	105.51	- -	03/2023	-	0/0
	<u>South Eastern Railway</u>								
40	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	41.78	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
41	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 -	2,161.36	82.47	- -	12/2023	-	0/0
42	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
43	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
44	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 -	367.77	-	- -	12/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
45	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	5,174.30	158.11	-	12/2024	-	0/0
46	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,404.03	1,087.98	-	12/2025	-	2/2
47	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	-	12/2025	-	0/0
	<u>Southern Railway</u>								
48	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	749.40	550.86	- 12/2021	01/2022	1(R3)	0/0
49	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	608.13	399.75	- 12/2021	02/2022	2(R3)	0/0
50	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,122.00	989.62	- 09/2021	12/2022	15(R3)	0/0
51	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,205.00	2.28	-	03/2024	-	0/0
52	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	1,431.90	492.74	-	03/2024	-	0/0
53	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 369.55	709.69	8.50	-	03/2025	-	0/0
54	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 275.21	448.10	6.73	-	03/2025	-	0/0
55	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 1,246.00	1,339.00	.82	-	03/2025	-	0/0
56	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	3,150.00	239.53	-	12/2025	-	0/0
57	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	227.40	65.02	-	03/2030	-	0/0
58	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.01	.63	-	03/2030	-	0/0
59	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.23	1.63	-	03/2030	-	0/0
	<u>Western Railway</u>								
60	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	254.99	- 03/2024	03/2024	0(R3)	0/0
61	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 393.62	393.62	152.98	- 12/2022	-	-	0/0
62	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 528.49	528.49	123.75	- 12/2022	-	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 154.15	154.15	103.45	- 12/2021	-	-	0/0
	Total		30,714.07 -	55,413.64	17,367.05				2/2
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
64	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	238.67	- 10/2021	10/2021	0(R3)	0/0
65	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	293.68	183.73	- 10/2021	10/2021	0(R3)	0/0
66	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	306.59	195.15	- -	11/2021	-	0/0
67	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	123.44	- -	12/2021	-	0/0
68	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	281.69	- 03/2021	03/2022	12(R3)	0/0
69	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 319.96	319.96	115.07	- -	03/2022	-	0/0
	National Highways And Infrastructure Development Corporation Ltd.								
70	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	210.50	145.76	- -	10/2021	-	4/4
71	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	520.01	199.64	- -	12/2021	-	3/4
72	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	11(R3)	3/4
73	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	200.44	125.91	- 08/2021	12/2021	4(R3)	3/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
74	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	1,049.51	155.61	- -	12/2021	-	2/4
75	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022	-3(R3)	2/4
76	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	568.92	310.07	- 11/2021	03/2022	4(R3)	0/0
77	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	188.78	104.07	- 03/2021	03/2022	12(R3)	3/4
78	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	90.86	- 04/2022	04/2022	0(R3)	3/4
79	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	76.96	- 04/2022	04/2022	0(R3)	2/4
80	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	215.66	- -	03/2023	-	1/4
National Highways Authority Of India									
81	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	799.07	- -	10/2021	-	2/4
82	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,314.63	- -	10/2021	-	0/0
83	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 866.55	866.55	864.82	- 10/2021	10/2021	0(R3)	0/0
84	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,378.36	- -	11/2021	-	0/0
85	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	205.00	- -	11/2021	-	0/0
86	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	1,296.00	-	- -	11/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	-	12/2021	-	0/0
88	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	2,169.00	-	-	12/2021	-	0/0
89	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	429.00	-	12/2021	-	1/3
90	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	-	01/2022	-	0/0
91	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	309.05	-	01/2022	-	0/0
92	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	224.45	-	01/2022	-	0/0
93	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	220.18	-	02/2022	-	0/0
94	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	827.00	-	02/2022	-	2/4
95	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	-	03/2022	-	0/0
96	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	281.06	-	03/2022	-	0/1
97	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-- [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	1,505.00	-	03/2022	-	0/0
98	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	282.63	-	03/2022	-	3/4
99	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	468.85	-	03/2022	-	0/0
100	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	382.61	-	03/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (October 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
101	CONSTRUCTION OF SIX LANE OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI, ANDHRA PRADESH	03/2018	314.43 -	314.43	85.61	- -	06/2022	-	0/0
102	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 827.05	827.05	387.83	- 07/2022	07/2022	0(R3)	0/0
103	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI, MADHYA PRADESH	12/2017	217.96 -	884.00	486.00	- -	10/2022	-	2/4
104	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI, MADHYA PRADESH	12/2017	656.98 -	840.00	297.00	- -	11/2022	-	2/4
105	FOUR LANNING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI, TAMIL NADU	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
106	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	720.00	206.32	- 10/2022	-	-	0/0
107	FOUR LANNING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	478.74	727.92	- 11/2021	-	-	0/0
	Total		31,844.18 -	32,793.46	18,027.04				38/64
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construction Corporation Ltd</u>								
108	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	2,694.00	896.32	- -	12/2022	-	0/9
	Total		2,694.00 -	2,694.00	896.32				0/9
	Grand Total		72,623.13	98,447.76	39,086.65				72/124

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	04/2020 -	06/2022	0/0
2	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63 -	08/2022 -	11/2022	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					
3	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	04/2018 -	10/2022	0/0
4	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	03/2017 -	10/2022	0/0
	<u>Eastern Coal Fields Limited</u>					
5	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
7	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>South-Eastern Coal Fields Limited</u>					
10	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
11	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL,MADHYA PRADESH	03/2021	496.28 -	03/2028 -	03/2028	0/0
12	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
13	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
14	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>Western Coal Fields Limited</u>					
15	DHUPTALA OC(SASTI UG TO OC) - [N06000209]WCL,MAHARASHTRA	02/2019	720.87 -	03/2028 -	03/2028	0/0
	<u>MINES</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Central Public Works Department</u>					
16	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N1000015]CPWD, WEST BENGAL	04/2019	255.37 -	04/2022 -	04/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
17	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL, CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
18	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
19	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	12/2021 -	03/2022	0/0
20	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
21	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	06/2022 -	09/2022	0/0
22	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL, KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
23	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL, MAHARASHTRA	08/2020	697.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
24	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	12/2021	0/0
	<u>Gas Authority Of India Limited</u>					
25	60 KTA POLYPROPYLENE PROJECT - [N16000429]GAIL, UTTAR PRADESH	03/2019	910.56 -	04/2024 -	04/2024	0/0
26	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]GAIL, MAHARASHTRA	05/2019	8,797.00 -	04/2025 -	04/2025	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
27	220 KV GRID SUPPLY - [N16000407]HPCL, ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	10/2021	0/0
28	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL, ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	03/2022	0/0
29	RUF PITCH LOADING GANTRY - [N16000406]HPCL, ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0
	<u>Indian Oil Corporation Limited</u>					
30	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021	0/0
31	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	01/2021 -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
32	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	09/2021	0/0
33	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 319.61	06/2020 12/2021	12/2021	0/0
34	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	12/2021	0/0
35	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 12/2021	12/2021	0/0
36	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	10/2021 -	12/2021	0/0
37	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 01/2022	01/2022	0/0
38	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 03/2022	03/2022	0/0
39	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	07/2021 03/2022	03/2022	0/0
40	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	07/2022	07/2022	0/0
41	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	01/2021 -	08/2022	0/0
42	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
43	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2022	0/0
44	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0
45	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	01/2023	0/0
46	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
47	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,199.60	12/2022 07/2023	07/2023	0/0
48	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
49	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
50	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	10/2023	0/0
51	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]IOCL,ASSAM	05/2021	412.00 -	10/2023 -	10/2023	0/0
52	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
53	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	02/2024	0/0
54	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT	09/2020	18,936.00 -	09/2024 -	08/2024	0/0
55	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]IOCL,HARYANA	02/2021	34,627.00 -	09/2024 -	09/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
56	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	02/2027 -	02/2027	0/0
57	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	08/2027 -	08/2027	0/0
58	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	08/2027 -	08/2027	0/0
59	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	02/2028 -	02/2028	0/0
60	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	02/2028 -	02/2028	0/0
61	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	02/2028 -	02/2028	0/0
62	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE	06/2019	303.00 -	02/2028 -	02/2028	0/0
63	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	12/2029 -	12/2029	0/0
64	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	12/2029 -	12/2029	0/0
65	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	12/2029 -	12/2029	0/0
66	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE	06/2019	169.00 -	12/2029 -	12/2029	0/0
67	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU	10/2018	2,998.00 -	03/2030 -	03/2030	0/0
68	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU	10/2018	1,304.00 -	03/2030 -	03/2030	0/0
69	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
<u>Numaligarh Refinery Limited</u>						
70	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]NRL,ASSAM	01/2019	12,366.00 18,968.00	10/2024 -	10/2024	0/0
71	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 9,058.00	10/2024 -	10/2024	0/0
<u>Oil India Limited</u>						
72	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 222.21	08/2020 09/2021	12/2021	0/0
<u>POWER</u>						
<u>Chenab Valley Power Projects [P] Limited</u>						
73	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	- 08/2024	08/2024	0/0
74	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 07/2025	07/2025	0/0
<u>National Hydro-Electric Power Corporation</u>						
75	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
76	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
77	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	04/2021 10/2021	10/2021	0/0
78	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	10/2021 01/2022	11/2021	0/0
79	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 11/2021	11/2021	0/0
80	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 2,311.89	12/2018 -	12/2021	0/0
81	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	06/2021 12/2021	12/2021	0/0
82	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	09/2021 10/2022	01/2022	0/0
83	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	11/2018 -	02/2022	0/0
84	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	09/2021 02/2022	02/2022	0/0
85	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	09/2021 02/2022	02/2022	0/0
86	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	09/2021 02/2022	02/2022	0/0
87	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	09/2021 02/2022	02/2022	0/0
88	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	03/2022 -	03/2022	0/0
89	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	07/2022 -	06/2022	0/0
90	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	07/2022 -	07/2022	0/0
91	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	07/2022 -	07/2022	0/0
92	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 07/2022	09/2022	0/0
93	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT	05/2021	674.92 -	09/2022 -	09/2022	0/0
94	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	09/2021 07/2022	01/2023	0/0
95	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
96	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
97	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
98	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	06/2021	0/0
99	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021	0/0
100	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	11/2019 07/2021	10/2021	0/0
101	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	02/2020 09/2021	10/2021	0/0
102	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 12/2017	12/2021	0/0
103	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	12/2021	0/0
104	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	06/2019 11/2021	12/2021	0/0
105	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	12/2019 09/2021	12/2021	0/0
106	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 219.66	07/2019 07/2021	12/2021	0/0
107	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	05/2020 08/2021	12/2021	0/0
108	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 09/2021	02/2022	0/0
109	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 12/2020	02/2022	0/0
110	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 6,700.00	12/2018 12/2021	03/2022	0/0
111	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL, MULTI STATE	12/2014	4,754.42 9,129.32	12/2018 03/2024	03/2024	0/0
<u>Satluj Jal Vidyut Nigam Limited</u>						
112	SHIYAL SOLAR POWER PROJECT - [N18000297]SJVN, GUJARAT	05/2021	296.20 -	10/2022 -	10/2022	0/0
113	PARASAN SOLAR POWER PROJECT - [N18000298]SJVN, UTTAR PRADESH	08/2021	313.58 -	12/2022 -	12/2022	0/0
114	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN, HIMACHAL PRADESH	10/2020	687.97 -	11/2025 -	11/2025	0/0
115	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN, HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
<u>HEAVY INDUSTRY</u>						
<u>Bharat Heavy Electricals Limited</u>						
116	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL, DELHI	08/2016	1,554.00 -	09/2019 -	-	0/0
<u>HEALTH AND FAMILY WELFARE</u>						
<u>Cpwd For Health</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
117	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
118	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
119	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
120	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					
121	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-	0/0
122	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-	0/0
123	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
124	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
125	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
126	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
127	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021	0/0
128	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
129	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021	0/0
130	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021	0/0
131	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	10/2021	0/0
132	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	10/2021	0/0
133	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	10/2021	0/0
134	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	11/2021	0/0
135	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	12/2021	0/0
136	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	03/2022	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
137	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [N220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
138	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
139	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0
140	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
141	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
142	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
143	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
144	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
145	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
146	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
147	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
148	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
149	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-	0/0
150	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-	0/0
<u>Container Corporation Of India</u>						
151	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-	0/0
152	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	-	0/0
153	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
154	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
155	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	-	0/0
156	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-	0/0
157	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-	0/0
158	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
159	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
160	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
	<u>East Central Railways</u>					
161	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021	0/0
162	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021	0/0
163	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	- 03/2022	03/2022	0/0
164	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2022	0/0
165	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	03/2022	0/0
166	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	- 03/2022	03/2022	0/0
167	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	03/2012 11/2022	11/2022	0/0
168	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- 03/2023	03/2023	0/0
169	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	- 03/2023	03/2023	0/0
170	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2023	0/0
171	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- 03/2023	03/2023	0/0
172	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2023	0/0
173	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	12/2023	0/0
174	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
175	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
176	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
177	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 03/2024	03/2024	0/0
178	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 03/2024	03/2024	0/0
179	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 03/2023	12/2024	0/0
180	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	03/2025	0/0
181	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
182	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
183	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
184	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0
185	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
186	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
187	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
188	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
189	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
190	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
191	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
<u>East Coast Railway</u>						
192	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 03/2022	03/2022	0/0
193	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	03/2020 -	03/2022	0/0
194	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
195	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
196	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 03/2024	03/2024	0/0
197	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
198	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0
199	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 03/2026	03/2026	0/0
200	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2026	0/0
201	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
<u>Eastern Railways</u>						
202	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
203	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
204	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0
205	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	03/2022	0/0
206	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
207	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
208	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
209	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
210	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
211	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
212	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
213	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR -CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
214	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
215	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
216	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
217	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
218	BARIPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
219	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
220	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
221	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
222	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
223	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
224	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
225	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
226	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
Indian Railway Construction Company Limited						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
227	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA <u>Kolkata Metro Rail Corporation Limited</u>	04/2016	5,200.00 -	03/2020 -	03/2025	0/0
228	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL <u>Metropolitan Rapid Transport Projects</u>	04/2010	2,397.72 -	03/2016 -	-	0/0
229	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	03/2004 06/2022	06/2022	0/0
230	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
231	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
232	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
233	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
234	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA <u>North Central Railway</u>	04/2012	714.10 -	04/2016 -	-	0/0
235	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- 04/2010	12/2021	0/0
236	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH <u>North East Frontier Railway</u>	03/2018	4,329.53 -	03/2023 -	06/2025	0/0
237	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	10/2021	0/0
238	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	11/2021	0/0
239	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- 12/2021	03/2022	0/0
240	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2022	0/0
241	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2023	0/0
242	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
243	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
244	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 4,084.69	12/2015 12/2023	12/2023	0/0
245	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 2,042.51	03/2019 -	12/2023	0/0
246	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0
247	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
248	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	03/2026	0/0
249	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-	0/0
250	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
251	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
252	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-	0/0
253	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
254	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
255	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
256	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-	0/0
257	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
<u>North Eastern Railway</u>						
258	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
259	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
260	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
261	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
262	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
263	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
264	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
265	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
266	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
267	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
268	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0
269	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
270	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
271	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
272	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
	<u>North Western Railway</u>					
273	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	09/2021	0/0
274	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022	0/0
275	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	10/2022	0/0
276	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	11/2022	0/0
277	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
278	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
279	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021	0/0
280	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	12/2022	0/0
281	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
282	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	09/2023	0/0
283	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
284	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
285	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
286	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,017.96	07/2012 -	11/2024	0/0
287	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
288	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 781.00	03/2016 -	-	0/0
289	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
	<u>National High Speed Rail Corporation Limited</u>					
290	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 -	12/2023	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
291	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
292	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	12/2021	0/0
293	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2021	0/0
294	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	12/2021	0/0
295	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	12/2021	0/0
296	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	12/2021	0/0
297	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2021	0/0
298	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
299	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
300	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	06/2022	0/0
301	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	06/2022	0/0
302	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
303	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
304	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2022	0/0
305	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
306	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
307	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76 -	12/2023 -	12/2023	0/0
308	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
309	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
310	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
311	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
312	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
313	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
314	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
315	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
316	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
317	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2026	0/0
	<u>Railway Electrification</u>					
318	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Central Railway</u>					
319	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 176.18	03/2022 03/2022	03/2022	0/0
320	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
321	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2024	0/0
322	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
323	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
324	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2024	0/0
325	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
326	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
327	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
	<u>South East Central Railway</u>					
328	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	12/2021 12/2023	12/2023	0/0
	<u>South Eastern Railway</u>					
329	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2022	0/0
330	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2023	0/0
331	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
332	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
333	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	03/2030	0/0
334	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
335	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
	<u>South Western Railway</u>					
336	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
337	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
338	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
339	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
340	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
341	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
342	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
343	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
344	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	03/2019 -	03/2024	0/0
345	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
346	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	03/2017 -	03/2025	0/0
347	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
348	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2025	0/0
	<u>Southern Railway</u>					
349	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021	0/0
350	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- 12/2021	01/2022	0/0
351	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 12/2021	02/2022	0/0
352	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 09/2021	12/2022	0/0
353	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	03/2024	0/0
354	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	03/2024	0/0
355	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0
356	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
357	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 369.55	- -	03/2025	0/0
358	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 275.21	- -	03/2025	0/0
359	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 1,246.00	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
360	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
361	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
362	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
363	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	03/2030	0/0
364	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	03/2030	0/0
365	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	03/2030	0/0
366	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	03/2030	0/0
367	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-	0/0
368	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
	<u>Western Railway</u>					
369	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,125.53	03/2021 12/2022	12/2022	0/0
370	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 12/2022	12/2022	0/0
371	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	03/2022 03/2023	03/2023	0/0
372	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,524.68	03/2022 03/2023	03/2023	0/0
373	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.96	03/2019 03/2023	03/2023	0/0
374	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0
375	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 -	03/2020 -	03/2023	0/0
376	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 10/2023	10/2023	0/0
377	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,246.59	03/2020 03/2024	03/2024	0/0
378	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2024	03/2024	0/0
379	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	03/2022 -	03/2024	0/0
380	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31 -	03/2024 -	03/2024	0/0
381	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	03/2022 03/2025	03/2025	0/0
382	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 311.36	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
383	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 393.62	- 12/2022	-	0/0
384	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 528.49	- 12/2022	-	0/0
385	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 154.15	- 12/2021	-	0/0
	ROAD TRANSPORT AND HIGHWAYS					
	Ministry Of Road Transport And Highways (State Pwds)					
386	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	09/2021	0/0
387	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	10/2021	0/0
388	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 & KM 158.419 TO KM 173.300) PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	10/2021	0/0
389	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019	0/0
390	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020	0/0
391	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
392	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020	0/0
393	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2020	12/2020	0/0
394	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021	0/0
395	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021	0/0
396	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021	0/0
397	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 03/2020	03/2021	0/0
398	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021	0/0
399	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	04/2021	0/0
400	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021	0/0
401	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 06/2021	06/2021	0/0
402	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021	0/0
403	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
404	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021	0/0
405	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021	0/0
406	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021	0/0
407	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021	0/0
408	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021	0/0
409	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021	0/0
410	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021	0/0
411	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 10/2021	10/2021	0/0
412	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- 10/2021	10/2021	0/0
413	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 237.80	11/2019 10/2021	10/2021	0/0
414	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2021	10/2021	0/0
415	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 06/2021	11/2021	0/0
416	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 08/2021	11/2021	0/0
417	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 11/2021	11/2021	0/0
418	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021	0/0
419	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	01/2021 -	11/2021	0/0
420	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	11/2021	0/0
421	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	11/2021	0/0
422	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 11/2021	11/2021	0/0
423	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDA-SAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021	0/0
424	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 12/2021	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
425	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 12/2021	12/2021	0/0
426	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 12/2021	12/2021	0/0
427	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 10/2021	12/2021	0/0
428	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 174.90	08/2018 08/2021	12/2021	0/0
429	R AND U OF KHUTAR - LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	12/2021	0/0
430	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 09/2021	12/2021	0/0
431	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 06/2021	12/2021	0/0
432	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 09/2021	12/2021	0/0
433	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 10/2021	12/2021	0/0
434	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 08/2021	12/2021	0/0
435	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 06/2021	12/2021	0/0
436	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	12/2021	0/0
437	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 04/2021	12/2021	0/0
438	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 12/2021	12/2021	0/0
439	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	12/2021	0/0
440	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2021	12/2021	0/0
441	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	12/2021	0/0
442	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 12/2021	12/2021	0/0
443	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	09/2016 12/2021	12/2021	0/0
444	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 12/2021	12/2021	0/0
445	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 12/2021	12/2021	0/0
446	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 12/2021	12/2021	0/0
447	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 01/2022	01/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
448	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	02/2022	0/0
449	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	03/2022	0/0
450	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL	03/2016	271.17 291.20	11/2018 01/2021	03/2022	0/0
451	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2022	03/2022	0/0
452	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 11/2021	03/2022	0/0
453	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	03/2022	0/0
454	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 319.96	- -	03/2022	0/0
455	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 03/2022	03/2022	0/0
456	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 319.96	03/2016 04/2022	04/2022	0/0
457	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 04/2021	04/2022	0/0
458	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 05/2022	05/2022	0/0
459	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 09/2021	06/2022	0/0
460	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	08/2016 06/2022	06/2022	0/0
461	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	08/2019 08/2022	08/2022	0/0
462	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
463	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	12/2022	0/0
464	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
465	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	07/2016 12/2022	12/2022	0/0
466	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
467	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373]MoRTH,ARUNACHAL PRADESH	01/2020	358.26 -	02/2024 -	02/2024	0/0
468	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]MoRTH,ARUNACHAL PRADESH	02/2021	588.09 -	03/2024 -	03/2024	0/0
469	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]MoRTH,ASSAM	02/2021	925.47 -	07/2025 -	07/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
470	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
471	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
472	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 12/2021	-	0/0
473	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
474	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
475	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-	0/0
476	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-	0/0
477	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-	0/0
478	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
479	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
480	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0
481	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
482	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-	0/0
483	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-	0/0
484	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
485	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
486	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-	0/0
487	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
488	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
489	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
490	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
491	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
492	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
493	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-	0/0
494	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-	0/0
495	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	-	0/0
496	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
497	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
498	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
499	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
500	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
501	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
502	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
503	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
504	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
505	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
506	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
507	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
508	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
509	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
510	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
511	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
512	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
513	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
514	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
515	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
516	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
517	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
518	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
519	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
520	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
521	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
522	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
523	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0
524	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
525	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
526	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
527	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
528	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
529	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
530	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
531	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
532	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-	0/0
533	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
534	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
535	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
536	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0
537	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
538	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
539	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
540	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
541	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
542	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
543	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
544	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
545	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
546	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
547	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
548	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
549	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
550	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
551	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
552	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
553	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
554	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
555	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
556	WIDENING TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
557	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
558	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
559	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-	0/0
560	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	-	0/0
561	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	-	0/0
562	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-	0/0
563	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 08/2021	-	0/0
564	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
565	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-	0/0
566	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-	0/0
567	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-	0/0
568	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-	0/0
569	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-	0/0
570	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-	0/0
571	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-	0/0
572	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-	0/0
573	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-	0/0
574	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-	0/0
575	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-	0/0
576	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-	0/0
577	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	-	0/0
578	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	-	0/0
579	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-	0/0
580	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-	0/0
581	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-	0/0
582	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-	0/0
583	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	-	0/0
584	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-	0/0
585	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 12/2021	-	0/0
586	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
National Highways And Infrastructure Development Corporation Ltd.						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
587	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- 11/2021	03/2022	0/0
588	IMPHAL – MOREH (PACKAGE 4) - [N24001399]NHIDCL,MANIPUR	03/2021	277.99 -	01/2023 -	01/2023	0/0
589	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR	07/2021	512.43 -	02/2023 -	02/2023	0/0
590	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR	07/2021	497.09 -	02/2023 -	02/2023	0/0
591	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR	02/2021	431.28 -	03/2023 -	03/2023	0/0
592	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR	07/2021	204.58 -	03/2023 -	03/2023	0/0
593	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR	07/2021	467.00 -	03/2023 -	03/2023	0/0
594	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR	07/2021	185.80 -	03/2023 -	03/2023	0/0
595	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL,MANIPUR	07/2021	483.87 -	03/2023 -	03/2023	0/0
596	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL,MANIPUR	07/2021	198.77 -	03/2023 -	03/2023	0/0
597	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL,NAGALAND	07/2021	258.52 -	03/2023 -	03/2023	0/0
598	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL,NAGALAND	02/2021	207.33 -	03/2023 -	03/2023	0/0
599	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR	07/2021	859.67 -	08/2023 -	08/2023	0/0
600	CHURACHANPUR TUIVAI PKG-3 - [N24001405]NHIDCL,MANIPUR	07/2021	673.27 -	10/2023 -	10/2023	0/0
National Highways Authority Of India						
601	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- 02/2018	02/2018	0/0
602	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- 02/2018	02/2018	0/0
603	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018	0/0
604	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019	0/0
605	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
606	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020	0/0
607	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
608	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020	0/0
609	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
610	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020	0/0
611	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
612	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
613	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
614	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020	0/0
615	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
616	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021	0/0
617	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
618	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	04/2021	0/0
619	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
620	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
621	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
622	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
623	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021	0/0
624	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021	0/0
625	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 1,201.51	- 06/2021	09/2021	0/0
626	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
627	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.24	- 05/2021	09/2021	0/0
628	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
629	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	10/2021	0/0
630	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 10/2021	10/2021	0/0
631	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
632	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 866.55	- 10/2021	10/2021	0/0
633	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
634	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	11/2021	0/0
635	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	11/2021	0/0
636	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	12/2021	0/0
637	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2021	0/0
638	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	12/2021	0/0
639	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	12/2021	0/0
640	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2021	0/0
641	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	12/2021	0/0
642	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
643	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF NH - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	12/2021	0/0
644	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021	0/0
645	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	01/2022	0/0
646	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	01/2022	0/0
647	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	01/2022	0/0
648	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	01/2022	0/0
649	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	01/2022	0/0
650	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	02/2022	0/0
651	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 02/2022	02/2022	0/0
652	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
653	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	02/2022	0/0
654	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2022	0/0
655	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 03/2022	03/2022	0/0
656	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2022	0/0
657	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
658	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	03/2022	0/0
659	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	03/2022	0/0
660	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	03/2022	0/0
661	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	03/2022	0/0
662	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	06/2022	0/0
663	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2022	0/0
664	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 827.05	- 07/2022	07/2022	0/0
665	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0
666	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
667	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	09/2022	0/0
668	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 10/2022	10/2022	0/0
669	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
670	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 01/2021	12/2022	0/0
671	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	12/2022	0/0
672	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 720.81	03/2023 -	03/2023	0/0
673	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	05/2023	0/0
674	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRA ROAD (SH-1 - [N24001414]NHAI,PUNJAB	12/2020	733.00 -	01/2024 -	01/2024	0/0
675	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	01/2024 -	01/2024	0/0
676	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB	12/2020	881.00 -	04/2024 -	04/2024	0/0
677	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB	12/2020	1,234.40 -	04/2024 -	04/2024	0/0
678	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB	12/2020	1,094.46 -	04/2024 -	04/2024	0/0
679	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB	02/2021	1,269.96 -	04/2024 -	04/2024	0/0
680	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420]NHAI,PUNJAB	02/2021	853.66 -	04/2024 -	04/2024	0/0
681	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
682	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
683	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
684	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
685	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
686	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
687	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-	0/0
688	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
689	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
690	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
691	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
692	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
693	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
694	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
695	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
696	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
697	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
698	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
699	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
700	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
701	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
702	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
703	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
704	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
705	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
706	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
707	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
708	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
709	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
710	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
711	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
712	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
713	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
714	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
715	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-	0/0
716	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 363.93	- -	-	0/0
717	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	-	0/0
718	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-	0/0
719	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
720	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
721	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
722	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-	0/0
723	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
724	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
725	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-	0/0
726	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-	0/0
727	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
728	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	-	0/0
729	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
730	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
731	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
732	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
733	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
734	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
735	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
736	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
737	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
738	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
739	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
740	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	-	0/0
741	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
742	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
743	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
744	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
745	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 1,096.52	04/2018 -	-	0/0
746	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
747	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
748	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
749	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
750	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
751	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
752	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
753	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
754	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
755	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
756	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-	0/0
757	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- 10/2022	-	0/0
758	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
759	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
760	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
761	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
762	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
763	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
764	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
765	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
766	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
767	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
768	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
769	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	-	0/0
770	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
771	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
772	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
773	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-	0/0
774	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
775	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-	0/0
776	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
777	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
778	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	03/2019 -	-	0/0
779	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHATTI - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	-	0/0
780	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
781	REHABILITATION AND UPGRADE TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-	0/0
782	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
783	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
784	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
785	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-	0/0
786	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
787	4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0
788	4-LANNING OF WARANGA-MAHAGAON SECTION (KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
789	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0
790	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
791	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
792	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
793	REHABILITATION AND UPGRADE BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	03/2020 -	-	0/0
794	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
795	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
796	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS (KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
797	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
798	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
799	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI, RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
800	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
801	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI, TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
802	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
803	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
804	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-	0/0
805	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
806	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
807	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
808	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
809	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
810	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
811	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
812	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
813	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
814	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
815	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
816	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
817	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
818	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
819	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
820	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
821	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
822	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
823	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
824	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
825	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
826	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
827	SIX LANING OF MIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
828	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-	0/0
829	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
830	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
831	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-	0/0
832	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
833	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
834	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM.50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
835	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
836	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
837	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
838	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
839	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
840	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
841	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
842	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
843	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-	0/0
844	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
845	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
846	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
847	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
848	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
849	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0
850	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
851	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
852	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
853	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-	0/0
854	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
855	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
856	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
857	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-	0/0
858	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019	-	0/0
859	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-	0/0
860	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
861	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
862	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
863	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-	0/0
864	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-	0/0
865	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-	0/0
866	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
867	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-	0/0
868	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-	0/0
869	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-	0/0
870	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-	0/0
871	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-	0/0
872	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
873	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-	0/0
874	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-	0/0
875	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 -	-	0/0
876	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	-	0/0
877	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	-	0/0
878	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
879	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-	0/0
880	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- 11/2021	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
881	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	06/2021 11/2021	11/2021	0/0
	<u>Department Of Telecommunication</u>					
882	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	07/2015 05/2020	03/2022	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
883	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 422.00	03/2021 06/2023	06/2023	0/0
884	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	03/2022 -	06/2023	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
885	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
886	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
887	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	03/2025	0/0
888	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	05/2025	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					
889	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11/2021 12/2022	12/2022	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
890	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA <u>Madhya Pradesh Metro Rail Co Limited</u>	07/2013	23,136.00 -	03/2020 03/2023	03/2023	0/0
891	BHOPAL METRO RAIL - [N28000124]MPMRCL, MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
892	INDORE METRO RAIL - [N28000125]MPMRCL, MADHYA PRADESH <u>Nagpur Metro Rail Corporation Ltd</u>	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
893	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA <u>Patna Metro Rail Corporation</u>	08/2014	8,680.00 -	03/2018 12/2021	12/2021	0/0
894	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
895	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB, MAHARASHTRA <u>Bihar Urban Infrastructure Development Corporation Ltd</u>	03/2017	233.57 -	12/2019 -	12/2021	0/0
896	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77 -	03/2020 -	03/2021	0/0
897	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
898	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
899	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
900	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO, BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
901	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19 -	08/2021 -	12/2021	0/0
902	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0
903	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO, BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
904	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 -	09/2020 -	-	0/0
905	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15 -	12/2020 06/2021	-	0/0
906	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63 -	01/2021 -	-	0/0
907	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62 -	11/2020 03/2021	-	0/0
	<u>Delhi Jal Board</u>					
908	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB, DELHI	12/2018	515.07 -	01/2021 -	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
909	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
910	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
911	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
912	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-	0/0
	<u>Kolkata Metropolitan Development Authority</u>					
913	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021	0/0
914	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0
915	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
916	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
917	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
918	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
919	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
920	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	02/2022 -	06/2022	0/0
921	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
922	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
923	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	02/2022 -	10/2022	0/0
924	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	-	0/0
	<u>Uttar Pradesh Jal Nigam</u>					
925	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021	0/0
926	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021	0/0
927	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
928	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
929	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
930	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
931	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
932	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 261.12	03/2022 -	03/2022	0/0
933	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
934	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	07/2021 -	06/2022	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
935	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-	0/0
	<u>COMMERCE</u>					
	<u>Nbcc For Commerce</u>					
936	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 302.64	10/2020 -	-	0/0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
	<u>Cpwd Of Higher Education</u>					
937	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD EDUCATION,UTTAR PRADESH	11/2017	171.72 135.00	03/2020 12/2021	12/2021	0/0
938	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 -	06/2022	0/0
939	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	07/2022 -	10/2022	0/0
940	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	07/2022 -	10/2022	0/0
941	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	09/2020 -	11/2022	0/0
942	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	09/2022 -	01/2023	0/0
943	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD EDUCATION,JAMMU AND KASHMIR	01/2018	676.00 748.19	04/2023 -	04/2023	0/0
944	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	06/2020 -	-	0/0
	<u>Rites Of Higher Education</u>					
945	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 -	09/2014 -	-	0/0
	<u>HOME AFFAIRS</u>					
	<u>Cpwd For Mha</u>					
946	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	01/2022 02/2022	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
947	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35 290.33	07/2022 10/2022	10/2022	0/0
948	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE - - [N28000147]CPWD FOR MHA,HARYANA	01/2020	166.98 167.00	10/2023 -	10/2023	0/0
949	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD FOR MHA,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0
	<u>DPIIT</u>					
	<u>Dmic For Dpiit</u>					
950	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0
	<u>Iicc For Dpiit</u>					
951	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	12/2019 05/2022	05/2022	0/0
	<u>RENEWABLE ENERGY</u>					
	<u>Cpwd For Renewable Energy</u>					
952	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-	0/0
	Total		11,70,529.48 -			0/0
	Grand Total		11,70,529.48			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA [N04000080]	1/2016	458.00	458.00	157.18	03/2020 06/2022	04/2022
	Total		458.00	458.00	157.18		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	201.80	09/2025	05/2024
	Total		1,828.00	1,828.00	201.80		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
3	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00	3,072.00	2,574.63	06/2021 08/2022	07/2022
	<u>Indian Oil Corporation Limited</u>						
4	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00	1,398.00	116.76	12/2023	10/2023
5	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00	18,936.00	796.97	09/2024	08/2024
	Total		23,011.00	23,406.00	3,488.36		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
6	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80	261.80	87.43	10/2021 01/2022	11/2021
7	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71	1,522.71	996.32	09/2021 10/2022	01/2022
8	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]	1/2021	842.27	842.27	92.08	07/2022	06/2022
	<u>Power Grid Corporation Of India Limited</u>						
9	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 14,719.10	14,719.10	12,979.18	08/2013 11/2022	08/2022
	Total		13,756.97	17,345.88	14,155.01		

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
10	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,721.84	03/2024	03/2023
	<u>North East Frontier Railway</u>						
11	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27	1,167.00	1,028.89	12/2021	10/2021
	<u>Rail Vikas Nigam Ltd.</u>						
12	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	1,809.22	12/2026	12/2025
13	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	2,400.15	03/2023	12/2022
14	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	0.19	12/2025	03/2025
	Total		10,047.51	15,271.67	6,960.29		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
15	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]	1/2017	396.86	396.86	271.47	09/2019 11/2021	10/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
16	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82	537.82	129.40	09/2019 06/2023	04/2023
17	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]	3/2017	1,718.59	1,718.59	519.92	- 06/2022	03/2022
	Total		2,653.27	2,653.27	920.79		
	Grand Total		51,754.75	60,962.82	25,883.43		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	6,054.37	09/2010 10/2022	10/2022
	Total		3,492.00 -	6,840.00	6,054.37		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	476.54	09/2018 06/2022	06/2022
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	199.30	11/2021 01/2023	01/2023
4	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT [N04000091]	4/2020	611.80 -	611.80	52.08	03/2023 -	03/2023
5	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]	6/2019	380.87 -	380.87	15.41	03/2022 12/2023	12/2023
6	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD [N04000086]	5/2020	353.61 -	353.61	81.41	05/2022 -	05/2022
	Total		2,153.22 -	2,443.72	824.74		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
7	MAGADH EXPANSION OC(51 MTY) - [N06000015]	8/2008	6,964.33 6,964.33	7,254.37	729.50	07/2012 03/2028	03/2028
8	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	37.16	03/2023 -	03/2023
9	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	778.80	349.76	03/2023 -	03/2023
10	RECAST EPR AMRAPALI OC - [N06000103]	2/2012	4,983.58 4,983.58	4,983.58	360.01	03/2020 03/2028	03/2028
	<u>Eastern Coal Fields Limited</u>						
11	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]	11/2015	1,210.12 -	1,210.12	49.04	03/2022 03/2029	03/2029
12	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	159.28	03/2024 -	03/2024
13	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	6.82	03/2025 -	03/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	.19	03/2027 -	03/2027
15	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	2.70	03/2027 -	03/2027
16	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	18.15	03/2029 -	03/2029
17	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.75	03/2026 -	03/2026
18	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	257.70	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
19	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,558.11	03/2026 -	03/2026
20	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]	12/2007	8,416.19 8,416.19	8,416.19	941.90	03/2013 03/2028	03/2028
21	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]	12/2007	3,504.21 3,504.21	3,504.21	589.86	03/2010 03/2029	03/2029
22	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,282.18	03/2029 -	03/2029
23	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	598.36	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
24	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	496.17	06/2015 03/2025	03/2025
25	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	12,656.73	11/2021 11/2022	11/2022
	<u>Northern Coal Fields Limited</u>						
26	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
27	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
28	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
29	NIGAHI EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
30	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
	<u>Singareni Colliers Company Limited</u>						
31	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	80.04	03/2023 -	03/2023
32	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	76.43	03/2024 -	03/2024
33	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	25.43	03/2023 -	03/2023
	<u>South-Eastern Coal Fields Limited</u>						
34	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
36	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	2,025.60	03/2029 -	03/2029
37	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
38	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	185.35	03/2024 -	03/2024
39	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	314.88	03/2029 -	03/2029
40	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	160.43	03/2022 -	03/2022
41	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	40.57	03/2026 -	03/2026
42	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
43	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	76.12	03/2026 -	03/2026
44	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.65	03/2021 04/2024	04/2024
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,118.22	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
46	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]	11/2015	313.34 -	313.34	149.32	03/2021 03/2024	03/2024
47	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]	11/2015	851.60 -	826.80	233.76	03/2020 03/2026	03/2026
48	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	9.86	03/2028 -	03/2028
49	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
50	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
51	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	296.56	03/2021 09/2023	09/2023
52	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	289.29 -	289.30	36.10	03/2022 03/2025	03/2025
53	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	246.02	03/2022 -	03/2022
54	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	7/2016	281.25 -	281.25	18.24	03/2022 03/2026	03/2026
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	390.11	03/2025 -	03/2025
56	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	299.67	164.36	03/2019 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.90	03/2023 -	03/2023
58	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]	11/2014	1,184.33 -	1,184.33	392.88	03/2020 03/2027	03/2027
59	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	1.00	03/2026 -	03/2026
60	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	103.38	03/2021 09/2022	09/2022
61	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	217.47	03/2021 09/2022	09/2022
62	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
63	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	402.90	336.00	03/2020 09/2022	09/2022
	Total		94,883.84 -	93,994.98	30,162.69		
	DEPARTMENT OF HIGHER EDUCATION						
	<u>Cpwd Of Higher Education</u>						
64	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]	11/2012	270.83 -	244.00	241.67	11/2014 11/2021	11/2021
65	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	213.47	04/2023 -	04/2023
66	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	110.13	03/2020 12/2021	12/2021
67	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	57.47	06/2022 -	06/2022
	Total		1,511.06 -	1,484.23	622.74		
	<u>DPIIT</u>						
	<u>Iicc For Dpiit</u>						
68	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,013.69	12/2019 05/2022	05/2022
	Total		4,773.00 -	5,178.00	3,013.69		
	FERTILISERS						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
69	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	314.91	04/2020 10/2021	10/2021
	Total		426.72 -	426.72	314.91		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FINANCE</u>						
	<u>Cpwd For Finance</u>						
70	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	189.00	11/2021 -	11/2021
	Total		348.77 -	348.77	189.00		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
71	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	333.02	09/2023 -	09/2023
72	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	Total		2,981.00 -	3,232.00	333.02		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
73	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	172.13	04/2018 12/2021	12/2021
74	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
75	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]	6/2019	277.35 -	290.33	27.25	07/2022 10/2022	10/2022
	Total		607.21 -	695.31	199.38		
	<u>MINES</u>						
	<u>Central Public Works Department</u>						
76	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]	4/2019	255.37 -	255.37	.86	04/2022 -	04/2022
	<u>National Aluminum Company Limited (Nalco)</u>						
77	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	988.67	04/2021 01/2024	01/2024
78	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	6.91	04/2021 12/2023	12/2023
	Total		6,278.37 -	6,278.37	996.44		
	<u>PETROLEUM</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Bharat Petroleum Corporation Limited</u>						
79	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 08/2022	08/2022
80	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	256.43	03/2023 -	03/2023
81	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	998.48	12/2021 -	12/2021
82	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023
	<u>Gas Authority Of India Limited</u>						
83	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,484.70	12/2020 12/2021	12/2021
84	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	246.25	04/2022 -	04/2022
85	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	151.09	07/2022 -	07/2022
86	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,773.40	12/2012 02/2022	02/2022
87	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	91.81	07/2022 -	07/2022
88	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	105.20	10/2022 -	10/2022
89	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	228.35	04/2025 -	04/2025
90	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	910.56	105.31	04/2024 -	04/2024
91	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,616.30	05/2023 -	05/2023
92	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	337.20	11/2022 -	11/2022
93	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	402.90	07/2022 -	07/2022
94	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,496.20	12/2021 -	12/2021
95	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	133.18	10/2022 -	10/2022
96	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	181.07	10/2022 -	10/2022
97	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	2,166.20	12/2020 12/2021	12/2021
98	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	939.30	12/2020 12/2021	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	2,129.90	12/2020 12/2021	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
100	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	26,264.00	16,536.13	07/2020 07/2022	07/2022
101	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	13.22	03/2024 -	03/2024
102	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	28.57	11/2022 -	11/2022
103	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB [N16000402]	5/2020	1,421.46 -	1,421.46	171.55	02/2023 -	02/2023
104	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	136.39	03/2031 08/2031	08/2031
105	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	369.06	03/2029 08/2029	08/2029
106	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	155.75	09/2026 02/2027	02/2027
107	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	368.60	11/2022 -	11/2022
108	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE [N16000369]	12/2018	854.00 -	854.00	179.41	12/2022 -	12/2022
109	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,334.00	06/2022 -	06/2022
	<u>Indian Oil Corporation Limited</u>						
110	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	3,338.00	3,071.72	12/2020 03/2022	03/2022
111	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,566.92	02/2022 -	02/2022
112	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU [N16000305]	12/2017	466.43 -	466.43	258.36	10/2020 01/2022	01/2022
113	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	340.76	145.36	02/2020 07/2022	07/2022
114	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	319.61	219.15	06/2020 12/2021	12/2021
115	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	6,025.00	4,049.27	12/2018 02/2022	02/2022
116	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	109.97	08/2020 03/2022	03/2022
117	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	2,292.73	09/2022 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	419.33	02/2020 02/2022	02/2022
119	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	466.82	01/2021 03/2022	03/2022
120	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	130.90	10/2021 03/2022	03/2022
121	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	376.88	03/2021 12/2021	12/2021
122	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	924.60	08/2020 04/2022	04/2022
123	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	3,485.97	10/2021 07/2022	07/2022
124	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	157.01	- 05/2023	05/2023
125	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	490.71	08/2022	08/2022
126	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	373.13	01/2024 -	01/2024
127	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	28.71	07/2022 -	07/2022
128	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	103.42	01/2023 -	01/2023
129	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	1,620.50	04/2023 -	04/2023
130	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	16.46	07/2021 03/2022	03/2022
131	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	552.22	05/2023 -	05/2023
132	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	553.94	12/2022 07/2023	07/2023
133	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	427.00	28.69	09/2022 03/2023	03/2023
134	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	100.38	06/2021 07/2022	07/2022
135	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	62.90	02/2027 -	02/2027
136	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]	10/2018	613.00 -	613.00	157.77	12/2029 -	12/2029

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
137	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]	10/2018	176.00 -	176.00	77.52	08/2027 -	08/2027
138	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	25.15	10/2023 -	10/2023
139	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	466.97	09/2024 -	09/2024
140	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	1.12	08/2023 -	08/2023
141	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	166.08	12/2022 -	12/2022
142	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	94.90	08/2022 -	08/2022
143	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	2,039.85	08/2021 09/2022	09/2022
144	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	118.98	02/2028 -	02/2028
145	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	37.29	12/2029 -	12/2029
146	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	283.56	02/2028 -	02/2028
147	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	94.78	02/2028 -	02/2028
148	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	24.46	12/2029 -	12/2029
149	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	119.54	02/2028 -	02/2028
150	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	41.60	12/2029 -	12/2029
151	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]	6/2019	2,880.00 -	2,880.00	104.89	08/2027 -	08/2027
152	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	39.09	03/2030 -	03/2030
153	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	191.16	03/2030 -	03/2030
154	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	107.63	09/2021 06/2022	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	72.98	10/2020 08/2022	08/2022
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
156	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	304.00	2.56	06/2023 01/2024	01/2024
	<u>Numaligarh Refinery Limited</u>						
157	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY [N16000379]	1/2019	12,366.00 -	18,968.00	648.35	10/2024 -	10/2024
158	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	526.70	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
159	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	2,001.34	1,599.60	05/2013 05/2022	05/2022
160	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	947.93	03/2026 -	03/2026
161	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	730.57	03/2023 03/2022	03/2022
162	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	217.38	03/2025 -	03/2025
163	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	115.83	08/2022 -	08/2022
164	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) [N16000371]	10/2018	156.67 -	156.67	62.93	03/2021 05/2022	05/2022
165	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	791.49	12/2020 12/2021	12/2021
166	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	1,463.48	03/2022 05/2023	05/2023
167	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,694.11	03/2022 -	03/2022
168	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	3,032.38	05/2021 01/2022	01/2022
169	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	2,121.13	05/2021 12/2021	12/2021
170	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	25,090.00	14,210.03	06/2020 06/2022	06/2022
171	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,375.90	2,884.63	04/2018 05/2022	05/2022
	Total		2,84,540.44 -	2,94,659.30	94,501.16		
	<u>POWER</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Chenab Valley Power Projects [P] Limited</u>						
172	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	2,083.10	04/2020 07/2025	07/2025
173	KIRU HYDRO ELECTRIC PROJECT - [N18000278]	3/2019	4,287.59 -	4,287.59	597.82	- 08/2024	08/2024
	<u>National Hydro-Electric Power Corporation</u>						
174	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,897.59	9,279.64	09/2009 03/2023	03/2023
175	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,992.43	14,458.38	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
176	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.54	721.34	09/2019 12/2024	12/2024
177	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	501.29	342.98	09/2021 02/2022	02/2022
178	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	19,311.93	10/2011 07/2023	07/2023
179	DEVIKOT SOLAR 150MW - [N18000281]	1/2020	798.24 -	798.24	415.99	09/2021 02/2022	02/2022
180	JETSAR SOLAR 160 MW - [N18000287]	12/2019	702.28 -	702.28	539.41	03/2021 11/2021	11/2021
181	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	1,277.87	09/2021 02/2022	02/2022
182	ANTA SOLAR 90 MW - [N18000292]	1/2021	382.22 -	382.22	-	03/2022 -	03/2022
183	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]	5/2021	674.92 -	674.92	76.00	09/2022 -	09/2022
184	CHHATTARGARH 150 MW - [N18000294]	2/2021	599.99 -	559.98	60.85	07/2022 -	07/2022
185	BHENSARA 320 MW - [N18000293]	1/2021	1,221.73 -	1,221.73	137.36	07/2022 -	07/2022
186	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	687.97	09/2021 02/2022	02/2022
187	KAYAMKULAM SOLAR 70 MW - [N18000288]	9/2019	403.62 -	403.62	116.32	06/2021 12/2021	12/2021
188	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	180.67	04/2021 10/2021	10/2021
	<u>Power Grid Corporation Of India Limited</u>						
189	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	546.36	480.66	11/2016 12/2021	12/2021
190	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	561.71	05/2017 12/2021	12/2021
191	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,697.96	12/2018 03/2024	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Satluj Jal Vidyut Nigam Limited</u>						
192	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	3,509.49	01/2024 -	01/2024
193	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	704.97	12/2021 06/2022	06/2022
194	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	313.58 -	313.58	-	12/2022 -	12/2022
195	SHIYAL SOLAR POWER PROJECT - [N18000297]	5/2021	296.20 -	296.20	-	10/2022 -	10/2022
196	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	182.27	11/2025 -	11/2025
197	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	532.10	01/2026 -	01/2026
	<u>Thdc India Limited</u>						
198	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,860.35	2,313.83	06/2013 12/2024	12/2024
199	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	629.21	09/2020 08/2022	08/2022
	Total		66,893.91 -	1,04,708.09	61,899.83		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
200	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,445.48	1,418.05	03/2023 -	03/2023
201	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
202	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	630.94	03/2023 -	03/2023
203	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>East Central Railways</u>						
204	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,630.00	3,630.96	- 03/2022	03/2022
205	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	4/2003	528.65 -	2,066.78	1,590.10	- 03/2023	03/2023
206	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,218.49	- 03/2022	03/2022
207	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	4/2016	731.64 -	1,185.73	383.26	03/2021 03/2024	03/2024
208	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	4/2016	744.04 -	1,215.54	513.54	03/2021 03/2024	03/2024
209	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	552.33	03/2020 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
210	ARARIA-SUPAUL (NL) - [N22000177]	4/2008	1,605.17 -	1,605.17	147.56	- 03/2023	03/2023
211	KODERMA-TILAIYA (NL), ECR - [220100305]	4/2002	459.91 -	1,625.87	904.73	- 03/2023	03/2023
212	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	926.80	03/2019 12/2021	12/2021
213	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,080.00	1,077.28	03/2012 11/2022	11/2022
	<u>East Coast Railway</u>						
214	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	4/2005	810.78 -	1,928.07	909.17	06/2021 03/2025	03/2025
215	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	1,111.99 -	1,539.28	1,195.24	02/2019 03/2022	03/2022
216	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	2,923.13 -	3,791.66	1,649.76	03/2009 03/2026	03/2026
217	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	3/2013	843.04 -	843.04	269.52	10/2020 03/2024	03/2024
218	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	692.35	12/2018 03/2024	03/2024
219	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	193.71	11/2018 03/2024	03/2024
220	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	493.76	03/2022 03/2026	03/2026
221	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	696.10	03/2022 03/2023	03/2023
222	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	1,010.84	03/2020 03/2023	03/2023
	<u>Metropolitan Rapid Transport Projects</u>						
223	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,866.85	03/2004 06/2022	06/2022
224	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	734.01	478.72	06/2013 07/2022	07/2022
	<u>North Central Railway</u>						
225	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	329.61	03/2022 12/2024	12/2024
	<u>North East Frontier Railway</u>						
226	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	8,600.00	1,656.78	12/2015 12/2023	12/2023
227	AGARTALA-AKHAURA NL - [N22000195]	4/2012	569.63 -	742.00	561.03	03/2020 06/2022	06/2022
	<u>North Eastern Railway</u>						
228	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
229	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,373.75	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
230	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	116.24	12/2021 -	12/2021
	<u>Northern Railway</u>						
231	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.13	242.55	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
232	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	17,009.45	12/2023 -	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
233	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	433.00	405.83	03/2009 12/2022	12/2022
234	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76	3,677.76	2,261.21	12/2023 -	12/2023
235	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	925.02	12/2024 -	12/2024
236	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,082.97	12/2023 -	12/2023
237	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,650.00	1,689.43	12/2021 -	12/2021
	<u>South Central Railway</u>						
238	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	242.28	67.24	03/2022 03/2022	03/2022
	<u>South East Central Railway</u>						
239	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	3,176.60	1,417.20	03/2023 12/2023	12/2023
240	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	1,096.00	40.47	12/2021 12/2024	12/2024
241	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.94	712.76	12/2021 12/2023	12/2023
242	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	2,135.34	700.69	03/2021 12/2023	12/2023
243	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	4/2010	585.93 -	1,268.32	1,082.34	02/2019 12/2021	12/2021
	<u>South Western Railway</u>						
244	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	760.00	642.52	03/2020 12/2021	12/2021
	<u>West Central Railway</u>						
245	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,378.97	03/2021 03/2024	03/2024
246	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,875.12	1,035.16	03/2022 06/2023	06/2023
	<u>Western Railway</u>						
247	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	6,171.08	2,327.60	03/2022 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
248	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	254.99	- 03/2024	03/2024
249	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]	4/2018	537.31 -	537.31	.64	03/2024 -	03/2024
250	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	314.13	06/2020 03/2023	03/2023
251	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,042.12	730.07	03/2021 12/2022	12/2022
252	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,383.69	1,199.84	03/2021 12/2022	12/2022
253	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	558.66	03/2019 03/2023	03/2023
254	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,873.10	869.58	03/2022 03/2025	03/2025
255	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,524.68	974.69	03/2022 03/2023	03/2023
256	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,886.76	1,875.42	03/2020 03/2024	03/2024
257	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	321.62	126.36	03/2012 10/2023	10/2023
	Total		1,84,461.68 -	2,25,256.40	68,690.40		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
258	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]	12/2015	291.05 -	291.05	238.67	- 10/2021	10/2021
259	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]	2/2021	240.99 -	240.99	-	11/2021 -	11/2021
260	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 & KM 158.419 TO KM 173.300 PKG-II. - [N24001412]	12/2020	339.65 -	339.65	-	10/2021 -	10/2021
261	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. [N24001411]	12/2020	379.23 -	379.23	-	10/2021 -	10/2021
262	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]	2/2021	925.47 -	925.47	-	07/2025 -	07/2025
263	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]	1/2020	358.26 -	358.26	1.15	02/2024 -	02/2024
264	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]	2/2021	588.09 -	588.09	83.83	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
265	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	236.18	33.22	12/2022 -	12/2022
266	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	1/2016	476.20 544.00	544.00	400.86	09/2016 12/2021	12/2021
267	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218	11/2015	335.32 -	335.32	279.60	06/2017 12/2021	12/2021
268	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	1/2016	497.14 -	572.66	284.62	08/2016 06/2022	06/2022
269	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	322.24	308.85	09/2014 12/2021	12/2021
270	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	96.49	12/2022 -	12/2022
271	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	552.29	12/2019 12/2021	12/2021
272	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894	2/2018	279.44 -	279.44	223.22	03/2018 11/2021	11/2021
273	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893	11/2017	254.17 -	254.17	183.37	02/2018 03/2022	03/2022
274	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	6/2016	236.78 -	263.26	77.57	08/2019 08/2022	08/2022
275	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229	12/2014	379.16 -	379.16	322.96	11/2017 11/2021	11/2021
276	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228	11/2017	188.80 -	188.80	90.41	05/2019 12/2021	12/2021
277	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226	12/2014	496.02 -	496.02	250.97	03/2015 03/2022	03/2022
278	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224	3/2017	423.79 -	423.79	295.71	01/2018 12/2021	12/2021
279	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222	3/2016	452.94 -	435.61	112.86	07/2016 12/2022	12/2022
280	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	1/2016	624.98 -	731.50	470.70	10/2016 12/2021	12/2021
281	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880	2/2018	426.18 -	426.18	254.43	09/2020 01/2022	01/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
282	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	121.78	11/2019 10/2021	10/2021
283	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021
284	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780	2/2018	293.68 -	293.68	183.73	- 10/2021	10/2021
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	207.83	06/2019 12/2021	12/2021
286	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	326.56	05/2017 05/2022	05/2022
287	CONSTRUCTION OF RING ROAD FOR RAEBAELI CITY (PHASE-I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	319.96	193.43	03/2016 04/2022	04/2022
288	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021
289	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240	3/2020	370.36 -	370.36	196.71	08/2022 -	08/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
290	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744	3/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022
291	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	118.96	09/2019 04/2023	04/2023
292	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972	2/2017	175.06 -	175.06	90.86	- 04/2022	04/2022
293	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	82.60	09/2019 09/2023	09/2023
294	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	25.63	04/2022 -	04/2022
295	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	27.79	12/2022 -	12/2022
296	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248	8/2020	208.84 -	208.84	17.93	04/2022 -	04/2022
297	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	17.58	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
298	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]	3/2020	154.51 -	154.51	39.78	07/2022 -	07/2022
299	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	17.68	04/2022 -	04/2022
300	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]	6/2020	277.50 -	277.50	103.62	01/2022 -	01/2022
301	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]	7/2020	345.38 -	345.38	74.52	04/2023 -	04/2023
302	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]	8/2020	311.00 -	311.00	21.62	04/2023 -	04/2023
303	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	40.94	04/2022 -	04/2022
304	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	7.80	04/2022 -	04/2022
305	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258]	8/2020	202.36 -	202.36	3.90	04/2022 -	04/2022
306	PEREN-DIMAPUR PKG-5 - [N24001407]	2/2021	207.33 -	207.33	8.04	03/2023 -	03/2023
307	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]	7/2021	258.52 -	258.52	8.04	03/2023 -	03/2023
308	CHURACHANPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	-	10/2023 -	10/2023
309	TAMENGLONG - MAHUR PKG-4 - [N24001404]	7/2021	198.77 -	198.77	-	03/2023 -	03/2023
310	TAMENGLONG - MAHUR PKG-2 - [N24001403]	7/2021	483.87 -	483.87	-	03/2023 -	03/2023
311	TAMENGLONG - MAHUR PKG-1 - [N24001402]	7/2021	185.80 -	185.80	-	03/2023 -	03/2023
312	IMPHAL - KHONGSANG PKG-3 - [N24001401]	7/2021	467.00 -	467.00	-	03/2023 -	03/2023
313	SENAPATI- IMPHAL PKG-5B - [N24001400]	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
314	IMPHAL - MOREH (PACKAGE 4) - [N24001399]	3/2021	277.99 -	277.99	-	01/2023 -	01/2023
315	MARIAM - PEREN (PKG 2A) - [N24001398]	7/2021	204.58 -	204.58	-	03/2023 -	03/2023
316	GOHA-KHELLANI PKG-3 - [N24001397]	2/2021	431.28 -	431.28	4.14	03/2023 -	03/2023
317	KHELLANI-KHANABAL PKG-5 - [N24001396]	7/2021	497.09 -	497.09	-	02/2023 -	02/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
318	KHELLANI-KHANABAL PKG-4 - [N24001395]	7/2021	859.67 -	859.67	-	08/2023 -	08/2023
319	KHELLANI-KHANABAL PKG-2 - [N24001394]	7/2021	512.43 -	512.43	-	02/2023 -	02/2023
320	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) [N24001393]	8/2020	184.88 -	184.88	32.58	04/2022 -	04/2022
321	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) [N24001392]	8/2020	199.03 -	199.03	39.84	04/2022 -	04/2022
322	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]	8/2020	294.04 -	294.04	56.85	04/2022 -	04/2022
323	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) [N24001390]	8/2020	228.71 -	228.71	27.48	04/2022 -	04/2022
324	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]	3/2020	206.53 -	206.53	81.84	06/2022 -	06/2022
325	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
326	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]	3/2021	636.42 -	636.42	-	12/2022 -	12/2022
327	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
328	DABOKA KATHKATI PACKAGE-4 - [N24001365]	2/2021	260.07 -	260.07	67.70	12/2023 -	12/2023
329	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	11.78	01/2024 -	01/2024
330	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	-	12/2022 -	12/2022
331	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
332	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
333	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	38.58	12/2022 -	12/2022
334	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
335	TLABUNG - LUNGLEI PKG-A - [N24001358]	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
336	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	12.16	06/2023 -	06/2023
337	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	-	12/2022 -	12/2022
338	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	23.26	12/2022 -	12/2022
339	TAMENGLONG - MAHUR PKG-3 - [N24001354]	3/2021	234.08 -	234.08	-	12/2022 -	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
340	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
341	IMPHAL – MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	25.85	12/2022 -	12/2022
342	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	-	12/2022 -	12/2022
343	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	-	12/2022 -	12/2022
344	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	-	12/2022 -	12/2022
345	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	3.39	01/2023 -	01/2023
346	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	31.14	06/2024 -	06/2024
347	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	31.14	05/2024 -	05/2024
348	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	-	01/2023 -	01/2023
349	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	-	01/2023 -	01/2023
350	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	7.11	01/2023 -	01/2023
351	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
352	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	-	12/2022 -	12/2022
353	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]	10/2020	157.86 -	157.86	53.58	04/2022 -	04/2022
354	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
355	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
356	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]	8/2020	230.45 -	230.45	2.58	04/2023 -	04/2023
357	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	40.21	12/2023 -	12/2023
358	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	173.17	12/2023 -	12/2023
359	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]	9/2019	761.54 -	761.54	116.54	05/2023 -	05/2023
360	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
361	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]	3/2020	261.13 -	261.13	23.56	06/2022 -	06/2022
362	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	40.96	12/2023 -	12/2023
363	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]	3/2020	165.54 -	165.54	5.26	07/2022 -	07/2022
364	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]	12/2020	804.00 -	804.00	7.04	08/2023 -	08/2023
365	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]	8/2020	292.80 -	292.80	27.45	05/2022 -	05/2022
366	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	532.08	09/2028 -	09/2028
367	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]	9/2020	262.84 -	262.84	118.63	05/2023 -	05/2023
368	KHELLANI-KHANABAL PKG-6 - [N24001324]	2/2021	285.28 -	285.28	18.65	09/2022	09/2022
369	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	36.09	09/2022 -	09/2022
370	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]	9/2020	183.31 -	183.31	75.61	05/2022 -	05/2022
371	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
372	DOGINALA - GAU - [N24001320]	12/2020	242.30 -	242.30	-	09/2022 -	09/2022
373	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]	6/2020	257.96 -	257.96	95.22	01/2022 -	01/2022
374	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]	9/2020	173.17 -	173.17	5.10	04/2022 -	04/2022
375	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]	6/2020	201.99 -	201.99	18.87	01/2022 -	01/2022
376	LADDA - BASAI - [N24001316]	2/2021	445.96 -	445.96	-	04/2023 -	04/2023
377	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
378	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	288.84	12/2023 -	12/2023
379	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.37	12/2023 -	12/2023
380	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]	3/2020	167.95 -	167.95	46.68	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
381	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]	11/2020	206.78 -	206.78	52.08	07/2022 -	07/2022
382	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]	11/2020	280.91 -	280.91	59.89	07/2022 -	07/2022
383	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022
384	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]	11/2020	332.14 -	332.14	10.88	07/2022 -	07/2022
385	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]	4/2020	330.80 -	330.80	38.65	12/2021 -	12/2021
386	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]	3/2020	330.78 -	330.78	54.27	12/2021 -	12/2021
387	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]	3/2020	278.95 -	278.95	79.89	06/2022 -	06/2022
388	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53 -	361.53	32.21	06/2022 -	06/2022
389	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]	3/2020	281.78 -	281.78	92.39	07/2022 -	07/2022
390	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	58.14	06/2022 -	06/2022
391	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24 -	292.24	49.59	07/2022 -	07/2022
392	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	39.60	06/2022 -	06/2022
393	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]	3/2020	216.49 -	216.49	53.72	07/2022 -	07/2022
394	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	30.06	07/2022 -	07/2022
395	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	24.56	10/2022 -	10/2022
396	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
397	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
398	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	5.07	04/2022 -	04/2022
399	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	25.18	08/2022 -	08/2022
400	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]	3/2020	167.95 -	167.95	28.20	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
401	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	42.84	08/2022 -	08/2022
402	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	36.80	06/2022 -	06/2022
403	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	40.09	03/2022 -	03/2022
404	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	154.09	07/2022 -	07/2022
405	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	10.30	07/2022 -	07/2022
406	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	32.33	10/2022 -	10/2022
407	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	275.00	09/2026 -	09/2026
408	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	32.98	06/2022 -	06/2022
409	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023
410	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	27.06	04/2023 -	04/2023
411	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251	3/2019	402.94 -	402.94	56.40	04/2022 -	04/2022
412	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	103.50	03/2022 -	03/2022
413	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249	6/2020	347.36 -	347.36	66.04	01/2022 -	01/2022
414	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247	3/2020	247.76 -	247.76	19.60	01/2022 -	01/2022
415	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245	9/2020	353.90 -	353.90	20.81	05/2022 -	05/2022
416	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973	2/2017	176.12 -	176.12	76.96	- 04/2022	04/2022
<u>National Highways Authority Of India</u>							
417	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	694.42	05/2018 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
418	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	716.78	622.88	05/2018 03/2022	03/2022
419	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	450.47	04/2019 10/2022	10/2022
420	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566	4/2016	804.97 -	804.97	594.02	06/2018 10/2021	10/2021
421	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564	3/2016	1,408.00 -	827.05	387.83	- 07/2022	07/2022
422	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
423	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
424	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
425	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
426	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI - [N24001416	12/2020	989.66 -	989.66	-	01/2024 -	01/2024
427	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
428	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 -	01/2024
429	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
430	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
431	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838	3/2018	874.25 -	866.55	864.82	- 10/2021	10/2021
432	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706	9/2017	990.61 -	990.61	719.29	09/2017 11/2021	11/2021
433	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	1,285.31	03/2020 12/2021	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
434	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 02/2022	02/2022
	Total		85,696.54 -	86,289.04	18,393.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
435	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	5,369.18 -	4,633.81	1,940.64	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,940.64		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
436	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	21,940.00	19,016.02	05/2015 01/2022	01/2022
437	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]	11/2015	2,907.00 -	2,907.00	439.00	06/2023 -	06/2023
	<u>Rastrya Ispat Nigam Limited</u>						
438	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	2,100.00	1,736.92	09/2018 11/2021	11/2021
439	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,858.00	2,004.81	12/2017 07/2022	07/2022
	<u>Steel Authority Of India Limited (Sail)</u>						
440	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	44.29	05/2023 -	05/2023
441	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]	11/2020	542.24 -	542.24	70.05	12/2023 -	12/2023
	Total		23,892.27 -	30,724.42	23,311.09		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
442	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]	3/2020	431.16 431.00	422.87	46.37	06/2021 11/2021	11/2021
	Total		431.16 -	422.87	46.37		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
443	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	247.58	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
444	SURAT METRO RAIL PROJECT - [N28000138 <u>Bangalore Metro Rail Corporation Limited</u>	3/2019	12,020.32 -	12,020.32	208.21	03/2024 -	03/2024
445	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058 <u>Central Public Works Department</u>	2/2014	26,405.14 -	30,695.12	18,874.67	02/2019 03/2025	03/2025
446	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	6/2015	197.33 -	217.00	173.51	04/2019 02/2022	02/2022
447	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	208.13	05/2020 11/2021	11/2021
448	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128	10/2016	1,180.00 -	1,100.80	35.74	07/2021 06/2023	06/2023
449	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110	10/2016	422.00 -	422.00	108.75	03/2021 06/2023	06/2023
450	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149	5/2019	299.97 -	299.97	20.39	09/2020 01/2023	01/2023
451	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114 <u>Delhi Metro Rail Corporation</u>	10/2016	392.00 -	392.00	161.81	08/2020 06/2022	06/2022
452	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS [N28000135 <u>Maharastra Metro Rail Corporation Ltd.</u>	7/2019	24,948.65 -	24,948.65	2,442.28	03/2025 -	03/2025
453	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121 <u>Mumbai Metro Rail Corporation Ltd</u>	12/2016	11,420.00 -	11,420.00	7,187.19	11/2021 12/2022	12/2022
454	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086 <u>Madhya Pradesh Metro Rail Co Limited</u>	7/2013	23,136.00 -	33,406.00	19,493.96	03/2020 03/2023	03/2023
455	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	248.29	02/2023 -	02/2023
456	INDORE METRO RAIL - [N28000125 <u>Nagpur Metro Rail Corporation Ltd</u>	11/2018	7,500.80 -	7,500.80	142.54	02/2023 -	02/2023
457	NAGPUR METRO RAIL - [N28000085 <u>National Capital Region Transport Corp</u>	8/2014	8,680.00 -	8,680.00	8,427.24	03/2018 12/2021	12/2021
458	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134 <u>Patna Metro Rail Corporation</u>	3/2019	30,274.00 -	30,274.00	5,222.09	06/2025 -	06/2025
459	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	2/2019	13,365.77 -	13,925.50	302.95	06/2024 -	06/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,72,806.11	1,87,866.29	63,505.33		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
460	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02	294.02	-	10/2021	10/2021
461	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89	578.89	42.75	06/2022	06/2022
462	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00	824.00	42.75	06/2022	06/2022
	<u>Delhi Jal Board</u>						
463	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78	665.78	230.58	12/2022	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
464	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96	384.96	-	04/2022	04/2022
465	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI [N30000048]	1/2018	172.10	172.10	11.56	12/2021	12/2021
466	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93	164.93	11.56	12/2021	12/2021
467	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22	185.22	11.56	12/2021	12/2021
468	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA [N30000034]	8/2017	307.12	307.12	-	09/2022	09/2022
469	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]	3/2019	287.53	287.53	-	04/2022	04/2022
470	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31	234.31	-	04/2022	04/2022
471	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS [N30000033]	3/2018	165.16	165.16	-	06/2022	06/2022
	<u>Uttar Pradesh Jal Nigam</u>						
472	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62	261.12	-	03/2022	03/2022
473	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH [N30000021]	1/2019	231.79	234.03	14.63	12/2021	12/2021
474	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05	206.05	53.62	10/2021	10/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
475	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
	Total		5,597.26 -	5,655.93	419.01		
	Grand Total		9,47,143.74	10,61,138.25	3,75,418.25		

FLASH REPORT

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	02/2022	44.69
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	03/2023	38.63
	Total		23,779.00 .00 23,779.00	33,659.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 - 1,938.00	1,983.00	09/2021 -	12/2023	43.38
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	12/2022	38.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2023	7.88
	Total		2,871.27 .00 3,426.27	3,695.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>						
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 - 479.53	708.55	03/2013 -	03/2024	47.76
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	11/2022	.00
	<u>Singareni Colliers Company Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86
10	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2023	5.85
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
<u>Western Coal Fields Limited</u>							
13	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 - 289.29	289.30	03/2022 -	03/2025	.00
Total			22,093.43 .00 22,093.43	25,136.67			
<u>DEPARTMENT OF HIGHER EDUCATION</u>							
<u>Cpwd Of Higher Education</u>							
14	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00 496.00	498.99	06/2017 -	03/2022	.60
15	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 - 135.00	171.72	03/2020 -	12/2021	.00
16	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 - 549.31	559.47	07/2019 -	-	1.85
17	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00 199.00	205.00	09/2020 -	-	3.02
<u>Rites Of Higher Education</u>							
18	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 - 484.32	626.26	09/2014 -	-	29.31
Total			1,887.53 695.00 1,863.63	2,061.44			
<u>DPIIT</u>							
<u>Dmic For Dpiit</u>							
19	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Iicc For Dpiit</u>						
20	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	05/2022	8.49
	Total		17,352.09 .00 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
21	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR [N21000030]	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>						
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 - 414.11	586.50	11/2013 -	09/2021	41.63
23	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 - 204.44	250.00	05/2017 -	03/2021	22.29
24	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
25	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 - 168.90	191.20	05/2017 -	07/2019	13.20
26	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 - 505.58	585.00	03/2018 -	09/2019	15.71
27	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 - 152.95	177.92	02/2018 -	03/2021	16.33
28	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 - 244.00	248.00	09/2018 -	05/2019	1.64
29	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 - 272.19	272.54	03/2019 -	03/2021	.13
30	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 - 156.56	190.34	- -	11/2021	21.58
31	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 - 249.01	249.07	- -	01/2021	.02
	<u>Nbcc For Health</u>						
32	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 - 1,351.00	1,471.00	09/2021 -	06/2022	8.88

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,589.39 .00 5,589.39	6,374.57			
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
33	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	03/2022	64.04
	Total		1,219.21 .00 1,219.21	2,000.00			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
34	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 - 2,677.00	3,072.00	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>						
35	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 - 423.00	502.00	08/2019 -	05/2021	18.68
	<u>Oil & Natural Gas Corporation Limited</u>						
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128	03/2011	861.79 - 1,846.46	2,001.34	05/2013 -	05/2022	132.23
	Total		3,961.79 .00 4,946.46	5,575.34			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
37	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 - 14,366.58	15,389.42	06/2019 -	09/2023	7.12
38	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
39	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
40	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	02/2022	14.11
	<u>Satluj Jal Vidyut Nigam Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
41	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 - 648.33	947.89	12/2021 -	06/2022	46.20
	Total		24,279.87 7,738.00 24,279.91	26,684.38			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
42	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	03/2023 -	03/2023	8.75
			3,168.29				
43	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	03/2021 -	03/2023	75.00
			792.89				
44	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	325.00	03/2019 -	-	76.57
			184.06				
45	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	03/2021 -	03/2023	111.08
			2,271.50				
46	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
			2,425.00				
47	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.49	03/2024 -	-	25.04
			2,750.00				
48	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	03/2022 -	03/2023	.89
			1,272.19				
49	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
50	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
			1,876.00				
	<u>Container Corporation Of India</u>						
51	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	03/2018 -	-	25.65
			387.70				
52	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	-	.21
			234.50				
	<u>East Central Railways</u>						
53	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,630.00	- -	03/2022	251.38
			3,020.95				

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
54	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	324.73 - 898.53	1,080.00	03/2012 -	11/2022	232.58
55	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 - 380.00	519.33	- -	03/2025	36.67
56	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 - 678.54	929.86	03/2019 -	12/2021	37.04
57	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 - 415.67	549.75	- -	-	32.26
58	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
59	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 - 378.56	1,858.75	- -	03/2023	391.01
60	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78
61	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 - 548.00	819.01	03/2020 -	12/2024	49.45
62	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15 - 332.15	546.71	07/2014 -	-	64.60
63	GARHWA ROAD-RAMNA - [N22000465	03/2015	348.23 - 348.23	390.00	03/2021 -	03/2022	11.99
64	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 - 803.11	1,483.14	- -	03/2022	350.27
	<u>East Coast Railway</u>						
65	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2024	15.45
	<u>Eastern Railways</u>						
66	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
68	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
69	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
70	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
71	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
72	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
73	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL [N22000241]	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
74	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15
75	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
76	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
77	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
78	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
79	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
80	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
81	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 - 288.35	502.48	- -	03/2021	74.26
82	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
83	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
Indian Railway Construction Company Limited							
84	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	09/2023	117.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
85	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	06/2022	.00
	<u>Metropolitan Rapid Transport Projects</u>						
86	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
87	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 - 495.44	2,980.41	03/2004 -	06/2022	501.57
88	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	734.01	06/2013 -	07/2022	48.06
89	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	-	75.91
	<u>North Central Railway</u>						
90	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
91	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	12/2021	1.80
	<u>North East Frontier Railway</u>						
92	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 - 200.34	614.00	03/2019 -	-	106.51
93	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	5,521.45	03/2014 -	03/2024	130.69
94	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 2,531.34	4,541.38	12/2008 -	11/2021	284.80
95	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	12,264.15	03/2011 -	12/2023	175.34
96	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,043.00	03/2019 -	03/2023	170.77
97	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 - 2,132.03	2,145.00	03/2019 -	03/2024	302.54
98	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 - 2,326.52	6,647.64	03/2015 -	03/2026	185.73
99	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	-	7.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
100	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 4,084.69	8,600.00	12/2015 -	12/2023	542.04
101	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62
102	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 90.00	742.00	03/2020 -	06/2022	30.26
103	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	4,083.02	03/2021 -	-	350.44
104	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
105	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	03/2022	54.80
106	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	750.00	03/2020 -	-	80.79
107	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,090.60	- -	-	33.13
108	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
109	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	03/2022	115.07
110	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 - 602.27	1,167.00	12/2021 -	10/2021	93.77
111	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,090.60	04/2010 -	-	186.55
<u>North Eastern Railway</u>							
112	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
113	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
114	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13
115	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	610.00	01/2019 -	02/2022	106.78

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
116	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
117	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 - 1,295.42	1,824.00	03/2022 -	03/2022	40.80
118	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	12/2021	.16
119	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 - 150.00	341.66	04/2017 -	10/2022	127.77
120	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,345.00	01/2018 -	-	.15
121	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	800.00	- -	12/2023	32.78
<u>North Western Railway</u>							
122	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	06/2022	109.82
123	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	10/2022	16.97
124	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 - 873.71	2,215.27	- -	-	153.55
125	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
126	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR [N22000152]	04/2013	420.18 - 420.18	480.00	03/2020 -	09/2021	14.24
<u>Northern Railway</u>							
127	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
128	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
129	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	09/2023	134.90
130	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
131	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
132	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 - 328.14	1,540.13	03/2023 -	03/2023	369.35
133	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 781.00	839.00	03/2016 -	-	34.24
	<u>Rail Vikas Nigam Ltd.</u>						
134	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
135	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	433.00	03/2009 03/2009	12/2022	109.18
136	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22
137	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	12/2025	127.62
138	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,000.00	03/2023 -	12/2022	41.04
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2025	7.78
140	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
141	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,377.00	03/2020 -	03/2022	124.58
142	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 - 975.62	1,650.00	12/2021 -	12/2021	69.12
143	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 - 644.38	872.65	03/2021 -	12/2021	35.42
144	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	1,868.89	12/2021 -	03/2022	20.68
145	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	12/2021	50.15
146	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
147	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,000.00	03/2022 -	12/2024	5.98
148	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 - 773.94	850.00	12/2024 -	12/2024	9.83
149	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,400.00	03/2019 -	06/2022	51.02
150	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	22,716.11	12/2024 -	03/2025	40.08
151	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,900.00	03/2020 -	12/2021	306.46
152	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
153	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91
154	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
155	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24
156	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
157	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
	<u>Railway Electrification</u>						
158	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
159	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
160	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 - 1,160.48	1,373.74	03/2010 -	03/2024	18.38
161	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
162	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
163	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
164	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
165	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06
166	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 176.18	242.28	03/2022 -	03/2022	30.96
	<u>South East Central Railway</u>						
167	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 852.50	1,096.00	12/2021 -	12/2024	378.60
	<u>South Eastern Railway</u>						
168	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
169	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
170	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
171	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
172	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 - 969.83	1,312.96	03/2020 -	03/2022	35.38
173	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 - 1,027.40	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
174	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	2,161.36	- -	12/2023	20.01
175	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 - 986.30	1,530.09	03/2016 -	12/2026	55.13
176	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 - 558.00	692.43	- -	12/2023	24.09

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
177	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	466.65	- -	12/2023	57.65
178	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,404.03	- -	12/2025	16.57
179	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 - 327.25	367.77	- -	12/2023	12.38
180	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	5,174.30	- -	12/2024	123.51
181	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 - 1,382.78	1,960.00	03/2002 -	03/2024	41.74
182	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,968.00	03/2020 -	03/2023	70.10
183	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,104.00	03/2020 -	09/2021	28.31
184	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	760.00	03/2020 -	12/2021	31.49
185	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,877.81	1,878.00	03/2019 -	03/2024	16.31
<u>Southern Railway</u>							
186	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 - 724.69	2,950.00	02/2019 -	03/2025	307.07
187	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	3,150.00	- -	12/2025	440.47
188	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,720.00	03/2020 -	03/2025	465.83
189	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
190	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	03/2030	247.32
191	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	1,205.00	- -	03/2024	130.17
192	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	839.01	- -	03/2030	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
193	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 457.08	749.40	- -	01/2022	177.41
194	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 369.55	709.69	- -	03/2025	180.55
195	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	603.23	- -	03/2030	109.04
196	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	608.13	- -	02/2022	269.89
197	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	1,122.00	- -	12/2022	20.39
198	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 275.21	448.10	- -	03/2025	136.79
199	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
200	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,246.00	1,339.00	- -	03/2025	33.90
201	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	09/2021	253.33
<u>West Central Railway</u>							
202	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
203	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 - 1,763.93	2,449.00	03/2020 -	03/2024	38.84
<u>Western Railway</u>							
204	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 - 5,839.02	6,171.08	03/2022 -	03/2023	76.13
205	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 - 1,246.59	1,886.76	03/2020 -	03/2024	127.39
206	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 - 858.96	1,378.11	03/2019 -	03/2023	329.77
207	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 - 1,125.53	1,383.69	03/2021 -	12/2022	33.41

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
208	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 - 1,002.39	1,042.12	03/2021 -	12/2022	3.96
	Total		1,80,828.29 4,842.30 1,95,131.24	3,33,189.11			
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
209	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 - 624.41	992.67	03/2011 -	-	58.98
210	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 - 193.69	327.92	10/2010 -	12/2021	69.30
211	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 - 280.16	290.59	- -	-	3.72
212	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
213	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 - 268.08	390.73	05/2017 -	05/2022	45.75
214	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 - 889.24	904.82	- -	-	1.75
215	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 - 195.04	377.99	10/2010 -	-	93.80
216	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 - 319.68	369.77	- -	-	15.67
217	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 - 460.73	461.00	- -	-	.06
218	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 - 237.80	238.00	11/2019 -	10/2021	.08
219	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 - 217.22	226.88	08/2018 -	12/2021	4.45
220	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]	10/2015	333.21 - 333.21	353.43	12/2015 -	-	6.07
221	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]	09/2016	372.68 - 309.37	372.68	02/2017 -	-	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
222	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	02/2017	429.43 - 373.05	429.43	11/2017 -	-	.00
223	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	03/2018	228.32 - 202.83	228.32	08/2018 -	-	.00
224	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	03/2018	289.67 290.00 274.73	289.67	08/2018 -	-	-.11
225	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00 995.00	995.09	05/2016 -	-	.01
226	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	01/2018	418.03 - 381.75	418.03	08/2018 -	-	.00
227	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965	01/2016	386.09 - 316.06	386.09	05/2016 -	-	.00
228	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
229	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
230	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15
231	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
232	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02
233	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
234	KARAD TO VITA - [N24001049	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
235	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00 257.00	257.38	12/2019 -	-	.15
236	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
237	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
238	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
239	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24
240	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
241	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
242	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
243	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08
244	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
245	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
246	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13
247	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
248	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11
249	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
250	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
251	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06
252	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
253	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
254	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	03/2016	536.65 356.00 356.00	536.65	12/2019 -	12/2021	50.74
255	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02
256	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
257	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
258	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
259	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
260	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31
261	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00 743.00	743.21	06/2021 -	-	.03
262	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
263	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
264	KALMATH TO ZARAP - [N24001137	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01
265	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00 215.00	215.16	09/2019 -	10/2019	.07
266	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2021	.13
267	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 - 297.30	318.28	01/2019 -	-	7.06
268	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 - 325.86	386.41	10/2018 -	-	18.58
269	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 - 186.96	322.24	09/2014 -	12/2021	72.36

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
270	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 - 1,979.00	2,036.90	- -	-	2.93
271	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00 543.73	544.00	09/2016 -	12/2021	.00
272	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239	03/2018	240.38 - 204.73	240.38	06/2019 -	-	.00
273	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 - 197.67	236.18	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
274	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 - 195.23	252.79	04/2017 -	03/2022	29.48
275	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 - 203.36	263.31	04/2017 -	03/2022	29.48
276	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 - 373.07	387.00	08/2016 -	05/2021	3.73
277	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 - 198.22	252.05	04/2017 -	03/2022	27.16
278	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
279	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	09/2020	277.44 - 177.00	277.44	10/2022 -	10/2022	.00
	<u>National Highways Authority Of India</u>						
280	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 - 280.00	612.58	02/2009 -	-	118.78
281	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
282	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
283	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
284	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
285	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
286	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
287	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
288	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
289	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 - 511.54	591.00	11/2013 -	-	15.53
290	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 - 291.36	469.31	01/2014 -	-	61.08
291	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 - 351.34	417.68	01/2016 -	-	18.88
292	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 - 495.78	627.93	01/2016 -	-	26.66
293	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 - 531.13	744.73	05/2018 -	03/2022	40.22
294	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
295	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37
296	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
297	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 - 247.00	322.09	04/2018 -	-	.00
298	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
299	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
300	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
301	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
302	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
303	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
304	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH- 29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
305	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	04/2021	7.53
306	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 - 458.03	486.00	- -	-	6.11
307	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	1,588.29	09/2019 -	-	14.40
308	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,367.00	2,280.00	- -	-	94.94
309	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
310	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 - 1,100.19	1,145.31	- -	-	4.10
311	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 - 290.73	315.00	- -	05/2017	8.35
312	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 - 605.84	722.46	07/2018 -	02/2022	19.25
313	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG- II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
314	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88
315	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
316	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 - 988.34	1,043.28	03/2020 -	-	5.56

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
317	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	-	1.06
318	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
319	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 - 754.54	756.27	03/2020 -	09/2022	.23
320	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38
321	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
322	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	-	10.24
323	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
324	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
325	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
326	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 - 894.00	929.32	04/2020 -	03/2022	3.95
327	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	-	1.78
328	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	-	9.67
329	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 - 273.46	276.17	- -	-	.99
330	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
331	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 - 1,166.26	1,296.93	- -	01/2022	11.20
332	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
333	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
334	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35
335	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
336	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 - 1,052.21	1,361.00	- -	-	29.35
337	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	07/2021	63.05
338	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 - 496.20	537.17	- -	-	8.26
339	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
340	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	01/2022	5.32
341	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	12/2021	4.99
342	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	11/2021	.12
343	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	925.96	- -	02/2018	45.89
344	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 906.65	922.64	- -	02/2018	15.98
345	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
346	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00
347	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
348	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	10/2022	305.58

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
349	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 - 720.81	724.60	03/2023 -	03/2023	.00
350	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 - 731.89	732.34	11/2019 -	-	.06
351	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 - 594.75	606.75	11/2019 -	-	2.02
	Total		95,897.94 17,965.00 95,479.17	1,12,893.82			
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
352	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85 - 1,682.85	2,100.00	09/2018 -	11/2021	24.79
	Total		1,682.85 .00 1,682.85	2,100.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
353	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	08/2022	18.69
	<u>Mumbai Metro Rail Corporation Ltd</u>						
354	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 - 23,136.00	33,406.00	03/2020 -	03/2023	44.39
	<u>Patna Metro Rail Corporation</u>						
355	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	02/2019	13,365.77 - 13,365.77	13,925.50	06/2024 -	06/2024	4.19
	Total		47,274.77 .00 47,274.77	60,118.50			
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
356	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027	10/2017	254.13 - 254.13	413.29	09/2020 -	-	62.63

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(October 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
357	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 - 225.77	398.90	03/2020 -	03/2021	76.68
	<u>Uttar Pradesh Jal Nigam</u>						
358	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2021	.97
359	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 - 681.78	690.71	06/2022 -	06/2022	1.31
	Total		1,393.47 .00 1,393.47	1,736.93			
	Grand Total		4,30,110.90 31,240.30 4,45,510.89	6,34,215.39			

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	11459	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	12/2023	380.87	21
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	05/2022	177.1	27
7	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	03/2023	1405	7
8	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	12/2022	412.24	18
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	11/2021	438.28	29
10	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	AAI	05/2018	10/2022	12/2023	1216.9	14
11	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	04/2022	458	25
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2022	346.27	15
13	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	AAI	11/2016	04/2020	06/2022	303.8	26
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2022	417.23	45
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	12/2023	2467	22
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT	AAI	08/2018	10/2021	10/2022	951.28	12
17	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383	27
18	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION	AAI	03/2017	04/2021	08/2022	475.39	16
19	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	01/2023	389.71	14
20	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2023	1142	24
21	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	09/2022	456.86	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
22	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	10/2022	304.13	67
23	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	10/2022	243	54
24	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13
25	BHUBANESWARI EXPENSION OCP(40.0 MTY)	MCL	12/2007	03/2017	03/2031	3145.45	168
26	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	132
27	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	MCL	12/2007	03/2010	03/2029	3504.21	228
28	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
29	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	02/2023	1230.27	94
30	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2023	447.06	96
31	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84
32	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
33	RECAST EPR AMRAPALI OC	CCL	02/2012	03/2020	03/2028	4983.58	96
34	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2022	869.44	12
35	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	03/2022	304.52	36
36	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	11/2022	17237	12
37	RPR FOR JAMUNIA UG (0.90 MTY)	WCL	07/2016	03/2022	03/2026	281.25	48
38	RECAST PR FOR DHANKASA UG (1.00 MTY)	WCL	09/2016	03/2022	03/2025	289.29	36
39	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	09/2023	328	30
40	KOLAR PIMPRI EXTENSION OC	WCL	03/2017	03/2020	09/2022	362.73	30
41	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
42	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
43	GARJANBAHAL OCP	MCL	11/2014	03/2021	09/2025	1375.38	54
44	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	WCL	11/2014	03/2020	03/2027	1184.33	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	AMRITDHARA OC PROJECT	SECL	02/2015	03/2023	03/2027	481.6	48
46	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
47	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	04/2024	357.8	37
48	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
49	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	12/2021	289.45	91
50	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	03/2022	295.56	36
51	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2022	1783.09	12
52	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84
53	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2028	6964.33	188
54	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
55	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
56	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
57	EXPANSION PR OF JHANJRA UG(5.00 MTY)	ECL	11/2015	03/2022	03/2029	1210.12	84
58	BATURA OCP (2.0 MTY)	SECL	08/2015	03/2023	03/2026	1186.64	36
59	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
60	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2026	178.44	144
61	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	03/2025	1458.17	117
62	MADANNAGAR OPENCAST PROJECT	SECL	10/2015	03/2024	03/2027	1875.32	36
63	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	WCL	11/2015	03/2021	03/2024	313.34	36
64	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	WCL	11/2015	03/2020	03/2026	851.6	72
65	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2022	555.52	12
66	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2029	1055.05	132
67	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
68	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
69	BATURA HIGHWALL PROJECT	SECL	07/2015	03/2022	03/2025	231.92	36
70	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
71	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2026	916.24	36
72	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
73	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	MCL	12/2007	03/2013	03/2028	8416.19	180
74	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2023	321.5	108
75	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
76	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
77	UKNI DEEP OC	WCL	11/2018	03/2021	09/2022	318.14	18
78	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	09/2022	252.71	18

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD FOR DEFEN	12/2016	02/2020	12/2021	246.31	22

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
80	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD EDUCATION	09/2018	09/2020	11/2022	375	26
81	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD EDUCATION	01/2018	07/2020	12/2021	223.37	17
82	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	CPWD EDUCATION	11/2017	03/2020	12/2021	171.72	21
83	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD EDUCATION	07/2019	03/2021	02/2023	753.63	23
84	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD EDUCATION	07/2019	03/2022	09/2022	851	6
85	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD EDUCATION	11/2012	11/2014	11/2021	270.83	84
86	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD EDUCATION	02/2016	06/2017	03/2022	496.18	57

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
87	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD EDUCATION	01/2018	05/2020	06/2022	430	25

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
88	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	05/2022	4773	29

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
89	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	10/2021	426.72	18
90	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	10/2021	215.92	23

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
91	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD FOR HEALTH	03/2018	09/2020	04/2022	195	19
92	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD FOR HEALTH	09/2017	03/2020	12/2021	150.29	21
93	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD FOR HEALTH	12/2018	06/2021	05/2022	260	11
94	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	03/2022	363.99	46
95	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	06/2022	1351	9
96	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	10/2021	355.15	31

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
97	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	03/2022	1219.21	29
98	NSG AT KOLKATA	CPWD FOR MHA	10/2014	04/2018	12/2021	162.88	44

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
99	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	01/2024	5540	33
100	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	12/2023	355	37
101	SOURCING OF BAUXITE ARRANGEMENT FOR	NALCO	11/2017	04/2021	12/2023	483	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN						

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFI	06/2020	06/2023	01/2024	200	7
103	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	BPCL	10/2018	03/2021	11/2021	206.26	8
104	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	08/2022	225.54	18
105	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
106	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
107	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
108	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	12/2021	286.42	16
109	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	BPCL	07/2017	02/2021	03/2023	580.2	25
110	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
111	PIPELINE REPLACEMENT PROJECT (PRP-VI)	ONGC	05/2019	12/2020	12/2021	763.92	12
112	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK)	ONGC	10/2018	03/2021	05/2022	156.67	14
113	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	BPCL	08/2019	08/2022	06/2023	1607	10
114	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7
115	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	01/2022	196.26	18
116	LPG BP PROJECT CHITTOOR	IOCL	07/2019	07/2022	01/2023	167	6
117	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	03/2022	164.69	8
118	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	49
119	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	06/2022	160.1	28
120	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	10/2022	161.59	34
121	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
122	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	11/2021	581	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
123	220 KV GRID SUPPLY	HPCL	10/2020	03/2021	10/2021	303.4	7
124	SULPHUR FORMING UNIT IN SRU	HPCL	10/2020	08/2021	03/2022	210.94	7
125	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	09/2022	607.06	59
126	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	03/2022	1823	12
127	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321	15
128	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	03/2022	690	44
129	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	08/2022	348	19
130	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2020	11/2021	2881.4	11
131	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1933	12
132	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	2433	12
133	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	3437	12
134	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1740	12
135	PIPELINE NETWORK PROJECT GELEKI, ASSAM	ONGC	07/2016	05/2020	11/2021	249.85	18
136	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677	13
137	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	01/2022	466.43	15
138	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2022	861.79	108
139	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	12/2021	327.78	44
140	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
141	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
142	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	06/2022	34012	24
143	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497	38
144	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	02/2022	1810	26

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
145	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	OIL	05/2016	10/2020	03/2022	406	17
146	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	12/2021	571.66	24
147	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
148	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	03/2022	249.26	21
149	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	03/2022	161.5	21
150	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	01/2022	206.5	10
151	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	29
152	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	03/2022	255.4	19
153	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2022	199.36	22
154	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	03/2022	906	25
155	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	07/2022	163.02	27
156	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	12/2021	421	16
157	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	IOCL	08/2017	08/2021	11/2022	318.8	15
158	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	IOCL	08/2017	06/2020	12/2021	236	18
159	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	12/2021	543.91	22
160	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	IOCL	07/2018	01/2021	12/2021	189	11
161	ETHYLENE GLYCOL PROJECT AT PARADIP	IOCL	04/2018	10/2021	07/2022	5654	9
162	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	11/2021	557	21
163	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
164	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	IOCL	08/2018	04/2021	12/2021	466	8
165	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
166	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	12/2021	522	9
167	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	12/2021	224.75	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
168	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	ONGC	02/2019	05/2021	12/2021	2292.46	7
169	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
170	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	ONGC	05/2019	05/2021	01/2022	3660.71	8
171	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	06/2022	462.3	9
172	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	09/2022	3361	13
173	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
174	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	03/2022	217.92	11

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
175	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	02/2022	529.68	39
176	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	12/2021	1885.13	36
177	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	02/2025	18668	23
178	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
179	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	6
180	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	63
181	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	12/2021	235.53	30
182	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	10/2021	14733.37	23
183	NORTH KARANPURA STPP (3X660 Mw)	NTPC	02/2014	06/2019	09/2023	14366.58	51
184	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63
185	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2021	197.4	45
186	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2021	1394.52	55
187	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	11/2021	5353	112
188	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2024	2491.58	138

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
189	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657	88
190	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	141
191	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10/2022	10598.98	23
192	KAYAMKULAM SOLAR 70 MW	NTPC	09/2019	06/2021	12/2021	403.62	6
193	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	02/2022	12964.6	45
194	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	162
195	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
196	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	11130.19	108
197	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2021	374.63	68
198	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	12/2021	522.29	61
199	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	09/2024	2978.48	138
200	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
201	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
202	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	02/2022	3500	19
203	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	12/2021	186.17	29
204	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	10/2021	1931.39	20
205	NOKHRA	NTPC	03/2020	09/2021	01/2023	1722.14	16
206	RAMAGUNDAM FLOATING SOLAR 100 MW	NTPC	06/2019	04/2021	10/2021	401.9	6
207	SAMBHU KI BHURJ-II SOLAR 300MW	NTPC	03/2020	09/2021	09/2022	1782	12
208	JETSAR SOLAR 160 MW	NTPC	12/2019	03/2021	11/2021	702.28	8
209	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	02/2022	322.3	36
210	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	12/2021	379.95	24
211	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	03/2022	5111.33	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
212	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	12/2021	358.83	19

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
213	ANAND GODHRA DOUBLING PROJECT 79 KMS	WR	04/2017	03/2020	03/2023	692.25	36
214	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	06/2022	3055	45
215	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	96
216	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
217	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
218	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	06/2022	760	27
219	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68
220	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
221	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
222	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
223	GARHWA ROAD-RAMNA	ECR	03/2015	03/2021	03/2022	348.23	12
224	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
225	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	36
226	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
227	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
228	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
229	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
230	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
231	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
232	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
233	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
234	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
235	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
236	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.3	129
237	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
238	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
239	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
240	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	02/2022	704.31	23
241	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
242	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
243	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
244	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
245	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	06/2022	495.44	219
246	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
247	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
248	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	11/2021	1180.19	155
249	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	204
250	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
251	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	07/2022	495.74	109
252	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
253	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
254	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	132
255	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
256	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	40
257	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450	148
258	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500	241
259	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
260	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
261	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
262	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
263	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
264	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	10/2023	318.24	139
265	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
266	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
267	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
268	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
269	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
270	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24
271	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	36
272	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600	31
273	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	12/2021	578	21
274	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	60
275	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	12/2021	678.54	33
276	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
277	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12
278	DAHOD-INDORE VIA SARDARPUR, JHABUA	WR	04/2007	03/2022	03/2025	1640.04	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AND DHAR (NL)						
279	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	12/2021	644.38	9
280	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
281	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	21
282	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
283	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
284	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC	ECR	04/2009	03/2020	12/2024	548	57
285	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798	57
286	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	03/2030	151.84	133
287	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	06/2022	569.63	27
288	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
289	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
290	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
291	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
292	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
293	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
294	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
295	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
296	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	48
297	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
298	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
299	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
300	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180
301	TARAKESWAR - BISHNUPUR NEW BG LINE	ER	04/2000	03/2019	03/2025	1188.91	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	(NL), ER						
302	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
303	RAMGANJMUHDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.6	36
304	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
305	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2022	133.41	165
306	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
307	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI- THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
308	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2024	2393.47	120
309	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	168
310	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
311	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
312	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
313	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	12/2021	668.7	21
314	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
315	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2026	2499.71	48
316	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
317	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
318	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
319	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
320	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	12
321	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
322	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
323	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	03/2022	969.83	24
324	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
325	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
326	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
327	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	39
328	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
329	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	21
330	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
331	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
332	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
333	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
334	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
335	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12
336	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2023	2478.23	15
337	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	12
338	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
339	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	03/2025	5200	60
340	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
341	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
342	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
343	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
344	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288	18
345	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
346	NIMACH BADI SADRI NEW LINE PROJECT	WR	04/2017	03/2022	03/2024	495.18	24
347	JHANSI BINA DOUBLING	NCR	09/2016	03/2021	12/2023	2001	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
348	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	NCR	03/2018	03/2023	06/2025	4329.53	27
349	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
350	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	NHAI	03/2019	05/2020	05/2022	1047	24
351	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	NHIDCL	11/2017	11/2017	12/2021	290.05	49
352	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MoRTH	06/2017	06/2019	12/2021	282.08	30
353	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	MoRTH	05/2018	05/2020	12/2021	248	19
354	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
355	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	12/2021	162.56	45
356	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	12/2021	166.21	40
357	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MoRTH	03/2016	11/2018	03/2022	271.17	40
358	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	04/2022	169.63	49
359	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MoRTH	01/2017	09/2019	10/2021	396.86	25
360	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	01/2022	426.18	16
361	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	12/2021	184.62	46
362	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	11/2022	160.27	39
363	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	MoRTH	11/2017	11/2019	10/2021	237.8	23
364	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	03/2022	829	74
365	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	NHIDCL	03/2018	07/2018	07/2022	1383.78	48
366	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
367	WIDENING AND UP-GRADATION TO 2-LANE	NHIDCL	04/2017	09/2019	07/2023	640.07	46

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO						
368	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
369	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
370	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
371	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
372	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
373	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	09/2023	428.11	48
374	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	MORTH	10/2016	08/2020	11/2021	171.9	15
375	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	12/2021	186.96	87
376	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	MORTH	01/2017	01/2021	11/2021	205.95	10
377	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MORTH	01/2019	03/2021	03/2022	264.5	12
378	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MORTH	03/2018	04/2020	03/2022	263.89	23
379	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J	MORTH	03/2018	08/2020	12/2021	288.3	16
380	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	MORTH	03/2016	09/2020	11/2021	296.5	14
381	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MORTH	01/2016	08/2016	06/2022	497.14	70
382	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	12/2021	193.69	134
383	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	12/2021	641.17	65
384	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
385	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	07/2022	1176.37	59
386	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	11/2021	990.61	50
387	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	07/2022	1227.87	58
388	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	03/2022	454.89	46
389	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
390	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
391	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	NHIDCL	03/2015	11/2018	11/2021	168.39	36
392	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	02/2022	588.95	39
393	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	MoRTH	01/2014	03/2016	04/2022	282.41	73
394	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MoRTH	11/2010	05/2017	05/2022	268.08	60
395	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	NHIDCL	12/2015	12/2018	12/2021	289.99	36
396	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	11/2021	628.45	22
397	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	11/2021	957.54	21
398	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	12/2022	511.83	64
399	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	03/2022	294.17	74
400	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	03/2022	252	74
401	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	MoRTH	03/2020	03/2021	04/2022	207.79	13
402	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	MoRTH	06/2020	05/2021	12/2022	221.4	19
403	REHABILITATION AND UPGRADE TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	MoRTH	08/2020	03/2021	03/2023	222.61	24
404	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	02/2022	374	105
405	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	01/2022	624	93
406	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2022	1724.55	108
407	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
408	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	11/2021	1078.84	99
409	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2023	998.79	118
410	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2021	1928.22	80
411	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	12/2021	822.9	44
412	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	05/2023	563.92	65

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
413	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	46
414	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	03/2022	593.26	46
415	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	06/2022	649.5	39
416	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	10/2021	1423.96	35
417	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36
418	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	01/2022	707.82	41
419	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	10/2022	899	42
420	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	12/2021	641.17	41
421	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
422	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
423	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	10/2021	804.97	40
424	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
425	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
426	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
427	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	NHIDCL	03/2018	09/2018	11/2021	237.72	38
428	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	NHIDCL	03/2018	09/2018	11/2021	251.97	38
429	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	NHIDCL	03/2018	09/2018	11/2021	282.98	38
430	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	11/2021	215.12	38
431	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
432	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
433	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2022	284.09	59
434	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	NHIDCL	02/2017	04/2017	03/2022	195.23	59
435	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN	NHIDCL	02/2017	04/2017	03/2022	203.36	59

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM. 34.000 TO KM. 51.825 [EXIST						
436	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	03/2022	198.22	59
437	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	03/2022	894	23
438	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	05/2018	03/2022	274.31	46
439	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	06/2018	03/2022	403.36	45
440	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	05/2018	03/2022	417.24	46
441	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	10/2018	01/2022	262.97	39
442	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	12/2022	1167.42	45
443	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2022	605.84	43
444	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	12/2021	848.45	21
445	FOUR LANNING OF JHANSI-KHAJURAHO SECTION (PKG-I) FROM KM 0.00 TO KM 76.3 (EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	12/2021	1373.28	21
446	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	09/2022	754.54	30
447	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	NHIDCL	03/2017	12/2017	03/2022	409.85	51
448	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	NHIDCL	03/2015	04/2017	10/2021	277.17	54
449	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	10/2018	03/2022	391	41
450	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	NHIDCL	03/2018	10/2018	03/2022	234.27	41
451	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	NHIDCL	02/2017	09/2018	03/2022	387	42
452	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
453	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
454	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
455	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MORTH	11/2015	06/2017	12/2021	335.32	54
456	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MORTH	01/2016	09/2016	12/2021	476.2	63
457	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	12/2021	624.98	62

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
458	REHABILITATION AND UPGRADE OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	12/2022	452.94	77
459	REHABILITATION AND UPGRADE OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION	MoRTH	03/2017	01/2018	12/2021	423.79	47
460	REHABILITATION AND UPGRADE OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	03/2022	496.02	84
461	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	12/2021	188.8	31
462	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	11/2021	379.16	48
463	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	08/2022	236.78	36
464	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	12/2021	205.05	57
465	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2022	214.69	51
466	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	12/2021	217.22	40
467	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	12/2021	233.04	45
468	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	12/2021	249.05	41
469	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2022	254.17	49
470	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	11/2021	279.44	44
471	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	12/2021	373.82	27
472	REHABILITATION AND UPGRADE OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	12/2021	809.16	41
473	REHABILITATION AND UPGRADE OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	12/2021	877.79	30
474	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	NHIDCL	03/2019	05/2019	03/2022	306.28	34
475	REHABILITATION AND UPGRADE OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	MoRTH	03/2016	12/2019	12/2021	536.65	24
476	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	12/2021	392.33	45
477	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25
478	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
479	REBUILDING OF COKE OVEN BATTERY NO-8	SAIL	11/2016	06/2019	12/2021	262.87	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AT BSL						
480	FORGED WHEEL PLANT	RINL	04/2014	09/2018	11/2021	1682.85	38
481	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	11/2022	1034.01	61
482	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	07/2022	2858	55
483	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	01/2022	15525	80

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
484	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD FOR TELECOM	10/2014	03/2018	12/2021	248.2	45
485	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	13334	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
486	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNITY)	CPWD	05/2019	09/2020	01/2023	299.97	28
487	KANPUR METRO RAIL PROJECT	LMRCL	05/2019	03/2024	03/2025	11076.48	12
488	AGRA METRO RAIL PROJECT	LMRCL	05/2019	03/2024	05/2025	8379.62	14
489	BANGALORE METRO RAIL PROJECT PHASE-2	BMRC	02/2014	02/2019	03/2025	26405.14	73
490	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	02/2022	197.33	34
491	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2021	8680	45
492	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	23136	36
493	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	CPWD	11/2017	05/2020	11/2021	238.56	18
494	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	CPWD	10/2016	03/2021	06/2023	422	27
495	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	06/2022	392	22
496	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	12/2022	11420	13
497	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44
498	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	CPWD	10/2016	03/2022	06/2023	1128	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
499	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	06/2023	1180	23

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
500	INTERCEPTION AND DIVERSION WITH STP AT HUGHLI-CHINSURAH	KMDA	05/2018	02/2022	10/2022	160	8
501	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	06/2022	298.12	11
502	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
503	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	BPB	03/2017	12/2019	12/2021	233.57	24
504	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
505	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12

FLASH REPORT

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(OCTOBER 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	1383	1983	600

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
10	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
11	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	6964.33	7254.37	290.04
12	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	479.53	708.55	229.02
13	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	UNITES OF HIGHER EDUCATION	09/2013	09/2014	484.32	626.26	141.94

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC FOR DPIIT	09/2011	09/2019	12579.09	13812.3	1233.21
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	4773	5178	405

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
17	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	414.11	586.5	172.39
18	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD FOR HEALTH	03/2019	09/2025	1577	1828	251
19	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	1351	1471	120

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3727.3	2009.3

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MH	10/2013	10/2019	1219.21	2000	780.79
22	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD FOR MH	12/2008	12/2013	114.26	266	151.74

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
23	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94
24	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
25	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
26	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
27	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
28	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395
29	DEVANGONTHI MARKETING TERMINAL	MANGALORE RE	06/2020	06/2023	200	304	104
30	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINERY	NRL	01/2019	10/2024	12366	18968	6602
31	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
32	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
33	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	206.63	340.76	134.13
34	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
35	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
36	ENMORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
37	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
38	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
39	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	2001.34	1139.55
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
40	LOKTAK D/S HEP(NHPC)	NHPC	12/1999	06/2006	578.62	1311.05	732.43
41	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
42	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978
43	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	529.68	633.8	104.12
44	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	1885.13	2311.89	426.76
45	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
46	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10997.7	398.72
47	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
48	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
49	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4825.6	3168.6
50	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
51	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
52	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213
53	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15389.42	1022.84
54	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
55	EASTERN REGION STRENGTHENING SCHEME- XVIII	PGCIL	03/2017	07/2020	3500	3994	494
56	NORTH EASTERN REGION POWER SYSTEM	PGCIL	12/2014	12/2018	5111.33	6700	1588.67

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES						
57	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
58	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
59	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
60	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
61	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3630	2596.93
62	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
63	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
64	RAMGANJ MUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
65	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	433	299.59
66	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	1160.48	1373.74	213.26
67	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
68	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
69	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5521.45	3127.98
70	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
71	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	3150	2567.17
72	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2950	2225.31
73	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
74	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
75	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
76	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
77	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
78	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
79	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35
80	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
81	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	986.3	1530.09	543.79
82	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	2161.36	360.35
83	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	325	140.94
84	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1043	657.8
85	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
86	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12264.15	7809.98
87	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
88	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	4541.38	3361.19
89	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
90	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1080	755.27
91	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
92	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
93	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1968	811.06
94	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
95	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
96	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1886.76	1057.02
97	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1720	1416.02
98	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	1382.78	1960	577.22
99	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	2315	5174.3	2859.3
100	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
101	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
102	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
103	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
104	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
105	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
106	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
107	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1383.69	346.54
108	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23
109	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
110	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
111	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	242.28	122.55
112	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3176.6	1268.09
113	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
114	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	2478.23	2875.12	396.89
115	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
116	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
117	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05
118	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96
119	VIZIANAGARAM -SAMBALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
120	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2900	2186.52
121	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	22716.11	6500.11
122	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
123	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
124	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1339	339
125	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
126	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	1167	564.73
127	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
128	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
129	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
130	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
131	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
132	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
133	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
134	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.49	688.49
135	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
136	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	1763.93	2449	685.07
137	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	1295.42	1824	528.58
138	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
139	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
140	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13
141	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
142	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
143	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
144	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
145	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
146	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1090.6	271.37
147	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	750	335.16
148	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
149	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
150	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
151	ERNAKULAM-KUMBALAM	SR	04/2010	N.A.	189.24	448.1	258.86
152	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	931.98	1122	190.02
153	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	608.13	443.72
154	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.23	314.66
155	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37
156	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
157	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	709.69	456.73
158	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	749.4	479.26
159	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1205	681.48
160	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
161	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51
162	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
163	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
164	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
165	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
166	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
167	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
168	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1650	674.38

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
169	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	1640.04	1873.1	233.06
170	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	1347.26	1524.68	177.42
171	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
172	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	610	315
173	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
174	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
175	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
176	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
177	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
178	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1878	263.41
179	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	760	182
180	AJMER(NASIRABAD)-SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	2215.27	1341.56
181	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
182	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1104	243.57
183	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
184	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
185	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	839	214
186	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
187	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
188	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
189	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
190	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
191	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
192	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	800	197.5
193	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
194	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
195	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	150	341.66	191.66
196	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	760	1536	776
197	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
198	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
199	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	WR	03/2012	N.A.	248.26	528.49	280.23
200	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	WR	03/2012	N.A.	217.38	393.62	176.24
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
202	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
203	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
204	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2017.96	1567.96
205	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
206	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
207	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6647.64	4321.12
208	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
209	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4794.6	2523.1
210	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
211	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
212	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
213	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
214	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
215	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2404.03	341.73
216	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
217	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
218	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
219	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
220	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1387.52	594.63
221	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	3168.29	3445.48	277.19
222	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	6171.08	2667.39
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
224	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
225	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
ROAD TRANSPORT AND HIGHWAYS					Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
226	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	612.58	332.58
227	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
228	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
229	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	624.41	992.67	368.26
230	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
231	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
232	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	193.69	327.92	134.23
233	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	624.98	731.5	106.52
234	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
235	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
236	CONSTRUCTION OF A NEW 2-LANE HIGHWAY	MoRTH	08/2010	09/2014	186.96	322.24	135.28

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD						
237	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
238	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
239	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	NHAI	03/2018	N.A.	795.5	922.64	127.14
240	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	925.96	291.26
241	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
242	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1296.93	130.67
243	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
244	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
245	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
246	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
247	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
248	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
249	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
250	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
251	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
252	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
253	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1361	308.79
254	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
255	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
256	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
257	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
258	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
259	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
260	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	N.A.	1251.11	1361	109.89
261	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
262	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
263	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
264	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	1588.29	199.95
265	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
266	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
267	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
268	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
269	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
270	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	726.67	1096.52	369.85
271	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
272	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15
273	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	593.26	716.78	123.52
274	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	744.73	213.6
275	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
276	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
277	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
278	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
279	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
280	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
281	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
282	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
283	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
284	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415
285	FORGED WHEEL PLANT	RINL	04/2014	09/2018	1682.85	2100	417.15
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
286	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
287	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	26405.14	30695.12	4289.98
288	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	18380	3780
289	PATNA METRO RAIL CORPORATION LIMITED	PATNA METRO	02/2019	06/2024	13365.77	13925.5	559.73
290	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	23136	33406	10270
291	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
292	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
293	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83
294	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	254.13	413.29	159.16
295	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	225.77	398.9	173.13

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	1,1459.00	1,6580.00	5121	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2022	346.27	480.33	134.06	15
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2022	417.23	707.73	290.5	45
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383.00	1983.00	600	27

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84
9	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2028	6964.33	7254.37	290.04	188
10	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
11	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	708.55	229.02	132

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	05/2022	4773.00	5178.00	405	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	06/2022	1351.00	1471.00	120	9

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
14	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	03/2022	1219.21	2000.00	780.79	29

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFIN	06/2020	06/2023	01/2024	200.00	304.00	104	7
16	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
17	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677.00	3072.00	395	13
18	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497.00	6025.00	1528	38
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	3375.90	185.21	49
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	5909.00	2994	110
21	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	09/2022	607.06	1236.00	628.94	59
22	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	03/2022	1823.00	3027.90	1204.9	12
23	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321.00	3338.00	1017	15
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2022	861.79	2001.34	1139.55	108
25	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66
26	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
27	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

515

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
28	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	340.76	134.13	29

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	02/2022	529.68	633.80	104.12	39
30	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	2,1312.11	12619.1	141
31	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	11/2021	5353.00	1,0566.00	5213	112
32	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	02/2022	3500.00	3994.00	494	19
33	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	02/2022	1,2964.60	1,7304.00	4339.4	45
34	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	9897.59	5978	162
35	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
36	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	1,1130.19	1,4719.10	3588.91	108
37	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	09/2024	2978.48	5867.38	2888.9	138
38	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2023	1,4366.58	1,5389.42	1022.84	51
39	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2024	2491.58	3860.35	1368.77	138
40	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657.00	4825.60	3168.6	88
41	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10/2022	1,0598.98	1,0997.70	398.72	23
42	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	03/2022	5111.33	6700.00	1588.67	39
43	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

516

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	TRANSMISSION AND DISTRIBUTION SYSTEM IN A P								
44	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	12/2021	1885.13	2311.89	426.76	36
45	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	947.89	299.56	6

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
46	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288.00	4970.11	2682.11	18
47	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	03/2022	969.83	1312.96	343.13	24
48	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
49	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	1400.00	472.99	39
50	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	2900.00	2186.52	21
51	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
52	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
53	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
54	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
55	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
56	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	1383.69	346.54	21
57	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
58	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
59	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-	ECR	04/2009	03/2020	12/2024	548.00	819.01	271.01	57

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

517

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	BARDIBAS(NEPAL) GC								
60	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798.00	2042.51	244.51	57
61	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	03/2030	151.84	527.37	375.53	133
62	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	06/2022	569.63	742.00	172.37	27
63	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
64	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
65	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1043.00	657.8	48
66	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60
67	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	6647.64	4321.12	132
68	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	8600.00	7260.52	96
69	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	860.41	450.33	40
70	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450.00	2017.96	1567.96	148
71	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
72	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
73	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
74	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180
75	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
76	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

518

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
77	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.60	2909.99	2485.39	36
78	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
79	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2022	133.41	433.00	299.59	165
80	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
81	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	2950.00	2225.31	73
82	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2024	2393.47	5521.45	3127.98	120
83	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	1373.74	213.26	168
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
85	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	6171.08	2667.39	12
86	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1387.52	594.63	24
87	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
88	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.30	1530.09	543.79	129
89	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	02/2022	704.31	927.94	223.63	23
90	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
91	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4794.60	2523.1	24
92	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	06/2022	495.44	2980.41	2484.97	219
93	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

519

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
94	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1080.00	755.27	128
95	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	11/2021	1180.19	4541.38	3361.19	155
96	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	3791.66	868.53	204
97	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,2264.15	7809.98	153
98	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	07/2022	495.74	734.01	238.27	109
99	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
100	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	03/2002	03/2024	1382.78	1960.00	577.22	264
101	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2025	303.98	1720.00	1416.02	60
102	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	1886.76	1057.02	48
103	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
104	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
105	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	1968.00	811.06	36
106	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600.00	701.81	101.81	31
107	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	12/2021	578.00	760.00	182	21
108	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	1878.00	263.41	60
109	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	12/2021	678.54	929.86	251.32	33
110	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	610.00	315	37
111	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	1524.68	177.42	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

520

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
112	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	1873.10	233.06	36
113	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	12/2021	644.38	872.65	228.27	9
114	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48
115	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
116	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
117	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
118	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	2449.00	685.07	48
119	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
120	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
121	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
122	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	1873.21	1002.25	12
123	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2023	2478.23	2875.12	396.89	15
124	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	1247.64	665.51	12
125	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3176.60	1268.09	9
126	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34
127	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	06/2022	760.00	1536.00	776	27
128	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150.00	341.66	191.66	66

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

521

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
129	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
130	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	1185.73	454.09	36
131	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
132	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
133	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	12/2021	624.98	731.50	106.52	62
134	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2022	605.84	722.46	116.62	43
135	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	744.73	213.6	46
136	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	03/2022	593.26	716.78	123.52	46
137	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	12/2021	186.96	322.24	135.28	87
138	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	05/2022	268.08	390.73	122.65	60
139	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	12/2021	193.69	327.92	134.23	134
140	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
141	FORGED WHEEL PLANT	RINL	04/2014	09/2018	11/2021	1682.85	2100.00	417.15	38
142	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	01/2022	1,5525.00	2,1940.00	6415	80

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

522

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2021)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
143	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	1,3334.00	2,4664.00	11330	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
144	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2787.00	2014	44
145	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	2,3136.00	3,3406.00	10270	36
146	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2025	2,6405.14	3,0695.12	4289.98	73

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
147	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

FLASH REPORT

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00	166.90	05/2013	02/2022	-55.37	105
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00	364.59	12/2009	09/2020	-39.64	129
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36	469.31	01/2014	-	61.08	0
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00	475.00	05/2013	-	46.15	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00	485.00	08/2013	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00	486.00	05/2010	-	.00	0
7	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00	516.00	07/2008	-	.00	0
8	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	06/2020	.00	46
9	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	-	.00	0
10	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	-	.00	0
11	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	-	.00	0
12	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	591.00	11/2013	-	15.53	0
13	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	-	.00	0
14	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	01/2022	.00	93
15	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	09/2019	.00	3
16	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - PPP BOT (Hybrid Annuity) - [N24001340]	11/2019	716.00	716.00	07/2021	-	.00	0
18	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	-	.00	0
19	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	-	.00	0
20	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	12/2021	.00	44
21	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	-	.00	0
22	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
23	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	-	.00	0
24	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2023	.00	118
25	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	-	.00	0
26	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	11/2021	.00	99
27	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	10/2020	.00	76
28	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	-	.00	0
29	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
30	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88	1,226.88	02/2021	-	.00	0
31	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
32	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
33	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	-	.00	0
34	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
35	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
37	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
38	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0
39	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
40	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10	1,601.10	02/2021	-	.00	0
41	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
42	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
43	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
44	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
45	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	03/2022	.00	108
46	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
47	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
48	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	12/2021	.00	80
49	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
50	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
51	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	09/2021	.00	29
52	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0
53	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	-	106.50	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	2,360.65	-	-	41.78	0
55	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (October 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
57	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		68,482.89 -	72,035.06				
	Grand Total		68,482.89	72,035.06				

FLASH REPORT

List of projects original without Date of Commissioning

Costing Rs.		150 Crore and above				(October 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>COAL</u> <u>Singareni Colliers Company Limited</u>								
	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75	-			2/6
2	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u>								
	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	541.38	-	10/2021	-	0/0
	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	591.68	-	10/2021	-	0/0
4	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	176.66	-	11/2021	-	0/0
5	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	487.74	-	12/2021	-	0/0
	Total		1,992.56	2,026.34	1,797.46				0/0
6	<u>RAILWAYS</u> <u>East Central Railways</u>								
	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56	1,858.75	386.36	-	03/2023	-	0/0
	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 1,470.50	1,470.50	1,436.01	-	03/2023	-	0/0
8	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 614.45	614.45	352.46	-	12/2023	-	0/0
9	BIHTA-AURANGABAD (NL) - [N22000170]ECR, BIHAR	04/2008	326.20	2,995.01	2.04	-	03/2024	-	0/0
10	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
11	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR	05/2015	380.00	519.33	309.90	-	03/2025	-	0/0
12	<u>Eastern Railways</u>								
	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80	495.10	313.03	-	03/2022	-	0/0
	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64	272.20	299.01	-	03/2022	-	0/0
14	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93	310.70	383.74	-	03/2024	-	0/0

Costing Rs.		150 Crore and above				(October 2021)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0
16	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.77	-	03/2025	-	0/0
17	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
18	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	250.55	20.11	-	03/2025	-	0/0
19	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
20	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	36.13	-	03/2025	-	0/0
21	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	40.65	-	03/2025	-	0/0
22	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
Metropolitan Rapid Transport Projects									
23	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
North Eastern Railway									
24	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50	800.00	128.90	-	12/2023	-	0/0
Northern Railway									
25	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	791.39	597.99	-	09/2023	-	0/0
26	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	419.00	160.79	-	09/2023	-	0/0
27	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65	359.00	116.87	-	03/2024	-	0/0
28	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	841.90	1.73	-	03/2024	-	0/0
29	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00	489.64	105.51	-	03/2023	-	0/0
South Eastern Railway									
30	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37	620.00	41.78	-	03/2025	-	0/0
South Western Railway									
31	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01	2,161.36	82.47	-	12/2023	-	0/0

Costing Rs.		150	Crore and above			(October 2021)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
32	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	692.43	-	-	12/2023	-	0/0
33	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	466.65	-	-	12/2023	-	0/0
34	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	367.77	-	-	12/2023	-	0/0
35	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	5,174.30	158.11	-	12/2024	-	0/0
36	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30	2,404.03	1,087.98	-	12/2025	-	2/2
37	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85	348.85	.36	-	12/2025	-	0/0
	<u>Southern Railway</u>								
38	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52	1,205.00	2.28	-	03/2024	-	0/0
39	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90	1,431.90	492.74	-	03/2024	-	0/0
40	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96	709.69	8.50	-	03/2025	-	0/0
41	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24	448.10	6.73	-	03/2025	-	0/0
42	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00	1,339.00	.82	-	03/2025	-	0/0
43	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	3,150.00	239.53	-	12/2025	-	0/0
44	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40	227.40	65.02	-	03/2030	-	0/0
45	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00	839.01	.63	-	03/2030	-	0/0
46	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57	603.23	1.63	-	03/2030	-	0/0
	Total		21,655.76	38,198.42	6,966.35				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
47	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59	306.59	195.15	-	11/2021	-	0/0
48	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	123.44	-	12/2021	-	0/0
49	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45	319.96	115.07	-	03/2022	-	0/0

Costing Rs.		150		Crore and above		(October 2021)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
50	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50	210.50	145.76	-	10/2021	-	4/4
51	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01	520.01	199.64	-	12/2021	-	3/4
52	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51	1,049.51	155.61	-	12/2021	-	2/4
53	FOUR LANING OF BALACHERA-HARAGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00	818.00	215.66	-	03/2023	-	1/4
	<u>National Highways Authority Of India</u>								
54	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04	825.17	799.07	-	10/2021	-	2/4
55	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00	1,959.00	1,314.63	-	10/2021	-	0/0
56	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34	2,400.00	3,378.36	-	11/2021	-	0/0
57	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76	207.00	205.00	-	11/2021	-	0/0
58	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47	1,296.00	-	-	11/2021	-	0/0
59	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84	1,117.84	-	-	12/2021	-	0/0
60	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96	2,169.00	-	-	12/2021	-	0/0
61	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88	743.89	429.00	-	12/2021	-	1/3
62	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26	1,296.93	346.17	-	01/2022	-	0/0

Costing Rs.			150 Crore and above			(October 2021)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92	1,071.00	309.05	-	01/2022	-	0/0
64	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21	289.21	224.45	-	01/2022	-	0/0
65	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53	291.53	220.18	-	02/2022	-	0/0
66	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97	1,094.97	827.00	-	02/2022	-	2/4
67	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00	479.00	456.80	-	03/2022	-	0/0
68	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28	752.28	281.06	-	03/2022	-	0/1
69	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95	1,031.95	1,505.00	-	03/2022	-	0/0
70	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27	950.27	282.63	-	03/2022	-	3/4
71	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09	953.09	468.85	-	03/2022	-	0/0
72	FOUR LANING OF MADURAI-CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71	628.71	382.61	-	03/2022	-	0/0
73	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43	314.43	85.61	-	06/2022	-	0/0
74	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96	884.00	486.00	-	10/2022	-	2/4
75	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98	840.00	297.00	-	11/2022	-	2/4

Costing Rs. 150 Crore and above (October 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
76	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI, TAMIL NADU Total <u>URBAN DEVELOPMENT</u> <u>National Building Construcion Corporation Ltd</u>	03/2018	505.35 - 24,114.25 -	505.35 25,652.18	255.05 13,703.85	- -	12/2022	-	0/0 22/40
77	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI Total	07/2016	2,694.00 - 2,694.00 -	2,694.00 2,694.00	896.32 896.32	- -	12/2022	-	0/9 0/9
	Grand Total		50,729.30	68,843.67	23,517.73				26/57

FLASH REPORT

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above				(October 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Mahanadi Coal Fields Limited</u>				
2	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	03/2021
	<u>Neyveli Lignite Corporation</u>				
3	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
9	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	09/2021
	Total		14,560.71 -		
	<u>FINANCE</u>				
	<u>Cpwd For Finance</u>				
10	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
	Total		209.00 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
11	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	11/2019 05/2021	-
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 05/2021	-
	Total		458.64 -		

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
13	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 12/2021	12/2020
14	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		700.62 -		
	<u>PETROLEUM</u>				
	<u>Indian Oil Corporation Limited</u>				
15	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021
16	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	08/2019 06/2021	05/2021
17	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	09/2021
18	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	09/2021
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
20	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,475.92	05/2021 05/2021	05/2021
21	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	03/2019 09/2021	09/2021
	Total		6,649.23 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
24	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
25	TALAIPELLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				
26	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
27	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	06/2021
28	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021
	Total		15,680.45 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
29	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-
	<u>Natrip Implementation Society</u>				
30	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 03/2021	03/2021
	Total		3,272.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
31	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
	<u>HII Infra Tech Services Limited</u>				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
33	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
34	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
35	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
36	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
37	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
38	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
39	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
40	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARAstra - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
41	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	-	01/2021
42	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	03/2021
43	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	03/2021

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
44	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021
45	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021
46	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
	Total		5,796.27 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
47	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-
48	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
49	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
50	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	-
51	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
52	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
53	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	-
54	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
55	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
56	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
57	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
58	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
59	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021
61	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	-
62	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
63	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
64	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
65	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
66	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
67	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
68	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
69	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
70	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
71	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
<u>Eastern Railways</u>					
72	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
73	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
<u>Kolkata Metro Rail Corporation Limited</u>					
74	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
<u>Metropolitan Rapid Transport Projects</u>					
75	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
76	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
77	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
78	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
<u>North East Frontier Railway</u>					
79	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
80	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
81	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
82	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
83	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
84	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
86	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-
87	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
88	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
89	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
90	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
91	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
92	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
93	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	420.18 -	03/2020 -	09/2021
94	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
95	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
96	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
97	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
98	ROHTAK-MEHAM HANSI - [N22000272]NR, HARYANA	04/2012	287.00 -	12/2011 -	06/2021
99	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR, MULTI STATE	03/2002	625.00 781.00	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
100	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES, TELANGANA	03/2015	636.38 -	03/2021 -	-
101	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES, CHHATISGARH	02/2016	393.98 -	03/2020 -	-
	<u>Railway Electrification</u>				
102	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
103	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	458.25 -	- -	-
104	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
105	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
106	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
107	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
108	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
109	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South Eastern Railway</u>				
110	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
111	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>South Western Railway</u>				
112	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021
	<u>Southern Railway</u>				
113	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021
114	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-
115	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
116	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 311.36	- -	-
117	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 393.62	- 12/2022	-
118	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 528.49	- 12/2022	-
119	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 154.15	- 12/2021	-
	Total		85,198.70 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
120	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	09/2021
121	REHABILITATION AND UPGRADEATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
122	REHABILITATION AND UPGRADEATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
123	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
124	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
125	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 10/2020	10/2020
126	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2020	12/2020
127	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021
128	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
129	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
130	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 03/2020	03/2021
131	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021
132	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	04/2021
133	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021
134	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 06/2021	06/2021
135	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021
136	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021
137	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021
138	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021
139	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021
140	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
141	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 12/2021	07/2021
142	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021
143	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021
144	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021
145	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021
146	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021
147	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
148	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	02/2017 -	-
149	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
150	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
151	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
152	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
153	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
154	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
155	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
156	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
157	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
158	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 12/2021	-
159	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 273.27	08/2015 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
160	REHABILITATION AND UPGRADE OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
161	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
162	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-
163	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
164	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
165	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
166	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
167	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUARI - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
168	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
169	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
170	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADE TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-
171	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADE TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
172	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADE TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
173	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-
174	4-LANING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
175	4-LANING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
176	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
177	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
178	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
179	REHABILITATION AND UPGADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
180	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-
181	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
182	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	-
183	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
184	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
185	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
186	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
187	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
188	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
189	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
190	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
191	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
192	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
193	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
194	REHABILITATION AND UPGADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 10/2021	-
195	REHABILITATION AND UPGADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	05/2017 10/2021	-
196	REHABILITATION AND UPGADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 02/2022	-
197	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 01/2022	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
198	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 12/2021	-
199	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 274.73	08/2018 11/2021	-
200	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 556.13	11/2018 07/2021	-
201	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	05/2016 09/2021	-
202	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
203	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
204	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
205	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
206	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
207	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 381.75	08/2018 10/2021	-
208	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 12/2021	-
209	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 11/2021	-
210	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 08/2021	-
211	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 12/2021	-
212	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 381.75	09/2017 05/2022	-
213	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 596.38	01/2018 04/2022	-
214	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
215	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
216	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH, TELANGANA	01/2017	244.54 -	05/2019 -	-
217	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH, TELANGANA	01/2017	196.52 -	10/2019 -	-
218	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH, TELANGANA	01/2017	283.00 -	12/2019 -	-
219	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH, TELANGANA	01/2017	359.27 -	05/2019 -	-
220	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH, TELANGANA	01/2017	300.00 -	05/2019 -	-
221	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH, TELANGANA	01/2018	283.15 -	05/2020 -	-
222	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH, TELANGANA	01/2018	230.03 -	12/2019 -	-
223	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA	02/2018	206.13 -	06/2020 -	-
224	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA	02/2018	294.13 -	11/2019 -	-
225	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA	02/2018	220.28 -	11/2019 -	-
226	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA	02/2018	426.52 -	04/2020 -	-
227	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA	03/2018	322.81 -	09/2020 -	-
228	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA	03/2018	626.76 -	07/2020 -	-
229	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA	01/2017	605.08 -	10/2019 -	-
230	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA	03/2018	192.67 -	07/2019 -	-
231	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA	01/2019	193.19 -	- -	-
232	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH, BIHAR	03/2018	153.24 -	- -	-
233	SARSAM TO KOTHARI - [N24001002]MoRTH, MAHARASHTRA	02/2016	545.64 -	07/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
234	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
235	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
236	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
237	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
238	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
239	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
240	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
241	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
242	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
243	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
244	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
245	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
246	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
247	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
248	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
249	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
250	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
251	AMD TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
252	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
253	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
254	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
255	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
256	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
257	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
258	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
259	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
260	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
261	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
262	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
263	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
264	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
265	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
266	KAJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
267	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
268	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
269	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
270	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
271	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
272	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
273	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
274	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
275	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
276	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
277	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
278	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
279	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
280	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
281	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
282	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
283	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
284	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
285	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
286	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
287	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
288	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
289	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
290	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
291	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
292	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
293	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
294	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
295	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
296	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
297	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
298	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
299	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
300	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
301	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
302	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
303	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
304	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
305	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
306	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
307	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
308	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
309	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
310	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
311	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
312	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
313	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
314	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
315	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
316	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
317	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
318	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
319	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
320	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
321	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
322	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
323	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
324	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
325	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
326	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
327	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
328	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
329	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
330	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
331	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
332	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
333	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
334	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
335	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
336	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
337	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
338	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
339	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
340	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
341	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	-
342	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
343	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
344	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
345	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
346	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
347	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
348	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
349	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
350	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
351	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
352	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
353	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
354	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
355	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
356	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	06/2021 -	-
357	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
358	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
359	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
360	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
361	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
362	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
363	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
364	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
365	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
366	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
367	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
368	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
369	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
370	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
371	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
372	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
373	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
374	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
375	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
376	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
377	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
378	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-
379	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	-
380	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	-
381	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-
382	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 08/2021	-
383	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
384	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
385	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
386	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 204.73	06/2019 -	-
387	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
388	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
389	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
390	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
391	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
392	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
393	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
394	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
395	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
396	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
397	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
398	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
399	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	-
400	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	-
401	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
402	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
403	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
404	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
405	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-
406	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	-
407	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
408	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 12/2021	-
409	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
410	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
411	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
412	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
413	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	03/2021

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
414	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
415	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
416	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- 09/2021	09/2021
417	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
418	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
419	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
420	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
421	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
422	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
423	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
<u>National Highways Authority Of India</u>					
424	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- 12/2016	05/2017
425	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- 02/2018	02/2018
426	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- 02/2018	02/2018
427	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018
428	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
429	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
430	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
431	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
432	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020
433	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
434	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
435	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
436	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
437	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
438	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
439	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
440	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
441	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
442	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI, TAMIL NADU	12/2017	379.90 -	- -	03/2021
443	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
444	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	04/2021
445	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	05/2021
446	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	06/2021
447	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- 10/2021	07/2021
448	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- 01/2022	07/2021
449	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI, ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 07/2021	07/2021
450	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	- -	07/2021
451	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021
452	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA	01/2018	607.00 -	- -	08/2021

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
453	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021
454	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021
455	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021
456	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 1,201.51	- 06/2021	09/2021
457	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021
458	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.24	- 05/2021	09/2021
459	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021
460	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
461	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
462	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
463	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
464	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
465	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
466	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
467	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
468	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-
469	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
470	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
471	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
472	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
473	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
474	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
475	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
476	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
477	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
478	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
479	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
480	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
481	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
482	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
483	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
484	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 12/2021	-
485	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
486	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
487	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
488	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
489	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
490	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
491	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
492	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
493	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
494	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
495	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
496	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
497	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
498	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
499	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
500	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
501	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
502	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
503	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
504	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
505	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 363.93	- -	-
506	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
507	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
508	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
509	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
510	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
511	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-
512	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
513	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
514	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
515	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
516	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
517	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	-
518	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
519	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
520	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
521	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
522	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
523	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
524	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
525	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
526	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
527	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
528	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
529	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	-
530	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
531	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
532	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
533	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
534	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
535	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 1,096.52	04/2018 -	-
536	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
537	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
538	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
539	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
540	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
541	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
542	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
543	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
544	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
545	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
546	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
547	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
548	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
549	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
550	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- 10/2022	-
551	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
552	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-
553	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
554	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-
555	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-
556	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-
557	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
558	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	-
559	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-
560	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-
561	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-
562	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
563	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-
564	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
565	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
566	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	-
567	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 1,367.00	- -	-
568	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL- SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
569	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
570	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
571	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
572	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-
573	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
574	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-
575	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
576	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
577	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
578	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
579	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
580	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
581	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
582	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
583	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
584	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
585	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 1,361.00	- 01/2019	-
586	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-
587	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
588	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
589	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
590	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
591	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
592	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
593	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
594	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
595	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
596	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	-
597	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
598	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	03/2020 -	-
599	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
600	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	-
601	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	-
602	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	-
603	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	07/2017 -	-
604	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	-
605	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
606	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI, RAJASTHAN	10/2017	964.17 -	10/2017 -	-
607	4-LANNING OF THALSERRY-MAHE BYPASS - [N24000704]NHAI, KERALA	09/2017	1,124.11 -	09/2017 -	-
608	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI, MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
609	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
610	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
611	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
612	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-
613	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
614	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
615	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
616	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
617	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
618	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
619	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
620	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
621	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
622	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
623	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
624	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
625	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
626	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
627	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
628	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
629	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
630	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-
631	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141) - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-
632	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	- -	-
633	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 -	- -	-
634	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
635	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-
636	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-
637	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 -	- -	-
638	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI, KARNATAKA	02/2018	2,177.80 -	- -	-
639	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-
640	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI, UTTAR PRADESH	03/2018	809.07 -	- -	-
641	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI, UTTAR PRADESH	03/2018	925.40 -	- -	-
642	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	-
643	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
644	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- -	-
645	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	- -	-
646	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI, UTTAR PRADESH	03/2018	1,120.57 -	- -	-
647	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- 01/2019	-
648	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
649	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
650	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
651	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
652	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
653	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
654	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
655	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-
656	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
657	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
658	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
659	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
660	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
661	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
662	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
663	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
664	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
665	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
666	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
667	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
668	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
669	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-
670	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
671	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
672	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
673	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
674	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
675	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
676	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
677	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
678	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
679	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
680	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
681	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
682	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
683	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
684	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
685	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
686	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
687	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-
688	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
689	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 731.89	11/2019 -	-
690	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 362.46	11/2019 -	-
691	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 594.75	11/2019 -	-
692	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
693	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
694	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- 11/2021	-
	Total		3,69,774.65 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
695	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 18,380.00	12/2015 02/2019	02/2019
696	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	02/2021
	<u>Delhi Metro Rail Corporation</u>				
697	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
698	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
699	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 6,218.14	07/2017 09/2020	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
700	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019
	Total		69,629.79 -		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
701	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021
702	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
703	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021
704	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021
705	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
706	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	-
707	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-
708	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-
	<u>Delhi Jal Board</u>				
709	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021
710	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hscl For Water</u>				
711	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL FOR WATER,BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
712	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021
713	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	-
	<u>Uttar Pradesh Jal Nigam</u>				
714	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
715	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021
716	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021
717	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021
718	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021
	<u>Uttarakhand Pey Jal Nigam</u>				
719	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-
	Total		7,307.68 -		
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				
720	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 302.64	10/2020 -	-

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		302.64		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Cpwd Of Higher Education</u>				
721	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND	09/2012	171.86	03/2016	-
722	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23	10/2012	-
723	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN	12/2016	549.31	07/2019	-
724	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD EDUCATION,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020	-
725	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83	06/2020	-
726	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90	03/2020	-
727	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH	02/2019	655.34	06/2020	-
	<u>Rites Of Higher Education</u>				
728	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32	09/2014	-
	Total		2,709.79		
	<u>HOME AFFAIRS</u>				
	<u>Cpwd For Mha</u>				
729	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31	01/2022 02/2022	01/2020
730	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD FOR MHA,UTTARAKHAND	12/2008	114.26 266.00	12/2013	-
	Total		313.57		
	<u>RURAL DEVELOPMENT</u>				
	<u>Cpwd For Rural</u>				
731	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD FOR RURAL,DELHI	11/2018	361.60	07/2021	-
	Total		361.60		

Costing Rs. 150 Crore and above					(October 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>DPIIT</u>				
	<u>Dmic For Dpiit</u>				
732	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021
	Total		12,579.09 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
733	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	08/2021
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
734	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		5,95,927.66		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(October 2021)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Nuclear Power Corporation Of India Limited</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	17,298.00	12/2015 -	02/2022	74	-
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,709.00	12/2016 -	03/2023	75	-
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	25,603.00	11/2020 -	11/2023	36	-
	Total		63,628.00 -	73,508.00	56,610.00				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	402.00	390.15	06/2019 10/2021	11/2021	29	1
5	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI, ANDHRA PRADESH	08/2017	177.10 -	177.10	104.49	02/2020 12/2021	05/2022	27	5
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	303.80 351.21	303.80	189.25	04/2020 -	06/2022	26	-
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]AAI, MAHARASHTRA	03/2017	475.39 -	475.39	169.84	04/2021 -	08/2022	16	-
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI, UTTARAKHAND	07/2018	456.86 -	456.86	314.79	09/2020 -	09/2022	24	-
9	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT - [N04000075]AAI, TAMIL NADU	08/2018	951.28 -	951.28	477.10	10/2021 -	10/2022	12	-
10	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI, ARUNACHAL PRADESH	02/2019	645.63 -	645.63	-	08/2022 -	11/2022	3	-
11	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI, LADAKH	07/2018	346.27 -	480.33	114.59	09/2021 -	12/2022	15	-
12	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI, MADHYA PRADESH	06/2016	412.24 -	412.24	212.35	06/2021 -	12/2022	18	-
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI, ASSAM	12/2016	1,142.00 -	1,232.00	371.33	03/2021 03/2022	03/2023	24	12
14	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	1,405.00	368.21	08/2022 -	03/2023	7	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	728.99	02/2022 -	12/2023	22	-
16	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 1,938.00	1,983.00	534.84	09/2021 -	12/2023	27	-
17	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	229.22	10/2022 -	12/2023	14	-
	Total		11,820.75 -	12,608.53	4,205.15				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
18	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	285.81	05/2014 -	12/2021	91	-
19	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2022	12	-
20	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	24.86	04/2018 -	10/2022	54	-
21	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 341.22	341.22	73.17	03/2017 -	10/2022	67	-
22	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	501.39	04/2015 -	02/2023	94	-
23	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	69.37	04/2014 -	04/2023	108	-
	<u>Central Coal Fields Limited</u>								
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	124.85	03/2011 -	03/2022	132	-
25	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	497.97	03/2016 -	03/2022	72	-
26	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.46	03/2014 -	03/2022	96	-
	<u>Eastern Coal Fields Limited</u>								
27	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,146.48	622.22	08/2019 -	08/2024	60	-
28	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	690.16	03/2018 -	03/2029	132	-
	<u>Mahanadi Coal Fields Limited</u>								
29	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	708.55	729.73	03/2013 -	03/2024	132	-
30	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	240.64	03/2019 -	03/2024	60	-
31	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	659.30	03/2021 -	09/2025	54	-
32	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA	12/2007	3,145.45 -	3,145.45	637.17	03/2017 -	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
33	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	37.13	08/2022 -	09/2023	13	-
	<u>Northern Coal Fields Limited</u>								

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
34	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	825.70	03/2021 -	03/2022	12	-
35	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH <u>Singareni Colliers Company Limited</u>	11/2017	1,255.17 -	1,255.17	316.50	03/2022 -	03/2023	12	-
36	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84	-
37	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	293.69	03/2015 -	03/2022	84	-
38	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	135.30	07/2016 -	03/2022	68	-
39	KAKATIYAKHANI OPENCASST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	112.99	03/2019 -	03/2022	36	-
40	KAKATIYAKHANI OPENCASST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	206.41	03/2019 -	03/2022	36	-
41	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
42	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA <u>South-Eastern Coal Fields Limited</u>	07/2011	447.06 -	473.22	183.12	03/2015 -	03/2023	96	-
43	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	199.99	03/2015 03/2020	03/2022	84	24
44	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	127.49	03/2021 -	03/2022	12	-
45	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH	06/2010	11,816.40 -	11,816.40	4,639.30	03/2023 03/2016	03/2023	0	84
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	210.73	03/2014 -	03/2023	108	-
47	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	-
48	AMGAON OPENCASST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	146.27	03/2020 -	03/2023	36	-
49	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	66.57	03/2021 -	03/2024	36	-
50	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	231.92	1.78	03/2022 -	03/2025	36	-
51	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	08/2015	1,186.64 -	1,186.64	234.04	03/2023 -	03/2026	36	-
52	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	11.37	03/2014 -	03/2026	144	-
53	DURGAPUR OPENCASST PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	-
54	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2027	48	-
55	MADANNAGAR OPENCASST PROJECT - [N06000140]SECL,CHHATISGARH <u>Western Coal Fields Limited</u>	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	-
56	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 327.41	327.41	160.84	03/2019 -	03/2022	36	-
57	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	145.08	03/2023 -	03/2024	12	-

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		39,974.43 -	43,408.44	13,926.22				
	<u>FERTILISERS</u>								
	<u>National Fertiliser Limited</u>								
58	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	172.93	11/2019 06/2021	10/2021	23	4
	Total		215.92 -	215.92	172.93				
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
59	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	355.00	95.45	11/2020 -	12/2023	37	-
	Total		355.00 -	355.00	95.45				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (Sail)</u>								
60	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	207.19	06/2019 10/2021	12/2021	30	2
61	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	557.75	10/2017 12/2021	11/2022	61	11
	Total		1,296.88 -	1,296.88	764.94				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
62	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	206.26	155.99	03/2021 -	11/2021	8	-
63	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	769.00	06/2019 -	02/2022	32	-
64	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA	07/2020	640.00 -	640.00	357.57	12/2021 -	03/2022	3	-
65	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	248.55	136.91	06/2022 -	09/2022	3	-
66	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	242.18	02/2021 -	03/2023	25	-
67	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	283.87	08/2022 -	06/2023	10	-
	<u>Chennai Petroleum Corporation Limited</u>								
68	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	305.00	288.20	08/2020 -	12/2021	16	-
	<u>Gas Authority Of India Limited</u>								

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
69	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,652.70	12/2020 -	11/2021	11	-
70	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	197.30	04/2018 -	12/2021	44	-
71	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	223.50	08/2020 05/2021	12/2021	16	7
72	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 217.92	217.92	101.80	04/2021 -	03/2022	11	-
73	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	47.78	02/2021 -	08/2022	18	-
	<u>Hindustan Petroleum Corporation Limited</u>								
74	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	303.40	216.34	03/2021 -	10/2021	7	-
75	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	104.54	07/2020 -	01/2022	18	-
76	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	183.21	06/2020 -	03/2022	21	-
77	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	111.34	06/2020 -	03/2022	21	-
78	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA	06/2018	380.00 -	380.00	306.50	11/2021 -	03/2022	4	-
79	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	125.01	08/2021 -	03/2022	7	-
	<u>Indian Oil Corporation Limited</u>								
80	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	315.00	223.98	12/2021 08/2021	11/2021	-1	3
81	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	556.96	02/2020 06/2021	11/2021	21	5
82	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU	12/2016	228.00 -	228.00	156.18	11/2021 -	12/2021	1	-
83	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	171.59	01/2021 06/2021	12/2021	11	6
84	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	290.69	04/2021 -	12/2021	8	-
85	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	1,255.00	298.37	10/2021 -	12/2021	2	-
86	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	157.79	03/2021 09/2021	01/2022	10	4
87	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,163.26	03/2021 12/2021	03/2022	12	3
88	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	596.34	07/2018 05/2021	03/2022	44	10

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
89	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	345.08	02/2020 10/2021	03/2022	25	5
90	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	823.08	10/2021 -	03/2022	5	-
91	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT	10/2019	403.00 -	403.00	181.90	12/2021 -	04/2022	4	-
92	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	104.05	02/2020 06/2021	06/2022	28	12
93	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 207.36	207.36	126.85	04/2020 10/2021	07/2022	27	9
94	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	179.80	01/2021 -	08/2022	19	-
95	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	500.28	10/2017 03/2022	09/2022	59	6
96	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	56.21	12/2019 03/2022	10/2022	34	7
97	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	173.55	08/2021 -	11/2022	15	-
98	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	90.20	12/2022 05/2022	-	-	7
99	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	10.81	07/2022 -	01/2023	6	-
100	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	124.99	04/2022 -	02/2023	10	-
101	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	96.02	04/2022 -	08/2023	16	-
102	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.29	09/2023 -	02/2024	5	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
103	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	534.34	03/2020 11/2020	11/2021	20	12
104	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,766.26	12/2019 04/2021	02/2022	26	10
	<u>Oil & Natural Gas Corporation Limited</u>								
105	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	222.27	05/2020 08/2021	11/2021	18	3
	<u>Oil India Limited</u>								
106	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	510.00	485.08	12/2019 -	12/2021	24	-
107	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 652.10	638.60	395.08	02/2020 -	12/2021	22	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 222.21	198.00	183.20	08/2020 09/2021	12/2021	16	3
109	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL, MULTI STATE	05/2016	406.00 -	406.00	281.34	10/2020 -	03/2022	17	-
	Total		27,020.97 -	28,437.34	16,804.58				
	POWER								
	National Thermal Power Corporation								
110	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,993.63	07/2012 06/2020	11/2021	112	17
111	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 2,311.89	2,311.89	1,922.67	12/2018 -	12/2021	36	-
112	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 17,304.00	17,304.00	16,371.88	05/2018 -	02/2022	45	-
113	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 633.80	633.80	472.23	11/2018 -	02/2022	39	-
114	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC, RAJASTHAN	03/2020	1,782.00 -	1,782.00	672.69	09/2021 07/2022	09/2022	12	2
115	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC, TELANGANA	01/2016	10,598.98 10,997.70	10,997.70	8,866.73	11/2020 07/2022	10/2022	23	3
116	NOKHRA - [N18000282]NTPC, UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	436.25	09/2021 07/2022	01/2023	16	6
117	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND	02/2014	14,366.58 -	15,389.42	12,291.69	06/2019 10/2022	09/2023	51	11
118	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	5,187.12	03/2013 12/2021	09/2024	138	33
119	PATRATU STPP-I (3X800MW) - [N18000275]NTPC, JHARKHAND	11/2017	18,668.00 -	17,112.00	4,391.63	03/2023 -	02/2025	23	-
	Power Grid Corporation Of India Limited								
120	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	14,733.37	11,683.96	11/2019 07/2021	10/2021	23	3
121	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	1,931.39	1,807.75	02/2020 09/2021	10/2021	20	1
122	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	252.99	04/2016 12/2017	12/2021	68	48
123	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	197.40	90.75	03/2018 -	12/2021	45	-
124	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	235.53	156.95	06/2019 11/2021	12/2021	30	1
125	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	379.95	235.98	12/2019 09/2021	12/2021	24	3

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
126	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	167.22	07/2019 07/2021	12/2021	29	5
127	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	260.80	05/2020 08/2021	12/2021	19	4
128	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	204.37	02/2019 09/2021	02/2022	36	5
129	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,096.25	07/2020 12/2020	02/2022	19	14
130	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	3,207.16	12/2018 12/2021	03/2022	39	3
	<u>Thdc India Limited</u>								
131	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 4,825.60	4,825.60	4,266.10	02/2016 -	06/2023	88	-
132	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	2,822.96	09/2023 -	08/2024	11	-
	Total		1,10,925.91 -	1,29,048.41	87,859.76				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Cpwd For Health</u>								
133	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	150.29	64.32	03/2020 -	12/2021	21	-
134	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
135	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
136	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	317.45	03/2019 -	10/2021	31	-
137	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	253.84	05/2018 -	03/2022	46	-
	<u>Nbcc For Health</u>								
138	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	870.80	09/2021 -	06/2022	9	-
	Total		2,675.43 -	2,795.43	1,548.20				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
139	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,905.60	03/2021 -	03/2023	24	-
140	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,387.52	357.95	03/2021 -	03/2023	24	-
141	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	515.13	03/2022 -	03/2023	12	-
142	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	354.61	03/2022 -	03/2024	24	-
143	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	466.67	03/2023 -	03/2024	12	-
144	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	314.37	03/2022 -	03/2024	24	-
145	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	237.71	03/2023 -	03/2024	12	-
	<u>East Central Railways</u>								
146	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	236.91	03/2019 -	03/2022	36	-
147	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	390.00	386.59	03/2021 -	03/2022	12	-
148	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 - 1,200.20	1,200.20	971.03	03/2020 -	03/2023	36	-
149	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,367.09	03/2020 -	03/2024	48	-
150	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	541.64	03/2020 03/2023	12/2024	57	21
	<u>East Coast Railway</u>								
151	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	223.69	03/2020 -	03/2022	24	-
152	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	737.43	03/2022 03/2024	03/2026	48	24
	<u>Eastern Railways</u>								
153	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	638.28	02/2013 -	03/2024	133	-
154	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	908.35	03/2019 12/2009	03/2025	72	183
155	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	-
156	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	439.23	03/2022 -	03/2025	36	-
157	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	614.87	03/2016 -	03/2025	108	-
158	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96	-
159	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	199.72	03/2016 -	03/2025	108	-

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
160	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	480.96	03/2017 -	03/2025	96	-
161	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240	-
162	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	157	-
163	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	109.51	03/2014 -	03/2025	132	-
164	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
165	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]JRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,707.85	09/2018 -	06/2022	45	-
166	GEVRA ROAD PENDRA ROAD - [N22000488]JRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	953.27	03/2022 -	09/2023	18	-
167	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JRCON,ODISHA	04/2016	5,200.00 -	5,200.00	101.77	03/2020 -	03/2025	60	-
	<u>North Central Railway</u>								
168	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	-	- 04/2010	12/2021	-	140
169	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	680.00	4.00	03/2020 -	12/2021	21	-
170	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	2,001.00	980.08	03/2021 12/2022	12/2023	33	12
171	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	71.56	03/2023 -	06/2025	27	-
	<u>North East Frontier Railway</u>								
172	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,881.59	12/2008 -	11/2021	155	-
173	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	333.46	- 12/2021	03/2022	-	3
174	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,498.64	03/2021 -	03/2022	12	-
175	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,043.00	873.80	03/2019 -	03/2023	48	-
176	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,842.95	03/2022 -	03/2023	12	-
177	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	11,504.51	03/2011 -	12/2023	153	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
178	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	328.75	03/2019 -	12/2023	57	-
179	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	1,021.19	03/2019 -	03/2024	60	-
180	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	4,232.46	03/2014 -	03/2024	120	-
181	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,647.64	1,369.40	03/2015 -	03/2026	132	-
<u>North Eastern Railway</u>									
182	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	69.01	04/2016 -	12/2021	68	-
183	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	610.00	580.83	01/2019 -	02/2022	37	-
184	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	315.05	01/2022 -	03/2022	2	-
185	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
186	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	-
187	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
<u>North Western Railway</u>									
188	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	759.31	02/2019 -	06/2022	40	-
189	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	313.14	03/2020 -	10/2022	31	-
190	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	356.84	08/2022 -	11/2022	3	-
<u>Northern Railway</u>									
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	25,828.58	11/2002 -	12/2022	241	-
192	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,017.96	2,017.96	878.49	07/2012 -	11/2024	148	-
193	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	-
<u>Rail Vikas Nigam Ltd.</u>									
194	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	872.65	937.77	03/2021 -	12/2021	9	-
195	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	836.26	03/2016 -	12/2021	69	-
196	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,900.00	2,831.13	03/2020 -	12/2021	21	-
197	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	2,119.84	03/2020 -	12/2021	21	-
198	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,347.35	03/2020 -	12/2021	21	-

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
199	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,972.62	12/2020 -	12/2021	12	-
200	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	2,128.65	12/2021 -	03/2022	3	-
201	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	3,126.39	03/2020 -	03/2022	24	-
202	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,842.99	02/2015 -	06/2022	88	-
203	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,429.50	03/2019 -	06/2022	39	-
204	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,233.58	03/2019 -	06/2022	39	-
205	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,056.49	03/2022 -	06/2022	3	-
206	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,409.57	03/2020 -	06/2022	27	-
207	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,710.66	12/2020 -	12/2022	24	-
208	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	945.85	03/2022 -	12/2024	33	-
209	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,054.05	03/2023 -	12/2024	21	-
210	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,033.55	03/2016 -	03/2025	108	-
211	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,422.91	03/2016 -	03/2025	108	-
212	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	4,874.57	12/2024 -	03/2025	3	-
213	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
214	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	1,887.58	12/2024 -	12/2026	24	-
<u>South Central Railway</u>									
215	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 927.94	927.94	680.25	03/2020 -	02/2022	23	-
216	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,004.42	03/2000 -	03/2023	276	-
217	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,035.50	03/2009 -	03/2024	180	-
218	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,373.74	646.34	03/2010 -	03/2024	168	-
219	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	714.51	03/2023 -	03/2024	12	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 2,333.00	2,333.00	1,290.39	03/2021 -	03/2024	36	-
221	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,582.36	03/2021 -	03/2024	36	-
222	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,365.73	03/2022 -	03/2024	24	-
223	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	347.10	03/2014 -	03/2027	156	-
	<u>South Eastern Railway</u>								
224	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.96	1,071.24	03/2020 -	03/2022	24	-
225	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,028.57	03/2021 -	12/2023	33	-
226	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
227	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
228	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,968.00	1,174.76	03/2020 -	03/2023	36	-
229	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.97	03/2016 -	12/2023	93	-
230	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	264	-
231	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
232	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	1,878.00	1,488.87	03/2019 -	03/2024	60	-
233	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	732.89	469.70	03/2017 -	03/2025	96	-
234	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	373.87	12/2018 -	06/2025	78	-
235	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	1,530.09	316.23	03/2016 -	12/2026	129	-
	<u>Southern Railway</u>								
236	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	749.40	550.86	- 12/2021	01/2022	-	1
237	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	608.13	399.75	- 12/2021	02/2022	-	2
238	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,122.00	989.62	- 09/2021	12/2022	-	15
239	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	705.52	03/2020 -	03/2025	60	-
240	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,950.00	1,667.29	02/2019 -	03/2025	73	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
241	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
242	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	285.53	03/2019 -	12/2027	105	-
243	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	527.37	2.59	02/2019 -	03/2030	133	-
	<u>West Central Railway</u>								
244	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	508.67	03/2022 -	03/2023	12	-
245	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	2,449.00	1,293.48	03/2020 -	03/2024	48	-
246	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202	-
	<u>Western Railway</u>								
247	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 -	692.25	.77	03/2020 -	03/2023	36	-
248	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	495.18	.33	03/2022 -	03/2024	24	-
	Total		1,52,896.93 -	2,57,409.39	1,37,106.46				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
249	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	448.61	01/2020 06/2021	11/2021	22	5
250	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	773.30	02/2020 08/2021	11/2021	21	3
251	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	142.81	08/2020 -	11/2021	15	-
252	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	205.95	108.58	01/2021 -	11/2021	10	-
253	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	237.29	09/2020 -	11/2021	14	-
254	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 10/2021	12/2021	45	2
255	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 174.90	174.90	154.26	08/2018 08/2021	12/2021	40	4
256	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	125.42	02/2018 09/2021	12/2021	46	3

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	129.31	03/2017 06/2021	12/2021	57	6
258	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	182.97	08/2018 09/2021	12/2021	40	3
259	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	166.48	03/2018 10/2021	12/2021	45	2
260	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	198.83	07/2018 08/2021	12/2021	41	4
261	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	238.57	09/2019 06/2021	12/2021	27	6
262	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	615.21	07/2018 05/2021	12/2021	41	7
263	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	743.57	06/2019 04/2021	12/2021	30	8
264	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	390.40	03/2018 06/2021	12/2021	45	6
265	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	192.35	08/2020 -	12/2021	16	-
266	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	160.00	124.58	09/2021 -	02/2022	5	-
267	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	281.69	- 03/2021	03/2022	-	12
268	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.51	11/2018 01/2021	03/2022	40	14
269	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	139.54	03/2021 11/2021	03/2022	12	4
270	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.89	04/2020 -	03/2022	23	-
271	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	61.20	03/2018 04/2021	04/2022	49	12

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
272	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	102.76	03/2021 -	04/2022	13	-
273	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	80.06	03/2018 09/2021	06/2022	51	9
274	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	26.91	08/2019 -	11/2022	39	-
275	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	403.23	08/2017 06/2021	12/2022	64	18
276	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	16.24	05/2021 -	12/2022	19	-
277	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	6.94	03/2021 -	03/2023	24	-
National Highways And Infrastructure Development Corporation Ltd.									
278	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	54	7
279	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	36	-
280	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	168.39	148.91	11/2018 -	11/2021	36	-
281	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	237.72	126.19	09/2018 -	11/2021	38	-
282	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	251.97	146.10	09/2018 -	11/2021	38	-
283	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	282.98	161.15	09/2018 -	11/2021	38	-
284	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	108.86	09/2018 -	11/2021	38	-
285	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	105.09	06/2018 -	12/2021	42	-

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
286	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	463.49	165.06	06/2018 -	12/2021	42	-
287	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	289.99	95.89	12/2018 -	12/2021	36	-
288	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	-	11
289	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	115.77	09/2018 -	12/2021	39	-
290	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	121.06	09/2018 -	12/2021	39	-
291	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	77.59	09/2018 -	12/2021	39	-
292	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL, SIKKIM	11/2017	290.05 -	290.05	154.83	11/2017 -	12/2021	49	-
293	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL, ARUNACHAL PRADESH	12/2016	200.44 -	200.44	125.91	- 08/2021	12/2021	-	4
294	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM	10/2014	588.95 -	588.95	504.10	11/2018 -	02/2022	39	-
295	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	454.89	346.86	05/2018 -	03/2022	46	-
296	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	219.83	01/2016 -	03/2022	74	-
297	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	252.00	136.10	01/2016 -	03/2022	74	-
298	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	167.81	04/2017 03/2021	03/2022	59	12
299	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	252.79	142.18	04/2017 -	03/2022	59	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
300	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	263.31	148.30	04/2017 -	03/2022	59	-
301	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	252.05	152.53	04/2017 -	03/2022	59	-
302	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31 -	274.31	126.90	05/2018 -	03/2022	46	-
303	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL, UTTARAKHAND	03/2018	403.36 -	403.36	217.43	06/2018 -	03/2022	45	-
304	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL, UTTARAKHAND	03/2018	417.24 -	417.24	265.48	05/2018 -	03/2022	46	-
305	2 LANE WITH HARD SHOULDER, REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51	12
306	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018	03/2022	41	-
307	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL, A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41	18
308	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	387.00	315.99	09/2018 -	03/2022	42	-
309	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	-
310	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDER FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL, MEGHALAYA	03/2019	306.28 -	306.28	133.81	05/2019 -	03/2022	34	-
311	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL, ARUNACHAL PRADESH	09/2016	568.92 -	568.92	310.07	- 11/2021	03/2022	-	4
312	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL, ARUNACHAL PRADESH	12/2016	188.78 -	188.78	104.07	- 03/2021	03/2022	-	12
313	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	116.27	09/2018 -	05/2022	44	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
314	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	169.77	09/2018 -	07/2022	46	-
315	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	280.16	07/2018 -	07/2022	48	-
316	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	89.53	09/2018 -	09/2022	48	-
317	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	63.44	09/2018 -	10/2022	49	-
318	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	115.32	09/2018 -	11/2022	50	-
319	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	83.73	09/2019 -	04/2023	43	-
320	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	106.57	09/2019 04/2023	06/2023	45	2
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	126.61	09/2019 04/2023	06/2023	45	2
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	94.28	09/2019 06/2023	07/2023	46	1
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	41.29	09/2019 03/2024	04/2024	55	1
<u>National Highways Authority Of India</u>									
324	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	1,003.47	11/2018 -	10/2021	35	-
325	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	11/2021	99	-
326	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 1,928.22	1,928.22	1,890.04	04/2015 01/2021	12/2021	80	11
327	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	12/2021	44	-
328	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	398.58	07/2018 -	12/2021	41	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
329	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29	-
330	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29	-
331	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	243.59	03/2020 -	12/2021	21	-
332	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	398.58	07/2016 -	12/2021	65	-
333	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	718.00	12/2019 -	12/2021	24	-
334	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	90.50	04/2014 -	01/2022	93	-
335	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	429.86	08/2018 -	01/2022	41	-
336	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	77.82	05/2013 -	02/2022	105	-
337	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	311.03	08/2017 -	02/2022	54	-
338	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,633.18	03/2013 -	03/2022	108	-
339	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36	-
340	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	03/2022	23	-
341	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	556.00	03/2020 -	04/2022	25	-
342	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	538.00	05/2020 -	05/2022	24	-
343	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	233.12	03/2019 12/2021	06/2022	39	6
344	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59	-
345	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	770.94	09/2017 -	07/2022	58	-

Costing Rs. 150 Crore and above

(October 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
346	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	443.91	03/2020 -	09/2022	30	-
347	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	-
348	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	348.00	03/2019 01/2021	12/2022	45	23
349	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	32.96	12/2017 -	05/2023	65	-
350	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023	118	-
	Total		53,524.64 -	53,404.90	36,174.09				
	<u>TELECOMMUNICATIONS</u>								
	<u>Cpwd For Telecom</u>								
351	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	145.26	03/2018 -	12/2021	45	-
	<u>Department Of Telecommunication</u>								
352	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	20,545.00	07/2015 05/2020	03/2022	80	22
	Total		13,582.20 -	24,912.20	20,690.26				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
353	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	9,472.48	12/2018 -	08/2022	44	-
	<u>Central Public Works Department</u>								
354	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	1,128.00	30.00	03/2022 -	06/2023	15	-
	<u>Lucknow Metro Rail Corporation Limited</u>								
355	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	1,917.78	03/2024 -	03/2025	12	-
356	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	426.47	03/2024 -	05/2025	14	-
	Total		31,357.10 -	33,371.10	11,846.73				
	<u>WATER RESOURCES</u>								
	<u>Brahmaputra Board</u>								
357	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	233.57	148.83	12/2019 -	12/2021	24	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
358	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	28.31	08/2021 -	12/2021	4	-
	<u>Delhi Jal Board</u>								
359	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	108.28	12/2021 -	12/2022	12	-
360	REHABILITATION AND UPGRADE OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	149.02	02/2022 -	12/2022	10	-
	<u>Kolkata Metropolitan Development Authority</u>								
361	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	06/2022	4	-
362	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022 -	10/2022	8	-
	<u>Polavaram Project Authority</u>								
363	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	18,317.91	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
364	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP Jal Nigam, UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-
	Total		11,797.25 -	57,131.86	18,752.35				
	<u>DEFENCE PRODUCTION</u>								
	<u>Cpwd For Defence</u>								
365	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]CPWD FOR DEFENCE, KARNATAKA	12/2016	246.31 210.00	210.00	149.80	02/2020 10/2021	12/2021	22	2
	Total		246.31 -	210.00	149.80				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
366	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION, MAHARASHTRA	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	17	-
367	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION, BIHAR	02/2016	496.18 496.00	498.99	292.81	06/2017 -	03/2022	57	-
368	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION, PUNJAB	01/2018	430.00 -	387.83	228.61	05/2020 -	06/2022	25	-
369	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION, ODISHA	01/2019	790.79 -	790.79	230.59	03/2022 -	06/2022	3	-
370	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION, KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	-

Costing Rs. 150 Crore and above

(October 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
371	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	424.93	55.00	07/2022 -	10/2022	3	-
372	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	249.81	07/2022 -	10/2022	3	-
373	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	24.91	05/2022 -	10/2022	5	-
374	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	110.13	09/2020 -	11/2022	26	-
375	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	-
376	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	177.82	03/2021 -	02/2023	23	-
	Total		6,090.48 -	6,051.12	1,528.22				
	HOME AFFAIRS								
	Cpwd For Mha								
377	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 -	2,000.00	1,007.93	10/2019 -	03/2022	29	-
	Total		1,219.21 -	2,000.00	1,007.93				
	Grand Total		5,28,627.41	7,26,164.52	4,09,243.07				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Nuclear Power Corporation Of India Limited</u>							
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	02/2022	44.69	74
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	03/2023	38.63	75
	Total		23,779.00 -	33,659.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	09/2021 -	12/2022	38.72	15
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	03/2021 -	03/2023	7.88	24
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	1,983.00	09/2021 -	12/2023	43.38	27
	Total		2,871.27 -	3,695.33				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	08/2019 -	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>							
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	708.55	03/2013 -	03/2024	47.76	132
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2022	.00	12
	<u>Singareni Colliers Company Limited</u>							
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2022	114.60	84
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2022	11.42	36
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2023	5.85	96

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							
13	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	03/2022 -	03/2025	.00	36
	Total		22,093.43 -	25,136.67				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
14	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR [N28000111]	11/2017	171.72 -	171.72	03/2020 -	12/2021	.00	21
15	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	09/2020 -	-	10.22	0
16	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	03/2022	.57	57
17	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	-	1.85	0
	<u>Rites Of Higher Education</u>							
18	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	09/2014 -	-	29.31	0
	Total		1,887.53 -	2,061.44				
	<u>DPIIT</u>							
	<u>Dmic For Dpiit</u>							
19	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>licc For Dpiit</u>							
20	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	05/2022	8.49	29
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Cpwd For Health</u>							
21	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
22	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	03/2021	16.33	37

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
23	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	190.34	-	11/2021	21.58	0
24	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
25	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
26	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022	01/2018	249.01 -	249.07	-	01/2021	.02	0
27	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46
28	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
29	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
30	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
31	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	586.50	11/2013 -	09/2021	41.63	94
	<u>Nbcc For Health</u>							
32	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	09/2021 -	06/2022	8.88	9
	Total		5,589.39 -	6,374.57				
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
33	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2022	64.04	29
	Total		1,219.21 -	2,000.00				
	<u>PETROLEUM</u>							
	<u>Hindustan Petroleum Corporation Limited</u>							
34	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	06/2021 -	07/2022	14.76	13
	<u>Indian Oil Corporation Limited</u>							
35	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 -	502.00	08/2019 -	05/2021	18.68	21
	<u>Oil & Natural Gas Corporation Limited</u>							
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	2,001.34	05/2013 -	05/2022	132.23	108

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		3,961.79	5,575.34				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
37	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW [N18000142]	07/2012	1,527.00	1,801.07	08/2017	-	17.95	0
38	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017	-	7.41	0
39	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58	15,389.42	06/2019	09/2023	7.12	51
	<u>Power Grid Corporation Of India Limited</u>							
40	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020	02/2022	14.11	19
	<u>Satluj Jal Vidyut Nigam Limited</u>							
41	NAITWAR MORI HEP - [N18000265]	10/2017	648.33	947.89	12/2021	06/2022	46.20	6
	Total		24,279.87	26,684.38				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
42	3RD LINE BETWEEN BHUSAVAL-JALGAON - [N22000247]	04/2011	184.06	325.00	03/2019	-	76.57	0
43	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19	1,283.49	03/2022	03/2023	.89	12
44	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89	1,387.52	03/2021	03/2023	75.00	24
45	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00	2,081.27	03/2023	03/2023	10.94	0
46	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00	3,438.49	03/2024	-	25.04	0
47	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29	3,445.48	03/2023	03/2023	8.75	0
48	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024	03/2023	.00	-12
49	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50	4,794.60	03/2021	03/2023	111.08	24
50	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00	5,341.68	03/2024	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
51	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50	235.00	03/2019	-	.21	0
52	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70	487.13	03/2018	-	25.65	0
	<u>East Central Railways</u>							

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
53	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 -	390.00	03/2021 -	03/2022	11.99	12
54	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	03/2025	36.67	0
55	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	07/2014 -	-	64.60	0
56	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26	0
57	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	03/2020 -	12/2024	49.45	57
58	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	03/2019 -	12/2021	37.04	33
59	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	-	376.78	0
60	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,080.00	03/2012 -	11/2022	232.58	128
61	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	03/2022	350.27	0
62	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	- -	03/2023	391.01	0
63	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15	0
64	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,630.00	- -	03/2022	251.38	0
<u>East Coast Railway</u>								
65	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2024	15.45	64
<u>Eastern Railways</u>								
66	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19	0
67	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
68	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25	0
69	MONIGRAM- NIMITTA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
70	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
71	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
72	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	- -	03/2022	181.63	0
74	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	- -	03/2021	74.26	0
75	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46	0
76	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
77	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
78	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
79	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
80	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30	0
81	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
82	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
83	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
<u>Indian Railway Construction Company Limited</u>								
84	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	09/2018 -	06/2022	.00	45
85	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	09/2023	117.23	18
<u>Metropolitan Rapid Transport Projects</u>								
86	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	07/2022	48.06	109
87	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	06/2022	501.57	219
88	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
89	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	-	75.91	0
<u>North Central Railway</u>								
90	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	12/2021	1.69	21
91	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
<u>North East Frontier Railway</u>								

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
92	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	-	7.86	0
93	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	- -	03/2022	54.80	0
94	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62	0
95	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
96	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
97	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	03/2020 -	06/2022	30.26	27
98	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	03/2020 -	-	80.79	0
99	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,043.00	03/2019 -	03/2023	170.77	48
100	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHAWA JAINTI - [N22000209]	04/1999	819.23 -	1,090.60	- -	-	33.13	0
101	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55	0
102	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	1,167.00	12/2021 -	10/2021	93.77	-2
103	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	03/2021 -	03/2022	115.07	12
104	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60
105	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12
106	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	03/2021 -	-	350.44	0
107	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	12/2008 -	11/2021	284.80	155
108	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	03/2014 -	03/2024	130.69	120
109	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,647.64	03/2015 -	03/2026	185.73	132
110	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	12/2015 -	12/2023	542.04	96
111	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>							
112	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16	68

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
113	KICHA-KHATIMA (NL) - NER - [N220100317	04/2003	142.45 -	228.40	- -	-	60.34	0
114	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459	04/2017	150.00 -	341.66	04/2017 -	10/2022	127.77	66
115	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	610.00	01/2019 -	02/2022	106.78	37
116	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP [N22000136	03/2013	643.00 -	644.00	- -	-	.16	0
117	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	800.00	- -	12/2023	32.78	0
118	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP [N22000131	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13	0
119	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15	0
120	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	1,409.09	- -	-	358.99	0
121	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	03/2015	1,295.42 -	1,824.00	03/2022 -	03/2022	40.80	0
	<u>North Western Railway</u>							
122	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152	04/2013	420.18 -	480.00	03/2020 -	09/2021	14.24	18
123	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	701.81	03/2020 -	10/2022	16.97	31
124	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82	40
125	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330	05/2015	873.71 -	2,215.27	- -	-	153.55	0
126	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
	<u>Northern Railway</u>							
127	GRADE SEPERATOR AT DAYABASTI - [N22000269	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
128	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
129	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274	04/2007	336.91 -	791.39	- -	09/2023	134.90	0
130	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	03/2002	625.00 -	839.00	03/2016 -	-	34.24	0
131	QADIAN-BEAS - [N22000295	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
132	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
133	CHANDIGARH-BADDI - [N22000467	04/2007	328.14 -	1,540.13	03/2023 -	03/2023	369.35	0
	<u>Rail Vikas Nigam Ltd.</u>							

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
134	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	433.00	03/2009 03/2009	12/2022	224.56	165
135	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
136	DHASA-JETALSAR (GC) - [N22000141	04/2012	644.38 -	872.65	03/2021 -	12/2021	35.42	9
137	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69
138	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
139	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02	39
140	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	03/2020 -	06/2022	102.11	27
141	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39
142	AHMEDABAD-BOTAD (GC) - [N22000140	04/2012	975.62 -	1,650.00	12/2021 -	12/2021	69.12	0
143	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
144	BINA - KOTA DOUBLING WITH RE - [N22000414	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12
145	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68	3
146	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	2,009.00	03/2020 -	12/2021	111.91	21
147	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
148	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
149	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,900.00	03/2020 -	12/2021	306.46	21
150	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
151	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
152	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
153	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
155	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
156	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
157	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
158	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0
	<u>South Central Railway</u>							
159	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	242.28	03/2022 -	03/2022	102.36	0
160	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	1,160.48 -	1,373.74	03/2010 -	03/2024	18.38	168
161	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
162	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
163	MANUGURU-RAMAGUNDAM - [N22000259	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
164	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156
165	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
166	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							
167	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
	<u>South Eastern Railway</u>							
168	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44	0
169	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
170	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
171	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0
172	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	03/2020 -	03/2022	35.38	24
173	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
174	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38	0
175	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65	0
176	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09	0
177	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	03/2020 -	12/2021	31.49	21
178	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,104.00	03/2020 -	09/2021	28.31	18
179	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	03/2016 -	12/2026	55.13	129
180	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	03/2019 -	03/2024	16.31	60
181	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,960.00	03/2002 -	03/2024	41.74	264
182	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,968.00	03/2020 -	03/2023	70.10	36
183	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	2,161.36	- -	12/2023	20.01	0
184	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,404.03	- -	12/2025	16.57	0
185	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	- -	12/2024	123.51	0
	<u>Southern Railway</u>							
186	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	448.10	- -	03/2025	136.79	0
187	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	03/2030	247.32	133
188	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.23	- -	03/2030	109.04	0
189	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	608.13	- -	02/2022	269.89	0
190	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	709.69	- -	03/2025	180.55	0
191	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	749.40	- -	01/2022	177.41	0
192	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	- -	03/2030	.00	0
193	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	09/2021	253.33	198
194	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,122.00	- -	12/2022	20.39	0
195	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	- -	03/2024	130.17	0

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
196	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400	02/2015	1,000.00 -	1,339.00	- -	03/2025	33.90	0
197	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	1,720.00	03/2020 -	03/2025	465.83	60
198	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,172.16	03/2019 -	12/2027	1,699.64	105
199	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
200	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079	09/2007	724.69 -	2,950.00	02/2019 -	03/2025	307.07	73
201	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	3,150.00	- -	12/2025	440.47	0
	<u>West Central Railway</u>							
202	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,763.93 -	2,449.00	03/2020 -	03/2024	38.84	48
203	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>							
204	SURENDRA NAGAR RAJKOT - [N22000392	04/2015	1,002.39 -	1,042.12	03/2021 -	12/2022	3.96	21
205	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH- KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	03/2019 -	03/2023	329.77	48
206	VIRAMGAM-SAMAKHALI (DL) - [N22000145	04/2011	1,037.15 -	1,383.69	03/2021 -	12/2022	33.41	21
207	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,886.76	03/2020 -	03/2024	127.39	48
208	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	6,171.08	03/2022 -	03/2023	76.13	12
	Total		1,80,828.29 -	3,33,189.11				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
209	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
210	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
211	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0
212	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
213	REHABILITATION AND UPGRADATION OF KABRAI- BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	10/2019	.00	1
214	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
215	MANGRUPHIR TO MAHAN - [N24001087	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
216	KUNDRAL TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
217	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	08/2018 -	12/2021	4.45	40
218	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
219	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	03/2018	228.32 -	228.32	08/2018 -	-	.00	0
220	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 -	236.18	12/2022 -	12/2022	19.48	0
221	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	10/2021	.08	23
222	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	-	.00	0
223	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	03/2021	.00	14
224	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239	03/2018	240.38 -	240.38	06/2019 -	-	.00	0
225	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
226	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
227	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
228	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
229	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	03/2018	289.67 290.00	289.67	08/2018 -	-	.00	0
230	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72	0
231	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
232	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
233	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0
234	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 -	318.28	01/2019 -	-	7.06	0
235	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	12/2021	72.36	87

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
236	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0
237	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	10/2010 -	12/2021	69.30	134
238	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
239	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00	336.47	12/2019 -	-	.00	0
240	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00	341.16	06/2019 -	-	.00	0
241	OSMANNAGAR TO KUNDAL - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
242	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
243	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47/NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0
244	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	353.43	12/2015 -	-	6.07	0
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	- -	-	15.67	0
246	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]	09/2016	372.68 -	372.68	02/2017 -	-	.00	0
247	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
248	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	10/2010 -	-	93.80	0
249	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
250	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]	01/2016	386.09 -	386.09	05/2016 -	-	.00	0
251	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 -	386.41	10/2018 -	-	18.58	0
252	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	05/2017 -	05/2022	45.75	60
253	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0
254	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
255	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
256	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
257	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	01/2018	418.03 -	418.03	08/2018 -	-	.00	0
258	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0
259	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0
260	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	02/2017	429.43 -	429.43	11/2017 -	-	.00	0
261	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06	0
262	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	03/2016	536.65 356.00	536.65	12/2019 -	12/2021	.00	24
263	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	09/2016 -	12/2021	14.24	63
264	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
265	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	-	.00	0
266	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75	0
267	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
268	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	-	58.98	0
269	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	-	.00	0
270	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0
271	KALMATH TO ZARAP - [N24001137	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
272	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
273	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
274	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	04/2017 -	03/2022	27.16	59
275	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	03/2022	29.48	59

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
276	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	03/2022	29.48	59
277	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	09/2020	277.44 -	277.44	10/2022 -	10/2022	.00	0
278	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73	57
279	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
	<u>National Highways Authority Of India</u>							
280	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0
281	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	- -	-	.99	0
282	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	- -	05/2017	8.35	0
283	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501	08/2015	322.09 -	322.09	04/2018 -	-	.00	0
284	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
285	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
286	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	04/2021	7.53	0
287	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	04/2014	351.34 -	417.68	01/2016 -	-	18.88	0
288	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
289	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	07/2012	291.36 -	469.31	01/2014 -	-	61.08	0
290	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
291	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594	07/2016	458.03 -	486.00	- -	-	6.11	0
292	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	- -	-	8.26	0
293	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	11/2013 -	-	15.53	0
294	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	11/2019 -	-	2.02	0
295	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	612.58	02/2009 -	-	118.78	0

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
296	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI [N24000367]	04/2014	495.78 -	627.93	01/2016 -	-	26.66	0
297	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR [N24000522]	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0
298	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
299	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	- -	-	6.11	0
300	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2022	19.25	43
301	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]	10/2020	724.60 -	724.60	03/2023 -	03/2023	.00	0
302	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]	02/2019	731.89 -	732.34	11/2019 -	-	.06	0
303	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0
304	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 -	743.89	- -	12/2021	.00	0
305	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	05/2018 -	03/2022	40.22	46
306	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	09/2022	.23	30
307	FOUR LANING OF AKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 -	807.00	- -	-	25.68	0
308	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	- -	10/2021	1.37	0
309	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]	12/2017	656.98 -	840.00	- -	11/2022	27.86	0
310	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]	12/2017	217.96 -	884.00	- -	10/2022	305.58	0
311	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	922.64	- -	02/2018	15.98	0
312	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	925.96	- -	02/2018	45.89	0
313	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691]	04/2017	894.00 -	929.32	04/2020 -	03/2022	3.95	23

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
314	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 [N24000459]	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
315	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) [N24000656]	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0
316	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	- -	-	44.60	0
317	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ [N24000521]	08/2015	854.80 -	1,038.56	- -	-	21.50	0
318	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	-	5.56	0
319	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
320	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06	0
321	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	- -	01/2022	5.32	0
322	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	- -	-	4.10	0
323	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
324	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
325	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 [N24000507]	12/2015	1,167.45 -	1,182.94	- -	-	1.33	0
326	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
327	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	- -	-	29.35	0
328	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	09/2017 -	-	9.67	0
329	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
330	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 -	1,296.00	- -	11/2021	.12	0
331	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 -	1,296.93	- -	01/2022	11.20	0

Costing Rs. 150 Crore and above					(October 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
332	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
333	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
334	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,361.00	- -	-	29.35	0
335	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24	0
336	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
337	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
338	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	1,588.29	09/2019 -	-	14.40	0
339	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
340	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0
341	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	06/2020 -	-	1.78	0
342	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	12/2021	4.99	0
343	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
344	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0
345	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28	0
346	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
347	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0
348	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	07/2021	63.05	4
349	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0

Costing Rs. 150 Crore and above

(October 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
350	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
351	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		95,897.94 -	1,12,893.82				
	<u>STEEL</u>							
	<u>Rastriya Ispat Nigam Limited</u>							
352	FORGED WHEEL PLANT - [N12000116]	04/2014	1,682.85 -	2,100.00	09/2018 -	11/2021	24.79	38
	Total		1,682.85 -	2,100.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
353	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	12/2018 -	08/2022	18.69	44
	<u>Mumbai Metro Rail Corporation Ltd</u>							
354	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	03/2020 -	03/2023	44.39	36
	<u>Patna Metro Rail Corporation</u>							
355	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 -	13,925.50	06/2024 -	06/2024	4.19	0
	Total		47,274.77 -	60,118.50				
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
356	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	398.90	03/2020 -	03/2021	76.68	12
357	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	413.29	09/2020 -	-	62.63	0
	<u>Uttar Pradesh Jal Nigam</u>							
358	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	12/2021 -	12/2021	.97	0
359	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	06/2022 -	06/2022	1.31	0
	Total		1,393.47 -	1,736.93				
	Grand Total		4,30,110.90	6,34,215.39				

North East Projects Costing Rs.150 crore and above (as on					31.10.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (-) [11/2022]	645.63 (-) [645.63]	0.00 (0.00) [3]
	<u>Power</u>				
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	14,458.38 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (-) [394.00]	390.07 (0.00) [0]
4	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	(-) [10/2021]	210.50 (-) [210.50]	145.76 (0.00) [-]
5	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	8/2021 (-) [0/0]	496.47 (-) [496.47]	0.00 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	217.60 (0.00) [0]
7	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	8/2021 (-) [0/0]	437.60 (-) [437.60]	0.00 (0.00) [0]
8	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	83.83 (0.00) [0]
9	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	1.15 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	64.64 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	119.81 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	37.16 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	83.55 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	172.41 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25	3/2019	9/2020 (-)	347.78 (-)	95.49 (0.00)

	(PACKAGE		[0/0]	[347.78]	[0]
16	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	35.37 (0.00) [0]
17	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	167.73 (0.00) [0]
18	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	50.14 (0.00) [0]
19	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (8/2021) [12/2021]	200.44 (-) [200.44]	125.91 (0.00) [-]
20	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (11/2021) [3/2022]	568.92 (-) [568.92]	310.07 (0.00) [-]
21	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (3/2021) [3/2022]	188.78 (-) [188.78]	104.07 (0.00) [-]
22	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (1/2021) [12/2021]	245.79 (-) [245.79]	204.42 (0.00) [-]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (6/2022) [3/2022]	1,718.59 (-) [1,718.59]	519.92 (0.00) [-]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	25.63 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	20.81 (0.00) [0]
26	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
27	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	0.00 (0.00) [0]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (-) [4/2022]	228.71 (-) [228.71]	27.48 (0.00) [0]
30	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (-) [4/2022]	294.04 (-) [294.04]	56.85 (0.00) [0]
31	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (-) [4/2022]	199.03 (-) [199.03]	39.84 (0.00) [0]
32	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (-) [4/2022]	184.88 (-) [184.88]	32.58 (0.00) [0]
33	LADDA - BASAI	2/2021	4/2023 (-) [4/2023]	445.96 (-) [445.96]	0.00 (0.00) [0]
34	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
35	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2021) [3/2022]	284.09 (284.09) [284.09]	167.81 (0.00) [59]

36	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	142.18 (57.56) [59]
37	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST]	2/2017	4/2017 (-) [3/2022]	203.36 (-) [263.31]	148.30 (59.95) [59]
38	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	152.53 (53.83) [59]
39	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX]	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	61.40 (0.00) [0]
40	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2022) [4/2022]	175.06 (-) [175.06]	90.86 (0.00) [-]
41	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	76.96 (0.00) [-]
42	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,242.74 (57.90) [0]
43	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	9/2021 (-) [9/2021]	182.55 (-) [182.55]	0.00 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
44	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2022) [3/2023]	1,142.00 (-) [1,232.00]	371.33 (90.00) [24]
	<u>Health And Family Welfare</u>				
45	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (-) [747.80]	417.16 (-127.20) [0]
46	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
47	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [11/2021]	557.00 (-) [557.00]	556.96 (0.00) [21]
48	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (9/2021) [12/2021]	224.75 (222.21) [198.00]	183.20 (-26.75) [16]
49	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [5/2021]	423.00 (-) [502.00]	444.35 (79.00) [0]
50	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [12/2021]	543.91 (652.10) [638.60]	395.08 (94.69) [22]
51	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	25.15 (0.00) [0]
52	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (18,968.00) [18,968.00]	648.35 (6,602.00) [0]
53	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (9,058.00) [9,058.00]	526.70 (-1,170.00) [0]
54	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (8/2021) [11/2021]	249.85 (303.75) [303.75]	222.27 (53.90) [18]

	<u>Railways</u>				
55	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,842.95 (717.68) [12]
56	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2022]	870.96 (-) [1,873.21]	1,498.64 (1,002.25) [12]
57	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	873.80 (657.80) [48]
	<u>Road Transport And Highways</u>				
58	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (5/2022) [5/2022]	268.08 (-) [390.73]	326.56 (122.65) [60]
59	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	23.56 (0.00) [0]
60	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
61	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	40.09 (0.00) [0]
62	4 LANING FROM JAMUGURI TO BISWANATH CHARALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	199.64 (0.00) [-]
63	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [2/2022]	588.95 (-) [588.95]	504.10 (0.00) [39]
64	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2021]	289.99 (-) [289.99]	95.89 (0.00) [36]
65	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	136.10 (0.00) [74]
66	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	105.09 (0.00) [42]
67	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	219.83 (0.00) [74]
68	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	532.08 (0.00) [0]
69	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	27.79 (0.00) [0]
70	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	32.27 (0.00) [0]
71	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	0.00 (0.00) [0]
72	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	11.78 (0.00) [0]
73	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	67.70 (0.00) [0]
74	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-)	288.85 (-)	0.00 (0.00)

			[1/2023]	[288.85]	[0]
75	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	148.91 (0.00) [36]
76	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [3/2023]	818.00 (-) [818.00]	215.66 (0.00) [-]
77	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	165.06 (0.00) [42]
78	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
79	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	346.86 (0.00) [46]
80	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [612.58]	612.58 (332.58) [0]
81	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
82	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	7.04 (0.00) [0]
83	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
84	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
85	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
86	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	155.61 (0.00) [-]
87	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [2/2022]	160.00 (-) [160.00]	124.58 (0.00) [5]
88	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [12/2022]	636.42 (-) [636.42]	0.00 (0.00) [0]
89	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
90	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	116.54 (0.00) [0]
91	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	17.93 (0.00) [0]
92	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	103.50 (0.00) [0]
	MANIPUR				
	Power				
93	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (1,311.05) [1,311.05]	156.99 (732.43) [0]
	Railways				

94	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	11,504.51 (7,809.98) [153]
	Road Transport And Highways				
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	46.68 (0.00) [0]
96	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	36.80 (0.00) [0]
97	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	42.84 (0.00) [0]
98	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	28.20 (0.00) [0]
99	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	25.18 (0.00) [0]
100	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [10/2023]	673.27 (-) [673.27]	0.00 (0.00) [0]
101	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
102	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [3/2023]	467.00 (-) [467.00]	0.00 (0.00) [0]
103	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	0.00 (0.00) [0]
104	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	25.85 (0.00) [0]
105	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
106	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
107	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	5.07 (0.00) [0]
108	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	154.09 (0.00) [0]
109	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	0.00 (0.00) [0]
110	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	0.00 (0.00) [0]
111	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	0.00 (0.00) [0]
112	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	0.00 (0.00) [0]
113	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]

114	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	0.00 (0.00) [0]
115	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	0.00 (0.00) [0]
116	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	0.00 (0.00) [0]
117	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	0.00 (0.00) [0]
118	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [36]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
119	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Doner</u>				
120	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [8/2021]	151.33 (-) [151.33]	149.33 (0.00) [0]
	<u>Health And Family Welfare</u>				
121	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [3/2022]	363.99 (-) [363.99]	253.84 (0.00) [46]
	<u>Railways</u>				
122	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.34 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
123	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.37 (0.00) [0]
124	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [3/2022]	306.28 (-) [306.28]	133.81 (0.00) [34]
125	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	40.21 (0.00) [0]
126	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	288.84 (0.00) [0]
127	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	173.17 (0.00) [0]
128	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	38.58 (0.00) [0]
129	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	53.58 (0.00) [0]
130	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
131	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (9/2021) [9/2021]	553.51 (-) [553.51]	197.23 (0.00) [0]
	<u>MIZORAM</u>				

	Railways				
132	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2024]	2,393.47 (5,021.45) [5,521.45]	4,232.46 (3,127.98) [120]
	Road Transport And Highways				
133	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [11/2021]	205.95 (-) [205.95]	108.58 (0.00) [10]
134	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2021) [0/0]	195.04 (-) [377.99]	368.39 (182.95) [0]
135	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2021) [12/2021]	186.96 (-) [322.24]	308.85 (135.28) [87]
136	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2021) [12/2021]	193.69 (-) [327.92]	323.23 (134.23) [134]
137	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	24.56 (0.00) [0]
138	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	30.06 (0.00) [0]
139	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	53.72 (0.00) [0]
140	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	49.59 (0.00) [0]
141	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	92.39 (0.00) [0]
142	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	23.26 (0.00) [0]
143	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	0.00 (0.00) [0]
144	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	12.16 (0.00) [0]
145	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
146	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
147	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	83.73 (0.00) [43]
148	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	642.96 (-) [642.96]	106.57 (0.00) [45]
149	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	518.53 (-) [518.53]	126.61 (0.00) [45]
150	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [4/2023]	537.82 (-) [537.82]	129.40 (0.00) [43]
151	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC	4/2017	9/2019 (4/2023)	473.18 (-)	118.96 (0.00)

	IMPROVEMENTS FRO		[4/2023]	[473.18]	[43]
152	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [7/2023]	640.07 (-) [640.07]	94.28 (0.00) [46]
153	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (3/2024) [4/2024]	404.29 (-) [404.29]	41.29 (0.00) [55]
154	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (9/2023) [9/2023]	428.11 (-) [428.11]	82.60 (0.00) [48]
155	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2021) [0/0]	624.41 (-) [992.67]	978.43 (368.26) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
156	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,647.64]	1,369.40 (4,321.12) [132]
	<u>Road Transport And Highways</u>				
158	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	116.27 (0.00) [44]
159	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	89.53 (0.00) [48]
160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	161.15 (0.00) [38]
161	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	315.99 (0.00) [42]
162	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	115.32 (0.00) [50]
163	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	39.60 (0.00) [0]
164	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	58.14 (0.00) [0]
165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	32.21 (0.00) [0]
166	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	54.27 (0.00) [0]
167	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	38.65 (0.00) [0]
168	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	79.89 (0.00) [0]
169	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [6/2022]	206.53 (-) [206.53]	81.84 (0.00) [0]
170	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (8/2021) [0/0]	217.35 (-) [217.35]	104.81 (0.00) [0]

171	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	40.94 (0.00) [0]
172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	3.90 (0.00) [0]
173	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (177.00) [277.44]	32.33 (0.00) [0]
174	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	169.77 (0.00) [46]
175	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	115.77 (0.00) [39]
176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	121.06 (0.00) [39]
177	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	108.86 (0.00) [38]
178	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	77.59 (0.00) [39]
179	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	63.44 (0.00) [49]
180	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	146.10 (0.00) [38]
181	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	126.19 (0.00) [38]
182	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	342.06 (13.93) [0]
183	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	304.39 (0.00) [0]
184	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (369.96) [369.96]	322.13 (33.71) [0]
185	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	8.04 (0.00) [0]
186	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	8.04 (0.00) [0]
187	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	167.62 (-) [167.62]	118.61 (0.00) [0]
188	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
189	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	7.80 (0.00) [0]
190	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	96.49 (0.00) [0]
	SIKKIM				

	<u>Railways</u>				
191	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	1,656.78 (7,260.52) [96]
	<u>Road Transport And Highways</u>				
192	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	2.58 (0.00) [0]
193	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
194	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	21.62 (0.00) [0]
195	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	74.52 (0.00) [0]
196	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	75.61 (0.00) [0]
197	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	118.63 (0.00) [0]
198	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	69.32 (0.00) [0]
199	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [12/2021]	290.05 (-) [290.05]	154.83 (0.00) [49]
200	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
201	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
202	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	56.40 (0.00) [0]
203	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	27.06 (0.00) [0]
204	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	32.98 (0.00) [0]
205	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	27.45 (0.00) [0]
206	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	295.14 (59.37) [0]
207	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
208	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
209	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (10/2021) [11/2021]	438.28 (-) [402.00]	390.15 (-36.28) [29]

	Railways				
210	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022) [6/2022]	569.63 (90.00) [742.00]	561.03 (172.37) [27]
	Road Transport And Highways				
211	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	358.78 (0.00) [0]
212	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	18.87 (0.00) [0]
213	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	19.60 (0.00) [0]
214	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	66.04 (0.00) [0]
215	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	5.10 (0.00) [0]
216	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	5.26 (0.00) [0]
217	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	52.08 (0.00) [0]
218	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	59.89 (0.00) [0]
219	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	7.72 (0.00) [0]
220	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	10.88 (0.00) [0]
221	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	0.00 (0.00) [0]
222	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	10.30 (0.00) [0]
223	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	39.78 (0.00) [0]
224	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	103.62 (0.00) [0]
225	STRENGTHENING OF CHURAIBARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	95.22 (0.00) [0]
226	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	33.22 (38.51) [0]
227	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	142.81 (0.00) [15]
	Total			1,30,738.00 (61,737.06) [1,81,649.99]	65,285.46 (50,911.99)

State Wise Projects Costing Rs.150 crore and above (as on					31.10.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (6/2022) [6/2022]	417.23 (707.73) [707.73]	476.54 (290.50) [45]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (3/2021) [3/2022]	409.85 (-) [409.85]	135.48 (0.00) [51]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	229.32 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (3/2021) [10/2021]	277.17 (-) [277.17]	202.59 (0.00) [54]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (1/2022) [1/2022]	262.97 (-) [262.97]	63.74 (0.00) [39]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (6/2021) [6/2021]	257.34 (-) [238.00]	214.90 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [3/2022]	391.00 (-) [391.00]	77.75 (0.00) [41]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (9/2020) [3/2022]	234.27 (-) [234.27]	75.22 (0.00) [41]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (10/2021) [10/2021]	237.80 (237.80) [238.00]	121.78 (0.20) [23]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	52.08 (0.00) [0]
11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (12/2021) [5/2022]	177.10 (-) [177.10]	104.49 (0.00) [27]
	<u>Department Of Higher Education</u>				
12	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [0/0]	186.00 (199.00) [205.00]	130.63 (19.00) [0]
13	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	9/2019	9/2022 (-) [1/2023]	588.72 (-) [588.72]	14.80 (0.00) [4]
14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [0/0]	655.34 (-) [655.34]	125.17 (0.00) [0]

	<u>Health And Family Welfare</u>				
15	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [12/2021]	601.02 (-) [601.02]	487.74 (0.00) [-]
16	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2021]	272.19 (-) [272.54]	268.55 (0.35) [0]
	<u>Petroleum</u>				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [10/2021]	303.40 (-) [303.40]	216.34 (0.00) [7]
18	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	8/2027 (-) [8/2027]	2,880.00 (-) [2,880.00]	104.89 (0.00) [0]
19	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [12/2021]	466.00 (-) [466.00]	290.69 (0.00) [8]
20	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (3/2021) [3/2021]	384.58 (-) [384.58]	291.62 (0.00) [0]
21	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	242.18 (0.00) [25]
22	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2022) [6/2022]	34,012.00 (-) [25,090.00]	14,210.03 (-8,922.00) [24]
23	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [1/2023]	167.00 (-) [167.00]	10.81 (0.00) [6]
24	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	124.99 (0.00) [10]
25	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (3/2022) [3/2022]	316.20 (-) [316.20]	130.90 (0.00) [5]
26	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	28.57 (0.00) [0]
27	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [3/2022]	210.94 (-) [210.94]	125.01 (0.00) [7]
28	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [1/2022]	196.26 (-) [196.26]	104.54 (0.00) [18]
29	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	16,536.13 (5,336.00) [24]
	<u>Railways</u>				
30	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
31	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
32	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
33	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2024]	3,631.00 (-) [3,887.48]	1,365.73 (256.48) [24]
34	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009	1,045.20	1,035.50

			(-) [3/2024]	(-) [2,120.16]	(1,074.96) [180]
35	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (3/2024) [3/2026]	2,499.71 (-) [2,499.71]	737.43 (0.00) [48]
36	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
37	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [487.13]	434.63 (99.43) [0]
38	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (2,333.00) [2,333.00]	1,290.39 (44.30) [36]
39	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	3,082.97 (302.42) [0]
40	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	3,126.39 (1,873.29) [24]
	Road Transport And Highways				
41	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/	328.67	266.63
			(-) [0/0]	(-) [328.67]	(0.00) [0]
42	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (-) [0/0]	1,226.88 (-) [1,226.88]	211.90 (0.00) [0]
43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [0/0]	1,601.10 (-) [1,601.10]	13.51 (0.00) [0]
44	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/	357.00	0.00
			(-) [0/0]	(-) [357.00]	(0.00) [0]
45	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/	557.30	433.20
			(-) [0/0]	(-) [557.30]	(0.00) [0]
46	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2022) [0/0]	263.45 (381.75) [263.45]	116.24 (0.00) [0]
47	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (1/2022) [0/0]	429.43 (373.05) [429.43]	325.31 (0.00) [0]
48	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/	314.43	85.61
			(-) [6/2022]	(-) [314.43]	(0.00) [-]
49	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2021) [0/0]	350.61 (-) [350.61]	324.69 (0.00) [0]
50	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [0/0]	333.21 (-) [353.43]	333.09 (20.22) [0]
51	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (7/2021) [7/2021]	1,532.62 (-) [2,499.00]	1,009.18 (966.38) [0]
52	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (4/2022) [0/0]	576.48 (596.38) [576.48]	388.43 (0.00) [0]
53	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (12/2021) [7/2021]	348.95 (-) [348.95]	231.08 (0.00) [0]
54	REHABILITATION AND UP GRADATION OF NH-544E FROM	3/2020	3/2021	207.79	102.76

	KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION		(-) [4/2022]	(-) [207.79]	(0.00) [13]
55	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21)	1/2016	5/2016 (11/2021) [0/0]	386.09 (316.06) [386.09]	214.31 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69)	11/2016	5/2017 (10/2021) [0/0]	290.15 (-) [290.15]	142.33 (0.00) [0]
57	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	654.33 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (9/2021) [0/0]	995.09 (995.00) [995.09]	561.45 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (8/2021) [0/0]	444.84 (-) [444.84]	349.19 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (12/2021) [0/0]	376.25 (-) [376.25]	314.18 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (11/2021) [0/0]	289.67 (274.73) [289.67]	208.86 (0.00) [0]
63	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (7/2021) [0/0]	504.19 (556.13) [504.19]	469.14 (0.00) [0]
64	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (6/2021) [0/0]	271.45 (-) [271.45]	243.29 (0.00) [0]
65	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (2/2022) [0/0]	319.28 (-) [319.28]	203.81 (0.00) [0]
66	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (10/2021) [0/0]	372.68 (309.37) [372.68]	256.21 (0.00) [0]
67	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (12/2021) [0/0]	228.32 (202.83) [228.32]	140.06 (0.00) [0]
68	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (10/2021) [0/0]	418.03 (381.75) [418.03]	324.42 (0.00) [0]
69	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	8/2020	3/2021 (-) [3/2023]	222.61 (-) [222.61]	6.94 (0.00) [24]
70	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [10/2021]	1,959.00 (-) [1,959.00]	1,314.63 (0.00) [-]
71	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (-) [0/0]	597.67 (-) [597.67]	216.39 (0.00) [0]
72	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	2/2019 (-) [0/0]	617.41 (-) [617.41]	526.54 (0.00) [0]
73	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [0/0]	1,323.15 (-) [1,323.15]	1,187.87 (0.00) [0]
74	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM	3/2018	/ (-)	1,550.98 (-)	1,633.66 (0.00)

	(DESIG		[9/2021]	[1,550.98]	[0]
75	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,283.85 (0.00) [0]
76	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	966.71 (145.48) [0]
77	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
78	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	0.00 (0.00) [0]
79	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	6/2020	5/2021 (-) [12/2022]	221.40 (-) [221.40]	16.24 (0.00) [19]
	<u>Steel</u>				
80	COKE OVEN BATTERY-5	12/2011	12/2017 (7/2022) [7/2022]	2,858.00 (-) [2,858.00]	2,004.81 (0.00) [55]
	<u>Water Resources</u>				
81	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	18,317.91 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
82	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (-) [11/2022]	645.63 (-) [645.63]	0.00 (0.00) [3]
	<u>Power</u>				
83	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	14,458.38 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
84	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (-) [394.00]	390.07 (0.00) [0]
85	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [10/2021]	210.50 (-) [210.50]	145.76 (0.00) [-]
86	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	8/2021 (-) [0/0]	496.47 (-) [496.47]	0.00 (0.00) [0]
87	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	217.60 (0.00) [0]
88	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	8/2021 (-) [0/0]	437.60 (-) [437.60]	0.00 (0.00) [0]
89	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	83.83 (0.00) [0]
90	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	1.15 (0.00) [0]
91	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	64.64 (0.00) [0]
92	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	119.81 (0.00) [0]

93	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	37.16 (0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	83.55 (0.00) [0]
95	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	172.41 (0.00) [0]
96	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	95.49 (0.00) [0]
97	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	35.37 (0.00) [0]
98	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	167.73 (0.00) [0]
99	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	50.14 (0.00) [0]
100	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (8/2021) [12/2021]	200.44 (-) [200.44]	125.91 (0.00) [-]
101	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (11/2021) [3/2022]	568.92 (-) [568.92]	310.07 (0.00) [-]
102	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (3/2021) [3/2022]	188.78 (-) [188.78]	104.07 (0.00) [-]
103	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (1/2021) [12/2021]	245.79 (-) [245.79]	204.42 (0.00) [-]
104	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (6/2022) [3/2022]	1,718.59 (-) [1,718.59]	519.92 (0.00) [-]
105	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	25.63 (0.00) [0]
106	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	20.81 (0.00) [0]
107	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
108	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	0.00 (0.00) [0]
109	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (0/0)	392.60 (-) [392.60]	0.00 (0.00) [0]
110	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (-) [4/2022]	228.71 (-) [228.71]	27.48 (0.00) [0]
111	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (-) [4/2022]	294.04 (-) [294.04]	56.85 (0.00) [0]
112	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (-) [4/2022]	199.03 (-) [199.03]	39.84 (0.00) [0]
113	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600	8/2020	4/2022	184.88	32.58

	TO KM138.00 (PKG-7)		(-) [4/2022]	(-) [184.88]	(0.00) [0]
114	LADDA - BASAI	2/2021	4/2023 (-) [4/2023]	445.96 (-) [445.96]	0.00 (0.00) [0]
115	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
116	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2021) [3/2022]	284.09 (284.09) [284.09]	167.81 (0.00) [59]
117	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	142.18 (57.56) [59]
118	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [3/2022]	203.36 (-) [263.31]	148.30 (59.95) [59]
119	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	152.53 (53.83) [59]
120	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	61.40 (0.00) [0]
121	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2022) [4/2022]	175.06 (-) [175.06]	90.86 (0.00) [-]
122	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	76.96 (0.00) [-]
123	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,242.74 (57.90) [0]
124	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	9/2021 (-) [9/2021]	182.55 (-) [182.55]	0.00 (0.00) [0]
ASSAM					
Civil Aviation					
125	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2022) [3/2023]	1,142.00 (-) [1,232.00]	371.33 (90.00) [24]
Health And Family Welfare					
126	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (-) [747.80]	417.16 (-127.20) [0]
127	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
Petroleum					
128	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [11/2021]	557.00 (-) [557.00]	556.96 (0.00) [21]
129	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (9/2021) [12/2021]	224.75 (222.21) [198.00]	183.20 (-26.75) [16]
130	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [5/2021]	423.00 (-) [502.00]	444.35 (79.00) [0]
131	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [12/2021]	543.91 (652.10) [638.60]	395.08 (94.69) [22]
132	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2	5/2021	10/2023	412.00	25.15

	MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN		(-) [10/2023]	(-) [412.00]	(0.00) [0]
133	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (18,968.00) [18,968.00]	648.35 (6,602.00) [0]
134	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (9,058.00) [9,058.00]	526.70 (-1,170.00) [0]
135	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (8/2021) [11/2021]	249.85 (303.75) [303.75]	222.27 (53.90) [18]
	<u>Railways</u>				
136	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,842.95 (717.68) [12]
137	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2022]	870.96 (-) [1,873.21]	1,498.64 (1,002.25) [12]
138	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	873.80 (657.80) [48]
	<u>Road Transport And Highways</u>				
139	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (5/2022) [5/2022]	268.08 (-) [390.73]	326.56 (122.65) [60]
140	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	23.56 (0.00) [0]
141	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
142	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	40.09 (0.00) [0]
143	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	199.64 (0.00) [-]
144	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [2/2022]	588.95 (-) [588.95]	504.10 (0.00) [39]
145	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2021]	289.99 (-) [289.99]	95.89 (0.00) [36]
146	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	136.10 (0.00) [74]
147	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	105.09 (0.00) [42]
148	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	219.83 (0.00) [74]
149	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	532.08 (0.00) [0]
150	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	27.79 (0.00) [0]
151	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	32.27 (0.00) [0]

152	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	0.00 (0.00) [0]
153	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	11.78 (0.00) [0]
154	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	67.70 (0.00) [0]
155	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
156	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	148.91 (0.00) [36]
157	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [3/2023]	818.00 (-) [818.00]	215.66 (0.00) [-]
158	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	165.06 (0.00) [42]
159	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
160	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	346.86 (0.00) [46]
161	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [612.58]	612.58 (332.58) [0]
162	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
163	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	7.04 (0.00) [0]
164	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
165	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
166	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
167	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	155.61 (0.00) [-]
168	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [2/2022]	160.00 (-) [160.00]	124.58 (0.00) [5]
169	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [12/2022]	636.42 (-) [636.42]	0.00 (0.00) [0]
170	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
171	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	116.54 (0.00) [0]
172	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED	8/2020	4/2022	208.84	17.93

	SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800		(-) [4/2022]	(-) [208.84]	(0.00) [0]
173	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	103.50 (0.00) [0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
174	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [12/2023]	1,216.90 (-) [1,216.90]	229.22 (0.00) [14]
	<u>Department Of Higher Education</u>				
175	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [3/2022]	496.18 (496.00) [498.99]	292.81 (2.81) [57]
176	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	110.13 (0.00) [26]
	<u>Petroleum</u>				
177	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	1,620.50 (0.00) [0]
178	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS	6/2019	12/2029 (-) [12/2029]	988.00 (-) [988.00]	41.60 (0.00) [0]
179	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	439.00 (-) [439.00]	119.54 (0.00) [0]
180	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	8/2027 (-) [8/2027]	176.00 (-) [176.00]	77.52 (0.00) [0]
181	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	12/2029 (-) [12/2029]	163.00 (-) [163.00]	24.46 (0.00) [0]
182	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	347.00 (-) [347.00]	94.78 (0.00) [0]
183	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	2,996.00 (-) [2,996.00]	283.56 (0.00) [0]
184	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	181.07 (0.00) [0]
185	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [12/2021]	522.00 (-) [522.00]	376.88 (0.00) [9]
186	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2022]	199.36 (-) [199.36]	72.98 (0.00) [22]
187	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [12/2021]	189.00 (-) [189.00]	171.59 (0.00) [11]
188	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (9/2021) [1/2022]	206.50 (-) [206.50]	157.79 (0.00) [10]
189	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	94.90 (0.00) [0]
	<u>Power</u>				
190	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2023]	8,692.97 (21,312.11) [21,312.11]	19,311.93 (12,619.14) [141]

191	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [11/2021]	5,353.00 (10,566.00) [10,566.00]	8,993.63 (5,213.00) [112]
192	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	3,509.49 (0.00) [0]
193	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (-) [2/2022]	12,964.60 (17,304.00) [17,304.00]	16,371.88 (4,339.40) [45]
	<u>Railways</u>				
194	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
195	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (-) [1,605.17]	147.56 (0.00) [-]
196	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	2.04 (2,668.81) [-]
197	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2023]	378.56 (-) [1,858.75]	386.36 (1,480.19) [-]
198	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
199	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF,	4/1991	/ (3/2022) [3/2022]	329.39 (803.11) [1,483.14]	1,218.49 (1,153.75) [-]
200	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	1.15 (0.00) [0]
201	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (3/2023) [3/2023]	528.65 (2,066.78) [2,066.78]	1,590.10 (1,538.13) [-]
202	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (11/2022) [11/2022]	324.73 (898.53) [1,080.00]	1,077.28 (755.27) [128]
203	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (3/2023) [12/2024]	548.00 (-) [819.01]	541.64 (271.01) [57]
204	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [12/2023]	162.87 (614.45) [614.45]	352.46 (451.58) [-]
205	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/ (-) [0/0]	333.76 (-) [360.00]	6.74 (26.24) [0]
206	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	971.03 (0.00) [36]
207	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [0/0]	499.41 (516.02) [516.02]	459.05 (16.61) [0]
208	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [0/0]	192.56 (-) [192.56]	0.39 (0.00) [0]
209	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (9/2021) [9/2021]	477.88 (751.55) [751.55]	719.65 (273.67) [0]
210	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [0/0]	211.00 (-) [1,006.00]	24.16 (795.00) [0]

211	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	4/2016	3/2021 (3/2024) [3/2024]	731.64 (1,185.73) [1,185.73]	383.26 (454.09) [36]
212	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/ (-) [0/0]	281.30 (-) [281.30]	0.60 (0.00) [0]
213	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/ (-) [3/2024]	228.05 (-) [228.05]	1.53 (0.00) [-]
214	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (-) [546.71]	560.09 (214.56) [0]
215	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	620.57 (-) [620.57]	0.31 (0.00) [0]
216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2024]	532.87 (2,132.03) [2,145.00]	1,021.19 (1,612.13) [60]
217	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (3/2023) [3/2023]	1,491.47 (-) [1,491.47]	552.33 (0.00) [36]
218	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (3/2024) [3/2024]	744.04 (1,215.54) [1,215.54]	513.54 (471.50) [36]
219	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (735.20) [735.20]	389.43 (410.20) [0]
220	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2023]	372.14 (1,470.50) [1,470.50]	1,436.01 (1,098.36) [-]
221	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [3/2025]	380.00 (-) [519.33]	309.90 (139.33) [-]
222	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	17.20 (0.00) [0]
<u>Road Transport And Highways</u>					
223	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [0/0]	511.54 (-) [591.00]	578.00 (79.46) [0]
224	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
225	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (12/2021) [0/0]	575.00 (-) [575.00]	503.83 (0.00) [0]
226	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	0.00 (0.00) [0]
227	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [0/0]	464.09 (-) [464.09]	0.00 (0.00) [0]
228	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [0/0]	649.90 (-) [649.90]	44.00 (0.00) [0]
229	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [0/0]	446.97 (-) [446.97]	0.00 (0.00) [0]
230	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	10/2019	2/2020 (-) [0/0]	1,101.99 (-) [1,101.99]	193.26 (0.00) [0]

231	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	218.52 (0.00) [0]
232	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING REHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	79.35 (0.00) [0]
233	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (1/2021) [0/0]	2,598.00 (1,962.50) [1,962.50]	235.00 (-635.50) [0]
234	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	11.00 (-7.71) [0]
235	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [537.17]	64.82 (40.97) [0]
236	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (683.82) [560.70]	694.71 (-123.13) [0]
237	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [152.62]	140.55 (-26.23) [0]
238	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	527.97 (-74.95) [0]
239	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [0/0]	1,167.45 (-) [1,182.94]	272.27 (15.49) [0]
240	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [0/0]	642.41 (-) [681.67]	503.71 (39.26) [0]
241	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [0/0]	322.09 (247.00) [322.09]	0.00 (0.00) [0]
242	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (2,138.16) [925.87]	1,209.93 (-482.98) [0]
243	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [10/2021]	814.04 (-) [825.17]	799.07 (11.13) [-]
244	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
245	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	414.67 (0.00) [0]
246	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.92 (0.00) [0]
247	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	1,197.27 (0.00) [0]
248	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,729.05 (0.00) [0]
249	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	82.47 (0.00) [0]
250	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	319.07 (50.09) [0]
251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE	1/1991	/	675.00	379.73

	WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR		(-) [0/0]	(780.77) [675.00]	(0.00) [0]
252	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/	895.39	0.00
			(-) [0/0]	(-) [895.39]	(0.00) [0]
253	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017	950.64	311.03
			(-) [2/2022]	(-) [950.64]	(0.00) [54]
254	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/	153.24	86.31
			(-) [0/0]	(-) [153.24]	(0.00) [0]
255	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/	854.80	1,023.88
			(-) [0/0]	(-) [1,038.56]	(183.76) [0]
256	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018	516.13	648.77
			(-) [0/0]	(-) [649.27]	(133.14) [0]
257	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020	672.89	75.90
			(-) [0/0]	(-) [736.01]	(63.12) [0]
	<u>Urban Development</u>				
258	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024	13,365.77	302.95
			(-) [6/2024]	(-) [13,925.50]	(559.73) [0]
	<u>Water Resources</u>				
259	I AND D AND STP AT CHAPRA	11/2018	12/2020	236.15	59.84
			(6/2021) [0/0]	(-) [236.15]	(0.00) [0]
260	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020	254.13	0.05
			(-) [0/0]	(-) [413.29]	(159.16) [0]
261	IRRIGATION WORK OF BAGMATI	10/2005	3/2015	956.00	712.37
			(-) [0/0]	(-) [721.37]	(-234.63) [0]
262	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021	268.63	326.75
			(-) [0/0]	(-) [268.63]	(0.00) [0]
263	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021	230.06	90.99
			(-) [7/2021]	(-) [230.06]	(0.00) [0]
264	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021	305.19	28.31
			(-) [12/2021]	(-) [305.19]	(0.00) [4]
265	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021	294.02	0.00
			(-) [10/2021]	(-) [294.02]	(0.00) [0]
266	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021	356.37	130.39
			(-) [4/2021]	(-) [356.37]	(0.00) [0]
267	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022	824.00	42.75
			(-) [6/2022]	(-) [824.00]	(0.00) [0]
268	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022	578.89	42.75
			(-) [6/2022]	(-) [578.89]	(0.00) [0]
269	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020	225.77	291.32
			(-) [3/2021]	(-) [398.90]	(173.13) [0]
270	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021	277.42	199.50
			(-) [5/2021]	(-) [277.42]	(0.00) [0]

271	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (3/2021) [0/0]	191.62 (-) [191.62]	64.43 (0.00) [0]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
272	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.42 (0.00) [60]
273	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	146.27 (0.00) [36]
274	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	314.88 (0.00) [0]
275	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	160.43 (0.00) [0]
276	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	2,025.60 (0.00) [0]
277	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2026]	916.24 (-) [916.24]	11.38 (0.00) [36]
278	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	4,639.30 (0.00) [0]
279	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	199.99 (307.06) [84]
280	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	185.35 (0.00) [0]
281	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
282	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	11.37 (0.00) [144]
283	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	3,118.22 (0.00) [0]
284	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2027]	1,875.32 (-) [1,875.32]	0.00 (0.00) [36]
285	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	40.57 (0.00) [0]
286	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2023]	321.50 (-) [321.50]	210.73 (0.00) [108]
287	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	9.08 (0.00) [0]
288	PORDA CHIMTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
289	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	76.12 (0.00) [0]
	<u>Department Of Higher Education</u>				
290	C/O PERMANENT CAMPUS OF IIT BHILAI AT	3/2020	7/2022	808.62	249.81

	KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.		(-) [10/2022]	(-) [808.62]	(0.00) [3]
	<u>Petroleum</u>				
291	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	3/2021	3/2024 (-) [3/2024]	456.00 (-) [456.00]	13.22 (0.00) [0]
	<u>Power</u>				
292	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	1,343.71 (0.00) [0]
	<u>Railways</u>				
293	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [0/0]	393.98 (-) [393.98]	339.31 (0.00) [0]
294	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [9/2023]	2,288.00 (-) [4,970.11]	953.27 (2,682.11) [18]
295	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023) [12/2023]	1,973.00 (2,135.34) [2,135.34]	700.69 (162.34) [33]
296	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [6/2022]	3,055.00 (-) [3,055.15]	2,707.85 (0.15) [45]
297	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	1,010.84 (0.83) [36]
298	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
299	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,347.35 (-102.02) [21]
	<u>Road Transport And Highways</u>				
300	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	402.95 (231.09) [0]
301	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [0/0]	726.67 (1,096.52) [1,096.52]	518.73 (369.85) [0]
302	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
303	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	439.27 (0.00) [0]
304	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (10/2021) [10/2021]	291.05 (-) [291.05]	238.67 (0.00) [-]
305	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (12/2021) [12/2021]	335.32 (-) [335.32]	279.60 (0.00) [54]
306	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (12/2021) [12/2021]	476.20 (543.73) [544.00]	400.86 (67.80) [63]
307	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (3/2022) [3/2022]	496.02 (-) [496.02]	250.97 (0.00) [84]
308	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (6/2022) [6/2022]	497.14 (572.66) [572.66]	284.62 (75.52) [70]
309	REHABILITATION AND UPGRADATION OF NH 78 FROM	1/2016	10/2016	624.98	470.70

	KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION		(12/2021) [12/2021]	(731.50) [731.50]	(106.52) [62]
310	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (12/2022) [12/2022]	452.94 (435.61) [435.61]	112.86 (-17.33) [77]
311	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (12/2021) [12/2021]	423.79 (-) [423.79]	295.71 (0.00) [47]
312	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (12/2021) [12/2021]	188.80 (-) [188.80]	90.41 (0.00) [31]
313	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (11/2021) [11/2021]	379.16 (-) [379.16]	322.96 (0.00) [48]
	<u>Steel</u>				
314	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (1/2022) [1/2022]	15,525.00 (21,940.00) [21,940.00]	19,016.02 (6,415.00) [80]
315	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (-) [6/2023]	2,907.00 (-) [2,907.00]	439.00 (0.00) [0]
316	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	70.05 (0.00) [0]
	<u>Urban Development</u>				
317	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	5/2019	9/2020 (1/2023) [1/2023]	299.97 (299.97) [299.97]	20.39 (0.00) [28]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
318	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [6/2022]	303.80 (351.21) [303.80]	189.25 (0.00) [26]
	<u>Commerce</u>				
319	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (302.64) [302.64]	30.00 (0.00) [0]
	<u>Dpiit</u>				
320	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (5/2022) [5/2022]	4,773.00 (-) [5,178.00]	3,013.69 (405.00) [29]
	<u>Health And Family Welfare</u>				
321	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	249.24 (45.56) [0]
322	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
323	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [11/2021]	156.56 (-) [190.34]	176.66 (33.78) [-]
324	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [9/2021]	414.11 (-) [586.50]	573.94 (172.39) [0]
	<u>Heavy Industry</u>				
325	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [0/0]	1,554.00 (-) [900.00]	815.00 (-654.00) [0]
	<u>Home Affairs</u>				
326	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/2019	7/2022 (10/2022)	277.35 (290.33)	27.25 (12.98)

			[10/2022]	[290.33]	[3]
327	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2022]	1,219.21 (-) [2,000.00]	1,007.93 (780.79) [29]
	<u>Power</u>				
328	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (12/2021) [12/2021]	1,394.52 (-) [1,394.52]	561.71 (0.00) [55]
	<u>Railways</u>				
329	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	160.79 (123.32) [-]
330	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [359.00]	116.87 (202.35) [-]
	<u>Renewable Energy</u>				
331	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [0/0]	271.90 (-) [271.90]	90.99 (0.00) [0]
	<u>Rural Development</u>				
332	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [0/0]	361.60 (-) [361.60]	12.44 (0.00) [0]
	<u>Telecommunications</u>				
333	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	3/2018 (-) [12/2021]	248.20 (-) [248.20]	145.26 (0.00) [45]
	<u>Urban Development</u>				
334	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (2/2022) [2/2022]	197.33 (217.00) [217.00]	173.51 (19.67) [34]
335	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	2,442.28 (0.00) [0]
336	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (9/2021) [0/0]	565.00 (-) [565.00]	484.46 (0.00) [0]
337	DELHI MRTS PHASE-III	9/2011	3/2016 (8/2021) [0/0]	38,585.00 (-) [38,585.00]	39,486.58 (0.00) [0]
338	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (11/2021) [11/2021]	238.56 (238.56) [238.56]	208.13 (0.00) [18]
339	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (6/2023) [6/2023]	1,180.00 (1,100.80) [1,100.80]	35.74 (-79.20) [23]
340	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (6/2022) [6/2022]	392.00 (392.00) [392.00]	161.81 (0.00) [22]
341	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [6/2023]	1,128.00 (1,128.00) [1,128.00]	30.00 (0.00) [15]
342	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (6/2023) [6/2023]	422.00 (422.00) [422.00]	108.75 (0.00) [27]
343	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [12/2022]	2,694.00 (-) [2,694.00]	896.32 (0.00) [-]
	<u>Water Resources</u>				
344	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN	5/2017	5/2020 (-)	344.81 (-)	0.00 (0.00)

	DHANSA TO		[0/0]	[344.81]	[0]
345	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [6/2021]	515.07 (-) [515.07]	336.27 (0.00) [0]
346	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	230.58 (0.00) [0]
347	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	108.28 (0.00) [12]
348	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	149.02 (0.00) [10]
	<u>GOA</u>				
	<u>Department Of Higher Education</u>				
349	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [0/0]	303.90 (-) [303.90]	37.80 (0.00) [0]
	<u>Health And Family Welfare</u>				
350	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [1/2021]	249.01 (-) [249.07]	231.05 (0.06) [0]
	<u>Road Transport And Highways</u>				
351	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	244.36 (10.43) [0]
352	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	118.37 (0.00) [0]
353	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	520.09 (0.00) [0]
354	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	325.55 (0.00) [0]
355	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [0/0]	852.67 (-) [852.67]	190.09 (0.00) [0]
356	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [0/0]	634.32 (-) [634.32]	292.34 (0.00) [0]
357	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	394.63 (0.00) [0]
358	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	362.15 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
359	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [2/2022]	11,459.00 (-) [16,580.00]	17,298.00 (5,121.00) [74]
	<u>Civil Aviation</u>				
360	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (-) [3/2023]	1,405.00 (-) [1,405.00]	368.21 (0.00) [7]
	<u>Petroleum</u>				
361	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	552.22 (0.00) [0]
362	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6	3/2018	/	588.20	157.01

	MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT		(5/2023) [5/2023]	(730.20) [730.20]	(142.00) [-]
363	AUGMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023 (-) [8/2023]	1,614.00 (-) [1,614.00]	1.12 (0.00) [0]
364	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [12/2021]	327.78 (-) [200.00]	197.30 (-127.78) [44]
365	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [3/2022]	906.00 (-) [906.00]	345.08 (0.00) [25]
366	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK)	10/2018	3/2021 (5/2022) [5/2022]	156.67 (-) [156.67]	62.93 (0.00) [14]
367	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [4/2022]	403.00 (-) [403.00]	181.90 (0.00) [4]
368	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024 (-) [8/2024]	18,936.00 (-) [18,936.00]	796.97 (0.00) [-1]
369	REDEVELOPMENT OF LINCH FIELD	4/2021	3/2025 (-) [3/2025]	631.03 (-) [631.03]	217.38 (0.00) [0]
370	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022 (-) [8/2022]	444.87 (-) [444.87]	115.83 (0.00) [0]
371	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [970.30]	947.93 (-192.26) [0]
372	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [12/2022]	1,378.00 (-) [1,378.00]	166.08 (0.00) [0]
373	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECT	9/2018	2/2021 (-) [8/2022]	225.54 (247.90) [247.90]	47.78 (22.36) [18]
	<u>Power</u>				
374	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	5/2021	9/2022 (-) [9/2022]	674.92 (-) [674.92]	76.00 (0.00) [0]
375	GUJARAT 200 MW (GUVNL TENDER)	1/2021	7/2022 (-) [6/2022]	842.27 (-) [842.27]	92.08 (0.00) [-1]
376	KAWAS SOLAR 56 MW	8/2020	10/2021 (1/2022) [11/2021]	261.80 (-) [261.80]	87.43 (0.00) [1]
377	SHIYAL SOLAR POWER PROJECT	5/2021	10/2022 (-) [10/2022]	296.20 (-) [296.20]	0.00 (0.00) [0]
	<u>Railways</u>				
378	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,650.00]	1,689.43 (674.38) [0]
379	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,246.59) [1,886.76]	1,875.42 (1,057.02) [48]
380	ANAND GODHRA DOUBLING PROJECT 79 KMS	4/2017	3/2020 (-) [3/2023]	692.25 (-) [692.25]	0.77 (0.00) [36]
381	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (10/2023) [10/2023]	318.24 (321.62) [321.62]	126.36 (3.38) [139]

382	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [12/2021]	644.38 (-) [872.65]	937.77 (228.27) [9]
383	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	4/2018	3/2024 (-) [3/2024]	537.31 (-) [537.31]	0.64 (0.00) [0]
384	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2024) [3/2024]	844.10 (844.10) [844.10]	254.99 (0.00) [-]
385	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
386	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (12/2021) [0/0]	153.83 (154.15) [154.15]	103.45 (0.32) [0]
387	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	2,128.65 (320.23) [3]
388	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (858.96) [1,378.11]	558.66 (1,057.45) [48]
389	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,002.39) [1,042.12]	730.07 (39.73) [21]
390	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (12/2022) [12/2022]	1,037.15 (1,125.53) [1,383.69]	1,199.84 (346.54) [21]
391	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (12/2022) [0/0]	248.26 (528.49) [528.49]	123.75 (280.23) [0]
Road Transport And Highways					
392	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	199.86 (0.00) [0]
393	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	235.85 (0.00) [0]
394	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [0/0]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [0]
395	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	439.91 (0.00) [0]
396	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [4/2021]	364.56 (-) [392.00]	353.42 (27.44) [0]
397	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
398	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	564.11 (0.00) [0]
399	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [0/0]	2,702.05 (-) [2,043.00]	1,888.51 (-659.05) [0]
400	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	175.16 (0.00) [0]
401	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	301.45 (0.00) [0]

402	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	602.77 (0.00) [0]
403	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	737.67 (0.00) [0]
404	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	505.33 (0.00) [0]
405	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
406	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	414.25 (0.00) [0]
407	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.44 (0.00) [0]
408	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
409	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	0.00 (0.00) [0]
410	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (1/2019) [0/0]	1,052.21 (-) [1,361.00]	449.41 (308.79) [0]
411	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (1/2019) [0/0]	1,251.11 (1,361.00) [1,361.00]	449.41 (109.89) [0]
412	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
413	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	172.78 (0.00) [0]
414	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	314.18 (0.00) [0]
	<u>Urban Development</u>				
415	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,787.00]	9,472.48 (2,014.00) [44]
416	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	247.58 (0.00) [0]
417	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	208.21 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
418	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (6/2021) [10/2021]	215.92 (-) [215.92]	172.93 (0.00) [23]
	<u>Health And Family Welfare</u>				
419	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [585.00]	586.96 (79.42) [0]
	<u>Home Affairs</u>				
420	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E.	1/2020	10/2023 (-)	166.98 (167.00)	0.00 (0.00)

	TYPE-		[10/2023]	[166.98]	[0]
	<u>Petroleum</u>				
421	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MTPA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	466.97 (0.00) [0]
422	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	466.82 (0.00) [14]
423	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (7/2022) [7/2022]	206.63 (340.76) [340.76]	145.36 (134.13) [29]
424	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	155.75 (0.00) [5]
425	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [3/2022]	164.69 (-) [164.69]	16.46 (0.00) [8]
426	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	419.33 (0.00) [24]
427	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	100.38 (0.00) [13]
428	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [4/2022]	1,636.00 (-) [1,636.00]	924.60 (0.00) [20]
429	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [12/2021]	1,255.00 (-) [1,255.00]	298.37 (0.00) [2]
430	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (3,199.60) [2,281.94]	553.94 (0.00) [7]
431	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (5/2021) [12/2021]	286.42 (327.01) [327.01]	223.50 (40.59) [16]
	<u>Railways</u>				
432	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [0/0]	346.32 (-) [346.32]	320.28 (0.00) [0]
433	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	717.17 (606.45) [0]
	<u>Road Transport And Highways</u>				
434	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	0.00 (-95.25) [0]
435	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	0.00 (-37.12) [0]
436	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [9/2021]	2,128.72 (-) [2,128.72]	1,577.44 (0.00) [0]
437	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [0/0]	247.25 (-) [247.25]	179.30 (0.00) [0]
438	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	275.72 (0.00) [0]
439	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]

440	ISMAILABAD-NARNAUL PKG-1	1/2019	/	996.65	1,000.97
			(-)	(-)	(0.00)
			[0/0]	[996.65]	[0]
441	ISMAILABAD-NARNAUL PKG-2	1/2019	/	1,243.45	985.75
			(-)	(-)	(0.00)
			[0/0]	[1,243.45]	[0]
442	ISMAILABAD-NARNAUL PKG-3	1/2019	/	889.36	692.40
			(-)	(-)	(0.00)
			[0/0]	[889.36]	[0]
443	ISMAILABAD-NARNAUL PKG-4	1/2019	/	1,018.79	804.31
			(-)	(-)	(0.00)
			[0/0]	[1,018.79]	[0]
444	ISMAILABAD-NARNAUL PKG-5	1/2019	/	1,051.91	870.68
			(-)	(-)	(0.00)
			[0/0]	[1,051.91]	[0]
445	ISMAILABAD-NARNAUL PKG-6	1/2019	/	1,120.06	905.59
			(-)	(-)	(0.00)
			[0/0]	[1,120.06]	[0]
446	ISMAILABAD-NARNAUL PKG-7	1/2019	/	1,137.42	978.00
			(-)	(-)	(0.00)
			[0/0]	[1,137.42]	[0]
447	ISMAILABAD-NARNAUL PKG-8	1/2019	/	1,033.19	898.54
			(-)	(-)	(0.00)
			[0/0]	[1,033.19]	[0]
448	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011	1,108.00	3,450.00
			(-)	(3,485.00)	(1,180.00)
			[0/0]	[2,288.00]	[0]
449	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/	275.12	172.62
			(-)	(-)	(0.00)
			[0/0]	[275.12]	[0]
450	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/	181.78	129.84
			(-)	(-)	(0.00)
			[0/0]	[181.78]	[0]
451	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/	198.05	136.17
			(-)	(-)	(0.00)
			[0/0]	[198.05]	[0]
452	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/	795.50	387.49
			(2/2018)	(906.65)	(127.14)
			[2/2018]	[922.64]	[0]
453	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/	634.70	341.09
			(2/2018)	(-)	(291.26)
			[2/2018]	[925.96]	[0]
HIMACHAL PRADESH					
Department Of Higher Education					
454	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	270.83	241.67
			(11/2021)	(-)	(-26.83)
			[11/2021]	[244.00]	[84]
455	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022	392.51	57.47
			(-)	(-)	(0.00)
			[6/2022]	[392.51]	[0]
Health And Family Welfare					
456	AIIMS BILASPUR	4/2018	9/2021	1,351.00	870.80
			(-)	(-)	(120.00)
			[6/2022]	[1,471.00]	[9]
457	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021	260.00	25.38
			(-)	(-)	(0.00)
			[5/2022]	[260.00]	[11]
Power					
458	DHAULASIDH HYDROELECTRIC PROJECT (66 MW)	10/2020	11/2025	687.97	182.27
			(-)	(-)	(0.00)
			[11/2025]	[687.97]	[0]

459	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	532.10 (0.00) [0]
460	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (3/2023) [3/2023]	3,919.59 (9,897.59) [9,897.59]	9,279.64 (5,978.00) [162]
	Railways				
461	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [6,753.42]	1,809.22 (3,786.43) [-12]
	Road Transport And Highways				
462	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [0/0]	273.20 (-) [273.20]	669.49 (0.00) [0]
463	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	1,025.14 (0.00) [0]
464	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
465	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (3/2021) [0/0]	934.46 (-) [934.46]	1,299.17 (0.00) [0]
466	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH- 22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (11/2021) [0/0]	478.74 (-) [478.74]	727.92 (0.00) [0]
467	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	860.13 (0.00) [0]
468	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [0/0]	447.75 (-) [447.75]	1,340.40 (0.00) [0]
469	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50.	8/2020	3/2021 (-) [0/0]	242.80 (-) [242.80]	10.23 (0.00) [0]
470	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA	8/2020	4/2021 (-) [0/0]	272.98 (-) [272.98]	11.86 (0.00) [0]
471	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75	8/2020	4/2021 (-) [0/0]	349.20 (-) [349.20]	17.99 (0.00) [0]
472	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]
	JAMMU AND KASHMIR				
	Department Of Higher Education				
473	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (748.19) [676.00]	213.47 (0.00) [0]
474	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [10/2022]	424.93 (-) [424.93]	55.00 (0.00) [3]
	Health And Family Welfare				
475	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	201.80 (0.00) [-16]
476	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
477	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-)	1,404.00 (-)	333.02 (0.00)

			[9/2023]	[1,404.00]	[0]
	<u>Power</u>				
478	KIRU HYDRO ELECTRIC PROJECT	3/2019	/ (8/2024) [8/2024]	4,287.59 (-) [4,287.59]	597.82 (0.00) [-]
479	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (7/2025) [7/2025]	8,112.12 (-) [8,112.12]	2,083.10 (0.00) [63]
	<u>Railways</u>				
480	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (27,949.00) [27,949.00]	25,828.58 (25,449.00) [241]
	<u>Road Transport And Highways</u>				
481	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	275.00 (0.00) [0]
482	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	953.12 (-132.75) [0]
483	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	878.00 (0.00) [0]
484	DONIPAWA TO ASHAJIPORA BYPASS PKG-7	3/2021	12/2022 (-) [12/2022]	260.40 (-) [260.40]	0.00 (0.00) [0]
485	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [0/0]	2,168.66 (-) [2,168.66]	1,158.40 (0.00) [0]
486	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,763.58 (0.00) [0]
487	GOHA-KHELLANI PKG-3	2/2021	3/2023 (-) [3/2023]	431.28 (-) [431.28]	4.14 (0.00) [0]
488	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,653.88 (0.00) [0]
489	KHELLANI-KHANABAL PKG-1	3/2021	9/2022 (-) [9/2022]	486.45 (-) [486.45]	36.09 (0.00) [0]
490	KHELLANI-KHANABAL PKG-2	7/2021	2/2023 (-) [2/2023]	512.43 (-) [512.43]	0.00 (0.00) [0]
491	KHELLANI-KHANABAL PKG-3	3/2021	12/2022 (-) [12/2022]	398.51 (-) [398.51]	0.00 (0.00) [0]
492	KHELLANI-KHANABAL PKG-4	7/2021	8/2023 (-) [8/2023]	859.67 (-) [859.67]	0.00 (0.00) [0]
493	KHELLANI-KHANABAL PKG-5	7/2021	2/2023 (-) [2/2023]	497.09 (-) [497.09]	0.00 (0.00) [0]
494	KHELLANI-KHANABAL PKG-6	2/2021	9/2022 (-) [9/2022]	285.28 (-) [285.28]	18.65 (0.00) [0]
495	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,758.92 (360.00) [0]
496	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,116.66 (0.00) [0]

497	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,933.30 (0.00) [0]
498	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	17.68 (0.00) [0]
499	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [4/2022]	210.79 (-) [210.79]	17.58 (0.00) [0]
500	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	85.34 (0.00) [0]
501	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	222.70 (0.00) [0]
502	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	112.12 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
503	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	159.28 (0.00) [0]
504	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	124.85 (0.00) [132]
505	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	257.70 (0.00) [0]
506	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	89.46 (0.00) [96]
507	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [12/2021]	289.45 (-) [289.45]	285.81 (0.00) [91]
508	MAGADH EXPANSION OC(51 MTY)	8/2008	7/2012 (3/2028) [3/2028]	6,964.33 (7,254.37) [7,254.37]	729.50 (290.04) [188]
509	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [2/2023]	1,230.27 (-) [1,230.27]	501.39 (0.00) [94]
510	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [4/2023]	339.88 (-) [339.88]	69.37 (0.00) [108]
511	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2022]	555.52 (-) [555.52]	5.87 (0.00) [12]
512	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [778.80]	349.76 (-774.26) [0]
513	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	37.13 (0.00) [13]
514	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [10/2022]	243.00 (334.27) [334.27]	24.86 (91.27) [54]
515	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	211.94 (0.00) [0]
516	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-)	510.85 (-)	497.97 (0.00)

			[3/2022]	[510.85]	[72]
517	RECAST EPR AMRAPALI OC	2/2012	3/2020 (3/2028) [3/2028]	4,983.58 (4,983.58) [4,983.58]	360.01 (0.00) [96]
518	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	37.16 (0.00) [0]
	<u>Department Of Higher Education</u>				
519	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [0/0]	171.86 (-) [171.86]	111.29 (0.00) [0]
	<u>Petroleum</u>				
520	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [3/2022]	161.50 (-) [161.50]	111.34 (0.00) [21]
521	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	12/2029 (-) [12/2029]	613.00 (-) [613.00]	157.77 (0.00) [0]
522	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	133.18 (0.00) [0]
523	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	105.20 (0.00) [0]
524	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	730.57 (314.52) [-12]
525	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [9/2022]	248.55 (-) [248.55]	136.91 (0.00) [3]
	<u>Power</u>				
526	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [9/2023]	14,366.58 (-) [15,389.42]	12,291.69 (1,022.84) [51]
527	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,824.26 (314.04) [0]
528	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [2/2025]	18,668.00 (-) [17,112.00]	4,391.63 (-1,556.00) [23]
	<u>Railways</u>				
529	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2023]	1,724.20 (-) [1,724.20]	1,028.57 (0.00) [33]
530	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [3/2022]	348.23 (-) [390.00]	386.59 (41.77) [12]
531	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (3/2022) [3/2022]	1,033.07 (3,020.95) [3,630.00]	3,630.96 (2,596.93) [-]
532	KODERMA-TILAIYA (NL), ECR	4/2002	/ (3/2023) [3/2023]	459.91 (1,625.87) [1,625.87]	904.73 (1,165.96) [-]
	<u>Road Transport And Highways</u>				
533	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2021) [0/0]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [0]
534	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	109.40 (2.71) [0]
535	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018	323.72	316.60

			(-) [0/0]	(-) [336.60]	(12.88) [0]
536	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/	1,155.16	498.07
			(-) [0/0]	(-) [1,155.16]	(0.00) [0]
537	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/	458.03	406.73
			(-) [0/0]	(-) [486.00]	(27.97) [0]
538	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021	196.00	109.08
			(-) [9/2021]	(-) [196.00]	(0.00) [0]
	<u>Steel</u>				
539	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017	1,034.01	557.75
			(12/2021) [11/2022]	(-) [1,034.01]	(0.00) [61]
540	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019	262.87	207.19
			(10/2021) [12/2021]	(-) [262.87]	(0.00) [30]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
541	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020	246.31	149.80
			(10/2021) [12/2021]	(210.00) [210.00]	(-36.31) [22]
	<u>Department Of Higher Education</u>				
542	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022	851.00	26.10
			(-) [9/2022]	(851.00) [851.00]	(0.00) [6]
	<u>Petroleum</u>				
543	BSVI UPGRADATION	9/2016	12/2019	1,810.00	1,766.26
			(4/2021) [2/2022]	(1,810.00) [1,810.00]	(0.00) [26]
544	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022	854.00	179.41
			(-) [12/2022]	(-) [854.00]	(0.00) [0]
545	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023	200.00	2.56
			(1/2024) [1/2024]	(304.00) [304.00]	(104.00) [7]
546	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022	2,166.38	1,334.00
			(-) [6/2022]	(-) [2,166.38]	(0.00) [0]
547	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021	206.26	155.99
			(-) [11/2021]	(-) [206.26]	(0.00) [8]
548	SEA WATER DESALINATION PLANT	11/2017	3/2020	581.00	534.34
			(11/2020) [11/2021]	(637.00) [637.00]	(56.00) [20]
549	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021	380.00	306.50
			(-) [3/2022]	(-) [380.00]	(0.00) [4]
	<u>Railways</u>				
550	ARSIKERE-TUMKUR	3/2015	3/2020	578.00	642.52
			(12/2021) [12/2021]	(-) [760.00]	(182.00) [21]
551	BAGALKOT-KUDACHI NL	4/2010	3/2016	986.30	316.23
			(-) [12/2026]	(-) [1,530.09]	(543.79) [129]
552	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002	1,382.78	7.35
			(-) [3/2024]	(-) [1,960.00]	(577.22) [264]
553	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/	327.25	0.00
			(-)	(-)	(40.52)

			[12/2023]	[367.77]	[-]
554	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/	558.00	0.00
			(-)	(-)	(134.43)
			[12/2023]	[692.43]	[-]
555	GADAG-WADI NL	4/2013	12/2018	2,841.84	373.87
			(-)	(-)	(0.00)
			[6/2025]	[2,841.84]	[78]
556	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023	2,127.00	2,400.15
			(-)	(-)	(873.00)
			[12/2022]	[3,000.00]	[-3]
557	HUBLI- CHIKJAJUR	3/2015	3/2020	1,156.94	1,174.76
			(-)	(-)	(811.06)
			[3/2023]	[1,968.00]	[36]
558	HUBLI-ANKOLA(NL),SWR	4/1997	/	2,315.00	158.11
			(-)	(-)	(2,859.30)
			[12/2024]	[5,174.30]	[-]
559	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017	644.78	469.70
			(-)	(889.00)	(88.11)
			[3/2025]	[732.89]	[96]
560	MARIKUPPAM - KUPPAM	4/2012	3/2016	279.54	36.97
			(-)	(-)	(0.00)
			[12/2023]	[279.54]	[93]
561	SHIMOGA-HARIHAR NL	4/2011	3/2016	832.47	0.94
			(-)	(-)	(0.00)
			[3/2024]	[832.47]	[96]
562	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/	1,801.01	82.47
			(-)	(-)	(360.35)
			[12/2023]	[2,161.36]	[-]
563	WHITE FIELD-KOLAR NL	4/2011	/	348.85	0.36
			(-)	(-)	(0.00)
			[12/2025]	[348.85]	[-]
	<u>Road Transport And Highways</u>				
564	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019	1,167.42	348.00
			(1/2021)	(-)	(-297.42)
			[12/2022]	[870.00]	[45]
565	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/	486.78	171.98
			(-)	(-)	(0.00)
			[0/0]	[486.78]	[0]
566	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016	1,655.01	1,867.51
			(-)	(-)	(0.00)
			[12/2020]	[1,655.01]	[0]
567	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019	701.40	146.05
			(-)	(-)	(0.00)
			[3/2022]	[701.40]	[36]
568	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019	870.00	36.30
			(-)	(-)	(0.00)
			[11/2020]	[870.00]	[0]
569	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	3/2019	12/2019	423.15	140.05
			(-)	(-)	(0.00)
			[0/0]	[423.15]	[0]
570	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019	157.32	0.28
			(-)	(188.00)	(0.00)
			[0/0]	[157.32]	[0]
571	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018	171.60	80.28
			(-)	(-)	(0.00)
			[0/0]	[171.60]	[0]
572	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018	1,388.00	1,311.10
			(-)	(-)	(0.00)
			[0/0]	[1,388.00]	[0]
573	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020	1,664.20	1,158.53
			(-)	(-)	(0.00)

			[12/2020]	[1,664.20]	[0]
574	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [0/0]	946.00 (-) [946.00]	818.53 (0.00) [0]
575	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [386.41]	345.82 (60.55) [0]
576	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	162.88 (0.00) [0]
577	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	61.80 (0.00) [0]
578	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,311.37 (440.84) [0]
579	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	912.41 (345.42) [0]
580	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,498.34 (272.20) [0]
581	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,378.36 (404.66) [-]
582	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	116.49 (0.00) [0]
583	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [9/2019]	709.00 (-) [709.00]	541.35 (0.00) [0]
584	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (1,918.36) [1,108.00]	1,462.67 (157.31) [0]
585	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	290.17 (0.00) [0]
586	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	212.86 (0.00) [0]
587	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	238.12 (0.00) [0]
588	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	1/2017	9/2017 (-) [0/0]	264.34 (-) [264.34]	184.91 (0.00) [0]
589	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	110.75 (0.00) [0]
590	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	221.32 (0.00) [0]
591	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	184.91 (0.00) [0]
592	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [318.28]	181.43 (20.98) [0]
593	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	116.36 (0.00) [0]

594	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	125.81 (0.00) [0]
	<u>Urban Development</u>				
595	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (3/2025) [3/2025]	26,405.14 (30,695.12) [30,695.12]	18,874.67 (4,289.98) [73]
	<u>KERALA</u>				
	<u>Department Of Higher Education</u>				
596	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [2/2023]	753.63 (-) [753.63]	177.82 (0.00) [23]
597	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [0/0]	165.23 (-) [165.23]	118.52 (0.00) [0]
	<u>Health And Family Welfare</u>				
598	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	64.32 (0.00) [21]
	<u>Petroleum</u>				
599	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	769.00 (395.24) [32]
600	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [9/2022]	607.06 (1,236.00) [1,236.00]	500.28 (628.94) [59]
601	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	425.30 (0.00) [0]
	<u>Power</u>				
602	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (12/2021) [12/2021]	403.62 (-) [403.62]	116.32 (0.00) [6]
	<u>Railways</u>				
603	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (1,566.00) [2,815.62]	264.50 (1,249.62) [0]
604	ERNAKULAM-KUMBALAM	4/2010	/ (-) [3/2025]	189.24 (275.21) [448.10]	6.73 (258.86) [-]
605	KUMBALAM-TURAVUR	4/2011	/ (-) [3/2025]	252.96 (369.55) [709.69]	8.50 (456.73) [-]
606	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
607	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [3/2024]	1,431.90 (-) [1,431.90]	492.74 (0.00) [-]
608	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [3/2025]	1,000.00 (1,246.00) [1,339.00]	0.82 (339.00) [-]
	<u>Road Transport And Highways</u>				
609	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (1/2020) [1/2020]	845.24 (-) [941.00]	902.51 (95.76) [0]
610	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (10/2021) [10/2021]	804.97 (-) [804.97]	594.02 (0.00) [40]
611	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-)	1,124.11 (-)	629.21 (108.65)

			[0/0]	[1,232.76]	[0]
612	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
613	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [0/0]	255.75 (348.00) [348.43]	314.12 (92.68) [0]
614	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [0/0]	617.00 (-) [617.00]	0.00 (0.00) [0]
615	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK	2/2017	8/2017 (-) [0/0]	294.28 (-) [294.26]	138.25 (-0.02) [0]
616	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49)	2/2017	9/2017 (-) [0/0]	380.76 (-) [380.76]	242.85 (0.00) [0]
	<u>Urban Development</u>				
617	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (9/2020) [9/2020]	5,181.79 (6,218.14) [6,218.14]	6,059.17 (1,036.35) [0]
	<u>LADAKH</u>				
	<u>Civil Aviation</u>				
618	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [12/2022]	346.27 (-) [480.33]	114.59 (134.06) [15]
	<u>Road Transport And Highways</u>				
619	KARGIL-ZANSKR PACKAGE-1	3/2021	1/2023 (-) [1/2023]	384.23 (-) [384.23]	7.11 (0.00) [0]
620	KARGIL-ZANSKR PACKAGE-2	3/2021	1/2023 (-) [1/2023]	404.89 (-) [404.89]	0.00 (0.00) [0]
621	KARGIL-ZANSKR PACKAGE-3	8/2020	1/2023 (-) [1/2023]	381.01 (-) [381.01]	0.00 (0.00) [0]
622	KARGIL-ZANSKR PACKAGE-5	8/2020	12/2023 (-) [12/2023]	169.79 (-) [169.79]	40.96 (0.00) [0]
623	KARGIL-ZANSKR PACKAGE-6	1/2021	5/2024 (-) [5/2024]	239.81 (-) [239.81]	31.14 (0.00) [0]
624	KARGIL-ZANSKR PACKAGE-7	1/2021	6/2024 (-) [6/2024]	308.86 (-) [308.86]	31.14 (0.00) [0]
625	KARGIL-ZANSKR PACKAGE-8	3/2021	1/2023 (-) [1/2023]	398.37 (-) [398.37]	3.39 (0.00) [0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
626	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (-) [12/2022]	412.24 (-) [412.24]	212.35 (0.00) [18]
	<u>Coal</u>				
627	AMADAND OPENCASET EXPANSION PROJECT	3/2016	3/2021 (-) [3/2022]	869.44 (-) [869.44]	127.49 (0.00) [12]
628	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2027]	481.60 (-) [481.60]	0.00 (0.00) [48]
629	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-)	231.92 (-)	1.78 (0.00)

			[3/2025]	[231.92]	[36]
630	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2026]	1,186.64 (-) [1,186.64]	234.04 (0.00) [36]
631	BATURA WEST OC PROJECT (0.80 MTY)	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]
632	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
633	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2023]	1,255.17 (-) [1,255.17]	316.50 (0.00) [12]
634	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	1.00 (0.00) [0]
635	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2022]	1,783.09 (-) [1,783.09]	825.70 (0.00) [12]
636	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	66.57 (0.00) [36]
637	NIGAH EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
638	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (4/2024) [4/2024]	357.80 (-) [357.80]	100.65 (0.00) [37]
639	RPR FOR JAMUNIA UG (0.90 MTY)	7/2016	3/2022 (3/2026) [3/2026]	281.25 (-) [281.25]	18.24 (0.00) [48]
640	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
641	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
642	CGD PROJECT AT REWA DISTRICT	10/2018	2/2027 (-) [2/2027]	177.00 (-) [177.00]	62.90 (0.00) [0]
643	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (12/2021) [12/2021]	236.00 (319.61) [319.61]	219.15 (83.61) [18]
	<u>Power</u>				
644	AMELIA COAL MINE	1/2017	9/2020 (8/2022) [8/2022]	2,104.21 (1,587.16) [1,587.16]	629.21 (-517.05) [23]
	<u>Railways</u>				
645	ANUPPUR-KATNI	4/2015	12/2021 (12/2023) [12/2023]	1,370.00 (1,370.94) [1,370.94]	712.76 (0.94) [24]
646	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	1,972.62 (349.98) [12]
647	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (12/2021) [12/2021]	585.93 (1,268.32) [1,268.32]	1,082.34 (682.39) [34]
648	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	314.13 (-96.31) [33]

649	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2024]	1,763.93 (-) [2,449.00]	1,293.48 (685.07) [48]
650	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2023]	582.13 (1,247.64) [1,247.64]	508.67 (665.51) [12]
651	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (6/2023) [6/2023]	2,478.23 (2,875.12) [2,875.12]	1,035.16 (396.89) [15]
652	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [0/0]	174.00 (-) [174.00]	172.08 (0.00) [0]
653	NIMACH BADI SADRI NEW LINE PROJECT	4/2017	3/2022 (-) [3/2024]	495.18 (-) [495.18]	0.33 (0.00) [24]
654	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2024) [3/2024]	424.60 (2,909.99) [2,909.99]	1,378.97 (2,485.39) [36]
655	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023) [3/2023]	3,503.69 (5,839.02) [6,171.08]	2,327.60 (2,667.39) [12]
Road Transport And Highways					
656	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (8/2021) [12/2021]	249.05 (-) [249.05]	198.83 (0.00) [41]
657	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	11/2019	7/2021 (-) [0/0]	716.00 (-) [716.00]	0.00 (0.00) [0]
658	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	322.21 (0.00) [0]
659	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [3/2022]	950.27 (-) [950.27]	282.63 (0.00) [-]
660	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [12/2021]	392.33 (428.55) [428.55]	390.40 (36.22) [45]
661	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	193.99 (0.00) [0]
662	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	316.97 (-169.75) [0]
663	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (11/2021) [11/2021]	990.61 (-) [990.61]	719.29 (0.00) [50]
664	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [3/2022]	390.51 (-) [390.51]	281.69 (0.00) [-]
665	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	297.00 (183.02) [-]
666	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	429.00 (0.01) [-]
667	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	827.00 (0.00) [-]
668	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [10/2022]	217.96 (-) [884.00]	486.00 (666.04) [-]

669	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (6/2021) [12/2021]	205.05 (-) [205.05]	129.31 (0.00) [57]
670	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2021) [3/2022]	264.50 (-) [264.50]	139.54 (0.00) [12]
671	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
672	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
673	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [0/0]	928.83 (-) [928.83]	867.83 (0.00) [0]
674	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [0/0]	794.30 (-) [691.38]	669.35 (-102.92) [0]
675	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [0/0]	795.76 (-) [686.13]	669.94 (-109.63) [0]
676	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [0/0]	810.22 (-) [810.22]	742.47 (0.00) [0]
677	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [0/0]	639.97 (-) [639.97]	485.73 (0.00) [0]
678	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	415.50 (0.00) [0]
679	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (8/2021) [11/2021]	957.54 (-) [957.54]	773.30 (0.00) [21]
680	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
681	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
682	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (6/2021) [11/2021]	628.45 (-) [628.45]	448.61 (0.00) [22]
683	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	410.72 (-) [410.72]	392.42 (0.00) [0]
684	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [12/2021]	990.97 (-) [990.97]	718.00 (0.00) [24]
685	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [5/2022]	1,047.00 (-) [1,047.00]	538.00 (0.00) [24]
686	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [4/2022]	847.00 (-) [847.00]	556.00 (0.00) [25]
687	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [0/0]	996.27 (-) [996.27]	601.00 (0.00) [0]
688	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (4/2021) [4/2022]	169.63 (-) [169.63]	61.20 (0.00) [49]
689	REHABILITATION AND UPGRADATION OF BARELI TO	3/2016	6/2019	877.79	743.57

	GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM		(4/2021) [12/2021]	(-) [877.79]	(0.00) [30]
690	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [12/2021]	809.16 (-) [809.16]	615.21 (0.00) [41]
691	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [12/2022]	511.83 (-) [511.83]	403.23 (0.00) [64]
692	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2022) [3/2022]	254.17 (-) [254.17]	183.37 (0.00) [49]
693	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [12/2021]	233.04 (-) [233.04]	166.48 (0.00) [45]
694	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (11/2021) [11/2021]	279.44 (-) [279.44]	223.22 (0.00) [44]
695	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (8/2021) [12/2021]	166.21 (174.90) [174.90]	154.26 (8.69) [40]
696	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (9/2021) [12/2021]	184.62 (-) [184.62]	125.42 (0.00) [46]
697	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (9/2021) [6/2022]	214.69 (-) [214.69]	80.06 (0.00) [51]
698	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021) [12/2021]	217.22 (-) [226.88]	182.97 (9.66) [40]
699	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [12/2021]	162.56 (-) [162.56]	137.52 (0.00) [45]
700	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (6/2021) [12/2021]	373.82 (-) [373.82]	238.57 (0.00) [27]
	<u>Urban Development</u>				
701	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	248.29 (0.00) [0]
702	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	142.54 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
703	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [8/2022]	475.39 (-) [475.39]	169.84 (0.00) [16]
	<u>Coal</u>				
704	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (333.43) [333.43]	145.08 (44.53) [12]
705	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (745.03) [745.03]	390.11 (17.75) [0]
706	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	252.71 (-) [252.71]	103.38 (0.00) [18]
707	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (409.68) [409.68]	86.90 (221.74) [0]
708	BHATADI EXPANSION OC MINE	2/2016	3/2019	304.52	160.84

			(-) [3/2022]	(327.41) [327.41]	(22.89) [36]
709	DHUPTALA OC(SASTI UG TO OC)	2/2019	3/2028 (-) [3/2028]	720.87 (-) [720.87]	9.86 (0.00) [0]
710	GHONSA EXPANSION DEEP OC	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	57.00 (0.00) [0]
711	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (9/2022) [9/2022]	362.73 (402.90) [402.90]	336.00 (40.17) [30]
712	NEW MAJRI UG TO OC	5/2015	3/2019 (3/2022) [3/2022]	295.56 (299.67) [299.67]	164.36 (4.11) [36]
713	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	3/2020 (3/2027) [3/2027]	1,184.33 (-) [1,184.33]	392.88 (0.00) [84]
714	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	3/2021 (3/2024) [3/2024]	313.34 (-) [313.34]	149.32 (0.00) [36]
715	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	3/2020 (3/2026) [3/2026]	851.60 (826.80) [826.80]	233.76 (-24.80) [72]
716	SASTI EXPANSION OC	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	52.55 (0.00) [0]
717	UKNI DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	318.14 (-) [318.14]	217.47 (0.00) [18]
<u>Department Of Higher Education</u>					
718	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [12/2021]	223.37 (-) [223.37]	117.64 (0.00) [17]
<u>Fertilisers</u>					
719	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (10/2021) [10/2021]	426.72 (-) [426.72]	314.91 (0.00) [18]
<u>Health And Family Welfare</u>					
720	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [10/2021]	582.99 (-) [582.99]	541.38 (0.00) [-]
721	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	259.46 (0.00) [0]
<u>Petroleum</u>					
722	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [3/2022]	249.26 (-) [249.26]	183.21 (0.00) [21]
723	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [9/2021]	261.00 (-) [261.00]	183.60 (0.00) [0]
724	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [9/2021]	212.00 (-) [212.00]	172.42 (0.00) [0]
725	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [8/2022]	348.00 (437.00) [437.00]	179.80 (89.00) [19]
726	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (5/2022) [5/2022]	861.79 (1,846.46) [2,001.34]	1,599.60 (1,139.55) [108]
727	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30	2/2019	5/2021	2,292.46	2,121.13

	AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION		(12/2021) [12/2021]	(-) [2,203.71]	(-88.75) [7]
728	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,520.44 (-410.83) [0]
729	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [3/2022]	640.00 (-) [640.00]	357.57 (0.00) [3]
730	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,694.11 (-139.96) [0]
731	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	256.43 (0.00) [0]
732	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,566.92 (0.00) [0]
733	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2022) [5/2022]	3,190.69 (3,375.90) [3,375.90]	2,884.63 (185.21) [49]
734	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	1,463.48 (747.87) [14]
735	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (1/2022) [1/2022]	3,660.71 (3,740.05) [3,740.05]	3,032.38 (79.34) [8]
736	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (12/2021) [12/2021]	763.92 (-) [733.86]	791.49 (-30.06) [12]
737	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	228.35 (0.00) [0]
	<u>Railways</u>				
738	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [0/0]	184.06 (-) [325.00]	325.01 (140.94) [0]
739	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2023]	2,271.50 (-) [4,794.60]	2,905.60 (2,523.10) [24]
740	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (6/2022) [6/2022]	495.44 (-) [2,980.41]	1,866.85 (2,484.97) [219]
741	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	630.94 (205.27) [0]
742	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [12/2021]	713.48 (-) [2,900.00]	2,831.13 (2,186.52) [21]
743	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
744	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
745	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	466.67 (0.00) [12]
746	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,387.52]	357.95 (594.63) [24]
747	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022	1,035.16	314.37

			(-) [3/2024]	(-) [1,035.16]	(0.00) [24]
748	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [0/0]	305.00 (-) [305.00]	269.73 (0.00) [0]
749	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (311.36) [311.36]	0.00 (45.48) [0]
750	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]
751	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,721.84 (0.00) [-12]
752	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
753	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (3,176.60) [3,176.60]	1,417.20 (1,268.09) [9]
754	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
755	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.49]	0.00 (688.49) [0]
756	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (12/2022) [0/0]	217.38 (393.62) [393.62]	152.98 (176.24) [0]
757	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (12/2024) [12/2024]	229.00 (852.50) [1,096.00]	40.47 (867.00) [36]
758	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	237.71 (0.00) [12]
759	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	515.13 (11.30) [12]
760	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,445.48]	1,418.05 (277.19) [0]
761	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	354.61 (0.00) [24]
Road Transport And Highways					
762	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
763	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	510.71 (0.00) [0]
764	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	595.00 (0.00) [0]
765	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	867.59 (0.00) [0]
766	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
767	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-	11/2016	/	1,071.61	1,154.03

	422.700)		(10/2021) [7/2021]	(-) [1,048.10]	(-23.51) [0]
768	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [0/0]	446.17 (-) [446.17]	128.88 (0.00) [0]
769	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,160.64]	0.00 (62.58) [0]
770	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	978.04 (0.00) [0]
771	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	334.55 (0.00) [0]
772	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [0/0]	400.25 (-) [400.25]	167.14 (0.00) [0]
773	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (1/2022) [7/2021]	1,064.88 (-) [1,021.00]	435.76 (-43.88) [0]
774	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [0/0]	1,059.73 (-) [1,071.00]	18.75 (11.27) [0]
775	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	0.00 (35.07) [0]
776	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [0/0]	988.34 (-) [1,043.28]	0.00 (54.94) [0]
777	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	444.50 (-1.00) [0]
778	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [0/0]	422.38 (-) [422.38]	224.47 (0.00) [0]
779	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [0/0]	955.40 (-) [955.40]	470.17 (0.00) [0]
780	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	98.37 (0.00) [0]
781	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	219.50 (0.00) [0]
782	AMD I TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	280.56 (0.00) [0]
783	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	197.37 (0.00) [0]
784	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	192.24 (0.00) [0]
785	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	330.00 (0.00) [0]
786	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	167.95 (0.00) [0]
787	BARASGAON TO RAHATEE	7/2016	9/2018 (-)	289.11 (290.00)	135.85 (0.00)

			[0/0]	[289.11]	[0]
788	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	204.49 (0.00) [0]
789	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	274.75 (0.00) [0]
790	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [0/0]	743.21 (743.00) [743.21]	290.00 (0.00) [0]
791	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	169.64 (0.90) [0]
792	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	159.96 (0.00) [0]
793	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	145.87 (0.00) [0]
794	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	107.85 (0.00) [0]
795	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	401.46 (0.00) [0]
796	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [0/0]	393.10 (393.00) [393.10]	240.73 (0.00) [0]
797	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	170.22 (0.00) [0]
798	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	61.31 (0.00) [0]
799	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [6/2022]	649.50 (-) [649.50]	233.12 (0.00) [39]
800	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [2/2022]	291.53 (-) [291.53]	220.18 (0.00) [-]
801	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [1/2022]	289.21 (-) [289.21]	224.45 (0.00) [-]
802	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (3/2022) [3/2022]	593.26 (717.24) [716.78]	622.88 (123.52) [46]
803	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (3/2022) [3/2022]	531.13 (-) [744.73]	694.42 (213.60) [46]
804	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	106.56 (0.00) [0]
805	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	31.97 (-89.53) [0]
806	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	410.01 (-0.51) [0]
807	DAHEGAON TO KUIH	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	154.69 (0.00) [0]

808	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	137.99 (0.00) [0]
809	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	268.44 (0.00) [0]
810	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	146.73 (0.00) [0]
811	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]
812	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [0/0]	336.21 (336.00) [336.21]	215.00 (0.00) [0]
813	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [0/0]	217.14 (217.00) [217.14]	137.57 (0.00) [0]
814	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [0/0]	391.06 (391.00) [391.06]	237.84 (0.00) [0]
815	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	310.14 (0.00) [0]
816	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
817	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	716.34 (164.87) [0]
818	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (3/2021) [0/0]	904.16 (911.07) [904.16]	0.00 (0.00) [0]
819	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	333.22 (0.00) [0]
820	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	223.81 (0.00) [0]
821	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	132.39 (0.00) [0]
822	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	269.58 (0.00) [0]
823	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	791.90 (0.00) [0]
824	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	324.19 (0.00) [0]
825	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	204.36 (0.00) [0]
826	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
827	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	169.59 (0.00) [0]
828	JINTUR TO PARBHANI	1/2017	/	356.66	125.61

			(-) [0/0]	(-) [356.66]	(0.00) [0]
829	KAIJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	302.14 (0.00) [0]
830	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	467.78 (0.00) [0]
831	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	1,346.39 (0.00) [0]
832	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	631.68 (0.00) [0]
833	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [0/0]	407.19 (407.00) [407.19]	194.17 (0.00) [0]
834	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	197.17 (0.00) [0]
835	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	220.46 (0.00) [0]
836	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	136.94 (0.00) [0]
837	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	260.43 (0.00) [0]
838	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	155.48 (0.00) [0]
839	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	160.15 (0.00) [0]
840	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	181.30 (-) [181.30]	137.37 (0.00) [0]
841	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	594.75 (594.75) [606.75]	167.02 (12.00) [0]
842	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	257.83 (0.00) [0]
843	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	74.00 (0.00) [0]
844	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	159.42 (0.00) [0]
845	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.64 (0.00) [0]
846	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	199.34 (0.00) [0]
847	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	190.69 (0.00) [0]
848	KUSUMBA TO MALEGAON	3/2018	12/2019 (-)	243.45 (244.00)	154.68 (0.00)

			[0/0]	[243.45]	[0]
849	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	203.39 (0.00) [0]
850	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	9.66 (0.00) [0]
851	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	174.63 (0.00) [0]
852	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	193.15 (0.00) [0]
853	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [0/0]	322.55 (-) [322.55]	191.12 (0.00) [0]
854	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
855	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	156.87 (0.00) [0]
856	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	159.32 (0.00) [0]
857	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	263.13 (0.00) [0]
858	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	304.27 (0.00) [0]
859	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	151.60 (0.00) [0]
860	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
861	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	233.89 (0.00) [0]
862	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	731.89 (731.89) [732.34]	279.40 (0.45) [0]
863	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	231.19 (0.00) [0]
864	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
865	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	48.40 (0.00) [0]
866	NAGAJ TO VAJJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	261.86 (0.00) [0]
867	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.40 (0.00) [0]
868	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [12/2021]	546.00 (-) [546.00]	309.98 (0.00) [29]

869	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [12/2021]	591.66 (-) [591.66]	319.05 (0.00) [29]
870	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	170.33 (0.00) [0]
871	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	143.39 (0.00) [0]
872	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	228.09 (0.00) [0]
873	NANDGAON TO MORSHI	1/2017	6/2019 (-) [0/0]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
874	NASHIK TO PETH	12/2015	11/2018 (-) [0/0]	289.60 (-) [289.60]	210.10 (0.00) [0]
875	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [0/0]	406.54 (407.00) [406.54]	172.47 (0.00) [0]
876	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	188.65 (0.00) [0]
877	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	218.03 (0.00) [0]
878	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	142.00 (0.00) [0]
879	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	159.96 (0.00) [0]
880	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	155.96 (0.00) [0]
881	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	138.05 (0.00) [0]
882	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.08 (302.00) [381.08]	9.66 (0.00) [0]
883	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	170.80 (0.00) [0]
884	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	177.80 (0.00) [0]
885	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	80.76 (0.00) [0]
886	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	725.27 (0.00) [0]
887	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	269.24 (0.00) [0]
888	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	121.71 (0.00) [0]
889	PEN TO KHOPOLI	3/2018	3/2018	301.39	80.25

			(-) [0/0]	(302.00) [301.39]	(0.00) [0]
890	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	292.53 (0.00) [0]
891	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	52.22 (0.00) [0]
892	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [0/0]	228.31 (-) [228.31]	88.39 (0.00) [0]
893	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [3/2022]	1,724.55 (-) [1,724.55]	2,633.18 (0.00) [108]
894	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	210.81 (0.00) [0]
895	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	303.72 (0.00) [0]
896	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	107.34 (0.00) [0]
897	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (12/2021) [12/2021]	536.65 (356.00) [536.65]	552.29 (0.00) [24]
898	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	238.22 (0.00) [0]
899	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	155.76 (0.00) [0]
900	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	262.66 (0.00) [0]
901	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.38 (257.00) [257.38]	166.31 (0.00) [0]
902	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	174.16 (0.00) [0]
903	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	183.00 (0.00) [0]
904	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	199.61 (0.00) [0]
905	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	284.02 (0.00) [0]
906	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	25.96 (0.00) [0]
907	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	59.88 (0.00) [0]
908	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [0/0]	373.10 (373.00) [373.10]	314.20 (0.00) [0]
909	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-)	211.34 (-)	130.63 (0.00)

			[0/0]	[211.34]	[0]
910	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	186.62 (0.00) [0]
911	SHIVUR TO YEOLA	3/2018	12/2019 (-) [0/0]	181.08 (-) [181.08]	97.86 (0.00) [0]
912	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	232.56 (0.00) [0]
913	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (5/2021) [9/2021]	404.94 (495.24) [448.18]	481.97 (43.24) [0]
914	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE	11/2016	/ (12/2016) [5/2017]	290.73 (-) [315.00]	246.70 (24.27) [0]
915	TAKARKHED TO JALNA	9/2017	6/2019 (-) [0/0]	417.90 (418.00) [417.90]	237.50 (0.00) [0]
916	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	173.14 (0.00) [0]
917	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	969.90 (0.00) [0]
918	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	116.30 (0.00) [0]
919	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	302.13 (0.00) [0]
920	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	1,026.75 (0.00) [0]
921	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	304.58 (305.00) [304.58]	128.89 (0.00) [0]
922	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	60.66 (0.00) [0]
923	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	111.20 (0.00) [0]
924	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	82.35 (0.00) [0]
925	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	840.10 (0.00) [0]
926	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	362.46 (362.46) [362.46]	201.85 (0.00) [0]
927	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	186.55 (0.00) [0]
928	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [0/0]	216.90 (217.00) [216.90]	148.93 (0.00) [0]
929	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	133.93 (0.00) [0]

930	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Urban Development</u>				
931	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	3/2020 (3/2023) [3/2023]	23,136.00 (-) [33,406.00]	19,493.96 (10,270.00) [36]
932	NAGPUR METRO RAIL	8/2014	3/2018 (12/2021) [12/2021]	8,680.00 (-) [8,680.00]	8,427.24 (0.00) [45]
933	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (12/2022) [12/2022]	11,420.00 (11,420.00) [11,420.00]	7,187.19 (0.00) [13]
	<u>Water Resources</u>				
934	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2021]	233.57 (-) [233.57]	148.83 (0.00) [24]
	<u>MANIPUR</u>				
	<u>Power</u>				
935	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (1,311.05) [1,311.05]	156.99 (732.43) [0]
	<u>Railways</u>				
936	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	11,504.51 (7,809.98) [153]
	<u>Road Transport And Highways</u>				
937	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	46.68 (0.00) [0]
938	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	36.80 (0.00) [0]
939	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	42.84 (0.00) [0]
940	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	28.20 (0.00) [0]
941	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	25.18 (0.00) [0]
942	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [10/2023]	673.27 (-) [673.27]	0.00 (0.00) [0]
943	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
944	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [3/2023]	467.00 (-) [467.00]	0.00 (0.00) [0]
945	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	0.00 (0.00) [0]
946	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	25.85 (0.00) [0]
947	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
948	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO	8/2020	4/2022	228.97	0.00

	4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI		(-) [4/2022]	(-) [228.97]	(0.00) [0]
949	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	5.07 (0.00) [0]
950	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	154.09 (0.00) [0]
951	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	0.00 (0.00) [0]
952	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	0.00 (0.00) [0]
953	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	0.00 (0.00) [0]
954	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	0.00 (0.00) [0]
955	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
956	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	0.00 (0.00) [0]
957	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	0.00 (0.00) [0]
958	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	0.00 (0.00) [0]
959	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	0.00 (0.00) [0]
960	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [36]
	MEGHALAYA				
	Department Of Higher Education				
961	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	Doner				
962	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [8/2021]	151.33 (-) [151.33]	149.33 (0.00) [0]
	Health And Family Welfare				
963	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [3/2022]	363.99 (-) [363.99]	253.84 (0.00) [46]
	Railways				
964	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.34 (3,176.56) [0]
	Road Transport And Highways				
965	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.37 (0.00) [0]
966	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING	3/2019	5/2019 (-)	306.28 (-)	133.81 (0.00)

	CHAINAGE FROM		[3/2022]	[306.28]	[34]
967	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	40.21 (0.00) [0]
968	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	288.84 (0.00) [0]
969	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	173.17 (0.00) [0]
970	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	38.58 (0.00) [0]
971	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	53.58 (0.00) [0]
972	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
973	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (9/2021) [9/2021]	553.51 (-) [553.51]	197.23 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
974	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2024]	2,393.47 (5,021.45) [5,521.45]	4,232.46 (3,127.98) [120]
	<u>Road Transport And Highways</u>				
975	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [11/2021]	205.95 (-) [205.95]	108.58 (0.00) [10]
976	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2021) [0/0]	195.04 (-) [377.99]	368.39 (182.95) [0]
977	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2021) [12/2021]	186.96 (-) [322.24]	308.85 (135.28) [87]
978	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2021) [12/2021]	193.69 (-) [327.92]	323.23 (134.23) [134]
979	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	24.56 (0.00) [0]
980	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	30.06 (0.00) [0]
981	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	53.72 (0.00) [0]
982	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	49.59 (0.00) [0]
983	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	92.39 (0.00) [0]
984	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	23.26 (0.00) [0]
985	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	0.00 (0.00) [0]

986	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	12.16 (0.00) [0]
987	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
988	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
989	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	83.73 (0.00) [43]
990	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [4/2023]	473.18 (-) [473.18]	118.96 (0.00) [43]
991	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	518.53 (-) [518.53]	126.61 (0.00) [45]
992	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (9/2023) [9/2023]	428.11 (-) [428.11]	82.60 (0.00) [48]
993	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (3/2024) [4/2024]	404.29 (-) [404.29]	41.29 (0.00) [55]
994	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [4/2023]	537.82 (-) [537.82]	129.40 (0.00) [43]
995	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [7/2023]	640.07 (-) [640.07]	94.28 (0.00) [46]
996	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	642.96 (-) [642.96]	106.57 (0.00) [45]
997	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2021) [0/0]	624.41 (-) [992.67]	978.43 (368.26) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
998	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
999	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (9/2023) [9/2023]	328.00 (-) [328.00]	296.56 (0.00) [30]
1000	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (404.45) [404.45]	246.02 (84.69) [0]
1001	RECAST PR FOR DHANKASA UG (1.00 MTY)	9/2016	3/2022 (3/2025) [3/2025]	289.29 (-) [289.30]	36.10 (0.01) [36]
	<u>Dpiit</u>				
1002	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	9,574.07 (1,233.21) [0]
	<u>Heavy Industry</u>				
1003	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIPI)	4/2011	9/2011 (3/2021) [3/2021]	1,718.00 (3,727.30) [3,727.30]	3,522.74 (2,009.30) [0]
	<u>Petroleum</u>				
1004	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND	1/2015	3/2021 (12/2021)	1,823.00 (3,027.90)	2,163.26 (1,204.90)

	MUZAFFARPUR		[3/2022]	[3,027.90]	[12]
1005	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2021]	571.66 (-) [510.00]	485.08 (-61.66) [24]
1006	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (3,060.00) [3,060.00]	2,496.20 (-248.00) [0]
1007	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	368.60 (0.00) [0]
1008	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	3,437.00 (3,048.00) [3,048.00]	2,129.90 (-389.00) [12]
1009	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	12/2029 (-) [12/2029]	169.00 (-) [169.00]	37.29 (0.00) [0]
1010	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	118.98 (0.00) [0]
1011	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	337.20 (0.00) [0]
1012	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	2,433.00 (-) [2,433.00]	2,166.20 (0.00) [12]
1013	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [7/2022]	2,677.00 (-) [3,072.00]	2,574.63 (395.00) [13]
1014	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (5,909.00) [5,909.00]	3,773.40 (2,994.00) [110]
1015	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [11/2021]	2,881.40 (-) [2,000.00]	1,652.70 (-881.40) [11]
1016	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	1,616.30 (0.00) [0]
1017	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (3/2022) [3/2022]	2,321.00 (3,338.00) [3,338.00]	3,071.72 (1,017.00) [15]
1018	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (5/2021) [3/2022]	690.00 (-) [690.00]	596.34 (0.00) [44]
1019	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2022]	406.00 (-) [406.00]	281.34 (0.00) [17]
1020	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	402.90 (0.00) [0]
	<u>Power</u>				
1021	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (3/2024) [3/2024]	4,754.42 (9,129.32) [9,129.32]	2,697.96 (4,374.90) [63]
1022	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (8/2021) [12/2021]	358.83 (-) [358.83]	260.80 (0.00) [19]
1023	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (12/2021) [12/2021]	522.29 (546.36) [546.36]	480.66 (24.07) [61]
1024	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (12/2020)	3,500.00 (3,500.00)	3,096.25 (494.00)

			[2/2022]	[3,994.00]	[19]
1025	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (11/2021) [12/2021]	235.53 (-) [235.53]	156.95 (0.00) [30]
1026	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (9/2021) [2/2022]	322.30 (-) [322.30]	204.37 (0.00) [36]
1027	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2021]	197.40 (-) [197.40]	90.75 (0.00) [45]
1028	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (9/2021) [6/2021]	5,070.13 (-) [5,070.13]	4,223.07 (0.00) [0]
1029	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (7/2021) [10/2021]	14,733.37 (-) [14,733.37]	11,683.96 (0.00) [23]
1030	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (9/2021) [10/2021]	1,931.39 (-) [1,931.39]	1,807.75 (0.00) [20]
1031	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2021) [3/2022]	5,111.33 (6,700.00) [6,700.00]	3,207.16 (1,588.67) [39]
1032	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (11/2022) [8/2022]	11,130.19 (14,719.10) [14,719.10]	12,979.18 (3,588.91) [108]
1033	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (9/2021) [12/2021]	379.95 (-) [379.95]	235.98 (0.00) [24]
1034	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (7/2021) [6/2021]	808.63 (-) [808.63]	688.55 (0.00) [0]
1035	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [12/2021]	374.63 (-) [374.63]	252.99 (0.00) [68]
	<u>Railways</u>				
1036	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	17,009.45 (0.00) [0]
1037	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [502.48]	517.25 (214.13) [0]
1038	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.11 (-200.00) [-]
1039	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (-) [2/2022]	704.31 (927.94) [927.94]	680.25 (223.63) [23]
1040	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [923.23]	2.39 (0.00) [0]
1041	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [495.10]	313.03 (319.30) [-]
1042	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.13]	242.55 (1,211.99) [0]
1043	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	40.65 (-1.00) [-]
1044	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-)	523.52 (-)	2.28 (681.48)

			[3/2024]	[1,205.00]	[-]
1045	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [610.00]	580.83 (315.00) [37]
1046	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	116.24 (651.22) [0]
1047	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	97.40 (173.89) [96]
1048	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,524.68) [1,524.68]	974.69 (177.42) [12]
1049	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2025) [3/2025]	1,640.04 (1,873.10) [1,873.10]	869.58 (233.06) [36]
1050	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	480.96 (74.13) [96]
1051	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [9/2023]	336.91 (-) [791.39]	597.99 (454.48) [-]
1052	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	638.28 (818.35) [133]
1053	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (4/2010) [12/2021]	2,030.50 (-) [2,030.50]	0.00 (0.00) [-]
1054	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1055	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1056	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.58 (134.08) [0]
1057	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (12/2024) [12/2024]	2,912.96 (-) [3,845.60]	329.61 (932.64) [33]
1058	HAJIPUR - BACHAWARA	5/2015	3/2019 (12/2021) [12/2021]	678.54 (678.54) [929.86]	926.80 (251.32) [33]
1059	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	11.77 (88.07) [-]
1060	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1061	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2024]	1,614.59 (1,877.81) [1,878.00]	1,488.87 (263.41) [60]
1062	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.74 (0.00) [0]
1063	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	0.02 (0.00) [-]
1064	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [0/0]	625.00 (781.00) [839.00]	839.36 (214.00) [0]

1065	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2027]	2,132.77 (-) [3,037.95]	347.10 (905.18) [156]
1066	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	614.87 (71.58) [108]
1067	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [174.56]	71.43 (0.00) [-]
1068	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,582.36 (0.00) [36]
1069	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [1,952.68]	714.51 (95.73) [12]
1070	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (12/2021) [1/2022]	270.14 (457.08) [749.40]	550.86 (479.26) [-]
1071	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	149.31 (138.71) [228]
1072	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,908.60 (8,000.84) [202]
1073	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	109.51 (0.00) [132]
1074	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,172.16]	285.53 (2,051.46) [105]
1075	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	141.76 (180.72) [157]
1076	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	383.74 (59.77) [-]
1077	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2023]	1,723.00 (-) [3,421.35]	2,004.42 (1,698.35) [276]
1078	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [0/0]	414.84 (-) [750.00]	157.19 (335.16) [0]
1079	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [11/2024]	450.00 (2,017.96) [2,017.96]	878.49 (1,567.96) [148]
1080	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	30.12 (0.05) [240]
1081	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [0/0]	242.22 (-) [471.00]	76.57 (228.78) [0]
1082	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (12/2021) [3/2022]	241.52 (-) [373.87]	333.46 (132.35) [-]
1083	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [12/2023]	1,798.00 (2,042.51) [2,042.51]	328.75 (244.51) [57]
1084	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,090.60]	1,089.12 (271.37) [0]
1085	NEW MAYNAGURI TO JOGIGHOPA VIA	4/2000	12/2008	1,180.19	3,881.59

	CHANGRABANDHA (NL),NEFR		(-) [11/2021]	(2,531.34) [4,541.38]	(3,361.19) [155]
1086	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	313.14 (101.81) [31]
1087	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	439.23 (1,221.83) [36]
1088	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1089	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,262.36]	191.39 (2,179.61) [0]
1090	RAYADURGA-TUMKUR NL	4/2007	/ (-) [12/2025]	2,062.30 (-) [2,404.03]	1,087.98 (341.73) [-]
1091	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	36.13 (0.75) [-]
1092	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	199.72 (-10.96) [108]
1093	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
1094	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1095	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1096	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1097	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [9/2021]	860.43 (-) [1,104.00]	966.68 (243.57) [0]
	Road Transport And Highways				
1098	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1099	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (1/2021) [12/2021]	1,928.22 (1,928.22) [1,928.22]	1,890.04 (0.00) [80]
1100	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [11/2021]	1,294.47 (-) [1,296.00]	0.00 (1.53) [-]
1101	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [11/2018]	998.70 (-) [962.00]	0.00 (-36.70) [0]
1102	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (9/2020) [9/2020]	604.00 (-) [364.59]	360.15 (-239.41) [0]
1103	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [0/0]	754.00 (-) [754.00]	1,364.18 (0.00) [0]
1104	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [0/0]	1,244.10 (-) [1,244.10]	1,665.00 (0.00) [0]
1105	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011	1,693.75	2,848.49

			(-) [0/0]	(-) [1,693.75]	(0.00) [0]
1106	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	3,379.45 (531.45) [105]
	<u>Shipping And Ports</u>				
1107	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (4,633.81) [4,633.81]	1,940.64 (-735.37) [0]
	<u>Telecommunications</u>				
1108	NETWORK FOR SPECTRUM	3/2012	7/2015 (5/2020) [3/2022]	13,334.00 (24,664.00) [24,664.00]	20,545.00 (11,330.00) [80]
1109	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (11/2021) [11/2021]	431.16 (422.87) [422.87]	46.37 (-8.29) [5]
	<u>Urban Development</u>				
1110	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	5,222.09 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1111	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1112	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,647.64]	1,369.40 (4,321.12) [132]
	<u>Road Transport And Highways</u>				
1113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	116.27 (0.00) [44]
1114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	89.53 (0.00) [48]
1115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	161.15 (0.00) [38]
1116	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	315.99 (0.00) [42]
1117	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	115.32 (0.00) [50]
1118	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	39.60 (0.00) [0]
1119	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	58.14 (0.00) [0]
1120	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	32.21 (0.00) [0]
1121	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	54.27 (0.00) [0]
1122	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	38.65 (0.00) [0]
1123	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-)	278.95 (-)	79.89 (0.00)

			[6/2022]	[278.95]	[0]
1124	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [6/2022]	206.53 (-) [206.53]	81.84 (0.00) [0]
1125	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (8/2021) [0/0]	217.35 (-) [217.35]	104.81 (0.00) [0]
1126	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	40.94 (0.00) [0]
1127	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	3.90 (0.00) [0]
1128	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (177.00) [277.44]	32.33 (0.00) [0]
1129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	169.77 (0.00) [46]
1130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	115.77 (0.00) [39]
1131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	121.06 (0.00) [39]
1132	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	108.86 (0.00) [38]
1133	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	77.59 (0.00) [39]
1134	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	63.44 (0.00) [49]
1135	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	146.10 (0.00) [38]
1136	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	126.19 (0.00) [38]
1137	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	342.06 (13.93) [0]
1138	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	304.39 (0.00) [0]
1139	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (369.96) [369.96]	322.13 (33.71) [0]
1140	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	8.04 (0.00) [0]
1141	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	8.04 (0.00) [0]
1142	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	167.62 (-) [167.62]	118.61 (0.00) [0]
1143	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]

1144	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	7.80 (0.00) [0]
1145	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	96.49 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1146	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	204.33 (0.00) [0]
1147	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	240.64 (0.00) [60]
1148	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3/2017 (-) [3/2031]	3,145.45 (-) [3,145.45]	637.17 (0.00) [168]
1149	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	3/2010 (3/2029) [3/2029]	3,504.21 (3,504.21) [3,504.21]	589.86 (0.00) [228]
1150	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	3/2013 (3/2028) [3/2028]	8,416.19 (8,416.19) [8,416.19]	941.90 (0.00) [180]
1151	GARJANBAHAL OCP	11/2014	3/2021 (-) [9/2025]	1,375.38 (-) [1,375.38]	659.30 (0.00) [54]
1152	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2024]	479.53 (-) [708.55]	729.73 (229.02) [132]
1153	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	598.36 (0.00) [0]
1154	NAINI COAL MINE	3/2020	3/2024 (-) [3/2024]	494.30 (-) [494.30]	76.43 (0.00) [0]
1155	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,282.18 (0.00) [0]
1156	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	2,558.11 (0.00) [0]
1157	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	898.53 (0.00) [0]
	<u>Department Of Higher Education</u>				
1158	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [6/2022]	790.79 (-) [790.79]	230.59 (0.00) [3]
	<u>Mines</u>				
1159	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (1/2024) [1/2024]	5,540.00 (6,435.90) [5,540.00]	988.67 (0.00) [33]
1160	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [12/2023]	355.00 (-) [355.00]	95.45 (0.00) [37]
1161	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (12/2023) [12/2023]	483.00 (483.00) [483.00]	6.91 (0.00) [32]
1162	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	391.52 (0.00) [0]

	Petroleum				
1163	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [6/2023]	1,607.00 (-) [1,607.00]	283.87 (0.00) [10]
1164	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (6/2022) [6/2022]	462.30 (-) [462.30]	107.63 (0.00) [9]
1165	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (8/2021) [11/2021]	315.00 (-) [315.00]	223.98 (0.00) [-1]
1166	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	151.09 (0.00) [0]
1167	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	91.81 (0.00) [0]
1168	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,933.00 (-) [1,933.00]	1,484.70 (0.00) [12]
1169	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (7/2022) [7/2022]	5,654.00 (-) [5,654.00]	3,485.97 (0.00) [9]
1170	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (9/2022) [9/2022]	3,361.00 (-) [3,361.00]	2,039.85 (0.00) [13]
1171	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	28.71 (0.00) [0]
1172	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023) [3/2023]	371.00 (427.00) [427.00]	28.69 (56.00) [6]
1173	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	373.13 (0.00) [0]
1174	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [10/2022]	161.59 (-) [161.59]	56.21 (0.00) [34]
1175	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [3/2022]	1,297.50 (-) [1,297.50]	823.08 (0.00) [5]
	Power				
1176	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [12/2021]	1,885.13 (2,311.89) [2,311.89]	1,922.67 (426.76) [36]
	Railways				
1177	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,233.58 (593.05) [39]
1178	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	269.52 (0.00) [41]
1179	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	692.35 (0.00) [63]
1180	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1181	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2025]	5,200.00 (-) [5,200.00]	101.77 (0.00) [60]
1182	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022	1,547.38	696.10

			(3/2023) [3/2023]	(1,547.38) [1,547.38]	(0.00) [12]
1183	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (3/2024) [3/2024]	701.61 (-) [810.02]	193.71 (108.41) [64]
1184	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (12/2022) [12/2022]	133.41 (207.00) [433.00]	405.83 (299.59) [165]
1185	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (3/2026) [3/2026]	2,923.13 (3,791.66) [3,791.66]	1,649.76 (868.53) [204]
1186	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	493.76 (0.00) [48]
1187	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [3/2022]	969.83 (-) [1,312.96]	1,071.24 (343.13) [24]
1188	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2022]	155.81 (238.03) [238.03]	223.69 (82.22) [24]
1189	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	2,119.84 (1,060.96) [21]
1190	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (3/2022) [3/2022]	1,111.99 (1,539.28) [1,539.28]	1,195.24 (427.29) [37]
1191	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,842.99 (1,237.83) [88]
1192	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	909.17 (1,117.29) [45]
1193	VIZIANAGARAM -SAMBALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	1,887.58 (992.05) [24]
Road Transport And Highways					
1194	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/	1,282.94	720.08
			(-) [0/0]	(-) [1,282.94]	(0.00) [0]
1195	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [0/0]	2,510.04 (-) [2,510.04]	633.26 (0.00) [0]
1196	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/	752.28	281.06
			(-) [3/2022]	(-) [752.28]	(0.00) [-]
1197	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/	1,069.65	836.93
			(-) [0/0]	(-) [1,069.65]	(0.00) [0]
1198	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	14.80 (0.00) [0]
1199	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/	1,008.96	1,125.65
			(-) [0/0]	(-) [1,008.96]	(0.00) [0]
1200	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/	564.66	387.54
			(-) [0/0]	(-) [564.66]	(0.00) [0]
1201	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [0/0]	476.56 (-) [476.56]	212.64 (0.00) [0]
1202	REHABILITATION AND UP-GRADATION OF EXISTING 2-	1/2018	/	633.68	165.60

	LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (		(-) [0/0]	(-) [633.68]	(0.00) [0]
1203	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/	953.09	468.85
			(-) [3/2022]	(-) [953.09]	(0.00) [-]
1204	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/	668.86	413.00
			(-) [0/0]	(-) [668.86]	(0.00) [0]
1205	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/	614.48	309.98
			(-) [8/2021]	(-) [614.48]	(0.00) [0]
1206	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/	503.88	130.36
			(-) [0/0]	(-) [503.88]	(0.00) [0]
1207	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020	1,288.07	1,033.61
			(-) [0/0]	(-) [1,420.00]	(131.93) [0]
1208	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/	686.65	290.00
			(-) [0/0]	(-) [686.65]	(0.00) [0]
1209	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	254.00
			(-) [0/0]	(-) [686.65]	(0.00) [0]
1210	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	246.25
			(-) [0/0]	(-) [417.51]	(0.00) [0]
1211	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/	999.00	178.93
			(-) [0/0]	(-) [999.00]	(0.00) [0]
1212	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016	171.96	100.67
			(-) [0/0]	(172.00) [172.00]	(0.04) [0]
1213	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/	1,522.00	512.80
			(-) [0/0]	(-) [1,522.00]	(0.00) [0]
1214	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014	1,047.00	1,873.47
			(-) [0/0]	(-) [1,047.00]	(0.00) [0]
1215	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/	806.11	362.39
			(-) [0/0]	(-) [806.11]	(0.00) [0]
1216	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016	191.50	183.94
			(-) [0/0]	(192.00) [192.00]	(0.50) [0]
1217	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015	191.08	182.41
			(-) [0/0]	(-) [191.08]	(0.00) [0]
1218	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017	287.70	213.19
			(-) [0/0]	(-) [287.70]	(0.00) [0]
1219	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018	214.23	112.86
			(-) [0/0]	(-) [214.23]	(0.00) [0]
1220	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018	223.50	143.52
			(-) [0/0]	(-) [223.50]	(0.00) [0]
1221	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018	199.16	124.19
			(-) [0/0]	(-) [199.16]	(0.00) [0]
1222	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017	295.67	207.20
			(-)	(-)	(0.00)

			[0/0]	[295.67]	[0]
1223	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	126.02 (0.00) [0]
	<u>Steel</u>				
1224	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	44.29 (0.00) [0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1225	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020 (-) [4/2022]	195.00 (-) [195.00]	16.41 (0.00) [19]
	<u>PUNJAB</u>				
	<u>Department Of Higher Education</u>				
1226	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [10/2022]	348.24 (-) [348.24]	24.91 (0.00) [5]
1227	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [6/2022]	430.00 (-) [387.83]	228.61 (-42.17) [25]
	<u>Fertilisers</u>				
1228	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (5/2021) [0/0]	218.83 (-) [218.83]	194.79 (0.00) [0]
1229	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (5/2021) [0/0]	239.81 (-) [239.81]	204.09 (0.00) [0]
	<u>Health And Family Welfare</u>				
1230	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [0/0]	703.00 (-) [557.48]	538.20 (-145.52) [0]
1231	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2021]	152.95 (-) [177.92]	164.17 (24.97) [0]
	<u>Petroleum</u>				
1232	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,421.46]	171.55 (0.00) [0]
	<u>Railways</u>				
1233	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]
1234	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	<u>Road Transport And Highways</u>				
1235	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (1,367.00) [2,280.00]	1,367.00 (1,110.39) [0]
1236	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [904.82]	851.32 (15.58) [0]
1237	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [1,588.29]	798.71 (199.95) [0]
1238	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [9/2022]	754.54 (-) [756.27]	443.91 (1.73) [30]
1239	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN	12/2020	1/2024 (-)	733.00 (-)	0.00 (0.00)

	ROAD (SH-1		[1/2024]	[733.00]	[0]
1240	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH-	2/2021	4/2024 (-) [4/2024]	1,269.96 (-) [1,269.96]	0.00 (0.00) [0]
1241	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR-	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]
1242	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO	12/2020	4/2024 (-) [4/2024]	1,094.46 (-) [1,094.46]	0.00 (0.00) [0]
1243	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI	12/2020	1/2024 (-) [1/2024]	989.66 (-) [989.66]	0.00 (0.00) [0]
1244	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO	12/2020	4/2024 (-) [4/2024]	1,234.40 (-) [1,234.40]	0.00 (0.00) [0]
1245	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO	12/2020	4/2024 (-) [4/2024]	881.00 (-) [881.00]	0.00 (0.00) [0]
1246	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [11/2021]	261.76 (-) [207.00]	205.00 (-54.76) [-]
1247	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2022]	479.00 (-) [479.00]	456.80 (0.00) [-]
1248	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [8/2021]	1,069.59 (-) [1,069.59]	734.04 (0.00) [0]
1249	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [0/0]	196.05 (-) [196.05]	143.03 (0.00) [0]
1250	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	124.52 (0.00) [0]
1251	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [0/0]	170.57 (-) [170.57]	70.83 (0.00) [0]
1252	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [0/0]	293.64 (-) [293.64]	261.09 (0.00) [0]
1253	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [0/0]	293.10 (-) [293.10]	183.87 (0.00) [0]
	RAJASTHAN				
	Atomic Energy				
1254	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [3/2023]	12,320.00 (-) [17,079.00]	13,709.00 (4,759.00) [75]
	Coal				
1255	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-) [0/0]	2,112.60 (-) [2,112.60]	93.05 (0.00) [0]
1256	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1257	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020 (-) [0/0]	2,196.30 (-) [2,196.30]	143.95 (0.00) [0]
1258	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]

	Department Of Higher Education				
1259	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (-) [0/0]	549.31 (-) [559.47]	458.38 (10.16) [0]
	Petroleum				
1260	LPG BP PROJECT JODHPUR	3/2018	/ (5/2022) [12/2022]	229.80 (-) [229.80]	90.20 (0.00) [-]
	Power				
1261	ANTA SOLAR 90 MW	1/2021	3/2022 (-) [3/2022]	382.22 (-) [382.22]	0.00 (0.00) [0]
1262	BHENSARA 320 MW	1/2021	7/2022 (-) [7/2022]	1,221.73 (-) [1,221.73]	137.36 (0.00) [0]
1263	CHHATTARGARH 150 MW	2/2021	7/2022 (-) [7/2022]	599.99 (-) [559.98]	60.85 (-40.01) [0]
1264	FATEHGARH SOLAR 296MW	3/2020	9/2021 (2/2022) [2/2022]	1,749.31 (-) [1,749.31]	1,277.87 (0.00) [5]
1265	JETSAR SOLAR 160 MW	12/2019	3/2021 (11/2021) [11/2021]	702.28 (-) [702.28]	539.41 (0.00) [8]
1266	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (10/2022) [1/2022]	1,522.71 (-) [1,522.71]	996.32 (0.00) [4]
1267	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (7/2022) [9/2022]	1,782.00 (-) [1,782.00]	672.69 (0.00) [12]
	Railways				
1268	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [2,215.27]	4.60 (1,341.56) [0]
1269	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [821.64]	0.00 (-0.36) [0]
1270	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	759.31 (450.33) [40]
1271	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	356.84 (0.00) [3]
1272	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [9/2021]	420.18 (-) [480.00]	378.63 (59.82) [0]
1273	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [0/0]	493.17 (-) [493.17]	464.53 (0.00) [0]
1274	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [322.98]	0.00 (-0.02) [0]
	Road Transport And Highways				
1275	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [8/2022]	370.36 (-) [370.36]	196.71 (0.00) [0]
1276	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	0.00 (0.00) [0]
1277	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-	11/2012	8/2016 (-)	530.07 (-)	556.02 (0.00)

	FATEHPUR-SALA		[6/2020]	[530.07]	[0]
1278	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG-	2/2021	11/2021 (-) [11/2021]	240.99 (-) [240.99]	0.00 (0.00) [0]
1279	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [0/0]	688.70 (-) [688.70]	870.48 (0.00) [0]
1280	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II	8/2020	12/2020 (-) [0/0]	216.72 (-) [216.72]	0.00 (0.00) [0]
1281	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 & KM 158.419 TO KM 173.300 PKG-II.	12/2020	10/2021 (-) [10/2021]	339.65 (-) [339.65]	0.00 (0.00) [0]
1282	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I.	12/2020	10/2021 (-) [10/2021]	379.23 (-) [379.23]	0.00 (0.00) [0]
1283	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I.	7/2020	9/2021 (-) [9/2021]	319.09 (-) [319.09]	0.00 (0.00) [0]
1284	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [3/2022]	1,031.95 (-) [1,031.95]	1,505.00 (0.00) [-]
1285	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	160.90 (0.00) [0]
1286	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [12/2021]	822.90 (-) [822.90]	844.08 (0.00) [44]
1287	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	496.04 (0.00) [0]
1288	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER - FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [7/2020]	163.95 (-) [163.95]	116.47 (0.00) [0]
1289	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	687.07 (0.00) [0]
1290	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	302.58 (0.00) [0]
1291	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	330.46 (0.00) [0]
1292	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [0/0]	763.23 (-) [763.23]	191.80 (0.00) [0]
1293	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [0/0]	649.00 (-) [649.00]	677.75 (0.00) [0]
1294	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	927.72 (0.00) [0]
1295	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1296	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020 (-) [0/0]	196.23 (-) [196.00]	34.51 (-0.23) [0]
1297	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [0/0]	1,100.19 (-) [1,145.31]	1,355.00 (45.12) [0]

1298	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [3/2022]	894.00 (-) [929.32]	810.00 (35.32) [23]
1299	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [0/0]	425.19 (-) [425.19]	276.40 (0.00) [0]
1300	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [0/0]	275.90 (-) [275.90]	289.13 (0.00) [0]
1301	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1302	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	550.35 (0.00) [0]
1303	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO	3/2020	8/2020 (-) [0/0]	255.23 (-) [255.23]	62.45 (0.00) [0]
1304	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (10/2021) [10/2021]	874.25 (866.55) [866.55]	864.82 (-7.70) [-]
1305	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	317.79 (0.00) [0]
1306	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [0/0]	1,103.88 (-) [1,103.88]	708.45 (0.00) [0]
1307	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	242.52 (0.00) [0]
1308	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	136.22 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1309	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	1,656.78 (7,260.52) [96]
	<u>Road Transport And Highways</u>				
1310	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	2.58 (0.00) [0]
1311	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
1312	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	21.62 (0.00) [0]
1313	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	74.52 (0.00) [0]
1314	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	75.61 (0.00) [0]
1315	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	118.63 (0.00) [0]
1316	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	69.32 (0.00) [0]
1317	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER	11/2017	11/2017	290.05	154.83

	INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5		(-) [12/2021]	(-) [290.05]	(0.00) [49]
1318	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
1319	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
1320	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	56.40 (0.00) [0]
1321	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	27.06 (0.00) [0]
1322	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	32.98 (0.00) [0]
1323	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	27.45 (0.00) [0]
1324	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	295.14 (59.37) [0]
1325	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
1326	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
TAMIL NADU					
Atomic Energy					
1327	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	25,603.00 (0.00) [36]
1328	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (10/2022) [10/2022]	3,492.00 (6,840.00) [6,840.00]	6,054.37 (3,348.00) [145]
Civil Aviation					
1329	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (12/2023) [12/2023]	380.87 (-) [380.87]	15.41 (0.00) [21]
1330	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [12/2023]	2,467.00 (-) [2,467.00]	728.99 (0.00) [22]
1331	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2022]	951.28 (-) [951.28]	477.10 (0.00) [12]
Coal					
1332	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (3/2025) [3/2025]	1,458.17 (709.06) [709.06]	496.17 (-749.11) [117]
1333	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (7,980.79) [7,980.79]	7,417.83 (2,073.68) [0]
Finance					
1334	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2021]	209.00 (-) [208.96]	205.75 (-0.04) [0]
1335	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	189.00 (0.00) [0]

	Mines				
1336	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2021) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [0]
	Petroleum				
1337	AUGMENTATION OF CTMPL	12/2016	11/2021 (-) [12/2021]	228.00 (-) [228.00]	156.18 (0.00) [1]
1338	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	191.16 (0.00) [0]
1339	CGD PROJECT AT SALEM DISTRICT	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	39.09 (0.00) [0]
1340	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [2/2024]	921.00 (-) [921.00]	5.29 (0.00) [5]
1341	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (1/2022) [1/2022]	466.43 (-) [466.43]	258.36 (0.00) [15]
1342	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (2/2022) [2/2022]	4,497.00 (6,025.00) [6,025.00]	4,049.27 (1,528.00) [38]
1343	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1344	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021) [9/2021]	650.82 (-) [624.35]	455.52 (-26.47) [0]
1345	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	19.44 (794.00) [66]
1346	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [12/2021]	421.00 (-) [305.00]	288.20 (-116.00) [16]
1347	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [10/2023]	1,398.00 (-) [1,398.00]	116.76 (0.00) [-2]
	Power				
1348	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (2/2022) [2/2022]	1,316.22 (-) [1,316.22]	687.97 (0.00) [5]
1349	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (7/2021) [12/2021]	186.17 (219.66) [219.66]	167.22 (33.49) [29]
	Railways				
1350	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [3/2030]	151.84 (-) [527.37]	2.59 (375.53) [133]
1351	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (9/2021) [12/2022]	931.98 (-) [1,122.00]	989.62 (190.02) [-]
1352	ERODE-PALANI	4/2008	/ (-) [3/2030]	288.57 (-) [603.23]	1.63 (314.66) [-]
1353	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (7/2022) [7/2022]	495.74 (-) [734.01]	478.72 (238.27) [109]
1354	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,409.57 (776.00) [27]

1355	MADURAI-BODINAYAKKANUR	4/2008	/ (12/2021) [2/2022]	164.41 (-) [608.13]	399.75 (443.72) [-]
1356	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [6/2022]	1,700.00 (-) [1,305.00]	1,056.49 (-395.00) [3]
1357	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [2,950.00]	1,667.29 (2,225.31) [73]
1358	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [3/2030]	839.00 (-) [839.01]	0.63 (0.01) [-]
1359	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [9/2021]	268.87 (-) [950.00]	920.91 (681.13) [0]
1360	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [3,150.00]	239.53 (2,567.17) [-]
1361	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [3/2030]	227.40 (-) [227.40]	65.02 (0.00) [-]
1362	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2025]	303.98 (-) [1,720.00]	705.52 (1,416.02) [60]
1363	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
<u>Road Transport And Highways</u>					
1364	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	264.10 (0.00) [0]
1365	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHT 170 KM)	4/2012	4/2014 (-) [1/2022]	624.00 (-) [624.00]	90.50 (0.00) [93]
1366	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	178.41 (0.00) [0]
1367	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	770.94 (0.00) [58]
1368	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (273.27) [268.92]	229.77 (9.95) [0]
1369	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [9/2021]	600.00 (-) [600.00]	6.35 (0.00) [0]
1370	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [1/2022]	1,016.92 (-) [1,071.00]	309.05 (54.08) [-]
1371	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [0/0]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1372	FOUR LANING OF MADURAI- CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [3/2022]	628.71 (-) [628.71]	382.61 (0.00) [-]
1373	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [12/2021]	2,065.96 (-) [2,169.00]	0.00 (103.04) [-]
1374	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [1/2022]	1,166.26 (-) [1,296.93]	346.17 (130.67) [-]

1375	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [12/2021]	641.17 (-) [641.17]	398.58 (0.00) [65]
1376	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/	505.35	255.05
			(-) [12/2022]	(-) [505.35]	(0.00) [-]
1377	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	742.16 (0.00) [59]
1378	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [1/2022]	707.82 (-) [707.82]	429.86 (0.00) [41]
1379	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2021]	848.45 (-) [848.45]	243.59 (0.00) [21]
1380	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [12/2021]	641.17 (-) [641.17]	398.58 (0.00) [41]
1381	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [3,426.00]	0.00 (0.00) [0]
1382	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/	379.90	242.86
			(-) [3/2021]	(-) [379.90]	(0.00) [0]
1383	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,342.23 (0.00) [0]
1384	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1385	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1386	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [2/2022]	374.00 (-) [166.90]	77.82 (-207.10) [105]
1387	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/	633.55	0.00
			(-) [0/0]	(-) [482.04]	(-151.51) [0]
1388	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [5/2023]	563.92 (-) [563.92]	32.96 (0.00) [65]
1389	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (204.73) [240.38]	129.04 (0.00) [0]
1390	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	8/2020	2/2021 (-) [0/0]	302.62 (-) [302.62]	51.88 (0.00) [0]
1391	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	210.16 (0.00) [0]
<u>Urban Development</u>					
1392	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (2/2021) [2/2021]	3,770.00 (-) [3,770.00]	2,996.83 (0.00) [0]
1393	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (2/2019) [2/2019]	14,600.00 (18,380.00) [18,380.00]	17,619.68 (3,780.00) [0]
<u>TELANGANA</u>					
<u>Civil Aviation</u>					
1394	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT	5/2020	5/2022	353.61	81.41

	BEGUMPET AIRPORT, HYDRABAD		(-) [5/2022]	(-) [353.61]	(0.00) [0]
	<u>Coal</u>				
1395	GODAVARIKHANI COAL MINE	7/2019	3/2023 (-) [3/2023]	438.98 (-) [438.98]	80.04 (0.00) [0]
1396	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2023]	447.06 (-) [473.22]	183.12 (26.16) [96]
1397	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	206.41 (0.00) [36]
1398	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2022]	397.09 (-) [442.42]	112.99 (45.33) [36]
1399	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	135.30 (-33.01) [68]
1400	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	143.08 (-78.25) [84]
1401	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1402	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2022]	162.76 (-) [349.28]	293.69 (186.52) [84]
1403	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [9/2021]	430.45 (-) [415.37]	213.44 (-15.08) [0]
1404	SRP OC-II EXPANSION PROJECT	11/2016	/ (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
1405	VENKATESH KHANI COAL MINE	10/2020	3/2023 (-) [3/2023]	484.51 (-) [484.51]	25.43 (0.00) [0]
	<u>Health And Family Welfare</u>				
1406	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	164.40 (0.00) [0]
	<u>Petroleum</u>				
1407	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	96.02 (0.00) [16]
	<u>Power</u>				
1408	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (10/2021) [10/2021]	401.90 (-) [401.90]	180.67 (0.00) [6]
1409	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [10/2022]	10,598.98 (10,997.70) [10,997.70]	8,866.73 (398.72) [23]
	<u>Railways</u>				
1410	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	836.26 (317.32) [69]
1411	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [0/0]	636.38 (-) [636.38]	634.20 (0.00) [0]
1412	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	723.00 (-) [723.00]	0.00 (0.00) [0]

1413	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/	458.25	3.69
			(-)	(-)	(0.00)
			[0/0]	[458.25]	[0]
1414	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022	119.73	67.24
			(3/2022)	(176.18)	(122.55)
			[3/2022]	[242.28]	[0]
1415	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010	1,160.48	646.34
			(-)	(-)	(213.26)
			[3/2024]	[1,373.74]	[168]
1416	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-)	(-)	(1,799.84)
			[0/0]	[2,911.84]	[0]
1417	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024	773.94	925.02
			(-)	(-)	(76.06)
			[12/2024]	[850.00]	[0]
	Road Transport And Highways				
1418	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016	1,266.60	1,446.45
			(-)	(-)	(277.40)
			[0/0]	[1,544.00]	[0]
1419	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020	283.15	138.84
			(-)	(-)	(0.00)
			[0/0]	[283.15]	[0]
1420	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020	626.76	207.51
			(-)	(-)	(0.00)
			[0/0]	[626.76]	[0]
1421	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017	153.21	100.95
			(-)	(-)	(0.00)
			[0/0]	[153.21]	[0]
1422	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017	4,429.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[4,429.00]	[0]
1423	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62	305.87
			(-)	(-)	(0.00)
			[0/0]	[857.62]	[0]
1424	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/	802.65	456.99
			(-)	(-)	(0.00)
			[0/0]	[802.65]	[0]
1425	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	673.91
			(-)	(-)	(0.00)
			[0/0]	[950.63]	[0]
1426	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/	828.29	0.00
			(-)	(-)	(0.00)
			[0/0]	[828.29]	[0]
1427	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018	1,423.96	1,003.47
			(-)	(-)	(-367.88)
			[10/2021]	[1,056.08]	[35]
1428	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019	192.67	164.44
			(-)	(-)	(0.00)
			[0/0]	[192.67]	[0]
1429	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019	605.08	407.38
			(-)	(-)	(0.00)
			[0/0]	[605.08]	[0]
1430	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020	426.52	391.57
			(-)	(-)	(0.00)
			[0/0]	[426.52]	[0]
1431	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016	270.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[270.00]	[0]
1432	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019	294.13	147.88
			(-)	(-)	(0.00)
			[0/0]	[294.13]	[0]

1433	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	148.95 (0.00) [0]
1434	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [0/0]	322.81 (-) [322.81]	192.25 (0.00) [0]
1435	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [295.47]	207.71 (0.00) [0]
1436	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [0/0]	248.83 (-) [248.83]	124.12 (0.00) [0]
1437	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	121.09 (0.00) [0]
1438	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	209.06 (0.00) [0]
1439	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	174.09 (0.00) [0]
1440	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	100.34 (0.00) [0]
1441	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	115.95 (0.00) [0]
1442	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECT	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	242.66 (0.00) [0]
1443	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	165.50 (0.00) [0]
1444	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	301.86 (0.00) [0]
1445	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	205.58 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1446	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (10/2021) [11/2021]	438.28 (-) [402.00]	390.15 (-36.28) [29]
	<u>Railways</u>				
1447	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022) [6/2022]	569.63 (90.00) [742.00]	561.03 (172.37) [27]
	<u>Road Transport And Highways</u>				
1448	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	358.78 (0.00) [0]
1449	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	18.87 (0.00) [0]
1450	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	19.60 (0.00) [0]
1451	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	66.04 (0.00) [0]

1452	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	5.10 (0.00) [0]
1453	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	5.26 (0.00) [0]
1454	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	52.08 (0.00) [0]
1455	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	59.89 (0.00) [0]
1456	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	7.72 (0.00) [0]
1457	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	10.88 (0.00) [0]
1458	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	0.00 (0.00) [0]
1459	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	10.30 (0.00) [0]
1460	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	39.78 (0.00) [0]
1461	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	103.62 (0.00) [0]
1462	STRENGTHENING OF CHURAI BARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	95.22 (0.00) [0]
1463	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	33.22 (38.51) [0]
1464	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	142.81 (0.00) [15]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1465	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [12/2023]	1,383.00 (1,938.00) [1,983.00]	534.84 (600.00) [27]
	<u>Coal</u>				
1466	KHADIA EXPANSION OCP	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	0.00 (0.00) [0]
1467	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (11/2022) [11/2022]	17,237.00 (-) [17,237.80]	12,656.73 (0.80) [12]
	<u>Department Of Higher Education</u>				
1468	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (12/2021) [12/2021]	171.72 (135.00) [171.72]	110.13 (0.00) [21]
	<u>Health And Family Welfare</u>				
1469	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [0/0]	785.00 (-) [715.06]	591.61 (-69.94) [0]
1470	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/	268.84	243.92
			(-)	(-)	(0.00)

			[3/2021]	[268.84]	[0]
	<u>Home Affairs</u>				
1471	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI	5/2019	1/2022 (2/2022) [1/2020]	199.31 (-) [199.31]	20.53 (0.00) [0]
	<u>Petroleum</u>				
1472	60 KTA POLYPROPYLENE PROJECT	3/2019	4/2024 (-) [4/2024]	910.56 (-) [910.56]	105.31 (0.00) [0]
1473	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	490.71 (0.00) [0]
1474	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (345.15) [345.15]	246.25 (57.66) [0]
1475	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (8/2029) [8/2029]	3,450.20 (-) [3,450.20]	369.06 (0.00) [5]
1476	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (-) [3/2022]	217.92 (217.92) [217.92]	101.80 (0.00) [11]
1477	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (3/2022) [3/2022]	255.40 (-) [255.40]	109.97 (0.00) [19]
1478	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	998.48 (0.00) [0]
1479	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2022]	318.80 (-) [318.80]	173.55 (0.00) [15]
	<u>Power</u>				
1480	DEVIKOT SOLAR 150MW	1/2020	9/2021 (2/2022) [2/2022]	798.24 (-) [798.24]	415.99 (0.00) [5]
1481	DEVIKOT SOLAR 90MW	3/2020	9/2021 (2/2022) [2/2022]	501.29 (-) [501.29]	342.98 (0.00) [5]
1482	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	2,822.96 (0.00) [11]
1483	NOKHRA	3/2020	9/2021 (7/2022) [1/2023]	1,722.14 (-) [1,722.14]	436.25 (0.00) [16]
1484	PARASAN SOLAR POWER PROJECT	8/2021	12/2022 (-) [12/2022]	313.58 (-) [313.58]	0.00 (0.00) [0]
	<u>Railways</u>				
1485	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1486	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	315.05 (-233.29) [2]
1487	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1488	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,710.66 (641.75) [24]
1489	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-)	602.50 (-)	128.90 (197.50)

			[12/2023]	[800.00]	[-]
1490	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1491	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1492	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	69.01 (0.35) [68]
1493	JHANSI BINA DOUBLING	9/2016	3/2021 (12/2022) [12/2023]	2,001.00 (-) [2,001.00]	980.08 (0.00) [33]
1494	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [6/2025]	4,329.53 (-) [4,329.53]	71.56 (0.00) [27]
1495	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1496	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2022]	528.57 (-) [528.57]	236.91 (0.00) [36]
1497	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [6/2022]	927.01 (-) [1,400.00]	1,429.50 (472.99) [39]
1498	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	2,261.21 (0.00) [0]
1499	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [12/2021]	668.70 (668.00) [680.00]	4.00 (11.30) [21]
1500	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,054.05 (0.00) [21]
1501	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [341.66]	0.00 (191.66) [66]
1502	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,345.00]	0.00 (2.00) [0]
1503	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,367.09 (0.00) [48]
1504	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,824.00]	1,373.75 (528.58) [0]
1505	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	346.17 (-149.01) [0]
1506	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [489.64]	105.51 (-739.36) [-]
1507	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	945.85 (56.40) [33]
Road Transport And Highways					
1508	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	242.67 (0.00) [0]
1509	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-)	351.34 (-)	433.68 (66.34)

			[0/0]	[417.68]	[0]
1510	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [627.93]	633.24 (132.15) [0]
1511	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [469.31]	459.07 (177.95) [0]
1512	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH- 56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1513	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,517.15 (211.43) [0]
1514	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [0/0]	1,668.00 (-) [1,668.00]	946.08 (0.00) [0]
1515	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1516	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (7/2022) [7/2022]	1,408.00 (827.05) [827.05]	387.83 (-580.95) [-]
1517	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (6/2021) [9/2021]	1,737.00 (1,201.51) [1,201.51]	1,077.55 (-535.49) [0]
1518	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH- 29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1519	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH- 29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1520	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH- 29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1521	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,118.76 (382.01) [0]
1522	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT- MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1523	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	985.40 (0.00) [0]
1524	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1525	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1526	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1527	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1528	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1529	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (4/2022) [4/2022]	282.41 (319.96) [319.96]	193.43 (37.55) [73]

1530	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	1,084.94 (-145.21) [0]
1531	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	766.64 (0.00) [0]
1532	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1533	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	75.10 (0.00) [0]
1534	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	838.28 (0.00) [0]
1535	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [1,197.00]	1,176.70 (271.60) [0]
1536	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1537	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1538	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1539	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1540	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1541	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	3/2018	8/2020 (-) [12/2021]	288.30 (-) [288.30]	192.35 (0.00) [16]
1542	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (12/2021) [12/2021]	1,373.28 (-) [1,373.28]	1,285.31 (0.00) [21]
1543	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [0/0]	1,184.71 (-) [1,310.00]	1,294.21 (125.29) [0]
1544	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (10/2022) [10/2022]	899.00 (-) [899.00]	450.47 (0.00) [42]
1545	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.00 (0.00) [0]
1546	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [3/2022]	281.45 (319.96) [319.96]	115.07 (38.51) [-]
1547	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [987.94]	0.00 (304.70) [0]
1548	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [12/2021]	326.99 (327.00) [326.99]	123.44 (0.00) [-]
1549	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [11/2021]	296.50 (-) [296.50]	237.29 (0.00) [14]
1550	REHABILITATION AND UP-GRADATION FROM 2 LANE TO	3/2018	/	1,025.80	222.94

	4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU		(-) [0/0]	(-) [677.07]	(-348.73) [0]
1551	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/	1,115.28	332.69
			(-) [0/0]	(-) [770.04]	(-345.24) [0]
1552	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [3/2022]	263.89 (-) [242.05]	188.89 (-21.84) [23]
1553	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [1/2021]	185.18 (-) [185.18]	124.69 (0.00) [0]
1554	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [4/2021]	249.50 (-) [249.50]	229.57 (0.00) [0]
1555	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (3/2020) [3/2021]	218.90 (-) [218.90]	147.70 (0.00) [0]
1556	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/	306.59	195.15
			(-) [11/2021]	(-) [306.59]	(0.00) [-]
1557	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [10/2019]	215.16 (215.00) [215.16]	145.76 (0.00) [0]
1558	REHABILITATION AND UPGRADATION OF KALUPUR- LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2- LANE WITH	3/2016	1/2020 (-) [3/2021]	240.30 (240.00) [240.30]	200.10 (0.00) [0]
1559	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [3/2021]	208.88 (-) [208.88]	183.54 (0.00) [0]
1560	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,650.78 (0.00) [0]
1561	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/	2,140.93	1,315.69
			(-) [0/0]	(-) [2,140.93]	(0.00) [0]
1562	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [3/2023]	724.60 (720.81) [724.60]	0.00 (0.00) [0]
1563	VARANASI RING ROAD PKG - I	1/2018	/	450.77	0.00
			(-) [0/0]	(-) [450.77]	(0.00) [0]
1564	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [1/2021]	164.54 (-) [164.54]	141.33 (0.00) [0]
	<u>Steel</u>				
1565	FORGED WHEEL PLANT	4/2014	9/2018 (11/2021) [11/2021]	1,682.85 (-) [2,100.00]	1,736.92 (417.15) [38]
	<u>Urban Development</u>				
1566	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [5/2025]	8,379.62 (-) [8,379.62]	426.47 (0.00) [14]
1567	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2025]	11,076.48 (-) [11,076.48]	1,917.78 (0.00) [12]
1568	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	6,928.00 (0.00) [0]
	<u>Water Resources</u>				
1569	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-)	213.62 (261.12)	0.00 (47.50)

			[3/2022]	[261.12]	[0]
1570	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	53.62 (0.00) [0]
1571	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [234.03]	14.63 (2.24) [0]
1572	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1573	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [6/2022]	298.12 (213.91) [213.91]	0.00 (-84.21) [11]
1574	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	132.29 (0.00) [0]
1575	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [5/2021]	460.45 (-) [460.45]	248.16 (0.00) [0]
1576	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [690.71]	0.00 (8.93) [0]
1577	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [1/2021]	279.91 (330.05) [330.05]	260.12 (50.14) [0]
1578	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2021]	967.23 (-) [967.23]	65.24 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1579	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2022]	456.86 (-) [456.86]	314.79 (0.00) [24]
	<u>Home Affairs</u>				
1580	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	<u>Petroleum</u>				
1581	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [6/2022]	160.10 (-) [160.10]	104.05 (0.00) [28]
	<u>Power</u>				
1582	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.93 (274.07) [0]
1583	NAITWAR MORI HEP	10/2017	12/2021 (6/2022) [6/2022]	648.33 (-) [947.89]	704.97 (299.56) [6]
1584	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [9/2024]	2,978.48 (5,867.38) [5,867.38]	5,187.12 (2,888.90) [138]
1585	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2023]	1,657.00 (4,825.60) [4,825.60]	4,266.10 (3,168.60) [88]
1586	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (12/2024) [12/2024]	2,491.58 (3,860.35) [3,860.35]	2,313.83 (1,368.77) [138]
	<u>Railways</u>				
1587	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]

1588	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [22,716.11]	4,874.57 (6,500.11) [3]
	Road Transport And Highways				
1589	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [3/2022]	403.36 (-) [403.36]	217.43 (0.00) [45]
1590	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [3/2022]	417.24 (-) [417.24]	265.48 (0.00) [46]
1591	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (2/2022) [2/2022]	605.84 (-) [722.46]	722.46 (116.62) [43]
1592	4-LANNING OF CHUTMALPUR-GANESHUPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [0/0]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [0]
1593	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [3/2022]	274.31 (-) [274.31]	126.90 (0.00) [46]
1594	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [7/2022]	1,383.78 (-) [1,383.78]	280.16 (0.00) [48]
1595	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (12/2021) [12/2021]	248.00 (-) [248.00]	109.23 (0.00) [19]
1596	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (10/2022) [0/0]	720.00 (-) [720.00]	206.32 (0.00) [0]
1597	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [0/0]	478.51 (-) [478.00]	315.11 (-0.51) [0]
1598	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (7/2021) [7/2021]	232.81 (-) [232.81]	171.22 (0.00) [0]
1599	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (5/2021) [5/2021]	283.51 (-) [283.51]	259.90 (0.00) [0]
1600	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (7/2021) [7/2021]	257.34 (-) [257.34]	214.90 (0.00) [0]
1601	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (12/2021) [12/2021]	282.08 (-) [282.08]	207.83 (0.00) [30]
1602	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (7/2021) [7/2021]	200.34 (-) [200.34]	185.44 (0.00) [0]
1603	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (9/2021) [9/2021]	418.88 (-) [418.88]	287.56 (0.00) [0]
1604	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (10/2020) [10/2020]	266.52 (-) [266.52]	186.16 (0.00) [0]
1605	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (12/2020) [12/2020]	234.88 (-) [234.88]	174.51 (0.00) [0]
1606	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (10/2021) [10/2021]	293.68 (-) [293.68]	183.73 (0.00) [-]
1607	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	116.25 (0.27) [0]

1608	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (8/2021) [8/2021]	248.22 (-) [248.22]	234.12 (0.00) [0]
	<u>Water Resources</u>				
1609	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (3/2021) [0/0]	158.00 (-) [158.00]	84.32 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1610	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (1/2023) [1/2023]	389.71 (-) [389.71]	199.30 (0.00) [14]
1611	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (6/2022) [4/2022]	458.00 (-) [458.00]	157.18 (0.00) [25]
	<u>Coal</u>				
1612	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [10/2022]	304.13 (341.22) [341.22]	73.17 (37.09) [67]
1613	EXPANSION PR OF JHANJRA UG(5.00 MTY)	11/2015	3/2022 (3/2029) [3/2029]	1,210.12 (-) [1,210.12]	49.04 (0.00) [84]
1614	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	18.15 (0.00) [0]
1615	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.19 (0.00) [0]
1616	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	622.22 (2,484.75) [60]
1617	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	6.82 (0.00) [0]
1618	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.75 (0.00) [0]
1619	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2029]	1,055.05 (-) [1,055.05]	690.16 (0.00) [132]
1620	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	2.70 (0.00) [0]
	<u>Department Of Higher Education</u>				
1621	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [0/0]	193.83 (-) [193.83]	170.60 (0.00) [0]
	<u>Health And Family Welfare</u>				
1622	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1623	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1624	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [10/2021]	651.99 (-) [651.99]	591.68 (0.00) [-]
1625	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [10/2021]	355.15 (-) [355.15]	317.45 (0.00) [31]
	<u>Home Affairs</u>				

1626	NSG AT KOLKATA	10/2014	4/2018 (12/2021) [12/2021]	162.88 (238.00) [238.00]	172.13 (75.12) [44]
	<u>Mines</u>				
1627	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	4/2019	4/2022 (-) [4/2022]	255.37 (-) [255.37]	0.86 (0.00) [0]
	<u>Petroleum</u>				
1628	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (3/2022) [3/2022]	3,712.00 (-) [3,696.00]	2,292.73 (-16.00) [-6]
1629	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (8/2031) [8/2031]	5,830.20 (-) [5,830.20]	136.39 (0.00) [5]
1630	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,740.00 (-) [1,740.00]	939.30 (0.00) [12]
1631	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	103.42 (0.00) [0]
1632	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [7/2022]	163.02 (207.36) [207.36]	126.85 (44.34) [27]
	<u>Power</u>				
1633	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [2/2022]	529.68 (633.80) [633.80]	472.23 (104.12) [39]
1634	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (3/2021) [6/2021]	454.11 (-) [454.11]	345.15 (0.00) [0]
1635	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [12/2024]	1,381.84 (-) [1,381.54]	721.34 (-0.30) [63]
	<u>Railways</u>				
1636	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [324]
1637	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	299.01 (16.56) [-]
1638	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	41.78 (352.63) [-]
1639	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1640	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [0]
1641	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1642	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1643	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (200.34) [614.00]	275.06 (316.68) [0]
1644	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,090.60]	1,089.12 (710.00) [0]

1645	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [10/2021]	602.27 (-) [1,167.00]	1,028.89 (564.73) [-2]
1646	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1647	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	1,422.91 (1,725.49) [108]
1648	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1649	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	3,033.55 (307.50) [108]
1650	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	908.35 (430.57) [72]
1651	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1652	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (2,587.75) [1,827.15]	989.55 (744.15) [0]
1653	4-LANING OF BRAHAMPUR-FARAKA	2/2011	8/2013 (-) [6/2023]	998.79 (-) [998.79]	1,890.84 (0.00) [118]
1654	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [11/2021]	1,078.84 (-) [1,078.84]	2,301.82 (0.00) [99]
1655	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	1,396.18 (0.00) [0]
1656	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/	361.15	277.34
			(-) [0/0]	(363.93) [363.93]	(2.78) [0]
1657	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (1/2021) [3/2022]	271.17 (291.20) [291.20]	120.51 (20.03) [40]
1658	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	26.91 (53.70) [39]
1659	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [0/0]	229.37 (-) [229.37]	0.00 (0.00) [0]
1660	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (8/2022) [8/2022]	236.78 (263.26) [263.26]	77.57 (26.48) [36]
1661	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (3/2021) [6/2021]	254.30 (254.30) [254.30]	118.34 (0.00) [0]
1662	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	696.60 (0.00) [0]
1663	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/	1,261.98	97.16
			(-) [0/0]	(2,145.96) [1,952.20]	(690.22) [0]
1664	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (-) [2/2020]	279.70 (398.52) [398.52]	331.86 (118.82) [0]

1665	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2021) [10/2021]	396.86 (396.86) [396.86]	271.47 (0.00) [25]
1666	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,511.49 (695.65) [0]
1667	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2021) [6/2021]	218.70 (218.70) [218.70]	111.78 (0.00) [0]
1668	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (1/2022) [1/2022]	426.18 (426.18) [426.18]	254.43 (0.00) [16]
	<u>Water Resources</u>				
1669	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (5/2021) [0/0]	274.76 (-) [274.76]	220.08 (0.00) [0]
1670	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1671	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1672	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1673	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [10/2022]	160.00 (154.73) [154.73]	0.00 (-5.27) [8]
1674	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1675	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	11.56 (0.00) [0]
1676	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [6/2022]	198.43 (224.69) [224.69]	0.00 (26.26) [4]
1677	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1678	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	11.56 (0.00) [0]
1679	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	11.56 (0.00) [0]
1680	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [3/2021]	272.32 (-) [272.32]	248.86 (0.00) [0]
	Total			21,74,182.86 (8,05,359.46) [26,08,330.02]	12,64,545.31 (4,34,147.16)
