

**395th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
September,2018**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for September 2018 contains information on the status of the 1420 Central Sector Infrastructure Projects costing ₹150 crore and above.
2. During the reference month, out of 1420 projects, 366 projects are delayed with respect to their original schedules and 70 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 70 projects, 30 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	574	90	11	3
2	RAILWAYS	375	94	31	15
3	PETROLEUM	138	28	5	3
4	POWER	105	63	16	8
5	COAL	97	35	0	0
6	URBAN DEVELOPMENT	61	25	5	0
7	STEEL	13	9	1	1
8	HEALTH AND FAMILY WELFARE	22	4	0	0
9	TELECOMMUNICATIONS	10	7	1	0
10	FERTILISERS	6	2	0	0
11	SHIPPING AND PORTS	5	2	0	0
12	ATOMIC ENERGY	4	4	0	0
13	MINES	4	0	0	0
14	CIVIL AVIATION	2	2	0	0
15	HEAVY INDUSTRY	2	1	0	0
16	DEFENCE PRODUCTION	2	0	0	0
Total		1420	366	70	30

3. Total original cost of implementation of the 1420 projects was ₹18,05,667.72 crore and their anticipated completion cost is likely to be ₹21,63,672.09 crore, which reflects overall cost overruns of ₹3,58,004.37 crore (19.83% of original cost). The expenditure incurred on these projects till September 2018 is ₹7,83,503.00 crore, which is 36.21% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-10-2018)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	74.68
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	78.87
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	291.29	1.87
2	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	170.37	1.60
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	13.31
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	322.00	2.88
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROLEUM					
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	83.01
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	330.35	62.78
5	PARADIP HALDIA DURGAPUR LPG PIPELINE	02/2011	913.00	1330.00	45.67
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW)	09/2003	6285.33	19496.34	210.19

	(NHPC)				
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4401.90	165.65
3	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1078.31	156.12
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
5	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	139.69
RAILWAYS					
1	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	04/2007	23.56	1330.73	5548.26
2	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
3	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	04/2011	120.70	1800.00	1391.30
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
5	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	880.06
2	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	114.56
3	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
4	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
5	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
1	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	818.00	2907.00	255.38
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
3	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	44.75
4	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58

5	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
---	----------------------------------	---------	----------	----------	-------

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-10-2018)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	2608.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	244.07
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	BHANEAGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	291.29	5.34
2	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	170.37	2.68
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	22.48
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	322.00	9.01
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROLEUM					
1	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	03/2014	3076.00	4190.00	1114.00
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	715.36
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00

4	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	5245.96	657.67
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	5475.21
4	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9141.97	4387.55
5	BONGAIGAON THERMAL POWER PROJECT	01/2008	4375.35	8150.00	3774.65
RAILWAYS					
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	13809.00	9354.83
5	BHANUPALI-BILASPUR BERI NL	04/2008	1046.88	7000.00	5953.12
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82
2	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	1728.77
3	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
4	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
5	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
STEEL					
1	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	818.00	2907.00	2089.00
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
4	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1420 projects, 385 are on schedule, 366 are delayed, 369 projects reported cost overrun and 136 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 300 if delay is calculated on the basis of latest schedule of completion. Further, for 651 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 366 delayed projects, 100 (27.32%) projects have overall delay in the range of 1 to 12 months, 69 (18.85%) projects have delay in the range of 13 to 24 months, 91 (24.86%) projects have delay in the range of 25 to 60 months and 106 (28.96%) projects have delay of 61 months and above. **The average time overrun in these 366 delayed projects is 45.95 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-09-2018)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)	Ratio
ATOMIC ENERGY						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	03/2019	102	0.55
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54	0.42
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48	0.36
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36	0.28
CIVIL AVIATION						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2018	92	0.79
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21	0.26
COAL						
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144	0.69
2	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132	0.83
3	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2019	108	0.80
4	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2020	108	0.72
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	03/2021	108	0.72
FERTILISERS						
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	04/2019	29	0.54
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	02/2016	12/2017	10/2018	10	0.31
HEALTH AND FAMILY WELFARE						
1	AIIMS - OPD(NEW)	08/2014	05/2017	09/2018	16	0.34

2	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	08/2019	15	0.44
3	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	12/2018	10	0.34
4	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	09/2018	6	0.13
HEAVY INDUSTRY						
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	08/2016	09/2019	37	1.00
PETROLEUM						
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2019	74	0.64
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	03/2019	72	0.60
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	03/2019	70	0.73
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70	0.62
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	12/2019	57	0.59
POWER						
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147	0.64
2	BARH STPP(3X660MW) NTPC	02/2005	01/2011	04/2021	123	0.63
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2018	121	0.74
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	03/2019	111	0.65
5	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103	0.66
RAILWAYS						
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324	0.00
2	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	12/2023	285	0.89
3	HUBLI-ANKOLA(NL),SWR	04/1997	03/2001	12/2024	285	0.86
4	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264	0.79
5	MANDHANA - BRAHMAWART NEW LINE PROJECT.	04/1997	04/1999	12/2018	236	0.91
ROAD TRANSPORT AND HIGHWAYS						
1	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	09/2018	118	0.67
2	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	04/2009	10/2018	114	0.64
3	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	10/2018	101	0.73
4	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	11/2011	06/2019	91	0.75
5	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	10/2011	10/2018	84	0.66
SHIPPING AND PORTS						
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	12/2018	96	0.67

2	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29	0.58
STEEL						
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	06/2019	49	0.43
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2019	29	0.26
3	COKE OVEN BATTERY-5	12/2011	12/2017	09/2019	21	0.23
4	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	12/2018	14	0.31
5	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	11/2018	11	0.26
TELECOMMUNICATIONS						
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58	0.59
2	MAHARASHTRA NODAL (LOT 1)	08/2017	04/2018	10/2018	6	0.43
3	MAHARASHTRA CORE (LOT1)	08/2017	04/2018	10/2018	6	0.43
4	GUJARAT ACCESS (LOT 1)	09/2017	05/2018	10/2018	5	0.38
5	MAHARASHTRA ACCESS (LOT 1)	08/2017	05/2018	10/2018	5	0.36
URBAN DEVELOPMENT						
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2019	77	0.70
2	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72	0.39
3	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70	0.54
4	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64	0.78
5	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	11/2019	56	0.81

*** Ratio = Anticipated DOC – Original DOC / Anticipated DOC – DOA**

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-10-2018)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	546.69	01/2011	09/2018
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
COAL							
1	RANIGANJ MASTER PLAN	08/2009	2661.73	2661.73	0.00	08/2019	08/2019
2	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	173.06	12/2019	12/2019
3	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	8.71	09/2019	09/2019
4	NEYVELI SOLAR POWER PROJECT 130 MW	05/2016	687.28	759.19	758.30	06/2017	12/2017
5	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	16.21	03/2022	03/2022
HEALTH AND FAMILY WELFARE							
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	414.11	141.00	11/2013	N.A.
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	276.91	06/2020	06/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	39.35	04/2020	04/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	214.62	09/2018	09/2018
HEAVY INDUSTRY							
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	161.86	08/2016	09/2019
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT	01/2006	993.00	1693.00	1549.85	01/2012	N.A.

	PADUR						
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.12	02/2017	N.A.
4	MMPL PIPELINE REROUTING PROJECT	04/2013	449.58	449.58	110.72	12/2019	12/2019
5	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10295.43	09/2010	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	2844.03	10/2017	12/2016
3	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	08/2008	771.00	1624.00	1429.45	02/2013	10/2018
4	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL- KHALSTI-LEH PROJECT	01/2014	1788.41	2333.71	1528.12	09/2017	09/2018
5	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	187.24	04/2016	10/2018
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	968.28	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	267.93	03/2019	03/2020
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	749.69	0.00	06/2005	N.A.
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	634.48	629.43	03/1994	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	520.01	520.01	0.00	N.A.	N.A.
2	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	0.00	N.A.	10/2020

3	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	319.68	0.00	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	411.12	12/2010	12/2018
4	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	257.90	1.45	12/2017	05/2020
STEEL							
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	4749.00	4749.00	105.87	09/2017	N.A.
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	172.30	06/2017	N.A.
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	214.10	33.46	05/2018	10/2018
4	MAHARASHTRA ACCESS (LOT 1)	08/2017	212.70	212.70	37.08	05/2018	10/2018
5	MAHARASHTRA CORE (LOT1)	08/2017	167.68	167.68	30.21	04/2018	10/2018
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MEDICAL COLLEGE AND	05/2005	768.88	1113.34	1085.64	02/2014	N.A.

	HOSPITAL AT GULBARGA						
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-10-2018)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	5687.52
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	546.69
COAL					
1	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	0.00	266.38
2	BALRAM OCP EXTENSION, MCL 8.00 MTY	12/2007	172.08	0.00	264.26
3	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	581.54
4	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	234.48
5	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	0.00	477.74
HEALTH AND FAMILY WELFARE					

1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	237.80
2	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	191.38
3	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	0.00	469.00
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	0.00	2289.00
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	871.35	0.00	961.00
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7058.21
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10295.43
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	6788.96
4	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	0.00	3666.44
5	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	0.00	963.23
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	968.28
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	274.56	629.43
3	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.21
4	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	759.20
5	AMRAVATI-NARKHER NL(CR)	06/1994	663.01	668.34	715.32
ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	410.32
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	268.94
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	209.80
4	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	297.81
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	312.79
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	411.12
2	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.00	275.98
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64

2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77
4	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	0.00	307.50

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on as on 01-10-2018)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	N.A.	N.A.
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	N.A.	03/2018
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	03/2012	N.A.	N.A.
3	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
4	RAJMAHAL OC EXP.	09/2009	03/2014	N.A.	N.A.
5	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 4	12/2016	05/2018	08/2018	08/2018
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	N.A.
3	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	N.A.
4	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	N.A.
5	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	N.A.	N.A.
3	PARADIP-RAIPUR- RANCHI	08/2009	12/2016	N.A.	N.A.

	PIPELINE				
4	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
5	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	12/2016
3	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
4	KUDGI STPP STAGE 1	01/2012	01/2017	N.A.	N.A.
5	MOUDA STPP STAGE 2	03/2012	09/2016	02/2017	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	N.A.	N.A.
4	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	N.A.	N.A.
5	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	03/2006	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	01/1991	10/2016	N.A.	N.A.
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	N.A.	N.A.
STEEL					

1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	09/2017	N.A.	N.A.
2	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 30.09.2018 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150.Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	574	11
2	RAILWAYS	375	31
3	PETROLEUM	138	5
4	POWER	105	16
5	COAL	97	0
6	URBAN DEVELOPMENT	61	5
7	HEALTH AND FAMILY WELFARE	22	0
8	STEEL	13	1
9	TELECOMMUNICATIONS	10	1
10	FERTILISERS	6	0
11	SHIPPING AND PORTS	5	0
12	ATOMIC ENERGY	4	0
13	MINES	4	0
14	CIVIL AVIATION	2	0
15	HEAVY INDUSTRY	2	0
16	DEFENCE PRODUCTION	2	0
	Total	1420	70

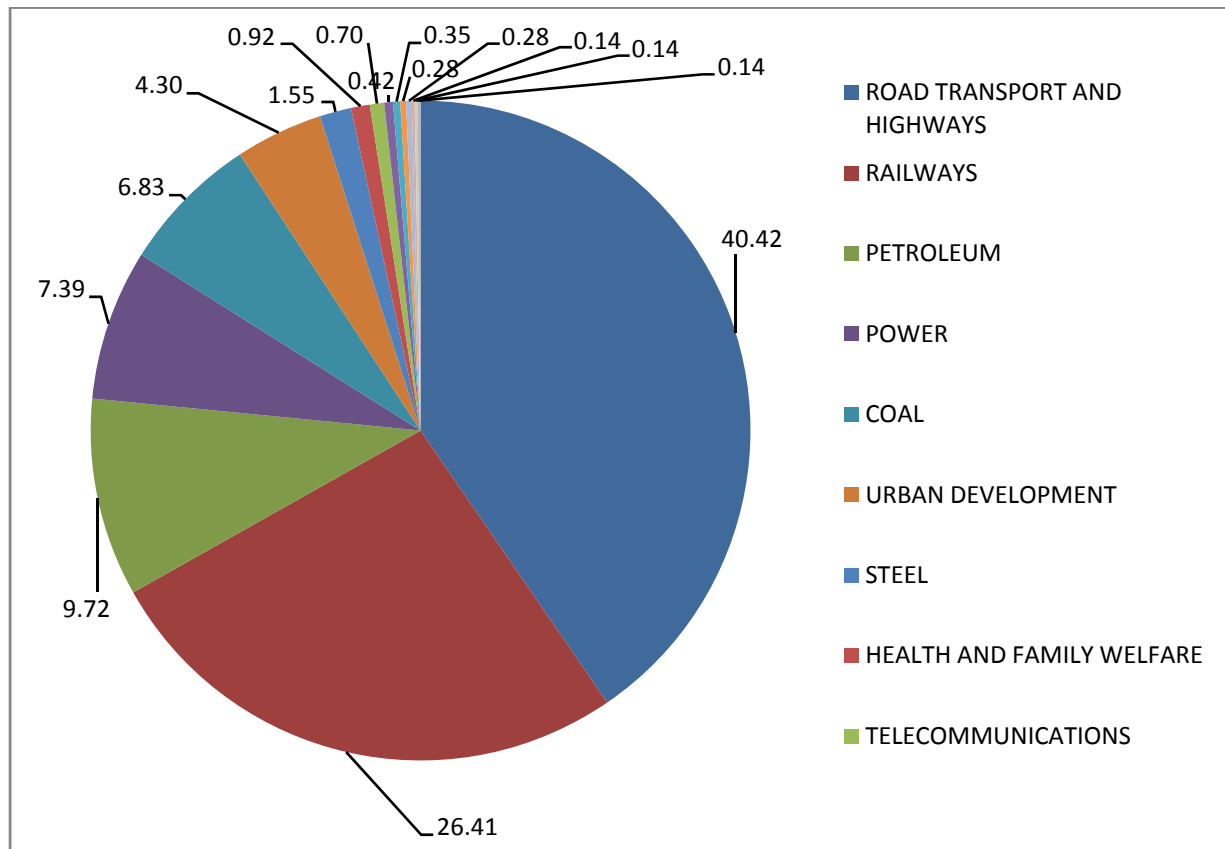


TABLE-2

Month wise List of Completed Projects Costing Rs.150 Crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2018			
	<u>STEEL</u>			
1	ALTERNATE GAS NETWORK AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000093]	255.19	03/2018	177.21
	<u>PETROLEUM</u>			
2	ENNORE TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000224]	393.00	04/2018	281.45
	<u>POWER</u>			
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000123]	198.63	09/2014	127.13
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000179]	6,517.36	04/2018	3,772.80
5	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000210]	207.88	07/2018	17.00
	<u>HEALTH AND FAMILY WELFARE</u>			
6	AIIMS-RAE BARELI-HOUSING (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000006]	159.50	11/2013	158.65
	<u>RAILWAYS</u>			
7	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000189]	822.39	-	1,713.20
8	NEW COOCHBEHAR TO SAMUKTALA (NORTH EAST FRONTIER RAILWAY) - [N22000197]	209.77	-	620.04
9	DELANG-PURI DOUBLING (EAST COAST RAILWAY) - [N22000320]	165.16	03/2015	226.35
10	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) (RAIL VIKAS NIGAM LTD.) - [N22000322]	190.10	-	320.41
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	TALEGAON-AMRAVATI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000140]	567.00	11/2013	1,055.94
12	MURADABAD-BAREILY PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000154]	1,267.00	06/2013	2,667.96
	<u>SHIPPING AND PORTS</u>			

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED PPP (ANNUITY)(KAMARAJAR PORT LIMITED) - [N25000065]	198.94	06/2017	255.02
14	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000067]	274.85	04/2017	251.64
	<u>URBAN DEVELOPMENT</u>			
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN Central Sector Projects(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000091]	350.02	03/2015	452.35
	May,2018			
	<u>PETROLEUM</u>			
16	TWENTY NOS. FEEDER GAS LINES (OIL INDIA LIMITED) - [N16000192]	228.64	12/2016	149.73
17	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000201]	238.50	03/2017	203.98
18	SIX PIPELINE REPLACEMENT PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000214]	181.02	01/2017	174.88
19	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000245]	931.00	07/2017	684.74
	<u>POWER</u>			
20	PARE HYDRO ELECTRIC PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000045]	573.99	08/2013	1,637.60
	<u>RAILWAYS</u>			
21	GADWAL - RAICHUR (NL), SCR (SOUTH CENTRAL RAILWAY) - [220100270]	92.63	02/2011	319.43
22	JAGGAYYAPET - MELLACHERUVU (SOUTH CENTRAL RAILWAY) - [N22000304]	313.24	01/1999	578.00
	June,2018			
	<u>POWER</u>			
23	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000197]	1,479.30	04/2017	897.12
24	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000237]	167.75	04/2019	86.62
	<u>RAILWAYS</u>			
25	RANCHI-LOHARDAGA(GC),SER (SOUTH EASTERN RAILWAY) - [220100214]	194.07	06/2004	194.07
26	BHOPAL BINA 3D LINE DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000077]	687.20	03/2010	1,033.77

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	July,2018			
	<u>STEEL</u>			
27	EXPANSION OF BHILAI STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000057]	17,265.00	03/2013	19,855.23
	<u>PETROLEUM</u>			
28	DEVELOPMENT OF C-26 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000133]	2,592.17	05/2014	2,049.26
29	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000134]	200.69	07/2014	109.58
30	CONSTRUCTION OF THREE ETPS, MEHSANA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000135]	260.74	11/2014	83.44
31	PIPELINE REPLACEMENT PROJECT, AHMEDABAD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000159]	202.25	07/2016	130.21
32	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000172]	4,124.35	04/2016	5,347.49
33	MH NORTH REDEVELOPMENT PHASE III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000188]	5,706.47	05/2017	5,724.54
34	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000246]	215.38	06/2017	198.98
	<u>POWER</u>			
35	BOKARO THERMAL POWER STATION-A (DAMODAR VALLEY CORPORATION) - [N18000199]	2,313.00	12/2011	3,965.00
36	RAGHUNATHPUR THERMAL POWER STATION PHASE-I (DAMODAR VALLEY CORPORATION) - [N18000202]	4,122.00	02/2011	8,479.00
	September,2018			
	<u>PETROLEUM</u>			
37	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000199]	257.87	11/2016	243.30
38	NAWAGAM-KOYALI PIPELINE PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000211]	195.63	09/2018	174.68
39	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000264]	337.06	08/2018	167.16
	<u>POWER</u>			
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000143]	514.20	06/2015	605.50
41	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000169]	288.49	02/2017	276.10

Month wise List of Completed Projects Costing Rs.150 Crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000220]	810.48	12/2018	528.50
43	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000254]	2,525.00	11/2017	2,015.38
44	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B Central Sector Projects(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000255]	2,225.00	01/2018	1,655.02
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
45	CHAMBAL BRIDGE, NH-76 (RJ-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000068]	275.00	02/2010	252.25
46	DEOLI KOTA PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000148]	593.00	07/2013	1,073.73
47	2-LANNING WITH PS KHAGARIA-PURNEA PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000184]	664.00	02/2014	654.59
48	2-LANING WITH PS BHILWARA-LODPURA SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000240]	240.10	03/2016	194.69
49	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000337]	538.08	02/2018	335.24
50	JAISALMER - BARMER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000348]	482.27	02/2018	308.83
51	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000352]	455.60	07/2017	202.68
52	JODHPUR - BARMER SECTION OF PACKAGE -I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000354]	264.72	04/2017	98.18
53	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000358]	562.34	04/2018	109.07
54	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000433]	768.56	03/2018	774.99
55	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000436]	664.53	03/2018	702.97
56	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000440]	789.31	03/2018	867.54
57	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000481]	1,232.00	08/2015	1,091.17
58	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000484]	239.23	12/2017	123.47
59	FOUR LANING OF KAITHAL - RAJASTHAN BORDER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000487]	1,393.00	-	1,917.40
60	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000500]	830.36	07/2018	326.23

Month wise List of Completed Projects Costing Rs.150 Crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
61	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) AUTHORITY OF INDIA) - [N24000597] (NATIONAL HIGHWAYS	600.85	05/2018	109.84


Summary of projects in the Flash Report for the month of September, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1417
Number of Projects completed/dropped/frozen in Current Month	25
Number of Projects elevated to the status of Major project during the current month	4
Number of Projects Added in Current Month	24
Number of Projects in Current Month	1420

Brief Analysis

Project Status with respect to Original Schedule: Out of 1420 projects, 18 projects are ahead of schedule, 385 projects are on schedule 366 projects are delayed. 591 projects do not have fixed dates of commissioning. 60 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

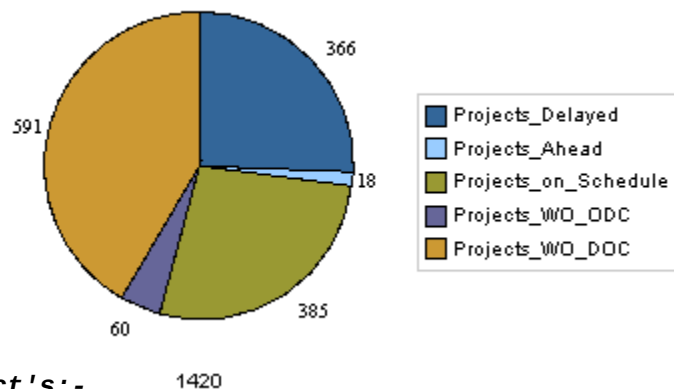

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1420 projects when sanctioned, was of the order of Rs. 1805667.72 crore but this was subsequently revised to Rs. 2163672.09 crore implying a cost overrun of 19.8%. The expenditure incurred on these projects till September, 2018 is Rs. 783503 crore, which is 36.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

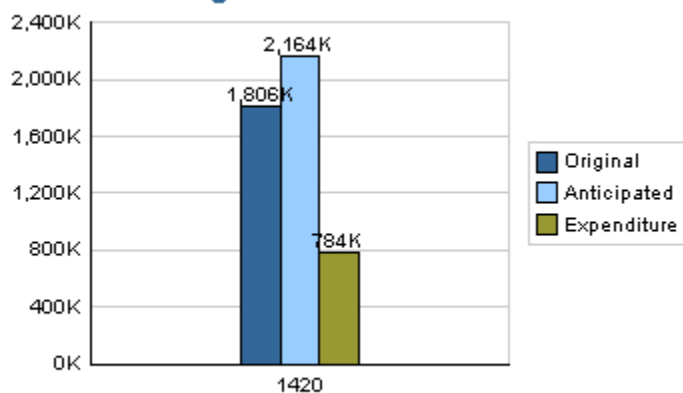


TABLE-3

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1417
No of Projects Completed/Dropped/Frozen in Current Month	25
Elevated	4
No of Projects added in Current Month	24
No of Projects in Current Month	1420

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	366 (25.77%)	18 (1.27%)	385(27.11%)	60 (4.23%)	591(1.62%)	1420
Latest Approved (Date)	300 (21.13%)	18 (1.27%)	462(32.54%)	49 (3.45%)	591(1.62%)	1420

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1229	15,21,293.17	17,26,702.33	5,60,930.72	32.50	2,05,409.16	13.50
Project with Revision in Cost	191	4,19,117.15	4,36,969.76	2,22,572.28	50.90	17,852.61	4.30
Total	1,420	19,40,410.32	21,63,672.09	7,83,503.00	36.21	2,23,261.77	11.51
Original Cost of All Projects							
Original Cost	1,420	18,05,667.72	21,63,672.09	7,83,503.00	36.21	3,58,004.37	19.83

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	366	6,93,478.12	8,49,677.29	4,30,021.88	50.60	1,56,199.17	22.50
Latest Approved (RCE)	300	4,87,930.73	5,64,856.58	2,65,002.57	46.90	76,925.85	15.80

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	70	92,822.43	1,26,022.15	69,069.70	54.80	33,199.72	35.80
Total	70	92,822.43	1,26,022.15	69,069.70	54.81	33,199.72	35.77

TABLE-4

Extent of cost overrun in projects with respect to original schedule(Sector Wise) RS. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	97	94,971.26	94,434.45	-0.57	9	19,751.90	21,082.91	6.74
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	5.89
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	13	32,529.65	34,406.05	5.77	2	1,161.00	3,395.40	192.45
7	PETROLEUM	138	2,24,159.63	2,24,611.19	0.20	15	19,129.74	24,806.72	29.68
8	POWER	105	3,07,223.51	3,72,561.25	21.27	43	1,77,202.39	2,42,540.13	36.87
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	3	987.47	1,036.38	4.95
11	RAILWAYS	375	4,78,359.05	7,25,343.31	51.63	227	1,87,092.08	4,38,377.89	134.31
12	ROAD TRANSPORT AND HIGHWAYS	574	3,86,925.98	4,01,159.04	3.68	46	29,048.52	43,967.62	51.36
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	3	760.89	1,545.44	103.11
14	TELECOMMUNICATIONS	10	17,191.20	28,420.00	65.32	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	61	1,71,744.40	1,79,453.64	4.49	12	33,337.41	41,055.54	23.15
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	2	453.64	461.66	1.77
Total		1420	18,05,667.72	21,63,672.09	19.83	369	4,99,749.90	8,70,645.29	74.22

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-5

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above
(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	67	1,06,162.46	1,10,244.37	3.85	10	8,218.07	13,170.09	60.26
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	5	9,181.79	26,308.30	186.53
3	ASSAM	47	31,336.57	40,105.00	27.98	12	10,673.39	19,649.33	84.10
4	BIHAR	90	75,487.50	1,12,167.59	48.59	33	40,729.24	77,484.96	90.24
5	GOA	10	4,292.52	4,300.54	0.19	2	453.64	461.66	1.77
6	GUJARAT	52	62,135.82	73,481.22	18.26	9	26,996.12	39,573.30	46.59
7	HARYANA	22	16,967.58	18,880.24	11.27	5	2,452.13	4,498.00	83.43
8	HIMACHAL PRADESH	12	14,659.32	26,087.65	77.96	2	4,966.47	16,394.80	230.11
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	606.15
10	KARNATAKA	46	82,148.90	87,206.53	6.16	12	21,085.29	26,339.67	24.92
11	KERALA	22	25,879.48	28,054.10	8.40	6	7,475.98	9,846.14	31.70
12	MADHYA PRADESH	62	69,052.01	78,734.42	14.02	11	30,035.14	40,701.17	35.51
13	MAHARASHTRA	130	1,87,818.64	1,99,946.17	6.46	25	35,748.90	50,287.07	40.67
14	MANIPUR	2	4,670.86	14,025.69	200.28	1	4,454.17	13,809.00	210.02
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	1	906.46	6,000.00	561.92
16	MIZORAM	4	3,406.61	5,613.14	64.77	1	2,393.47	4,600.00	92.19
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	28.95
18	ODISHA	81	91,616.58	97,021.18	5.90	19	24,687.84	30,093.10	21.89
19	PUNJAB	32	17,169.94	17,175.67	0.03	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	56	44,581.43	47,282.81	6.06	13	5,869.36	8,579.63	46.18
21	SIKKIM	10	3,786.19	6,834.56	80.51	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	70	1,15,478.79	1,33,318.11	15.45	26	30,018.91	48,949.44	63.06
23	TRIPURA	9	4,422.36	8,312.05	87.96	7	3,555.47	7,445.16	109.40
24	UTTAR PRADESH	109	1,27,439.00	1,31,279.91	3.01	19	26,906.98	32,195.23	19.65
25	WEST BENGAL	58	58,359.34	72,814.63	24.77	23	18,570.71	33,395.68	79.83
26	A & N ISLANDS	6	1,889.87	2,016.59	6.71	1	314.61	441.33	40.28
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	23	56,043.88	63,419.24	13.16	4	6,411.04	13,786.40	115.04
29	CHHATISGARH	44	76,704.81	83,784.60	9.23	8	18,135.35	25,215.14	39.04
30	JHARKHAND	49	46,809.17	50,840.74	8.61	9	21,439.84	25,475.19	18.82
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	9	9,874.84	15,740.60	59.40
32	TELANGANA	39	31,759.07	35,867.19	12.94	13	6,071.40	10,403.63	71.35
33	MULTI STATE	170	3,45,958.11	4,60,717.93	33.17	75	1,12,142.92	2,30,071.70	105.16
Total		1420	18,05,667.72	21,63,672.09	19.83	369	4,99,749.90	8,70,645.29	74.22

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21 - 92
3	COAL	97	94,971.26	94,434.45	-0.57	35	20,501.12	20,380.18	12 - 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	2	680.64	692.29	10 - 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	13	32,529.65	34,406.05	5.77	9	26,510.85	26,298.25	2 - 49
7	PETROLEUM	138	2,24,159.63	2,24,611.19	0.20	28	87,288.24	89,385.13	1 - 74
8	POWER	105	3,07,223.51	3,72,561.25	21.27	63	2,09,517.83	2,57,352.17	2 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	4	1,316.17	1,333.59	6 - 16
11	RAILWAYS	375	4,78,359.05	7,25,343.31	51.63	94	1,05,326.39	1,87,189.36	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	574	3,86,925.98	4,01,159.04	3.68	90	75,482.85	78,261.00	1 - 118
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	2	966.39	927.36	29 - 96
14	TELECOMMUNICATIONS	10	17,191.20	28,420.00	65.32	7	14,429.97	25,758.77	2 - 58
15	URBAN DEVELOPMENT	61	1,71,744.40	1,79,453.64	4.49	25	82,159.60	84,701.33	2 - 77
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	0	0.00	0.00	-
Total		1420	18,05,667.72	21,63,672.09	19.83	366	6,93,478.12	8,49,677.29	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-7

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	67	1,06,162.46	1,10,244.37	3.85	14	46,002.17	48,800.38	2 - 168
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	2	2,635.83	6,334.96	36 - 111
3	ASSAM	47	31,336.57	40,105.00	27.98	11	14,479.62	22,268.88	8 - 140
4	BIHAR	90	75,487.50	1,12,167.59	48.59	23	39,677.58	56,243.17	6 - 123
5	GOA	10	4,292.52	4,300.54	0.19	0	0.00	0.00	-
6	GUJARAT	52	62,135.82	73,481.22	18.26	10	25,172.74	32,721.64	5 - 84
7	HARYANA	22	16,967.58	18,880.24	11.27	6	6,805.81	8,003.23	2 - 101
8	HIMACHAL PRADESH	12	14,659.32	26,087.65	77.96	4	7,041.67	12,516.88	12 - 147
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	4	14,387.53	40,381.83	12 - 220
10	KARNATAKA	46	82,148.90	87,206.53	6.16	19	46,986.26	47,837.26	3 - 285
11	KERALA	22	25,879.48	28,054.10	8.40	10	16,924.36	17,842.75	8 - 79
12	MADHYA PRADESH	62	69,052.01	78,734.42	14.02	9	18,663.95	20,708.34	5 - 96
13	MAHARASHTRA	130	1,87,818.64	1,99,946.17	6.46	35	81,313.88	87,006.68	2 - 192
14	MANIPUR	2	4,670.86	14,025.69	200.28	2	4,670.86	14,025.69	56 - 132
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	4	1,530.52	1,530.52	10 - 58
16	MIZORAM	4	3,406.61	5,613.14	64.77	1	2,393.47	4,600.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	4	3,525.63	4,199.11	36 - 81
18	ODISHA	81	91,616.58	97,021.18	5.90	26	35,793.91	40,902.93	5 - 147
19	PUNJAB	32	17,169.94	17,175.67	0.03	5	2,036.78	2,038.51	1 - 18
20	RAJASTHAN	56	44,581.43	47,282.81	6.06	17	22,006.65	22,904.21	1 - 84
21	SIKKIM	10	3,786.19	6,834.56	80.51	2	1,648.94	4,638.22	51 - 92
22	TAMIL NADU	70	1,15,478.79	1,33,318.11	15.45	21	68,808.13	72,089.70	1 - 121
23	TRIPURA	9	4,422.36	8,312.05	87.96	2	1,711.63	4,024.00	31 - 60
24	UTTAR PRADESH	109	1,27,439.00	1,31,279.91	3.01	21	36,958.95	38,111.55	2 - 236
25	WEST BENGAL	58	58,359.34	72,814.63	24.77	12	15,476.08	17,881.29	2 - 324
26	A & N ISLANDS	6	1,889.87	2,016.59	6.71	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	23	56,043.88	63,419.24	13.16	6	5,543.01	5,915.80	5 - 37
29	CHHATISGARH	44	76,704.81	83,784.60	9.23	10	30,222.51	32,158.07	14 - 117
30	JHARKHAND	49	46,809.17	50,840.74	8.61	17	22,917.64	24,286.01	11 - 154
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	5	7,719.83	13,097.50	63 - 102
32	TELANGANA	39	31,759.07	35,867.19	12.94	15	18,452.17	19,234.54	3 - 144
33	MULTI STATE	170	3,45,958.11	4,60,717.93	33.17	47	85,569.32	1,21,090.00	2 - 285
Total		1420	18,05,667.72	21,63,672.09	19.83	366	6,93,478.12	8,49,677.29	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	4	74,426.00	74,849.00	36 - 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21 - 92
3	COAL	97	94,039.87	94,434.45	0.42	33	19,051.17	19,172.45	0 - 132
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	-
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	13	32,529.65	34,406.05	5.77	8	10,985.85	10,773.25	2 - 29
7	PETROLEUM	138	2,26,915.41	2,24,611.19	-1.02	11	15,073.00	15,138.69	1 - 57
8	POWER	105	3,39,329.16	3,72,561.25	9.79	42	1,10,038.28	1,21,086.44	2 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	4	1,316.17	1,333.59	6 - 16
11	RAILWAYS	375	5,71,070.81	7,25,343.31	27.01	81	92,395.40	1,40,818.25	0 - 285
12	ROAD TRANSPORT AND HIGHWAYS	574	3,87,566.77	4,01,159.04	3.51	90	75,675.71	78,261.00	1 - 118
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	2	624.39	927.36	29 - 96
14	TELECOMMUNICATIONS	10	17,190.00	28,420.00	65.33	1	13,334.00	24,664.00	58 - 58
15	URBAN DEVELOPMENT	61	1,72,216.10	1,79,453.64	4.20	21	72,832.69	75,283.69	2 - 77
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	0	0.00	0.00	-
Total		1420	19,40,410.32	21,63,672.09	11.51	300	4,87,930.73	5,64,856.58	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	7.45
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	97	94,039.87	94,434.45	0.42	5	18,475.22	19,005.69	2.87
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0.00
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	13	32,529.65	34,406.05	5.77	2	1,161.00	3,395.40	192.45
7	PETROLEUM	138	2,26,915.41	2,24,611.19	-1.02	7	6,531.66	7,870.53	20.50
8	POWER	105	3,39,329.16	3,72,561.25	9.79	21	1,25,010.01	1,63,868.10	31.08
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	3	987.47	1,036.38	4.95
11	RAILWAYS	375	5,71,070.81	7,25,343.31	27.01	210	1,48,568.73	3,13,102.63	110.75
12	ROAD TRANSPORT AND HIGHWAYS	574	3,87,566.77	4,01,159.04	3.51	36	26,689.82	41,226.74	54.47
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	3	774.39	1,545.44	99.57
14	TELECOMMUNICATIONS	10	17,190.00	28,420.00	65.33	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	61	1,72,216.10	1,79,453.64	4.20	10	33,380.23	40,626.66	21.71
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	2	454.00	461.66	1.69
Total		1420	19,40,410.32	21,63,672.09	11.51	304	3,83,385.60	6,27,725.39	63.73

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-10

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	102- 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21- 92
3	COAL	97	94,039.87	94,434.45	0.42	2	581.73	838.90	72- 132
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0- 0
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	13	32,529.65	34,406.05	5.77	1	343.00	488.40	29- 29
7	PETROLEUM	138	2,26,915.41	2,24,611.19	-1.02	2	959.62	1,153.09	17- 24
8	POWER	105	3,39,329.16	3,72,561.25	9.79	10	37,587.79	54,261.95	12- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	1	505.58	523.00	6- 6
11	RAILWAYS	375	5,71,070.81	7,25,343.31	27.01	46	47,987.31	93,426.67	1- 285
12	ROAD TRANSPORT AND HIGHWAYS	574	3,87,566.77	4,01,159.04	3.51	13	12,047.07	14,633.38	1- 91
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	10	17,190.00	28,420.00	65.33	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	61	1,72,216.10	1,79,453.64	4.20	5	13,030.93	15,490.82	5- 51
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	0	0.00	0.00	0- 0
Total		1420	19,40,410.32	21,63,672.09	11.51	85	1,33,044.49	2,13,244.53	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-11

Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21- 92
3	COAL	97	94,971.26	94,434.45	-0.57	4	983.19	1,747.25	60- 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	29- 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	13	32,529.65	34,406.05	5.77	1	343.00	488.40	29- 29
7	PETROLEUM	138	2,24,159.63	2,24,611.19	0.20	9	13,085.77	16,272.79	4- 70
8	POWER	105	3,07,223.51	3,72,561.25	21.27	36	1,38,904.26	1,86,738.60	8- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,660.03	0.57	1	505.58	523.00	6- 6
11	RAILWAYS	375	4,78,359.05	7,25,343.31	51.63	59	60,309.92	1,42,758.34	1- 324
12	ROAD TRANSPORT AND HIGHWAYS	574	3,86,925.98	4,01,159.04	3.68	14	12,008.91	14,788.38	1- 91
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	10	17,191.20	28,420.00	65.32	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	61	1,71,744.40	1,79,453.64	4.49	5	12,935.37	15,485.99	5- 70
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	0	0.00	0.00	0- 0
Total		1420	18,05,667.72	21,63,672.09	19.83	136	2,68,549.25	4,28,020.51	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	67	1,06,162.46	1,10,244.37	3.85	6	3,561.49	6,930.66	2 - 168
2	ARUNACHAL PRADESH	31	16,421.02	33,547.53	104.30	2	2,635.83	6,334.96	36 - 111
3	ASSAM	47	31,336.57	40,105.00	27.98	5	8,507.51	16,383.35	12 - 140
4	BIHAR	90	75,487.50	1,12,167.59	48.59	12	31,878.47	48,444.06	12 - 123
5	GOA	10	4,292.52	4,300.54	0.19	0	0.00	0.00	-
6	GUJARAT	52	62,135.82	73,481.22	18.26	4	22,870.90	30,547.58	19 - 84
7	HARYANA	22	16,967.58	18,880.24	11.27	1	1,108.00	2,288.00	91 - 91
8	HIMACHAL PRADESH	12	14,659.32	26,087.65	77.96	1	3,919.59	9,394.80	147 - 147
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	12 - 220
10	KARNATAKA	46	82,148.90	87,206.53	6.16	3	2,469.52	3,500.52	3 - 36
11	KERALA	22	25,879.48	28,054.10	8.40	4	5,718.26	6,660.69	9 - 17
12	MADHYA PRADESH	62	69,052.01	78,734.42	14.02	3	13,370.09	15,414.48	21 - 96
13	MAHARASHTRA	130	1,87,818.64	1,99,946.17	6.46	12	17,125.99	23,215.82	2 - 192
14	MANIPUR	2	4,670.86	14,025.69	200.28	1	4,454.17	13,809.00	132 - 132
15	MEGHALAYA	7	4,484.97	9,578.51	113.57	0	0.00	0.00	-
16	MIZORAM	4	3,406.61	5,613.14	64.77	1	2,393.47	4,600.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	81 - 81
18	ODISHA	81	91,616.58	97,021.18	5.90	10	21,681.75	26,791.07	10 - 147
19	PUNJAB	32	17,169.94	17,175.67	0.03	1	754.54	756.27	1 - 1
20	RAJASTHAN	56	44,581.43	47,282.81	6.06	3	1,771.90	2,678.35	1 - 60
21	SIKKIM	10	3,786.19	6,834.56	80.51	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	70	1,15,478.79	1,33,318.11	15.45	5	8,039.88	12,412.66	24 - 121
23	TRIPURA	9	4,422.36	8,312.05	87.96	2	1,711.63	4,024.00	31 - 60
24	UTTAR PRADESH	109	1,27,439.00	1,31,279.91	3.01	4	1,944.47	3,292.83	12 - 236
25	WEST BENGAL	58	58,359.34	72,814.63	24.77	4	7,575.12	9,980.34	12 - 324
26	A & N ISLANDS	6	1,889.87	2,016.59	6.71	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	23	56,043.88	63,419.24	13.16	1	1,219.21	1,592.00	5 - 5
29	CHHATISGARH	44	76,704.81	83,784.60	9.23	4	13,013.75	14,949.31	24 - 117
30	JHARKHAND	49	46,809.17	50,840.74	8.61	4	15,086.49	16,454.86	20 - 154
31	UTTARAKHAND	28	33,689.40	39,554.65	17.41	4	7,241.32	12,619.50	63 - 102
32	TELANGANA	39	31,759.07	35,867.19	12.94	5	2,730.04	3,648.31	33 - 144
33	MULTI STATE	170	3,45,958.11	4,60,717.93	33.17	27	56,681.80	92,411.83	4 - 285
Total		1420	18,05,667.72	21,63,672.09	19.83	134	2,67,734.21	4,26,943.98	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	174	15
2	ROAD TRANSPORT AND HIGHWAYS	127	3
3	POWER	56	8
4	PETROLEUM	51	3
5	COAL	14	0
6	URBAN DEVELOPMENT	14	0
7	STEEL	8	1
8	ATOMIC ENERGY	4	0
9	HEAVY INDUSTRY	2	0
10	TELECOMMUNICATIONS	2	0
11	MINES	1	0
12	SHIPPING AND PORTS	1	0
	Total	454	30

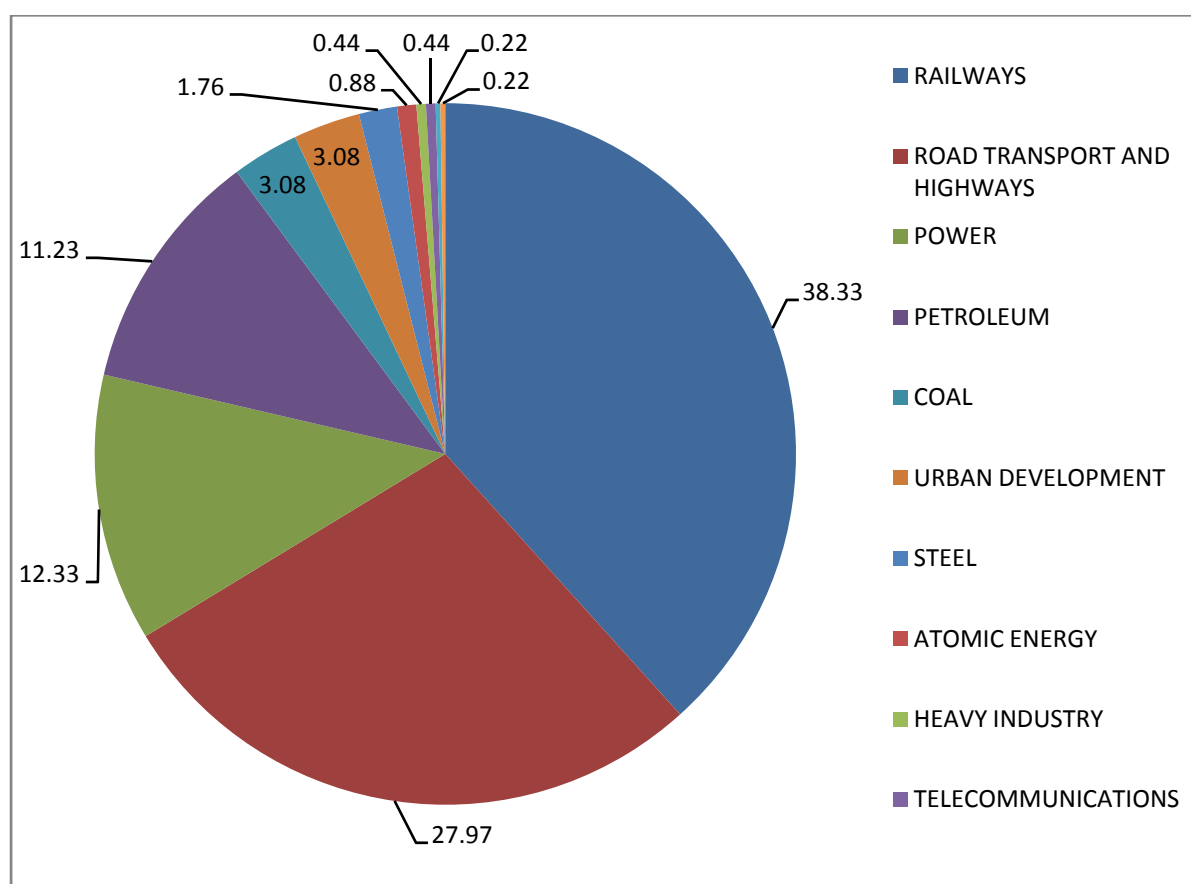


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	422
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	13
No of Projects in Current Month	454

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	163 (35.90%)	4 (.88%)	135(29.74%)	21 (4.63%)	131(8.85%)	454
Latest Approved (Date)	126 (27.75%)	7 (1.54%)	171(37.67%)	19 (4.19%)	131(8.85%)	454

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	368	11,65,627.67	13,49,949.60	4,50,928.23	33.40	1,84,321.93	15.80
Project with Revision in Cost	86	3,76,086.46	3,91,903.27	2,02,232.86	51.60	15,816.81	4.20
Total	454	15,41,714.13	17,41,852.87	6,53,161.09	37.50	2,00,138.74	12.98
Original Cost of All Projects							
Original Cost	454	14,09,148.54	17,41,852.87	6,53,161.09	37.50	3,32,704.33	23.61

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	163	6,03,371.87	7,53,183.86	3,80,214.25	50.50	1,49,811.99	24.80
Latest Approved (RCE)	126	4,09,146.55	4,82,328.66	2,21,498.37	45.90	73,182.11	17.90

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	34	75,721.82	1,06,966.87	60,082.90	56.20	31,245.05	41.30
Total	34	75,721.82	1,06,966.87	60,082.90	56.17	31,245.05	41.26

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs._1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	COAL	14	60,321.08	60,321.88	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	8	30,948.34	32,679.34	5.59	1	818.00	2,907.00	255.38
5	PETROLEUM	51	1,86,910.53	1,88,543.07	0.87	8	16,553.75	21,148.95	27.76
6	POWER	56	2,88,605.36	3,52,792.27	22.24	32	1,73,171.13	2,37,358.04	37.07
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	174	4,01,588.19	6,25,006.02	55.63	112	1,49,297.35	3,75,476.91	151.50
9	ROAD TRANSPORT AND HIGHWAYS	127	1,88,545.45	2,01,847.92	7.06	17	20,393.80	33,696.27	65.23
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	14	1,58,425.02	1,65,789.50	4.65	5	31,625.09	38,989.57	23.29
Total		454	14,09,148.54	17,41,852.87	23.61	180	4,39,099.12	7,77,985.84	77.18

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	90,958.16	94,896.23	4.33	6	7,059.25	11,355.32	60.86
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	2	8,782.23	25,676.30	192.37
3	ASSAM	9	18,394.76	26,148.26	42.15	4	8,861.92	16,702.00	88.47
4	BIHAR	26	47,239.16	80,380.11	70.16	18	34,984.91	68,125.86	94.73
5	GUJARAT	16	44,522.71	56,396.97	26.67	5	25,960.46	37,834.72	45.74
6	HARYANA	5	9,406.39	10,586.39	12.54	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	23,654.41	93.48	2	4,966.47	16,394.80	230.11
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	606.15
9	KARNATAKA	20	68,819.94	73,410.38	6.67	6	18,932.46	23,702.90	25.20
10	KERALA	8	19,741.86	21,625.11	9.54	2	6,154.29	8,061.58	30.99
11	MADHYA PRADESH	20	46,362.91	56,801.77	22.52	10	29,775.74	40,214.60	35.06
12	MAHARASHTRA	43	1,52,130.85	1,62,823.31	7.03	16	32,457.05	45,426.72	39.96
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	210.02
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	4,600.00	92.19	1	2,393.47	4,600.00	92.19
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	26	67,212.17	71,624.13	6.56	6	19,852.05	24,264.01	22.22
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	12	24,386.29	25,742.23	5.56	4	3,178.64	4,534.58	42.66
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	25	96,395.00	1,11,652.94	15.83	11	25,501.52	40,759.46	59.83
22	TRIPURA	3	2,458.01	6,185.51	151.65	3	2,458.01	6,185.51	151.65
23	UTTAR PRADESH	40	94,778.46	98,178.18	3.59	7	23,115.64	27,138.30	17.40
24	WEST BENGAL	25	46,130.66	57,457.63	24.55	10	14,953.83	26,280.81	75.75
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	7	50,481.91	57,816.75	14.53	3	6,254.39	13,589.23	117.28
27	CHHATISGARH	15	65,114.98	71,716.25	10.14	6	17,599.38	24,200.65	37.51
28	JHARKHAND	11	33,289.32	36,388.70	9.31	3	19,637.61	22,736.99	15.78
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	4	8,654.06	14,154.57	63.56
30	TELANGANA	7	20,115.45	23,093.25	14.80	3	2,503.03	5,480.84	118.97
31	MULTI STATE	78	3,10,268.10	4,18,340.29	34.83	41	1,00,639.67	2,11,101.69	109.76
Total		454	14,09,148.54	17,41,852.87	23.61	180	4,39,099.12	7,77,985.84	77.18

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 102
2	COAL	14	60,321.08	60,321.88	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	8	30,948.34	32,679.34	5.59	6	25,381.34	25,023.34	4 - 49
5	PETROLEUM	51	1,86,910.53	1,88,543.07	0.87	16	81,919.38	83,622.54	2 - 74
6	POWER	56	2,88,605.36	3,52,792.27	22.24	39	2,00,866.70	2,47,550.38	3 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
8	RAILWAYS	174	4,01,588.19	6,25,006.02	55.63	56	86,596.60	1,64,349.86	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	127	1,88,545.45	2,01,847.92	7.06	30	41,881.00	44,465.10	2 - 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	14	1,58,425.02	1,65,789.50	4.65	6	75,395.14	77,781.93	5 - 64
Total		454	14,09,148.54	17,41,852.87	23.61	163	6,03,371.87	7,53,183.86	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	94,896.23	4.33	8	43,646.40	46,511.67	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	9	18,394.76	26,148.26	42.15	5	12,688.04	20,112.89	9 - 140
4	BIHAR	26	47,239.16	80,380.11	70.16	10	32,659.99	48,769.28	12 - 123
5	GUJARAT	16	44,522.71	56,396.97	26.67	2	22,232.00	29,367.00	19 - 54
6	HARYANA	5	9,406.39	10,586.39	12.54	2	4,637.00	5,817.00	2 - 91
7	HIMACHAL PRADESH	6	12,226.08	23,654.41	93.48	2	5,836.38	11,311.59	29 - 147
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	4	14,387.53	40,381.83	12 - 220
9	KARNATAKA	20	68,819.94	73,410.38	6.67	10	40,770.46	41,376.72	3 - 285
10	KERALA	8	19,741.86	21,625.11	9.54	4	14,207.19	14,840.82	8 - 33
11	MADHYA PRADESH	20	46,362.91	56,801.77	22.52	6	17,896.92	19,941.31	5 - 96
12	MAHARASHTRA	43	1,52,130.85	1,62,823.31	7.03	19	73,748.66	78,867.66	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	132 - 132
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,600.00	92.19	1	2,393.47	4,600.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	81 - 81
17	ODISHA	26	67,212.17	71,624.13	6.56	9	27,216.90	31,496.93	10 - 147
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	12	24,386.29	25,742.23	5.56	4	15,476.63	16,325.70	48 - 84
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	25	96,395.00	1,11,652.94	15.83	9	61,668.64	65,793.87	18 - 121
22	TRIPURA	3	2,458.01	6,185.51	151.65	1	1,142.00	3,374.00	60 - 60
23	UTTAR PRADESH	40	94,778.46	98,178.18	3.59	12	33,584.74	34,783.58	2 - 236
24	WEST BENGAL	25	46,130.66	57,457.63	24.55	7	13,711.20	15,799.73	11 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	7	50,481.91	57,816.75	14.53	3	4,167.73	4,540.52	5 - 37
27	CHHATISGARH	15	65,114.98	71,716.25	10.14	3	28,002.78	29,459.82	24 - 111
28	JHARKHAND	11	33,289.32	36,388.70	9.31	5	18,910.93	19,708.40	11 - 48
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	3	7,127.06	12,353.50	63 - 102
30	TELANGANA	7	20,115.45	23,093.25	14.80	4	14,450.02	14,727.41	3 - 144
31	MULTI STATE	78	3,10,268.10	4,18,340.29	34.83	25	76,106.05	1,10,006.67	3 - 285
Total		454	14,09,148.54	17,41,852.87	23.61	163	6,03,371.87	7,53,183.86	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	4	74,426.00	74,849.00	36 - 102
2	COAL	14	60,321.08	60,321.88	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	8	30,948.34	32,679.34	5.59	5	9,856.34	9,498.34	4 - 21
5	PETROLEUM	51	1,89,756.77	1,88,543.07	-0.64	4	12,021.65	12,021.65	2 - 57
6	POWER	56	3,19,726.11	3,52,792.27	10.34	24	1,04,270.65	1,15,153.05	3 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
8	RAILWAYS	174	4,92,578.70	6,25,006.02	26.88	48	75,764.06	1,21,697.88	0 - 285
9	ROAD TRANSPORT AND HIGHWAYS	127	1,88,545.45	2,01,847.92	7.06	30	41,881.00	44,465.10	2 - 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	14	1,58,727.11	1,65,789.50	4.45	5	66,715.14	69,101.93	5 - 64
Total		454	15,41,714.13	17,41,852.87	12.98	126	4,09,146.55	4,82,328.66	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule RS. 1000 Crore and above
(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	7.45
2	COAL	14	60,321.08	60,321.88	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	8	30,948.34	32,679.34	5.59	1	818.00	2,907.00	255.38
5	PETROLEUM	51	1,89,756.77	1,88,543.07	-0.64	3	5,055.04	6,140.19	21.47
6	POWER	56	3,19,726.11	3,52,792.27	10.34	19	1,23,783.20	1,62,475.36	31.26
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	174	4,92,578.70	6,25,006.02	26.88	102	1,12,874.73	2,53,671.32	124.74
9	ROAD TRANSPORT AND HIGHWAYS	127	1,88,545.45	2,01,847.92	7.06	17	20,393.80	33,696.27	65.23
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	14	1,58,727.11	1,65,789.50	4.45	5	31,927.18	38,989.57	22.12
Total		454	15,41,714.13	17,41,852.87	12.98	151	3,32,817.95	5,49,708.81	65.17

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	102- 102
2	COAL	14	60,321.08	60,321.88	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	8	30,948.34	32,679.34	5.59	0	0.00	0.00	0- 0
5	PETROLEUM	51	1,89,756.77	1,88,543.07	-0.64	0	0.00	0.00	0- 0
6	POWER	56	3,19,726.11	3,52,792.27	10.34	9	37,151.11	53,659.51	12- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	174	4,92,578.70	6,25,006.02	26.88	26	39,139.09	81,570.00	12- 285
9	ROAD TRANSPORT AND HIGHWAYS	127	1,88,545.45	2,01,847.92	7.06	10	10,592.53	13,176.63	2- 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	14	1,58,727.11	1,65,789.50	4.45	2	11,992.21	14,379.00	5- 19
Total		454	15,41,714.13	17,41,852.87	12.98	49	1,17,885.94	1,93,549.14	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 102
2	COAL	14	60,321.08	60,321.88	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	8	30,948.34	32,679.34	5.59	0	0.00	0.00	0- 0
5	PETROLEUM	51	1,86,910.53	1,88,543.07	0.87	5	11,613.40	14,065.95	4- 70
6	POWER	56	2,88,605.36	3,52,792.27	22.24	26	1,35,663.13	1,82,346.81	10- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	174	4,01,588.19	6,25,006.02	55.63	34	48,857.90	1,27,000.85	12- 324
9	ROAD TRANSPORT AND HIGHWAYS	127	1,88,545.45	2,01,847.92	7.06	10	10,592.53	13,176.63	2- 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	14	1,58,425.02	1,65,789.50	4.65	2	11,992.21	14,379.00	5- 19
Total		454	14,09,148.54	17,41,852.87	23.61	80	2,47,004.17	3,98,313.24	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	94,896.23	4.33	4	2,983.99	6,207.26	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	9	18,394.76	26,148.26	42.15	3	7,990.57	15,502.00	12 - 140
4	BIHAR	26	47,239.16	80,380.11	70.16	8	29,968.32	46,077.61	12 - 123
5	GUJARAT	16	44,522.71	56,396.97	26.67	2	22,232.00	29,367.00	19 - 54
6	HARYANA	5	9,406.39	10,586.39	12.54	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	12,226.08	23,654.41	93.48	1	3,919.59	9,394.80	147 - 147
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	12 - 220
9	KARNATAKA	20	68,819.94	73,410.38	6.67	2	1,824.74	2,611.00	3 - 3
10	KERALA	8	19,741.86	21,625.11	9.54	1	4,588.29	5,245.96	9 - 9
11	MADHYA PRADESH	20	46,362.91	56,801.77	22.52	3	13,370.09	15,414.48	21 - 96
12	MAHARASHTRA	43	1,52,130.85	1,62,823.31	7.03	9	16,084.12	21,598.44	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	132 - 132
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,600.00	92.19	1	2,393.47	4,600.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	81 - 81
17	ODISHA	26	67,212.17	71,624.13	6.56	5	18,563.98	22,844.01	10 - 147
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	12	24,386.29	25,742.23	5.56	2	1,482.93	2,332.00	60 - 60
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	25	96,395.00	1,11,652.94	15.83	3	7,211.42	11,336.65	49 - 121
22	TRIPURA	3	2,458.01	6,185.51	151.65	1	1,142.00	3,374.00	60 - 60
23	UTTAR PRADESH	40	94,778.46	98,178.18	3.59	1	609.04	1,807.88	236 - 236
24	WEST BENGAL	25	46,130.66	57,457.63	24.55	3	7,277.80	9,366.34	108 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	7	50,481.91	57,816.75	14.53	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	15	65,114.98	71,716.25	10.14	2	12,477.78	13,934.82	24 - 111
28	JHARKHAND	11	33,289.32	36,388.70	9.31	1	14,366.58	15,164.05	20 - 20
29	UTTARAKHAND	6	26,313.06	31,813.57	20.90	3	7,127.06	12,353.50	63 - 102
30	TELANGANA	7	20,115.45	23,093.25	14.80	1	1,266.60	1,544.00	33 - 33
31	MULTI STATE	78	3,10,268.10	4,18,340.29	34.83	16	52,891.11	87,001.08	4 - 285
Total		454	14,09,148.54	17,41,852.87	23.61	80	2,47,004.17	3,98,313.24	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	05/2015	257.87	11/2016	257.87	09/2018	243.30
2	NAWAGAM-KOYALI PIPELINE PROJECT Central Sector Projects	11/2014	195.63	09/2018	187.10	09/2018	174.68
3	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY	05/2015	337.06	08/2018	337.06	09/2018	167.16
	<u>POWER</u>						
4	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	08/2014	288.49	02/2017	376.09	09/2018	276.10
5	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I	04/2016	810.48	12/2018	810.48	09/2018	528.50
6	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	03/2013	514.20	06/2015	703.10	09/2018	605.50
7	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) Central Sector Projects	04/2015	2,525.00	11/2017	2,525.00	09/2018	2,015.38
8	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B Central Sector Projects	04/2015	2,225.00	01/2018	2,225.00	09/2018	1,655.02
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
9	DEOLI KOTA PPP (BOT)	01/2011	593.00	07/2013	593.00	09/2018	1,073.73
10	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N	08/2015	538.08	02/2018	538.08	09/2018	335.24
11	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50)	07/2015	455.60	07/2017	455.60	09/2018	202.68
12	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2)	10/2015	562.34	04/2018	562.34	09/2018	109.07
13	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V)	09/2015	664.53	03/2018	664.53	09/2018	702.97
14	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	02/2013	1,232.00	08/2015	1,232.00	09/2018	1,091.17
15	UP/HARYANA BORDER - YAMUNA NAGAR	05/2015	600.85	05/2018	600.85	09/2018	109.84

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	-SAHA- BARWALA - PANCHKULA (PKG - 1)						
16	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I PPP (BOT)	01/2016	830.36	07/2018	830.36	09/2018	326.23
17	FOUR LANING OF KAITHAL - RAJASTHAN BORDER PPP (BOT)	07/2015	1,393.00	N.A.	1,393.00	09/2018	1,917.40
18	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21	12/2015	239.23	12/2017	239.23	09/2018	123.47
19	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV)	09/2015	789.31	03/2018	789.31	09/2018	867.54
20	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI)	09/2015	768.56	03/2018	768.56	09/2018	774.99
21	JODHPUR - BARMER SECTION OF PACKAGE -I	10/2014	264.72	04/2017	264.72	09/2018	98.18
22	JAISALMER - BARMER	08/2015	482.27	02/2018	482.27	09/2018	308.83
23	2-LANNING WITH PS KHAGARIA-PURNEA PPP (ANNUITY)	05/2011	664.00	02/2014	664.00	09/2018	654.59
24	2-LANING WITH PS BHILWARA-LODPURA SECTION	03/2014	240.10	03/2016	240.10	09/2018	194.69
25	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	275.00	02/2010	281.31	09/2018	252.25

TABLE-26

List of projects added Rs. 150 Crore and above					(September 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	RANIGANJ MASTER PLAN	8/2009	2,661.73	8/2019	2,661.73	8/2019
2	MAHAMAYA OPENCAST PROJECT	5/2018	410.26	3/2026	410.26	3/2026
3	SIDULI MINE (OC AND UG)	5/2018	535.18	3/2026	535.18	3/2026
	<u>RAILWAYS</u>					
4	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	602.50	/	714.34	3/2022
5	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	600.00	1/2022	600.00	1/2022
6	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	1,177.96	3/2014	1,177.96	12/2019
7	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	4/2016	744.04	3/2021	1,215.54	3/2022
8	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	4/2016	731.64	3/2021	1,185.73	3/2022
9	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	11/2001	624.47	2/2016	3,550.00	3/2021
10	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	180.82	/	528.26	12/2018
11	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF,	4/1991	329.39	/	566.41	12/2021
12	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	229.00	12/2021	403.00	12/2021
13	CHHINDWARA-MANDLA FORT GC	3/2011	556.54	3/2012	1,342.46	3/2020
14	KENDRI-DHMTARI INCLUDING ABHANPUR-RAJIM	4/2011	543.00	3/2022	543.00	3/2022
15	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	872.00	12/2019	1,279.00	12/2019
16	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	1,973.00	3/2021	1,973.00	3/2021
17	ANUPPUR-KATNI	4/2015	1,370.00	12/2021	1,370.00	12/2021
18	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	644.78	3/2017	889.52	3/2020
19	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	551.51	3/2019	551.51	3/2019
20	GEVRA ROAD PENDRA ROAD	2/2014	2,288.00	3/2022	4,919.00	3/2022
21	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	3,055.00	9/2018	3,055.00	9/2018
22	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24.	4/1998	1,027.40	3/2022	2,373.00	3/2022

List of projects added Rs. 150 Crore and above					(September 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
23	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	625.00	3/2016	845.58	3/2016
	<u>URBAN DEVELOPMENT</u>					
24	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10,773.00	12/2018	12,787.00	7/2020

TABLE-27

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	4537
Achieved up to month	2247

TABLE-28

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(September 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>STEEL</u>						
1	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	15,525.00	05/2015	03/2019	06/2019	3
	<u>PETROLEUM</u>						
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,577.15	05/2013	12/2018	03/2019	3
3	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU IOCL	466.43	466.43	10/2020	10/2020	05/2021	7
4	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY BPCL	3,313.00	3,288.96	02/2020	02/2020	10/2020	8
5	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP IOCL	384.58	384.58	04/2021	04/2020	04/2021	12
6	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE IOCL	4,497.00	4,497.00	12/2018	12/2018	12/2020	24
	<u>POWER</u>						
7	EASTERN REGION STRENGTHENING SCHEME- III PGCIL	1,272.80	1,731.10	11/2012	09/2018	10/2018	1
8	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L PGCIL	1,940.13	2,702.65	09/2014	09/2018	10/2018	1
9	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL	2,514.88	3,190.27	12/2015	10/2018	11/2018	1
10	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP PGCIL	268.80	340.88	03/2018	10/2018	11/2018	1
11	INSTALLATION OF STATCOMS IN WESTERN REGION PGCIL	1,071.24	1,071.24	09/2017	10/2018	11/2018	1
12	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B PGCIL	307.18	307.18	11/2017	10/2018	11/2018	1
13	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION PGCIL	1,455.47	1,455.47	07/2018	09/2018	10/2018	1
14	WESTERN REGION STRENGTHENING SCHEME- XVI PGCIL	150.99	150.99	07/2018	09/2018	10/2018	1


<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (September 2018)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
15	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V PGCIL Central Sector Projects	1,750.00	1,750.00	06/2018	10/2018	11/2018	1
16	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,932.88	12/2012	09/2018	11/2018	2
17	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	534.02	08/2014	10/2018	12/2018	2
18	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) PGCIL	287.99	287.99	06/2018	10/2018	12/2018	2
19	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) PGCIL	408.46	408.46	01/2019	01/2019	03/2019	2
20	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO PGCIL	197.40	197.40	03/2018	09/2018	12/2018	3
21	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) SJVN	330.00	330.00	11/2017	09/2018	12/2018	3
22	PARBATI HEP (4X200 MW) (NHPC) II NHPC	3,919.59	9,394.80	09/2009	12/2020	12/2021	12
	<u>RAILWAYS</u>						
23	RANI-MARWAR JN. PATCH DOUBLING NWR	288.97	346.35	11/2018	11/2018	12/2018	1
24	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) NFR	2,326.52	3,000.00	03/2015	10/2021	12/2021	2
25	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT SECR	585.93	1,420.39	02/2019	12/2018	02/2019	2
26	MANDHANA - BRAHMAWART NEW LINE PROJECT. NER	609.04	1,807.88	04/1999	10/2018	12/2018	2
27	GONDIA-JABALPUR(GC),(SECR) SECR	511.86	1,756.00	04/2020	12/2019	04/2020	4
28	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) NFR	2,232.32	2,232.00	03/2022	03/2022	12/2022	9
29	KIUL - GAYA DOUBLING PROJECT ECR	1,200.20	1,200.20	03/2020	12/2020	10/2021	10
30	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE ECR	1,491.47	1,491.47	03/2020	12/2020	10/2021	10
31	KATNI - SINGRAULI DOUBLING PROJECT WCR	1,763.93	1,763.93	03/2020	12/2020	10/2021	10

List of projects reporting additional delayed Rs. 150 Crore and above							(September 2018)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
32	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR NFR	532.87	2,145.00	03/2019	03/2020	03/2021	12
33	AMBARI FALAKATA TO NEW MAYNAGURI NFR	314.00	551.00	03/2019	03/2019	03/2020	12
34	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I SCR	2,206.29	1,996.94	03/2014	03/2023	03/2024	12
35	BHADRAK - NERGUNDI 3RD LINE ECR	810.28	843.04	10/2020	03/2021	03/2022	12
36	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) NFR	602.27	612.00	12/2021	03/2020	03/2021	12
37	SAMBALPUR - TITLAGARH - DOUBLING RVNL	948.04	970.00	03/2020	03/2020	03/2021	12
38	HAJIPUR - BACHAWARA ECR	678.54	678.54	03/2019	12/2018	03/2020	15
39	KARAILA ROAD - SHAKTINAGAR DOUBLING ECR	528.57	528.57	03/2019	12/2019	03/2021	15
40	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) SECR	1,908.51	2,686.63	03/2023	12/2021	03/2023	15
41	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR NFR	3,230.02	5,820.00	04/2008	06/2018	12/2019	18
42	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	3,040.00	12/2008	03/2019	12/2020	21
43	ROURKELA JHARSUGUDA THIRD LINE 101 KM SER	969.83	969.83	03/2020	06/2020	03/2022	21
44	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) NFR	4,454.17	13,809.00	03/2011	03/2020	03/2022	24
45	VIRAMGAM-SAMAKHIALI (DL) WR	1,037.15	1,037.15	03/2021	03/2019	03/2021	24
46	HUBLI- CHIKJAJUR SWR	1,156.94	1,156.94	03/2020	03/2020	03/2022	24
47	YELAHANKA-PENKONDA SWR	860.43	958.00	03/2020	03/2020	03/2022	24
48	KATNI GRADE SEPARATOR/BYE PASS WCR	582.13	1,260.61	03/2022	03/2020	03/2022	24
49	ROSA-SITAPUR CANTT-BURHWAL DOUBLING NER	1,295.42	1,295.42	03/2022	02/2019	03/2022	37
50	AGARTALA-AKHAURA NL NFR	569.63	650.00	03/2020	07/2019	10/2022	39
51	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP NER	243.78	871.56	12/2021	08/2018	12/2021	40
52	HATHUA-BHATNI (N L) (NER) NER	230.03	718.54	12/2022	05/2019	12/2022	43


<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (September 2018)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
53	MUNEERABAD-MAHABOBNAGAR(NL),SCR SCR	1,723.00	3,501.83	03/2000	03/2019	12/2023	57
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
54	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN NHAI	754.54	756.27	03/2020	03/2020	04/2020	1
55	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO NHAI	1,989.00	1,989.00	03/2020	03/2020	05/2020	2
56	2 LANNING OF MUZAFFARPUR - SONBARSA NHAI PPP (ANNUITY)	511.54	511.54	11/2013	09/2018	12/2018	3
57	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI NHAI	400.25	400.25	03/2019	03/2019	06/2019	3
58	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 NHAI PPP (BOT)	972.50	972.50	07/2017	08/2018	12/2018	4
59	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,423.96	11/2018	03/2019	07/2019	4
60	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM NHAI PPP (BOT)	617.00	617.00	08/2012	09/2018	03/2019	6
61	4-LANNING OF CHAPRA-HAJIPUR NHAI PPP (ANNUITY)	575.00	575.00	07/2013	12/2018	06/2019	6
62	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 NHAI	2,016.00	2,016.00	04/2019	04/2019	11/2019	7
63	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 NHAI	574.28	574.28	07/2018	07/2018	03/2019	8
64	FOUR LANING OF FORBESGANJ - JOGBANI NHAI	322.09	322.09	04/2018	04/2019	04/2020	12
	<u>TELECOMMUNICATIONS</u>						
65	GUJARAT ACCESS (LOT 1) BSNL Central Sector Projects	171.54	171.54	05/2018	09/2018	10/2018	1
	<u>URBAN DEVELOPMENT</u>						
66	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA CPWD	156.57	156.57	08/2016	11/2018	01/2019	2
67	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND CPWD	270.83	270.83	11/2014	12/2018	02/2019	2
68	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN CPWD	549.31	540.42	07/2019	07/2019	09/2019	2

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (September 2018)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
69	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN CPWD	884.30	884.30	12/2015	07/2018	12/2018	5
70	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI CPWD	197.33	197.33	04/2019	04/2019	06/2020	14

Graphical Presentation of All Projects w.r.t. Original Schedule

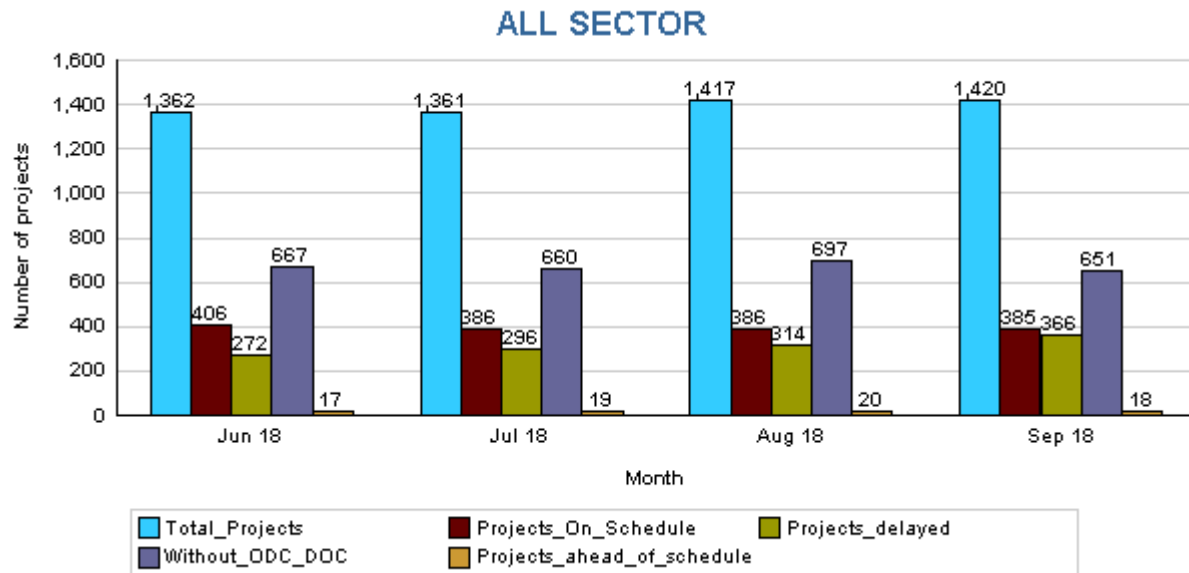


Break-up of 366 Delayed projects in September 2018

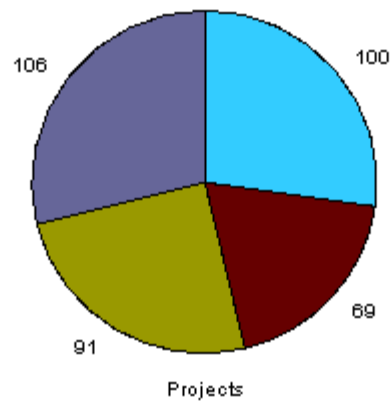


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

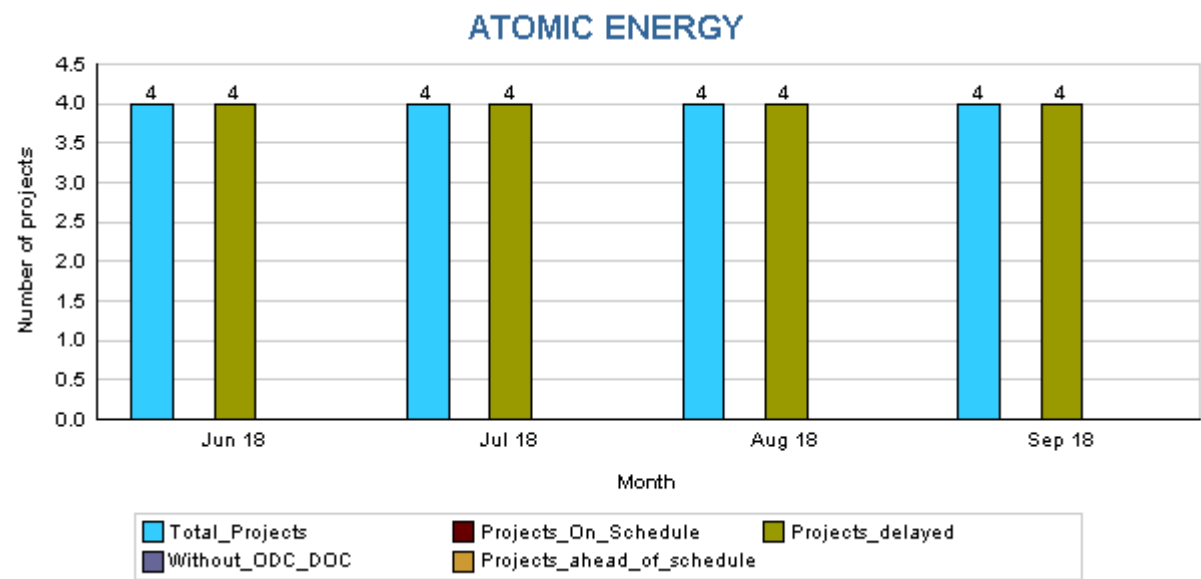


Break-up of 4 Delayed projects in September 2018

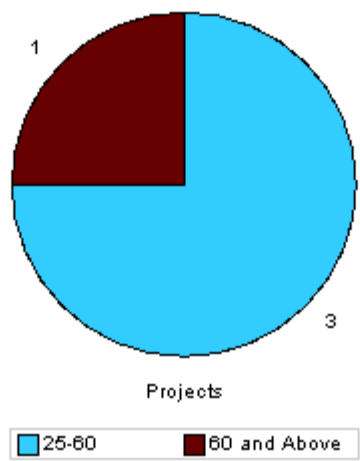


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

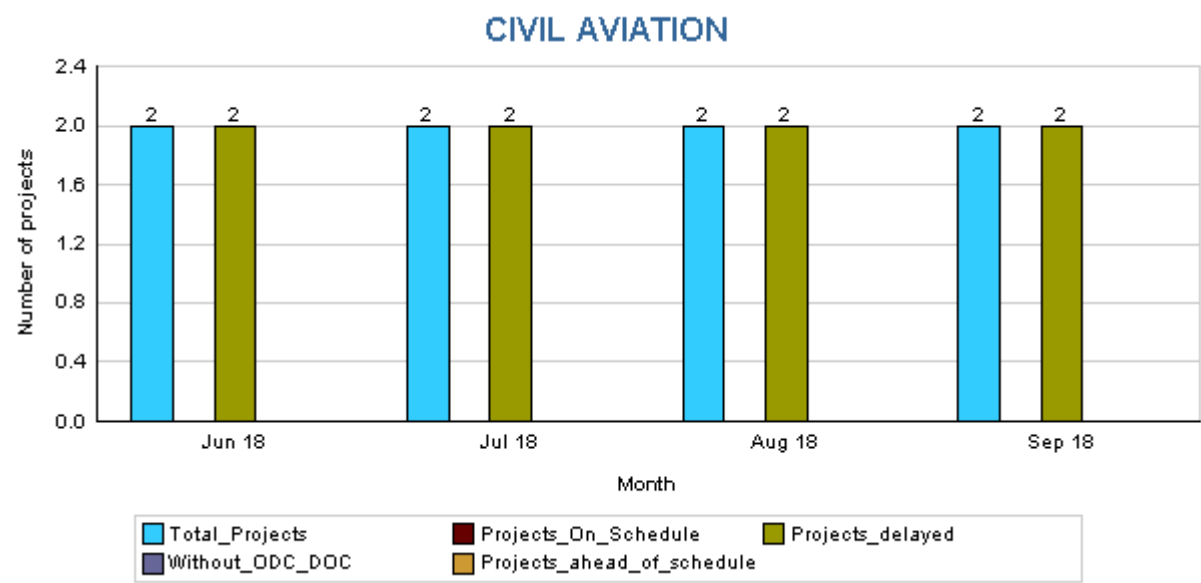


Break-up of 2 Delayed projects in September 2018

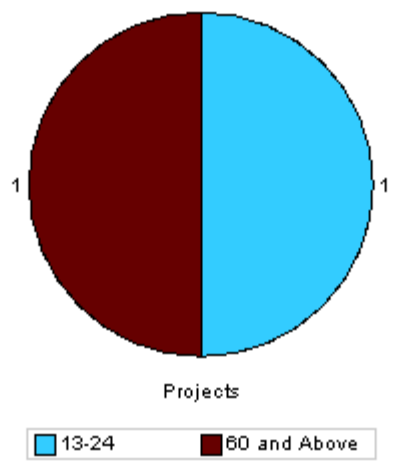


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

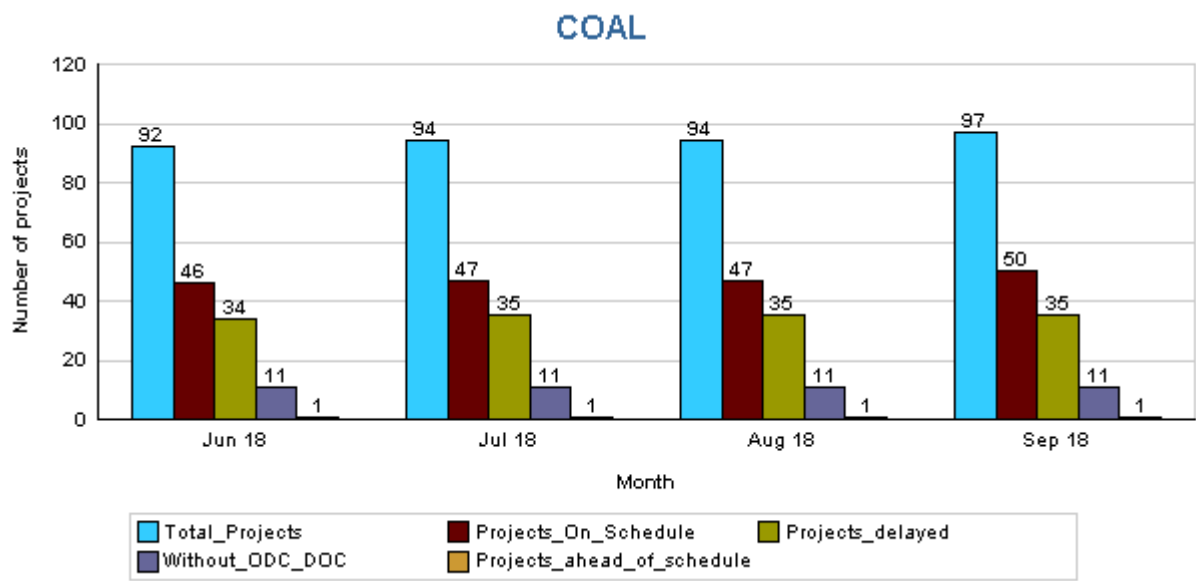


Break-up of 35 Delayed projects in September 2018

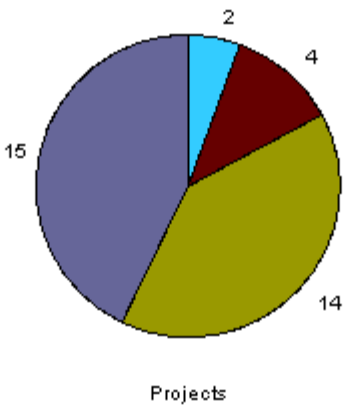


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

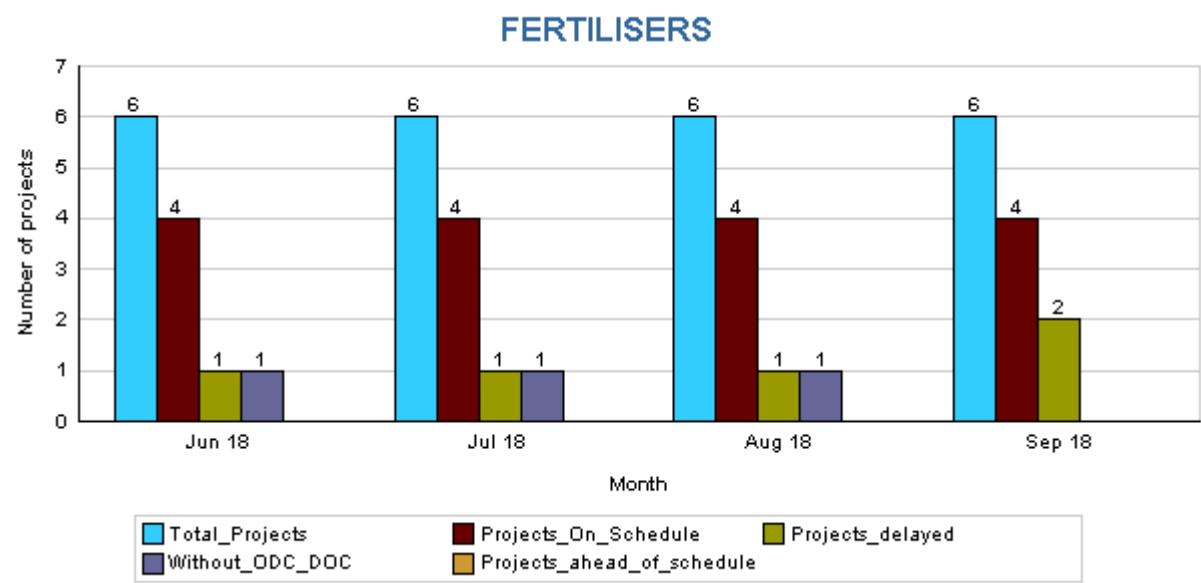


Break-up of 2 Delayed projects in September 2018

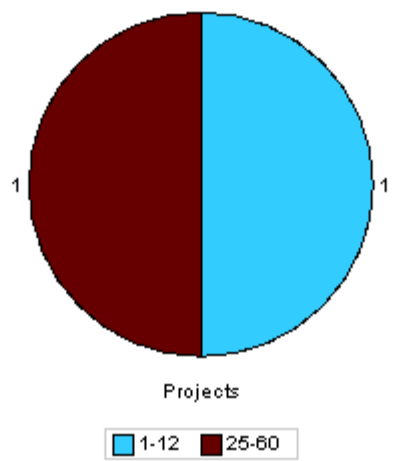


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

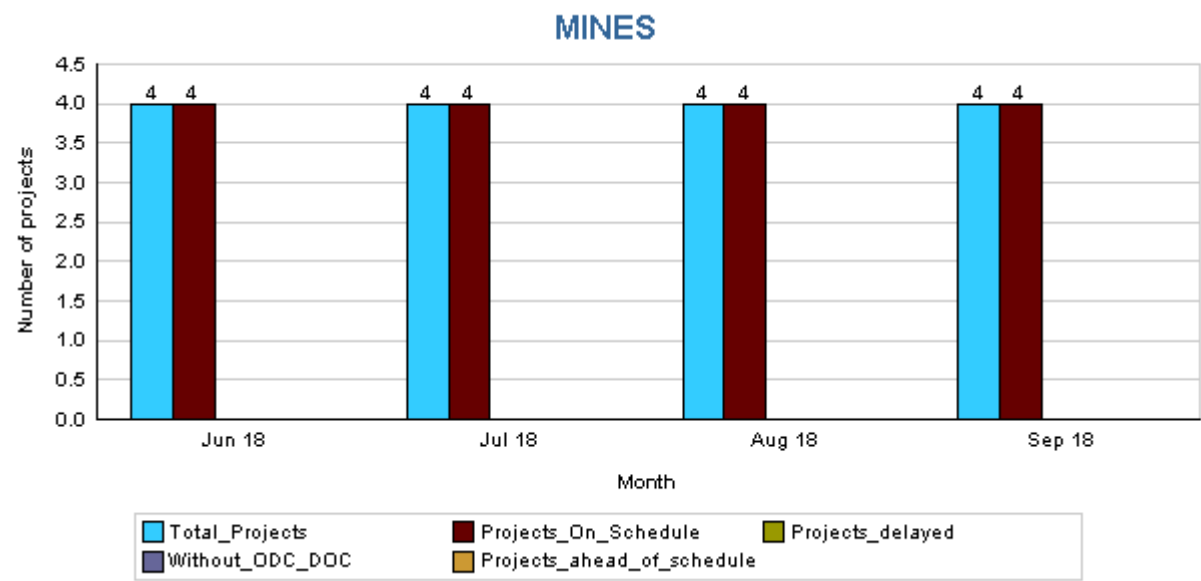


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

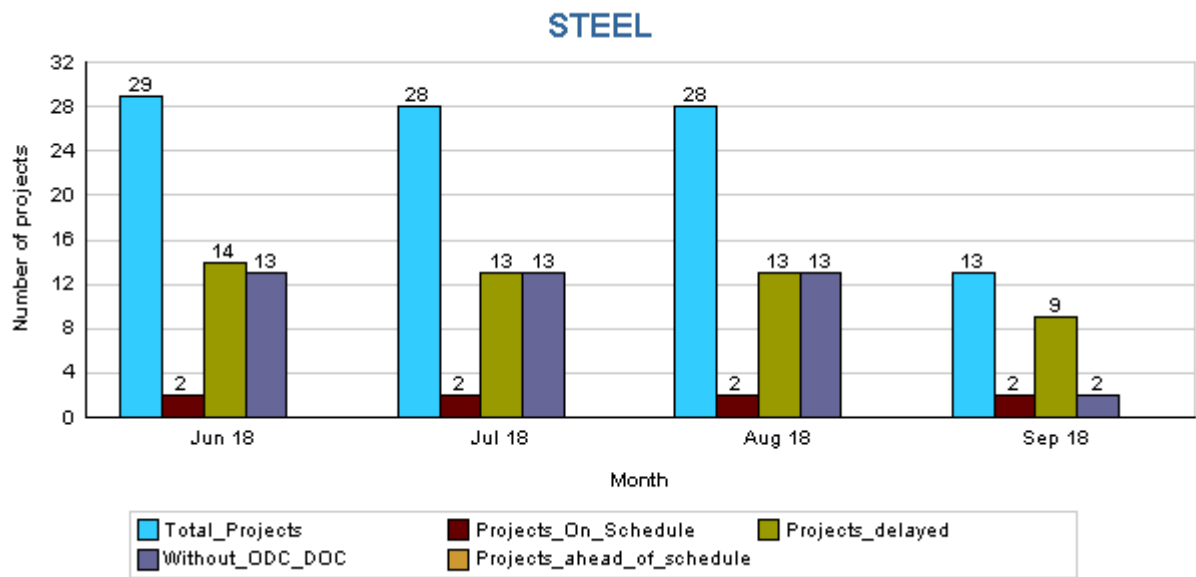


Break-up of 9 Delayed projects in September 2018

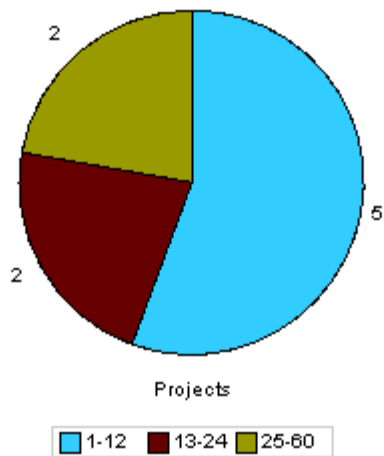


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

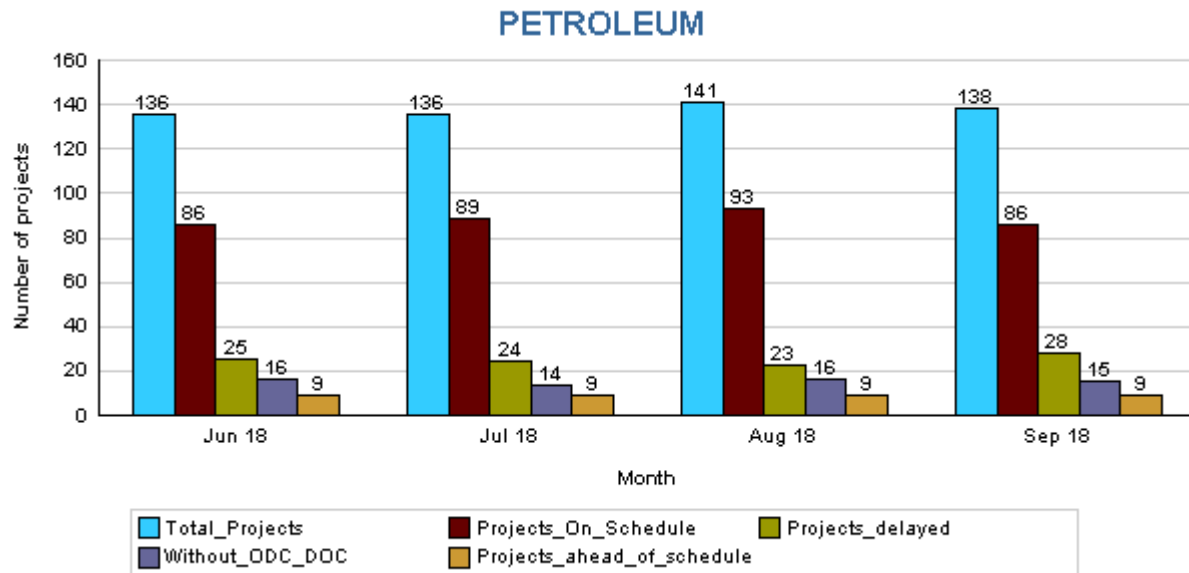


Break-up of 28 Delayed projects in September 2018

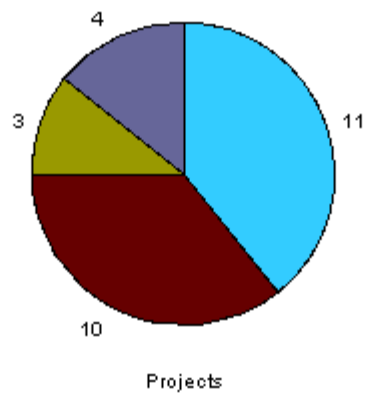


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

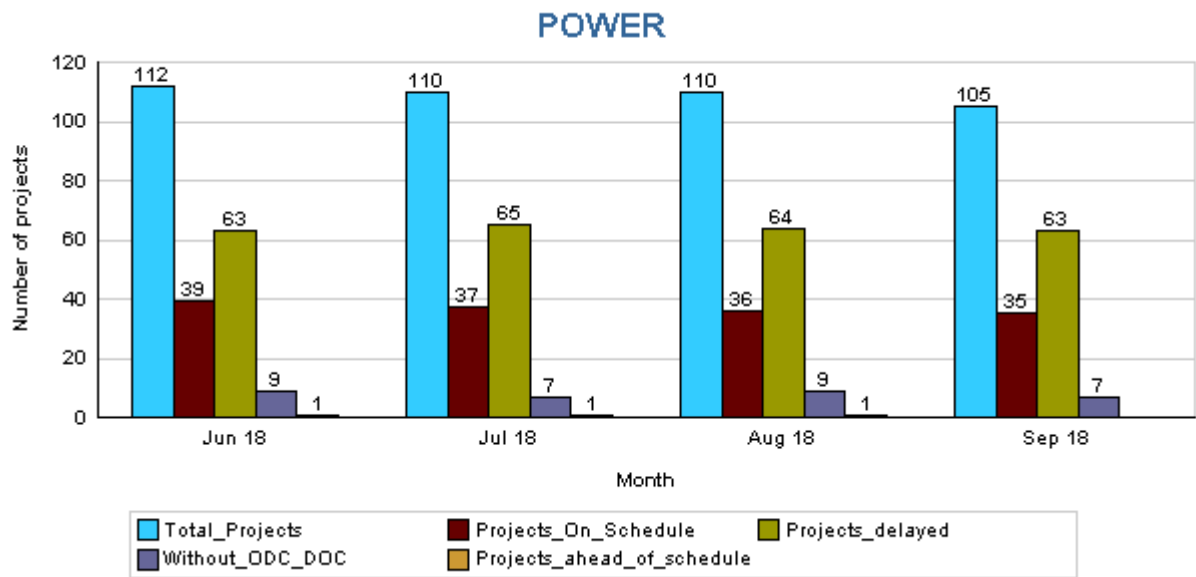


Break-up of 63 Delayed projects in September 2018

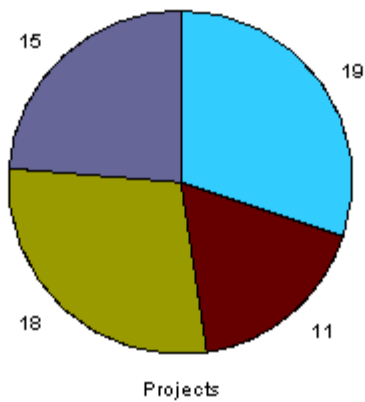


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

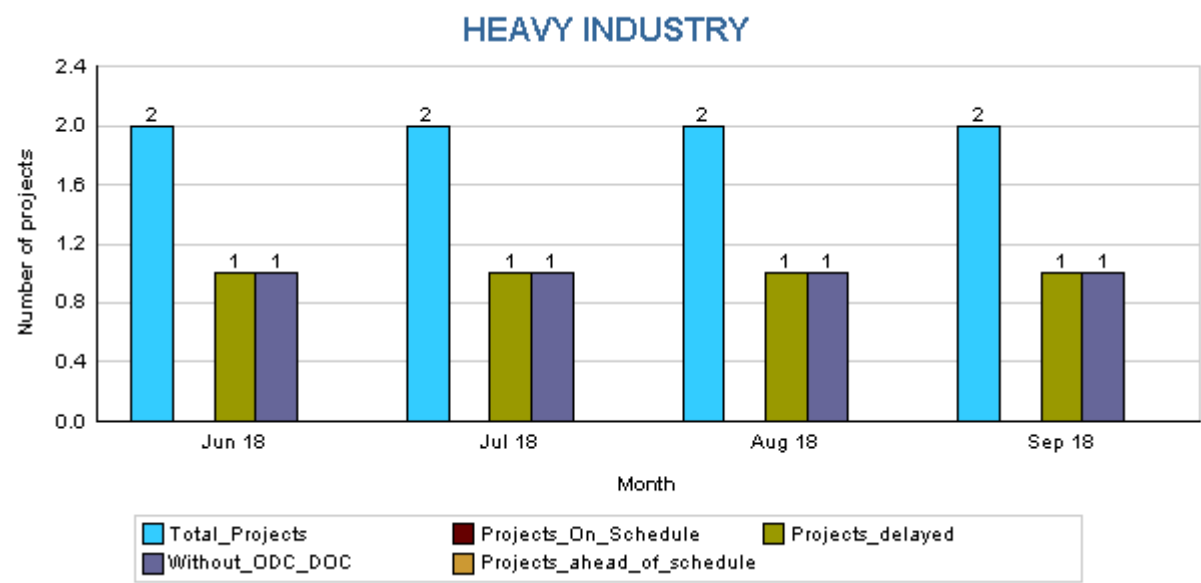


Break-up of 1 Delayed projects in September 2018

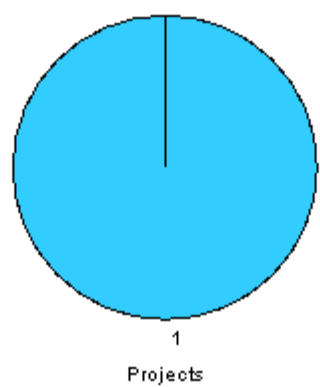


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

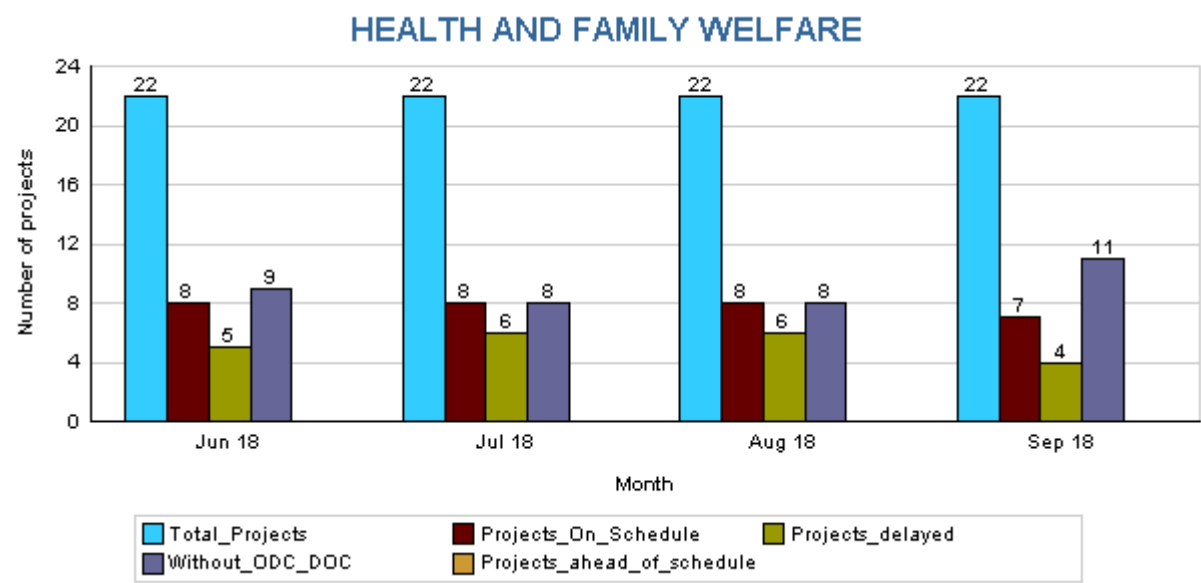


Break-up of 4 Delayed projects in September 2018

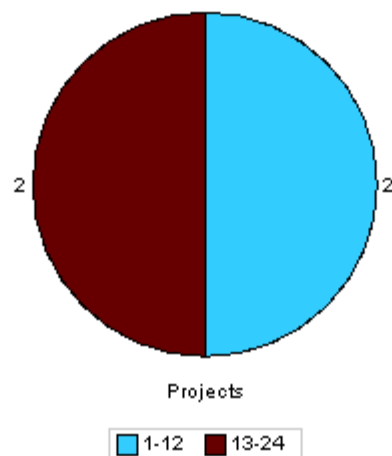


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

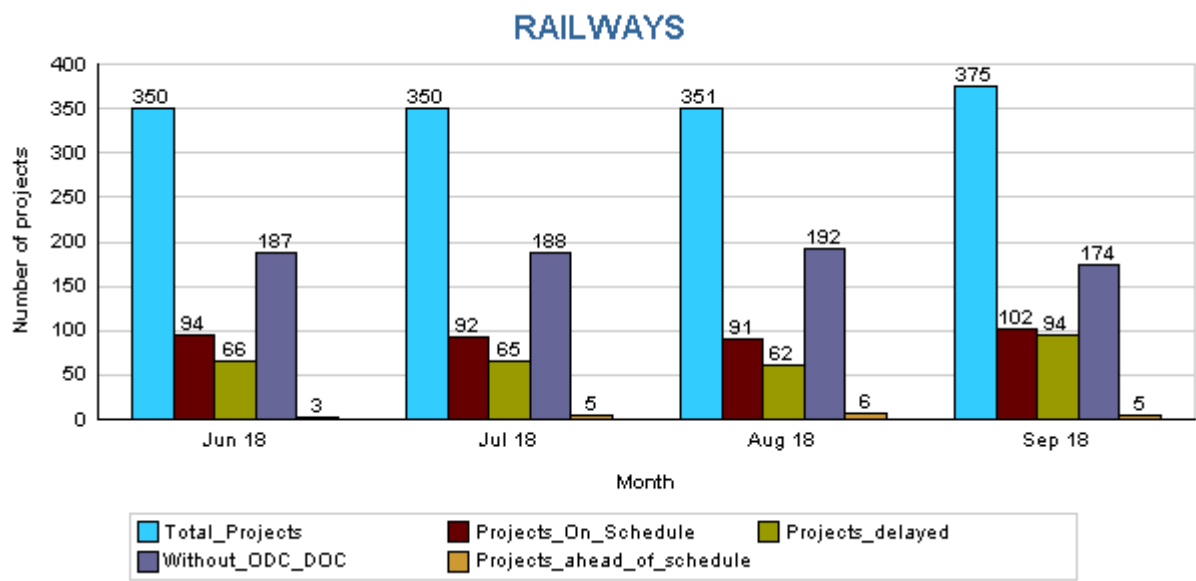


Break-up of 94 Delayed projects in September 2018

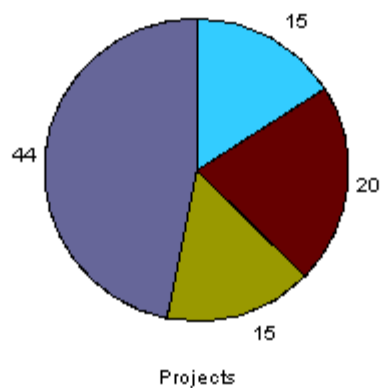


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

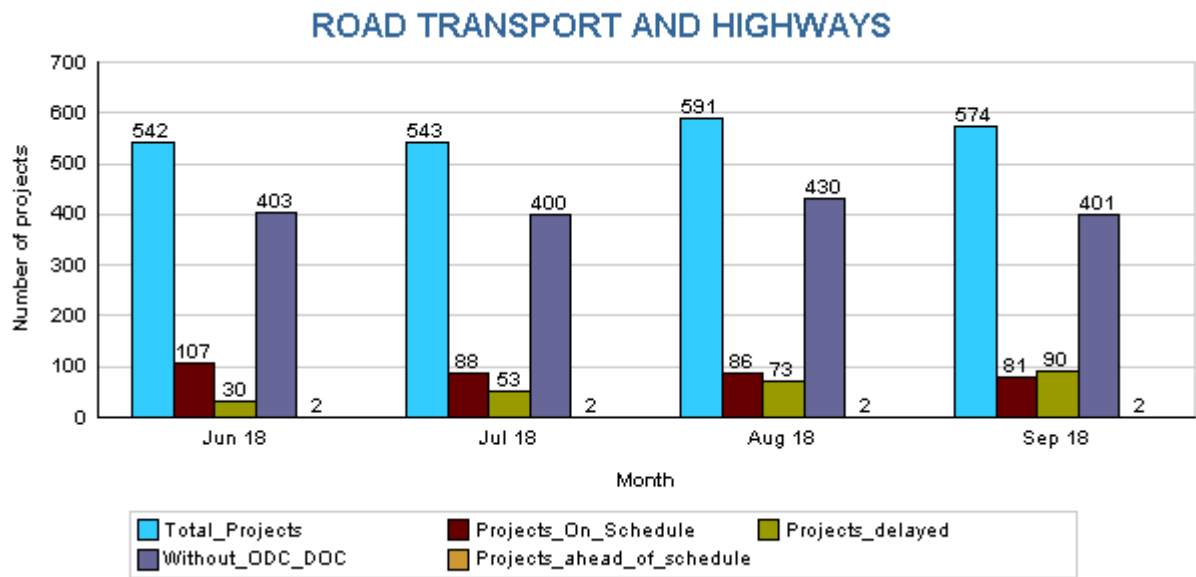


Break-up of 90 Delayed projects in September 2018

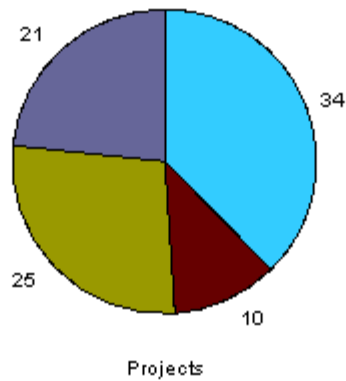


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

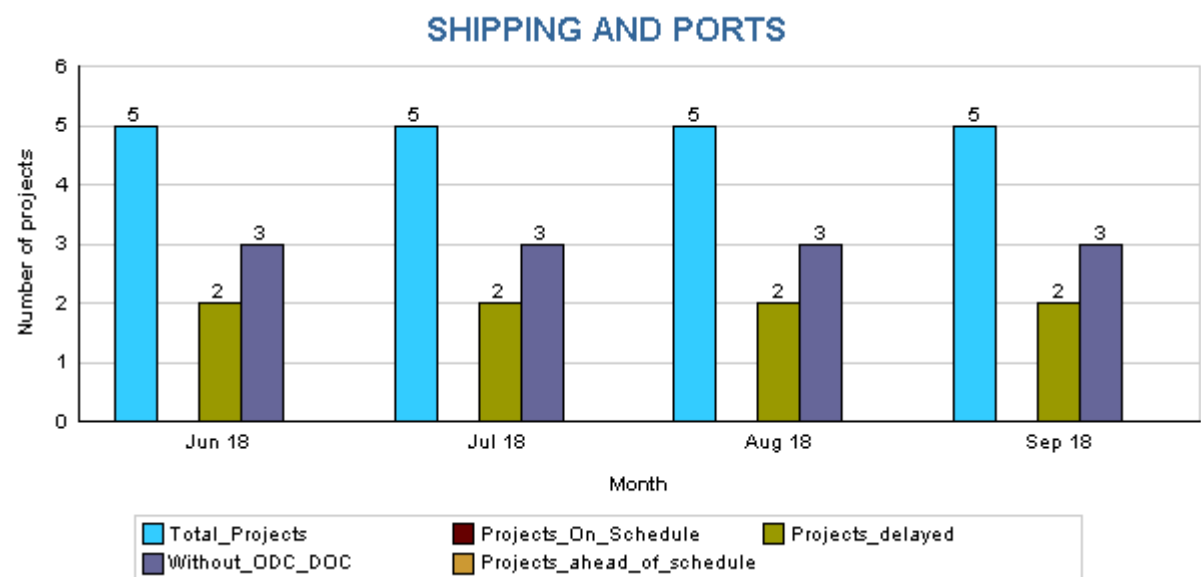


Break-up of 2 Delayed projects in September 2018

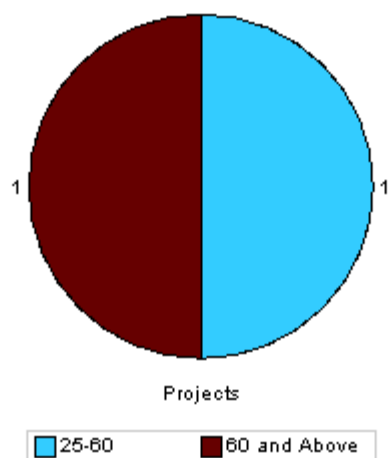


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

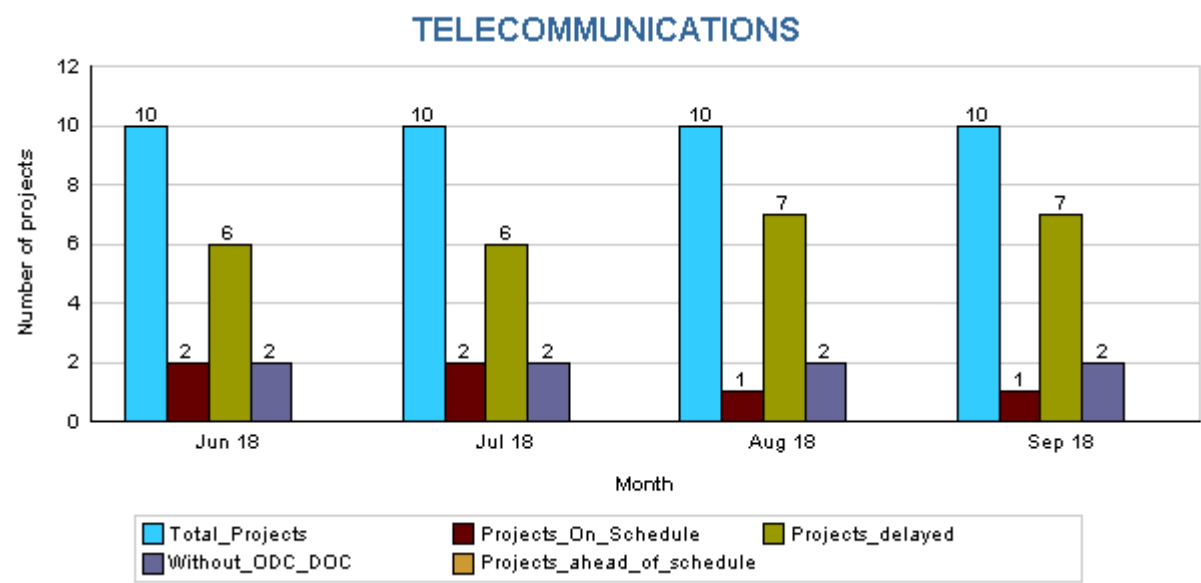


Break-up of 7 Delayed projects in September 2018

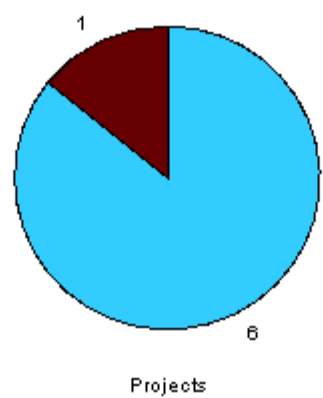


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

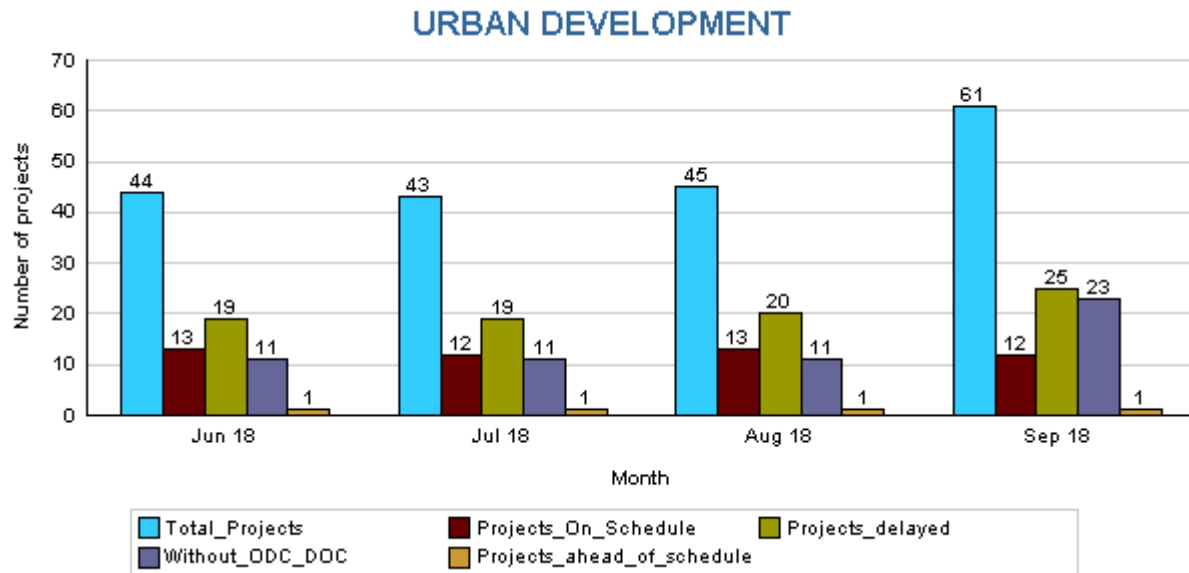


Break-up of 25 Delayed projects in September 2018

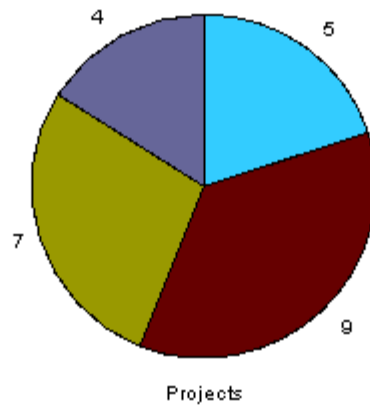

Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

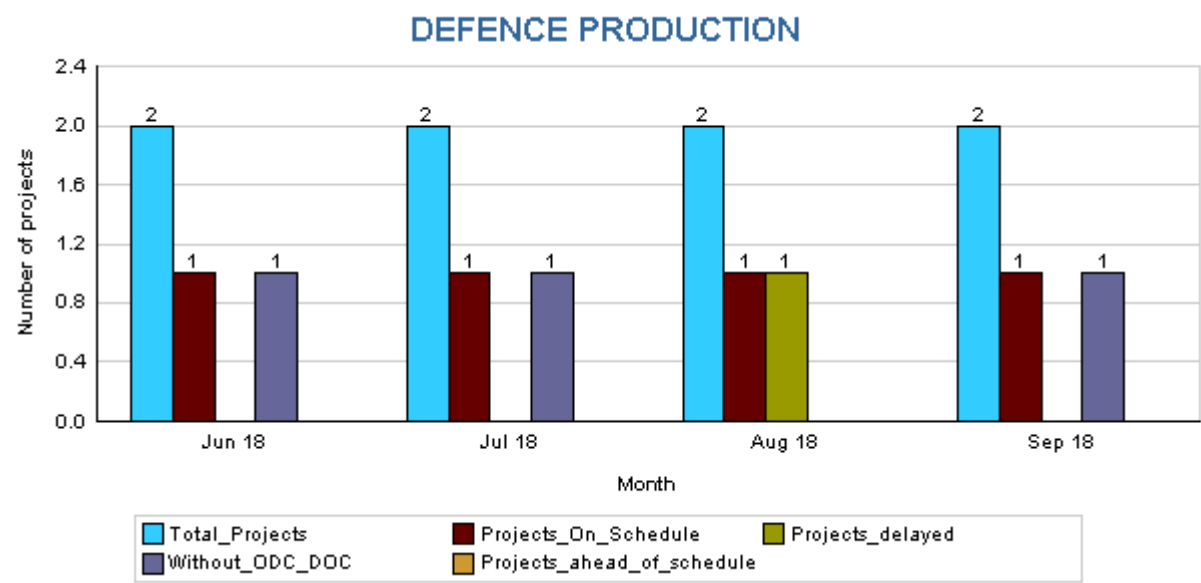

Delay in Months

TABLE-29

<u>Sector wise analysis of projects</u> Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	744,26.00	74,849.00	37,737.52
CIVIL AVIATION	2	624.07	6,24.07	994.86	632.48
COAL	97	94,971.26	940,39.87	94,434.45	27,771.96
FERTILISERS	6	1,781.92	17,93.57	1,793.57	634.37
MINES	4	6,912.00	69,12.00	6,912.00	428.19
STEEL	13	32,529.65	325,29.65	34,406.05	20,373.84
PETROLEUM	138	2,24,159.63	2,269,15.41	2,24,611.19	66,455.03
POWER	105	3,07,223.51	3,393,29.16	3,72,561.25	2,34,528.96
HEAVY INDUSTRY	2	3,272.00	32,72.00	5,381.30	2,450.86
HEALTH AND FAMILY WELFARE	22	8,611.12	86,11.12	8,660.03	2,970.30
RAILWAYS	375	4,78,359.05	5,710,70.81	7,25,343.31	1,72,361.85
ROAD TRANSPORT AND HIGHWAYS	574	3,86,925.98	3,875,66.77	4,01,159.04	1,32,643.89
SHIPPING AND PORTS	5	3,788.29	34,59.79	4,230.74	1,659.56
TELECOMMUNICATIONS	10	17,191.20	171,90.00	28,420.00	9,126.90
URBAN DEVELOPMENT	61	1,71,744.40	1,722,16.10	1,79,453.64	73,603.22
DEFENCE PRODUCTION	2	453.64	4,54.00	461.66	124.07
Grand total	1420	18,05,667.72	19,40,410.32	21,63,672.09	7,83,503.00

Table-30

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	12,463.00	12/2015 11/2016	06/2020	54(O) 43(R)	50/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	9,760.00	12/2016 03/2017	12/2020	48(O) 45(R)	36/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,100.00	5,687.52	09/2010 09/2016	03/2019	102(O) 30(R)	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	9,827.00	11/2020 -	11/2023	36(O) -	17/76
	Total		67,120.00 -	74,849.00	37,737.52				186/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	546.69	01/2011 -	09/2018	92(O) -	0/0
	Total		624.07 -	994.86	632.48				0/0
	<u>COAL</u>								
7	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,834.56	03/2023 -	03/2023	0(O) -	14/18
8	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,881.64	03/2023 -	03/2023	0(O) -	6/20
9	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.06	03/2023 -	03/2023	0(O) -	1/12
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	165.78	03/2015 03/2020	03/2020	60(O) 0(R)	5/9
11	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	1/7
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	202.31	03/2014 -	03/2020	72(O) -	0/4
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36(O) -	7/9
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	163.85	03/2016 -	03/2019	36(O) -	4/7
15	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	68.52	03/2022 -	03/2022	0(O) -	2/9
16	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	54.71	03/2020 -	03/2020	0(O) -	3/8

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	51.29	03/2018 -	03/2018	-	1/7
18	AMGAON OPENCASST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	56.54	03/2020 -	03/2020	0(O) -	0/6
19	DURGAPUR OPENCASST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	3.74	03/2023 -	03/2023	0(O) -	1/10
20	MADANNAGAR OPENCASST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	0/4
21	VIJAY WEST OPENCASST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
22	MAHAMAYA OPENCASST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	.00	03/2026 -	03/2026	0(O) -	0/0
23	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,JHARKHAND ,	08/2008	706.40 -	706.40	125.15	07/2012 -	03/2021	104(O) -	3/5
24	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	131.07	03/2014 -	-	-	6/6
25	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND ,	08/2007	163.51 -	163.51	93.93	03/2011 -	03/2020	108(O) -	3/5
26	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND ,	12/2007	179.87 -	179.87	139.30	03/2012 -	03/2019	84(O) -	3/5
27	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND ,	08/2008	264.68 -	264.68	155.09	03/2012 -	03/2019	84(O) -	4/5
28	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL,JHARKHAND ,	12/2009	510.85 -	510.85	352.34	03/2016 -	03/2019	36(O) -	4/5
29	KARMA OCP (1.0MTY) - [N06000088]JCL,JHARKHAND ,	06/2009	162.46 -	162.46	82.97	03/2014 -	03/2019	60(O) -	4/5
30	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
31	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	295.38	04/2015 -	04/2019	48(O) -	2/6
32	AMRAPALI OC(12MTY) - [N06000103]JCL,JHARKHAND ,	02/2012	858.11 -	858.11	196.02	03/2020 -	03/2020	0(O) -	5/6
33	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
34	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
35	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	189.33	05/2014 -	04/2018	-	0/8
36	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	178.46	04/2014 -	04/2018	-	0/10
37	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	42.27	03/2022 -	03/2022	0(O) -	1/21
38	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 -	486.57	266.38	03/2012 -	-	-	1/3
39	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 203.82	203.82	102.09	03/2023 03/2021	03/2021	-24(O) 0(R)	3/10
40	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/8
41	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	113.06	03/2021 -	03/2021	0(O) -	2/9
42	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	41.27	03/2021 -	03/2021	0(O) -	1/7

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/7
44	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	1.90	03/2023 -	03/2023	0(O) -	0/4
45	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	111.27	03/2021 -	03/2021	0(O) -	2/4
46	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	16.21	03/2022 -	03/2022	0(O) -	0/0
47	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	196.70	03/2021 -	03/2021	0(O) -	0/9
48	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022	0(O) -	0/9
49	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	179.06	03/2020 -	03/2020	0(O) -	7/11
50	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	389.77	03/2020 -	03/2020	0(O) -	2/8
51	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	143.28	03/2021 -	03/2021	0(O) -	12/12
52	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	207.28	03/2018 -	03/2018	-	7/7
53	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	93.19	03/2023 02/2017	03/2023	0(O) 73(R)	7/11
54	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	88.13	03/2019 -	03/2019	0(O) -	10/13
55	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	102.75	03/2020 -	03/2020	0(O) -	5/10
56	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	82.13	03/2021 -	03/2021	0(O) -	2/6
57	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	236.37	03/2025 -	03/2025	0(O) -	5/13
58	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	.00	03/2023 -	03/2023	0(O) -	2/10
59	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	22.07	03/2021 -	03/2021	0(O) -	3/6
60	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	52.83	03/2020 -	03/2020	0(O) -	2/6
61	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	254.72	03/2019 -	03/2019	0(O) -	2/9
62	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	128.93	03/2019 -	03/2019	0(O) -	2/8
63	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	257.35	03/2020 -	03/2020	0(O) -	0/0
64	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	58.04	03/2022 -	03/2022	0(O) -	0/3
65	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	16.00	03/2022 -	03/2022	0(O) -	0/12
66	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	88.13	03/2021 -	03/2021	0(O) -	1/6
67	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2018	-	9/10

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	363.95	03/2017 -	03/2020	36(O) -	11/12
69	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	581.54	03/2013 -	03/2019	72(O) -	8/9
70	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	264.26	03/2010 -	03/2019	108(O) -	3/4
71	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	234.48	03/2012 -	03/2021	108(O) -	5/5
72	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	239.22	03/2013 -	03/2020	84(O) -	6/9
73	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	104.48	03/2019 -	03/2021	24(O) -	2/9
74	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	689.20	03/2026 -	03/2026	0(O) -	5/15
75	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	44.91	03/2019 -	03/2021	24(O) -	5/6
76	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	33.53	03/2018 -	03/2020	24(O) -	3/5
77	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	413.85	03/2021 -	03/2021	0(O) -	5/9
78	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	8.71	09/2019 -	09/2019	0(O) -	0/0
79	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	173.06	12/2019 -	12/2019	0(O) -	0/0
80	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	5,666.08	12/2015 10/2018	12/2018	36(O) 2(R)	26/35
81	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	390.90	06/2015 09/2019	09/2019	51(O) 0(R)	5/7
82	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU ,	05/2016	687.28 759.19	759.19	758.30	06/2017 12/2017	12/2017	-	0/0
83	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 448.86	448.86	186.91	03/2012 03/2024	03/2024	144(O) 0(R)	35/42
84	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
85	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132(O) -	0/2
86	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48(O) -	30/31
87	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	-	5/6
88	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72(O) -	0/5
89	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72(O) -	4/29
90	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72(O) -	6/13
91	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45(O) -	35/36
92	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44(O) -	21/28
93	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36(O) -	37/39

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
94	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	79.96	03/2019 -	03/2019	0(O) -	10/18
95	KOYAGUDEM OPENCAS PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.00	03/2018 -	03/2019	12(O) -	0/9
96	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	.00	03/2020 -	03/2020	0(O) -	1/17
97	KAKATIYAKHANI OPENCAS III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	.00	03/2019 -	03/2019	0(O) -	0/11
98	KHADIA EXPANSION OPENCAS PROJECT(4 TO 10 MTPA 6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	572.40	03/2018 -	03/2019	12(O) -	10/10
99	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	3,072.20	11/2021 -	11/2021	0(O) -	0/0
100	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	296.10	03/2022 -	03/2022	0(O) -	8/13
101	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	376.04	03/2018 -	03/2020	24(O) -	11/16
102	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	2,661.73	.00	08/2019 -	08/2019	0(O) -	0/0
103	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/0
	Total		94,971.26 -	94,434.45	27,771.96				483/955
	<u>FERTILISERS</u>								
104	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	24.50	11/2019 -	11/2019	0(O) -	0/1
105	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	121.76	11/2016 04/2019	04/2019	29(O) 0(R)	1/13
106	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 482.85	482.85	413.00	12/2017 10/2018	10/2018	10(O) 0(R)	0/1
107	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	23.29	04/2020 -	04/2020	0(O) -	0/14
108	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	23.51	11/2019 -	11/2019	0(O) -	0/2
109	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	28.31	11/2019 -	11/2019	0(O) -	0/2
	Total		1,781.92 -	1,793.57	634.37				1/33
	<u>MINES</u>								
110	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	95.59	04/2021 04/2021	04/2021	0(O) 0(R)	3/3
111	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	300.68	01/2020 01/2020	01/2020	0(O) 0(R)	1/2

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 355.00	355.00	31.92	11/2020 11/2020	11/2020	0(O) 0(R)	2/2
113	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.00	04/2021 04/2021	04/2021	0(O) 0(R)	1/1
	Total		6,912.00 -	6,912.00	428.19				7/8
	<u>STEEL</u>								
114	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	238.69	10/2016 -	03/2019	29(O) -	1/2
115	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	971.76	12/2017 -	09/2019	21(O) -	4/6
116	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	89.83	08/2018 -	10/2018	2(O) -	2/4
117	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	211.25	07/2018 -	11/2018	4(O) -	2/4
118	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	120.15	04/2015 -	-	-	4/5
119	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	14,283.70	05/2015 06/2019	06/2019	49(O) 0(R)	60/86
120	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	2,907.00	29.51	06/2020 -	06/2020	0(O) -	5/12
121	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	343.36	10/2017 -	12/2018	14(O) -	0/2
122	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	842.32	12/2017 -	11/2018	11(O) -	1/2
123	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	105.87	09/2017 -	-	-	0/0
124	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	63.54	06/2019 -	06/2019	0(O) -	0/1
125	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,426.76	04/2018 -	02/2019	10(O) -	3/3
126	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	647.10	09/2018 -	01/2019	4(O) -	3/5
	Total		32,529.65 -	34,406.05	20,373.84				85/132
	<u>PETROLEUM</u>								
127	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0(O) -	0/111
128	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	199.63	09/2019 -	09/2019	0(O) -	19/27
129	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	1,200.29	06/2020 08/2021	08/2021	14(O) 0(R)	0/20

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
131	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
132	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 207.80	207.80	13.39	09/2018 02/2019	02/2019	5(O) 0(R)	0/5
133	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	25.21	04/2021 -	04/2021	0(O) -	0/0
134	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	131.32	02/2019 -	12/2018	-2(O) -	3/10
135	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.89	2,105.18	03/2013 03/2019	03/2019	72(O) 0(R)	5/15
136	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	40.04	01/2014 11/2019	11/2019	70(O) 0(R)	2/7
137	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	-	-	46/61
138	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	190.66	08/2019 -	08/2019	0(O) -	2/13
139	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,098.69	11/2019 -	11/2019	0(O) -	12/17
140	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 249.85	244.70	98.07	05/2020 05/2020	05/2020	0(O) 0(R)	0/5
141	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8(O) -	0/0
142	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	241.91	09/2019 -	09/2019	0(O) -	4/7
143	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	543.91	1.65	02/2020 -	02/2020	0(O) -	1/14
144	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	64.70	02/2020 -	02/2022	24(O) -	0/0
145	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	961.00	03/2015 -	-	-	0/5
146	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	712.49	11/2018 -	11/2018	0(O) -	6/8
147	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	333.63	12/2020 -	02/2020	-10(O) -	2/2
148	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	78.63	06/2020 -	06/2020	0(O) -	2/2
149	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	.00	03/2021 -	03/2021	0(O) -	4/26
150	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	.00	10/2020 -	10/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	24.18	10/2022 -	10/2022	0(O) -	0/0
152	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	.00	01/2021 -	01/2021	0(O) -	0/0
153	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 300.00	300.00	.00	04/2021 04/2021	04/2021	0(O) 0(R)	0/0
154	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,231.37	05/2019 10/2019	10/2019	5(O) 0(R)	0/14
155	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 567.22	567.22	449.65	11/2019 12/2018	12/2018	-11(O) 0(R)	0/5
156	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	156.83	03/2018 -	03/2018	-	20/22
157	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	100.65	04/2018 -	12/2018	8(O) -	18/20
158	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	269.97	03/2026 03/2026	03/2026	0(O) 0(R)	0/10
159	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	59.66	07/2020 -	07/2020	0(O) -	0/0
160	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	-	-	0/0
161	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	3.09	08/2020 -	08/2020	0(O) -	0/0
162	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,018.23	09/2019 -	09/2019	0(O) -	0/9
163	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020	0(O) -	0/0
164	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	.00	- -	-	-	2/17
165	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 255.00	255.00	3.60	11/2020 11/2020	11/2020	0(O) 0(R)	0/0
166	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	.12	02/2020 -	02/2020	0(O) -	0/0
167	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	793.22	07/2019 -	09/2019	2(O) -	0/9
168	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	122.32	08/2020 -	08/2020	0(O) -	0/0
169	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	169.04	05/2019 -	12/2018	-5(O) -	3/13
170	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	74.43	09/2019 -	09/2019	0(O) -	2/2
171	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 -	-	-	8/12

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
172	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	70.98	03/2023 03/2022	03/2022	-12(O) 0(R)	0/10
173	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
174	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	19.08	10/2022 -	10/2022	0(O) -	5/9
175	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	18.64	10/2022 -	10/2022	0(O) -	0/0
176	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
177	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	682.57	02/2020 -	02/2020	0(O) -	0/0
178	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019	0(O) -	6/8
179	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 171.00	170.70	111.05	03/2019 -	03/2019	0(O) -	4/11
180	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019	0(O) -	7/9
181	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	581.00	.00	03/2020 -	03/2020	0(O) -	0/0
182	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	341.41	10/2017 -	03/2019	17(O) -	39/52
183	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	2,150.27	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
184	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	215.97	02/2020 10/2020	10/2020	8(O) 0(R)	0/20
185	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019	0(O) -	0/0
186	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	.00	06/2020 -	06/2020	0(O) -	0/0
187	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,577.15	1,577.15	1,195.52	05/2013 03/2019	03/2019	70(O) 0(R)	1/8
188	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 03/2018	12/2019	57(O) 21(R)	0/17
189	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,524.08	04/2019 03/2019	03/2019	-1(O) 0(R)	0/9
190	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 -	2,504.61	1,973.99	05/2017 12/2018	12/2018	19(O) 0(R)	0/4
191	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	1,622.94	03/2019 05/2020	05/2020	14(O) 0(R)	0/5

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
192	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 4,619.94	4,619.94	3,886.50	12/2017 03/2019	03/2019	15(O) 0(R)	0/5
193	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,172.39	04/2018 05/2019	05/2019	13(O) 0(R)	0/10
194	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	475.41	08/2021 -	08/2021	0(O) -	2/2
195	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	105.67	02/2020 -	02/2020	0(O) -	0/10
196	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	110.72	12/2019 -	12/2019	0(O) -	0/0
197	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA ,	05/2015	193.40 -	193.40	88.38	01/2019 -	01/2019	0(O) -	0/18
198	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	.08	01/2021 -	01/2021	0(O) -	0/0
199	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0(O) -	0/0
200	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0(O) -	0/0
201	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
202	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	299.26	05/2019 05/2019	05/2019	0(O) 0(R)	0/5
203	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	102.53	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
204	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	78.15	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
205	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	302.59	11/2019 11/2019	11/2019	0(O) 0(R)	0/5
206	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,006.83	4,006.83	570.63	05/2021 05/2021	05/2021	0(O) 0(R)	0/15
207	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	48.20	08/2020 -	08/2020	0(O) -	0/15
208	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
209	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	.00	12/2019 -	12/2019	0(O) -	0/5
210	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	2,212.79	12/2018 -	12/2018	0(O) -	33/39
211	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	543.05	09/2011 -	-	-	0/3
212	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8
213	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	1,308.86	06/2018 -	10/2018	4(O) -	1/1
214	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	545.82	10/2014 02/2019	02/2019	52(O) 0(R)	32/40
215	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	180.72	03/2017 11/2018	03/2019	24(O) 4(R)	2/15
216	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	306.51	12/2020 -	12/2020	0(O) -	0/0
217	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	619.33	12/2020 -	08/2020	-4(O) -	2/2
218	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	475.64	10/2019 -	10/2019	0(O) -	3/3
219	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	161.13	07/2018 10/2020	10/2020	27(O) 0(R)	20/36
220	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	855.11	06/2020 -	06/2020	0(O) -	14/24
221	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	78.89	02/2019 -	02/2019	0(O) -	10/13
222	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	18.56	10/2020 -	10/2020	0(O) -	6/12
223	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	13.06	12/2019 -	12/2019	0(O) -	6/22
224	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	568.10	12/2019 12/2020	12/2019	0(O) -12(R)	15/24
225	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	611.91	12/2020 -	12/2020	0(O) -	14/24
226	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	448.61	12/2020 -	12/2020	0(O) -	13/24
227	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	2,915.00	1,921.34	12/2012 02/2019	02/2019	74(O) 0(R)	13/42
228	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	40.68	03/2021 -	03/2021	0(O) -	2/26
229	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
230	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	1.03	12/2021 -	12/2021	0(O) -	0/0
231	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,189.60	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
232	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	597.57	12/2020 -	12/2020	0(O) -	15/24
233	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	232.84	01/2019 -	01/2019	0(O) -	5/6
234	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	33.57	12/2019 -	12/2019	0(O) -	16/26
235	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	29.47	07/2022 -	07/2022	0(O) -	0/0
236	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	1.51	12/2021 -	12/2021	0(O) -	0/0
237	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	181.20 -	181.20	12.65	07/2022 -	07/2022	0(O) -	0/0
238	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	4,807.08 -	4,807.08	19.10	07/2021 -	07/2021	0(O) -	0/0
239	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	14.96	12/2020 -	12/2020	0(O) -	0/14
240	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
241	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.04	-	-	-	2/26
242	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
243	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.42	11/2015 -	-	-	52/52
244	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.12	02/2017 -	-	-	0/0
245	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 390.52	390.52	154.56	03/2019 -	04/2019	1(O) -	0/5
246	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	283.91	12/2018 -	12/2020	24(O) -	2/2
247	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	.17	06/2020 -	06/2020	0(O) -	2/3
248	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	465.00	12/2019 -	12/2019	0(O) -	0/0
249	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	11.79	08/2020 -	08/2020	0(O) -	0/0
250	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	1.18	10/2020 -	05/2021	7(O) -	0/0
251	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	800.00	577.39	12/2018 -	12/2018	0(O) -	16/20
252	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	89.65	04/2022 -	04/2022	0(O) -	26/33

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
253	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	.00	08/2021 -	08/2021	0(O) -	0/0
254	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	168.63	09/2019 -	09/2019	0(O) -	0/6
255	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.00	08/2020 -	08/2020	0(O) -	0/0
256	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	1.47	12/2021 -	12/2021	0(O) -	0/0
257	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	24.22	02/2020 -	02/2020	0(O) -	18/26
258	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,	03/2014	3,076.00 4,190.00	4,190.00	3,209.47	09/2017 06/2018	06/2018	-	6/7
259	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	694.00	470.83	10/2018 12/2018	12/2018	2(O) 0(R)	0/15
260	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
261	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	17.48	12/2020 -	12/2020	0(O) -	10/24
262	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	32.34	04/2020 -	04/2020	0(O) -	11/26
263	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	711.29	09/2019 -	09/2019	0(O) -	0/11
264	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,712.00	.98	09/2022 -	06/2021	-15(O) -	0/0
	Total		2,24,159.63 -	2,24,611.19	66,455.03				605/1484
	<u>POWER</u>								
265	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,295.43	09/2010 -	-	-	0/0
266	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,788.96	12/2009 03/2019	03/2019	111(O) 0(R)	28/30
267	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	7,154.15	09/2011 06/2018	10/2018	85(O) 4(R)	35/37
268	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	14,937.25	01/2011 04/2021	04/2021	123(O) 0(R)	26/47
269	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 13,624.00	7,998.00	7,128.72	05/2014 01/2018	05/2019	60(O) 16(R)	3/18
270	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	12,079.00	01/2018 -	05/2020	28(O) -	31/34
271	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	499.77	12/2016 -	12/2018	24(O) -	13/19

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
272	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.30	502.54	06/2019 -	06/2019	0(O) -	0/0
273	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	10,383.95	06/2017 06/2019	06/2019	24(O) 0(R)	34/40
274	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,218.88	11/2019 -	11/2019	0(O) -	0/0
275	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	191.64	05/2017 06/2019	06/2019	25(O) 0(R)	4/9
276	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	516.25	10/2018 -	10/2018	0(O) -	0/0
277	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	194.26	12/2018 -	12/2018	0(O) -	0/0
278	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	309.48	11/2017 -	12/2018	13(O) -	1/4
279	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	52.14	09/2018 -	06/2019	9(O) -	0/0
280	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPPT AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	2.50	06/2019 -	06/2019	0(O) -	0/0
281	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,394.80	7,058.21	09/2009 -	12/2021	147(O) -	2/3
282	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	980.00	04/2020 -	10/2023	42(O) -	0/0
283	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,333.71	1,528.12	09/2017 -	09/2018	12(O) -	0/0
284	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	7,574.04	02/2019 10/2020	10/2020	20(O) 0(R)	20/23
285	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	2,844.03	10/2017 -	12/2016	-	0/0
286	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 -	-	-	48/48
287	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	197.76	02/2019 -	02/2019	0(O) -	0/0
288	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	9,767.60	09/2017 06/2019	06/2019	21(O) 0(R)	33/41
289	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	5,809.85	09/2019 -	09/2019	0(O) -	26/28
290	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	215.81	03/2017 09/2018	11/2018	20(O) 2(R)	0/0
291	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	161.82	06/2018 -	12/2018	6(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
292	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	62.71	09/2020 -	09/2020	0(O) -	9/16
293	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	1,276.62	06/2018 -	11/2018	5(O) -	0/0
294	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	669.46	09/2010 12/2018	12/2018	99(O) 0(R)	5/8
295	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 02/2017	-	-	41/41
296	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	8,870.26	11/2016 03/2019	03/2019	28(O) 0(R)	34/38
297	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,538.37	10/2012 12/2018	02/2019	76(O) 2(R)	8/11
298	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,714.20	08/2013 03/2022	03/2022	103(O) 0(R)	23/26
299	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,654.96	12/2012 06/2018	11/2018	71(O) 5(R)	18/23
300	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,461.65	11/2012 09/2018	10/2018	71(O) 1(R)	12/13
301	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	499.90	06/2014 12/2018	12/2018	54(O) 0(R)	10/12
302	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 534.02	534.02	426.98	08/2014 09/2018	12/2018	52(O) 3(R)	8/10
303	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 3,190.27	3,190.27	2,281.28	12/2015 06/2018	11/2018	35(O) 5(R)	15/18
304	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,202.20	04/2016 12/2018	12/2018	32(O) 0(R)	8/12
305	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	187.24	04/2016 12/2017	10/2018	30(O) 10(R)	0/0
306	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	419.63	06/2016 09/2018	12/2018	30(O) 3(R)	9/11
307	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 550.18	550.18	433.43	11/2016 06/2019	06/2019	31(O) 0(R)	8/12
308	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	145.22	03/2016 09/2018	11/2018	32(O) 2(R)	4/6
309	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	2,716.40	03/2018 03/2019	03/2019	12(O) 0(R)	9/12
310	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	148.92	02/2016 09/2018	11/2018	33(O) 2(R)	16/17
311	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	229.40	03/2018 09/2018	11/2018	8(O) 2(R)	1/3
312	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	407.22	10/2017 09/2019	09/2019	23(O) 0(R)	0/5

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
313	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	181.16	07/2017 06/2019	06/2019	23(O) 0(R)	3/5
314	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	74.71	03/2018 -	12/2018	9(O) -	0/0
315	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	630.56	09/2017 09/2018	11/2018	14(O) 2(R)	0/0
316	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	2,518.90	04/2018 09/2018	12/2018	8(O) 3(R)	5/9
317	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	1,420.89	07/2018 -	12/2018	5(O) -	0/0
318	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	1,028.69	07/2018 -	10/2018	3(O) -	0/0
319	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	332.96	01/2018 03/2019	03/2019	14(O) 0(R)	0/0
320	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	375.34	11/2018 -	11/2018	0(O) -	0/0
321	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	1,861.40	05/2019 -	05/2019	0(O) -	0/0
322	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	3,710.05	11/2019 -	11/2019	0(O) -	0/0
323	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	97.53	11/2018 -	11/2018	0(O) -	0/0
324	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	88.66	07/2018 -	10/2018	3(O) -	0/0
325	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	250.73	03/2019 -	03/2019	0(O) -	0/0
326	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	191.76	02/2019 -	02/2019	0(O) -	0/0
327	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	76.98	02/2019 -	02/2019	0(O) -	0/0
328	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	26.40	03/2019 -	03/2019	0(O) -	0/0
329	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	79.31	06/2019 -	06/2019	0(O) -	0/0
330	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	25.85	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
331	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	139.34	01/2019 -	03/2019	2(O) -	0/0
332	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	354.00	04/2019 -	04/2019	0(O) -	0/0
333	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	55.10	02/2020 -	02/2020	0(O) -	0/0
334	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	103.28	02/2019 -	02/2019	0(O) -	0/0
335	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	22.42	03/2019 -	03/2019	0(O) -	0/0
336	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	20.09	06/2019 -	06/2019	0(O) -	0/0
337	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	21.82	12/2019 -	12/2019	0(O) -	0/0
338	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	89.17	09/2019 -	09/2019	0(O) -	0/0
339	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	552.21	04/2020 -	04/2020	0(O) -	0/0
340	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	16.10	06/2019 -	06/2019	0(O) -	0/0
341	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,141.97	840.87	12/2018 -	12/2019	12(O) -	0/0
342	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,652.57	802.18	12/2018 -	12/2019	12(O) -	0/0
343	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 -	1,364.00	1,190.30	12/2015 -	09/2018	33(O) -	0/0
344	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	2,591.63	04/2019 -	04/2019	0(O) -	0/0
345	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	481.12	07/2020 -	07/2020	0(O) -	0/0
346	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	321.99	02/2020 -	02/2020	0(O) -	0/0
347	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	.80	09/2019 -	02/2020	5(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
348	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	.00	05/2020 -	05/2020	0(O) -	0/0
349	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE ,	08/2008	771.00 1,624.00	1,624.00	1,429.45	02/2013 -	10/2018	68(O) -	0/0
350	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	8,027.68	08/2018 06/2019	06/2019	10(O) 0(R)	27/37
351	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	303.70	04/2019 -	04/2019	0(O) -	0/0
352	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	206.21	11/2017 10/2018	11/2018	12(O) 1(R)	0/0
353	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJASTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	743.82	01/2019 -	01/2019	0(O) -	0/0
354	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,534.00	2,051.63	11/2008 09/2018	12/2018	121(O) 3(R)	20/22
355	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 2,702.65	2,702.65	2,529.92	09/2014 09/2018	10/2018	49(O) 1(R)	11/13
356	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	50.27	07/2019 -	07/2019	0(O) -	0/0
357	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	2,555.03	07/2020 10/2020	10/2020	3(O) 0(R)	19/20
358	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 -	1,078.31	963.23	07/2013 -	-	-	26/26
359	FGUTPP UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
360	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	5,071.82	03/2019 09/2019	09/2019	6(O) 0(R)	19/30
361	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	195.00	02/2014 02/2018	03/2019	61(O) 13(R)	5/8
362	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	8,554.00	12/2016 -	08/2019	32(O) -	31/34
363	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	4,401.90	2,611.13	02/2016 12/2020	05/2021	63(O) 5(R)	16/30
364	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,666.44	03/2013 12/2020	12/2020	93(O) 0(R)	6/15
365	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,105.30	1,468.26	06/2013 -	12/2021	102(O) -	9/13
366	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.17	08/2017 -	-	-	0/15
367	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	118.79	12/2021 -	12/2021	0(O) -	0/32
368	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	371.98	09/2019 02/2022	02/2022	29(O) 0(R)	5/9
369	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	238.92	04/2018 -	11/2019	19(O) -	0/0
	Total		3,07,223.51 -	3,72,561.25	2,34,528.96				772/1021

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>HEAVY INDUSTRY</u>								
370	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37(O) -	0/0
371	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-	-	0/1
	Total		3,272.00 -	5,381.30	2,450.86				0/1
	<u>HEALTH AND FAMILY WELFARE</u>								
372	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	76.88	03/2019 -	03/2019	0(O) -	0/0
373	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	36.93	- -	-	-	0/0
374	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
375	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	174.00	05/2021 -	05/2021	0(O) -	0/0
376	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
377	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	237.80	05/2017 -	-	-	0/2
378	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	237.86	05/2017 -	09/2018	16(O) -	0/5
379	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.56	22.59	- -	-	-	0/0
380	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	17.00	- -	-	-	0/0
381	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	355.00	03/2018 -	09/2018	6(O) -	0/2
382	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	322.00	469.00	08/2018 -	-	-	0/1
383	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	122.66	03/2019 -	03/2019	0(O) -	0/0
384	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	4.80	- -	-	-	0/0
385	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	71.00	05/2018 -	08/2019	15(O) -	0/0
386	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	58.52	02/2018 -	12/2018	10(O) -	0/1
387	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	276.91	06/2020 -	06/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
388	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	18.50	- -	-	-	0/0
389	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	39.35	04/2020 -	04/2020	0(O) -	0/0
390	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC, WEST BENGAL ,	12/2014	168.90 -	191.38	191.38	05/2017 -	-	-	0/3
391	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL ,	08/2016	244.00 -	244.00	214.62	09/2018 -	09/2018	0(O) -	0/0
392	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	71.50	03/2019 -	03/2019	0(O) -	0/0
393	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	19.50	- -	-	-	0/0
	Total		8,611.12 -	8,660.03	2,970.30				0/14
	<u>RAILWAYS</u>								
394	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR, ANDHRA PRADESH ,	03/1996	164.36 164.36	1,050.00	999.64	02/2009 -	10/2018	116(O) -	0/0
395	KOTPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	280.17	03/2009 03/2023	03/2023	168(O) 0(R)	0/0
396	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH ,	07/2006	732.81 -	1,850.00	1,863.44	03/2008 06/2008	03/2019	132(O) 129(R)	0/0
397	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH ,	04/2011	283.54 -	761.37	.52	- -	-	-	0/0
398	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	- -	-	-	0/1
399	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	362.69	03/2021 03/2022	03/2022	12(O) 0(R)	0/1
400	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	819.86	03/2020 -	03/2022	24(O) -	0/0
401	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.07	- -	-	-	0/0
402	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	99.11	03/2022 03/2023	03/2022	0(O) -12(R)	0/0
403	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	92.48	12/2023 -	12/2023	0(O) -	0/0
404	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	2,499.71	163.03	03/2022 -	03/2022	0(O) -	0/0
405	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
406	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH ,	08/2016	234.50 -	235.00	2.98	03/2019 -	12/2020	21(O) -	0/0
407	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM ,	09/1997	3,230.02 4,857.00	5,820.00	5,224.22	04/2008 12/2011	12/2019	140(O) 96(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
408	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020	12(O) -	0/0
409	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 -	551.00	595.01	03/2019 -	03/2020	12(O) -	0/0
410	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	264.69	03/2019 -	03/2019	0(O) -	0/0
411	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.00	193.12	03/2022 -	12/2022	9(O) -	0/0
412	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	821.00	163.08	03/2021 -	03/2021	0(O) -	0/0
413	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 335.77	1,156.41	876.49	03/2012 -	03/2020	96(O) -	0/0
414	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	792.46 -	1,320.00	928.50	12/2010 -	-	-	0/0
415	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	589.15	183.72	-	03/2022	-	0/0
416	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.77	330.82	-	03/2023	-	0/0
417	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	640.78	03/2012 -	03/2020	96(O) -	0/0
418	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
419	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	413.56	361.13	06/2018 -	06/2018	-	0/0
420	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96(O) -	0/0
421	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2021	24(O) -	0/0
422	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	1,300.00	4.11	-	03/2020	-	0/0
423	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	633.87 -	2,396.88	.39	-	-	-	0/0
424	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	2,626.98	.00	-	-	-	0/0
425	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	2,860.55	.00	-	-	-	0/0
426	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	2,995.01	1.68	-	-	-	0/0
427	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.73 -	729.92	253.10	-	03/2021	-	0/0
428	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	2,614.36	111.71	-	03/2022	-	0/0
429	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
430	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
431	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	-	-	-	0/0
432	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
433	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	.19	-	03/2023	-	0/0
434	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	-	-	-	0/0
435	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	-	-	-	0/0
436	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,474.47	338.44	-	03/2021	-	0/0
437	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	785.87	40.00	03/2020	03/2020	0(O)	0/0
438	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	-	-	-	0/0
439	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	.00	-	-	-	0/0
440	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	.00	03/2020	10/2021	19(O)	0/1
441	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	.00	03/2020	10/2021	19(O)	1/1
442	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014	-	-	0/0
443	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	1.81	03/2021	03/2022	12(O)	0/0
444	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	.00	03/2021	03/2022	12(O)	0/0
445	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR ,	11/2001	624.47 -	3,550.00	97.63	02/2016	03/2021	61(O)	0/0
446	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	528.26	462.75	-	12/2018	-	0/0
447	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	566.41	759.20	-	12/2021	-	0/0
448	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) NL RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	631.78 632.00	1,195.00	626.99	12/2012	03/2022	111(O)	0/0
449	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	383.54 -	555.00	564.30	03/2010	12/2019	117(O)	0/3
450	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,143.60 1,160.83	1,160.83	566.17	03/2020	03/2020	0(O)	1/1
451	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	814.23	03/2020	03/2020	0(O)	0/0
452	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018	03/2018	-	0/0
453	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH ,	04/2011	543.00 -	543.00	.00	03/2022	03/2022	0(O)	0/0
454	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,279.00	.00	12/2019	12/2019	0(O)	0/0
455	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	1,973.00	78.00	03/2021	03/2021	0(O)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
456	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH ,	02/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022	0(O) -	0/0
457	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	600.00	09/2018 -	09/2018	0(O) -	0/0
458	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
459	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
460	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 416.86	2,783.00	444.72	03/2020 03/2020	03/2020	0(O) 0(R)	0/0
461	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 2,446.85	2,446.85	2,127.13	03/2014 03/2018	05/2018	-	0/0
462	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	83.10	03/2012 -	03/2019	84(O) -	0/0
463	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
464	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	975.62	573.13	12/2021 -	12/2021	0(O) -	0/0
465	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	81.99	03/2021 -	03/2021	0(O) -	0/0
466	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	844.10	58.31	- 03/2022	03/2022	- 0(R)	0/0
467	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.12	858.96	549.56	03/2019 03/2019	03/2022	36(O) 36(R)	0/0
468	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	704.64	12/2021 -	12/2021	0(O) -	0/0
469	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,037.15	1,037.15	882.80	03/2021 03/2020	03/2021	0(O) 12(R)	0/0
470	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 384.32	355.00	334.93	- -	-	-	0/0
471	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	202.09	03/2021 03/2019	03/2021	0(O) 24(R)	0/0
472	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	285.62	03/2019 -	12/2019	9(O) -	0/0
473	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
474	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
475	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
476	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 -	551.51	257.05	03/2019 -	03/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
477	JIND-SONEPAT (NL) NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
478	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	12/2011 -	-	-	0/0
479	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	.00	- -	-	-	0/0
480	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	243.30	03/2019 -	03/2019	0(O) -	0/0
481	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	7,000.00	212.83	12/2026 -	12/2026	0(O) -	0/0
482	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	16,500.26	11/2002 03/2021	03/2021	220(O) 0(R)	0/0
483	MANDARHILL-DUMKA-RAMPURHAT (NL) ER - [220100168]ER,JHARKHAND ,	04/1995	1,125.89 -	1,125.89	899.49	03/2016 12/2010	03/2020	48(O) 111(R)	0/0
484	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 -	3,020.94	.00	- -	03/2021	-	0/0
485	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
486	GOELKERA-MANOHARPUR (LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	388.00	388.06	02/2006 -	12/2018	154(O) -	0/1
487	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 -	167.73	264.57	03/2012 -	-	-	0/0
488	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	525.81	485.03	12/2015 12/2018	12/2018	36(O) 0(R)	0/0
489	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	175.61	- 12/2018	12/2018	- 0(R)	0/0
490	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	147.34	12/2016 08/2018	12/2018	24(O) 4(R)	0/0
491	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 1,724.20	1,724.20	140.51	03/2021 03/2021	03/2021	0(O) 0(R)	0/0
492	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	88.01	03/2021 -	12/2020	-3(O) -	0/0
493	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	134.79	03/2001 12/2024	12/2024	285(O) 0(R)	0/0
494	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264(O) 0(R)	0/0
495	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,801.01	11.56	03/2016 12/2023	12/2023	93(O) 0(R)	0/0
496	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	889.05	- -	12/2023	-	0/1
497	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 986.30	986.30	283.34	03/2016 12/2023	12/2023	93(O) 0(R)	0/1
498	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- 12/2023	12/2023	- 0(R)	0/0
499	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96(O) 0(R)	0/0
500	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 -	348.85	.36	- 12/2023	12/2023	- 0(R)	0/0
501	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	1,059.52	03/2023 -	03/2023	0(O) -	0/1
502	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	- 0(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
503	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 2,841.84	2,841.84	22.72	12/2018 12/2024	12/2024	72(O) 0(R)	0/0
504	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	- 0(R)	0/0
505	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 279.54	279.54	7.48	03/2016 12/2023	12/2023	93(O) 0(R)	0/0
506	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 1,141.00	1,156.94	646.90	03/2020 03/2020	03/2022	24(O) 24(R)	0/5
507	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 578.00	578.00	439.87	03/2020 11/2015	03/2020	0(O) 52(R)	0/2
508	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	889.52	10.91	03/2017 -	03/2020	36(O) -	0/0
509	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 1,566.00	2,815.62	255.37	- -	-	-	0/0
510	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0
511	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 342.85	369.83	427.92	- -	-	-	0/0
512	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.70	- -	-	-	0/0
513	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	18.16	- -	-	-	0/0
514	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.08	- -	-	-	0/0
515	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
516	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA ,	02/2005	241.00 -	241.00	295.12	03/2014 -	-	-	0/0
517	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 727.13	2,713.09	898.83	03/2021 -	03/2021	0(O) -	0/0
518	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	-	-	0/0
519	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 2,473.40	5,554.24	1,047.53	03/2022 03/2019	03/2022	0(O) 36(R)	0/0
520	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,763.93	.00	03/2020 -	10/2021	19(O) -	1/1
521	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	812.47	12/2020 -	12/2020	0(O) -	0/0
522	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022	0(O) -	0/1
523	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,260.61	.00	03/2022 -	03/2022	0(O) -	0/1
524	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	137.61	03/2019 -	08/2019	5(O) -	0/0
525	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019	0(O) -	0/0
526	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH ,	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96(O) -	0/0
527	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
528	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.96	715.32	06/1999 -	-	-	0/0
529	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	1,316.34	03/2004 -	03/2020	192(O) -	0/0
530	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 2,271.50	3,712.50	1,759.34	03/2021 -	03/2021	0(O) -	0/0
531	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
532	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
533	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 3,168.29	3,168.29	937.42	03/2023 -	03/2023	0(O) -	0/0
534	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 792.89	792.89	267.58	03/2021 -	03/2021	0(O) -	0/0
535	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	240.00	219.77	03/2019 -	03/2019	0(O) -	0/0
536	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 540.02	540.02	152.67	03/2022 -	03/2022	0(O) -	0/0
537	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	.00	03/2024 -	03/2024	0(O) -	0/0
538	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
539	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
540	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 1,272.19	1,272.19	109.03	03/2022 -	03/2022	0(O) -	0/0
541	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 2,449.91	2,449.91	77.75	03/2023 -	03/2023	0(O) -	0/0
542	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.47	4,817.69	148.42	03/2024 -	03/2024	0(O) -	0/0
543	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	1.05	03/2023 -	03/2023	0(O) -	0/0
544	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 1,035.16	1,035.16	12.96	03/2022 -	03/2022	0(O) -	0/0
545	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 637.95	637.95	24.71	03/2022 -	03/2022	0(O) -	0/0
546	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,750.00	1,510.51	03/2020 -	03/2020	0(O) -	0/0
547	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.22	12/2025 -	03/2025	-9(O) -	0/0
548	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 1,908.00	2,686.63	.00	03/2023 -	03/2023	0(O) -	0/0
549	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	251.08	03/2019 -	03/2019	0(O) -	0/0
550	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
551	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
552	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	403.00	36.28	12/2021 -	12/2021	0(O) -	0/0
553	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2022	132(O) -	0/0
554	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	259.43	03/2021 -	03/2021	0(O) -	0/0
555	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 2,393.48	4,600.00	2,318.33	03/2014 12/2020	12/2020	81(O) 0(R)	0/0
556	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
557	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	- -	-	-	0/0
558	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020	0(O) -	0/0
559	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	968.28	07/2012 -	-	-	0/0
560	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 236.41	3,501.83	719.03	03/2000 03/2019	12/2023	285(O) 57(R)	0/0
561	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
562	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 -	1,126.79	751.05	- -	-	-	1/1
563	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
564	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.87	- -	-	-	0/6
565	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	12/2020	144(O) -	0/0
566	DEOGHAR - SULTANGANJ (NL) ER - [220100273]ER,MULTI STATE ,	04/2000	584.41 -	1,005.23	1,069.44	02/2013 12/2012	06/2016	-	0/0
567	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	718.54	274.46	12/2022 -	12/2022	0(O) -	0/0
568	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	871.56	97.82	12/2021 -	12/2021	0(O) -	0/0
569	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	174.83	01/2019 -	01/2019	0(O) -	0/0
570	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	593.72	03/2022 03/2019	03/2022	0(O) 36(R)	0/0
571	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	599.20	03/2022 03/2019	03/2022	0(O) 36(R)	0/0
572	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,878.97	182.36	- -	-	-	0/1
573	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022	0(O) -	0/0
574	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	10.34	- -	12/2022	-	0/0
575	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
576	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
577	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	.00	03/2019 -	03/2019	0(O) -	0/0
578	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
579	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 346.15	457.08	343.65	- -	-	-	0/0
580	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	64.09	03/2020 -	03/2020	0(O) -	0/0
581	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 374.00	394.28	148.33	- -	-	-	0/0
582	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	123.11	03/2020 -	03/2020	0(O) -	0/0
583	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	03/2018	-	0/0
584	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	103.10	03/2019 -	03/2019	0(O) -	0/0
585	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	318.50 -	852.80	147.81	03/2006 -	-	-	0/0
586	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	23.56 -	1,330.73	9.31	- -	-	-	0/0
587	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.60	14.50	- -	-	-	0/0
588	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,142.49	291.74	03/2022 -	03/2022	0(O) -	0/0
589	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 -	234.41	148.00	03/2015 -	-	-	0/0
590	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	281.82	- -	-	-	0/0
591	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	343.42	- -	-	-	0/0
592	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	563.51 -	1,813.59	332.87	03/2016 -	-	-	0/0
593	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	236.21 -	1,395.63	98.43	03/2017 -	-	-	0/0
594	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	160.97	70.86	- -	-	-	0/0
595	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	136.55 -	534.24	143.74	03/2016 -	03/2020	48(O) -	0/0
596	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	528.34	99.67	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
597	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]JER,MULTI STATE ,	04/2010	157.94 -	157.94	50.50	11/2018 -	11/2018	0(O) -	0/0
598	BARIARPUUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]JER,MULTI STATE ,	04/2007	450.55 -	251.05	19.71	- -	-	-	0/0
599	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]JER,MULTI STATE ,	04/2010	365.17 -	365.67	1.76	- -	-	-	0/0
600	HANSDIHA-GODDA NL - [N22000236]JER,MULTI STATE ,	04/2011	542.18 -	693.90	310.26	03/2020 -	03/2020	0(O) -	0/0
601	SAINTHIA-TARAPITH 3RD LINE - [N22000237]JER,MULTI STATE ,	04/2011	193.44 -	186.64	166.25	- -	-	-	0/0
602	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]JER,MULTI STATE ,	04/2011	175.80 -	173.91	148.10	- -	-	-	0/0
603	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]JER,MULTI STATE ,	04/2011	299.60 -	269.60	1.12	03/2017 -	-	-	0/0
604	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]JER,MULTI STATE ,	04/2010	115.27 -	857.30	31.99	03/2005 -	-	-	0/0
605	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]JER,MULTI STATE ,	04/2000	297.47 -	153.02	52.10	- -	-	-	0/0
606	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]JER,MULTI STATE ,	04/2003	337.96 -	186.89	69.96	- -	-	-	0/0
607	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]JER,MULTI STATE ,	04/2009	278.66 -	1,255.98	147.21	02/2012 -	-	-	0/0
608	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]JER,MULTI STATE ,	04/2010	423.66 -	720.59	529.28	03/2017 -	-	-	0/0
609	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]JER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
610	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]JER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	-	-	0/0
611	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,955.27	225.85	03/2023 03/2024	03/2023	0(O) -12(R)	0/0
612	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	2,154.83	2.46	- -	-	-	0/1
613	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]JNR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	.00	- -	-	-	0/0
614	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]JNR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
615	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- 12/2023	12/2023	- 0(R)	0/0
616	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 -	2,062.20	674.76	- -	03/2022	-	0/2

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
617	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 704.31	704.31	119.69	03/2020 03/2020	03/2020	0(O) 0(R)	0/1
618	KADAPA-BANGALORE (NL) KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,206.29 -	1,996.94	215.72	03/2014 03/2023	03/2024	120(O) 12(R)	0/1
619	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
620	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
621	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	.00	- -	-	-	0/0
622	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
623	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	189.85	- -	-	-	0/0
624	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	- 0(R)	0/0
625	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	3.38	03/2020 -	03/2020	0(O) -	0/0
626	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	182.68	- 03/2021	03/2021	- 0(R)	0/0
627	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	958.00	469.91	03/2020 03/2020	03/2022	24(O) 24(R)	0/0
628	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,614.59	1,614.59	641.23	03/2019 03/2021	03/2021	24(O) 0(R)	0/0
629	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 -	678.54	.00	03/2019 -	03/2020	12(O) -	0/38
630	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
631	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	343.70	03/2021 -	03/2021	0(O) -	0/0
632	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
633	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	550.04	12/2023 12/2023	12/2023	0(O) 0(R)	0/0
634	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
635	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023	0(O) -	0/0
636	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	845.58	.00	03/2016 -	03/2016	-	0/0
637	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 2,446.57	3,000.00	655.38	03/2015 10/2021	12/2021	81(O) 2(R)	0/0
638	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
639	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,791.66	1,088.86	03/2009 -	06/2021	147(O) -	0/0
640	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,277.02	12/2017 09/2009	03/2019	15(O) 114(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
641	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 245.00	1,202.70	618.94	02/2015 -	12/2021	82(O) -	0/0
642	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	370.38	03/2009 03/2009	12/2018	117(O) 117(R)	1/1
643	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	564.41	06/2021 -	03/2023	21(O) -	0/0
644	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
645	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	742.32	02/2019 -	03/2020	13(O) -	0/0
646	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	810.28 843.04	843.04	73.71	10/2020 -	03/2022	17(O) -	0/0
647	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	180.78	03/2020 -	03/2020	0(O) -	0/0
648	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	183.12	03/2022 -	03/2022	0(O) -	0/0
649	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	77.20	03/2022 -	03/2022	0(O) -	0/0
650	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	83.66	11/2018 -	03/2021	28(O) -	0/0
651	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	210.71	12/2018 -	03/2020	15(O) -	0/0
652	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	348.22	03/2020 03/2020	03/2022	24(O) 24(R)	0/0
653	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADE FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024	36(O) 0(R)	0/0
654	VIZIANAGARAM -SAMBALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 2,735.00	2,335.67	243.95	12/2024 -	12/2024	0(O) -	0/0
655	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	970.00	918.32	03/2020 -	03/2021	12(O) -	0/0
656	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	879.77	03/2019 -	03/2021	24(O) -	0/0
657	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	.00	03/2020 -	03/2020	0(O) -	0/0
658	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
659	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
660	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	437.03	02/2019 -	02/2019	0(O) -	0/0
661	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,216.00	687.70	03/2015 -	03/2020	60(O) -	0/0
662	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	1,116.00	756.73	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
663	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	113.46	12/2019 -	06/2019	-6(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
664	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	157.63	10/2018 -	10/2018	0(O) -	0/0
665	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
666	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
667	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 295.02	865.00	65.19	03/2020 -	12/2019	-3(O) -	0/0
668	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	171.82	11/2019 -	11/2019	0(O) -	0/0
669	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	346.35	282.12	11/2018 -	12/2018	1(O) -	0/0
670	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	248.23	02/2019 -	02/2019	0(O) -	0/0
671	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,103.04	2.32	- -	-	-	0/0
672	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	407.32	03/2018 -	12/2019	21(O) -	0/0
673	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	.00	08/2022 -	08/2022	0(O) -	0/0
674	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	385.84	12/2015 -	03/2020	51(O) -	0/0
675	KARUR-SALEM(NL) SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0
676	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	980.00	1,292.55	03/2020 -	03/2020	0(O) -	0/0
677	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 495.74	734.01	438.72	06/2013 03/2019	03/2019	69(O) 0(R)	1/4
678	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,129.33	02/2019 -	02/2019	0(O) -	0/0
679	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
680	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	61.81	- -	-	-	0/0
681	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	236.09	- -	-	-	0/0
682	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019	0(O) -	0/0
683	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
684	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	- -	-	-	0/0
685	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
686	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	73.45	- -	03/2020	-	0/0
687	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU ,	02/1997	458.63 -	458.63	.92	03/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
688	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU ,	02/2000	200.84 -	200.84	394.26	03/2014 -	-	-	0/0
689	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	302.02	304.07	03/2005 -	-	-	0/0
690	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	.00	03/2018 -	03/2018	-	0/0
691	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
692	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU ,	02/2005	600.00 600.00	645.54	671.00	03/2010 -	-	-	0/0
693	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,700.00	.00	03/2022 -	03/2022	0(O) -	0/0
694	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU ,	02/2003	199.55 -	330.32	2.12	03/2009 -	-	-	0/0
695	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	.00	03/2020 -	03/2020	0(O) -	0/0
696	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU ,	02/2006	208.00 -	208.00	3.58	03/2012 -	-	-	0/0
697	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 926.23	1,025.00	1,018.51	- 03/2017	03/2017	-	0/0
698	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	815.00	3.69	- -	-	-	0/0
699	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.47	93.75	03/2010 03/2022	03/2022	144(O) 0(R)	0/1
700	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	561.52	03/2016 03/2017	12/2020	57(O) 45(R)	0/0
701	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 2,911.84	2,911.84	.92	- -	-	-	0/1
702	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	723.00	.00	- -	-	-	0/1
703	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
704	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	197.87	12/2024 -	12/2024	0(O) -	0/0
705	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	.00	03/2022 -	03/2022	0(O) -	0/0
706	AGARTALA SABROOM NL NEFR - [N22000099]NFR,TRIPURA ,	04/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019	60(O) -9(R)	0/0
707	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 4,118.00	1,733.20	1,543.99	03/2007 -	04/2016	-	0/0
708	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	650.00	.00	03/2020 -	10/2022	31(O) -	2/3
709	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
710	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
711	UTRATIA-ZAFRABAD NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	369.90 -	1,581.53	618.19	03/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
712	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]NER,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
713	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
714	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	474.30	443.26	- -	03/2018	-	0/0
715	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	270.00	259.93	08/2018 -	08/2018	-	0/0
716	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
717	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
718	FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	.00	- -	-	-	0/0
719	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
720	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
721	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	81.15	03/2022 -	03/2022	0(O)	0/0
722	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	668.00	.00	03/2020 -	03/2020	0(O)	0/6
723	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	943.60	102.17	03/2022 -	03/2022	0(O)	0/0
724	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	977.00	939.56	03/2019 -	03/2020	12(O)	0/0
725	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	228.15	03/2023 -	03/2023	0(O)	0/0
726	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	868.67	12/2020 -	03/2021	3(O)	0/0
727	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	238.38	03/2020 -	03/2021	12(O)	0/0
728	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	.59	03/2019 -	03/2021	24(O)	0/0
729	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH ,	04/1997	233.00 -	318.42	317.61	04/1999 -	-	-	0/0
730	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	.00	04/2016 -	01/2022	69(O)	0/0
731	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O)	0/0
732	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH ,	04/1997	609.04 1,063.00	1,807.88	1,793.99	04/1999 -	12/2018	236(O)	0/0
733	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O)	0/0
734	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
735	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	5.83	04/2017 -	10/2022	66(O) -	0/0
736	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
737	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	.00	- -	03/2022	- -	0/0
738	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	600.00	.00	01/2022 -	01/2022	0(O) -	0/0
739	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,177.96	.00	03/2014 -	12/2019	69(O) -	0/0
740	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
741	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
742	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	893.22	12/2024 -	12/2024	0(O) -	0/0
743	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 274.41	614.00	267.93	03/2019 -	03/2020	12(O) -	0/0
744	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
745	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]M RTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
746	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER, WEST BENGAL ,	04/2000	614.25 -	2,532.49	841.36	03/2019 12/2009	03/2019	0(O) 111(R)	0/0
747	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	501.78 -	1,960.06	724.30	12/2010 -	-	-	7/7
748	TAMLUK DIGHA LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL ,	03/1984	293.97 -	749.69	.00	06/2005 -	-	-	0/0
749	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
750	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
751	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	1,804.86	03/2016 -	03/2025	108(O) -	0/0
752	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 4,200.00	2,913.50	764.97	03/2016 -	03/2025	108(O) -	0/0
753	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,	04/2009	259.51 -	673.85	145.41	02/2012 -	-	-	0/0
754	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,	04/2009	193.08 -	683.88	148.63	12/2011 -	-	-	0/0
755	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL ,	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
756	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]SER,WEST BENGAL ,	04/1999	207.52 -	334.87	334.76	12/2012 -	-	-	0/0
757	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	-	-	0/0
758	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	- 0(R)	0/0
759	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
760	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	726.00	97.55	- -	03/2020	-	0/0
761	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL ,	04/2012	283.55 -	451.00	457.51	03/2019 -	03/2019	0(O) -	0/0
762	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
763	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	82.49	- -	-	-	0/0
764	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69 -	426.00	.00	- 03/2030	03/2030	- 0(R)	0/0
765	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27 -	612.00	18.38	12/2021 -	03/2021	-9(O) -	0/0
766	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	1,013.45 1,013.45	1,428.00	484.48	12/2021 12/2021	12/2021	0(O) 0(R)	0/0
767	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	484.43	03/2003 03/2030	03/2030	324(O) 0(R)	0/0
768	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]SER,WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	481.65	03/2022 -	03/2022	0(O) -	0/0
	Total		4,78,359.05 -	7,25,343.31	1,72,361.85				18/105
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
769	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	10/2018	0(O) -	0/0
770	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	.00	12/2017 -	-	-	0/4
771	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	.00	04/2017 -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
772	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	.00	10/2018 -	10/2018	0(O) -	0/4
773	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	.00	10/2018 -	10/2018	0(O) -	0/4
774	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,159.63	05/2013 -	-	-	0/0
775	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62(O) -	0/0
776	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,993.77	05/2014 -	-	-	0/0
777	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUEDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	.00	02/2015 -	-	-	0/4
778	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	-	-	0/1
779	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	.00	02/2017 -	-	-	0/0
780	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 -	207.40	44.08	07/2014 -	-	-	0/1
781	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	-	-	0/1
782	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/1
783	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	.00	- -	-	-	0/1
784	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	.00	- -	-	-	0/4
785	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	.00	- -	-	-	0/0
786	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	.00	12/2015 -	-	-	0/2

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
787	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
788	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	-	-	0/4
789	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	.00	- -	-	-	0/0
790	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	05/2015 -	-	-	2/4
791	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	.00	09/2015 -	-	-	0/4
792	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	.00	10/2015 -	-	-	0/0
793	FOUR LANNING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	.00	12/2015 -	-	-	0/0
794	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	.00	06/2014 -	-	-	0/2
795	FOUR LANNING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	.00	11/2015 -	-	-	0/0
796	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	04/2015 -	-	-	0/0
797	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018	0(O) -	0/0
798	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
799	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	03/2020	0(O) -	0/0
800	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2(O) -	0/0
801	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	.00	06/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
802	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	.00	- -	-	-	0/0
803	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	- -	-	-	0/0
804	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
805	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	.00	- -	-	-	0/0
806	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	1,532.62	.00	03/2021 -	03/2021	0(O) -	0/0
807	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	.00	- -	-	-	0/0
808	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	.00	- -	-	-	0/0
809	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	.00	- -	-	-	0/0
810	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	.00	- -	-	-	0/0
811	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
812	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2011 -	-	-	0/0
813	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSponding TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	.00	05/2012 -	-	-	0/0
814	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
815	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
816	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
817	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	.00	06/2018 -	-	-	0/3
818	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	.00	- -	-	-	0/0
819	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	.00	09/2010 -	-	-	0/0
820	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	.00	09/2010 -	-	-	0/0
821	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	-	-	1/4
822	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	.00	11/2016 -	-	-	0/0
823	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	.00	06/2016 -	-	-	0/4
824	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	.00	- -	-	-	0/0
825	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	.00	10/2016 -	-	-	0/4
826	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	.00	- -	-	-	0/0
827	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	.00	01/2017 -	01/2020	36(O) -	0/0
828	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	.00	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
829	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	.00	04/2017 -	-	-	0/0
830	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	.00	04/2017 -	-	-	0/0
831	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	.00	04/2017 -	-	-	0/0
832	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	.00	04/2017 -	-	-	0/0
833	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	.00	04/2017 -	-	-	0/0
834	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	.00	04/2017 -	-	-	0/0
835	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	.00	04/2017 -	-	-	0/0
836	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	.00	04/2017 -	-	-	0/0
837	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	.00	04/2017 -	-	-	0/0
838	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	-	-	-	0/0
839	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	410.32	02/2009 -	-	-	0/0
840	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	209.80	04/2009 -	-	-	0/0
841	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	118(O)	0/0
842	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
843	MAIBANG TO LUMDING (AS-27) KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	114(O)	0/0
844	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	214.88	03/2008 -	11/2017	-	0/0
845	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	312.79	06/2008 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
846	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	208.00	297.81	04/2008 -	-	-	0/0
847	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	198.82	05/2008 -	-	-	0/0
848	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
849	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	309.56	389.08	04/2010 -	-	-	0/0
850	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	-	-	0/4
851	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	-	-	0/4
852	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	-	-	0/4
853	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
854	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
855	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4
856	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	.00	05/2017 -	-	-	0/0
857	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	.00	02/2011 -	-	-	0/0
858	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	.00	02/2018 -	-	-	0/0
859	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	.00	02/2018 -	-	-	0/0
860	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	.00	12/2018 -	12/2018	0(O) -	0/4
861	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	.00	06/2018 -	-	-	0/0
862	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	.00	- -	-	-	0/0
863	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	.00	12/2018 -	12/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
864	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	.00	01/2016 -	-	-	0/4
865	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4
866	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	883.96	02/2013 -	12/2018	70(O) -	0/0
867	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	-	-	0/0
868	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2018	54(O) -	0/0
869	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
870	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	823.46	07/2013 -	06/2019	71(O) -	0/0
871	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	563.48	11/2013 -	12/2018	61(O) -	0/0
872	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	.00	-	-	-	0/0
873	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	-	-	0/0
874	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	-	-	0/0
875	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	-	-	-	0/0
876	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	138.78	04/2019 -	04/2019	0(O) -	0/0
877	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	157.20	-	01/2020	-	0/0
878	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	56.79	04/2018 -	04/2020	24(O) -	0/0
879	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	.00	-	10/2020	-	0/0
880	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	27.94	-	12/2019	-	0/0
881	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	133.02	04/2019 -	10/2019	6(O) -	0/0
882	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	-	-	-	0/0
883	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	510.69	-	-	-	0/0
884	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	400.35	04/2018 -	12/2018	8(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
885	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
886	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	.00	- -	-	-	0/0
887	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	.00	03/2014 -	-	-	0/0
888	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
889	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	.00	08/2014 -	-	-	0/0
890	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	.00	07/2016 -	-	-	0/0
891	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
892	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	.00	05/2016 -	-	-	0/0
893	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
894	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	.00	05/2016 -	-	-	0/0
895	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	.00	10/2016 -	-	-	0/0
896	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	.00	07/2016 -	-	-	0/0
897	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	.00	11/2015 -	-	-	0/0
898	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25(O) -	0/0
899	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	.00	12/2016 -	-	-	0/0
900	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
901	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	03/2020	0(O) -	0/0
902	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	.00	08/2017 -	-	-	0/0
903	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
904	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
905	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
906	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
907	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	.00	03/2015 -	-	-	0/0
908	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	.00	03/2015 -	-	-	0/0
909	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	.00	03/2015 -	-	-	0/0
910	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	.00	- -	-	-	0/0
911	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	.00	12/2012 -	-	-	0/0
912	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	.00	- -	-	-	0/0
913	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	.00	12/2015 -	-	-	0/0
914	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
915	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	.00	05/2018 -	-	-	0/0
916	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	7.21	04/2018 -	-	-	0/0
917	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	5.65	04/2018 -	06/2019	14(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
918	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,029.96	.00	- -	-	-	0/0
919	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	07/2018	-	0/0
920	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	04/2018 -	-	-	0/1
921	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
922	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
923	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
924	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	.00	- -	-	-	0/0
925	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	.00	- -	-	-	0/0
926	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	.00	- -	-	-	0/0
927	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	3,176.22	09/2012 -	08/2018	-	2/3
928	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	974.83	07/2013 -	12/2018	65(O) -	0/0
929	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3
930	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	346.60	08/2016 -	-	-	0/0
931	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	59.12	- -	08/2019	- -	0/0
932	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	22.03	- -	10/2019	- -	0/0
933	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	9.60	- -	09/2019	- -	0/0
934	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	5.64	- -	08/2019	- -	0/0
935	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	03/2019	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
936	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	364.56	72.51	- -	12/2019	- -	0/0
937	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	.00	- -	01/2020	- -	0/0
938	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	30.19	- -	09/2019	- -	0/0
939	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	.00	- -	-	-	0/0
940	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	.00	06/2020 -	06/2020	0(O) -	0/0
941	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
942	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,052.21	.00	- -	-	-	0/0
943	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	-	-	0/0
944	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	101(O) -	0/0
945	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,869.30	11/2011 -	06/2019	91(O) -	0/0
946	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	-	-	0/0
947	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -1 - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
948	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 -	602.95	54.89	06/2016 -	12/2018	30(O) -	0/0
949	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 -	574.28	51.47	07/2018 -	03/2019	8(O) -	0/0
950	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	162.60	04/2019 -	04/2019	0(O) -	0/0
951	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
952	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	.00	05/2019 -	05/2019	0(O) -	0/0
953	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	05/2019	0(O) -	0/0
954	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA ,	03/2017	639.79 -	552.90	.00	03/2020 -	03/2020	0(O) -	0/0
955	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29(O) -	0/0
956	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI, HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	104.98	03/2018 -	03/2019	12(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
957	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	18.36	02/2019 -	02/2019	0(O) -	0/0
958	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	09/2020	- -	0/0
959	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	-	-	0/0
960	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	.00	- -	-	-	0/0
961	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	.00	06/2020 -	06/2020	0(O) -	0/0
962	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,584.87	07/2015 -	03/2019	44(O) -	0/0
963	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
964	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
965	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,216.15	06/2014 -	-	-	0/0
966	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	.00	06/2019 -	06/2019	0(O) -	0/0
967	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	.00	12/2018 -	12/2018	0(O) -	0/0
968	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	.00	- -	-	-	0/0
969	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
970	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	328.14	03/2019 -	03/2019	0(O) -	0/0
971	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	.00	- -	-	-	0/0
972	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	37.20	08/2018 -	08/2018	-	0/0
973	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	10.57	03/2020 -	06/2019	-9(O) -	0/0
974	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	21.98	03/2020 -	03/2020	0(O) -	0/0
975	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
976	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
977	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9(O) -	3/3
978	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
979	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
980	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	351.24	09/2017 -	12/2018	15(O) -	0/0
981	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
982	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31(O) -	0/0
983	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	791.18	08/2018 -	04/2019	8(O) -	0/0
984	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	22.02	03/2019 -	07/2019	4(O) -	0/0
985	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	9.12	03/2019 -	11/2020	20(O) -	0/0
986	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	-	-	-	0/0
987	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	234.18	04/2020 -	04/2020	0(O) -	0/0
988	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	191.05	03/2019 -	03/2019	0(O) -	0/0
989	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	277.34	08/2019 -	08/2019	0(O) -	0/0
990	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	48.27	03/2020 -	06/2020	3(O) -	0/0
991	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	279.54	03/2020 -	06/2020	3(O) -	0/0
992	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	.00	-	-	-	0/0
993	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	1,995.34	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
994	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,177.80	.00	- -	-	-	0/0
995	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2019	79(O) -	0/0
996	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	231.56	09/2017 -	11/2018	14(O) -	0/0
997	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	201.35	11/2017 -	10/2018	11(O) -	0/0
998	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	56.32	- -	04/2019	- -	0/0
999	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	14.94	06/2018 -	04/2019	10(O) -	0/0
1000	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	.00	09/2017 -	06/2020	33(O) -	0/0
1001	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,424.77	.00	- -	-	-	0/0
1002	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67(O) -	0/0
1003	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
1004	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	-	-	0/0
1005	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1006	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
1007	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	.00	05/2015 -	-	-	0/0
1008	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	-	-	0/0
1009	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	.00	05/2017 -	-	-	0/0
1010	SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	-	-	0/0
1011	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1012	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1013	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	-	-	0/0
1014	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	-	-	0/0
1015	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	-	-	0/0
1016	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	101.33	-	10/2018	-	0/0
1017	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	72.51	-	10/2018	-	0/0
1018	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	-	-	0/0
1019	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	-	-	0/0
1020	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	-	-	0/0
1021	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	143.96	-	12/2018	-	0/0
1022	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	-	-	0/0
1023	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36(O)	0/0
1024	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	83.86	-	10/2018	-	0/0
1025	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	392.08	01/2019 -	01/2019	0(O)	0/0
1026	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	-	-	0/0
1027	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	.00	01/2019 -	01/2019	0(O)	0/0
1028	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	.00	10/2017 -	-	-	0/0
1029	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1030	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1031	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	- -	-	-	0/0
1032	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	- -	-	-	0/0
1033	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	- -	-	-	0/0
1034	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,042.82	03/2013 -	06/2019	75(O) -	0/0
1035	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	374.75	06/2014 -	03/2019	57(O) -	0/0
1036	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019	64(O) -	2/2
1037	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	-	-	0/2
1038	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	-	-	0/4
1039	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	-	-	0/12
1040	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	-	-	0/4
1041	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	-	-	0/4
1042	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	.00	- -	-	-	0/0
1043	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	65.16	- -	-	-	0/0
1044	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	205.97	- -	-	-	0/0
1045	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
1046	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	05/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1047	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	169.20	05/2018 -	03/2019	10(O) -	0/0
1048	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	-	-	0/0
1049	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	.00	05/2019 -	05/2019	0(O) -	0/0
1050	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	45.11	05/2018 -	-	-	0/0
1051	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	41.20	03/2019 -	03/2019	0(O) -	0/0
1052	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	165.31	05/2018 -	04/2019	11(O) -	0/0
1053	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,302.48	07/2017 -	12/2018	17(O) -	0/0
1054	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	444.33	11/2016 -	03/2019	28(O) -	0/0
1055	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1056	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,263.50	01/2018 -	12/2018	11(O) -	0/0
1057	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018	78(O) -	0/0
1058	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	-	-	0/0
1059	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	.00	07/2018 -	07/2018	-	0/0
1060	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	87.19	07/2019 -	07/2019	0(O) -	0/0
1061	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	237.07	07/2019 -	07/2019	0(O) -	0/0
1062	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	.00	07/2018 -	-	-	0/0
1063	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	.00	-	-	-	0/0
1064	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	-	-	-	0/0
1065	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	-	-	-	0/0
1066	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1067	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	37.39	03/2019 -	06/2019	3(O) -	0/0
1068	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	.00	03/2019 -	03/2019	0(O) -	0/0
1069	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA ,	11/2016	290.73 -	290.73	24.46	- -	05/2019	- -	0/0
1070	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	51.51	05/2019 -	05/2019	0(O) -	0/0
1071	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	97.53	02/2020 -	05/2020	3(O) -	0/0
1072	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	03/2020	0(O) -	0/0
1073	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1074	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	196.43	03/2020 -	05/2020	2(O) -	0/0
1075	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	182.85	03/2020 -	08/2020	5(O) -	0/0
1076	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	20.00	03/2017 -	11/2020	44(O) -	0/0
1077	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	86.95	03/2020 -	05/2019	-10(O) -	0/0
1078	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	50.30	03/2020 -	08/2020	5(O) -	0/0
1079	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	.00	- -	-	-	0/0
1080	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	.00	- -	-	-	0/0
1081	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	.00	- -	-	-	0/0
1082	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	674.52	01/2014 -	11/2018	58(O) -	0/0
1083	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	.00	02/2011 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1084	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	6.14	05/2018 -	03/2019	10(O) -	0/0
1085	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	159.00	- -	-	-	0/0
1086	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	.00	03/2011 -	-	-	0/0
1087	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	.00	10/2010 -	-	-	0/0
1088	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	-	-	0/0
1089	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	-	-	0/0
1090	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	-	-	2/2
1091	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,489.54	08/2014 -	-	-	0/0
1092	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,136.31	03/2014 -	12/2019	69(O) -	0/0
1093	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,363.43	03/2013 -	07/2019	76(O) -	0/0
1094	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	2,294.94	04/2015 -	-	-	0/0
1095	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	- -	-	-	0/0
1096	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1097	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	.00	- -	02/2020	- -	0/0
1098	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1099	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	.00	08/2016 -	08/2019	36(O) -	0/0
1100	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	.00	08/2016 -	08/2019	36(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1101	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	.00	08/2016 -	08/2019	36(O) -	0/0
1102	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	.00	04/2017 -	-	-	0/0
1103	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	.00	09/2018 -	09/2018	0(O) -	0/0
1104	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	09/2018	0(O) -	0/0
1105	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	09/2018	0(O) -	0/0
1106	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	09/2018	0(O) -	0/0
1107	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	09/2018	0(O) -	0/0
1108	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	.00	09/2018 -	09/2018	0(O) -	0/0
1109	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	.00	09/2018 -	09/2018	0(O) -	0/0
1110	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	.00	09/2018 -	09/2018	0(O) -	0/0
1111	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	.00	09/2018 -	09/2018	0(O) -	0/0
1112	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	.00	09/2018 -	09/2018	0(O) -	0/0
1113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	.00	09/2018 -	09/2018	0(O) -	0/0
1114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	09/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	09/2018	0(O) -	0/0
1116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	09/2018	0(O) -	0/0
1117	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	10/2015	-	0/0
1118	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	-	-	0/0
1119	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1120	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	.00	10/2016 -	-	-	0/0
1121	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1122	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	.00	01/2017 -	-	-	0/0
1123	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	-	-	-	0/0
1124	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	-	0/0
1125	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	.00	11/2017 -	-	-	0/0
1126	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	.00	08/2015 -	-	-	0/0
1127	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	-	-	-	0/0
1128	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0(O) -	0/0
1129	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	.00	-	-	-	0/0
1130	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	.00	05/2016 -	-	-	0/0
1131	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	.00	04/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1132	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	.00	10/2017 -	-	-	0/0
1133	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	.00	10/2017 -	-	-	0/0
1134	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	.00	05/2016 -	-	-	0/0
1135	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	.00	01/2017 -	-	-	0/0
1136	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	.00	06/2016 -	-	-	0/0
1137	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	.00	06/2018 -	11/2018	5(O) -	0/0
1138	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	.00	05/2016 -	-	-	0/0
1139	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	.00	03/2020 -	03/2020	0(O) -	0/0
1140	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	11/2020	40(O) -	0/0
1141	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	.00	- -	-	-	0/0
1142	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1143	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	-	-	0/0
1144	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	-	-	0/0
1145	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1146	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	-	-	0/0
1147	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1148	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	.00	- -	-	-	0/0
1149	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1150	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1151	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	-	-	0/0
1152	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1153	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1154	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1155	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1156	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	170.68	01/2016 -	-	-	0/0
1157	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1158	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1159	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1160	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1161	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1162	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1163	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1164	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1165	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1166	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	17.85	- -	04/2019	- -	0/0
1167	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	391.33	- -	11/2018	- -	0/0
1168	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	17.60	12/2017 -	04/2019	16(O) -	0/0
1169	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1170	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1171	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	72.07	09/2019 -	09/2019	0(O) -	0/0
1172	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	120.68	- -	04/2020	- -	0/0
1173	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	.00	03/2020 -	04/2020	1(O) -	0/0
1174	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	261.76	.00	- -	-	-	0/0
1175	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1176	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1177	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1178	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1179	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51(O) -	0/0
1180	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	.00	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1181	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30(O) -	0/0
1182	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	211.16	05/2017 -	10/2018	17(O) -	0/0
1183	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	42.79	03/2018 -	11/2018	8(O) -	0/0
1184	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	-	-	0/0
1185	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	206.78	05/2016 -	-	-	0/0
1186	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	596.06	10/2017 -	10/2018	12(O) -	0/0
1187	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27(O) -	0/0
1188	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	647.00	04/2018 -	12/2018	8(O) -	0/0
1189	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1190	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1191	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	10/2018	84(O) 13(R)	0/0
1192	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	242.51	- -	10/2018	- -	0/0
1193	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	535.30	06/2019 -	09/2019	3(O) -	0/0
1194	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	.00	06/2019 -	06/2019	0(O) -	0/0
1195	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1196	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	426.85	- -	11/2019	- -	0/0
1197	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	232.15	10/2018 -	10/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1198	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	174.91	01/2019 -	01/2019	0(O) -	0/0
1199	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	475.69	- -	05/2020	- -	0/0
1200	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	530.00	- -	12/2019	- -	0/0
1201	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1202	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	.00	04/2020 -	04/2020	0(O) -	0/0
1203	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	.00	10/2017 -	-	-	0/0
1204	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	-	-	0/0
1205	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	.00	- -	-	-	0/0
1206	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1207	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	.00	- -	-	-	0/0
1208	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	.00	08/2013 -	-	-	0/0
1209	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	.00	08/2013 -	-	-	0/0
1210	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1211	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	.00	10/2017 -	-	-	0/0
1212	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	7.50	11/2017 -	-	-	0/0
1213	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	.00	- -	-	-	0/0
1214	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	18.12	11/2017 -	11/2017	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1215	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	06/2018	-	0/0
1216	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018	60(O) -	0/0
1217	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	324.02	06/2013 -	-	-	0/0
1218	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67(O) -	0/0
1219	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64(O) -	0/0
1220	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2019	68(O) -	0/0
1221	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1222	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1223	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1224	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	881.98	11/2017 -	05/2019	18(O) -	0/0
1225	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18(O) -	0/0
1226	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1227	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	-	-	0/0
1228	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	627.37	07/2008 -	-	-	0/0
1229	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	168.88	08/2018 -	06/2019	10(O) -	0/0
1230	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	204.31	07/2018 -	-	-	0/0
1231	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	5.00	03/2020 -	03/2020	0(O) -	0/0
1232	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1233	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	-	-	0/0
1234	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	.00	09/2017 -	-	-	0/0
1235	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	-	-	0/0
1236	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	.00	-	-	-	0/0
1237	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	-	-	-	0/0
1238	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,407.12	09/2016 -	06/2019	33(O) -	0/0
1239	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1240	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1241	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1242	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	.00	03/2016 -	-	-	0/2
1243	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1244	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	.00	12/2016 -	-	-	0/4
1245	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1246	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1247	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1248	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	502.66	11/2018 -	07/2019	8(O) -	0/0
1249	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1250	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	.00	- -	-	-	0/0
1251	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	-	-	0/4
1252	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	-	-	0/4
1253	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,948.72	08/2013 -	-	-	0/0
1254	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	09/2018	60(O) -	0/0
1255	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	414.14	01/2014 -	09/2018	56(O) -	0/0
1256	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,898.25	09/2015 -	-	-	0/0
1257	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	.00	- -	-	-	0/0
1258	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	.00	03/2016 -	-	-	0/0
1259	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	.00	10/2016 -	-	-	0/0
1260	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1261	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	420.32	01/2016 -	-	-	0/0
1262	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	230.47	09/2016 -	-	-	0/0
1263	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	189.14	01/2016 -	-	-	0/0
1264	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	595.31	01/2016 -	-	-	0/0
1265	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	.00	03/2017 -	-	-	0/0
1266	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1267	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	.00	10/2016 -	-	-	0/0
1268	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	.00	03/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1269	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	-	-	0/0
1270	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	.00	10/2016 -	-	-	0/0
1271	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	.00	03/2017 -	-	-	0/0
1272	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.63	03/2018 -	-	-	0/0
1273	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	1,910.00	01/2019 -	01/2019	0(O) -	0/0
1274	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	660.22	06/2016 -	-	-	0/0
1275	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	281.19	06/2018 -	-	-	0/0
1276	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	374.12	06/2018 -	-	-	0/0
1277	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	321.86	07/2018 -	-	-	0/0
1278	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	394.53	06/2018 -	-	-	0/0
1279	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	.00	08/2015 -	-	-	0/0
1280	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1281	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1282	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	391.80	- -	-	-	0/0
1283	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	841.92	05/2019 -	05/2019	0(O) -	0/0
1284	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	708.59	06/2019 -	06/2019	0(O) -	0/0
1285	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	409.11	04/2019 -	04/2019	0(O) -	0/0
1286	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	193.08	- -	-	-	0/0
1287	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	105.56	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1288	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	110.58	04/2019 -	04/2019	0(O) -	0/0
1289	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	301.30	04/2019 -	04/2019	0(O) -	0/0
1290	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	253.54	- -	02/2020	- -	0/0
1291	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	.00	- -	07/2020	- -	0/0
1292	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	.00	- -	04/2020	- -	0/0
1293	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,310.42	04/2019 -	11/2019	7(O) -	0/0
1294	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	170.92	- -	-	-	0/0
1295	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	264.99	- -	-	-	0/0
1296	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	.00	03/2020 -	11/2020	8(O) -	0/0
1297	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	.00	03/2020 -	03/2020	0(O) -	0/0
1298	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	.00	03/2020 -	05/2020	2(O) -	0/0
1299	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	738.75	03/2020 -	03/2020	0(O) -	0/0
1300	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	498.25	- -	-	-	0/0
1301	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1302	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1303	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1304	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1305	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1306	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1307	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	-	-	0/0
1308	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1309	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0
1310	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	1,025.80	.00	- -	-	-	0/0
1311	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	1,115.28	.00	- -	-	-	0/0
1312	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	.00	- -	-	-	0/0
1313	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69(O) -	0/0
1314	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	138.57	- -	10/2019	- -	0/0
1315	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	22.50	- -	-	-	0/0
1316	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018	-	0/0
1317	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	.00	05/2018 -	-	-	0/4
1318	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	.00	06/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1319	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	.00	05/2018 -	-	-	0/4
1320	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	.00	12/2019 -	12/2019	0(O) -	0/0
1321	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	.00	12/2019 -	12/2019	0(O) -	0/0
1322	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	.00	12/2019 -	12/2019	0(O) -	0/0
1323	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	.00	06/2019 -	06/2019	0(O) -	0/0
1324	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	.00	11/2019 -	11/2019	0(O) -	0/0
1325	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	284.00	.00	11/2019 -	11/2019	0(O) -	0/0
1326	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	.00	11/2019 -	11/2019	0(O) -	0/0
1327	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	.00	02/2020 -	02/2020	0(O) -	0/0
1328	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	.00	- -	-	-	0/0
1329	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1330	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1331	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,310.60	08/2013 -	-	-	0/0
1332	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,822.70	08/2013 -	-	-	0/0
1333	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	-	-	0/0
1334	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	441.57	07/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1335	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1336	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	.00	- -	12/2019	-	0/0
1337	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	105.70	06/2018 -	05/2019	11(O) -	0/0
1338	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,836.44	- -	-	-	0/0
1339	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	6.39	11/2018 -	11/2018	0(O) -	0/0
1340	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	123.31	08/2018 -	08/2018	-	0/0
1341	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	.00	06/2018 -	06/2018	-	0/0
1342	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0
	Total		3,86,925.98 -	4,01,159.04	1,32,643.89				23/210
	<u>SHIPPING AND PORTS</u>								
1343	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96(O) -	0/0
1344	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1345	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
1346	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	275.98	275.98	12/2017 -	-	-	1/1
1347	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU ,	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29(O) -	0/0
	Total		3,788.29 -	4,230.74	1,659.56				1/1
	<u>TELECOMMUNICATIONS</u>								
1348	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL, DELHI ,	06/2016	418.26 -	418.26	172.30	06/2017 -	-	-	0/0
1349	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL, GUJARAT , Central Sector Projects	09/2017	171.54 -	171.54	72.46	05/2018 10/2018	10/2018	5(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1350	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	159.30 -	159.30	12.40	04/2018 10/2018	10/2018	6(O) 0(R)	0/0
1351	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	167.68 -	167.68	30.21	04/2018 10/2018	10/2018	6(O) 0(R)	0/0
1352	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	212.70 -	212.70	37.08	05/2018 10/2018	10/2018	5(O) 0(R)	0/0
1353	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 214.10	214.10	33.46	05/2018 10/2018	10/2018	5(O) 0(R)	0/0
1354	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 -	231.80	39.75	10/2018 10/2018	10/2018	0(O) 0(R)	0/0
1355	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0
1356	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
1357	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH ,	11/2017	169.45 -	169.45	78.34	08/2018 10/2018	10/2018	2(O) 0(R)	0/0
	Total		17,191.20 -	28,420.00	9,126.90				0/70
	<u>URBAN DEVELOPMENT</u>								
1358	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1359	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	134.62	03/2017 -	-	-	4/5
1360	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1361	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	.02	03/2019 -	03/2019	0(O) -	0/7
1362	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1363	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	17.72	06/2017 07/2017	06/2020	36(O) 35(R)	0/0
1364	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	-	-	0/0
1365	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	282.67	10/2019 -	03/2020	5(O) -	0/7

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1366	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	626.67	12/2015 -	12/2018	36(O) -	0/0
1367	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,376.53	11/2019 -	11/2019	0(O) -	3/7
1368	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	5.08	04/2019 06/2020	06/2020	14(O) 0(R)	0/2
1369	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1370	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	.36	05/2020 -	05/2020	0(O) -	0/0
1371	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	55.43	06/2019 -	06/2019	0(O) -	0/0
1372	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	.00	- -	-	-	0/0
1373	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	.00	- -	-	-	0/0
1374	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	1.21	04/2018 -	-	-	0/0
1375	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	1.84	11/2019 -	11/2019	0(O) -	0/0
1376	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1377	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	2,078.80	12/2018 -	07/2020	19(O) -	0/0
1378	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 210.00	270.83	163.97	11/2014 -	02/2019	51(O) -	2/8
1379	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1380	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1381	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
1382	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1383	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	41.24	03/2016 -	12/2019	45(O) -	1/6
1384	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1385	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1386	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1387	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	21.94	02/2020 09/2020	09/2020	7(O) 0(R)	0/0
1388	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77(O) -	1/5
1389	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	5,181.79	.00	07/2017 -	12/2019	29(O) -	0/0
1390	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020	0(O) -3(R)	2/7
1391	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	05/2016	164.00 -	164.00	117.49	11/2018 09/2018	09/2018	-2(O) 0(R)	11/11
1392	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 -	349.33	307.50	03/2016 -	04/2018	-	0/13
1393	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 8,680.00	8,680.00	4,256.12	03/2018 12/2019	12/2019	21(O) 0(R)	0/0
1394	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1395	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	.00	07/2020 09/2018	09/2020	2(O) 24(R)	0/14
1396	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	1,793.83	11/2021 -	11/2021	0(O) -	0/0
1397	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 216.69	216.69	52.00	03/2015 11/2018	11/2019	56(O) 12(R)	0/10
1398	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0
1399	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	379.31	05/2017 08/2018	11/2018	18(O) 3(R)	7/12
1400	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	112.23	04/2019 06/2019	06/2019	2(O) 0(R)	3/8
1401	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	.00	09/2018 -	09/2018	0(O) -	0/5
1402	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1403	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	540.42	152.99	07/2019 -	09/2019	2(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1404	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	342.00	321.13	09/2016 03/2018	09/2018	24(O) 6(R)	0/0
1405	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-	-	12/24
1406	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	52.00	10/2019 -	10/2019	0(O) -	0/6
1407	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/0
1408	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	.00	- -	-	-	0/0
1409	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	6.61	03/2020 -	03/2020	0(O) -	0/5
1410	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1411	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1412	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1413	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1414	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	.00	03/2020 -	03/2020	0(O) -	0/0
1415	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1416	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1417	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	143.14	08/2016 -	01/2019	29(O) -	8/16
1418	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	81.75	04/2018 -	07/2019	15(O) -	3/6
	Total		1,71,744.40 -	1,79,453.64	73,603.22				57/184
	DEFENCE PRODUCTION								
1419	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	170.37	74.12	05/2018 08/2018	08/2018	-	5/10
1420	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	291.29	49.95	08/2020 -	08/2020	0(O) -	4/8
	Total		453.64 -	461.66	124.07				9/18

Detail of ongoing Projects Costing Rs.150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(September 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Grand Total		18,05,667.72	21,63,672.09	7,83,503.00				2247/4537


Summary of projects in the Flash Report for the month of September, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1417
Number of Projects completed/dropped/frozen in Current Month	25
Number of Projects elevated to the status of Major project during the current month	4
Number of Projects Added in Current Month	24
Number of Projects in Current Month	1420

Brief Analysis

Project Status with respect to Original Schedule: Out of 1420 projects, 18 projects are ahead of schedule, 385 projects are on schedule 366 projects are delayed. 591 projects do not have fixed dates of commissioning. 60 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

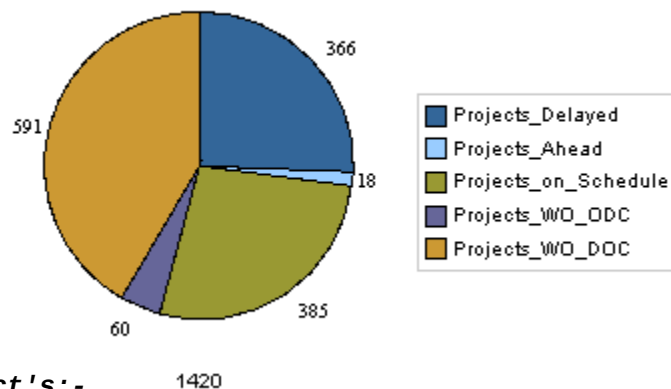


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1420 projects when sanctioned, was of the order of Rs. 1805667.72 crore but this was subsequently revised to Rs. 2163672.09 crore implying a cost overrun of 19.8%. The expenditure incurred on these projects till September, 2018 is Rs. 783503 crore, which is 36.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

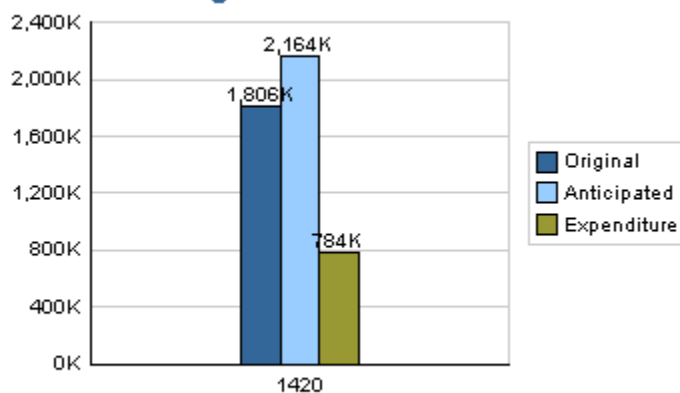

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

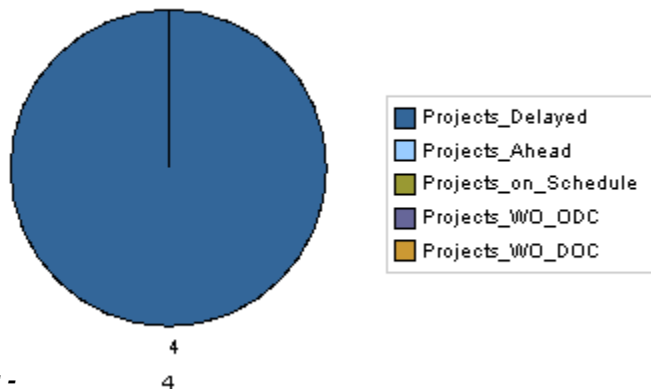

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 74849 crore implying a cost overrun of 11.5%. The expenditure incurred on these projects till September, 2018 is Rs. 37737.52 crore, which is 50.4% of the anticipated cost of the projects.

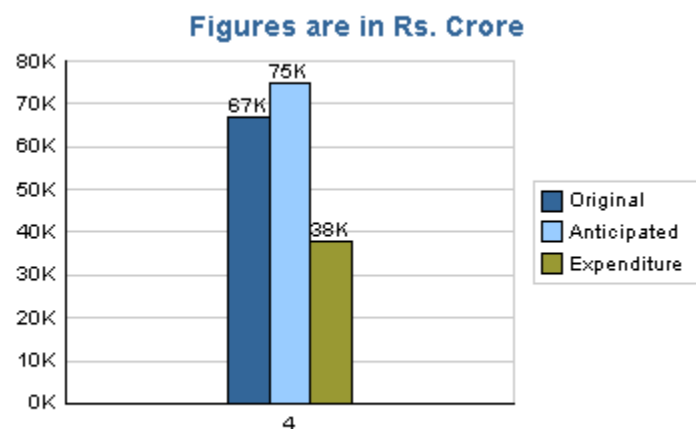

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.

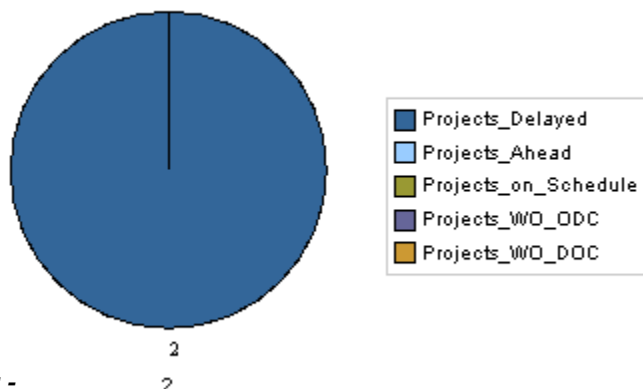

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till September, 2018 is Rs. 632.48 crore, which is 63.6% of the anticipated cost of the projects.

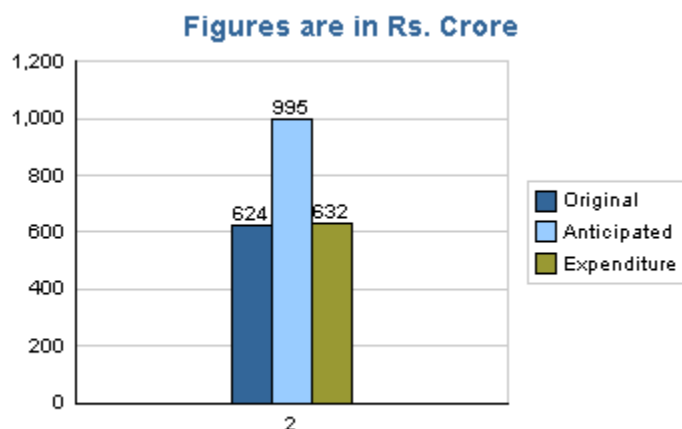

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	97
Number of Projects On Schedule	50
Number of Projects Delayed	35
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 97 projects, 1 project is ahead of schedule, 50 projects are on schedule 35 projects are delayed. 11 projects do not have fixed dates of commissioning.

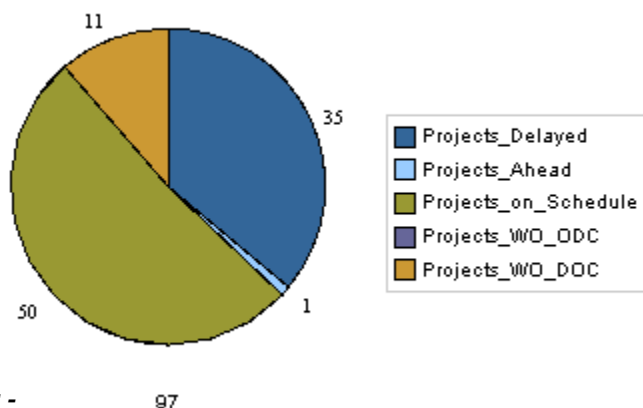


Total No Of Project's:-

97

Investment Scenario

Total original cost of implementation of 97 projects when sanctioned, was of the order of Rs. 94971.26 crore but this was subsequently anticipated to Rs. 94434.45 cr The expenditure incurred on these projects till September, 2018 is Rs. 27771.96 crore, which is 29.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

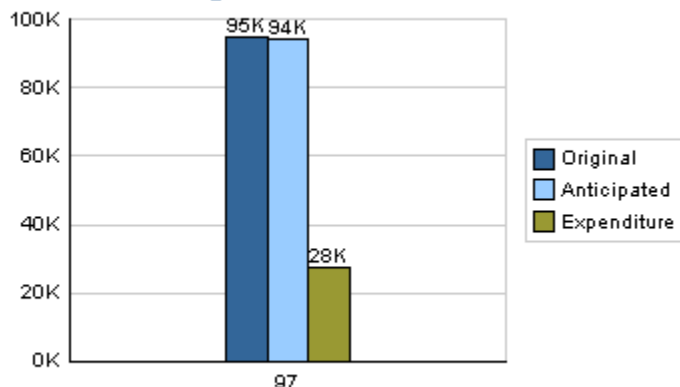

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule 2 projects are delayed.

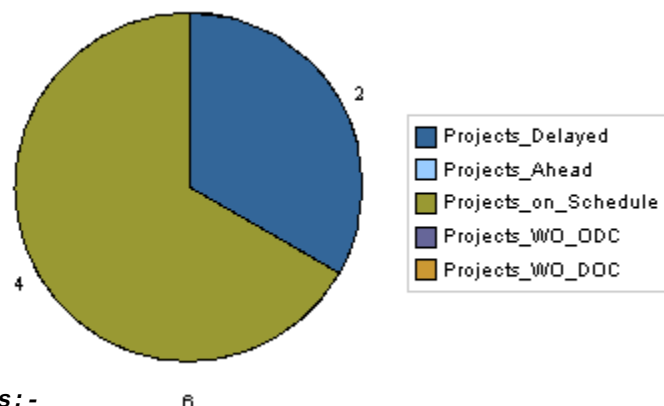


Total No Of Project's:-

6

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1781.92 crore but this was subsequently anticipated to Rs. 1793.57 crore implying a cost overrun of .7%. The expenditure incurred on these projects till September, 2018 is Rs. 634.37 crore, which is 35.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

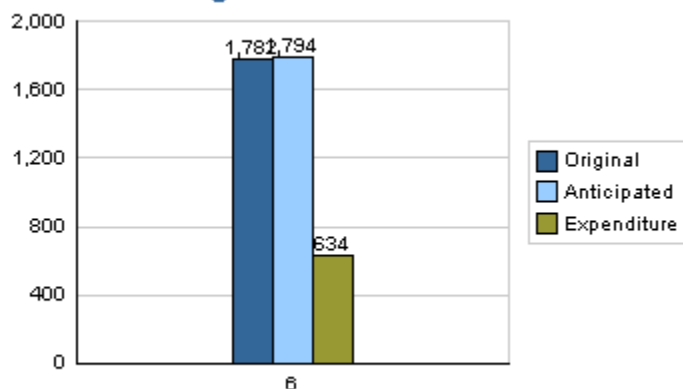

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	4
Number of Projects On Schedule	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are on schedule

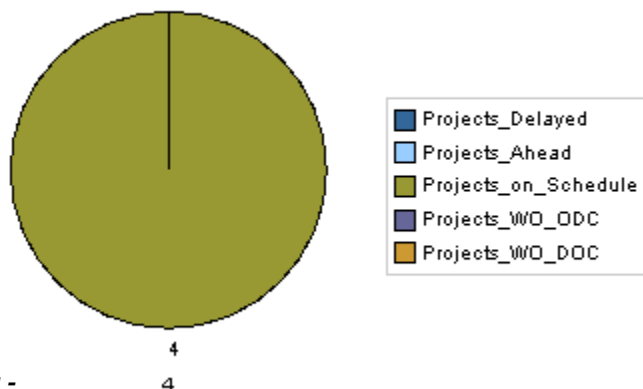


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6912 crore but this was subsequently anticipated to Rs. 6912 crore. The expenditure incurred on these projects till September, 2018 is Rs. 428.19 crore, which is 6.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

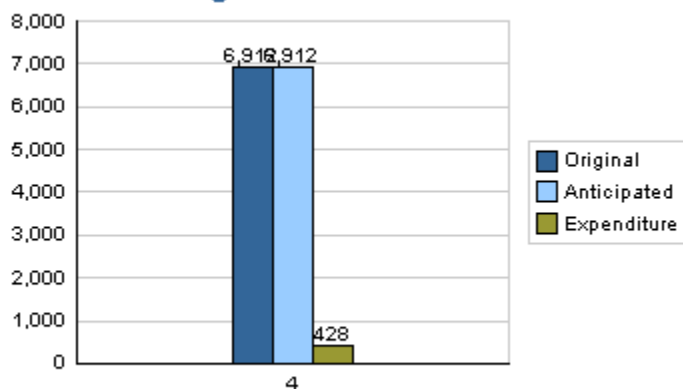

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	13
Number of Projects On Schedule	2
Number of Projects Delayed	9

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 2 projects are on schedule 9 projects are delayed. 2 projects do not have fixed dates of commissioning.

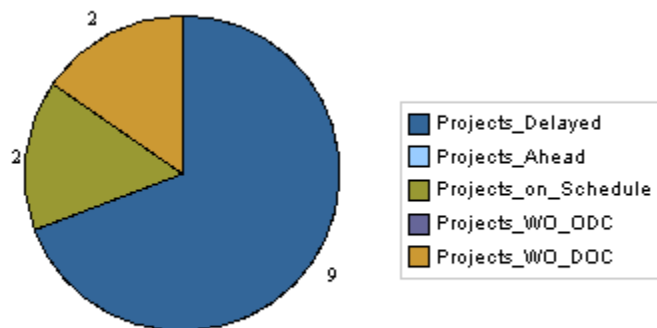


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 32529.65 crore but this was subsequently anticipated to Rs. 34406.05 crore implying a cost overrun of 5.8%. The expenditure incurred on these projects till September, 2018 is Rs. 20373.84 crore, which is 59.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

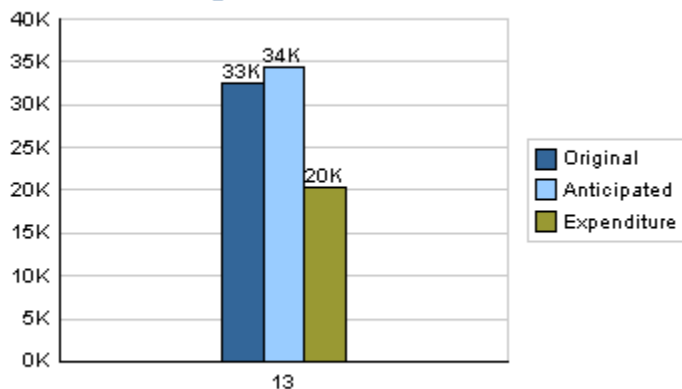

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	138
Number of Projects On Schedule	86
Number of Projects Delayed	28
Number of Projects Ahead	9
Number of Projects Without Date Of Commissioning	15

Brief Analysis

Project Status with respect to Original Schedule: Out of 138 projects, 9 projects are ahead of schedule, 86 projects are on schedule 28 projects are delayed. 15 projects do not have fixed dates of commissioning.

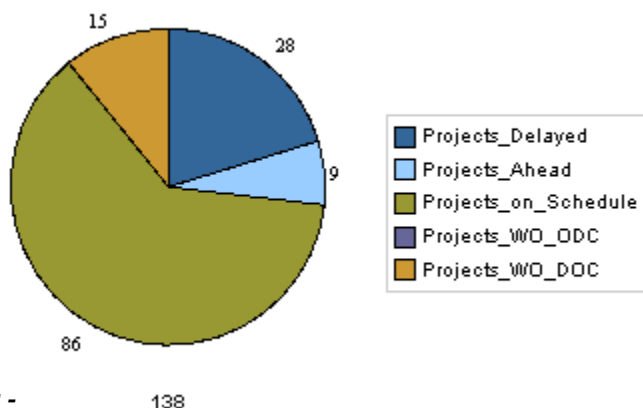


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 138 projects when sanctioned, was of the order of Rs. 224159.63 crore but this was subsequently anticipated to Rs. 224611.19 crore implying a cost overrun of .2%. The expenditure incurred on these projects till September, 2018 is Rs. 66455.03 crore, which is 29.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

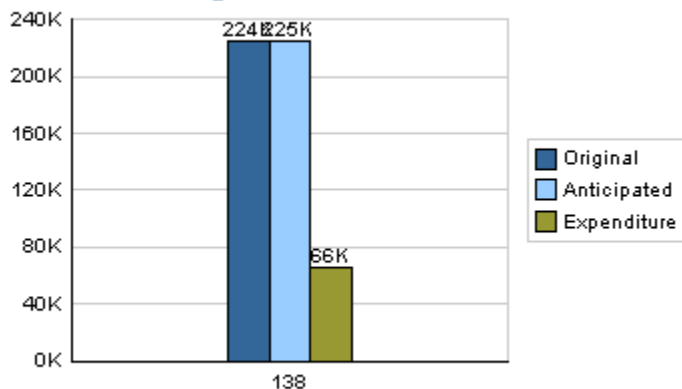

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	105
Number of Projects On Schedule	35
Number of Projects Delayed	63

Number of Projects Without Date Of Commissioning 7

Brief Analysis

Project Status with respect to Original Schedule: Out of 105 projects, 35 projects are on schedule 63 projects are delayed. 7 projects do not have fixed dates of commissioning.

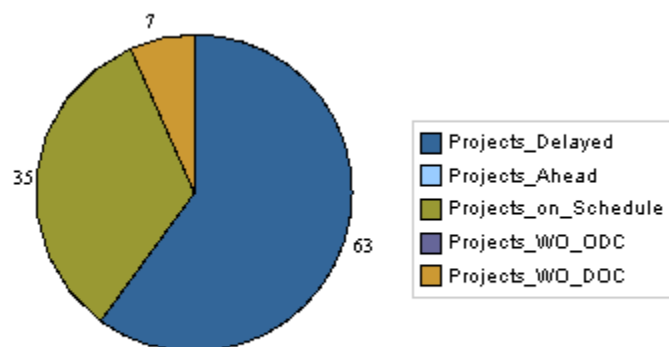


Total No Of Project's:-

105

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 307223.51 crore but this was subsequently anticipated to Rs. 372561.25 crore implying a cost overrun of 21.3%. The expenditure incurred on these projects till September, 2018 is Rs. 234528.96 crore, which is 63% of the anticipated cost of the projects.

Figures are in Rs. Crore

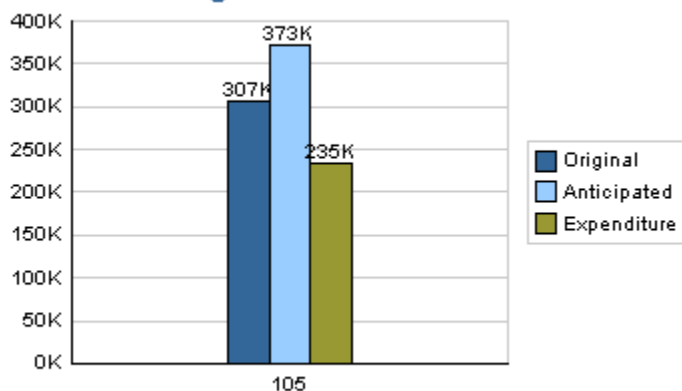

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	22
Number of Projects On Schedule	7
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning 11

Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 7 projects are on schedule 4 projects are delayed. 11 projects do not have fixed dates of commissioning.

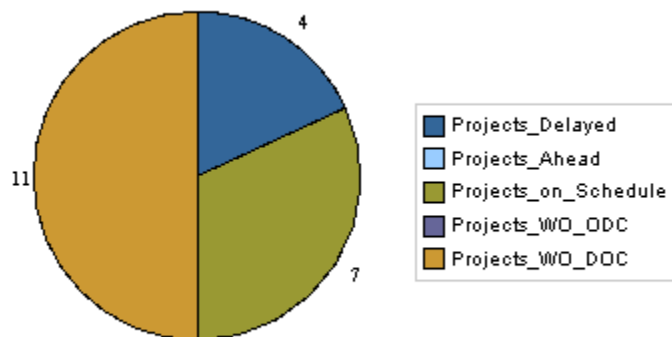


Total No Of Project's:-

22

Investment Scenario

Total original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 8611.12 crore but this was subsequently anticipated to Rs. 8660.03 crore implying a cost overrun of .6%. The expenditure incurred on these projects till September, 2018 is Rs. 2970.3 crore, which is 34.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

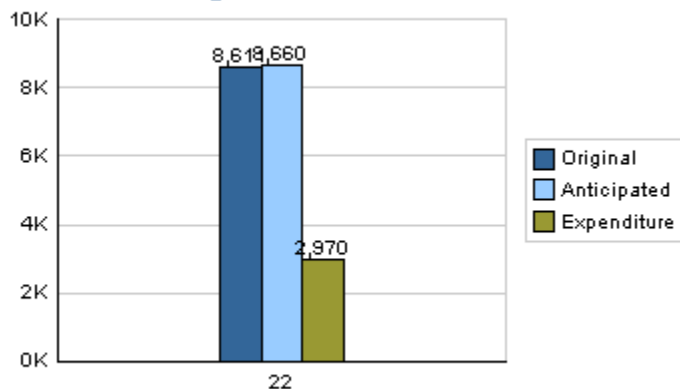

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

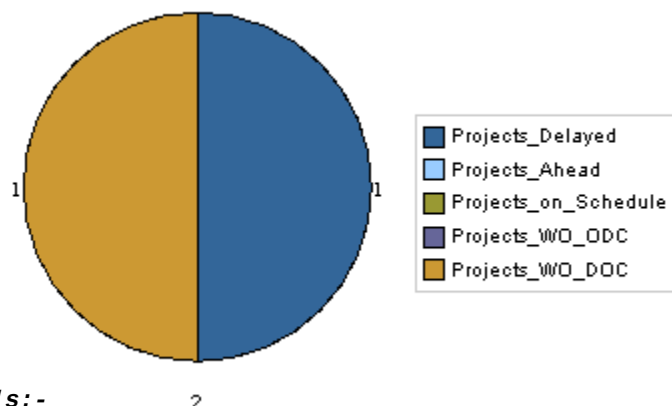


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5381.3 crore implying a cost overrun of 64.5%. The expenditure incurred on these projects till September, 2018 is Rs. 2450.86 crore, which is 45.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

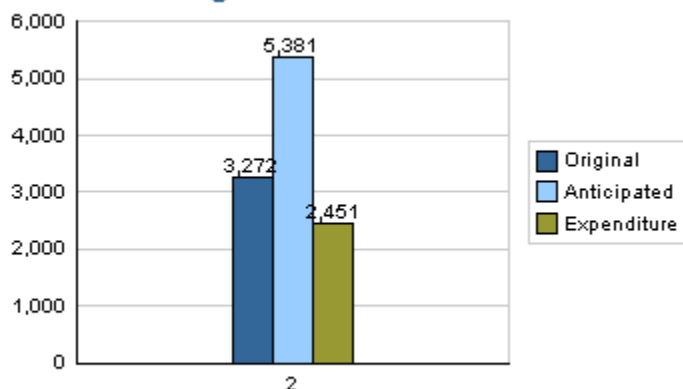

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	375
Number of Projects On Schedule	102
Number of Projects Delayed	94
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	147

Brief Analysis

Project Status with respect to Original Schedule: Out of 375 projects, 5 projects are ahead of schedule, 102 projects are on schedule 94 projects are delayed. 147 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

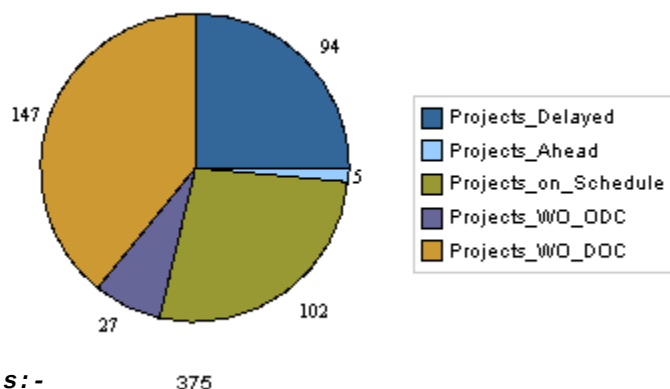


Total No Of Project's:-

375

Investment Scenario

Total original cost of implementation of 375 projects when sanctioned, was of the order of Rs. 478359.05 crore but this was subsequently anticipated to Rs. 725343.31 crore implying a cost overrun of 51.6%. The expenditure incurred on these projects till September, 2018 is Rs. 172361.85 crore, which is 23.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

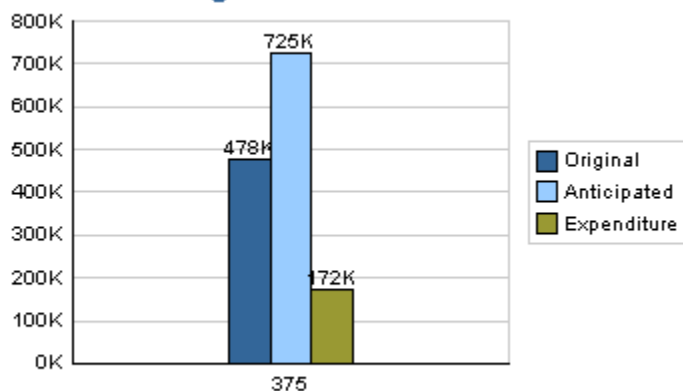

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	574
Number of Projects On Schedule	81
Number of Projects Delayed	90
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	33
Number of Projects Without Date Of Commissioning	368

Brief Analysis

Project Status with respect to Original Schedule: Out of 574 projects, 2 projects are ahead of schedule, 81 projects are on schedule 90 projects are delayed. 368 projects do not have fixed dates of commissioning. 33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

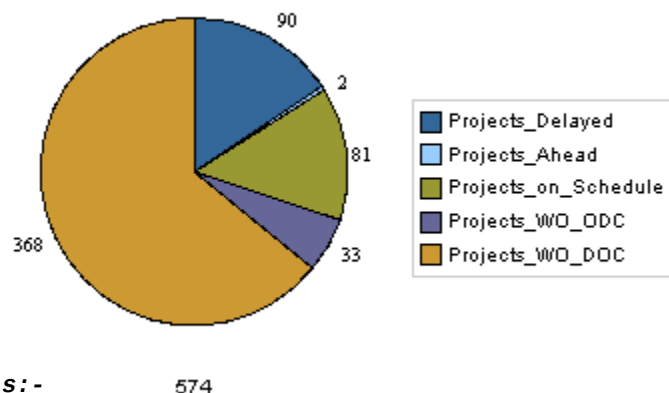


Total No Of Project's:-

574

Investment Scenario

Total original cost of implementation of 574 projects when sanctioned, was of the order of Rs. 386925.98 crore but this was subsequently anticipated to Rs. 401159.04 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till September, 2018 is Rs. 132643.89 crore, which is 33.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

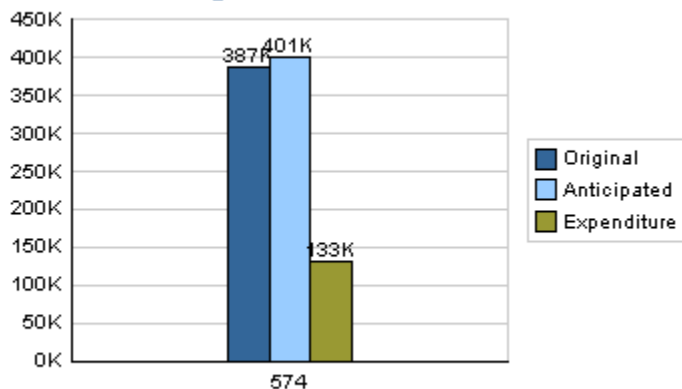

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	5
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

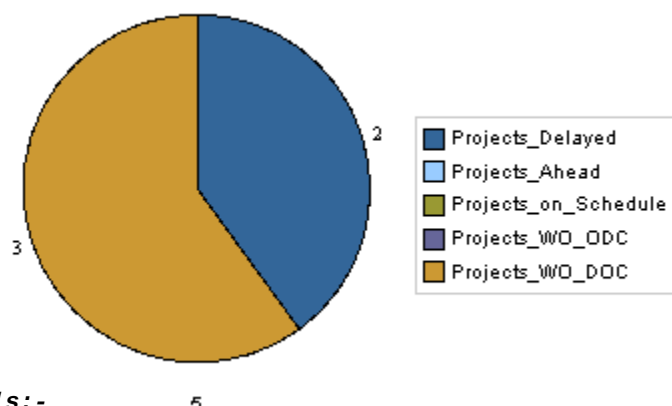


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 3788.29 crore but this was subsequently anticipated to Rs. 4230.74 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till September, 2018 is Rs. 1659.56 crore, which is 39.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

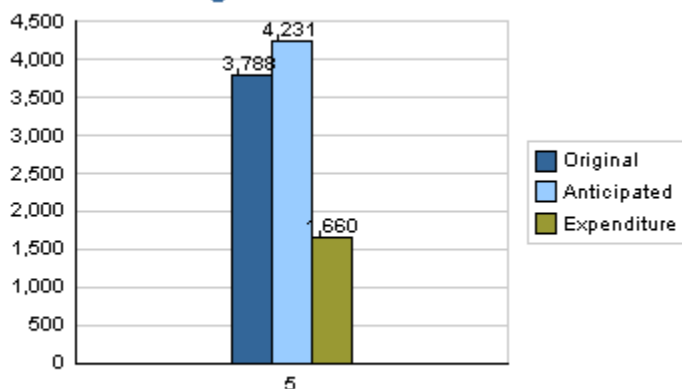

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	10
Number of Projects On Schedule	1
Number of Projects Delayed	7

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 10 projects, 1 project is on schedule 7 projects are delayed. 2 projects do not have fixed dates of commissioning.

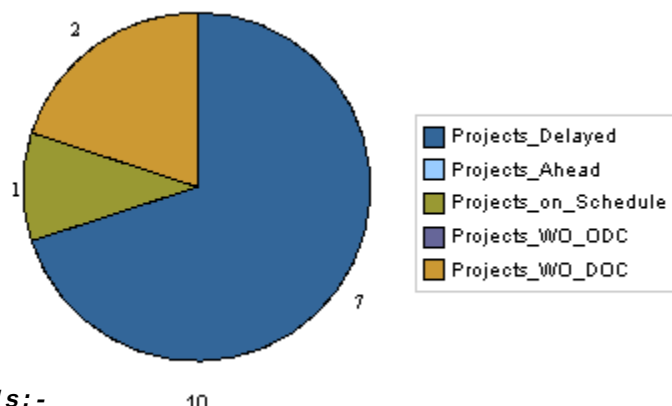


Total No Of Project's:-

10

Investment Scenario

Total original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 17191.2 crore but this was subsequently anticipated to Rs. 28420 crore implying a cost overrun of 65.3%. The expenditure incurred on these projects till September, 2018 is Rs. 9126.9 crore, which is 32.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

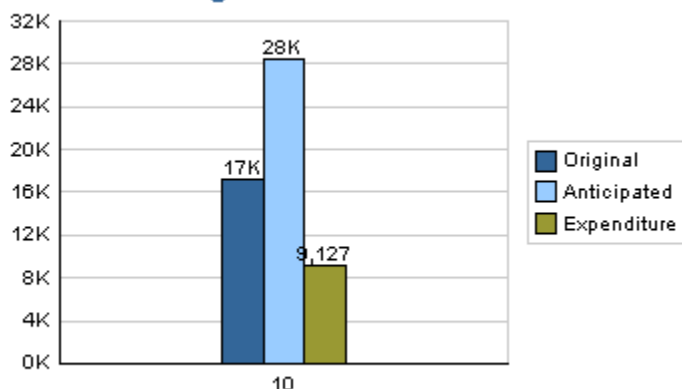

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	61
Number of Projects On Schedule	12
Number of Projects Delayed	25
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	23

Brief Analysis

Project Status with respect to Original Schedule: Out of 61 projects, 1 project is ahead of schedule, 12 projects are on schedule 25 projects are delayed. 23 projects do not have fixed dates of commissioning.

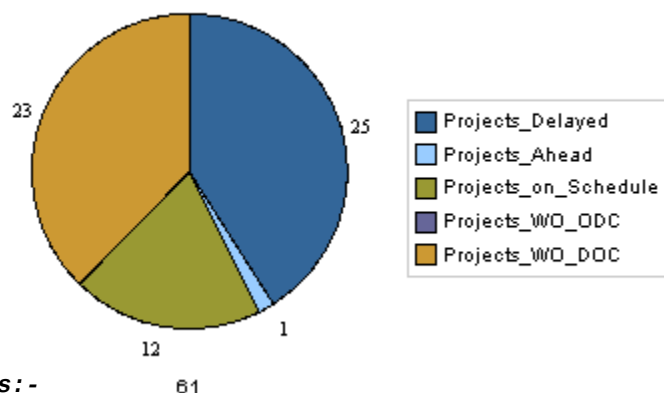


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 61 projects when sanctioned, was of the order of Rs. 171744.4 crore but this was subsequently anticipated to Rs. 179453.64 crore implying a cost overrun of 4.5%. The expenditure incurred on these projects till September, 2018 is Rs. 73603.22 crore, which is 41% of the anticipated cost of the projects.

Figures are in Rs. Crore

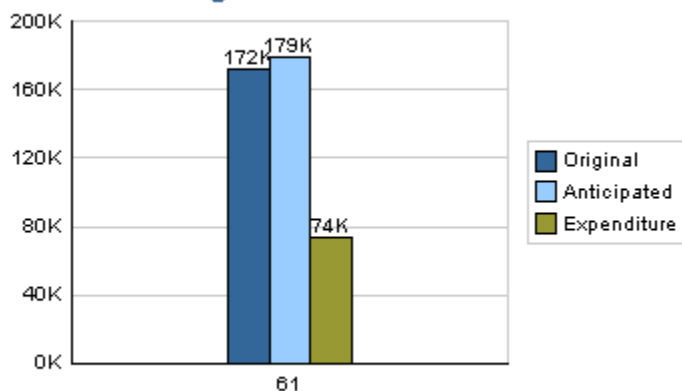

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.




Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 461.66 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till September, 2018 is Rs. 124.07 crore, which is 26.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

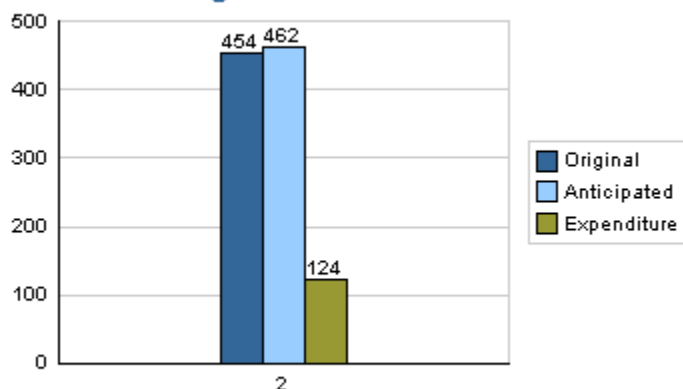

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (SEPTEMBER 2018)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	6	1,889.87	2,016.59	85.79
2	ANDHRA PRADESH	67	1,06,162.46	1,10,244.37	14,656.38
3	ARUNACHAL PRADESH	31	16,421.02	33,547.53	17,473.76
4	ASSAM	47	31,336.57	40,105	22,824.1
5	BIHAR	90	75,487.5	1,12,167.59	50,336.24
6	CHHATISGARH	44	76,704.81	83,784.6	35,281.43
7	D & N HAVELI	1	6,086.08	5,842.31	4,231.37
8	DELHI	23	56,043.88	63,419.24	40,620.48
9	GOA	10	4,292.52	4,300.54	222.28
10	GUJARAT	52	62,135.82	73,481.22	33,589.15
11	HARYANA	22	16,967.58	18,880.24	9,217.91
12	HIMACHAL PRADESH	12	14,659.32	26,087.65	9,539.73
13	JAMMU AND KASHMIR	10	25,238.37	51,232.67	28,190.21
14	JHARKHAND	49	46,809.17	50,840.74	18,808.02
15	KARNATAKA	46	82,148.9	87,206.53	30,050.08
16	KERALA	22	25,879.48	28,054.1	4,639.78
17	MADHYA PRADESH	62	69,052.01	78,734.42	28,397.44
18	MAHARASHTRA	130	1,87,818.64	1,99,946.17	68,889.15
19	MANIPUR	2	4,670.86	14,025.69	7,971.05
20	MEGHALAYA	7	4,484.97	9,578.51	1,177.24
21	MIZORAM	4	3,406.61	5,613.14	2,449.15
22	MULTI STATE	170	3,45,958.11	4,60,717.93	1,32,745.95
23	NAGALAND	21	13,711.07	14,384.55	655.38
24	ODISHA	81	91,616.58	97,021.18	28,895.9
25	PUNJAB	32	17,169.94	17,175.67	3,816.75
26	RAJASTHAN	56	44,581.43	47,282.81	23,544.52
27	SIKKIM	10	3,786.19	6,834.56	982.51
28	TAMIL NADU	70	1,15,478.79	1,33,318.11	61,108.91
29	TELANGANA	39	31,759.07	35,867.19	8,986.66
30	TRIPURA	9	4,422.36	8,312.05	6,150.45
31	UTTAR PRADESH	109	1,27,439	1,31,279.91	48,588.14
32	UTTARAKHAND	28	33,689.4	39,554.65	10,262.41
33	WEST BENGAL	58	58,359.34	72,814.63	29,114.68
TOTAL		1,420	18,05,667.72	21,63,672.09	7,83,503

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

ATOMIC ENERGY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	3492	5677	5687.52
CIVIL AVIATION						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	546.69
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
3	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	259.4	-	266.38
4	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	457.77	-	581.54
5	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	264.26
6	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	234.48
7	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	418.97	-	477.74
8	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	198.68	-	254.72
HEALTH AND FAMILY WELFARE						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	204.44	-	237.8
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	168.9	-	191.38
11	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	HSCC	07/2016	312.99	-	469
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	1718	-	2289
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1549.85
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	871.35	-	961

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
15	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	7058.21
16	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	10295.43
17	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	2496.9	6179.96	6788.96
18	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3666.44
19	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	421.01	-	963.23
20	KUDGI STPP STAGE 1	NTPC	01/2012	15166.19	-	15364
21	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	499.77
22	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	955	-	1190.3
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
23	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
24	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	124.43	926.23	1018.51
25	AMRAVATI-NARKHER NL (CR)	CR	06/1994	663.01	668.34	715.32
26	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.3
27	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	511.86	-	967.96
28	NANGALDAM-TALWARA (NL), NR	NR	03/1981	450	-	968.28
29	KARUR-SALEM (NL), SR	SR	02/1997	155.55	-	856.94
30	NANDYAL-YERRAGUNTLA (NL), SCR	SCR	03/1996	164.36	164.36	999.64
31	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	3230.02	4857	5224.22
32	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
33	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	324.73	335.77	876.49
34	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
35	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	792.46	-	928.5
36	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	-	751.05

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
37	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
38	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	625.3	408.76	841.57
39	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	303.98	-	1292.55
40	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.87
41	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	1180.19	-	3036.52
42	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	1049.69	-	3544.3
43	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	614.25	-	841.36
44	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	584.41	-	1069.44
45	JIND-SONEPAT (NL), NR	NR	01/2004	238.56	-	722.65
46	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	1185.64	-	1277.02
47	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	4454.17	-	7919.05
48	KOSI BRIDGE (NL), ECR	ECR	04/2002	499.41	-	640.78
49	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	424.6	727.13	898.83
50	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	361.13
51	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	120	-	210.67
52	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	274.46
53	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	370.38
54	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	477.88	283.95	495.4
55	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	261.7	-	388.06
56	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	732.81	-	1863.44
57	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	383.54	-	564.3
58	MAYLADUTHURAI - THIRUVARUR -KARAIKUDI -THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	724.69	-	1129.33

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
59	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1049.68
60	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	385.2	-	538.17
61	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	532.87	-	928.89
62	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	369.9	-	618.19
63	BARDHAMAN-KATWA (GC)	ER	04/2007	501.78	-	724.3
64	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	1142	1942	3015.98
65	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	653.19	-	756.73
66	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	-	264.57
67	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	207.52	-	334.76
68	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
69	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	443.26
70	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	259.93
71	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	242.09	-	248.23
72	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	-	485.03
73	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.73	-	253.1
74	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	468.18
75	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	283.55	-	457.51
76	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	342.85	427.92
77	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	819.23	-	1082.01
78	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	314	-	595.01
79	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	246.07	-	264.69
80	PIRPAINTI-BHAGALPUR	ER	04/2011	261.38	-	343.42
81	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	136.55	-	143.74

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
82	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	423.66	-	529.28
83	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	184.06	199.12	219.77
84	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	ER	04/2011	166.89	-	246
85	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	155.81	-	180.78
86	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
87	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	927.01	-	939.56
88	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	758.09	-	814.23
89	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	SR	02/2000	200.84	-	394.26
90	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	268.87	-	304.07
91	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	SR	02/2005	600	600	671
92	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	SR	02/2005	241	-	295.12
93	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	NER	04/1997	233	-	317.61
94	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	609.04	1063	1793.99
95	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	180.82	-	462.75
96	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	329.39	-	759.2

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
97	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	410.32
98	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	209.8
99	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	268.94
100	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	195.35
101	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	200	-	245.83
102	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	312.79
103	NALBARI T BIJNI (AS-7)	NHAI	12/2003	208	-	297.81

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
104	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	198.82
105	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	340.12
106	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	-	389.08
107	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	1509.1	-	3176.22
108	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	1693.75	-	2675.28
109	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	1108	-	3869.3
110	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	1175	-	1209.67
111	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2159.63
112	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2042.82
113	INDORE-DEWAS(NH-3)	NHAI	11/2010	325	-	469.54
114	NASHRI- CHANANI	NHAI	05/2011	2159	-	3986.82
115	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2393.99
116	PATNA-MUZZAFFARPUR	NHAI	08/2010	671.3	-	883.96
117	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
118	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1948.72
119	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.17
120	KANDLA - MUNDRA PORT	NHAI	01/2011	953.88	-	974.83
121	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	582.52
122	JORBAT - BARAPANI	NHAI	01/2011	536	-	674.52
123	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	2993.77
124	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	574	-	898.99
125	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	375.09	-	494.33

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
126	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	575	-	823.46
127	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	511.54	-	563.48
128	SRINAGAR TO BANIHAL	NHAI	06/2011	1100.7	-	1216.15
129	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	1555.96
130	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1363.43
131	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2310.6
132	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	998.79	-	1822.7
133	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1613.62
134	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2614.84
135	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	414.14
136	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1898.25
137	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	2125.24	-	4659.71
138	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	2294.94
139	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	3386.77
140	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1407.12
141	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	420.32
142	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	495.78	-	595.31
143	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	530.07	-	556.02
144	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	NHAI	09/2015	785.78	-	839.63
145	6 LANING OF AGRA - ETAWAH BYPASS	NHAI	07/2015	1657.2	-	1910
146	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1302.48
147	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	611.65	-	660.22
148	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(SEPTEMBER 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
149	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3079.44
150	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	1055	-	1328.85
151	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	2263.5
152	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2056.03
153	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	1836.44
154	TRICHY - KARUR	NHAI	03/2007	516	-	627.37
155	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	NHAI	01/2016	701.12	-	841.92
156	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	605.84	-	722.46

SHIPPING AND PORTS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
157	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	411.12
158	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	KPL	02/2015	244.5	258	275.98

URBAN DEVELOPMENT

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
159	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
160	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64
161	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	241.33	-	307.5
162	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	14600	-	16352.77

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	568.10	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	619.33	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52	247.52	131.32	02/2019 -	12/2018
5	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00	356.00	169.04	05/2019 -	12/2018
6	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	.98	09/2022 -	06/2021
7	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	333.63	12/2020 -	02/2020
	Total		14,380.92 -	13,499.52	2,017.37		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
8	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	88.01	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
9	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019
10	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	18.38	12/2021 -	03/2021
	<u>North Western Railway</u>						
11	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	113.46	12/2019 -	06/2019
12	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	4/2013	420.18 295.02	865.00	65.19	03/2020 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
13	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.22	12/2025 -	03/2025
	<u>South Central Railway</u>						
14	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	4/2012	1,856.95 1,856.95	1,955.27	225.85	03/2023 03/2024	03/2023

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
15	GUNTUR-GUNTAKAL - [N22000368]	4/2016	3,631.00 -	3,631.00	99.11	03/2022 03/2023	03/2022
	Total		8,970.49 -	11,857.83	3,626.20		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
16	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	86.95	03/2020 -	05/2019
17	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	10.57	03/2020 -	06/2019
	Total		461.69 -	426.16	97.52		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
18	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020
	Total		150.29 -	150.29	2.58		
	Grand Total		23,963.39	25,933.80	5,743.67		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	196.02	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	296.10	03/2022 -	03/2022
4	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
5	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	-	08/2019 -	08/2019
6	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.27	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
7	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	413.85	03/2021 -	03/2021
8	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	689.20	03/2026 -	03/2026
	<u>Neyveli Lignite Corporation</u>						
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	3,072.20	11/2021 -	11/2021
10	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	8.71	09/2019 -	09/2019
11	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	173.06	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
12	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022
13	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	196.70	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
14	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 -	03/2019
15	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
16	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
17	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.27	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.90	03/2023 -	03/2023
19	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
20	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.74	03/2023 -	03/2023
21	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
22	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.06	03/2023 -	03/2023
23	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	68.52	03/2022 -	03/2022
24	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
25	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,881.64	03/2023 -	03/2023
26	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,834.56	03/2023 -	03/2023
27	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	54.71	03/2020 -	03/2020
28	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	-	03/2026 -	03/2026
29	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	56.54	03/2020 -	03/2020
30	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.27	03/2021 -	03/2021
31	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
32	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.06	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
33	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
34	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	88.13	03/2021 -	03/2021
35	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
36	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	389.77	03/2020 -	03/2020
37	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	257.35	03/2020 -	03/2020
38	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
39	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	93.19	03/2023 02/2017	03/2023
40	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
41	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	102.75	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	179.06	03/2020 -	03/2020
43	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.28	03/2021 -	03/2021
44	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	236.37	03/2025 -	03/2025
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	16.21	03/2022 -	03/2022
46	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	22.07	03/2021 -	03/2021
47	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	82.13	03/2021 -	03/2021
48	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
49	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	52.83	03/2020 -	03/2020
50	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	128.93	03/2019 -	03/2019
	Total		69,093.96 -	69,361.83	12,725.51		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
51	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	49.95	08/2020 -	08/2020
	Total		285.95 -	291.29	49.95		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	28.31	11/2019 -	11/2019
53	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	23.51	11/2019 -	11/2019
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	24.50	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
55	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	23.29	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	99.61		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
56	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	276.91	06/2020 -	06/2020
57	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
58	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
	<u>Hospital Services Consultancy Corporation</u>						
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	76.88	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
60	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	214.62	09/2018 -	09/2018
61	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	71.50	03/2019 -	03/2019
62	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	122.66	03/2019 -	03/2019
	Total		3,508.53 -	3,508.53	975.92		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
63	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	300.68	01/2020 01/2020	01/2020
64	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 11/2020	11/2020
65	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	95.59	04/2021 04/2021	04/2021
66	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	428.19		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
67	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	88.38	01/2019 -	01/2019
68	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	105.67	02/2020 -	02/2020
69	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	110.72	12/2019 -	12/2019
70	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
71	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	14.96	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
72	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	48.20	08/2020 -	08/2020
	<u>Chennai Petroleum Corporation Limited</u>						
73	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	11.79	08/2020 -	08/2020
74	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	465.00	12/2019 -	12/2019
	<u>Gas Authority Of India Limited</u>						
75	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	19.08	10/2022 -	10/2022
76	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1.03	12/2021 -	12/2021
77	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	568.10	12/2019 12/2020	12/2019
78	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	611.91	12/2020 -	12/2020
79	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	12.65	07/2022 -	07/2022
80	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	800.00	577.39	12/2018 -	12/2018
81	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	17.48	12/2020 -	12/2020
82	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	29.47	07/2022 -	07/2022
83	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	682.57	02/2020 -	02/2020
84	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	89.65	04/2022 -	04/2022
85	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	597.57	12/2020 -	12/2020
86	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	2,212.79	12/2018 -	12/2018
87	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	18.64	10/2022 -	10/2022
88	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	24.18	10/2022 -	10/2022
89	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	448.61	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
90	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	78.89	02/2019 -	02/2019
91	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	3.60	11/2020 11/2020	11/2020
92	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
93	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	199.63	09/2019 -	09/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
94	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
95	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	40.68	03/2021 -	03/2021
96	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
97	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	855.11	06/2020 -	06/2020
98	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 04/2021	04/2021
	<u>Indian Oil Corporation Limited</u>						
99	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	1.51	12/2021 -	12/2021
100	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,018.23	09/2019 -	09/2019
101	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	33.57	12/2019 -	12/2019
102	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	0.17	06/2020 -	06/2020
103	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
104	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	78.63	06/2020 -	06/2020
105	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
106	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020
107	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
108	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
109	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
110	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	306.51	12/2020 -	12/2020
111	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	475.41	08/2021 -	08/2021
112	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	190.66	08/2019 -	08/2019
113	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
114	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	-	01/2021 -	01/2021
116	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,098.69	11/2019 -	11/2019
117	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	24.22	02/2020 -	02/2020
118	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	59.66	07/2020 -	07/2020
119	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.08	01/2021 -	01/2021
120	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	712.49	11/2018 -	11/2018
121	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	241.91	09/2019 -	09/2019
122	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	25.21	04/2021 -	04/2021
123	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.09	08/2020 -	08/2020
124	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	168.63	09/2019 -	09/2019
125	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
126	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	32.34	04/2020 -	04/2020
127	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	122.32	08/2020 -	08/2020
128	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	0.12	02/2020 -	02/2020
129	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	74.43	09/2019 -	09/2019
130	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
131	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	-	08/2020 -	08/2020
132	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	232.84	01/2019 -	01/2019
133	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	711.29	09/2019 -	09/2019
134	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	1.47	12/2021 -	12/2021
135	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	4,807.08 -	4,807.08	19.10	07/2021 -	07/2021
136	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	475.64	10/2019 -	10/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
137	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
138	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
139	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	111.05	03/2019 -	03/2019
140	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
141	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
142	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	98.07	05/2020 05/2020	05/2020
143	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	570.63	05/2021 05/2021	05/2021
144	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	299.26	05/2019 05/2019	05/2019
145	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	78.15	11/2019 11/2019	11/2019
146	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	-	12/2019 -	12/2019
147	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	269.97	03/2026 03/2026	03/2026
148	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	302.59	11/2019 11/2019	11/2019
149	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	102.53	11/2019 11/2019	11/2019
	<u>Oil India Limited</u>						
150	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	18.56	10/2020 -	10/2020
151	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	13.06	12/2019 -	12/2019
152	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	1.65	02/2020 -	02/2020
	Total		1,02,384.59 -	1,00,326.05	16,892.07		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
153	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,218.88	11/2019 -	11/2019
154	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	5,809.85	09/2019 -	09/2019
	<u>Power Grid Corporation Of India Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
155	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	55.10	02/2020 -	02/2020
156	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	552.21	04/2020 -	04/2020
157	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	3,710.05	11/2019 -	11/2019
158	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	197.76	02/2019 -	02/2019
159	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	50.27	07/2019 -	07/2019
160	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,591.63	04/2019 -	04/2019
161	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	481.12	07/2020 -	07/2020
162	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
163	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	26.40	03/2019 -	03/2019
164	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	743.82	01/2019 -	01/2019
165	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	502.54	06/2019 -	06/2019
166	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	375.34	11/2018 -	11/2018
167	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	516.25	10/2018 -	10/2018
168	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	2.50	06/2019 -	06/2019
169	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	25.85	11/2019 -	11/2019
170	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,861.40	05/2019 -	05/2019
171	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	22.42	03/2019 -	03/2019
172	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	321.99	02/2020 -	02/2020
173	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	354.00	04/2019 -	04/2019
174	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	103.28	02/2019 -	02/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
175	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244	2/2017	235.53 -	235.53	20.09	06/2019 -	06/2019
176	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223	4/2016	844.64 -	844.64	303.70	04/2019 -	04/2019
177	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230	7/2016	333.17 -	333.17	250.73	03/2019 -	03/2019
178	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231	8/2016	431.89 -	431.89	191.76	02/2019 -	02/2019
179	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236	3/2017	251.60 -	251.60	79.31	06/2019 -	06/2019
180	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232	8/2016	177.52 -	177.52	76.98	02/2019 -	02/2019
181	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246	2/2017	204.12 -	204.12	89.17	09/2019 -	09/2019
182	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248	3/2017	337.75 -	337.75	16.10	06/2019 -	06/2019
183	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228	7/2016	300.94 -	300.94	194.26	12/2018 -	12/2018
184	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245	3/2017	379.95 -	379.95	21.82	12/2019 -	12/2019
185	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224	5/2016	167.01 -	167.01	97.53	11/2018 -	11/2018
	<u>Satluj Jal Vidyut Nigam Limited</u>						
186	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	118.79	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
187	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	2,104.21	62.71	09/2020 -	09/2020
	Total		58,783.60 -	60,062.12	21,045.61		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
188	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250	4/2012	540.02 -	540.02	152.67	03/2022 -	03/2022
189	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	240.00	219.77	03/2019 -	03/2019
190	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	8,857.98	-	03/2024 -	03/2024
191	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
192	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	1.05	03/2023 -	03/2023
193	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	2/2015	1,272.19 -	1,272.19	109.03	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
194	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	937.42	03/2023 -	03/2023
195	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	1,759.34	03/2021 -	03/2021
196	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	4,817.69	148.42	03/2024 -	03/2024
197	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	77.75	03/2023 -	03/2023
198	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	267.58	03/2021 -	03/2021
199	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	2/2016	1,035.16 -	1,035.16	12.96	03/2022 -	03/2022
200	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
201	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	24.71	03/2022 -	03/2022
	<u>Container Corporation Of India</u>						
202	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	251.08	03/2019 -	03/2019
203	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	243.30	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
204	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
205	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
206	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	163.03	03/2022 -	03/2022
207	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	77.20	03/2022 -	03/2022
208	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	183.12	03/2022 -	03/2022
209	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
210	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
211	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,143.60 -	1,160.83	566.17	03/2020 -	03/2020
	<u>Eastern Railways</u>						
212	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	4/2000	614.25 -	2,532.49	841.36	03/2019 12/2009	03/2019
213	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	2,142.49	291.74	03/2022 -	03/2022
214	HANSIDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	693.90	310.26	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
215	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]	4/2010	157.94 -	157.94	50.50	11/2018 -	11/2018
	<u>North Central Railway</u>						
216	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
217	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
	<u>North East Frontier Railway</u>						
218	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	163.08	03/2021 -	03/2021
219	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	259.43	03/2021 -	03/2021
220	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	457.51	03/2019 -	03/2019
221	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
222	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	64.09	03/2020 -	03/2020
223	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
224	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	264.69	03/2019 -	03/2019
225	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	123.11	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
226	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	871.56	97.82	12/2021 -	12/2021
227	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	-	01/2022 -	01/2022
228	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
229	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	718.54	274.46	12/2022 -	12/2022
230	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	174.83	01/2019 -	01/2019
231	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	81.15	03/2022 -	03/2022
	<u>North Western Railway</u>						
232	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	171.82	11/2019 -	11/2019
233	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	349.00	248.23	02/2019 -	02/2019
234	PHULERA - DIGANA DOUBLING - [N22000326]	5/2015	600.00 -	685.99	3.38	03/2020 -	03/2020
235	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	294.90	157.63	10/2018 -	10/2018
236	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	795.01	437.03	02/2019 -	02/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
237	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	-	08/2022 -	08/2022
	<u>Northern Railway</u>						
238	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
239	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	550.04	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
240	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
241	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	197.87	12/2024 -	12/2024
242	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	704.64	12/2021 -	12/2021
243	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	243.95	12/2024 -	12/2024
244	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	1,046.88 -	7,000.00	212.83	12/2026 -	12/2026
245	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	943.60 -	943.60	102.17	03/2022 -	03/2022
246	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	812.47	12/2020 -	12/2020
247	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,510.51	03/2020 -	03/2020
248	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	814.23	03/2020 -	03/2020
249	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	81.99	03/2021 -	03/2021
250	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	92.48	12/2023 -	12/2023
251	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,127.00	1,059.52	03/2023 -	03/2023
252	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	16,216.00 -	16,216.00	893.22	12/2024 -	12/2024
253	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.92 -	1,765.92	228.15	03/2023 -	03/2023
254	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	975.62	573.13	12/2021 -	12/2021
	<u>South Central Railway</u>						
255	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	343.70	03/2021 -	03/2021
256	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	4/2012	1,856.95 -	1,955.27	225.85	03/2023 03/2024	03/2023
257	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
258	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	119.69	03/2020 03/2020	03/2020
259	GUNTUR-GUNTAKAL - [N22000368]	4/2016	3,631.00 -	3,631.00	99.11	03/2022 03/2023	03/2022
	<u>South East Central Railway</u>						
260	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
261	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019
262	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	543.00 -	543.00	-	03/2022 -	03/2022
263	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
264	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
265	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
266	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
267	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
268	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
269	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	4/2013	3,055.00 -	3,055.00	600.00	09/2018 -	09/2018
	<u>South Eastern Railway</u>						
270	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	4/1998	1,027.40 -	2,373.00	481.65	03/2022 -	03/2022
271	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	140.51	03/2021 03/2021	03/2021
272	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.48	12/2021 12/2021	12/2021
	<u>South Western Railway</u>						
273	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	439.87	03/2020 11/2015	03/2020
	<u>Southern Railway</u>						
274	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	980.00	1,292.55	03/2020 -	03/2020
275	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	1,800.00	103.10	03/2019 -	03/2019
276	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
277	ATTIPPATTU PUTTUR - [N22000184]	4/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019
278	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,072.50	1,129.33	02/2019 -	02/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
279	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
	<u>West Central Railway</u>						
280	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
281	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
282	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
	<u>Western Railway</u>						
283	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	599.20	03/2022 03/2019	03/2022
284	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	202.09	03/2021 03/2019	03/2021
285	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	551.51	257.05	03/2019 -	03/2019
286	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	593.72	03/2022 03/2019	03/2022
287	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	5,554.24	1,047.53	03/2022 03/2019	03/2022
288	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	2,783.00	444.72	03/2020 03/2020	03/2020
289	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,037.15	882.80	03/2021 03/2020	03/2021
	Total		2,73,180.84 -	3,52,522.52	52,706.26		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
290	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]	11/2017	232.81 -	232.81	-	11/2019 -	11/2019
291	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	-	02/2020 -	02/2020
292	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	-	12/2019 -	12/2019
293	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
294	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	-	12/2019 -	12/2019
295	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]	6/2017	282.08 -	282.08	-	06/2019 -	06/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
296	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	284.00	-	11/2019 -	11/2019
297	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
298	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	-	11/2019 -	11/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
299	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763	3/2018	215.79 -	215.79	-	09/2018 -	09/2018
300	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761	3/2018	282.98 -	282.98	-	09/2018 -	09/2018
301	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755	3/2018	239.30 -	239.30	-	09/2018 -	09/2018
302	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756	3/2018	285.68 -	285.68	-	09/2018 -	09/2018
303	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
304	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748	2/2018	391.00 -	391.00	-	10/2018 -	10/2018
305	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760	3/2018	251.97 -	251.97	-	09/2018 -	09/2018
306	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749	3/2018	234.27 -	234.27	-	10/2018 -	10/2018
307	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759	3/2018	237.72 -	237.72	-	09/2018 -	09/2018
308	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753	3/2018	500.09 -	500.09	-	09/2018 -	09/2018
309	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762	3/2018	215.12 -	215.12	-	09/2018 -	09/2018
310	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765	3/2018	323.98 -	323.98	-	09/2018 -	09/2018
311	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757	3/2018	315.03 -	315.03	-	09/2018 -	09/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
312	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
313	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
314	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
315	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
316	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
317	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
318	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]	3/2018	240.64 -	240.64	-	09/2018 -	09/2018
319	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]	3/2018	272.89 -	272.89	-	09/2018 -	09/2018
320	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]	3/2015	262.97 -	262.97	-	10/2018 -	10/2018
321	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]	3/2018	339.57 -	339.57	-	09/2018 -	09/2018
322	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]	2/2017	387.00 -	387.00	-	09/2018 -	09/2018
<u>National Highways Authority Of India</u>							
323	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	1,041.10	138.78	04/2019 -	04/2019
324	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	18.36	02/2019 -	02/2019
325	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	87.19	07/2019 -	07/2019
326	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
327	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
328	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
329	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	5.00	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
330	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	950.69	277.34	08/2019 -	08/2019
331	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
332	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541	1/2016	1,081.57 -	1,081.57	708.59	06/2019 -	06/2019
333	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
334	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	3/2016	1,587.49 -	1,587.49	110.58	04/2019 -	04/2019
335	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
336	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	234.18	04/2020 -	04/2020
337	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630	11/2016	446.17 -	446.17	-	03/2019 -	03/2019
338	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
339	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
340	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545	1/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018
341	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	1,167.42	191.05	03/2019 -	03/2019
342	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439	7/2015	1,885.74 -	1,885.74	-	05/2019 -	05/2019
343	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
344	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
345	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	162.60	04/2019 -	04/2019
346	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	1,910.00	01/2019 -	01/2019
347	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505	6/2015	1,583.79 -	1,583.79	392.08	01/2019 -	01/2019
348	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553	3/2016	229.37 -	229.37	6.39	11/2018 -	11/2018
349	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
350	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
351	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	301.30	04/2019 -	04/2019
352	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]	7/2016	331.46 -	331.46	232.15	10/2018 -	10/2018
353	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
354	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	738.75	03/2020 -	03/2020
355	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
356	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	72.07	09/2019 -	09/2019
357	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
358	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]	1/2017	244.90 -	244.90	51.51	05/2019 -	05/2019
359	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
360	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	2/2016	997.15 -	997.15	328.14	03/2019 -	03/2019
361	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
362	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
363	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	21.98	03/2020 -	03/2020
364	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]	8/2016	227.49 -	227.49	-	01/2019 -	01/2019
365	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	41.20	03/2019 -	03/2019
366	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	237.07	07/2019 -	07/2019
367	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]	1/2016	701.12 -	701.12	841.92	05/2019 -	05/2019
368	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]	8/2016	320.30 -	320.30	174.91	01/2019 -	01/2019
369	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]	8/2016	248.97 -	248.97	-	05/2019 -	05/2019
370	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	409.11	04/2019 -	04/2019
	Total		61,123.50 -	61,664.75	7,927.84		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
371	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	2,907.00	29.51	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
372	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	63.54	06/2019 -	06/2019
	Total		1,080.87 -	3,169.87	93.05		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
373	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	231.80	39.75	10/2018 10/2018	10/2018
	Total		231.80 -	231.80	39.75		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
374	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]	1/2018	206.58 -	206.58	0.02	03/2019 -	03/2019
375	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020
376	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	1.84	11/2019 -	11/2019
377	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	6.61	03/2020 -	03/2020
378	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	0.36	05/2020 -	05/2020
379	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	55.43	06/2019 -	06/2019
380	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
381	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	209.00	52.00	10/2019 -	10/2019
382	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]	1/2018	430.00 -	430.00	-	09/2018 -	09/2018
	<u>Lucknow Metro Rail Corporation Limited</u>						
383	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
384	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	1,793.83	11/2021 -	11/2021
	<u>National Building Construcion Corporation Ltd</u>						
385	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,376.53	11/2019 -	11/2019
	Total		24,687.89 -	24,863.12	7,825.97		
	Grand Total		6,02,374.81	6,84,015.16	1,20,809.73		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
	Total		14,951.00 -	22,680.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	-	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
5	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	759.19	06/2017 -	12/2017	10.46
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
9	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
13	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
	Total		19,751.90 -	21,082.91			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
14	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	170.37	05/2018 -	08/2018	1.60
15	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	08/2020 -	08/2020	1.87
	Total		453.64 -	461.66			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
16	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
17	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.38	05/2017 -	-	13.31
18	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
19	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	07/2016	312.99 -	322.00	08/2018 -	-	2.88
	Total		987.47 -	1,036.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
20	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Bharat Petroleum Corporation Limited</u>						
21	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33
	<u>Hindustan Petroleum Corporation Limited</u>						
22	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50
23	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
24	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
25	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
26	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	10/2018	45.67
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
28	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
29	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
30	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,577.15	05/2013 -	03/2019	83.01
31	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
32	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
33	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						
34	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	03/2019	24.47
35	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		19,129.74 -	24,806.72			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
36	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69
37	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
38	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
39	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
40	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	10/2018	86.27
41	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
42	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
43	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
44	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
45	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65
46	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
47	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
48	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
49	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
50	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	12/2016	7.41
	<u>North East Electric Power Corporation</u>						
51	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51
52	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
53	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59
54	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14
55	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
56	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88 -	12/2012 -	11/2018	36.79
57	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41 -	04/2016 -	12/2018	38.61
58	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18 -	11/2016 -	06/2019	5.34
59	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42 -	03/2016 -	11/2018	32.69
60	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28 -	02/2016 -	11/2018	14.60
61	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88 -	03/2018 -	11/2018	26.82
62	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03 -	07/2017 -	06/2019	27.92
63	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10 -	11/2012 -	10/2018	36.01
64	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65 -	09/2014 -	10/2018	39.30
65	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46 -	06/2014 -	12/2018	31.17
66	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02 -	08/2014 -	12/2018	79.61
67	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,534.00 -	11/2008 -	12/2018	42.42
68	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27 -	12/2015 -	11/2018	26.86
69	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71 -	09/2017 -	09/2018	30.49
70	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30 -	06/2019 -	06/2019	.02
71	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97 -	12/2018 -	12/2019	92.28
72	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57 -	12/2018 -	12/2019	30.15
73	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00 -	12/2015 -	09/2018	42.83
74	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]	08/2008	771.00 -	1,624.00 -	02/2013 -	10/2018	110.64
	<u>Satluj Jal Vidyut Nigam Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
75	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
76	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75
77	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77
78	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,77,202.39 -	2,42,540.13			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
79	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	240.00	03/2019 -	03/2019	30.39
80	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44
81	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	29.55
82	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
83	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
84	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	4,817.69	03/2024 -	03/2024	32.81
85	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
86	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
87	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
88	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
89	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	- -	03/2021	192.42
90	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	- -	03/2023	290.95
91	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73
92	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
93	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
94	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2012 -	03/2020	3.33
95	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	-	323.32
96	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
97	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
98	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 -	1,474.47	- -	03/2021	296.21
99	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
100	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
101	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
102	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
103	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
104	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
105	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	- -	12/2018	192.15
106	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	- -	12/2021	71.96
<u>East Coast Railway</u>							
107	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
108	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	06/2021	29.71
109	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2020	38.43
110	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	03/2013	810.28 -	843.04	10/2020 -	03/2022	4.04
111	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,143.60 -	1,160.83	03/2020 -	03/2020	1.51
112	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
113	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	-	542.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
114	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
115	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	-	818.15
116	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.73 -	729.92	- -	03/2021	315.36
117	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	2,614.36	- -	03/2022	817.09
118	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
119	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	614.25 -	2,532.49	03/2019 12/2009	03/2019	312.29
120	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	584.41 -	1,005.23	02/2013 -	06/2016	72.01
121	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	501.78 -	1,960.06	12/2010 -	-	290.62
122	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	673.85	02/2012 -	-	159.66
123	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL [N22000228]	04/2010	136.55 -	534.24	03/2016 -	03/2020	291.24
124	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	528.34	03/2017 -	-	44.68
125	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
126	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.90	03/2020 -	03/2020	27.98
127	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL - [N22000240]	04/2010	115.27 -	857.30	03/2005 -	-	643.73
128	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	278.66 -	1,255.98	02/2012 -	-	350.72
129	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
130	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
131	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
132	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	193.08 -	683.88	12/2011 -	-	254.20
133	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
134	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	318.50 -	852.80	03/2006 -	-	167.76
135	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	23.56 -	1,330.73	- -	-	5,548.26
136	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
137	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,142.49	03/2022 -	03/2022	133.90
138	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
139	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	563.51 -	1,813.59	03/2016 -	-	221.84
140	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	236.21 -	1,395.63	03/2017 -	-	490.84
	<u>Metropolitan Rapid Transport Projects</u>						
141	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
142	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
143	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
144	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
145	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
146	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
147	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
148	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
	<u>North East Frontier Railway</u>						
149	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
150	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
151	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,600.00	03/2014 -	12/2020	92.19
152	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	3,230.02 -	5,820.00	04/2008 12/2011	12/2019	80.18

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
153	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266	04/2000	1,180.19 -	3,040.00	12/2008 -	12/2020	157.59
154	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2022	210.02
155	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
156	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2021	302.54
157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	3,000.00	03/2015 -	12/2021	28.95
158	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	1,142.00 -	3,374.00	03/2014 -	03/2019	195.45
159	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	1,300.00	- -	03/2020	289.50
160	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
161	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	726.00	- -	03/2020	227.88
162	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,733.20	03/2007 -	04/2016	93.65
163	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11
164	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198	04/2012	283.55 -	451.00	03/2019 -	03/2019	59.05
165	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
166	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
167	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	394.28	- -	-	63.25
168	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
169	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	- -	03/2018	128.39
170	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	551.00	03/2019 -	03/2020	75.48
171	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12
172	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390	04/2016	602.27 -	612.00	12/2021 -	03/2021	1.62
	<u>North Eastern Railway</u>						
173	MAHARAJGANJ-MASRAKH (NL) - NER - [N220100316	04/2003	218.19 -	413.56	06/2018 -	06/2018	89.54

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
174	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
175	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	12/2022 -	12/2022	212.37
176	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
177	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
178	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
179	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	871.56	12/2021 -	12/2021	257.52
180	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	- -	03/2018	142.44
181	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	08/2018	35.17
182	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2019	61.80
183	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
184	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
185	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16
186	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	12/2018	196.84
187	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
188	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	03/2022	18.56
	<u>North Western Railway</u>						
189	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	03/2019	70.85
190	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	02/2019	93.87
191	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	03/2020	14.33
192	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTHA KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
193	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55
194	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2019	41.64
195	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97	- -	-	38.23

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
196	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2018	24.47
197	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
198	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
199	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	865.00	03/2020 -	12/2019	105.86
200	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35
201	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	12/2018	19.86
202	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	02/2019	44.16
	<u>Northern Railway</u>						
203	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
204	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
205	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	12/2011 -	-	117.77
206	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
207	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
208	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
209	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96
210	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
211	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
212	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
213	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
214	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2019	55.57
215	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	188.58
216	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2018	48.26
217	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,850.00	03/2008 -	03/2019	152.45

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
218	BHANUPALI-BILASPUK BERI NL - [N22000273]	04/2008	1,046.88 -	7,000.00	12/2026 -	12/2026	568.65
219	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	2,062.20	- -	03/2022	112.52
220	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
221	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
224	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
225	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
226	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39
227	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
228	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	970.00	03/2020 -	03/2021	2.32
	<u>Railway Electrification</u>						
229	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
230	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
231	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
232	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,955.27	03/2023 -	03/2023	5.29
233	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	2,154.83	- -	-	133.40
234	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	761.37	- -	-	168.52
235	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
236	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	10/2018	538.84
237	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,501.83	03/2000 -	12/2023	103.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
238	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	815.00	- -	-	77.85
239	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,025.00	- -	03/2017	723.76
240	KONDAPALLI-KOTHAGUEDEM - [N22000364]	04/2013	616.08 -	723.00	- -	-	17.35
241	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE - GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	<u>South East Central Railway</u>						
242	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
243	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	04/2020 -	04/2020	243.06
244	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
245	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,420.39	02/2019 -	02/2019	142.42
246	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	403.00	12/2021 -	12/2021	75.98
247	CHHINDWARA-MANDLA FORT GC - [N22000481]	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22
248	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,279.00	12/2019 -	12/2019	46.67
249	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,919.00	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
250	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00	- -	12/2024	114.37
251	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	- -	03/2030	53.96
252	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
253	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
254	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41
255	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
256	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99
257	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
258	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
259	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81	12/2015 -	12/2018	69.92
260	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2018	41.36
261	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	- -	-	278.13
262	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
263	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
264	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
265	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	04/1998	1,027.40 -	2,373.00	03/2022 -	03/2022	130.97
<u>South Western Railway</u>							
266	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	12/2023	651.97
267	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
268	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
269	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	12/2023	2.29
270	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
271	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
272	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	958.00	03/2020 -	03/2022	11.34
273	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
<u>Southern Railway</u>							
274	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
275	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
276	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
277	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2019	185.98
278	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
279	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
280	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
281	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2020	222.39
282	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
283	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	02/2019	627.74
284	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
285	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
286	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
287	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
288	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
289	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
290	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	369.83	- -	-	92.90
291	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	03/2019	1,391.30
292	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	302.02	03/2005 -	-	12.33
293	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
294	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55 -	330.32	03/2009 -	-	65.53
295	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
296	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
297	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
298	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
<u>Western Railway</u>							
299	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,554.24	03/2022 -	03/2022	58.53

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
300	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
301	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	04/2008	1,389.62 -	2,446.85	03/2014 -	05/2018	76.08
302	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
303	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,783.00	03/2020 -	03/2020	235.41
304	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
305	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
	Total		1,87,092.08 -	4,38,377.89			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
306	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
307	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
308	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	-	.26
309	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	-	.11
310	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	-	.04
311	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	-	.06
312	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	-	.02
313	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	-	.30
314	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	11/2019 -	11/2019	.17

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
315	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
316	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
317	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
318	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	-	28.93
319	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
320	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
321	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
322	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
323	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	-	42.25
324	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
325	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
326	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
327	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
328	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
329	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609	09/2015	771.18 -	7,558.00	- -	07/2018	880.06
330	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
331	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
332	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
333	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
334	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
335	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
336	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
337	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
338	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
339	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
340	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
341	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
342	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
343	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
344	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
345	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
346	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
347	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
348	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	11/2018	36.24
349	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	10/2018	31.78
350	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	-	10.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
351	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		29,048.52 -	43,967.62			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
352	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
	<u>Mumbai Port Trust</u>						
353	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
354	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
355	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	2,907.00	06/2020 -	06/2020	255.38
	<u>Rastrya Ispat Nigam Limited</u>						
356	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,161.00 -	3,395.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
357	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
358	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	12/2018 -	07/2020	18.69
	<u>Central Public Works Department</u>						
359	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	04/2014	332.72 -	342.00	09/2016 -	09/2018	2.79

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
360	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	-	44.75
361	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
362	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
363	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	<u>Chennai Metro Rail Ltd</u>						
364	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
365	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
366	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
367	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
368	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>National Building Construction Corporation Ltd</u>						
369	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		33,337.41 -	41,055.54			
	Grand Total		4,99,749.90	8,70,645.29			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (September 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,687.52	09/2010 09/2016	03/2019	102	74.68	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	12,463.00	12/2015 11/2016	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,760.00	12/2016 03/2017	12/2020	48	0	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	9,827.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	74,849.00	37,737.52					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	546.69	01/2011 -	09/2018	92	78.87	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
	Total		624.07 -	994.86	632.48					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
7	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
8	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	295.38	04/2015 -	04/2019	48	0	
	<u>Central Coal Fields Limited</u>									
9	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	139.30	03/2012 -	03/2019	84	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
10	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	155.09	03/2012	03/2019	84	0	
11	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	352.34	03/2016	03/2019	36	0	
12	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	82.97	03/2014	03/2019	60	0	
13	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	93.93	03/2011	03/2020	108	0	
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40	706.40	125.15	07/2012	03/2021	104	0	
	<u>Eastern Coal Fields Limited</u>									
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	376.04	03/2018	03/2020	24	0	1. Rehabilitation of PAFs- Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	<u>Mahanadi Coal Fields Limited</u>									
16	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	581.54	03/2013	03/2019	72	0	
17	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	264.26	03/2010	03/2019	108	0	
18	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	363.95	03/2017	03/2020	36	0	
19	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.53	239.22	03/2013	03/2020	84	0	
20	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03	289.03	33.53	03/2018	03/2020	24	0	
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	234.48	03/2012	03/2021	108	0	
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	104.48	03/2019	03/2021	24	0	
23	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	44.91	03/2019	03/2021	24	0	
	<u>Neyveli Lignite Corporation</u>									
24	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11	5,907.11	5,666.08	12/2015 10/2018	12/2018	36	0	
25	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	390.90	06/2015 09/2019	09/2019	51	-51.37	
	<u>Northern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
26	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	572.40	03/2018 -	03/2019	12	0	
	<u>Singareni Colliers Company Limited</u>									
27	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48	0	
28	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45	0	
29	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36	-3.5	
30	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
31	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44	-7.91	
32	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72	-32.3	
33	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72	114.6	
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72	-2.14	
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	16.86	
36	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	186.91	03/2012 03/2024	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
37	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	0	
38	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	163.85	03/2016 -	03/2019	36	0	
39	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	165.78	03/2015 03/2020	03/2020	60	201.44	
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	202.31	03/2014 -	03/2020	72	0	
	Total		20,501.12 -	20,380.18	12,532.25					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
42	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85 482.85	482.85	413.00	12/2017 10/2018	10/2018	10	0	
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	121.76	11/2016 04/2019	04/2019	29	5.89	
	Total		680.64 -	692.29	534.76					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
44	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	14,283.70	05/2015 06/2019	06/2019	49	0	
	<u>Rastriya Ispat Nigam Limited</u>									
45	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	89.83	08/2018 -	10/2018	2	0	
46	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	211.25	07/2018 -	11/2018	4	0	
47	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	647.10	09/2018 -	01/2019	4	0	No
48	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	238.69	10/2016 -	03/2019	29	42.39	No
49	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	971.76	12/2017 -	09/2019	21	-12.53	No
	<u>Steel Authority Of India Limited (Sail)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
50	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	842.32	12/2017 -	11/2018	11	0	
51	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	343.36	10/2017 -	12/2018	14	0	
52	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,426.76	04/2018 -	02/2019	10	0	
	Total		26,510.85 -	26,298.25	20,054.77					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
53	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 1,097.54	694.00	470.83	10/2018 12/2018	12/2018	2	0	
54	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	2,150.27	08/2018 05/2019	05/2019	9	14.33	
55	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	215.97	02/2020 10/2020	10/2020	8	-73	
	<u>Gas Authority Of India Limited</u>									
56	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	100.65	04/2018 -	12/2018	8	-38.98	
57	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	2,915.00	1,921.34	12/2012 02/2019	02/2019	74	0	
	<u>Hindustan Petroleum Corporation Limited</u>									
58	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	545.82	10/2014 02/2019	02/2019	52	133.5	
	<u>Indian Oil Corporation Limited</u>									
59	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	1,330.00	1,308.86	06/2018 -	10/2018	4	45.67	
60	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,189.60	09/2017 12/2018	12/2018	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
61	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06	714.25	341.41	10/2017	03/2019	17	17.66	
62	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00	3,529.00	793.22	07/2019	09/2019	2	0	
63	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00	690.00	161.13	07/2018	10/2020	27	0	
64	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00	4,497.00	283.91	12/2018	12/2020	24	0	
65	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43	466.43	1.18	10/2020	05/2021	7	0	
66	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00	557.00	64.70	02/2020	02/2022	24	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
67	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93	2,504.61	1,973.99	05/2017	12/2018	19	-13.63	
68	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 207.80	207.80	13.39	09/2018	02/2019	5	-50.61	
69	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15	2,378.89	2,105.18	03/2013	03/2019	72	-3.5	
70	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,577.15	1,577.15	1,195.52	05/2013	03/2019	70	83.01	
71	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 4,619.94	4,619.94	3,886.50	12/2017	03/2019	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
72	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	154.56	03/2019 -	04/2019	1	0	Due to non-availability of Environmental Clearance (EC) and Consent to Establishment (CTE), as per the directives of Tamil Nadu Pollution Control Board (TNPCB) constructional activities at Madanam CPF are suspended since 07/08/2018 till such time EC and CTE are obtained by the Asset
73	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,172.39	04/2018 05/2019	05/2019	13	1.77	
74	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,231.37	05/2019 10/2019	10/2019	5	-4.01	
75	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	40.04	01/2014 11/2019	11/2019	70	62.78	
76	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 03/2018	12/2019	57	29.42	
77	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	1,622.94	03/2019 05/2020	05/2020	14	0	
78	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	1,200.29	06/2020 08/2021	08/2021	14	0	
	<u>Oil India Limited</u>									
79	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	180.72	03/2017 11/2018	03/2019	24	24.47	
80	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
	Total		87,288.24 -	89,385.13	31,170.26					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
81	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	980.00	04/2020 -	10/2023	42	0	
	<u>National Hydro-Electric Power Corporation</u>									
82	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,394.80	7,058.21	09/2009 -	12/2021	147	139.69	
	<u>National Thermal Power Corporation</u>									
83	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,154.15	09/2011 06/2018	10/2018	85	86.27	
84	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,870.26	11/2016 03/2019	03/2019	28	0	
85	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 13,624.00	7,998.00	7,128.72	05/2014 01/2018	05/2019	60	49.41	
86	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	10,383.95	06/2017 06/2019	06/2019	24	7.55	
87	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	9,767.60	09/2017 06/2019	06/2019	21	10.55	
88	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	8,027.68	08/2018 06/2019	06/2019	10	9.64	
89	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,554.00	12/2016 -	08/2019	32	0	
90	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	5,071.82	03/2019 09/2019	09/2019	6	0	
91	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	12,079.00	01/2018 -	05/2020	28	5.91	
92	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	7,574.04	02/2019 10/2020	10/2020	20	5.55	
93	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	2,555.03	07/2020 10/2020	10/2020	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
94	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,666.44	03/2013 12/2020	12/2020	93	29.14	
95	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	14,937.25	01/2011 04/2021	04/2021	123	73.65	
96	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	371.98	09/2019 02/2022	02/2022	29	0	
	<u>North East Electric Power Corporation</u>									
97	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,788.96	12/2009 03/2019	03/2019	111	147.51	
	<u>Power Grid Corporation Of India Limited</u>									
98	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,528.12	09/2017 -	09/2018	12	30.49	
99	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 -	1,364.00	1,190.30	12/2015 -	09/2018	33	42.83	
100	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,461.65	11/2012 09/2018	10/2018	71	36.01	
101	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,529.92	09/2014 09/2018	10/2018	49	39.3	02 out of 03 line completed. Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS – Madhugiri line. Obstruction are being removed progressively with the help of Police protection.
102	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	187.24	04/2016 12/2017	10/2018	30	0	PDC in control centre are under commissioning. Due to unavailability of accredited lab as per IEEE std. and availability of work front from constituents etc.
103	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	1,455.47	1,028.69	07/2018 -	10/2018	3	0	Erection completed. Commissioning matching with Hindupur Wind Generation project.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
104	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	150.99	88.66	07/2018 -	10/2018	3	0	03 out of 04 elements completed. Completion delayed due to non-availability of down-stream system by MPPTCL. Critical.
105	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE	08/2008	771.00 1,624.00	1,624.00	1,429.45	02/2013 -	10/2018	68	110.64	
106	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,654.96	12/2012 06/2018	11/2018	71	36.79	14/17 line & 06/07 S/s completed. Implementation of balance lines affected due to local disturbances & geographical constraints. 01 line in Mizoram (Silcher-Melriat line) was affected due to delay in tree cutting. Issue now resolved with support of state/Distt. Admn. Work also affected due to heavy rains during last 03 months. Tower erection 01 loc. was held up due to request of shifting of line of Mizoram. Now issue resolved.
107	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 3,190.27	3,190.27	2,281.28	12/2015 06/2018	11/2018	35	26.86	Generation project delayed/uncertain. Implementation also affected due to severe ROW problem mostly at Angul end & huge forest involvement. Working permission issued. Progress affected due to difficult hilly terrain and heavy rains. Work under progress.
108	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	145.22	03/2016 09/2018	11/2018	32	32.69	04 out of 05 elements completed. Erection work affected due to heavy rains & non-readiness of down stream line by State Govt. at Hamirpur. Critical.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
109	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	148.92	02/2016 09/2018	11/2018	33	14.6	Project completed except procurement of ICT (500MVA, 765/400KV) at Gaya. Transformer supply also delayed. ICT expected to be dispatched by Oct'18.
110	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	229.40	03/2018 09/2018	11/2018	8	26.82	01 out of 02 lines completed. Work affected due to severe ROW problem at 01 loc. & 5 Kms stringing. Slow progress due to compensation issues which are being resolved. Govt. help required to resolve compensation issue. Critical.
111	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	630.56	09/2017 09/2018	11/2018	14	0	
112	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	206.21	11/2017 10/2018	11/2018	12	0	Generation project ant. in March 2020. Working permission received on end of Jun'18.
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	215.81	03/2017 09/2018	11/2018	20	0	
114	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	1,750.00	1,276.62	06/2018 -	11/2018	5	0	
115	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,534.00	2,051.63	11/2008 09/2018	12/2018	121	42.42	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
116	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	669.46	09/2010 12/2018	12/2018	99	54.59	02/03 line line completed. Balance portion (02 Kms) of line being executed using under ground cable. Work affected due to water logging. Severe ROW problem being encountered at Navi Mumbai end, miscreants have burnt and damaged part of laid cable. Matter critical. Commissioning linked to availability of State down stream system at Navi Mumbai . Critical.
117	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	499.90	06/2014 12/2018	12/2018	54	31.17	01 out of 02 lines completed. Balance 400KV Madugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Balance work re-award in Dec'17. Issue being resolved with the help of admin.
118	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 534.02	534.02	426.98	08/2014 09/2018	12/2018	52	79.61	Implementation affected due to severe ROW problem in Bengaluru area. With the support of State Govt. ROW issues being resolved. Work under progress with the support of Police protection.
119	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,202.20	04/2016 12/2018	12/2018	32	38.61	
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	419.63	06/2016 09/2018	12/2018	30	0	01 out of 02 lines completed. Implementation affected due to severe ROW problem at Singrauli end. Work also affected due to poor performance by executing agency. Working permission received in Jul'18 for MP portion.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
121	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	74.71	03/2018 -	12/2018	9	0	
122	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,518.90	04/2018 09/2018	12/2018	8	0	01 out of 03 line completed. Implementation affected due to forest clearance. Stage-I received. Working permission awaited. Commissioning matching with Generation (ant. by Dec'18).
123	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	1,420.89	07/2018 -	12/2018	5	0	
124	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	287.99	161.82	06/2018 -	12/2018	6	0	Completion matching with TBCB line (line under severe ROW issues).
125	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,538.37	10/2012 12/2018	02/2019	76	5.14	8 out of 9 lines completed progressively by Dec'16. Balance 400kV Wardha – Aurangabad (on 1200KV tower) affected due to delay in implementation arising out of complexities involved (1200KV tower) & poor performance by executing agency necessitating termination & re-awarding fresh contracts. Work under progress after re-award. Severe ROW problem being encountered. Due to thunderstorm and cyclone in Jun'18, about 10 foundations, 15 tower erection & 09 ckm stringing damaged.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
126	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	2,716.40	03/2018 03/2019	03/2019	12	0	01 out of 03 element completed. Implementation affected due to delay in land acquisition & delay in off-shore supplies.
127	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	332.96	01/2018 03/2019	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through buffer zone of Tiger reserve area. Wildlife clearance proposal discussed in NBWL. Further processing of forest case being taken up. Alternate arrangements made for evacuation (contingency through Punatsanghu ATS ready). Generation project ant. by Nov'18.
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	139.34	01/2019 -	03/2019	2	0	ICT supply critical. Severe ROW affecting the progress.
129	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	433.43	11/2016 06/2019	06/2019	31	5.34	
130	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	181.16	07/2017 06/2019	06/2019	23	27.92	03 elements out of 04 elements completed. Project commissioned except Bus Reactor at Yelankha As per MoM of 40th SCPSPSR held on 19.11.16. Procurement being taken up after resolution resolved. Award placed in May'18. Engg. in progress.
131	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	191.64	05/2017 06/2019	06/2019	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
132	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	52.14	09/2018 -	06/2019	9	0	Completion matching with Banaskantha (Radhanesda) S/stn. (Sch. by Jun'19)
133	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	407.22	10/2017 09/2019	09/2019	23	0	04 locs. under severe ROW problem. Line linked with Tehri Generation completion expected by December 2020.
134	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	238.92	04/2018 -	11/2019	19	0	
135	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	840.87	12/2018 -	12/2019	12	92.28	
136	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,652.57	802.18	12/2018 -	12/2019	12	30.15	53 packages out of 56 packages award. Balance award under progress. Award have delayed due to poor response & high prices quoted by bidders. Increased BE 18-19 allocation from Rs. 282.5 Cr. to 1500 Cr. required.
137	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	.80	09/2019 -	02/2020	5	0	
138	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,714.20	08/2013 03/2022	03/2022	103	23.65	06/08 line completed). Balance 02 lines (linked to Gen. Proj.) to be completed matching with Gen. Proj. Lower Subhansiri HEP is schedule uncertain. Works presently stand-still over uncertainty of generation on a/c of local disturbance/ agitation against big dams.
	<u>Satluj Jal Vidyut Nigam Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
139	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR	05/2015	436.68 -	602.44	499.77	12/2016 -	12/2018	24	37.96	
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN, GUJARAT	11/2016	330.00 -	330.00	309.48	11/2017 -	12/2018	13	0	
	<u>Thdc India Limited</u>									
141	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 294.60	294.60	195.00	02/2014 02/2018	03/2019	61	50.75	Final stage forest clearance of 1.39 Ha. land required for power evacuation is pending.
142	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,611.13	02/2016 12/2020	05/2021	63	165.65	Decision on 10 Ha. land identified for compensatory afforestation for 5 Ha. land is to be expedited.
143	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	4,105.30	1,468.26	06/2013 -	12/2021	102	64.77	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Regular support of Distt. Administration is required.
	Total		2,09,517.83 -	2,57,352.17	1,76,321.49					
	<u>HEAVY INDUSTRY</u>									
	<u>Indira Gandhi Centre For Atomic Research</u>									
144	DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR, DELHI	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37	0	
	Total		1,554.00 -	1,554.00	161.86					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Hospital Services Consultancy Corporation Ltd</u>									
145	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	237.86	05/2017 -	09/2018	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
146	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	523.00	355.00	03/2018 -	09/2018	6	3.45	
147	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	58.52	02/2018 -	12/2018	10	0	
148	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	71.00	05/2018 -	08/2019	15	0	
	Total		1,316.17 -	1,333.59	722.38					
	<u>RAILWAYS</u>									
	<u>Container Corporation Of India</u>									
149	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	137.61	03/2019 -	08/2019	5	0	
150	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	407.32	03/2018 -	12/2019	21	0	
151	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	285.62	03/2019 -	12/2019	9	0	
152	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	2.98	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
153	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 335.77	1,156.41	876.49	03/2012 -	03/2020	96	256.11	
154	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	516.02	640.78	03/2012 -	03/2020	96	3.33	
155	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	56.73	
156	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	0	
157	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	238.38	03/2020 -	03/2021	12	0	
158	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	.59	03/2019 -	03/2021	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
159	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	468.48	
160	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	0	
161	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	0	
162	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	63.37	
163	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	62.06	
	<u>East Coast Railway</u>									
164	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	742.32	02/2019 -	03/2020	13	38.43	
165	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	210.71	12/2018 -	03/2020	15	0	
166	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	83.66	11/2018 -	03/2021	28	15.45	
167	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,088.86	03/2009 -	06/2021	147	29.71	
168	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	810.28 843.04	843.04	73.71	10/2020 -	03/2022	17	4.04	
169	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	564.41	06/2021 -	03/2023	21	137.8	
	<u>Eastern Railways</u>									
170	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	1,125.89	899.49	03/2016 12/2010	03/2020	48	0	Acquisition by State Govt. is awaited.
171	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	136.55 -	534.24	143.74	03/2016 -	03/2020	48	291.24	
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
172	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 495.74	734.01	438.72	06/2013 03/2019	03/2019	69	48.06	
173	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	
174	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,316.34	03/2004 -	03/2020	192	259.68	
	<u>North East Frontier Railway</u>									
175	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019	60	195.45	
176	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	3,230.02 4,857.00	5,820.00	5,224.22	04/2008 12/2011	12/2019	140	80.18	
177	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 274.41	614.00	267.93	03/2019 -	03/2020	12	106.51	
178	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020	12	297.72	
179	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	385.84	12/2015 -	03/2020	51	204.95	
180	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 -	551.00	595.01	03/2019 -	03/2020	12	75.48	
181	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	12/2020	144	157.59	
182	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 2,393.48	4,600.00	2,318.33	03/2014 12/2020	12/2020	81	92.19	
183	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2021	24	302.54	
184	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 2,446.57	3,000.00	655.38	03/2015 10/2021	12/2021	81	28.95	
185	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2022	132	210.02	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
186	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	14.11	
187	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,232.00	193.12	03/2022 -	12/2022	9	-.01	
	<u>North Eastern Railway</u>									
188	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,793.99	04/1999 -	12/2018	236	196.84	
189	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,177.96	-	03/2014 -	12/2019	69	0	
190	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	-	04/2016 -	01/2022	69	.16	
191	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
192	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
193	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	5.83	04/2017 -	10/2022	66	-31.45	
	<u>North Western Railway</u>									
194	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	346.35	282.12	11/2018 -	12/2018	1	19.86	
195	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	1,116.00	756.73	03/2014 03/2019	03/2019	60	70.85	
196	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	687.70	03/2015 -	03/2020	60	46.55	
	<u>Northern Railway</u>									
197	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	16,500.26	11/2002 03/2021	03/2021	220	1017.96	
	<u>Rail Vikas Nigam Ltd.</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
198	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	385.00	370.38	03/2009 03/2009	12/2018	117	188.58	
199	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	388.00	388.06	02/2006 -	12/2018	154	48.26	
200	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	1,844.47	1,277.02	12/2017 09/2009	03/2019	15	55.57	
201	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	732.81 -	1,850.00	1,863.44	03/2008 06/2008	03/2019	132	152.45	
202	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	383.54 -	555.00	564.30	03/2010 -	12/2019	117	44.7	
203	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N220000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	977.00	939.56	03/2019 -	03/2020	12	5.39	
204	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N220000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	561.52	03/2016 03/2017	12/2020	57	29.06	
205	SAMBALPUR - TITLAGARH - DOUBLING - [N220000410]RVNL, ODISHA	03/2006	948.04 -	970.00	918.32	03/2020 -	03/2021	12	2.32	
206	BANASPANI- JAKHPURA - DOUBLING - [N220000412]RVNL, ODISHA	03/2009	942.95 -	942.95	879.77	03/2019 -	03/2021	24	0	
207	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N220000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	868.67	12/2020 -	03/2021	3	0	
208	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 245.00	1,202.70	618.94	02/2015 -	12/2021	82	0	
209	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	631.78 632.00	1,195.00	626.99	12/2012 -	03/2022	111	89.15	
210	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N220000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	819.86	03/2020 -	03/2022	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
211	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,804.86	03/2016 -	03/2025	108	7.78	
212	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	764.97	03/2016 -	03/2025	108	0	
213	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	
	<u>South Central Railway</u>									
214	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 164.36	1,050.00	999.64	02/2009 -	10/2018	116	538.84	
215	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.47	93.75	03/2010 03/2022	03/2022	144	0	
216	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	362.69	03/2021 03/2022	03/2022	12	0	
217	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	280.17	03/2009 03/2023	03/2023	168	102.85	
218	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 236.41	3,501.83	719.03	03/2000 03/2019	12/2023	285	103.24	
219	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,206.29 -	1,996.94	215.72	03/2014 03/2023	03/2024	120	-9.49	
	<u>South East Central Railway</u>									
220	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	141.22	
	<u>South Eastern Railway</u>									
221	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	525.81	485.03	12/2015 12/2018	12/2018	36	69.92	
222	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	147.34	12/2016 08/2018	12/2018	24	153.41	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
223	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	969.83	348.22	03/2020 03/2020	03/2022	24	0	
224	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108	54.99	
225	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024	36	79.05	
226	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	484.43	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
227	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	10.91	03/2017 -	03/2020	36	37.96	
228	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,614.59	1,614.59	641.23	03/2019 03/2021	03/2021	24	0	
229	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,141.00	1,156.94	646.90	03/2020 03/2020	03/2022	24	0	
230	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	958.00	469.91	03/2020 03/2020	03/2022	24	11.34	
231	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	1,801.01	11.56	03/2016 12/2023	12/2023	93	0	
232	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	283.34	03/2016 12/2023	12/2023	93	0	
233	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	7.48	03/2016 12/2023	12/2023	93	0	
234	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264	0	
235	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96	0	
236	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	2,135.00	134.79	03/2001 12/2024	12/2024	285	-7.78	
237	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	22.72	12/2018 12/2024	12/2024	72	0	
	<u>Southern Railway</u>									
238	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
239	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	0	
240	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	<u>Western Railway</u>									
241	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	83.10	03/2012 -	03/2019	84	1.06	
242	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	858.96	549.56	03/2019 03/2019	03/2022	36	167.87	
	Total		1,05,326.39 -	1,87,189.36	78,148.66					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
243	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	
244	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
245	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
246	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
247	FOUR LANE OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
248	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	<u>National Highways Authority Of India</u>									
249	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	118	0	
250	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2018	54	0	
251	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	09/2018	60	0	
252	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	414.14	01/2014 -	09/2018	56	0	
253	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	114	0	
254	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	101	0	
255	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	279.14	211.16	05/2017 -	10/2018	17	0	
256	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	596.06	10/2017 -	10/2018	12	0	
257	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	10/2018	84	0	
258	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67	2.65	
259	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	674.52	01/2014 -	11/2018	58	0	
260	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	42.79	03/2018 -	11/2018	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
261	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27	0	
262	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	883.96	02/2013 -	12/2018	70	0	
263	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018	60	0	
264	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	974.83	07/2013 -	12/2018	65	0	
265	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	0	
266	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	0	
267	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	0	
268	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	563.48	11/2013 -	12/2018	61	0	
269	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	709.00	351.24	09/2017 -	12/2018	15	0	
270	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	54.89	06/2016 -	12/2018	30	0	
271	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	822.90	647.00	04/2018 -	12/2018	8	0	
272	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,302.48	07/2017 -	12/2018	17	0	
273	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	1,871.34	2,263.50	01/2018 -	12/2018	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
274	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018	78	0	
275	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	516.13	400.35	04/2018 -	12/2018	8	0	
276	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9	0	
277	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2019	79	0	
278	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,584.87	07/2015 -	03/2019	44	0	
279	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	374.75	06/2014 -	03/2019	57	0	
280	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	0	
281	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	414.00	169.20	05/2018 -	03/2019	10	-12	
282	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	574.28	51.47	07/2018 -	03/2019	8	0	
283	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	444.33	11/2016 -	03/2019	28	0	
284	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31	0	
285	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	934.46	104.98	03/2018 -	03/2019	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
286	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36	0	
287	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	6.14	05/2018 -	03/2019	10	0	
288	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29	0	
289	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	165.31	05/2018 -	04/2019	11	0	
290	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	791.18	08/2018 -	04/2019	8	0	
291	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	17.60	12/2017 -	04/2019	16	0	
292	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	14.94	06/2018 -	04/2019	10	0	
293	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	0	
294	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	881.98	11/2017 -	05/2019	18	0	
295	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	105.70	06/2018 -	05/2019	11	0	
296	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,869.30	11/2011 -	06/2019	91	106.5	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
297	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,042.82	03/2013 -	06/2019	75	0	
298	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	823.46	07/2013 -	06/2019	71	0	
299	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019	64	0	
300	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,407.12	09/2016 -	06/2019	33	21.9	
301	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18	0	
302	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	5.65	04/2018 -	06/2019	14	0	
303	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	168.88	08/2018 -	06/2019	10	0	
304	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	0	
305	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	37.39	03/2019 -	06/2019	3	0	
306	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	07/2019	76	0	
307	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-11	
308	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	502.66	11/2018 -	07/2019	8	0	
309	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	22.02	03/2019 -	07/2019	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
310	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	535.30	06/2019 -	09/2019	3	0	
311	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	0	
312	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	133.02	04/2019 -	10/2019	6	0	
313	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,310.42	04/2019 -	11/2019	7	0	
314	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,136.31	03/2014 -	12/2019	69	0	
315	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2019	68	0	
316	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	56.79	04/2018 -	04/2020	24	0	
317	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	-	03/2020 -	04/2020	1	.23	
318	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	97.53	02/2020 -	05/2020	3	0	
319	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	196.43	03/2020 -	05/2020	2	3.4	
320	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FROM - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	-	03/2020 -	05/2020	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
321	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2	13.97	
322	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	48.27	03/2020 -	06/2020	3	41.54	
323	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	279.54	03/2020 -	06/2020	3	44.39	
324	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	-	09/2017 -	06/2020	33	0	
325	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	182.85	03/2020 -	08/2020	5	5.56	
326	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	50.30	03/2020 -	08/2020	5	5.7	
327	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	9.12	03/2019 -	11/2020	20	0	
328	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	-	03/2020 -	11/2020	8	0	
329	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	20.00	03/2017 -	11/2020	44	1.06	
330	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	0	
	<u>Public Works Dept Of State</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
331	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	352.05	201.35	11/2017 -	10/2018	11	31.77	
332	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	231.56	09/2017 -	11/2018	14	36.24	
	Total		75,482.85 -	78,261.00	50,801.20					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
333	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-57.02	
	<u>Mumbai Port Trust</u>									
334	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	82.72	
	Total		966.39 -	927.36	412.57					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
335	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 -	159.30	12.40	04/2018 10/2018	10/2018	6	0	
336	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 -	167.68	30.21	04/2018 10/2018	10/2018	6	0	
337	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA	08/2017	212.70 -	212.70	37.08	05/2018 10/2018	10/2018	5	0	
338	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 214.10	214.10	33.46	05/2018 10/2018	10/2018	5	-56	
339	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT	09/2017	171.54 -	171.54	72.46	05/2018 10/2018	10/2018	5	0	
340	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH	11/2017	169.45 -	169.45	78.34	08/2018 10/2018	10/2018	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Department Of Telecommunication</u>									
341	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	
	Total		14,429.97 -	25,758.77	8,660.95					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
342	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	2,078.80	12/2018 -	07/2020	19	18.69	
	<u>Bangalore Metro Rail Corporation Limited</u>									
343	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
344	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	342.00	321.13	09/2016 03/2018	09/2018	24	2.79	
345	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	379.31	05/2017 08/2018	11/2018	18	0	
346	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	626.67	12/2015 -	12/2018	36	0	
347	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	143.14	08/2016 -	01/2019	29	0	
348	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 210.00	270.83	163.97	11/2014 -	02/2019	51	0	
349	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	0	
350	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	112.23	04/2019 06/2019	06/2019	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
351	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	81.75	04/2018 -	07/2019	15	0	
352	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	540.42	152.99	07/2019 -	09/2019	2	-1.62	
353	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
354	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 216.69	216.69	52.00	03/2015 11/2018	11/2019	56	0	
355	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.24	03/2016 -	12/2019	45	0	
356	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	282.67	10/2019 -	03/2020	5	30.58	
357	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	5.08	04/2019 06/2020	06/2020	14	0	
358	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	17.72	06/2017 07/2017	06/2020	36	.57	
359	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	21.94	02/2020 09/2020	09/2020	7	0	
360	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	-	07/2020 09/2018	09/2020	2	0	
	<u>Hindustan Steelwork Construction Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
361	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
362	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
363	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
364	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
365	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
366	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 8,680.00	8,680.00	4,256.12	03/2018 12/2019	12/2019	21	0	
	Total		82,159.60 -	84,701.33	12,130.73					
	Grand Total		6,93,478.12	8,49,677.29	4,30,021.88					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(September 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69	102
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
	Total		14,951.00 -	22,680.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	01/2009	309.46 -	553.53	01/2011 -	-	78.87	92
	Total		624.07 -	994.86				
	<u>COAL</u>							
	<u>Singareni Colliers Company Limited</u>							
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
8	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	Total		983.19 -	1,747.25				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29
	Total		197.79 -	209.44				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
10	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45	6
	Total		505.58 -	523.00				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
11	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33	9
	<u>Hindustan Petroleum Corporation Limited</u>							
12	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
13	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
14	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	10/2018	45.67	4
	<u>Oil & Natural Gas Corporation Limited</u>							
15	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,577.15	05/2013 -	03/2019	83.01	70
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42	57
18	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77	13
	<u>Oil India Limited</u>							
19	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	03/2019	24.47	24
	Total		13,085.77 -	16,272.79				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
20	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69	147
	<u>National Thermal Power Corporation</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
21	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93
22	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41	60
23	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	8,150.00	09/2011 -	10/2018	86.27	85
24	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) [N18000140	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
25	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I [N18000151	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
26	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91	28
27	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
28	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
29	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
	<u>North East Electric Power Corporation</u>							
30	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51	111
	<u>Power Grid Corporation Of India Limited</u>							
31	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	03/2014	155.57 -	206.42	03/2016 -	11/2018	32.69	32
32	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	02/2014	196.58 -	225.28	02/2016 -	11/2018	14.60	33
33	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92	23
34	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180	01/2015	268.80 -	340.88	03/2018 -	11/2018	26.82	8
35	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	534.02	08/2014 -	12/2018	79.61	52
36	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34	31
37	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17	54
38	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59	99
39	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253	03/2015	955.00 -	1,364.00	12/2015 -	09/2018	42.83	33
40	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270	08/2008	771.00 -	1,624.00	02/2013 -	10/2018	110.64	68
41	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100	07/2010	1,272.80 -	1,731.10	11/2012 -	10/2018	36.01	71

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
42	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61	32
43	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49	12
44	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,534.00	11/2008 -	12/2018	42.42	121
45	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	10/2018	39.30	49
46	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	11/2018	36.79	71
47	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	11/2018	26.86	35
48	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14	76
49	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15	12
50	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28	12
51	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
52	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96	24
	<u>Thdc India Limited</u>							
53	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75	61
54	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77	102
55	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65	63
	Total		1,38,904.26 -	1,86,738.60				
	<u>RAILWAYS</u>							
	<u>Container Corporation Of India</u>							
56	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
57	KOSI BRIDGE (NL), ECR - [N20100304]	04/2002	499.41 -	516.02	03/2012 -	03/2020	3.33	96
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73	96
59	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11	96
60	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
61	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
62	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48	61
<u>East Coast Railway</u>								
63	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
64	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	03/2013	810.28 -	843.04	10/2020 -	03/2022	4.04	17
65	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2020	38.43	13
66	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
67	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	06/2021	29.71	147
<u>Eastern Railways</u>								
68	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL [N22000228]	04/2010	136.55 -	534.24	03/2016 -	03/2020	291.24	48
<u>Metropolitan Rapid Transport Projects</u>								
69	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06	69
70	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
71	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
<u>North East Frontier Railway</u>								
72	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00	03/2019 -	03/2020	75.48	12
73	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
74	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11	31
75	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2021	302.54	24
77	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	12/2021	28.95	81
78	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	12/2020	157.59	144
79	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,374.00	03/2014 -	03/2019	195.45	60
80	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
81	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,600.00	03/2014 -	12/2020	92.19	81
82	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	3,230.02 -	5,820.00	04/2008 12/2011	12/2019	80.18	140
83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2022	210.02	132
<u>North Eastern Railway</u>								
84	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16	69
85	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	12/2018	196.84	236
<u>North Western Railway</u>								
86	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	12/2018	19.86	1
87	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	03/2019	70.85	60
88	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55	60
<u>Northern Railway</u>								
89	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96	220
<u>Rail Vikas Nigam Ltd.</u>								
90	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	188.58	117
91	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2018	48.26	154
92	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70	117
93	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
94	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	970.00	03/2020 -	03/2021	2.32	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
95	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39	12
96	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15	111
97	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2019	55.57	15
98	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	732.81 -	1,850.00	03/2008 -	03/2019	152.45	132
99	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
100	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							
101	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	164.36 -	1,050.00	02/2009 -	10/2018	538.84	116
102	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168
103	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,501.83	03/2000 -	12/2023	103.24	285
	<u>South East Central Railway</u>							
104	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22	96
	<u>South Eastern Railway</u>							
105	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41	24
106	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	12/2018	69.92	36
107	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADEATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05	36
108	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99	108
109	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
110	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96	36
111	YELAHANKA-PENUKONDA - [N22000328	05/2015	860.43 -	958.00	03/2020 -	03/2022	11.34	24
	<u>West Central Railway</u>							
112	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
113	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
114	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
	Total		60,309.92 -	1,42,758.34				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
115	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
116	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
117	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
118	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
119	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
120	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
121	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54	3
122	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
123	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
124	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
125	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
126	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
	<u>Public Works Dept Of State</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
127	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	11/2018	36.24	14
128	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	10/2018	31.78	11
	Total		12,008.91 -	14,788.38				
	<u>SHIPPING AND PORTS</u>							
	<u>Mumbai Port Trust</u>							
129	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		366.39 -	669.46				
	<u>STEEL</u>							
	<u>Rastrya Ispat Nigam Limited</u>							
130	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39	29
	Total		343.00 -	488.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
131	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
132	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	12/2018 -	07/2020	18.69	19
	<u>Central Public Works Department</u>							
133	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
134	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	04/2014	332.72 -	342.00	09/2016 -	09/2018	2.79	24
135	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36
136	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		12,935.37	15,485.99				
	Grand Total		2,68,549.25	4,28,020.51				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(September 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	05/2014 -	04/2018
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2018
3	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
4	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	-
	<u>Mahanadi Coal Fields Limited</u>				
5	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	03/2010 -	03/2018
	<u>Neyveli Lignite Corporation</u>				
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 759.19	06/2017 12/2017	12/2017
	<u>Northern Coal Fields Limited</u>				
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	03/2012 -	-
	<u>Singareni Colliers Company Limited</u>				
8	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 -	03/2018
9	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
	<u>South-Eastern Coal Fields Limited</u>				
10	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	03/2018 -	03/2018
	<u>Western Coal Fields Limited</u>				
11	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018
	Total		4,189.54 -		
	<u>STEEL</u>				
	<u>Steel Authority Of India Limited (Sail)</u>				
12	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
13	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		4,937.93		
			-		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
14	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00	02/2017	-
			-	-	
	<u>Chennai Petroleum Corporation Limited</u>				
15	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36	11/2015	-
			-	-	
	<u>Gas Authority Of India Limited</u>				
16	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT	07/2014	199.95	03/2018	03/2018
			-	-	
	<u>Hindustan Petroleum Corporation Limited</u>				
17	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00	03/2013	-
			-	-	
	<u>Indian Oil Corporation Limited</u>				
18	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00	09/2017	06/2018
			4,190.00	06/2018	
19	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00	12/2016	-
			-	-	
20	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96	05/2015	-
			-	-	
21	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00	08/2018	-
			-	-	
22	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80	-	-
			-	-	
23	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20	-	-
			-	-	
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00	01/2012	-
			-	-	
	<u>Numaligarh Refinery Limited</u>				
25	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM	07/2015	1,031.37	01/2018	-
			-	-	
	<u>Oil & Natural Gas Corporation Limited</u>				
26	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65	09/2011	-
			-	-	
	<u>Oil India Limited</u>				
27	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00	06/2017	-
			-	-	
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35	03/2015	-
			-	-	
	Total		14,588.64		
			-		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
30	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016
31	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19 -	01/2017 -	-
32	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	09/2016 02/2017	-
33	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
34	FGUTPP, UNCHAHAIR STAGE-IV (1X500 MW) - [N18000174]NTPC, UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
	<u>North East Electric Power Corporation</u>				
35	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 -	07/2013 -	-
	Total		38,922.08 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natip Implementation Society</u>				
36	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00 -	09/2011 -	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation</u>				
37	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	- -	-
38	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	- -	-
39	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	- -	-
40	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	- -	-
41	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
42	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	-
43	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-
44	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	05/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
45	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	-
46	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA	07/2016	312.99 -	08/2018 -	-
47	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	-
	Total		3,786.42 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
48	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Container Corporation Of India</u>				
49	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018
50	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
51	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
52	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
53	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
54	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
55	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
56	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
57	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
58	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
59	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
60	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
61	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
62	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
63	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>East Coast Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
64	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
65	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
66	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
	<u>Eastern Railways</u>				
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	584.41 -	02/2013 12/2012	06/2016
68	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	501.78 -	12/2010 -	-
69	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
70	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	02/2012 -	-
71	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	193.08 -	12/2011 -	-
72	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
73	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-
74	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	318.50 -	03/2006 -	-
75	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	23.56 -	- -	-
76	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
77	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-
78	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
79	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
80	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	563.51 -	03/2016 -	-
81	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	236.21 -	03/2017 -	-
82	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
83	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-
84	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
85	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
87	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
88	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
89	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	115.27 -	03/2005 -	-
90	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
91	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
92	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	278.66 -	02/2012 -	-
93	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-
94	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
95	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
96	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
97	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
98	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
99	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
100	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
101	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-
102	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
103	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
104	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
105	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 4,118.00	03/2007 -	04/2016
107	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	03/2018
108	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	792.46 -	12/2010 -	-
109	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 374.00	- -	-
	<u>North Eastern Railway</u>				
110	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018
111	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	06/2018
112	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	08/2018
113	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	- -	-
114	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
115	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
116	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
117	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
118	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-
119	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
120	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
121	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
122	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
123	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
124	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	03/2016
125	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
126	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
127	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
128	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-
129	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
130	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
131	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
132	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
133	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
134	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-
135	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
136	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
137	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
138	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
139	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
140	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
141	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
142	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
143	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
144	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
145	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
146	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
147	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017
148	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
149	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 2,911.84	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
150	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
151	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
152	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
153	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
154	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
155	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
	<u>South Eastern Railway</u>				
156	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
157	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
158	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
159	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
160	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	633.87 -	- -	-
	<u>Southern Railway</u>				
161	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018
162	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
163	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
164	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-
165	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
166	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
167	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
168	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
169	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
170	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
171	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
172	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 346.15	- -	-
173	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
174	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
175	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 342.85	- -	-
176	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
177	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
178	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
179	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-
180	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-
181	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
182	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
183	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-
184	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-
185	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-
186	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-
	<u>Western Railway</u>				
187	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 03/2018	05/2018
188	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
189	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-
190	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
191	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
192	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
193	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
194	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		82,723.90		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
195	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33	-	-
196	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05	-	-
197	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16	-	-
198	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
199	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43	-	-
200	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60	-	-
201	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	-	-
202	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	-	-
203	REHABILITATION AND UPGADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34	-	-
204	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21	-	-
205	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22	01/2015	-
206	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09	01/2015	-
207	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87	05/2014	-
208	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52	04/2014	-
209	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97	08/2015	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
210	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
211	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
212	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
213	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
214	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
215	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
216	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
217	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
218	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-
219	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-
220	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
221	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
223	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
224	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
225	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
228	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
229	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
230	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
231	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
232	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
233	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
234	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
235	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
236	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
237	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
238	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
239	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
240	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
241	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
242	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
243	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
244	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
245	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH, BIHAR	08/2015	288.24 -	11/2015 -	-
246	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-
247	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH, ODISHA	03/2014	191.50 192.00	05/2016 -	-
248	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY - [N24000640]MORTH, ODISHA	01/2015	326.63 327.00	04/2018 -	-
249	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH, ODISHA	02/2015	239.91 240.00	10/2017 -	-
250	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH, ODISHA	03/2015	226.31 226.00	10/2017 -	-
251	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH, ODISHA	12/2013	319.80 320.00	05/2016 -	-
252	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-
253	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH, ODISHA	08/2013	171.96 172.00	06/2016 -	-
254	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH, ODISHA	03/2014	162.51 163.00	05/2016 -	-
255	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH, UTTARAKHAND	02/2018	293.68 -	- -	-
256	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH, UTTARAKHAND	03/2018	460.73 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
257	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24000769]NHIDCL, SIKKIM	03/2018	264.84 -	06/2018 -	06/2018
258	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL	03/2017	158.65 -	06/2018 -	06/2018
259	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL, SIKKIM	11/2017	290.05 -	11/2017 -	11/2017
260	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	05/2018 -	-
261	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	06/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
262	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	06/2018 -	-
263	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL, ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-
264	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
265	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA	10/2014	369.00 -	03/2018 -	-
266	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA	05/2014	497.89 -	04/2017 -	-
267	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL, ARUNACHAL PRADESH	03/2015	235.08 -	05/2018 -	-
268	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	-
269	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-
270	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	01/2016 -	-
271	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	01/2016 -	-
272	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
273	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL, ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	-
274	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
275	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL, ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
276	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
277	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
278	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
279	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
280	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
281	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
282	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
283	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
284	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
285	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
286	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
287	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
288	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
289	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
290	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
291	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
292	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
293	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
294	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
295	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
296	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	-
	National Highways Authority Of India				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
297	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015
298	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017
299	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	07/2018
300	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	07/2018
301	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018
302	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	08/2018
303	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	08/2018
304	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	08/2018
305	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
306	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
307	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
308	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	-
309	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	-
310	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	-
311	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
312	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	-
313	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
314	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
315	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
316	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
317	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
318	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
319	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
320	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
321	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-
322	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
323	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
324	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
325	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
326	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
327	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	-
328	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	-
329	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
330	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
331	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	-
332	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
333	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
334	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
335	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
336	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-
337	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	-
338	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
339	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
340	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
341	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
342	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
343	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
344	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
345	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	-
346	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-
347	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	05/2018 -	-
348	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	05/2018 -	-
349	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	-
350	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
351	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
352	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
353	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
354	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
355	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	05/2018 -	-
356	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
357	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
358	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
359	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
360	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
361	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
362	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
363	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
364	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
365	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
366	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
367	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
368	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-
369	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	07/2018 -	-
370	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA	03/2016	244.00 -	07/2018 -	-
371	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
372	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
373	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI, KARNATAKA	05/2014	720.69 -	- -	-
374	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
375	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- -	-
376	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- -	-
377	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
378	REHABILITATION AND UPGRADE TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-
379	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-
380	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-
381	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
382	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	- -	-
383	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI, BIHAR	08/2017	950.64 -	08/2017 -	-
384	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI, TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
385	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI, ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-
386	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	-
387	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
388	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
389	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
390	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
391	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
392	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
393	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
394	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
395	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
396	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
397	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-
398	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
399	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
400	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
401	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
402	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
403	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
404	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
405	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
406	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
407	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
408	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
409	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
410	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
411	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
412	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
413	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-
414	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
415	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-
416	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
417	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
418	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-
419	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
420	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
421	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
422	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
423	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
424	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
425	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
426	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
427	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
428	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-
429	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
430	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-
431	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
432	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-
433	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	-
434	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
435	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
436	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-
437	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
438	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-
439	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
440	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
441	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-
442	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
443	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
444	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
445	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
446	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
447	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
448	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
449	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	-
450	REHABILITATION AND UPGADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-
451	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	-
452	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
453	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
454	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-
455	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-
	<u>National Highways Development Project</u>				
456	REHABILITATION AND UPGADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	-
457	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
458	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
459	REHABILITATION AND UPGADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
460	REHABILITATION AND UPGADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	-
461	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
462	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
463	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-
464	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
465	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
466	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
467	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-
468	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-
469	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-
470	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
471	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-
472	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-
473	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-
474	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
475	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-
476	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
477	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-
478	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-
479	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-
<u>Public Works Dept Of State</u>					
480	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
481	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
482	YAN TO NIRMAL SEREHAIBLITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
483	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
484	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
485	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	-
486	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	-
487	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-
488	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
489	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
490	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	-
491	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-
492	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
493	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	-
494	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
495	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
496	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
497	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
498	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
499	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
500	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
501	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
502	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
503	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
504	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	-
505	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
506	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
507	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
508	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
509	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
510	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
511	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	-
512	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	-
513	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-
514	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
515	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	-
516	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
517	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
518	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
519	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
520	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
521	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
522	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
523	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
524	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
525	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
526	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
527	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
528	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
529	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
530	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
531	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
532	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
533	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
534	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
535	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
536	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
537	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
538	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
539	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-
540	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
541	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
542	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
543	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-
544	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-
545	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-
546	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
547	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-
548	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
549	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
550	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
551	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
552	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
553	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-
554	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
555	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
556	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
557	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-
558	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
559	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
560	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
561	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
562	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
	Total		2,21,680.16 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
563	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	-
	<u>Port Trust</u>				
564	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
565	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
	Total		2,821.90 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
566	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
567	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2018)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
568	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	03/2016 -	04/2018
569	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
570	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-
571	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-
572	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-
573	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
	<u>Chennai Metro Rail Ltd</u>				
574	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
575	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
576	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
577	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
578	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
579	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
580	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
581	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
582	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
583	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
584	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
585	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
586	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
587	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
588	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Maharashtra Metro Rail Corporation Ltd.</u>				
589	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>National Building Construcion Corporation Ltd</u>				
590	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-
	Total		64,732.91 -		
	<u>DEFENCE PRODUCTION</u>				
	<u>Goa Shipyard Limited</u>				
591	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA	12/2016	167.69 168.00	05/2018 08/2018	08/2018
	Total		167.69 -		
	Grand Total		4,42,798.60		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (September 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
1	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	528.26	462.75	- -	12/2018	-	0/0
2	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 -	3,020.94	-	- -	03/2021	-	0/0
3	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	1,474.47	338.44	- -	03/2021	-	0/0
4	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	566.41	759.20	- -	12/2021	-	0/0
5	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	589.15	183.72	- -	03/2022	-	0/0
6	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.77	330.82	- -	03/2023	-	0/0
7	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	.19	- -	03/2023	-	0/0
	<u>East Coast Railway</u>								
8	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	175.73 -	729.92	253.10	- -	03/2021	-	0/0
9	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	285.07 -	2,614.36	111.71	- -	03/2022	-	0/0
	<u>North Central Railway</u>								
10	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	10.34	- -	12/2022	-	0/0
	<u>North East Frontier Railway</u>								
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	1,300.00	4.11	- -	03/2020	-	0/0
12	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	726.00	97.55	- -	03/2020	-	0/0
	<u>North Eastern Railway</u>								
13	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	714.34	-	- -	03/2022	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
14	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	2,062.20	674.76	- -	03/2022	-	0/2
	<u>South Eastern Railway</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	365.00	175.61	- 12/2018	12/2018	0(R3)	0/0
16	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	0(R3)	0/0
17	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	0(R3)	0/0
18	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	- 03/2030	03/2030	0(R3)	0/0
	<u>South Western Railway</u>								
19	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	1,190.92	182.68	- 03/2021	03/2021	0(R3)	0/0
20	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	1,350.91	889.05	- -	12/2023	-	0/1
21	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	692.43	-	- 12/2023	12/2023	0(R3)	0/0
22	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- 12/2023	12/2023	0(R3)	0/0
23	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	.36	- 12/2023	12/2023	0(R3)	0/0
24	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	0(R3)	0/0
25	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	0(R3)	0/0
	<u>Southern Railway</u>								
26	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	73.45	- -	03/2020	-	0/0
	<u>Western Railway</u>								
27	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	844.10	58.31	- 03/2022	03/2022	0(R3)	0/0
	Total		14,787.38 -	28,318.62	4,648.40				0/3
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
28	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	795.76	101.33	- -	10/2018	-	0/0
29	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	794.30	72.51	- -	10/2018	-	0/0
30	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	83.86	- -	10/2018	-	0/0
31	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	242.51	- -	10/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
32	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	391.33	- -	11/2018	-	0/0
33	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	143.96	- -	12/2018	-	0/0
34	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	425.60	-	- -	03/2019	-	0/0
35	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	56.32	- -	04/2019	-	0/0
36	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	17.85	- -	04/2019	-	0/0
37	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	290.73	24.46	- -	05/2019	-	0/0
38	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	59.12	- -	08/2019	-	0/0
39	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	5.64	- -	08/2019	-	0/0
40	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	9.60	- -	09/2019	-	0/0
41	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	417.19	30.19	- -	09/2019	-	0/0
42	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	138.57	- -	10/2019	-	0/0
43	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	834.64	22.03	- -	10/2019	-	0/0
44	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0
45	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	688.70	426.85	- -	11/2019	-	0/0
46	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	12/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
47	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,167.45	27.94	- -	12/2019	-	0/0
48	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	364.56	72.51	- -	12/2019	-	0/0
49	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,100.19	530.00	- -	12/2019	-	0/0
50	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	814.04	157.20	- -	01/2020	-	0/0
51	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	-	- -	01/2020	-	0/0
52	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	253.54	- -	02/2020	-	0/0
53	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	-	- -	02/2020	-	0/0
54	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	-	- -	04/2020	-	0/0
55	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	1,169.61	120.68	- -	04/2020	-	0/0
56	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	475.69	- -	05/2020	-	0/0
57	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	-	- -	07/2020	-	0/0
58	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
59	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	-	- -	09/2020	-	0/0
60	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	-	- -	10/2020	-	0/0
	Total		28,177.78 -	28,177.78	3,830.69				0/0
	Grand Total		42,965.16	56,496.40	8,479.09				0/3

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	09/2018	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Eastern Coal Fields Limited</u>					
3	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	08/2019 -	08/2019	0/0
4	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL	05/2018	535.18 -	03/2026 -	03/2026	0/0
	<u>Neyveli Lignite Corporation</u>					
5	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 759.19	06/2017 12/2017	12/2017	0/0
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>South-Eastern Coal Fields Limited</u>					
9	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH	05/2018	410.26 -	03/2026 -	03/2026	0/0
	<u>Western Coal Fields Limited</u>					
10	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
11	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
12	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
13	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
14	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
15	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
16	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
17	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
18	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
19	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	12/2021 -	12/2021	0/0
20	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
21	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	181.20 -	07/2022 -	07/2022	0/0
22	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
23	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
24	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
25	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	06/2020 -	06/2020	0/0
26	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	06/2020 -	06/2020	0/0
27	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 255.00	11/2020 11/2020	11/2020	0/0
28	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 300.00	04/2021 04/2021	04/2021	0/0
	<u>Indian Oil Corporation Limited</u>					
29	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	02/2020 -	02/2020	0/0
30	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	02/2020 -	02/2020	0/0
31	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
32	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	06/2020	0/0
33	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0
34	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT	08/2017	1,342.00 -	08/2020 -	08/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
35	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	08/2020 -	08/2020	0/0
36	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	08/2020 -	08/2020	0/0
37	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	10/2020 -	10/2020	0/0
38	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
39	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
40	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
41	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
42	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
43	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	01/2021 -	01/2021	0/0
44	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
45	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
46	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2021	0/0
47	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	05/2021	0/0
48	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL	03/2018	3,712.00 -	09/2022 -	06/2021	0/0
49	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	4,807.08 -	07/2021 -	07/2021	0/0
50	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	08/2021	0/0
51	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	12/2021 -	12/2021	0/0
52	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH	03/2018	676.00 -	12/2021 -	12/2021	0/0
53	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	02/2020 -	02/2022	0/0
54	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-	0/0
<u>Indian Strategic Petroleum Reserves Ltd</u>						
55	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
<u>Mangalore Refinery And Petrochemicals Limited</u>						
56	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	03/2020 -	03/2020	0/0
<u>Oil India Limited</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
57	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
58	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL, MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
59	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	10/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
60	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					
61	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016	0/0
62	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
	<u>Power Grid Corporation Of India Limited</u>					
63	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
64	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL, MULTI STATE	03/2015	955.00 -	12/2015 -	09/2018	0/0
65	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 12/2017	10/2018	0/0
66	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0
67	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	10/2018	0/0
68	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	07/2018 -	10/2018	0/0
69	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL, MULTI STATE	08/2008	771.00 1,624.00	02/2013 -	10/2018	0/0
70	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24 -	09/2017 09/2018	11/2018	0/0
71	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	11/2017 10/2018	11/2018	0/0
72	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 -	03/2017 09/2018	11/2018	0/0
73	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
74	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
75	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL, MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	11/2018	0/0
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
77	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	12/2018	0/0
78	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	12/2018	0/0
79	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
80	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
81	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
82	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
83	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
84	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
85	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 03/2019	03/2019	0/0
86	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
87	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
88	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	03/2019	0/0
89	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
90	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
91	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
92	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
93	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
94	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
95	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
96	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
97	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
98	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	06/2019	0/0
99	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	06/2019	0/0
100	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
101	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
102	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	11/2019	0/0
103	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
104	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
105	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
106	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
107	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
108	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
109	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
110	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	02/2020	0/0
111	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALUR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
112	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
113	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Indira Gandhi Centre For Atomic Research</u>					
114	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI	08/2016	1,554.00 -	08/2016 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
115	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	04/2020	0/0
116	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	06/2020	0/0
117	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	05/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
118	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
119	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
120	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	-	0/0
121	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	-	0/0
122	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	-	0/0
123	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
124	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
125	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0
126	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0
127	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	08/2019	0/0
128	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0
129	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
130	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
131	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 -	03/2019	0/0
132	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 2,271.50	03/2021 -	03/2021	0/0
133	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 792.89	03/2021 -	03/2021	0/0
134	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 540.02	03/2022 -	03/2022	0/0
135	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 1,272.19	03/2022 -	03/2022	0/0
136	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	03/2022 -	03/2022	0/0
137	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 637.95	03/2022 -	03/2022	0/0
138	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 3,168.29	03/2023 -	03/2023	0/0
139	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 2,449.91	03/2023 -	03/2023	0/0
140	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
141	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00	03/2024	03/2024	0/0
142	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00	03/2024	03/2024	0/0
143	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00	03/2024	03/2024	0/0
144	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47	03/2024	03/2024	0/0
145	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01	06/1999	-	0/0
	<u>Container Corporation Of India</u>		668.34	-		
146	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00	03/2018	03/2018	0/0
147	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00	03/2019	03/2019	0/0
148	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32	03/2019	03/2019	0/0
149	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00	03/2019	08/2019	0/0
150	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17	03/2018	12/2019	0/0
151	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00	03/2019	12/2019	0/0
152	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50	03/2019	12/2020	0/0
153	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70	03/2018	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
154	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00	03/2020	03/2020	0/0
155	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	51,101.00	-	-	0/0
	<u>East Central Railways</u>		11,589.00	-	-	0/0
156	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	30,357.00	-	12/2018	0/0
157	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	180.82	03/2012	03/2020	0/0
158	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	324.73	-	03/2020	0/0
159	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	335.77	03/2012	03/2020	0/0
160	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	499.41	-	03/2020	0/0
161	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	477.88	03/2021	12/2020	0/0
162	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	283.95	-	03/2021	0/0
			548.00	-		
			348.23	-		
			1,033.07	-		

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
163	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	03/2021	0/0
164	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
165	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2021	0/0
166	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	02/2016 -	03/2021	0/0
167	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FROM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	- -	12/2021	0/0
168	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	03/2022	0/0
169	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2022	0/0
170	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	03/2021 -	03/2022	0/0
171	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
172	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
173	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
174	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
175	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
176	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
177	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
178	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
179	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
180	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
181	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
182	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
183	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
184	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
<u>East Coast Railway</u>						
185	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
186	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
187	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2020	0/0
188	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
189	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.73 -	- -	03/2021	0/0
190	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2021	0/0
191	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	06/2021	0/0
192	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	03/2022	0/0
193	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	810.28 843.04	10/2020 -	03/2022	0/0
194	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 -	03/2022	0/0
195	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2022 -	03/2022	0/0
196	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 -	03/2022	0/0
197	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 -	03/2023	0/0
198	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
199	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
200	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
<u>Eastern Railways</u>						
201	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	584.41 -	02/2013 12/2012	06/2016	0/0
202	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	11/2018	0/0
203	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	614.25 -	03/2019 12/2009	03/2019	0/0
204	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	03/2016 12/2010	03/2020	0/0
205	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	136.55 -	03/2016 -	03/2020	0/0
206	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
207	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2022	0/0
208	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
209	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	02/2012 -	-	0/0
210	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	193.08 -	12/2011 -	-	0/0
211	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
212	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
213	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	318.50 -	03/2006 -	-	0/0
214	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	23.56 -	- -	-	0/0
215	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	- -	-	0/0
216	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
217	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- -	-	0/0
218	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	- -	-	0/0
219	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	563.51 -	03/2016 -	-	0/0
220	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	236.21 -	03/2017 -	-	0/0
221	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56 -	- -	-	0/0
222	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	365.17 -	03/2017 -	-	0/0
223	BARIAPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55 -	- -	-	0/0
224	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17 -	- -	-	0/0
225	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER, MULTI STATE	04/2011	193.44 -	- -	-	0/0
226	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	- -	-	0/0
227	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
228	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	115.27 -	03/2005 -	-	0/0
229	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER, MULTI STATE	04/2000	297.47 -	- -	-	0/0
230	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER, MULTI STATE	04/2003	337.96 -	- -	-	0/0
231	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	278.66 -	02/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
232	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
233	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
234	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
235	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
236	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
237	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
238	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
239	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
240	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
241	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
242	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0
243	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
244	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	03/2022 -	03/2022	0/0
245	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	12/2022	0/0
246	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
247	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
248	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
	<u>North East Frontier Railway</u>					
249	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 4,118.00	03/2007 -	04/2016	0/0
250	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	03/2018	0/0
251	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	1,142.00 1,942.00	03/2014 12/2019	03/2019	0/0
252	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
253	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	03/2019 -	03/2019	0/0
254	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	03/2019 -	03/2019	0/0
255	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [N220100201]NFR, ASSAM	09/1997	3,230.02 4,857.00	04/2008 12/2011	12/2019	0/0
256	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [N220100135]NFR, WEST BENGAL	04/1983	297.32 274.41	03/2019 -	03/2020	0/0
257	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2020	0/0
258	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	03/2020	0/0
259	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
260	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
261	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
262	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
263	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
264	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 -	03/2019 -	03/2020	0/0
265	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [N220100266]NFR, MULTI STATE	04/2000	1,180.19 -	12/2008 -	12/2020	0/0
266	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 2,393.48	03/2014 12/2020	12/2020	0/0
267	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087]NFR, BIHAR	09/2006	532.87 -	03/2019 -	03/2021	0/0
268	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
269	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
270	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2021	0/0
271	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 2,446.57	03/2015 10/2021	12/2021	0/0
272	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	03/2022	0/0
273	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	12/2022	0/0
274	KATIHAR - JOGBANI (GC)(NEFR) - [N220100247]NFR, BIHAR	09/2001	792.46 -	12/2010 -	-	0/0
275	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 374.00	- -	-	0/0
	<u>North Eastern Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
276	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
277	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	06/2018	0/0
278	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	08/2018	0/0
279	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	04/1999 -	12/2018	0/0
280	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2019	0/0
281	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	03/2014 -	12/2019	0/0
282	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
283	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	01/2022	0/0
284	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
285	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2022	0/0
286	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
287	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	03/2022	0/0
288	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
289	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
290	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	10/2022	0/0
291	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
292	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
293	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
294	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
295	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
296	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-	0/0
297	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
<u>North Western Railway</u>						
298	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
299	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	11/2018 -	12/2018	0/0
300	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	02/2019	0/0
301	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2019	0/0
302	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 03/2019	03/2019	0/0
303	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2019	0/0
304	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	11/2019	0/0
305	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 295.02	03/2020 -	12/2019	0/0
306	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2020	0/0
307	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	03/2020	0/0
308	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	08/2022	0/0
309	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
310	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
311	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	03/2016	0/0
312	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 03/2021	03/2021	0/0
313	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
314	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
315	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
316	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
317	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-	0/0
318	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
319	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
320	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
321	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
322	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
323	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-	0/0
324	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
325	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
326	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
327	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
328	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
329	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
330	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
331	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
332	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
333	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
334	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
335	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
336	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 09/2009	03/2019	0/0
337	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	03/2008 06/2008	03/2019	0/0
338	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
339	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
340	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
341	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 03/2017	12/2020	0/0
342	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
343	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
344	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	03/2020 -	03/2021	0/0
345	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
346	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
347	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 245.00	02/2015 -	12/2021	0/0
348	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
349	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
350	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	631.78 632.00	12/2012 -	03/2022	0/0
351	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
352	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	03/2022 -	03/2022	0/0
353	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	03/2023	0/0
354	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
355	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
356	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	12/2024	0/0
357	VIZIANAGARAM - SAMBALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 2,735.00	12/2024 -	12/2024	0/0
358	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
359	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	03/2016 -	03/2025	0/0
360	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
361	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
362	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	1,046.88 -	12/2026 -	12/2026	0/0
<u>Railway Electrification</u>						
363	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
364	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017	0/0
365	NANDYAL-YERRAGUNTALA (NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 164.36	02/2009 -	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
366	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2021	0/0
367	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 03/2023	03/2022	0/0
368	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
369	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 03/2023	03/2023	0/0
370	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 1,856.95	03/2023 03/2024	03/2023	0/0
371	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 236.41	03/2000 03/2019	12/2023	0/0
372	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
373	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
374	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
375	KHARSIA DHARAMJAGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00 -	09/2018 -	09/2018	0/0
376	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	02/2019 -	02/2019	0/0
377	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	12/2019	0/0
378	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	03/2012 -	03/2020	0/0
379	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	04/2020 -	04/2020	0/0
380	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	03/2021 -	03/2021	0/0
381	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	12/2021 -	12/2021	0/0
382	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 -	12/2021	0/0
383	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH	04/2011	543.00 -	03/2022 -	03/2022	0/0
384	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH	02/2014	2,288.00 -	03/2022 -	03/2022	0/0
385	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 1,908.00	03/2023 -	03/2023	0/0
386	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
<u>South Eastern Railway</u>						
387	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 12/2018	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
388	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- 12/2018	12/2018	0/0
389	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 08/2018	12/2018	0/0
390	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	03/2021 03/2021	03/2021	0/0
391	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	1,013.45 1,013.45	12/2021 12/2021	12/2021	0/0
392	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 03/2020	03/2022	0/0
393	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]SER,WEST BENGAL	04/1998	1,027.40 -	03/2022 -	03/2022	0/0
394	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 03/2024	03/2024	0/0
395	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	- 12/2024	12/2024	0/0
396	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 12/2024	12/2024	0/0
397	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
398	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	- 03/2030	03/2030	0/0
399	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
400	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
401	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
402	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
403	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
404	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	633.87 -	- -	-	0/0
<u>South Western Railway</u>						
405	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2020	0/0
406	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- 03/2021	03/2021	0/0
407	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,614.59	03/2019 03/2021	03/2021	0/0
408	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	03/2020 03/2020	03/2022	0/0
409	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	03/2016 12/2023	12/2023	0/0
410	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- 12/2023	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
411	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- 12/2023	12/2023	0/0
412	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- 12/2023	12/2023	0/0
413	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	- 12/2023	12/2023	0/0
414	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- 12/2023	12/2023	0/0
415	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	03/2016 12/2023	12/2023	0/0
416	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	03/2002 03/2024	03/2024	0/0
417	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 03/2024	03/2024	0/0
418	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	03/2001 12/2024	12/2024	0/0
419	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	12/2018 12/2024	12/2024	0/0
<u>Southern Railway</u>						
420	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018	0/0
421	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2019	0/0
422	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	02/2019	0/0
423	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	03/2019	0/0
424	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2020	0/0
425	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
426	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	03/2020	0/0
427	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
428	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
429	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
430	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
431	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 1,566.00	- -	-	0/0
432	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
433	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
434	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
435	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
436	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
437	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
438	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 346.15	- -	-	0/0
439	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
440	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
441	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 342.85	- -	-	0/0
442	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
443	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
444	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
445	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-	0/0
446	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-	0/0
447	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
448	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
449	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-	0/0
450	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-	0/0
451	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-	0/0
452	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-	0/0
<u>West Central Railway</u>						
453	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 727.13	03/2021 -	03/2021	0/0
<u>Western Railway</u>						
454	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 03/2018	05/2018	0/0
455	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
456	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 -	03/2019 -	03/2019	0/0
457	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 416.86	03/2020 03/2020	03/2020	0/0
458	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	03/2021 03/2020	03/2021	0/0
459	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	03/2021 03/2019	03/2021	0/0
460	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 2,473.40	03/2022 03/2019	03/2022	0/0
461	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	03/2022 03/2019	03/2022	0/0
462	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	03/2022 03/2019	03/2022	0/0
463	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	- 03/2022	03/2022	0/0
464	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	03/2019 03/2019	03/2022	0/0
465	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
466	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-	0/0
467	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
468	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
469	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
470	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
471	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
472	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
473	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	06/2019	0/0
474	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	06/2019	0/0
475	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
476	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
477	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
478	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
479	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
480	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
481	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
482	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
483	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
484	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
485	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
486	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
487	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
488	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
489	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
490	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
491	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
492	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
493	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
494	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
495	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
496	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
497	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
498	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
499	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-	0/0
500	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
501	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
502	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-	0/0
503	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-	0/0
504	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
505	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
506	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
507	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
508	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
509	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
510	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-	0/0
511	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
512	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
513	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
514	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
515	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
516	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
517	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
518	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
519	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
520	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
521	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
522	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
523	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
524	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
525	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
526	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
527	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
528	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
529	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
530	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
531	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
532	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
533	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
534	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
535	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0
536	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
537	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
538	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-	0/0
539	REHABILITATION AND UPGRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
540	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
541	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	06/2018	0/0
542	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	06/2018	0/0
543	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
544	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	09/2018	0/0
545	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	09/2018	0/0
546	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	09/2018	0/0
547	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	09/2018	0/0
548	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	09/2018	0/0
549	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	09/2018	0/0
550	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	09/2018	0/0
551	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	09/2018	0/0
552	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	09/2018	0/0
553	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	09/2018	0/0
554	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	09/2018	0/0
555	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	09/2018	0/0
556	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	09/2018	0/0
557	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	11/2017	0/0
558	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	10/2018	0/0
559	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
560	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
561	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
562	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
563	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
564	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-	0/0
565	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
566	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450 - [N24000614] NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-	0/0
567	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616] NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
568	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618] NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
569	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677] NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
570	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678] NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
571	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679] NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
572	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680] NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
573	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681] NHIDCL, ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
574	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682] NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
575	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683] NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
576	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684] NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
577	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685] NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
578	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689] NHIDCL, NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
579	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690] NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
580	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695] NHIDCL, SIKKIM	04/2017	388.00 -	10/2017 -	-	0/0
581	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWAY TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766] NHIDCL, SIKKIM	04/2017	318.42 -	11/2017 -	-	0/0
582	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767] NHIDCL, SIKKIM	03/2017	375.80 -	- -	-	0/0
583	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771] NHIDCL, MEGHALAYA	04/2017	553.51 -	- -	-	0/0
National Highways Authority Of India						
584	PANIKHOLI-RIMOLI - [N24000197] NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
585	SONAPUR TO GUWAHTI (AS-3) - [N24000044] NHAI, ASSAM	12/2003	245.00 -	03/2008 -	11/2017	0/0
586	BALANCE WORK OF 4-LANING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542] NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	07/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
587	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_ NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	07/2018	0/0
588	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018	0/0
589	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	08/2018	0/0
590	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	08/2018	0/0
591	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	09/2018	0/0
592	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2018	0/0
593	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	09/2018	0/0
594	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018	0/0
595	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	10/2018	0/0
596	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	10/2018	0/0
597	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	10/2018	0/0
598	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2018	0/0
599	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	10/2018	0/0
600	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	10/2018	0/0
601	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 09/2017	10/2018	0/0
602	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	10/2018	0/0
603	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	10/2018	0/0
604	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	10/2018	0/0
605	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	11/2018	0/0
606	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	11/2018	0/0
607	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	11/2018	0/0
608	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	11/2018	0/0
609	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	11/2018	0/0
610	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	11/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
611	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	11/2018	0/0
612	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	12/2018	0/0
613	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
614	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	12/2018	0/0
615	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018	0/0
616	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
617	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018	0/0
618	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	12/2018	0/0
619	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	12/2018	0/0
620	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	12/2018	0/0
621	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	12/2018	0/0
622	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	12/2018	0/0
623	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
624	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	-	12/2018	0/0
625	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	12/2018	0/0
626	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	12/2018	0/0
627	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	12/2018	0/0
628	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019	0/0
629	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	01/2019	0/0
630	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN	08/2016	320.30 -	01/2019 -	01/2019	0/0
631	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	01/2019	0/0
632	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	02/2019	0/0
633	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	03/2019	0/0
634	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
635	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2019	0/0
636	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019	0/0
637	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 -	03/2019	0/0
638	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB, SERVICE ROADS, FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50 -	03/2019 -	03/2019	0/0
639	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	03/2019	0/0
640	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	03/2019	0/0
641	4-LANING OF GOA/KARNATKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATKA	05/2014	1,655.01 -	08/2016 -	03/2019	0/0
642	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2019	0/0
643	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
644	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	03/2019	0/0
645	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	03/2019 -	03/2019	0/0
646	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	03/2019	0/0
647	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	03/2019 -	03/2019	0/0
648	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2019	0/0
649	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019	0/0
650	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019	0/0
651	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	05/2018 -	04/2019	0/0
652	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- -	04/2019	0/0
653	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, PUNJAB	09/2015	273.06 -	- -	04/2019	0/0
654	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019	0/0
655	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	04/2019	0/0
656	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
657	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019	0/0
658	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
659	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	04/2019	0/0
660	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	04/2019	0/0
661	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	04/2019	0/0
662	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	05/2019	0/0
663	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019	0/0
664	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019	0/0
665	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	05/2019	0/0
666	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	05/2019 -	05/2019	0/0
667	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	05/2019	0/0
668	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019	0/0
669	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2019	0/0
670	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	05/2019	0/0
671	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
672	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2019	0/0
673	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	06/2019	0/0
674	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	06/2019	0/0
675	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	06/2019	0/0
676	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2019	0/0
677	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
678	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	06/2019	0/0
679	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	06/2019	0/0
680	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	06/2019	0/0
681	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
682	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
683	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	06/2019	0/0
684	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	06/2019	0/0
685	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	07/2019	0/0
686	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2019	0/0
687	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	07/2019	0/0
688	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	07/2019	0/0
689	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	07/2019	0/0
690	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	07/2019	0/0
691	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	08/2019	0/0
692	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	08/2019	0/0
693	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
694	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	08/2019	0/0
695	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
696	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
697	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
698	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	09/2019	0/0
699	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
700	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0
701	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	10/2019	0/0
702	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
703	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	11/2019	0/0
704	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	11/2019	0/0
705	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
706	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
707	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2019	0/0
708	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	12/2019	0/0
709	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
710	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
711	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0
712	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
713	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
714	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	02/2020	0/0
715	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
716	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
717	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
718	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
719	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
720	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
721	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
722	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
723	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
724	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
725	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
726	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
727	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
728	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
729	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
730	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
731	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
732	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
733	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	05/2020	0/0
734	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
735	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
736	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	05/2020	0/0
737	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
738	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2020	0/0
739	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
740	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
741	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
742	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
743	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
744	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
745	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
746	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
747	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
748	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0
749	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
750	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020	0/0
751	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
752	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	11/2020	0/0
753	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 -	03/2021	0/0
754	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
755	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
756	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
757	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	-	0/0
758	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	-	0/0
759	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	-	0/0
760	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
761	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	-	0/0
762	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
763	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
764	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
765	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
766	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
767	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
768	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
769	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
770	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
771	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
772	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
773	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
774	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
775	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	-	0/0
776	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	-	0/0
777	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
778	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
779	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-	0/0
780	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
781	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
782	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
783	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
784	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	-	0/0
785	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
786	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
787	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
788	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
789	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
790	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
791	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
792	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	-	0/0
793	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-	0/0
794	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	05/2018 -	-	0/0
795	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	05/2018 -	-	0/0
796	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
797	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
798	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
799	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
800	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-	0/0
801	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
802	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	05/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
803	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
804	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
805	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
806	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
807	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
808	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
809	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
810	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0
811	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
812	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
813	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
814	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
815	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
816	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	-	0/0
817	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-	0/0
818	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
819	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
820	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
821	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
822	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
823	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
824	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
825	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
826	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
827	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
828	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
829	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
830	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
831	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0
832	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-	0/0
833	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
834	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-	0/0
835	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
836	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
837	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
838	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
839	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
840	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
841	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-	0/0
842	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
843	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
844	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-	0/0
845	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
846	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
847	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
848	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-	0/0
849	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
850	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
851	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
852	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
853	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
854	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
855	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
856	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
857	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
858	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0
859	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
860	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
861	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-	0/0
862	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM 206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
863	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
864	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
865	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0
866	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
867	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
868	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
869	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
870	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
871	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
872	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
873	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
874	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
875	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-	0/0
876	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
877	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-	0/0
878	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
879	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
880	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	-	0/0
881	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
882	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
883	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-	0/0
884	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
885	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-	0/0
886	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
887	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
888	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-	0/0
889	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
890	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-	0/0
891	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
892	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
893	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
894	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
895	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
896	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	-	0/0
897	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
898	CONSTRUCTION OF SIX LANE OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	-	0/0
899	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
900	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
901	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-	0/0
902	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-	0/0
National Highways Development Project						
903	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-	0/0
904	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
905	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-	0/0
906	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
907	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
908	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
909	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-	0/0
910	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-	0/0
911	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-	0/0
912	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
913	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-	0/0
914	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-	0/0
915	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-	0/0
916	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
917	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-	0/0
918	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
919	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-	0/0
920	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
921	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-	0/0
	<u>Public Works Dept Of State</u>					
922	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	10/2018	0/0
923	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	11/2018	0/0
924	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
925	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-	0/0
926	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
927	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
928	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
929	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
930	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
931	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
932	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
933	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
934	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
935	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
936	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
937	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-	0/0
938	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-	0/0
939	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
940	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
941	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
942	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
943	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
944	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
945	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
946	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
947	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
948	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
949	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
950	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
951	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
952	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
953	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
954	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
955	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
956	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
957	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
958	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
959	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
960	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
961	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
962	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-	0/0
963	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
964	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
965	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
966	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
967	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
968	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
969	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
970	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-	0/0
971	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
972	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
973	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
974	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
975	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
976	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-	0/0
977	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
978	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
979	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
980	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
981	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
982	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
983	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
984	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
985	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Kamarajar Port Limited</u>					
986	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	05/2020	0/0
	<u>Mumbai Port Trust</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
987	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
	<u>Port Trust</u>					
988	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
989	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
990	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 -	04/2018 10/2018	10/2018	0/0
991	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 -	04/2018 10/2018	10/2018	0/0
992	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA	08/2017	212.70 -	05/2018 10/2018	10/2018	0/0
993	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 214.10	05/2018 10/2018	10/2018	0/0
994	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT	09/2017	171.54 -	05/2018 10/2018	10/2018	0/0
995	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH	11/2017	169.45 -	08/2018 10/2018	10/2018	0/0
996	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 -	10/2018 10/2018	10/2018	0/0
	<u>Department Of Telecommunication</u>					
997	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
998	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
999	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	07/2020	0/0
	<u>Bangalore Metro Rail Corporation Limited</u>					
1000	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
1001	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 03/2018	09/2018	0/0
1002	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1003	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
1004	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	09/2019	0/0
1005	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1006	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0
1007	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0
1008	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1009	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 07/2017	06/2020	0/0
1010	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 09/2020	09/2020	0/0
1011	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-	0/0
1012	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-	0/0
1013	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-	0/0
1014	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
	<u>Chennai Metro Rail Ltd</u>					
1015	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					
1016	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
1017	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
1018	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1019	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1020	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1021	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1022	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1023	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1024	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1025	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	- -	-	0/0
1026	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1027	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1028	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL, JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1029	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL, JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1030	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1031	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1032	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1033	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1034	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC, MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	11/2021	0/0
1035	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1036	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1037	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 8,680.00	03/2018 12/2019	12/2019	0/0
	<u>National Building Construction Corporation Ltd</u>					
1038	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-	0/0
	Total		11,38,948.46 -			0/0
	Grand Total		11,38,948.46			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	568.10	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	619.33	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52	247.52	131.32	02/2019 -	12/2018
5	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00	356.00	169.04	05/2019 -	12/2018
6	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	0.98	09/2022 -	06/2021
7	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	333.63	12/2020 -	02/2020
	Total		14,380.92 -	13,499.52	2,017.37		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
8	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	88.01	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
9	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	1,142.00 1,942.00	3,374.00	3,015.98	03/2014 12/2019	03/2019
10	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	18.38	12/2021 -	03/2021
	<u>North Western Railway</u>						
11	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	113.46	12/2019 -	06/2019
12	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	4/2013	420.18 295.02	865.00	65.19	03/2020 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
13	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.22	12/2025 -	03/2025
	<u>South Central Railway</u>						

Costing Rs. 150 Crore and above

(September 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
14	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	4/2012	1,856.95 1,856.95	1,955.27	225.85	03/2023 03/2024	03/2023
15	GUNTUR-GUNTAKAL - [N22000368]	4/2016	3,631.00 -	3,631.00	99.11	03/2022 03/2023	03/2022
	Total		8,970.49 -	11,857.83	3,626.20		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
16	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	86.95	03/2020 -	05/2019
17	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	10.57	03/2020 -	06/2019
	Total		461.69 -	426.16	97.52		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
18	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 06/2020	03/2020
	Total		150.29 -	150.29	2.58		
	Grand Total		23,963.39	25,933.80	5,743.67		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	196.02	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	296.10	03/2022 -	03/2022
4	RANIGANJ MASTER PLAN - [N06000163]	8/2009	2,661.73 -	2,661.73	-	08/2019 -	08/2019
5	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.27	03/2022 -	03/2022
6	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
	<u>Mahanadi Coal Fields Limited</u>						
7	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	689.20	03/2026 -	03/2026
8	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	413.85	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
9	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	390.90	06/2015 09/2019	09/2019
10	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	173.06	12/2019 -	12/2019
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	3,072.20	11/2021 -	11/2021
12	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	8.71	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
13	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	196.70	03/2021 -	03/2021
14	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.68	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
15	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	186.91	03/2012 03/2024	03/2024
16	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
17	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
18	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129 <u>South-Eastern Coal Fields Limited</u>	5/2015	397.09 -	442.42	79.96	03/2019 -	03/2019
19	JAGANNATHPOR OCP(3.00MTY) - [N06000075	9/2008	152.43 -	459.49	165.78	03/2015 03/2020	03/2020
20	BATURA OCP (2.0 MTY) - [N06000049	8/2015	1,186.64 -	203.82	102.09	03/2023 03/2021	03/2021
21	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.63	68.52	03/2022 -	03/2022
22	MADANNAGAR OPENCAST PROJECT - [N06000140	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
23	MAHAMAYA OPENCAST PROJECT - [N06000164	5/2018	410.26 -	410.26	-	03/2026 -	03/2026
24	VIJAY WEST OPENCAST PROJECT - [N06000158	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
25	AMADAND OPENCAST EXPANSION PROJECT - [N06000148	3/2016	869.44 -	869.44	111.27	03/2021 -	03/2021
26	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093	6/2010	11,816.40 -	11,816.40	2,834.56	03/2023 -	03/2023
27	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	1,881.64	03/2023 -	03/2023
28	DURGAPUR OPENCAST PROJECT - [N06000136	2/2015	916.24 -	916.24	3.74	03/2023 -	03/2023
29	AMGAON OPENCAST PROJECT RCE - [N06000135	7/2015	316.10 -	316.10	56.54	03/2020 -	03/2020
30	BATURA HIGHWALL PROJECT - [N06000134	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
31	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	41.27	03/2021 -	03/2021
32	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	113.06	03/2021 -	03/2021
33	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
34	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	54.71	03/2020 -	03/2020
35	MALACHUA OPENCAST PROJECT - [N06000139	10/2015	488.33 -	488.33	1.90	03/2023 -	03/2023
36	PELMA OCP(15.00MTY) - [N06000045 <u>Western Coal Fields Limited</u>	11/2014	1,624.59 -	1,624.59	6.06	03/2023 -	03/2023
37	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	277.65	22.07	03/2021 -	03/2021
38	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142	11/2015	498.42 -	498.42	52.83	03/2020 -	03/2020
39	KOLAR PIMPRI EXTENSION OC - [N06000160	3/2017	362.73 -	362.73	257.35	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	88.13	03/2021 -	03/2021
41	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
42	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
43	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	16.21	03/2022 -	03/2022
44	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	254.72	03/2019 -	03/2019
45	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	179.06	03/2020 -	03/2020
46	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
47	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	236.37	03/2025 -	03/2025
48	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	82.13	03/2021 -	03/2021
49	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	102.75	03/2020 -	03/2020
50	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
51	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.28	03/2021 -	03/2021
52	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	389.77	03/2020 -	03/2020
53	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	128.93	03/2019 -	03/2019
	Total		71,952.29 -	70,773.38	13,478.00		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
54	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	49.95	08/2020 -	08/2020
	Total		285.95 -	291.29	49.95		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	24.50	11/2019 -	11/2019
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	28.31	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	23.51	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
58	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	121.76	11/2016 04/2019	04/2019
59	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	23.29	04/2020 -	04/2020
60	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	413.00	12/2017 10/2018	10/2018
	Total		1,781.92 -	1,793.57	634.37		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
61	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
62	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	276.91	06/2020 -	06/2020
63	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
	<u>Hospital Services Consultancy Corporation</u>						
64	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	76.88	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
65	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	214.62	09/2018 -	09/2018
66	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	122.66	03/2019 -	03/2019
67	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	71.50	03/2019 -	03/2019
	Total		3,508.53 -	3,508.53	975.92		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
68	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	95.59	04/2021 04/2021	04/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	300.68	01/2020 01/2020	01/2020
70	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
71	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 11/2020	11/2020
	Total		6,912.00 -	6,912.00	428.19		
	PETROLEUM						
	<u>Bharat Petroleum Corporation Limited</u>						
72	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	470.83	10/2018 12/2018	12/2018
73	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	105.67	02/2020 -	02/2020
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	110.72	12/2019 -	12/2019
75	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	88.38	01/2019 -	01/2019
76	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
77	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	14.96	12/2020 -	12/2020
78	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	48.20	08/2020 -	08/2020
79	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	215.97	02/2020 10/2020	10/2020
80	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	2,150.27	08/2018 05/2019	05/2019
	<u>Chennai Petroleum Corporation Limited</u>						
81	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	465.00	12/2019 -	12/2019
82	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	11.79	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
83	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	2,212.79	12/2018 -	12/2018
84	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	682.57	02/2020 -	02/2020
85	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	29.47	07/2022 -	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
86	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	89.65	04/2022 -	04/2022
87	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285]	6/2009	2,915.00 2,915.00	2,915.00	1,921.34	12/2012 02/2019	02/2019
88	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	17.48	12/2020 -	12/2020
89	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	448.61	12/2020 -	12/2020
90	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	611.91	12/2020 -	12/2020
91	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	597.57	12/2020 -	12/2020
92	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	800.00	577.39	12/2018 -	12/2018
93	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1.03	12/2021 -	12/2021
94	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	18.64	10/2022 -	10/2022
95	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	19.08	10/2022 -	10/2022
96	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	12.65	07/2022 -	07/2022
97	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	24.18	10/2022 -	10/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
98	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	545.82	10/2014 02/2019	02/2019
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	199.63	09/2019 -	09/2019
100	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	78.89	02/2019 -	02/2019
101	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	40.68	03/2021 -	03/2021
102	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	3.60	11/2020 11/2020	11/2020
103	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
104	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 04/2021	04/2021
106	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	855.11	06/2020 -	06/2020
107	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
	<u>Indian Oil Corporation Limited</u>						
108	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
109	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	161.13	07/2018 10/2020	10/2020
110	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	.17	06/2020 -	06/2020
111	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	59.66	07/2020 -	07/2020
112	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	78.63	06/2020 -	06/2020
113	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
114	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	74.43	09/2019 -	09/2019
115	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	475.41	08/2021 -	08/2021
116	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	712.49	11/2018 -	11/2018
117	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,098.69	11/2019 -	11/2019
118	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	190.66	08/2019 -	08/2019
119	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	475.64	10/2019 -	10/2019
120	LPG BP PROJECT KHRDHA - [N16000283]	12/2016	161.59 -	161.59	33.57	12/2019 -	12/2019
121	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	24.22	02/2020 -	02/2020
122	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	232.84	01/2019 -	01/2019
123	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
124	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
125	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
126	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021
127	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	.08	01/2021 -	01/2021
128	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	306.51	12/2020 -	12/2020
129	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	122.32	08/2020 -	08/2020
130	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	4,807.08 -	4,807.08	19.10	07/2021 -	07/2021
131	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	-	01/2021 -	01/2021
132	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
133	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,018.23	09/2019 -	09/2019
134	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.09	08/2020 -	08/2020
135	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	1.51	12/2021 -	12/2021
136	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	168.63	09/2019 -	09/2019
137	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
138	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
139	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	25.21	04/2021 -	04/2021
140	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	32.34	04/2020 -	04/2020
141	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	1.47	12/2021 -	12/2021
142	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
143	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
144	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	-	08/2020 -	08/2020
145	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	711.29	09/2019 -	09/2019
146	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	.12	02/2020 -	02/2020
147	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	241.91	09/2019 -	09/2019
148	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	2,189.60	09/2017 12/2018	12/2018
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
149	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
150	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	111.05	03/2019 -	03/2019
151	BSVI UPGRADEATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
152	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
153	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	2,105.18	03/2013 03/2019	03/2019
154	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	1,622.94	03/2019 05/2020	05/2020
155	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,577.15	1,195.52	05/2013 03/2019	03/2019
156	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	70.98	03/2023 03/2022	03/2022
157	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	-	12/2019 -	12/2019
158	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	302.59	11/2019 11/2019	11/2019
159	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	78.15	11/2019 11/2019	11/2019
160	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	102.53	11/2019 11/2019	11/2019
161	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	299.26	05/2019 05/2019	05/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
162	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	207.80	13.39	09/2018 02/2019	02/2019
163	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	269.97	03/2026 03/2026	03/2026
164	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	98.07	05/2020 05/2020	05/2020
165	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	1,200.29	06/2020 08/2021	08/2021
166	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,172.39	04/2018 05/2019	05/2019
167	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	3,886.50	12/2017 03/2019	03/2019
168	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	570.63	05/2021 05/2021	05/2021
169	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	40.04	01/2014 11/2019	11/2019
170	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,504.61	1,973.99	05/2017 12/2018	12/2018
171	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,524.08	04/2019 03/2019	03/2019
172	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	449.65	11/2019 12/2018	12/2018
173	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,231.37	05/2019 10/2019	10/2019
	<u>Oil India Limited</u>						
174	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	18.56	10/2020 -	10/2020
175	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	1.65	02/2020 -	02/2020
176	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	13.06	12/2019 -	12/2019
	Total		1,81,140.09 -	1,79,346.87	47,465.25		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
177	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	9,767.60	09/2017 06/2019	06/2019
178	TALAIALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,218.88	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
179	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	2,555.03	07/2020 10/2020	10/2020
180	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	5,809.85	09/2019 -	09/2019
181	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10,383.95	06/2017 06/2019	06/2019
182	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	8,870.26	11/2016 03/2019	03/2019
183	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	14,937.25	01/2011 04/2021	04/2021
184	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	371.98	09/2019 02/2022	02/2022
185	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	7,574.04	02/2019 10/2020	10/2020
186	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	8,027.68	08/2018 06/2019	06/2019
187	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	5,071.82	03/2019 09/2019	09/2019
188	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,666.44	03/2013 12/2020	12/2020
	<u>North East Electric Power Corporation</u>						
189	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,788.96	12/2009 03/2019	03/2019
	<u>Power Grid Corporation Of India Limited</u>						
190	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	669.46	09/2010 12/2018	12/2018
191	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,714.20	08/2013 03/2022	03/2022
192	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	2,716.40	03/2018 03/2019	03/2019
193	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	550.18	433.43	11/2016 06/2019	06/2019
194	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,202.20	04/2016 12/2018	12/2018
195	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	26.40	03/2019 -	03/2019
196	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	76.98	02/2019 -	02/2019
197	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	191.76	02/2019 -	02/2019
198	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	250.73	03/2019 -	03/2019
199	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	194.26	12/2018 -	12/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
200	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	743.82	01/2019 -	01/2019
201	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	97.53	11/2018 -	11/2018
202	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	303.70	04/2019 -	04/2019
203	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	502.54	06/2019 -	06/2019
204	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	3,710.05	11/2019 -	11/2019
205	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,861.40	05/2019 -	05/2019
206	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	375.34	11/2018 -	11/2018
207	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	332.96	01/2018 03/2019	03/2019
208	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
209	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	321.99	02/2020 -	02/2020
210	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	197.76	02/2019 -	02/2019
211	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	50.27	07/2019 -	07/2019
212	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	481.12	07/2020 -	07/2020
213	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,591.63	04/2019 -	04/2019
214	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	16.10	06/2019 -	06/2019
215	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	552.21	04/2020 -	04/2020
216	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	89.17	09/2019 -	09/2019
217	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	21.82	12/2019 -	12/2019
218	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	20.09	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
219	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	22.42	03/2019 -	03/2019
220	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	103.28	02/2019 -	02/2019
221	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	55.10	02/2020 -	02/2020
222	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	354.00	04/2019 -	04/2019
223	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	25.85	11/2019 -	11/2019
224	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	79.31	06/2019 -	06/2019
225	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	2.50	06/2019 -	06/2019
226	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	499.90	06/2014 12/2018	12/2018
227	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	516.25	10/2018 -	10/2018
228	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	191.64	05/2017 06/2019	06/2019
229	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	181.16	07/2017 06/2019	06/2019
230	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRIL PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	407.22	10/2017 09/2019	09/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
231	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	118.79	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
232	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	62.71	09/2020 -	09/2020
	Total		1,76,312.10 -	1,96,327.85	1,18,409.19		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
233	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	937.42	03/2023 -	03/2023
234	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	1,759.34	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
235	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
236	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	24.71	03/2022 -	03/2022
237	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	2/2016	1,035.16 -	1,035.16	12.96	03/2022 -	03/2022
238	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	1.05	03/2023 -	03/2023
239	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	4,817.69	148.42	03/2024 -	03/2024
240	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	77.75	03/2023 -	03/2023
241	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	109.03	03/2022 -	03/2022
242	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
243	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	-	03/2024 -	03/2024
244	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	152.67	03/2022 -	03/2022
245	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	267.58	03/2021 -	03/2021
246	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	240.00	219.77	03/2019 -	03/2019
<u>Container Corporation Of India</u>							
247	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	251.08	03/2019 -	03/2019
248	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	243.30	03/2019 -	03/2019
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
249	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
<u>East Central Railways</u>							
250	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
<u>East Coast Railway</u>							
251	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,143.60 -	1,160.83	566.17	03/2020 -	03/2020
252	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
253	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	183.12	03/2022 -	03/2022
254	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	163.03	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
255	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	77.20	03/2022 -	03/2022
256	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
257	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) [N22000230]	4/2010	157.94 -	157.94	50.50	11/2018 -	11/2018
258	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	2,142.49	291.74	03/2022 -	03/2022
259	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	693.90	310.26	03/2020 -	03/2020
	<u>Metropolitan Rapid Transport Projects</u>						
260	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	734.01	438.72	06/2013 03/2019	03/2019
	<u>North Central Railway</u>						
261	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
262	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
	<u>North East Frontier Railway</u>						
263	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	4,600.00	2,318.33	03/2014 12/2020	12/2020
264	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	457.51	03/2019 -	03/2019
265	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	64.09	03/2020 -	03/2020
266	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	163.08	03/2021 -	03/2021
267	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	264.69	03/2019 -	03/2019
268	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	123.11	03/2020 -	03/2020
269	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	259.43	03/2021 -	03/2021
270	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
271	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
	<u>North Eastern Railway</u>						
272	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	718.54	274.46	12/2022 -	12/2022
273	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	871.56	97.82	12/2021 -	12/2021
274	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	174.83	01/2019 -	01/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
275	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	-	01/2022 -	01/2022
276	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
277	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	81.15	03/2022 -	03/2022
	<u>North Western Railway</u>						
278	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) [N22000113]	4/2008	653.19 -	1,116.00	756.73	03/2014 03/2019	03/2019
279	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	795.01	437.03	02/2019 -	02/2019
280	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	294.90	157.63	10/2018 -	10/2018
281	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	171.82	11/2019 -	11/2019
282	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	-	08/2022 -	08/2022
283	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	349.00	248.23	02/2019 -	02/2019
284	PHULERA - DIGANA DOUBLING - [N22000326]	5/2015	600.00 -	685.99	3.38	03/2020 -	03/2020
	<u>Northern Railway</u>						
285	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	27,949.00	16,500.26	11/2002 03/2021	03/2021
286	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
287	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	550.04	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
288	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
289	BHANUPALI-BILASPUR BERTH NL - [N22000273]	4/2008	1,046.88 -	7,000.00	212.83	12/2026 -	12/2026
290	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	812.47	12/2020 -	12/2020
291	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	814.23	03/2020 -	03/2020
292	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	243.95	12/2024 -	12/2024
293	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	3/2009	1,514.45 -	1,750.00	1,510.51	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
294	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	16,216.00 -	16,216.00	893.22	12/2024 -	12/2024
295	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.92 -	1,765.92	228.15	03/2023 -	03/2023
296	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	197.87	12/2024 -	12/2024
297	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	943.60 -	943.60	102.17	03/2022 -	03/2022
298	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	92.48	12/2023 -	12/2023
299	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	704.64	12/2021 -	12/2021
300	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	81.99	03/2021 -	03/2021
301	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	975.62	573.13	12/2021 -	12/2021
302	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,127.00	1,059.52	03/2023 -	03/2023
	<u>South Central Railway</u>						
303	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	280.17	03/2009 03/2023	03/2023
304	NADIKUDE-SRI KALAHASTI - [N22000286]	4/2011	2,288.70 -	2,288.70	362.69	03/2021 03/2022	03/2022
305	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	119.69	03/2020 03/2020	03/2020
306	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	4/2006	1,160.48 -	1,160.47	93.75	03/2010 03/2022	03/2022
307	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
308	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	343.70	03/2021 -	03/2021
	<u>South East Central Railway</u>						
309	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
310	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	4/2010	585.93 -	1,420.39	104.10	02/2019 -	02/2019
311	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	543.00 -	543.00	-	03/2022 -	03/2022
312	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
313	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
314	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	4/2013	3,055.00 -	3,055.00	600.00	09/2018 -	09/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
315	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
316	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
317	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
318	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
	<u>South Eastern Railway</u>						
319	MM FROM BURAMARA-CHAKULIA - [N22000305]	4/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024
320	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024
321	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	140.51	03/2021 03/2021	03/2021
322	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	4/1998	1,027.40 -	2,373.00	481.65	03/2022 -	03/2022
323	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024
324	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	4/1998	1,027.40 -	2,373.00	484.43	03/2003 03/2030	03/2030
325	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.48	12/2021 12/2021	12/2021
326	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	4/2012	258.20 -	365.00	175.61	- 12/2018	12/2018
327	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	525.81	485.03	12/2015 12/2018	12/2018
328	MM FROM PANSKURA-GHATAL NL - [N22000309]	4/2011	276.69 -	426.00	-	- 03/2030	03/2030
329	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.77	- 03/2025	03/2025
	<u>South Western Railway</u>						
330	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	4/2011	1,801.01 -	1,801.01	11.56	03/2016 12/2023	12/2023
331	HUBLI-ANKOLA(NL),SWR - [220100193]	4/1997	2,315.00 -	2,135.00	134.79	03/2001 12/2024	12/2024
332	MARIKUPPAM - KUPPAM - [N22000308]	4/2012	279.54 -	279.54	7.48	03/2016 12/2023	12/2023
333	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	4/2013	327.25 -	367.77	.31	- 12/2023	12/2023
334	GADAG-WADI NL - [N22000299]	4/2013	2,841.84 -	2,841.84	22.72	12/2018 12/2024	12/2024
335	TORANAGALLU-RANJITPURA DL - [N22000298]	4/2011	146.75 -	167.50	.34	- 12/2023	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
336	BAGALKOT-KUDACHI NL - [N22000258]	4/2010	986.30 -	986.30	283.34	03/2016 12/2023	12/2023
337	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	4/2013	558.00 -	692.43	-	- 12/2023	12/2023
338	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	4/2013	296.00 -	466.65	-	- 12/2023	12/2023
339	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,614.59	641.23	03/2019 03/2021	03/2021
340	MIRAJ-LONDA - [N22000327]	3/2015	1,830.00 -	1,190.92	182.68	- 03/2021	03/2021
341	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	4/1996	1,382.78 -	1,382.78	7.35	03/2002 03/2024	03/2024
342	WHITE FIELD-KOLAR NL - [N22000280]	4/2011	341.05 -	348.85	.36	- 12/2023	12/2023
343	SHIMOGA-HARIHAR NL - [N22000278]	4/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024
	<u>Southern Railway</u>						
344	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079]	9/2007	724.69 -	2,072.50	1,129.33	02/2019 -	02/2019
345	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	1,800.00	103.10	03/2019 -	03/2019
346	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
347	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
348	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	980.00	1,292.55	03/2020 -	03/2020
349	ATTIPPATTU PUTTUR - [N22000184]	4/2008	151.84 -	1,105.00	3.34	02/2019 -	02/2019
	<u>West Central Railway</u>						
350	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
351	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
352	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
	<u>Western Railway</u>						
353	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	2,783.00	444.72	03/2020 03/2020	03/2020
354	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	58.31	- 03/2022	03/2022
355	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	551.51	257.05	03/2019 -	03/2019
	Total		2,88,684.58 -	3,96,422.58	71,255.51		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
356	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
357	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	-	06/2019 -	06/2019
358	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	-	11/2019 -	11/2019
359	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	-	11/2019 -	11/2019
360	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
361	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	-	02/2020 -	02/2020
362	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	284.00	-	11/2019 -	11/2019
363	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	-	12/2019 -	12/2019
364	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	-	12/2019 -	12/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
365	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
366	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765	3/2018	323.98 -	323.98	-	09/2018 -	09/2018
367	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764	3/2018	272.89 -	272.89	-	09/2018 -	09/2018
368	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763	3/2018	215.79 -	215.79	-	09/2018 -	09/2018
369	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762	3/2018	215.12 -	215.12	-	09/2018 -	09/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
370	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761	3/2018	282.98 -	282.98	-	09/2018 -	09/2018
371	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760	3/2018	251.97 -	251.97	-	09/2018 -	09/2018
372	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759	3/2018	237.72 -	237.72	-	09/2018 -	09/2018
373	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758	3/2018	240.64 -	240.64	-	09/2018 -	09/2018
374	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757	3/2018	315.03 -	315.03	-	09/2018 -	09/2018
375	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756	3/2018	285.68 -	285.68	-	09/2018 -	09/2018
376	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755	3/2018	239.30 -	239.30	-	09/2018 -	09/2018
377	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754	3/2018	339.57 -	339.57	-	09/2018 -	09/2018
378	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753	3/2018	500.09 -	500.09	-	09/2018 -	09/2018
379	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752	2/2017	387.00 -	387.00	-	09/2018 -	09/2018
380	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749	3/2018	234.27 -	234.27	-	10/2018 -	10/2018
381	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748	2/2018	391.00 -	391.00	-	10/2018 -	10/2018
382	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744	3/2015	262.97 -	262.97	-	10/2018 -	10/2018
383	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
384	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
385	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
386	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
387	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
388	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
<u>National Highways Authority Of India</u>							
389	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
390	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	1,910.00	01/2019 -	01/2019
391	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
392	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
393	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
394	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
395	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	738.75	03/2020 -	03/2020
396	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
397	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	237.07	07/2019 -	07/2019
398	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	87.19	07/2019 -	07/2019
399	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	301.30	04/2019 -	04/2019
400	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]	3/2016	229.37 -	229.37	6.39	11/2018 -	11/2018
401	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	110.58	04/2019 -	04/2019
402	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION [N24000548]	2/2016	997.15 -	997.15	328.14	03/2019 -	03/2019
403	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) [N24000546]	2/2016	273.20 -	273.20	18.36	02/2019 -	02/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
404	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]	1/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018
405	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	409.11	04/2019 -	04/2019
406	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	708.59	06/2019 -	06/2019
407	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]	1/2016	701.12 -	701.12	841.92	05/2019 -	05/2019
408	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]	6/2015	1,583.79 -	1,583.79	392.08	01/2019 -	01/2019
409	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
410	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	1,041.10	138.78	04/2019 -	04/2019
411	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
412	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]	8/2016	320.30 -	320.30	174.91	01/2019 -	01/2019
413	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]	8/2016	248.97 -	248.97	-	05/2019 -	05/2019
414	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]	8/2016	1,167.42 -	1,167.42	191.05	03/2019 -	03/2019
415	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]	8/2016	227.49 -	227.49	-	01/2019 -	01/2019
416	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	234.18	04/2020 -	04/2020
417	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	72.07	09/2019 -	09/2019
418	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]	7/2016	331.46 -	331.46	232.15	10/2018 -	10/2018
419	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
420	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	7/2015	2,128.72 -	2,128.72	162.60	04/2019 -	04/2019
421	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	21.98	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
422	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
423	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
424	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
425	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
426	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
427	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
428	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
429	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	5.00	03/2020 -	03/2020
430	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]	1/2017	244.90 -	244.90	51.51	05/2019 -	05/2019
431	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]	11/2016	446.17 -	446.17	-	03/2019 -	03/2019
432	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
433	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	950.69	277.34	08/2019 -	08/2019
434	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
435	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]	7/2015	1,885.74 -	1,885.74	-	05/2019 -	05/2019
436	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	41.20	03/2019 -	03/2019
	Total		61,123.50 -	61,664.75	7,927.84		
	<u>STEEL</u>						
	National Mineral Development Corporation (Nmhc)						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
437	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	14,283.70	05/2015 06/2019	06/2019
438	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	2,907.00	29.51	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
439	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	63.54	06/2019 -	06/2019
	Total		16,605.87 -	18,694.87	14,376.75		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
440	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	12.40	04/2018 10/2018	10/2018
441	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	72.46	05/2018 10/2018	10/2018
442	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	231.80	39.75	10/2018 10/2018	10/2018
443	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	169.45 -	169.45	78.34	08/2018 10/2018	10/2018
444	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	214.10	33.46	05/2018 10/2018	10/2018
445	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	212.70	37.08	05/2018 10/2018	10/2018
446	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	167.68	30.21	04/2018 10/2018	10/2018
	Total		1,327.77 -	1,326.57	303.70		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
447	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	197.33	5.08	04/2019 06/2020	06/2020
448	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB [N28000120]	1/2018	430.00 -	430.00	-	09/2018 -	09/2018
449	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	1.84	11/2019 -	11/2019
450	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
451	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUDEM AP [N28000108]	1/2018	206.58 -	206.58	.02	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
452	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	55.43	06/2019 -	06/2019
453	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	.36	05/2020 -	05/2020
454	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	209.00	52.00	10/2019 -	10/2019
455	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	8/2016	294.00 -	294.00	112.23	04/2019 06/2019	06/2019
456	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]	12/2016	246.31 -	246.31	21.94	02/2020 09/2020	09/2020
457	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	6.61	03/2020 -	03/2020
458	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	5/2016	164.00 -	164.00	117.49	11/2018 09/2018	09/2018
	<u>Lucknow Metro Rail Corporation Limited</u>						
459	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Maharastra Metro Rail Corporation Ltd.</u>						
460	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	1,793.83	11/2021 -	11/2021
	<u>Nagpur Metro Rail Corporation Ltd</u>						
461	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	4,256.12	03/2018 12/2019	12/2019
	<u>National Building Construcion Corporation Ltd</u>						
462	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,376.53	11/2019 -	11/2019
	Total		34,119.24 -	34,294.47	12,336.25		
	Grand Total		8,43,753.84	9,71,356.73	2,87,640.92		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	-	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
5	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	Total		18,475.22 -	19,005.69			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
9	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	170.37	05/2018 -	08/2018	1.41

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	291.29	08/2020 -	08/2020	1.85
	Total		453.64 -	461.66			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
11	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	-	13.31
12	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
13	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014	07/2016	312.99 -	322.00	08/2018 -	-	2.88
	Total		987.47 -	1,036.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
16	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
18	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RU [N16000255	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	<u>Oil & Natural Gas Corporation Limited</u>						
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
	<u>Oil India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	03/2019	24.47
21	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		6,548.66 -	7,870.53			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
22	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
24	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
25	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
26	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
27	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
28	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
29	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
30	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
31	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
32	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
	<u>North East Electric Power Corporation</u>						
33	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
34	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,534.00	11/2008 -	12/2018	42.42
35	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
36	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
37	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
38	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15
39	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	09/2018	42.83
	<u>Satluj Jal Vidyut Nigam Limited</u>						
40	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
41	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2021	64.77
42	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,23,280.12 -	1,63,868.10			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
43	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	240.00	03/2019 -	03/2019	30.39
44	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44
45	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	389.99
46	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
47	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
48	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	4,817.69	03/2024 -	03/2024	32.83
	<u>Container Corporation Of India</u>						
49	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
50	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	-	03/2021	192.42
51	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	-	03/2023	290.95
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	163.78

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
54	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
55	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2012 -	03/2020	3.33
56	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	-	323.32
57	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
58	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
59	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	- -	03/2021	296.21
60	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
61	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
62	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
63	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
64	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
65	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
66	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	- -	12/2018	192.15
67	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	- -	12/2021	71.96
	<u>East Coast Railway</u>						
68	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	06/2021	29.71
69	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
70	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	-	542.46
71	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
72	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	-	818.15

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
73	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.73 -	729.92	-	03/2021	315.36
74	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	2,614.36	-	03/2022	817.09
75	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
76	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	614.25 -	2,532.49	03/2019 12/2009	03/2019	312.29
77	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	584.41 -	1,005.23	02/2013 -	06/2016	72.01
78	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	501.78 -	1,960.06	12/2010 -	-	290.62
79	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	673.85	02/2012 -	-	159.66
80	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]	04/2010	136.55 -	534.24	03/2016 -	03/2020	291.24
81	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	528.34	03/2017 -	-	44.68
82	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
83	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.90	03/2020 -	03/2020	27.98
84	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	115.27 -	857.30	03/2005 -	-	643.73
85	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	278.66 -	1,255.98	02/2012 -	-	350.72
86	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
87	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
88	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
89	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	193.08 -	683.88	12/2011 -	-	254.20
90	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
91	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	318.50 -	852.80	03/2006 -	-	167.76

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
92	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	23.56 -	1,330.73	-	-	5,548.26
93	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	-	-	51.49
94	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,142.49	03/2022 -	03/2022	133.90
95	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	-	-	27.07
96	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	563.51 -	1,813.59	03/2016 -	-	221.84
97	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	236.21 -	1,395.63	03/2017 -	-	490.84
	<u>Metropolitan Rapid Transport Projects</u>						
98	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
99	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
100	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
101	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
102	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
103	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
104	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
	<u>North East Frontier Railway</u>						
105	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
106	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
107	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,600.00	03/2014 -	12/2020	92.19
108	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	3,230.02 -	5,820.00	04/2008 12/2011	12/2019	80.18
109	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,040.00	12/2008 -	12/2020	157.59
110	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2022	210.02

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
111	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
112	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2021	302.54
113	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	12/2021	28.95
114	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,374.00	03/2014 -	03/2019	195.45
115	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	1,300.00	- -	03/2020	289.50
116	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
117	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	726.00	- -	03/2020	227.88
118	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11
119	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	451.00	03/2019 -	03/2019	59.05
120	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
121	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
122	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
123	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
124	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	03/2018	128.39
125	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00	03/2019 -	03/2020	75.48
126	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12
127	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2021	1.62
<u>North Eastern Railway</u>							
128	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56	06/2018 -	06/2018	89.54
129	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
130	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	12/2022 -	12/2022	212.37

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
131	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [N220100256]	04/1999	744.71 -	1,126.79	-	-	51.31
132	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	8.10
133	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	-	358.99
134	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	871.56	12/2021 -	12/2021	257.52
135	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	-	03/2018	142.44
136	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	08/2018	35.17
137	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2019	61.80
138	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
139	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
140	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16
141	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	12/2018	70.07
142	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
143	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	-	03/2022	18.56
	<u>North Western Railway</u>						
144	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,116.00	03/2014 -	03/2019	70.85
145	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	02/1997	410.08 -	795.01	02/2019 -	02/2019	93.87
146	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	03/2020	14.33
147	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	-	-	26.25
148	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55
149	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2019	41.64
150	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97	-	-	38.23
151	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2018	24.47

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
152	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	-	-	33.76
153	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	-	33.81
154	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	865.00	03/2020 -	12/2019	105.86
155	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35
156	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	12/2018	19.86
157	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	02/2019	44.16
	<u>Northern Railway</u>						
158	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
159	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
160	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	12/2011 -	-	117.77
161	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
162	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
163	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
164	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
165	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
166	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
167	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
168	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2019	55.57
169	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	1,202.70	02/2015 -	12/2021	.00
170	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	85.99
171	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2018	48.26
172	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,850.00	03/2008 -	03/2019	152.45

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	7,000.00	12/2026 -	12/2026	568.65
174	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	2,062.20	- -	03/2022	112.52
175	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
176	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	383.54 -	555.00	03/2010 -	12/2019	44.70
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
178	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
179	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
180	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
181	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39
182	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
183	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	970.00	03/2020 -	03/2021	2.32
	<u>Railway Electrification</u>						
184	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
185	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
186	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,955.27	03/2023 -	03/2023	5.29
187	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	2,154.83	- -	-	133.40
188	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	761.37	- -	-	168.52
189	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
190	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	10/2018	538.84
191	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,501.83	03/2000 -	12/2023	3,50,083.00
192	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	815.00	- -	-	77.85

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
193	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	1,025.00 -	- -	03/2017	723.76
194	KONDAPALLI-KOTHAGUDEM - [N22000364	04/2013	616.08 -	723.00 -	- -	-	17.35
	<u>South East Central Railway</u>						
195	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16 -	- -	-	186.92
196	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	1,756.00 -	04/2020 -	04/2020	243.06
197	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	2,686.63 -	03/2023 -	03/2023	40.77
198	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	04/2010	585.93 -	1,420.39 -	02/2019 -	02/2019	142.42
199	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	403.00 -	12/2021 -	12/2021	75.98
200	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46 -	03/2012 -	03/2020	141.22
201	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,279.00 -	12/2019 -	12/2019	46.67
202	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,919.00 -	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
203	MM FROM BURAMARA-CHAKULIA - [N22000305	04/2008	466.48 -	1,000.00 -	- -	12/2024	114.37
204	MM FROM PANSKURA-GHATAL NL - [N22000309	04/2011	276.69 -	426.00 -	- -	03/2030	53.96
205	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00 -	03/2007 03/2007	-	564.94
206	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69 -	06/2005 -	-	155.02
207	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00 -	12/2016 -	12/2018	153.41
208	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00 -	- -	03/2025	131.89
209	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00 -	03/2015 -	03/2024	54.99
210	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161	04/2011	289.64 -	760.00 -	- -	-	162.39
211	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00 -	03/2015 -	-	53.44
212	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81 -	12/2015 -	12/2018	69.92
213	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	365.00 -	- -	12/2018	41.36

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
214	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	-	-	278.13
215	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
216	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
217	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
218	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24. - [N22000491]	04/1998	1,027.40 -	2,373.00	03/2022 -	03/2022	130.97
	<u>South Western Railway</u>						
219	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	12/2023	57.65
220	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	-	12/2023	2.29
221	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,156.94	03/2020 -	03/2022	.00
222	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	958.00	03/2020 -	03/2022	11.34
223	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
224	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	-	-	141.40
225	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	-	-	491.45
226	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	-	-	300.71
227	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2019	185.98
228	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	-	-	210.34
229	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	-	-	295.78
230	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	-	-	294.63
231	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2020	222.39
232	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	-	-	79.80

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
233	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	02/2019	627.74
234	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
235	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
236	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
237	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
238	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
239	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
240	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	369.83	- -	-	92.90
241	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	03/2019	1,391.30
242	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	302.02	03/2005 -	-	12.33
243	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
244	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55 -	330.32	03/2009 -	-	65.53
245	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
246	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
247	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
248	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
<u>Western Railway</u>							
249	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	5,554.24	03/2022 -	03/2022	58.53
250	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
251	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
252	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,783.00	03/2020 -	03/2020	235.41

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		1,47,194.57	3,13,102.63			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
253	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
	<u>Ministry Of Road Transport And Highways</u>						
254	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
255	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	284.00	11/2019 -	11/2019	.17
256	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
257	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
258	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	-	28.93
259	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
260	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
261	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
262	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
263	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	-	42.25
264	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
265	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
266	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
267	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
268	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
269	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	07/2018	880.06
270	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
271	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
272	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
273	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
274	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
275	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
276	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
277	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
278	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
279	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
280	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
281	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
282	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
283	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
Public Works Dept Of State							
284	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	-	6.02
285	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
286	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	11/2018	.12
287	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	10/2018	.01
288	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		26,512.85 -	41,226.74			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
289	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Mumbai Port Trust</u>						
290	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
291	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
292	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	2,907.00	06/2020 -	06/2020	255.38
	<u>Rastriya Ispat Nigam Limited</u>						
293	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,161.00 -	3,395.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
294	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
295	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	12/2018 -	07/2020	18.69
	<u>Central Public Works Department</u>						
296	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	04/2014	332.72 -	342.00	09/2016 -	09/2018	2.79
297	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]	11/2012	270.83 -	270.83	11/2014 -	02/2019	.00
298	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	-	44.75
299	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
300	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.60
	<u>Chennai Metro Rail Ltd</u>						
301	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
302	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
303	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>National Building Construcion Corporation Ltd</u>						
304	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		33,115.88 -	40,626.66			
	Grand Total		3,77,658.37	6,27,725.39			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above						(September 2018)			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,687.52	09/2010 09/2016	03/2019	102	30
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	12,463.00	12/2015 11/2016	06/2020	54	43
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,760.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	9,827.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	74,849.00	37,737.52				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	546.69	01/2011 -	09/2018	92	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
	Total		624.07 -	994.86	632.48				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
7	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
8	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	295.38	04/2015 -	04/2019	48	-
	<u>Central Coal Fields Limited</u>								
9	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	139.30	03/2012 -	03/2019	84	-
10	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	155.09	03/2012 -	03/2019	84	-
11	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	352.34	03/2016 -	03/2019	36	-
12	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	82.97	03/2014 -	03/2019	60	-
13	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	93.93	03/2011 -	03/2020	108	-
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	125.15	07/2012 -	03/2021	104	-
	<u>Eastern Coal Fields Limited</u>								

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	376.04	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
16	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	581.54	03/2013 -	03/2019	72	-
17	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	264.26	03/2010 -	03/2019	108	-
18	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	363.95	03/2017 -	03/2020	36	-
19	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	239.22	03/2013 -	03/2020	84	-
20	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	33.53	03/2018 -	03/2020	24	-
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	234.48	03/2012 -	03/2021	108	-
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	104.48	03/2019 -	03/2021	24	-
23	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	44.91	03/2019 -	03/2021	24	-
	<u>Neyveli Lignite Corporation</u>								
24	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,666.08	12/2015 10/2018	12/2018	36	2
	<u>Northern Coal Fields Limited</u>								
25	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]JNCL, UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	572.40	03/2018 -	03/2019	12	-
	<u>Singareni Colliers Company Limited</u>								
26	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	154.21	03/2015 -	03/2019	48	-
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	204.26	06/2015 -	03/2019	45	-
28	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	160.45	03/2016 -	03/2019	36	-
29	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
30	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	146.45	07/2016 -	03/2020	44	-
31	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	12.69	03/2015 -	03/2021	72	-
32	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2021	72	-
33	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	437.51	353.61	03/2015 -	03/2021	72	-
34	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	-
	<u>South-Eastern Coal Fields Limited</u>								
35	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	-
36	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	163.85	03/2016 -	03/2019	36	-

Costing Rs. 150 Crore and above

(September 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
37	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
38	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	202.31	03/2014 -	03/2020	72	-
	<u>Western Coal Fields Limited</u>								
39	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 409.68	409.68	93.19	03/2023 02/2017	03/2023	0	73
	Total		18,829.43 -	19,172.45	11,881.85				
	<u>STEEL</u>								
	<u>Rastriya Ispat Nigam Limited</u>								
40	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	89.83	08/2018 -	10/2018	2	-
41	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	211.25	07/2018 -	11/2018	4	-
42	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	647.10	09/2018 -	01/2019	4	-
43	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	238.69	10/2016 -	03/2019	29	-
44	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	971.76	12/2017 -	09/2019	21	-
	<u>Steel Authority Of India Limited (Sail)</u>								
45	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	842.32	12/2017 -	11/2018	11	-
46	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	343.36	10/2017 -	12/2018	14	-
47	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,426.76	04/2018 -	02/2019	10	-
	Total		10,985.85 -	10,773.25	5,771.07				
	<u>PETROLEUM</u>								
	<u>Gas Authority Of India Limited</u>								
48	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	100.65	04/2018 -	12/2018	8	-
	<u>Indian Oil Corporation Limited</u>								
49	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	1,330.00	1,308.86	06/2018 -	10/2018	4	-
50	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	341.41	10/2017 -	03/2019	17	-
51	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	793.22	07/2019 -	09/2019	2	-
52	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	4,497.00	283.91	12/2018 -	12/2020	24	-
53	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	1.18	10/2020 -	05/2021	7	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
54	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]OCL,ASSAM	08/2018	557.00	557.00	64.70	02/2020	02/2022	24	-
	<u>Oil & Natural Gas Corporation Limited</u>								
55	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52	390.52	154.56	03/2019	04/2019	1	-
56	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63	2,665.65	1,842.42	03/2015	12/2019	57	21
	<u>Oil India Limited</u>								
57	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56	438.84	180.72	03/2017	03/2019	24	4
58	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00	350.00	2.06	01/2019	09/2019	8	-
	Total		14,049.98	15,138.69	5,073.69				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
59	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12	8,112.12	980.00	04/2020	10/2023	42	-
	<u>National Hydro-Electric Power Corporation</u>								
60	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59	9,394.80	7,058.21	09/2009	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
61	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35	8,150.00	7,154.15	09/2011	10/2018	85	4
62	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00	7,998.00	7,128.72	05/2014	05/2019	60	16
63	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89	9,750.89	8,554.00	12/2016	08/2019	32	-
64	NPGL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60	13,731.26	12,079.00	01/2018	05/2020	28	-
	<u>Power Grid Corporation Of India Limited</u>								
65	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41	2,333.71	1,528.12	09/2017	09/2018	12	-
66	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00	1,364.00	1,190.30	12/2015	09/2018	33	-
67	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80	1,731.10	1,461.65	11/2012	10/2018	71	1
68	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13	2,702.65	2,529.92	09/2014	10/2018	49	1
69	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63	374.63	187.24	04/2016	10/2018	30	10
70	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47	1,455.47	1,028.69	07/2018	10/2018	3	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
71	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	150.99	88.66	07/2018 -	10/2018	3	-
72	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE	08/2008	771.00 1,624.00	1,624.00	1,429.45	02/2013 -	10/2018	68	-
73	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,654.96	12/2012 06/2018	11/2018	71	5
74	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 3,190.27	3,190.27	2,281.28	12/2015 06/2018	11/2018	35	5
75	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	145.22	03/2016 09/2018	11/2018	32	2
76	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	148.92	02/2016 09/2018	11/2018	33	2
77	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	229.40	03/2018 09/2018	11/2018	8	2
78	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	630.56	09/2017 09/2018	11/2018	14	2
79	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	206.21	11/2017 10/2018	11/2018	12	1
80	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	215.81	03/2017 09/2018	11/2018	20	2
81	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	1,750.00	1,276.62	06/2018 -	11/2018	5	-
82	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,534.00	2,051.63	11/2008 09/2018	12/2018	121	3
83	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 534.02	534.02	426.98	08/2014 09/2018	12/2018	52	3
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	419.63	06/2016 09/2018	12/2018	30	3
85	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	74.71	03/2018 -	12/2018	9	-
86	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,518.90	04/2018 09/2018	12/2018	8	3
87	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	1,420.89	07/2018 -	12/2018	5	-
88	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	287.99	161.82	06/2018 -	12/2018	6	-
89	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,538.37	10/2012 12/2018	02/2019	76	2

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	139.34	01/2019 -	03/2019	2	-
91	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	52.14	09/2018 -	06/2019	9	-
92	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	238.92	04/2018 -	11/2019	19	-
93	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	840.87	12/2018 -	12/2019	12	-
94	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,652.57	802.18	12/2018 -	12/2019	12	-
95	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	.80	09/2019 -	02/2020	5	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
96	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	499.77	12/2016 -	12/2018	24	-
97	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	309.48	11/2017 -	12/2018	13	-
	<u>Thdc India Limited</u>								
98	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	195.00	02/2014 02/2018	03/2019	61	13
99	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,611.13	02/2016 12/2020	05/2021	63	5
100	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,105.30	1,468.26	06/2013 -	12/2021	102	-
	Total		91,989.33 -	1,21,086.44	78,957.91				
	<u>HEAVY INDUSTRY</u>								
	<u>Indira Gandhi Centre For Atomic Research</u>								
101	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]JGCAR,DELHI	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37	-
	Total		1,554.00 -	1,554.00	161.86				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
102	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	237.86	05/2017 -	09/2018	16	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
103	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	523.00	355.00	03/2018 -	09/2018	6	-
104	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	58.52	02/2018 -	12/2018	10	-
105	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	71.00	05/2018 -	08/2019	15	-
	Total		1,316.17 -	1,333.59	722.38				
	<u>RAILWAYS</u>								
	<u>Container Corporation Of India</u>								
106	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	137.61	03/2019 -	08/2019	5	-
107	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	407.32	03/2018 -	12/2019	21	-
108	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	285.62	03/2019 -	12/2019	9	-
109	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	2.98	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
110	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 335.77	1,156.41	876.49	03/2012 -	03/2020	96	-
111	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	516.02	640.78	03/2012 -	03/2020	96	-
112	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	-
113	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	-
114	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	238.38	03/2020 -	03/2021	12	-
115	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	.59	03/2019 -	03/2021	24	-
116	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	-
117	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	-
118	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	-
119	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	-
120	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	-
	<u>East Coast Railway</u>								
121	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	742.32	02/2019 -	03/2020	13	-
122	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	210.71	12/2018 -	03/2020	15	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
123	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	83.66	11/2018 -	03/2021	28	-
124	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,088.86	03/2009 -	06/2021	147	-
125	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	810.28 843.04	843.04	73.71	10/2020 -	03/2022	17	-
126	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	564.41	06/2021 -	03/2023	21	-
	<u>Eastern Railways</u>								
127	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	614.25 -	2,532.49	841.36	03/2019 12/2009	03/2019	0	111
128	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	1,125.89	899.49	03/2016 12/2010	03/2020	48	111
129	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	136.55 -	534.24	143.74	03/2016 -	03/2020	48	-
	<u>Metropolitan Rapid Transport Projects</u>								
130	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
131	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,316.34	03/2004 -	03/2020	192	-
	<u>North East Frontier Railway</u>								
132	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	3,230.02 4,857.00	5,820.00	5,224.22	04/2008 12/2011	12/2019	140	96
133	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 274.41	614.00	267.93	03/2019 -	03/2020	12	-
134	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	538.17	03/2019 -	03/2020	12	-
135	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	385.84	12/2015 -	03/2020	51	-
136	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 -	551.00	595.01	03/2019 -	03/2020	12	-
137	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 -	3,040.00	3,036.52	12/2008 -	12/2020	144	-
138	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	928.89	03/2019 -	03/2021	24	-
139	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 2,446.57	3,000.00	655.38	03/2015 10/2021	12/2021	81	2
140	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	7,919.05	03/2011 -	03/2022	132	-
141	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	-
142	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,232.00	193.12	03/2022 -	12/2022	9	-
	<u>North Eastern Railway</u>								

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
143	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,793.99	04/1999 -	12/2018	236	-
144	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,177.96	-	03/2014 -	12/2019	69	-
145	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	-	04/2016 -	01/2022	69	-
146	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
147	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
148	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	5.83	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
149	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	346.35	282.12	11/2018 -	12/2018	1	-
150	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	687.70	03/2015 -	03/2020	60	-
	<u>Rail Vikas Nigam Ltd.</u>								
151	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	370.38	03/2009 03/2009	12/2018	117	117
152	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	388.06	02/2006 -	12/2018	154	-
153	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,277.02	12/2017 09/2009	03/2019	15	114
154	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	1,850.00	1,863.44	03/2008 06/2008	03/2019	132	129
155	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	383.54 -	555.00	564.30	03/2010 -	12/2019	117	-
156	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	977.00	939.56	03/2019 -	03/2020	12	-
157	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	561.52	03/2016 03/2017	12/2020	57	45
158	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	970.00	918.32	03/2020 -	03/2021	12	-
159	BANASPAANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	942.95	879.77	03/2019 -	03/2021	24	-
160	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	868.67	12/2020 -	03/2021	3	-
161	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 245.00	1,202.70	618.94	02/2015 -	12/2021	82	-
162	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	631.78 632.00	1,195.00	626.99	12/2012 -	03/2022	111	-
163	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	819.86	03/2020 -	03/2022	24	-

Costing Rs. 150 Crore and above

(September 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
164	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,804.86	03/2016 -	03/2025	108	-
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	764.97	03/2016 -	03/2025	108	-
166	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
<u>South Central Railway</u>									
167	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 164.36	1,050.00	999.64	02/2009 -	10/2018	116	-
168	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 236.41	3,501.83	719.03	03/2000 03/2019	12/2023	285	57
169	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR, MULTI STATE	04/2008	2,206.29 -	1,996.94	215.72	03/2014 03/2023	03/2024	120	12
<u>South East Central Railway</u>									
170	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR, MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	-
<u>South Eastern Railway</u>									
171	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	377.00	147.34	12/2016 08/2018	12/2018	24	4
172	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA	11/2015	969.83 -	969.83	348.22	03/2020 03/2020	03/2022	24	24
<u>South Western Railway</u>									
173	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	578.00 578.00	578.00	439.87	03/2020 11/2015	03/2020	0	52
174	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 -	889.52	10.91	03/2017 -	03/2020	36	-
175	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,156.94 1,141.00	1,156.94	646.90	03/2020 03/2020	03/2022	24	24
176	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 860.43	958.00	469.91	03/2020 03/2020	03/2022	24	24
<u>Southern Railway</u>									
177	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR, TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
<u>West Central Railway</u>									
178	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR, MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	-
179	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
<u>Western Railway</u>									
180	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	83.10	03/2012 -	03/2019	84	-
181	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	1,037.15 1,037.15	1,037.15	882.80	03/2021 03/2020	03/2021	0	12

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
182	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	202.09	03/2021 03/2019	03/2021	0	24
183	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 2,473.40	5,554.24	1,047.53	03/2022 03/2019	03/2022	0	36
184	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	593.72	03/2022 03/2019	03/2022	0	36
185	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	599.20	03/2022 03/2019	03/2022	0	36
186	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	858.96	549.56	03/2019 03/2019	03/2022	36	36
	Total		88,804.59 -	1,40,818.25	56,717.68				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
187	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
188	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
189	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
190	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
191	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
192	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
193	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	118	-
194	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2018	54	-
195	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	09/2018	60	-
196	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	414.14	01/2014 -	09/2018	56	-
197	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	114	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
198	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	101	-
199	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	279.14	211.16	05/2017 -	10/2018	17	-
200	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	596.06	10/2017 -	10/2018	12	-
201	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 09/2017	10/2018	84	13
202	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67	-
203	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	674.52	01/2014 -	11/2018	58	-
204	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	42.79	03/2018 -	11/2018	8	-
205	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27	-
206	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	883.96	02/2013 -	12/2018	70	-
207	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.17	12/2013 -	12/2018	60	-
208	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	974.83	07/2013 -	12/2018	65	-
209	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	-
210	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	-
211	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	-
212	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	563.48	11/2013 -	12/2018	61	-
213	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	351.24	09/2017 -	12/2018	15	-
214	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	54.89	06/2016 -	12/2018	30	-
215	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	647.00	04/2018 -	12/2018	8	-
216	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,302.48	07/2017 -	12/2018	17	-
217	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	1,871.34	2,263.50	01/2018 -	12/2018	11	-
218	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,056.03	06/2012 -	12/2018	78	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
219	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	516.13	400.35	04/2018 -	12/2018	8	-
220	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	03/2019	9	-
221	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	245.89	08/2012 -	03/2019	79	-
222	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,584.87	07/2015 -	03/2019	44	-
223	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	374.75	06/2014 -	03/2019	57	-
224	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	-
225	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	414.00	169.20	05/2018 -	03/2019	10	-
226	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	574.28	51.47	07/2018 -	03/2019	8	-
227	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	444.33	11/2016 -	03/2019	28	-
228	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	03/2019	31	-
229	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	934.46	104.98	03/2018 -	03/2019	12	-
230	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36	-
231	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	479.20	6.14	05/2018 -	03/2019	10	-
232	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29	-
233	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	505.00	165.31	05/2018 -	04/2019	11	-
234	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	1,388.00	791.18	08/2018 -	04/2019	8	-
235	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	17.60	12/2017 -	04/2019	16	-
236	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	14.94	06/2018 -	04/2019	10	-
237	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	-

Costing Rs. 150 Crore and above

(September 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
238	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	881.98	11/2017 -	05/2019	18	-
239	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	105.70	06/2018 -	05/2019	11	-
240	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,869.30	11/2011 -	06/2019	91	-
241	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,042.82	03/2013 -	06/2019	75	-
242	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	823.46	07/2013 -	06/2019	71	-
243	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	3,386.77	02/2014 -	06/2019	64	-
244	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,407.12	09/2016 -	06/2019	33	-
245	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	96.48	12/2017 -	06/2019	18	-
246	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	5.65	04/2018 -	06/2019	14	-
247	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	168.88	08/2018 -	06/2019	10	-
248	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	-
249	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	37.39	03/2019 -	06/2019	3	-
250	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	07/2019	76	-
251	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-
252	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	502.66	11/2018 -	07/2019	8	-
253	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	22.02	03/2019 -	07/2019	4	-
254	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	535.30	06/2019 -	09/2019	3	-
255	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
256	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	133.02	04/2019 -	10/2019	6	-
257	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,310.42	04/2019 -	11/2019	7	-

Costing Rs. 150 Crore and above

(September 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
258	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,136.31	03/2014 -	12/2019	69	-
259	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2019	68	-
260	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	56.79	04/2018 -	04/2020	24	-
261	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	-	03/2020 -	04/2020	1	-
262	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	97.53	02/2020 -	05/2020	3	-
263	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	196.43	03/2020 -	05/2020	2	-
264	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	-	03/2020 -	05/2020	2	-
265	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2	-
266	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	48.27	03/2020 -	06/2020	3	-
267	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	279.54	03/2020 -	06/2020	3	-
268	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	-	09/2017 -	06/2020	33	-
269	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	182.85	03/2020 -	08/2020	5	-
270	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	50.30	03/2020 -	08/2020	5	-
271	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	9.12	03/2019 -	11/2020	20	-
272	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	-	03/2020 -	11/2020	8	-
273	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	20.00	03/2017 -	11/2020	44	-
274	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	-
	Public Works Dept Of State								

Costing Rs. 150 Crore and above

(September 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
275	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	352.05	201.35	11/2017 -	10/2018	11	-
276	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	231.56	09/2017 -	11/2018	14	-
	Total		75,482.85 -	78,261.00	50,801.20				
	<u>SHIPPING AND PORTS</u>								
	<u>Kamarajar Port Limited</u>								
277	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-
	<u>Mumbai Port Trust</u>								
278	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	-
	Total		966.39 -	927.36	412.57				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
279	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
280	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	2,078.80	12/2018 -	07/2020	19	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
281	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
282	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	342.00	321.13	09/2016 03/2018	09/2018	24	6
283	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	379.31	05/2017 08/2018	11/2018	18	3
284	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	626.67	12/2015 -	12/2018	36	-
285	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	143.14	08/2016 -	01/2019	29	-

Costing Rs. 150 Crore and above

(September 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
286	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 210.00	270.83	163.97	11/2014 -	02/2019	51	-
287	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	-
288	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL	10/2014	162.88 -	162.88	81.75	04/2018 -	07/2019	15	-
289	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	540.42	152.99	07/2019 -	09/2019	2	-
290	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
291	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 216.69	216.69	52.00	03/2015 11/2018	11/2019	56	12
292	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.24	03/2016 -	12/2019	45	-
293	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	282.67	10/2019 -	03/2020	5	-
294	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	17.72	06/2017 07/2017	06/2020	36	35
295	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	-	07/2020 09/2018	09/2020	2	24
	<u>Hindustan Steelwork Construction Limited</u>								
296	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
297	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
298	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
299	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
300	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	Total		72,741.96 -	75,283.69	7,735.36				
	Grand Total		4,57,798.62	5,64,856.58	2,65,002.57				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	03/2019	3492	102
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2018	309.46	92

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2019	430.45	36
8	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
9	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2019	365.01	45
10	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
11	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2018	5907.11	36
12	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
13	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2019	258.56	36
14	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2019	457.77	72
15	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.5	72
16	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
17	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
18	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2020	479.53	84
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2019	209.78	48
20	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54
22	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
23	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
24	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
25	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
26	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
27	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
28	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
29	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
30	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
31	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	36
32	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
33	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
34	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
35	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
36	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
37	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2021	479.15	24
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2021	337.66	24
39	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
40	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL)	NCL	06/2011	03/2018	03/2019	1131.28	12
41	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2019	510.85	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
42	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	RCF	02/2016	12/2017	10/2018	482.85	10
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	03/2018	09/2018	505.58	6
46	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	12/2018	152.95	10
47	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	16

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	IGCAR	08/2016	08/2016	09/2019	1554	37

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	02/2022	557	24
50	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	05/2021	466.43	7
51	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	52
52	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2019	352.56	24
53	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
54	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
55	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
56	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	12/2018	2899.93	19
57	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
58	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
59	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2019	861.79	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
61	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
62	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2019	3190.69	13
63	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915	74
64	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2019	2465.15	72
65	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
66	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	12/2018	327.78	8
67	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9
68	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
69	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
70	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	12/2020	4497	24

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
71	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	PGCIL	08/2008	02/2013	10/2018	771	68
72	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
73	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	21
74	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
75	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	11/2018	2144	71
76	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
77	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	10/2018	4375.35	85
78	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPSPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2019	5151.37	12
79	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	11/2018	196.58	33
80	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	10/2023	8112.12	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
82	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	10
83	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	20
84	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
85	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	32
86	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	10/2018	374.63	30
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	12/2018	539.82	30
88	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	06/2019	522.29	31
89	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	11/2018	155.57	32
90	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	11/2018	268.8	8
91	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
92	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	23
93	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	10/2018	1272.8	71
94	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2018	197.4	9
95	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	11/2018	1071.24	14
96	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
97	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	61
98	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	09/2018	955	33
99	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	06/2019	175.64	9
100	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	12964.6	28
101	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	08/2019	9750.89	32
102	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
103	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	99

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2019	4824.12	76
105	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353	60
106	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	24
107	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	PGCIL	04/2015	04/2018	12/2018	3705.61	8
108	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.9	111
109	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	10/2018	1940.13	49
110	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657	63
111	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	54
112	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	123
113	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	28
114	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 Mw)	NTPC	12/2012	06/2017	06/2019	11846	24
115	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	11/2018	2514.88	35
116	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	11/2018	305.04	20
117	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
118	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	11/2019	454.11	19
119	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
120	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	PGCIL	04/2016	06/2018	12/2018	287.99	6
121	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	11/2018	307.18	12
122	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	102
123	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2018	297.33	52
124	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2018	1779.29	121
125	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	12/2018	330	13
126	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND	PGCIL	12/2014	12/2018	12/2019	4754.42	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DISTRIBUTION SYSTEM IN A P						

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
127	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
128	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	96
129	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	61
130	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
131	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	10/2022	622.5	66
132	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	12/2018	609.04	236
133	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
134	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
135	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2019	1185.64	15
136	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
137	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2018	133.41	117
138	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21
139	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2018	261.7	154
140	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	81
141	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
142	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2022	1160.48	144
143	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2019	732.81	132
144	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINROY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
145	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
146	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2020	136.55	48
147	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	03/2016	12/2023	1801.01	93

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
149	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
150	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2022	2288.7	12
151	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2206.29	120
152	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
153	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
154	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
155	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	03/2016	03/2020	1125.89	48
156	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	12/2019	3230.02	140
157	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
158	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	04/1997	03/2012	03/2020	324.73	96
159	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	12/2020	1180.19	144
160	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	147
161	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2022	4454.17	132
162	KOSI BRIDGE (NL), ECR	ECR	04/2002	03/2012	03/2020	499.41	96
163	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2019	495.74	69
164	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
165	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2021	532.87	24
166	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2021	2326.52	81
167	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
168	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2019	1142	60
169	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
170	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	03/2021	2500	220

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
171	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	111
172	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	383.54	117
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
174	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
175	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	10/2018	164.36	116
176	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	12/2023	1723	285
177	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	03/2001	12/2024	2315	285
178	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
179	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
180	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
181	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2020	1111.99	13
182	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2022	810.28	17
183	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2018	148.77	24
184	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	03/2020	678.54	12
185	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2020	829.74	60
186	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
187	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651	108
188	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	12/2018	309.44	36
189	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	10/2022	569.63	31
190	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314	12
191	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
192	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	36
193	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2022	1156.94	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
194	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	03/2022	860.43	24
195	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
196	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
197	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
198	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	12
199	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
200	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
201	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2021	528.57	24
202	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	12/2019	493.17	21
203	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
204	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
205	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	10/2021	1491.47	19
206	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2021	1763.93	19
207	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	28
208	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2020	1172.92	15
209	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	12/2022	2232.32	9
210	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	03/2022	969.83	24
211	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
212	TRANSMISSION LINE BETWEEN CHENNAI- HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
213	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	01/2022	213	69
214	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
215	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
216	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU- SHAHGANJ (EXCL. MAU-INDARA) PATCH	NER	04/2016	03/2014	12/2019	1177.96	69

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DOUBLING.						
217	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
218	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
219	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2019	478.51	69
220	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2019	942.69	57
221	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	12/2018	709	15
222	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	03/2019	425.19	30
223	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	05/2019	1387.11	18
224	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2019	563.92	18
225	PADI - DAHOD	NHAI	11/2014	05/2017	10/2018	279.14	17
226	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	NHAI	09/2015	03/2018	11/2018	567.51	8
227	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	10/2018	597	12
228	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	03/2019	414.51	10
229	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	12/2018	602.95	30
230	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	03/2019	574.28	8
231	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	04/2019	505	11
232	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	05/2019	1083	11
233	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2019	934.46	12
234	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
235	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	06/2019	707.82	10
236	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	04/2019	804.97	10
237	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	NHAI	05/2015	05/2017	06/2019	581.84	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
239	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
240	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
241	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
242	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
243	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	03/2019	946	9
244	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	07/2019	1423.96	8
245	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
246	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
247	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
248	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	12/2018	1170.52	78
249	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	06/2019	726.67	14
250	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	03/2019	479.2	10
251	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
252	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	12/2018	516.13	8
253	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2018	571	62
254	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
255	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	09/2018	574	54
256	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	09/2018	1046	60
257	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	07/2019	754	76
258	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2018	291.36	56
259	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	11/2018	530.07	27
260	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND	NHAI	08/2014	04/2018	12/2018	822.9	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	TWO-LANE PAVED SHOULDER FROM						
261	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	12/2018	972.5	17
262	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2018	671.3	70
263	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2018	374	67
264	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2018	485	64
265	JORBAT - BARAPANI	NHAI	01/2011	01/2014	11/2018	536	58
266	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	06/2019	575	71
267	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2018	511.54	61
268	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	12/2019	624	68
269	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	10/2018	486	101
270	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108	91
271	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	04/2019	641.17	33
272	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	11/2020	476.56	40
273	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
274	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	MORTH	02/2015	03/2015	06/2019	383.4	51
275	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	11/2018	255.75	14
276	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	PWD	01/2014	11/2017	10/2018	267.16	11
277	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
278	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	06/2019	1348.2	64
279	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2019	617	79
280	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	06/2019	1724.55	75
281	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	04/2019	1916.79	29
282	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.6	33
283	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	11/2018	1175	67

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
284	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2018	1250	60
285	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	12/2018	953.88	65
286	4-LANING OF SOLAPUR - MAHARASHTRA/KARNATKA SECTION	NHAI	06/2014	11/2016	03/2019	923.04	28
287	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2019	1655.01	31
288	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	10/2018	1673.7	84
289	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	04/2019	1388	8
290	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	12/2018	1871.34	11
291	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	09/2018	167.64	118
292	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	10/2018	200	114
293	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
294	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29
295	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
296	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	09/2019	2858	21
297	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343	29
298	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	06/2019	15525	49
299	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2018	1154.18	11
300	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2018	1034.01	14
301	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
302	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
303	MAHARASHTRA NODAL (LOT 1)	BSNL	08/2017	04/2018	10/2018	159.3	6
304	MAHARASHTRA CORE (LOT1)	BSNL	08/2017	04/2018	10/2018	167.68	6

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	10773	19
306	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
307	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
308	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
309	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2019	165.23	77
310	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	02/2019	270.83	51
311	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	09/2018	332.72	24
312	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
313	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2019	216.69	56
314	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15
315	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
316	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	12/2018	151.33	15
317	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
318	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSCL	02/2014	12/2016	12/2018	787.29	24
319	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	11/2018	388	18
320	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	01/2019	156.57	29
321	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2019	171.86	45
322	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	12/2018	884.3	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
323	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
324	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36
325	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
8	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
9	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
12	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
13	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1577.15	715.36
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
20	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
21	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9394.8	5475.21
23	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
25	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
26	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
27	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
28	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2534	754.71
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	534.02	236.69
32	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
33	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4401.9	2744.9
34	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
35	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
36	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
37	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
38	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09
40	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
41	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
42	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
43	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
44	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
45	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
46	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
47	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	2514.88	3190.27	675.39
48	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
50	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
51	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4105.3	1613.72
52	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
53	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	PGCIL	08/2008	02/2013	771	1624	853
54	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
55	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6652.57	1541.24
56	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9141.97	4387.55
57	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
58	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
59	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	297.32	614	316.68
60	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE
(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	920	764.45
62	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	ECR	03/1999	N.A.	1033.07	3020.94	1987.87
63	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	792.46	1320	527.54
64	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
65	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
66	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	261.7	388	126.3
67	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
68	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
69	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
70	HATHUA-BHATNI (N L) (NER)	NER	04/2005	12/2022	230.03	718.54	488.51
71	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
72	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	06/2018	218.19	413.56	195.37
73	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	2713.09	2288.49
74	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	732.81	1850	1117.19
75	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	749	271.12
76	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.77	1538.12
77	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	4600	2206.53
78	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
79	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	501.78	1960.06	1458.28
80	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
81	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
82	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
84	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
85	MM FROM PANSKURA-GHATAL NL	SER	04/2011	N.A.	276.69	426	149.31
86	MM FROM BURAMARA-CHAKULIA	SER	04/2008	N.A.	466.48	1000	533.52
87	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
88	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
89	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
90	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	2062.2	1091.86
91	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
92	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	1013.45	1428	414.55
93	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
94	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
95	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
96	KONDAPALLI-KOTHAGUDEM	SCR	04/2013	N.A.	616.08	723	106.92
97	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
98	PUNE-MIRAJ-LONDA (467 KM)	CR	02/2015	03/2024	3627.47	4817.69	1190.22
99	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
100	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
101	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
102	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	236.21	1395.63	1159.42
103	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	563.51	1813.59	1250.08
104	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2142.49	1226.51
105	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	23.56	1330.73	1307.17

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	318.5	852.8	534.3
107	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
108	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
109	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	246.07	398.93	152.86
110	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	551	237
111	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
112	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
113	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
114	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
115	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
116	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	369.83	178.11
117	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
118	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
119	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	283.55	451	167.45
120	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1733.2	838.2
121	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	726	504.58
122	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
123	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
124	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
125	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
126	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
127	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
128	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	785.87	237.87

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1474.47	1102.33
130	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
131	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
132	CHHAPRA-MUZAFFARPUR (NL)	ECOR	04/2006	N.A.	285.07	2614.36	2329.29
133	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.73	729.92	554.19
134	BIHTA-AURANGABAD (NL)	ECOR	04/2008	N.A.	326.2	2995.01	2668.81
135	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
136	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECOR	04/2008	N.A.	445.25	2860.55	2415.3
137	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	620.57	2626.98	2006.41
138	ARA-BHABHUA ROAD (NL)	SER	04/2008	N.A.	633.87	2396.88	1763.01
139	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
140	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	525.81	216.37
141	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
142	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
143	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
144	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	349	106.91
145	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR	NWR	04/2013	03/2020	420.18	865	444.82
146	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
147	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
148	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
149	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2878.97	796.22
150	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
151	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
153	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
154	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	871.56	627.78
155	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
156	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	333.76	1300	966.24
157	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	1142	3374	2232
158	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
159	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	5300	7986.04	2686.04
160	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
161	GHUTIASHARIF-CANNING (ER)	ER	04/2009	12/2011	193.08	683.88	490.8
162	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
163	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
164	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	495.74	734.01	238.27
165	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	845.58	220.58
166	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24.	SER	04/1998	03/2022	1027.4	2373	1345.6
167	GEVRA ROAD PENDRA ROAD	SECR	02/2014	03/2022	2288	4919	2631
168	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
169	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1279	407
170	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	556.54	1342.46	785.92
171	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	403	174
172	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	566.41	237.02
173	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	528.26	347.44
174	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	624.47	3550	2925.53

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
176	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
177	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
178	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
179	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
180	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	609.04	1807.88	1198.84
181	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
182	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING	SR	02/2003	03/2009	199.55	330.32	130.77
183	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1420.39	834.46
184	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
185	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1260.61	678.48
186	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	1514.45	1750	235.55
187	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
188	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
189	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
190	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.96	195.95
191	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1025	900.57
192	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1216	386.26
193	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTHA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1103.04	229.33
194	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
195	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
196	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
197	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	N.A.	458.25	815	356.75

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	MUNEERABAD-MAHABOONAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3501.83	1778.83
199	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
202	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	383.54	555	171.46
203	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
204	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
205	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	2783	1953.26
206	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	1389.62	2446.85	1057.23
207	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
208	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	631.78	1195	563.22
209	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	369.9	1581.53	1211.63
210	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
211	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
212	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
213	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	795.01	384.93
214	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
215	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
216	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	13809	9354.83
217	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
218	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	3040	1859.81
219	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	589.15	426.28
220	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
221	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1156.41	831.68
222	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
223	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	3230.02	5820	2589.98
224	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
225	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	1046.88	7000	5953.12
226	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	625	338
227	GUDUR-DURGARA JAPATNAM	SCR	04/2011	N.A.	283.54	761.37	477.83
228	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	2154.83	1231.6
229	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
230	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
231	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
232	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	278.66	1255.98	977.32
233	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	115.27	857.3	742.03
234	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.9	151.72
235	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	365.17	528.34	163.17
236	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	136.55	534.24	397.69
237	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	5554.24	2050.55
238	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	ER	04/2009	02/2012	259.51	673.85	414.34
239	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	1116	462.81
240	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
241	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
242	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	614.25	2532.49	1918.24
243	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	584.41	1005.23	420.82

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
244	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
245	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
246	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
247	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
248	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
249	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
250	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
251	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
252	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
253	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
254	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
255	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
256	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
257	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
258	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
259	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
260	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
261	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
262	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
263	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2018)

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
264	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
265	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
266	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
267	2 MTPA PELLETT PLANT AT NAGARNAR	NMDC	11/2015	06/2020	818	2907	2089

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
268	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
269	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
270	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
271	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
272	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
273	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
274	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
275	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(SEPTEMBER 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	03/2019	3492.00	6100.00	2608	102

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2018	309.46	553.53	244.07	92

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
7	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	5245.96	657.67	9
9	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	723.40	413.59	52
10	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70
13	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2019	861.79	1577.15	715.36	70

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(SEPTEMBER 2018)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
14	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	PGCIL	08/2008	02/2013	10/2018	771.00	1624.00	853	68
15	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	6652.57	1541.24	12
16	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9141.97	4387.55	12
17	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2018	1779.29	2534.00	754.71	121
18	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	10/2018	1272.80	1731.10	458.3	71
19	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353.00	7998.00	2645	60
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	602.44	165.76	24
21	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	4105.30	1613.72	102
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.90	6179.96	3683.06	111
23	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	10/2018	1940.13	2702.65	762.52	49
24	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657.00	4401.90	2744.9	63
25	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	639.46	151.97	54
26	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2018	297.33	534.02	236.69	52
27	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	738.48	260.79	99
28	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2019	4824.12	5071.94	247.82	76
29	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	1,1638.55	1,2865.92	1227.37	21
30	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,3762.80	2632.61	103
31	TRANSMISSION SYSTEM ASSOCIATED	PGCIL	02/2010	12/2012	11/2018	2144.00	2932.88	788.88	71

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	WITH PALLATANA GBPP and BPTS.								
32	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	1891.41	526.89	32
33	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	867.82	93
34	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	10/2018	4375.35	8150.00	3774.65	85
35	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	1,2532.44	1,3740.53	1208.09	10
36	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	1,4366.58	1,5164.05	797.47	20
37	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	09/2018	955.00	1364.00	409	33
38	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	1,2964.60	1,3731.26	766.66	28
39	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9394.80	5475.21	147
40	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	1,5095.67	6402.7	123
41	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	11/2018	2514.88	3190.27	675.39	35
42	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	1,1846.00	1,2739.82	893.82	24
43	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	545.3	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
44	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
45	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	1342.46	785.92	96
46	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
47	JARAPADA - BUDHAPANK WITH FLY	ECOR	04/2015	11/2018	03/2021	701.61	810.02	108.41	28

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	OVER AT TALCHER ROAD 3RD AND 4TH LINE								
48	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
49	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2019	1185.64	1844.47	658.83	15
50	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2018	133.41	385.00	251.59	117
51	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
52	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2018	261.70	388.00	126.3	154
53	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	4600.00	2206.53	81
54	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	749.00	271.12	96
55	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2019	732.81	1850.00	1117.19	132
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2022	4454.17	1,3809.00	9354.83	132
57	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
58	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2019	495.74	734.01	238.27	69
59	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
60	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2021	532.87	2145.00	1612.13	24
61	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2021	2326.52	3000.00	673.48	81
62	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
63	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2019	1142.00	3374.00	2232	60
64	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
65	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	03/2021	2500.00	2,7949.00	25449	220
66	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	1116.00	462.81	60
67	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2020	136.55	534.24	397.69	48
68	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
69	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	12/2019	3230.02	5820.00	2589.98	140
70	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
71	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1156.41	831.68	96
72	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	12/2020	1180.19	3040.00	1859.81	144
73	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	3791.66	868.53	147
74	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	1195.00	563.22	111
75	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	383.54	555.00	171.46	117
76	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
77	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
78	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	10/2018	164.36	1050.00	885.64	116
79	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	12/2023	1723.00	3501.83	1778.83	285
80	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2020	1111.99	1539.28	427.29	13
81	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2018	148.77	377.00	228.23	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
82	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2020	829.74	1216.00	386.26	60
83	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
84	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651.00	1009.00	358	108
85	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	12/2018	309.44	525.81	216.37	36
86	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314.00	551.00	237	12
87	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
88	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	939.00	414.57	36
89	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	3550.00	2925.53	61
90	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
91	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	12/2018	609.04	1807.88	1198.84	236
92	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
93	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.60	1544.00	277.4	33
94	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108.00	2288.00	1180	91

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
95	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(SEPTEMBER 2018)

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
96	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343.00	488.40	145.4	29

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
98	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	1,0773.00	1,2787.00	2014	19
99	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(September 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2018	.00	56
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2018	.00	67
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	10/2018	.00	101
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2018	.00	61
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	11/2018	.00	27
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	11/2018	.00	58
11	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2018	.00	62
12	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2018	.00	54
13	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	06/2019	.00	71
14	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
15	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	03/2019	.00	79
16	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	12/2019	.00	68
17	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(September
2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	-	.00	0
19	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	12/2018	.00	70
20	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	-	.00	0
21	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	07/2019	.00	76
22	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	06/2019	.00	0
23	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	12/2018	.00	8
24	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	03/2019	.00	28
25	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	12/2018	.00	65
26	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	12/2018	.00	17
27	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	-	.00	0
28	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	09/2018	.00	60
29	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
30	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	-	.00	0
31	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
32	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
33	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
34	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2018	.00	60
35	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	06/2019	.00	64
36	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	04/2019	.00	8
37	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	-	.00	0
38	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	10/2015	.00	13

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(September
2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
40	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	-	.00	0
41	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 (BOT) - [N24000233] - PPP	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
42	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	-	.00	0
43	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79 -	1,583.79	01/2019 -	01/2019	.00	0
44	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM (BOT) - [N24000145] - PPP	11/2010	1,585.00 -	1,585.00	05/2013 -	-	.00	0
45	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
46	4-LANING OF GOA/KARNATAKA BORDER- KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	03/2019	.00	31
47	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	01/2019 -	01/2019	.00	0
48	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	-	.00	0
49	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	10/2018	.00	84
50	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	-	.00	0
51	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	06/2019	.00	75
52	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	-	.00	0
53	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	12/2018	.00	11
54	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	04/2019	.00	29
55	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	03/2019	.00	44
56	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
57	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	04/2019	.00	0
58	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
59	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(September
2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	05/2019	.00	0
61	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
62	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	12/2019	.00	69
63	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
64	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56	71
	Total		76,530.12 -	81,310.94				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
65	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88	0
	<u>Mumbai Port Trust</u>							
66	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		610.89 -	945.44				
	Grand Total		77,141.01	82,256.38				

State-wise Ongoing Project Detail's

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.09.2018)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	0.00 (0.00) [0]
3	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	0.00 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [10/2018]	262.97 (-) [262.97]	0.00 (0.00) [0]
5	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [10/2018]	391.00 (-) [391.00]	0.00 (0.00) [0]
6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [10/2018]	234.27 (-) [234.27]	0.00 (0.00) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
7	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [0/0]	601.02 (-) [601.02]	36.93 (0.00) [0]
8	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2019]	272.19 (-) [272.19]	76.88 (0.00) [0]
	<u>Petroleum</u>				
9	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
10	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2021]	384.58 (-) [384.58]	25.21 (0.00) [0]
11	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (2/2019) [2/2019]	420.76 (207.80) [207.80]	13.39 (-212.96) [5]
12	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (8/2021) [8/2021]	34,012.00 (-) [34,012.00]	1,200.29 (0.00) [14]
13	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
14	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020	20,928.00	540.49

			(-) [7/2020]	(-) [20,928.00]	(0.00) [0]
15	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	199.63 (0.00) [0]
	<u>Railways</u>				
16	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
17	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.07 (0.00) [0]
18	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	283.54 (-) [761.37]	0.52 (477.83) [0]
19	GUNTUR-GUNTAKAL	4/2016	3/2022 (3/2023) [3/2022]	3,631.00 (-) [3,631.00]	99.11 (0.00) [0]
20	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (3/2023) [3/2023]	1,045.20 (-) [2,120.16]	280.17 (1,074.96) [168]
21	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (2,499.71) [2,499.71]	163.03 (0.00) [0]
22	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	2.98 (0.50) [21]
23	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
24	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (3/2022) [3/2022]	2,288.70 (-) [2,288.70]	362.69 (0.00) [12]
25	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [10/2018]	164.36 (164.36) [1,050.00]	999.64 (885.64) [116]
26	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	7/2006	3/2008 (6/2008) [3/2019]	732.81 (-) [1,850.00]	1,863.44 (1,117.19) [132]
27	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	92.48 (302.41) [0]
28	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	819.86 (0.00) [24]
	<u>Road Transport And Highways</u>				
29	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	0.00 (0.00) [0]
30	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
31	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	0.00 (0.00) [0]
32	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
33	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	5/2013 (-) [0/0]	1,585.00 (-) [1,585.00]	2,159.63 (0.00) [0]

34	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
35	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	0.00 (0.00) [0]
36	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
37	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [3/2021]	1,532.62 (-) [1,532.62]	0.00 (0.00) [0]
38	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [0/0]	648.33 (-) [648.33]	0.00 (0.00) [0]
39	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [11/2018]	1,134.97 (-) [1,134.97]	16.31 (0.00) [0]
40	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	/ (-) [0/0]	480.21 (-) [480.21]	0.00 (0.00) [0]
41	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHMAPATNAM TO CHANDR	7/2015	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
42	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUEDEM TO A	12/2014	2/2015 (-) [0/0]	201.12 (201.00) [201.12]	0.00 (0.00) [0]
43	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	1/2014	7/2014 (-) [0/0]	361.30 (-) [207.40]	44.08 (-153.90) [0]
44	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	5/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
45	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
46	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	11/2014 (-) [0/0]	170.21 (-) [170.21]	5.65 (0.00) [0]
47	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [0/0]	565.09 (-) [565.09]	0.00 (0.00) [0]
48	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	/ (-) [0/0]	175.03 (-) [175.00]	0.00 (-0.03) [0]
49	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	2/2015	2/2017 (-) [0/0]	241.61 (-) [241.61]	7.71 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	2/2015	4/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [0/0]	271.45 (-) [271.45]	0.00 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [503.10]	15.10 (-145.22) [0]
53	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	/ (-) [0/0]	266.00 (-) [266.00]	0.00 (0.00) [0]
54	REHABILITATION AND UPGRADATION OF NH-42 FROM	3/2015	9/2015	309.01	0.00

	KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU		(-) [0/0]	(-) [309.01]	(0.00) [0]
55	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	2/2014	7/2014 (-) [0/0]	258.99 (-) [258.99]	16.54 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION)	2/2014	6/2014 (-) [0/0]	417.61 (-) [417.61]	0.00 (0.00) [0]
57	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	11/2014	2/2017 (-) [0/0]	297.78 (330.00) [330.00]	0.00 (32.22) [0]
58	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
59	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [0/0]	1,959.00 (-) [1,959.00]	0.00 (0.00) [0]
60	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [0/0]	1,323.15 (-) [1,323.15]	0.00 (0.00) [0]
61	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [0/0]	1,550.98 (-) [1,550.98]	0.00 (0.00) [0]
62	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	2,993.77 (0.00) [0]
63	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	5.37 (145.48) [2]
64	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [12/2018]	571.00 (-) [571.00]	582.52 (0.00) [62]
65	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
66	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018 (-) [11/2018]	465.85 (-) [465.85]	211.25 (0.00) [4]
67	CENTRAL DISPATCH YARD	8/2015	8/2018 (-) [10/2018]	320.66 (-) [320.66]	89.83 (0.00) [2]
68	COKE OVEN BATTERY-5	12/2011	12/2017 (-) [9/2019]	2,858.00 (-) [2,500.00]	971.76 (-358.00) [21]
69	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016 (-) [3/2019]	343.00 (-) [488.40]	238.69 (145.40) [29]
	<u>Urban Development</u>				
70	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [3/2019]	206.58 (-) [206.58]	0.02 (0.00) [0]
71	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
72	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [157.84]	134.62 (0.00) [0]
73	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]

	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
74	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019 (-) [12/2018]	247.52 (-) [247.52]	131.32 (0.00) [-2]
	<u>Power</u>				
75	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (3/2019) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,788.96 (3,683.06) [111]
76	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,295.43 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
77	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
78	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
79	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
80	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
81	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
82	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
83	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
84	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
85	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	38.50 (0.00) [0]
86	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
87	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
88	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]
89	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
90	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
91	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
92	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]

93	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
94	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
95	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
96	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
97	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
98	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
99	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]
100	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
101	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
102	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
103	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
104	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
105	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
106	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
107	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (3/2019) [3/2019]	2,465.15 (-) [2,378.89]	2,105.18 (-86.26) [72]
108	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2022]	557.00 (-) [557.00]	64.70 (0.00) [24]
109	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	241.91 (0.00) [0]
110	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
111	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	40.04 (127.41) [70]
112	DEVELOPMENT OF FACILITIES AT MOINARBAND	6/2016	8/2019	423.00	190.66

	(SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT		(-) [8/2019]	(-) [423.00]	(0.00) [0]
113	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	1.65 (0.00) [0]
114	DIESEL HYDROTREATOR	7/2015	1/2018 (-) [0/0]	1,031.37 (-) [1,031.37]	305.91 (0.00) [0]
115	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,098.69 (0.00) [0]
116	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	98.07 (-5.15) [0]
117	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	961.00 (328.65) [0]
	<u>Power</u>				
118	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [10/2018]	4,375.35 (8,150.00) [8,150.00]	7,154.15 (3,774.65) [85]
	<u>Railways</u>				
119	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (-) [551.00]	595.01 (237.00) [12]
120	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [12/2022]	2,232.32 (-) [2,232.00]	193.12 (-0.32) [9]
121	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [12/2019]	3,230.02 (4,857.00) [5,820.00]	5,224.22 (2,589.98) [140]
122	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	163.08 (-49.96) [0]
123	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (-) [398.93]	264.69 (152.86) [0]
124	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	538.17 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
125	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
126	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
127	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]
128	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
129	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
130	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
131	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-)	289.99 (-)	0.00 (0.00)

			[12/2018]	[289.99]	[0]
132	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
133	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
134	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
135	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [0/0]	217.61 (-) [309.56]	389.08 (91.95) [0]
136	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [0/0]	160.00 (-) [160.00]	198.82 (0.00) [0]
137	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
138	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
139	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
140	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
141	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [361.00]	410.32 (81.00) [0]
142	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
143	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
144	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [385.13]	209.80 (185.32) [0]
145	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [118]
146	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	245.83 (0.00) [114]
147	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [0/0]	208.00 (-) [208.00]	297.81 (0.00) [0]
148	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [0/0]	225.00 (-) [225.00]	312.79 (0.00) [0]
149	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [11/2017]	245.00 (-) [245.00]	214.88 (0.00) [0]
150	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
151	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]

	<u>BIHAR</u>				
	<u>Petroleum</u>				
152	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	333.63 (0.00) [-10]
153	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	24.18 (0.00) [0]
154	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	0.00 (0.00) [0]
155	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [11/2018]	822.66 (-) [822.66]	712.49 (0.00) [0]
156	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	0.00 (0.00) [0]
157	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	0.00 (0.00) [0]
158	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [6/2020]	324.00 (-) [324.00]	78.63 (0.00) [0]
	<u>Power</u>				
159	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR- II TIPS	4/2016	6/2019 (-) [6/2019]	790.13 (-) [790.30]	502.54 (0.17) [0]
160	BARH STPP(3X660MW) NTPC	2/2005	1/2011 (4/2021) [4/2021]	8,692.97 (15,095.67) [15,095.67]	14,937.25 (6,402.70) [123]
161	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	5/2014 (1/2018) [5/2019]	5,353.00 (13,624.00) [7,998.00]	7,128.72 (2,645.00) [60]
162	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	1/2018 (-) [5/2020]	12,964.60 (-) [13,731.26]	12,079.00 (766.66) [28]
163	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	12/2016 (-) [12/2018]	436.68 (-) [602.44]	499.77 (165.76) [24]
	<u>Railways</u>				
164	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [2,396.88]	0.39 (1,763.01) [0]
165	ARARIA-SUPAUL (NL)	4/2008	/ (-) [3/2023]	1,605.17 (-) [1,605.17]	0.19 (0.00) [-]
166	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [0/0]	326.20 (-) [2,995.01]	1.68 (2,668.81) [0]
167	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	285.07 (-) [2,614.36]	111.71 (2,329.29) [-]
168	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
169	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
170	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN- BIHARSHARIF,	4/1991	/ (-) [12/2021]	329.39 (-) [566.41]	759.20 (237.02) [-]

171	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	0.00
			(-)	(-)	(2,415.30)
			[0/0]	[2,860.55]	[0]
172	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	13.00
			(-)	(-)	(154.16)
			[0/0]	[367.17]	[0]
173	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	330.82
			(-)	(-)	(1,538.12)
			[3/2023]	[2,066.77]	[-]
174	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	876.49
			(-)	(335.77)	(831.68)
			[3/2020]	[1,156.41]	[96]
175	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	40.00
			(-)	(-)	(237.87)
			[3/2020]	[785.87]	[0]
176	KATIHAR - JOGBANI (GC)(NEFR)	9/2001	12/2010	792.46	928.50
			(-)	(-)	(527.54)
			[0/0]	[1,320.00]	[0]
177	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	183.72
			(-)	(-)	(426.28)
			[3/2022]	[589.15]	[-]
178	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	4.11
			(-)	(-)	(966.24)
			[3/2020]	[1,300.00]	[-]
179	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	0.00
			(-)	(-)	(0.00)
			[10/2021]	[1,200.20]	[19]
180	KOSI BRIDGE (NL), ECR	4/2002	3/2012	499.41	640.78
			(-)	(-)	(16.61)
			[3/2020]	[516.02]	[96]
181	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.38
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
182	MAHARAJGANJ-MASRAKH (NL) - NER	4/2003	6/2018	218.19	361.13
			(-)	(-)	(195.37)
			[6/2018]	[413.56]	[0]
183	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	495.40
			(-)	(283.95)	(271.12)
			[3/2020]	[749.00]	[96]
184	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.41
			(-)	(-)	(715.09)
			[0/0]	[926.09]	[0]
185	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	0.00
			(-)	(-)	(454.09)
			[3/2022]	[1,185.73]	[12]
186	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.58
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
187	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.52
			(-)	(-)	(0.00)
			[0/0]	[228.05]	[0]
188	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	538.21
			(-)	(-)	(227.76)
			[0/0]	[559.91]	[0]
189	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.00
			(-)	(-)	(2,006.41)
			[0/0]	[2,626.98]	[0]
190	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	928.89
			(-)	(-)	(1,612.13)
			[3/2021]	[2,145.00]	[24]
191	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN	11/2001	2/2016	624.47	97.63

	PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM		(-) [3/2021]	(-) [3,550.00]	(2,925.53) [61]
192	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	462.75
			(-) [12/2018]	(-) [528.26]	(347.44) [-]
193	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	0.00
			(-) [10/2021]	(-) [1,491.47]	(0.00) [19]
194	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	1.81
			(-) [3/2022]	(-) [1,215.54]	(471.50) [12]
195	SAKRI-HASANPUR ROAD (NL)	4/1999	/	175.73	253.10
			(-) [3/2021]	(-) [729.92]	(554.19) [-]
196	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	338.44
			(-) [3/2021]	(-) [1,474.47]	(1,102.33) [-]
197	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	0.00
			(-) [0/0]	(-) [380.00]	(0.00) [0]
198	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.17
			(-) [0/0]	(-) [2,393.23]	(1,714.61) [0]
	<u>Road Transport And Highways</u>				
199	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013	351.54	351.23
			(-) [0/0]	(-) [351.54]	(0.00) [0]
200	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	563.48
			(-) [12/2018]	(-) [511.54]	(0.00) [61]
201	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-) [0/0]	(-) [375.09]	(0.00) [0]
202	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	823.46
			(-) [6/2019]	(-) [575.00]	(0.00) [71]
203	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	77.43
			(-) [6/2019]	(-) [581.84]	(0.00) [25]
204	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	0.00
			(-) [0/0]	(-) [288.24]	(0.00) [0]
205	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-) [0/0]	(-) [2,598.00]	(0.00) [0]
206	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020	235.48	0.00
			(-) [3/2020]	(-) [227.77]	(-7.71) [0]
207	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	0.00
			(-) [0/0]	(-) [496.20]	(0.00) [0]
208	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016	683.83	0.00
			(-) [0/0]	(-) [683.83]	(0.00) [0]
209	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	553.30	0.00
			(-) [0/0]	(-) [553.30]	(0.00) [0]
210	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	178.85	0.00
			(-) [0/0]	(-) [178.85]	(0.00) [0]
211	ENGINEERING, PROCUREMENT, AND CONSTRUCTION	2/2016	6/2016	369.77	0.00

	OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P		(-) [0/0]	(-) [369.77]	(0.00) [0]
212	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	27.94 (0.00) [-]
213	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	0.00 (0.00) [-]
214	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	56.79 (0.00) [24]
215	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	0.00 (0.00) [0]
216	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	157.20 (0.00) [-]
217	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
218	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [4/2019]	1,041.10 (-) [1,041.10]	138.78 (0.00) [0]
219	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [9/2018]	574.00 (-) [574.00]	898.99 (0.00) [54]
220	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [12/2018]	671.30 (-) [671.30]	883.96 (0.00) [70]
221	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	0.00 (0.00) [0]
222	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
223	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	3/2014 (-) [0/0]	377.64 (-) [377.64]	0.00 (0.00) [0]
224	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
225	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [319.68]	0.00 (0.00) [0]
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [282.41]	67.52 (0.00) [0]
229	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/2013	8/2014 (-) [0/0]	322.01 (-) [322.01]	0.00 (0.00) [0]
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [358.22]	188.71 (0.00) [0]
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR -	1/1991	/ (-)	675.00 (-)	0.00 (0.00)

	BIHPUR		[0/0]	[675.00]	[0]
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/	154.62	0.00
			(-)	(-)	(0.00)
			[0/0]	[154.62]	[0]
233	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/	895.39	0.00
			(-)	(-)	(0.00)
			[0/0]	[895.39]	[0]
234	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017	950.64	0.00
			(-)	(-)	(0.00)
			[0/0]	[950.64]	[0]
235	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV	3/2015	7/2016	206.80	0.00
			(-)	(-)	(0.00)
			[0/0]	[206.80]	[0]
236	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019	399.54	133.02
			(-)	(-)	(0.00)
			[10/2019]	[399.54]	[6]
237	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/	854.80	510.69
			(-)	(-)	(0.00)
			[0/0]	[854.80]	[0]
238	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018	516.13	400.35
			(-)	(-)	(0.00)
			[12/2018]	[516.13]	[8]
239	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020	672.89	0.00
			(-)	(-)	(63.12)
			[3/2020]	[736.01]	[0]
	<u>Urban Development</u>				
240	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017	496.18	17.72
			(7/2017)	(496.00)	(2.81)
			[6/2020]	[498.99]	[36]
241	IRRIGATION WORK OF BAGMATI	10/2005	3/2015	956.00	651.21
			(-)	(-)	(0.00)
			[3/2021]	[956.00]	[72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
242	AMERA OC RCE	2/2015	3/2018	335.97	51.29
			(-)	(-)	(0.00)
			[3/2018]	[335.97]	[0]
243	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020	316.10	56.54
			(-)	(-)	(0.00)
			[3/2020]	[316.10]	[0]
244	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016	198.59	169.49
			(-)	(-)	(0.00)
			[3/2019]	[198.59]	[36]
245	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016	258.56	163.85
			(-)	(-)	(0.00)
			[3/2019]	[258.56]	[36]
246	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020	164.49	54.71
			(-)	(-)	(0.00)
			[3/2020]	[164.49]	[0]
247	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022	610.63	68.52
			(-)	(-)	(0.00)
			[3/2022]	[610.63]	[0]
248	DURGAPUR OPENCAST PROJECT	2/2015	3/2023	916.24	3.74
			(-)	(-)	(0.00)
			[3/2023]	[916.24]	[0]
249	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023	11,816.40	2,834.56
			(-)	(-)	(0.00)
			[3/2023]	[11,816.40]	[0]
250	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015	152.43	165.78
			(3/2020)	(459.49)	(307.06)
			[3/2020]	[459.49]	[60]

251	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	5.16 (0.00) [72]
252	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	1,881.64 (0.00) [0]
253	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
254	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	0.00 (0.00) [0]
255	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2020]	321.50 (-) [321.50]	202.31 (0.00) [72]
256	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.06 (0.00) [0]
257	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
258	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (4/2021) [4/2021]	300.00 (300.00) [300.00]	0.00 (0.00) [0]
	<u>Power</u>				
259	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	6/2017 (6/2019) [6/2019]	11,846.00 (-) [12,739.82]	10,383.95 (893.82) [24]
260	TALAIPELLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,218.88 (0.00) [0]
	<u>Railways</u>				
261	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (-) [12/2019]	872.00 (-) [1,279.00]	0.00 (407.00) [0]
262	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	4/1995	12/2012 (-) [3/2022]	631.78 (632.00) [1,195.00]	626.99 (563.22) [111]
263	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [3/2022]	2,288.00 (-) [4,919.00]	67.00 (2,631.00) [0]
264	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [3/2021]	1,973.00 (-) [1,973.00]	78.00 (0.00) [0]
265	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM	4/2011	3/2022 (-) [3/2022]	543.00 (-) [543.00]	0.00 (0.00) [0]
266	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [9/2018]	3,055.00 (-) [3,055.00]	600.00 (0.00) [0]
267	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2020]	1,143.60 (1,160.83) [1,160.83]	566.17 (17.23) [0]
268	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [3/2018]	207.00 (-) [207.00]	153.83 (0.00) [0]
269	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [3/2020]	758.09 (-) [758.09]	814.23 (0.00) [0]
270	SALKA ROAD -ANUPNAGAR LINE DOUBLING	9/2006	3/2010	383.54	564.30

			(-) [12/2019]	(-) [555.00]	(171.46) [117]
	<u>Road Transport And Highways</u>				
271	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/	1,029.96	0.00
			(-) [0/0]	(-) [1,029.96]	(0.00) [0]
272	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	12/2010	12/2012	169.26	0.00
			(-) [0/0]	(-) [169.26]	(0.00) [0]
273	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018	726.67	5.65
			(-) [6/2019]	(-) [726.67]	(0.00) [14]
274	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018	509.13	7.21
			(-) [0/0]	(-) [509.13]	(0.00) [0]
275	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018	596.67	0.00
			(-) [0/0]	(-) [596.67]	(0.00) [0]
276	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.	10/2014	3/2015	213.47	0.00
			(-) [0/0]	(-) [213.47]	(0.00) [0]
277	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/	291.05	0.00
			(-) [0/0]	(-) [291.05]	(0.00) [0]
278	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.	12/2014	/	394.20	0.00
			(-) [0/0]	(-) [394.20]	(0.00) [0]
279	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015	485.44	0.00
			(-) [0/0]	(-) [485.44]	(0.00) [0]
280	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV	10/2014	3/2015	298.34	0.00
			(-) [0/0]	(-) [298.34]	(0.00) [0]
281	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	3/2015	262.54	0.00
			(-) [0/0]	(-) [262.54]	(0.00) [0]
282	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	/	422.34	22.25
			(-) [0/0]	(-) [422.34]	(0.00) [0]
	<u>Steel</u>				
283	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020	818.00	29.51
			(-) [6/2020]	(-) [2,907.00]	(2,089.00) [0]
284	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015	188.93	120.15
			(-) [0/0]	(-) [188.93]	(0.00) [0]
285	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015	15,525.00	14,283.70
			(6/2019) [6/2019]	(-) [15,525.00]	(0.00) [49]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
286	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019	6,086.08	4,231.37
			(10/2019) [10/2019]	(5,842.31) [5,842.31]	(-243.77) [5]
	<u>DELHI</u>				
	<u>Health And Family Welfare</u>				
287	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017	204.44	237.80
			(-) [0/0]	(-) [204.44]	(0.00) [0]
288	AIIMS - OPD(NEW)	8/2014	5/2017	293.65	237.86
			(-)	(-)	(0.00)

			[9/2018]	[293.65]	[16]
289	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [0/0]	156.56 (-) [156.56]	22.59 (0.00) [0]
290	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [0/0]	414.11 (-) [414.11]	141.00 (0.00) [0]
	<u>Heavy Industry</u>				
291	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	8/2016 (-) [9/2019]	1,554.00 (-) [1,554.00]	161.86 (0.00) [37]
	<u>Power</u>				
292	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [6/2019]	1,394.52 (-) [1,394.52]	191.64 (0.00) [25]
293	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)	5/2015	10/2018 (-) [10/2018]	780.33 (-) [780.33]	516.25 (0.00) [0]
	<u>Railways</u>				
294	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [0/0]	295.68 (-) [295.68]	1.20 (0.00) [0]
295	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [0/0]	156.65 (-) [197.17]	56.10 (40.52) [0]
	<u>Road Transport And Highways</u>				
296	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [7/2018]	771.18 (-) [7,558.00]	261.77 (6,786.82) [0]
	<u>Telecommunications</u>				
297	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	172.30 (0.00) [0]
	<u>Urban Development</u>				
298	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2020) [6/2020]	197.33 (-) [197.33]	5.08 (0.00) [14]
299	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [12/2018]	884.30 (-) [884.30]	626.67 (0.00) [36]
300	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [11/2019]	271.90 (-) [271.90]	1.84 (0.00) [0]
301	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [6/2019]	188.00 (-) [188.00]	55.43 (0.00) [0]
302	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,270.32 (0.00) [0]
303	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2020]	1,219.21 (-) [1,592.00]	282.67 (372.79) [5]
304	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	0.36 (0.00) [0]
305	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,439.23]	3,376.53 (175.23) [0]
306	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/ (-) [0/0]	392.00 (-) [392.00]	0.00 (0.00) [0]

307	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (-) [0/0]	422.00 (-) [422.00]	0.00 (0.00) [0]
308	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]
309	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (-) [0/0]	248.20 (-) [248.20]	1.21 (0.00) [0]
	<u>GOA</u>				
	<u>Defence Production</u>				
310	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020 (-) [8/2020]	285.95 (286.00) [291.29]	49.95 (5.34) [0]
311	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018 (8/2018) [8/2018]	167.69 (168.00) [170.37]	74.12 (2.68) [0]
	<u>Health And Family Welfare</u>				
312	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [0/0]	249.01 (-) [249.01]	17.00 (0.00) [0]
	<u>Road Transport And Highways</u>				
313	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [280.16]	16.06 (0.00) [0]
314	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	10.72 (0.00) [0]
315	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	0.00 (0.00) [0]
316	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	16.10 (0.00) [0]
317	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	38.33 (0.00) [0]
318	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	0.00 (0.00) [0]
319	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	0.00 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
320	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (11/2016) [6/2020]	11,459.00 (16,580.00) [16,580.00]	12,463.00 (5,121.00) [54]
	<u>Petroleum</u>				
321	ANKLESHWAR BARODA PIPELINE PROJECT	7/2014	3/2018 (-) [3/2018]	199.95 (-) [199.95]	156.83 (0.00) [0]
322	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [0/0]	588.20 (-) [588.20]	0.00 (0.00) [0]
323	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [9/2019]	3,380.00 (-) [3,380.00]	1,018.23 (0.00) [0]
324	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [12/2018]	327.78 (-) [200.00]	100.65 (-127.78) [8]

325	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	3.09 (0.00) [0]
326	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [2/2020]	906.00 (-) [906.00]	12.74 (0.00) [0]
327	GAMJI REDEVELOPMENT PROJECT	5/2015	11/2019 (12/2018) [12/2018]	1,671.22 (567.22) [567.22]	449.65 (-1,104.00) [-11]
328	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	59.66 (0.00) [0]
329	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (3/2026) [3/2026]	1,162.56 (1,162.56) [1,162.56]	269.97 (0.00) [0]
330	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [0/0]	279.00 (-) [279.00]	200.05 (0.00) [0]
	<u>Power</u>				
331	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [6/2019]	193.14 (-) [193.14]	2.50 (0.00) [0]
332	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (-) [6/2019]	175.64 (-) [175.64]	52.14 (0.00) [9]
333	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)	7/2016	12/2018 (-) [12/2018]	300.94 (-) [300.94]	194.26 (0.00) [0]
334	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [12/2018]	330.00 (-) [330.00]	309.48 (0.00) [13]
	<u>Railways</u>				
335	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [975.62]	573.13 (0.00) [0]
336	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2020) [3/2020]	829.74 (416.86) [2,783.00]	444.72 (1,953.26) [0]
337	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [203.00]	202.29 (85.64) [0]
338	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (-) [3/2019]	551.51 (-) [551.51]	257.05 (0.00) [0]
339	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [3/2019]	318.24 (-) [321.62]	83.10 (3.38) [84]
340	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	81.99 (0.00) [0]
341	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
342	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2022) [3/2022]	844.10 (-) [844.10]	58.31 (0.00) [-]
343	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	285.62 (0.00) [9]
344	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-)	153.83 (-)	0.00 (0.00)

			[0/0]	[153.83]	[0]
345	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,548.66 (-) [1,548.66]	704.64 (0.00) [0]
346	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2019) [3/2022]	320.66 (1,378.12) [858.96]	549.56 (538.30) [36]
347	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2019) [3/2021]	1,002.39 (-) [1,002.39]	202.09 (0.00) [0]
348	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	4/2008	3/2014 (3/2018) [5/2018]	1,389.62 (2,446.85) [2,446.85]	2,127.13 (1,057.23) [0]
349	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (3/2020) [3/2021]	1,037.15 (1,037.15) [1,037.15]	882.80 (0.00) [0]
350	VIRAMGAM-SURENDRANAGAR (DL)	4/2010	/ (-) [0/0]	279.40 (384.32) [355.00]	334.93 (75.60) [0]
351	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	<u>Road Transport And Highways</u>				
352	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	30.19 (0.00) [-]
353	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	0.00 (0.00) [-]
354	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [6/2020]	1,958.88 (-) [1,958.88]	0.00 (0.00) [0]
355	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,659.71 (0.00) [0]
356	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2019]	364.56 (-) [364.56]	72.51 (0.00) [-]
357	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [0/0]	2,702.05 (-) [2,702.05]	0.00 (0.00) [0]
358	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [8/2019]	998.18 (-) [998.18]	59.12 (0.00) [-]
359	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [9/2019]	723.64 (-) [723.64]	9.60 (0.00) [-]
360	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [10/2019]	834.64 (-) [834.64]	22.03 (0.00) [-]
361	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [8/2019]	763.08 (-) [763.08]	5.64 (0.00) [-]
362	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [8/2018]	1,509.10 (-) [3,237.87]	3,176.22 (1,728.77) [0]
363	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
364	KANDLA - MUNDRA PORT	1/2011	7/2013 (-)	953.88 (-)	974.83 (0.00)

			[12/2018]	[953.88]	[65]
365	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/	1,052.21	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,052.21]	[0]
366	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/	1,251.11	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,251.11]	[0]
367	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/	425.60	0.00
			(-)	(-)	(0.00)
			[3/2019]	[425.60]	[-]
368	VADODARA-SURAT SECTION	3/2014	8/2016	503.16	346.60
			(-)	(-)	(0.00)
			[0/0]	[503.16]	[0]
	<u>Telecommunications</u>				
369	GUJARAT ACCESS (LOT 1)	9/2017	5/2018	171.54	72.46
			(10/2018)	(-)	(0.00)
			[10/2018]	[171.54]	[5]
	<u>Urban Development</u>				
370	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	10,773.00	2,078.80
			(-)	(-)	(2,014.00)
			[7/2020]	[12,787.00]	[19]
371	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/	175.00	1.83
			(-)	(-)	(0.00)
			[0/0]	[175.00]	[0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
372	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019	215.92	24.50
			(-)	(-)	(0.00)
			[11/2019]	[215.92]	[0]
	<u>Health And Family Welfare</u>				
373	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018	505.58	355.00
			(-)	(-)	(17.42)
			[9/2018]	[523.00]	[6]
374	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	7/2016	8/2018	312.99	469.00
			(-)	(-)	(9.01)
			[0/0]	[322.00]	[0]
	<u>Petroleum</u>				
375	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019	3,529.00	793.22
			(-)	(-)	(0.00)
			[9/2019]	[3,529.00]	[2]
376	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020	206.63	0.12
			(-)	(-)	(0.00)
			[2/2020]	[206.63]	[0]
377	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020	255.00	3.60
			(11/2020)	(255.00)	(0.00)
			[11/2020]	[255.00]	[0]
378	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020	1,636.00	122.32
			(-)	(-)	(0.00)
			[8/2020]	[1,636.00]	[0]
	<u>Railways</u>				
379	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/	400.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[400.00]	[0]
380	JIND-SONEPAT (NL),NR	1/2004	3/2012	238.56	722.65
			(-)	(-)	(501.44)
			[0/0]	[740.00]	[0]
381	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019	346.32	243.30
			(-)	(-)	(-46.32)
			[3/2019]	[300.00]	[0]
382	ROHTAK-MEHAM HANSI	4/2012	12/2011	287.00	4.38
			(-)	(-)	(338.00)

			[0/0]	[625.00]	[0]
	<u>Road Transport And Highways</u>				
383	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [12/2018]	602.95 (-) [602.95]	54.89 (0.00) [30]
384	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [3/2019]	574.28 (-) [574.28]	51.47 (0.00) [8]
385	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [3/2020]	639.79 (-) [552.90]	0.00 (-86.89) [0]
386	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [4/2019]	2,128.72 (-) [2,128.72]	162.60 (0.00) [0]
387	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [5/2019]	248.97 (-) [248.97]	0.00 (0.00) [0]
388	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [5/2019]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
389	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [10/2018]	486.00 (-) [486.00]	475.57 (0.00) [101]
390	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
391	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
392	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [6/2019]	1,108.00 (-) [2,288.00]	3,869.30 (1,180.00) [91]
393	ROHTAK-BAWAL	5/2011	11/2013 (-) [0/0]	650.00 (-) [650.00]	832.39 (0.00) [0]
	<u>HIMACHAL PRADESH</u>				
	<u>Petroleum</u>				
394	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [9/2019]	151.00 (-) [151.00]	74.43 (0.00) [0]
395	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP	2/2016	5/2019 (-) [12/2018]	356.00 (-) [356.00]	169.04 (0.00) [-5]
	<u>Power</u>				
396	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,394.80]	7,058.21 (5,475.21) [147]
	<u>Railways</u>				
397	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2026]	1,046.88 (-) [7,000.00]	212.83 (5,953.12) [0]
	<u>Road Transport And Highways</u>				
398	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [2/2019]	273.20 (-) [273.20]	18.36 (0.00) [0]
399	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [6/2020]	2,485.93 (-) [2,485.93]	0.00 (0.00) [0]
400	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [4/2019]	1,916.79 (-) [1,916.79]	1,737.91 (0.00) [29]

401	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2019]	934.46 (-) [934.46]	104.98 (0.00) [12]
402	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	0.00 (0.00) [0]
403	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [0/0]	447.75 (-) [447.75]	0.00 (0.00) [0]
404	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (-) [1,583.18]	0.00 (0.00) [-]
	<u>Urban Development</u>				
405	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [2/2019]	270.83 (210.00) [270.83]	163.97 (0.00) [51]
	<u>JAMMU AND KASHMIR</u>				
	<u>Power</u>				
406	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [10/2023]	8,112.12 (-) [8,112.12]	980.00 (0.00) [42]
407	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT	1/2014	9/2017 (-) [9/2018]	1,788.41 (-) [2,333.71]	1,528.12 (545.30) [12]
	<u>Railways</u>				
408	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (3/2021) [3/2021]	2,500.00 (27,949.00) [27,949.00]	16,500.26 (25,449.00) [220]
	<u>Road Transport And Highways</u>				
409	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [0/0]	1,471.75 (-) [1,471.75]	0.00 (0.00) [0]
410	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH- 1A	12/2015	6/2019 (-) [6/2019]	2,168.66 (-) [2,168.66]	0.00 (0.00) [0]
411	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [12/2018]	2,136.97 (-) [2,136.97]	0.00 (0.00) [0]
412	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
413	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
414	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [3/2019]	1,987.00 (-) [1,987.00]	1,584.87 (0.00) [44]
415	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [0/0]	1,100.70 (-) [1,100.70]	1,216.15 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
416	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	196.02 (0.00) [0]
417	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2020]	163.51 (-) [163.51]	93.93 (0.00) [108]
418	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	42.27 (0.00) [0]

419	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
420	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2019]	162.46 (-) [162.46]	82.97 (0.00) [60]
421	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	189.33 (0.00) [0]
422	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2021]	706.40 (-) [706.40]	125.15 (0.00) [104]
423	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	295.38 (0.00) [48]
424	MURAIIDH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [54]
425	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	4.57 (0.00) [0]
426	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [3/2019]	179.87 (-) [179.87]	139.30 (0.00) [84]
427	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2018]	269.82 (-) [269.82]	178.46 (0.00) [0]
428	RAJMAHAL OC EXP.	9/2009	3/2014 (-) [0/0]	153.82 (-) [153.82]	131.07 (0.00) [0]
429	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2019]	510.85 (-) [510.85]	352.34 (0.00) [36]
430	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2019]	264.68 (-) [264.68]	155.09 (0.00) [84]
	<u>Petroleum</u>				
431	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]
432	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	18.64 (0.00) [0]
433	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	19.08 (0.00) [0]
434	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	658.62 (910.23) [910.23]	70.98 (251.61) [-12]
435	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	176.28 (0.00) [0]
	<u>Power</u>				
436	NORTH KARANPURA STPP (3X660 MW)	2/2014	2/2019 (10/2020) [10/2020]	14,366.58 (-) [15,164.05]	7,574.04 (797.47) [20]
437	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [12/2016]	4,237.96 (4,552.00) [4,552.00]	2,844.03 (314.04) [0]
	<u>Railways</u>				
438	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021	1,724.20	140.51

			(3/2021) [3/2021]	(1,724.20) [1,724.20]	(0.00) [0]
439	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	4/2010	12/2015 (12/2018) [12/2018]	309.44 (-) [525.81]	485.03 (216.37) [36]
440	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	88.01 (0.00) [-3]
441	GOELKERA-MANOHARPUR,(LD)(SER)	3/1997	2/2006 (-) [12/2018]	261.70 (-) [388.00]	388.06 (126.30) [154]
442	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (-) [3,020.94]	0.00 (1,987.87) [-]
443	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [0/0]	459.91 (-) [459.91]	221.54 (0.00) [0]
444	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	4/1995	3/2016 (12/2010) [3/2020]	1,125.89 (-) [1,125.89]	899.49 (0.00) [48]
445	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (12/2018) [12/2018]	258.20 (-) [365.00]	175.61 (106.80) [-]
446	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [12/2018]	148.77 (-) [377.00]	147.34 (228.23) [24]
447	TINPAHAR - SAHIBGANJ (ER)	4/2008	3/2012 (-) [0/0]	167.73 (-) [167.73]	264.57 (0.00) [0]
	Road Transport And Highways				
448	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [3/2020]	239.68 (-) [235.90]	21.98 (-3.78) [0]
449	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [6/2019]	165.50 (-) [172.16]	10.57 (6.66) [-9]
450	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [3/2019]	997.15 (-) [997.15]	328.14 (0.00) [0]
451	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
452	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [8/2018]	323.72 (-) [323.72]	37.20 (0.00) [0]
453	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
454	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
455	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [458.03]	0.00 (0.00) [0]
	Steel				
456	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	9/2017 (-) [0/0]	4,749.00 (-) [4,749.00]	105.87 (0.00) [0]
457	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (-) [11/2018]	1,154.18 (-) [1,154.18]	842.32 (0.00) [11]

458	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (-) [12/2018]	1,034.01 (-) [1,034.01]	343.36 (0.00) [14]
459	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (-) [6/2019]	262.87 (-) [262.87]	63.54 (0.00) [0]
	<u>Urban Development</u>				
460	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [12/2019]	171.86 (-) [171.86]	41.24 (0.00) [45]
461	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
462	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
463	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [12/2018]	787.29 (-) [787.29]	285.30 (0.00) [24]
464	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
465	BSVI UPGRADATION	9/2016	12/2019 (-) [12/2019]	1,810.00 (1,810.00) [1,810.00]	130.79 (0.00) [0]
466	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [4/2019]	224.00 (207.00) [207.25]	99.99 (-16.75) [0]
467	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [749.00]	682.57 (0.00) [0]
468	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (-) [3/2019]	135.00 (171.00) [170.70]	111.05 (35.70) [0]
469	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [3/2020]	581.00 (-) [581.00]	0.00 (0.00) [0]
470	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
471	KUDGI STPP STAGE 1	1/2012	1/2017 (-) [0/0]	15,166.19 (-) [16,934.65]	15,364.00 (1,768.46) [0]
472	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [2/2019]	445.89 (-) [445.89]	197.76 (0.00) [0]
	<u>Railways</u>				
473	ARSIKERE-TUMKUR	3/2015	3/2020 (11/2015) [3/2020]	578.00 (578.00) [578.00]	439.87 (0.00) [0]
474	BAGALKOT-KUDACHI NL	4/2010	3/2016 (12/2023) [12/2023]	986.30 (986.30) [986.30]	283.34 (0.00) [93]
475	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (3/2024) [3/2024]	1,382.78 (1,382.78) [1,382.78]	7.35 (0.00) [264]
476	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (12/2023)	327.25 (367.77)	0.31 (40.52)

			[12/2023]	[367.77]	[-]
477	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (12/2023) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
478	GADAG-WADI NL	4/2013	12/2018 (12/2024) [12/2024]	2,841.84 (2,841.84) [2,841.84]	22.72 (0.00) [72]
479	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,127.00]	1,059.52 (0.00) [0]
480	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2020) [3/2022]	1,156.94 (1,141.00) [1,156.94]	646.90 (0.00) [24]
481	HUBLI-ANKOLA(NL),SWR	4/1997	3/2001 (12/2024) [12/2024]	2,315.00 (-) [2,135.00]	134.79 (-180.00) [285]
482	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (-) [889.52]	10.91 (244.74) [36]
483	MARIKUPPAM - KUPPAM	4/2012	3/2016 (12/2023) [12/2023]	279.54 (279.54) [279.54]	7.48 (0.00) [93]
484	MUNIRABAD (GINGERA) -RAICHUR NL	4/2007	/ (-) [12/2023]	179.65 (1,350.91) [1,350.91]	889.05 (1,171.26) [-]
485	SHIMOGA-HARIHAR NL	4/2011	3/2016 (3/2024) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
486	TORANAGALLU-RANJITPURA DL	4/2011	/ (12/2023) [12/2023]	146.75 (167.50) [167.50]	0.34 (20.75) [-]
487	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	3/2016 (12/2023) [12/2023]	1,801.01 (-) [1,801.01]	11.56 (0.00) [93]
488	WHITE FIELD-KOLAR NL	4/2011	/ (12/2023) [12/2023]	341.05 (-) [348.85]	0.36 (7.80) [-]
	Road Transport And Highways				
489	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [3/2019]	1,167.42 (-) [1,167.42]	191.05 (0.00) [0]
490	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	0.00 (0.00) [0]
491	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [3/2019]	1,655.01 (-) [1,655.01]	1,515.16 (0.00) [31]
492	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/ (-) [0/0]	720.69 (-) [720.69]	99.03 (0.00) [0]
493	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [7/2019]	701.40 (-) [701.40]	22.02 (0.00) [4]
494	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	9.12 (0.00) [20]
495	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [4/2019]	1,388.00 (-) [1,388.00]	791.18 (0.00) [8]
496	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-)	1,664.20 (-)	234.18 (0.00)

			[4/2020]	[1,664.20]	[0]
497	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [3/2019]	946.00 (-) [946.00]	818.53 (0.00) [9]
498	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
499	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	279.54 (440.84) [3]
500	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [6/2020]	831.58 (-) [1,177.00]	48.27 (345.42) [3]
501	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,177.80]	0.00 (0.00) [0]
502	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [0/0]	1,995.34 (-) [1,995.34]	0.00 (0.00) [0]
503	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
504	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
505	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [12/2018]	709.00 (-) [709.00]	351.24 (0.00) [15]
506	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [8/2019]	950.69 (-) [950.69]	277.34 (0.00) [0]
	<u>Urban Development</u>				
507	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	2,391.46 (0.00) [13]
508	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
509	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
510	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (9/2020) [9/2020]	246.31 (-) [246.31]	21.94 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
511	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [6/2019]	1,112.00 (-) [1,112.00]	108.79 (0.00) [0]
512	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [3/2019]	607.06 (-) [714.25]	341.41 (107.19) [17]
513	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	215.97 (-24.04) [8]
514	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (5/2019) [5/2019]	4,588.29 (5,245.96) [5,245.96]	2,150.27 (657.67) [9]
	<u>Railways</u>				
515	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-)	1,566.00 (1,566.00)	255.37 (1,249.62)

			[0/0]	[2,815.62]	[0]
516	CHENGANNUR-CHINGAVANAM	4/2006	/ (-) [0/0]	191.72 (342.85) [369.83]	427.92 (178.11) [0]
517	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (-) [189.24]	6.70 (0.00) [0]
518	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (-) [252.96]	8.50 (0.00) [0]
519	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	2/2005	3/2014 (-) [0/0]	241.00 (-) [241.00]	295.12 (0.00) [0]
520	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
521	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [0/0]	1,431.90 (-) [1,431.90]	18.16 (0.00) [0]
522	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (-) [828.50]	0.08 (-171.50) [0]
	<u>Road Transport And Highways</u>				
523	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [4/2019]	845.24 (-) [845.24]	56.32 (0.00) [-]
524	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [4/2019]	804.97 (-) [804.97]	14.94 (0.00) [10]
525	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,124.11]	0.00 (0.00) [33]
526	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,424.77]	0.00 (0.00) [0]
527	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	11/2017 (-) [10/2018]	267.16 (352.00) [352.05]	201.35 (84.89) [11]
528	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [11/2018]	255.75 (348.00) [348.43]	231.56 (92.68) [14]
529	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [3/2019]	617.00 (-) [617.00]	245.89 (0.00) [79]
	<u>Urban Development</u>				
530	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (6/2020) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
531	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2019]	165.23 (-) [165.23]	58.85 (0.00) [77]
532	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,181.79]	0.00 (0.00) [29]
	<u>MADHYA PRADESH</u>				
	<u>Coal</u>				
533	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	111.27 (0.00) [0]
534	AMRITDHARA OC PROJECT	2/2015	3/2023 (-)	481.60 (-)	0.00 (0.00)

			[3/2023]	[481.60]	[0]
535	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
536	BATURA OCP (2.0 MTY)	8/2015	3/2023 (3/2021) [3/2021]	1,186.64 (203.82) [203.82]	102.09 (-982.82) [-24]
537	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	16.21 (0.00) [0]
538	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	94.68 (0.00) [0]
539	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	196.70 (0.00) [0]
540	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	41.27 (0.00) [0]
541	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	1.90 (0.00) [0]
542	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	3/2012 (-) [0/0]	259.40 (-) [486.57]	266.38 (227.17) [0]
543	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	113.06 (0.00) [0]
	<u>Petroleum</u>				
544	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [6/2020]	236.00 (-) [236.00]	0.00 (0.00) [0]
	<u>Power</u>				
545	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [2,104.21]	62.71 (0.00) [0]
546	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	9/2017 (6/2019) [6/2019]	11,638.55 (-) [12,865.92]	9,767.60 (1,227.37) [21]
547	KHARGONE STPP STAGE I (1320 MW)	3/2015	9/2019 (-) [9/2019]	9,870.51 (-) [11,148.86]	5,809.85 (1,278.35) [0]
548	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	4/2016	6/2018 (-) [12/2018]	287.99 (-) [287.99]	161.82 (0.00) [6]
549	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	1/2016	3/2017 (9/2018) [11/2018]	305.04 (-) [305.04]	215.81 (0.00) [20]
550	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V	2/2015	6/2018 (-) [11/2018]	1,750.00 (-) [1,750.00]	1,276.62 (0.00) [5]
	<u>Railways</u>				
551	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2021]	1,370.00 (-) [1,370.00]	101.00 (0.00) [0]
552	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	812.47 (0.00) [0]
553	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,101.16]	194.91 (717.37) [0]

554	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [2/2019]	585.93 (-) [1,420.39]	104.10 (834.46) [0]
555	CHHINDWARA-MANDLA FORT GC	3/2011	3/2012 (-) [3/2020]	556.54 (-) [1,342.46]	396.00 (785.92) [96]
556	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,763.93 (-) [1,763.93]	0.00 (0.00) [19]
557	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2022]	582.13 (-) [1,260.61]	0.00 (678.48) [0]
558	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2022]	2,478.23 (-) [2,478.23]	112.07 (0.00) [0]
559	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [8/2019]	174.00 (-) [174.00]	137.61 (0.00) [5]
560	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2021]	424.60 (727.13) [2,713.09]	898.83 (2,288.49) [0]
561	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2019) [3/2022]	3,503.69 (2,473.40) [5,554.24]	1,047.53 (2,050.55) [0]
	<u>Road Transport And Highways</u>				
562	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
563	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [1/2019]	227.49 (-) [227.49]	0.00 (0.00) [0]
564	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]
565	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	0.00 (0.00) [0]
566	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
567	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [0/0]	390.51 (-) [390.51]	43.25 (0.00) [0]
568	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	2/2015 (-) [0/0]	670.82 (-) [670.82]	590.00 (0.00) [0]
569	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015 (-) [0/0]	704.26 (-) [704.26]	0.00 (0.00) [0]
570	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	2/2016 (-) [0/0]	257.80 (-) [257.80]	59.30 (0.00) [0]
571	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [1/2019]	1,583.79 (-) [1,583.79]	392.08 (0.00) [0]
572	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [0/0]	960.24 (-) [960.24]	0.00 (0.00) [0]
573	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [3/2019]	1,012.90 (-) [1,012.90]	439.07 (0.00) [36]

574	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,328.85 (546.77) [0]
575	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [12/2018]	928.83 (-) [928.83]	143.96 (0.00) [-]
576	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [10/2018]	794.30 (-) [794.30]	72.51 (0.00) [-]
577	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [10/2018]	795.76 (-) [795.76]	101.33 (0.00) [-]
578	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [10/2018]	810.22 (-) [810.22]	83.86 (0.00) [-]
579	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [0/0]	639.97 (-) [639.97]	0.00 (0.00) [0]
580	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
581	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	6/2018 (-) [0/0]	927.54 (-) [927.54]	29.17 (0.00) [0]
582	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [0/0]	497.05 (-) [497.05]	0.00 (0.00) [0]
583	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
584	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [11/2018]	1,175.00 (-) [1,206.10]	1,209.67 (31.10) [67]
585	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	3/2018 (-) [0/0]	628.45 (-) [628.45]	20.74 (0.00) [0]
586	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	5/2017 (-) [0/0]	327.32 (-) [327.32]	142.73 (0.00) [0]
587	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	7/2017 (-) [0/0]	377.83 (-) [377.83]	57.42 (0.00) [0]
588	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	12/2017 (-) [0/0]	641.02 (-) [641.02]	89.88 (0.00) [0]
589	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	381.86 (-) [381.86]	252.03 (0.00) [0]
590	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
591	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	5/2017 (-) [0/0]	532.49 (-) [532.49]	137.08 (0.00) [0]
592	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [0/0]	871.15 (-) [871.15]	332.25 (0.00) [0]
593	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [0/0]	511.83 (-) [511.83]	40.87 (0.00) [0]
	<u>Urban Development</u>				

594	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY	5/2016	11/2018 (9/2018) [9/2018]	164.00 (-) [164.00]	117.49 (0.00) [-2]
	<u>MAHARASHTRA</u>				
	<u>Coal</u>				
595	ADASA UG TO OC	8/2015	3/2023 (-) [3/2023]	288.90 (-) [288.90]	0.00 (0.00) [0]
596	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2019]	198.68 (-) [198.68]	254.72 (0.00) [0]
597	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	82.13 (0.00) [0]
598	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	236.37 (0.00) [0]
599	BHANEAGAON OC	2/2015	3/2023 (2/2017) [3/2023]	187.94 (409.68) [409.68]	93.19 (221.74) [0]
600	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2019]	304.52 (-) [304.52]	128.93 (0.00) [0]
601	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	389.77 (0.00) [0]
602	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	207.28 (0.00) [0]
603	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2021]	277.65 (-) [277.65]	22.07 (0.00) [0]
604	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	257.35 (0.00) [0]
605	MAKARDHOKRA I OC	9/2014	3/2021 (-) [3/2021]	266.23 (-) [266.23]	143.28 (0.00) [0]
606	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	52.83 (0.00) [0]
607	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	88.13 (0.00) [0]
608	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	179.06 (0.00) [0]
609	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	102.75 (0.00) [0]
	<u>Fertilisers</u>				
610	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	23.29 (0.00) [0]
611	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	2/2016	12/2017 (10/2018) [10/2018]	482.85 (482.85) [482.85]	413.00 (0.00) [10]
612	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (4/2019) [4/2019]	197.79 (209.44) [209.44]	121.76 (11.65) [29]
	<u>Health And Family Welfare</u>				

613	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [0/0]	582.99 (-) [582.99]	4.80 (0.00) [0]
614	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2019]	274.19 (-) [274.19]	122.66 (0.00) [0]
	Petroleum				
615	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
616	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (11/2019) [11/2019]	968.61 (968.61) [968.61]	302.59 (0.00) [0]
617	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	0.05 (0.00) [0]
618	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	212.00 (-) [212.00]	0.08 (0.00) [0]
619	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	348.00 (-) [348.00]	0.05 (0.00) [0]
620	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (3/2019) [3/2019]	861.79 (1,577.15) [1,577.15]	1,195.52 (715.36) [70]
621	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (11/2019) [11/2019]	546.15 (546.15) [546.15]	102.53 (0.00) [0]
622	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (11/2019) [11/2019]	511.30 (511.30) [511.30]	78.15 (0.00) [0]
623	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,006.83) [4,006.83]	570.63 (0.00) [0]
624	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2019) [3/2019]	4,619.94 (4,619.94) [4,619.94]	3,886.50 (0.00) [15]
625	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	105.67 (0.00) [0]
626	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (3/2018) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,842.42 (606.02) [57]
627	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	475.41 (0.00) [0]
628	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY	5/2015	1/2019 (-) [1/2019]	193.40 (-) [193.40]	88.38 (0.00) [0]
629	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2019) [5/2019]	3,190.69 (-) [3,247.19]	2,172.39 (56.50) [13]
630	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	110.72 (0.00) [0]
631	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (3/2019) [3/2019]	6,068.80 (6,068.80) [5,296.93]	4,524.08 (-771.87) [-1]
632	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [7/2019]	4,199.00 (-) [4,199.00]	194.97 (0.00) [-8]

633	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	1,622.94 (0.00) [14]
634	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY	1/2017	5/2019 (5/2019) [5/2019]	474.15 (474.15) [474.15]	299.26 (0.00) [0]
635	PIPELINE REPLACEMENT PROJECT -4	2/2015	5/2017 (12/2018) [12/2018]	2,899.93 (-) [2,504.61]	1,973.99 (-395.32) [19]
636	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	0.00 (0.00) [0]
637	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	48.20 (0.00) [0]
	<u>Power</u>				
638	MOUDA STPP STAGE 2	3/2012	9/2016 (2/2017) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
639	SOLAPUR STPP	3/2012	11/2016 (3/2019) [3/2019]	9,395.18 (-) [9,395.18]	8,870.26 (0.00) [28]
640	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	9/2010 (12/2018) [12/2018]	477.69 (738.48) [738.48]	669.46 (260.79) [99]
	<u>Railways</u>				
641	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [3/2019]	184.06 (199.12) [240.00]	219.77 (55.94) [0]
642	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2021]	2,271.50 (2,271.50) [3,712.50]	1,759.34 (1,441.00) [0]
643	AMRAVATI-NARKHER NL(CR)	6/1994	6/1999 (-) [0/0]	663.01 (668.34) [858.96]	715.32 (195.95) [0]
644	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2020]	495.44 (1,781.98) [1,781.98]	1,316.34 (1,286.54) [192]
645	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (2,081.27) [2,081.27]	1.05 (205.27) [0]
646	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	1,514.45 (-) [1,750.00]	1,510.51 (235.55) [0]
647	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.22 (0.00) [-9]
648	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [8,857.98]	0.00 (-1,110.02) [0]
649	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (2,449.91) [2,449.91]	77.75 (0.00) [0]
650	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2021]	792.89 (792.89) [792.89]	267.58 (0.00) [0]
651	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2022]	1,035.16 (1,035.16) [1,035.16]	12.96 (0.00) [0]
652	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-)	305.00 (-)	251.08 (0.00)

			[3/2019]	[305.00]	[0]
653	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
654	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2019]	5,300.00 (-) [7,986.04]	2,423.55 (2,686.04) [60]
655	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2024]	3,627.47 (3,627.47) [4,817.69]	148.42 (1,190.22) [0]
656	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
657	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (-) [3/2023]	1,908.51 (1,908.00) [2,686.63]	0.00 (778.12) [0]
658	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
659	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
660	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
661	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2021]	229.00 (-) [403.00]	36.28 (174.00) [0]
662	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2022 (-) [3/2022]	637.95 (637.95) [637.95]	24.71 (0.00) [0]
663	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2022]	1,272.19 (1,272.19) [1,272.19]	109.03 (0.00) [0]
664	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (3,168.29) [3,168.29]	937.42 (0.00) [0]
665	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2022]	540.02 (540.02) [540.02]	152.67 (0.00) [0]
	<u>Road Transport And Highways</u>				
666	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]
667	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [5/2019]	1,885.74 (-) [1,885.74]	0.00 (0.00) [0]
668	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [12/2018]	972.50 (-) [972.50]	1,302.48 (0.00) [17]
669	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [0/0]	607.00 (-) [607.00]	0.00 (0.00) [0]
670	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	0.00 (0.00) [0]
671	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [3/2019]	923.04 (-) [923.04]	444.33 (0.00) [28]
672	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-)	744.64 (-)	0.00 (237.36)

			[3/2020]	[982.00]	[0]
673	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/	1,071.61	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,071.61]	[0]
674	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019	446.17	0.00
			(-)	(-)	(0.00)
			[3/2019]	[446.17]	[0]
675	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020	1,098.06	50.30
			(-)	(-)	(62.58)
			[8/2020]	[1,160.64]	[5]
676	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/	1,142.62	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,142.62]	[0]
677	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/	1,101.58	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,101.58]	[0]
678	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019	400.25	37.39
			(-)	(-)	(0.00)
			[6/2019]	[400.25]	[3]
679	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/	1,064.88	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,064.88]	[0]
680	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017	1,059.73	20.00
			(-)	(-)	(11.27)
			[11/2020]	[1,071.00]	[44]
681	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020	1,030.44	196.43
			(-)	(-)	(35.07)
			[5/2020]	[1,065.51]	[2]
682	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020	988.34	182.85
			(-)	(-)	(54.94)
			[8/2020]	[1,043.28]	[5]
683	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018	505.00	165.31
			(-)	(-)	(0.00)
			[4/2019]	[505.00]	[11]
684	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018	197.69	0.00
			(-)	(-)	(0.00)
			[7/2018]	[197.69]	[0]
685	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60	3/2016	7/2018	244.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[244.00]	[0]
686	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019	649.50	41.20
			(-)	(-)	(0.00)
			[3/2019]	[649.50]	[0]
687	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019	244.90	51.51
			(-)	(-)	(0.00)
			[5/2019]	[244.90]	[0]
688	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018	593.26	45.11
			(-)	(-)	(0.00)
			[0/0]	[593.26]	[0]
689	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/	156.26	65.16
			(-)	(227.00)	(0.00)
			[0/0]	[156.26]	[0]
690	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	/	185.82	205.97
			(-)	(292.00)	(0.00)
			[0/0]	[185.82]	[0]
691	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018	531.13	163.10
			(-)	(-)	(0.00)
			[0/0]	[531.13]	[0]
692	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/	168.30	13.43
			(-)	(-)	(0.00)
			[0/0]	[168.30]	[0]

693	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	57.60 (0.00) [0]
694	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [3/2020]	247.02 (-) [157.49]	0.00 (-89.53) [0]
695	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (-) [3/2019]	414.51 (-) [414.00]	169.20 (-0.51) [10]
696	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [5/2019]	296.19 (-) [254.00]	86.95 (-42.19) [-10]
697	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS	4/2010	6/2012 (-) [12/2018]	1,170.52 (-) [1,170.52]	2,056.03 (0.00) [78]
698	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [12/2018]	1,871.34 (-) [1,871.34]	2,263.50 (0.00) [11]
699	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [5/2020]	904.16 (-) [904.16]	97.53 (0.00) [3]
700	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	279.92 (0.00) [0]
701	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [7/2019]	546.00 (-) [546.00]	87.19 (0.00) [0]
702	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [7/2019]	591.66 (-) [591.66]	237.07 (0.00) [0]
703	PANVEL-INDAPUR	12/2011	6/2014 (-) [3/2019]	942.69 (-) [942.69]	374.75 (0.00) [57]
704	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [6/2019]	1,724.55 (-) [1,724.55]	2,042.82 (0.00) [75]
705	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	12/2013	11/2016 (-) [0/0]	220.72 (-) [220.72]	95.02 (0.00) [0]
706	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	11/2016 (-) [0/0]	260.39 (-) [260.39]	87.43 (0.00) [0]
707	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	87.62 (0.00) [0]
708	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	11/2014 (-) [0/0]	292.98 (-) [292.98]	95.60 (0.00) [0]
709	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	6.50 (0.00) [0]
710	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [0/0]	404.94 (-) [404.94]	0.00 (0.00) [0]
711	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [5/2019]	290.73 (-) [290.73]	24.46 (0.00) [-]
712	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	0.00 (0.00) [0]
713	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK	5/2013	2/2014	1,348.20	3,386.77

	SECTION OF NH-50		(-) [6/2019]	(-) [1,348.20]	(0.00) [64]
	<u>Shipping And Ports</u>				
714	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	1/2007	12/2010 (-) [12/2018]	366.39 (-) [669.46]	411.12 (303.07) [96]
	<u>Telecommunications</u>				
715	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (10/2018) [10/2018]	215.30 (214.10) [214.10]	33.46 (-1.20) [5]
716	MAHARASHTRA ACESS (LOT 1)	8/2017	5/2018 (10/2018) [10/2018]	212.70 (-) [212.70]	37.08 (0.00) [5]
717	MAHARASHTRA CORE (LOT1)	8/2017	4/2018 (10/2018) [10/2018]	167.68 (-) [167.68]	30.21 (0.00) [6]
718	MAHARASHTRA NODAL (LOT 1)	8/2017	4/2018 (10/2018) [10/2018]	159.30 (-) [159.30]	12.40 (0.00) [6]
719	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (10/2018) [10/2018]	231.80 (-) [231.80]	39.75 (0.00) [0]
	<u>Urban Development</u>				
720	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2018) [9/2020]	223.37 (-) [223.37]	0.00 (0.00) [2]
721	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
722	NAGPUR METRO RAIL	8/2014	3/2018 (12/2019) [12/2019]	8,680.00 (8,680.00) [8,680.00]	4,256.12 (0.00) [21]
723	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	2/2011	3/2016 (-) [4/2018]	241.33 (-) [349.33]	307.50 (108.00) [0]
724	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	1,793.83 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
725	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2022]	4,454.17 (-) [13,809.00]	7,919.05 (9,354.83) [132]
	<u>Urban Development</u>				
726	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (11/2018) [11/2019]	216.69 (216.69) [216.69]	52.00 (0.00) [56]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
727	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [8/2019]	363.99 (-) [363.99]	71.00 (0.00) [15]
	<u>Railways</u>				
728	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	259.43 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
729	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
730	JORBAT - BARAPANI	1/2011	1/2014	536.00	674.52

			(-) [11/2018]	(-) [536.00]	(0.00) [58]
731	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [3/2019]	479.20 (-) [479.20]	6.14 (0.00) [10]
732	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	<u>Urban Development</u>				
733	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	<u>MIZORAM</u>				
	<u>Railways</u>				
734	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,600.00]	2,318.33 (2,206.53) [81]
	<u>Road Transport And Highways</u>				
735	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
736	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
737	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
738	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	16.00 (0.00) [0]
739	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	88.13 (0.00) [0]
740	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	58.04 (0.00) [0]
	<u>Heavy Industry</u>				
741	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	4/2011	9/2011 (-) [0/0]	1,718.00 (-) [3,827.30]	2,289.00 (2,109.30) [0]
	<u>Petroleum</u>				
742	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
743	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (-) [1,823.00]	306.51 (0.00) [0]
744	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	13.06 (0.00) [0]
745	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	1.03 (0.00) [0]
746	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	448.61 (0.00) [0]
747	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	9/2011 (-) [0/0]	736.65 (-) [571.47]	543.05 (-165.18) [0]

748	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	611.91 (0.00) [0]
749	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	40.68 (0.00) [0]
750	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [10/2019]	890.00 (-) [887.00]	475.64 (-3.00) [0]
751	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2019) [2/2019]	2,915.00 (2,915.00) [2,915.00]	1,921.34 (0.00) [74]
752	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2019 (12/2020) [12/2019]	2,881.40 (-) [2,000.00]	568.10 (-881.40) [0]
753	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	855.11 (0.00) [0]
754	PARADIP HALDIA DURGAPUR LPG PIPELINE	2/2011	6/2018 (-) [10/2018]	913.00 (1,330.00) [1,330.00]	1,308.86 (417.00) [4]
755	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (-) [2,321.00]	619.33 (0.00) [-4]
756	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (10/2020) [10/2020]	690.00 (-) [690.00]	161.13 (0.00) [27]
757	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
758	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [12/2018]	3,957.00 (3,561.00) [3,397.00]	2,212.79 (-560.00) [0]
759	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	18.56 (0.00) [0]
760	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)	11/2016	2/2019 (-) [2/2019]	230.00 (-) [230.00]	78.89 (0.00) [0]
761	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (11/2018) [3/2019]	352.56 (-) [438.84]	180.72 (86.28) [24]
762	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (2/2019) [2/2019]	309.81 (723.40) [723.40]	545.82 (413.59) [52]
	<u>Power</u>				
763	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [2/2020]	198.49 (-) [198.49]	0.80 (0.00) [5]
764	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	8/2008	2/2013 (-) [10/2018]	771.00 (1,624.00) [1,624.00]	1,429.45 (853.00) [68]
765	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	3/2014	3/2016 (9/2018) [11/2018]	155.57 (206.42) [206.42]	145.22 (50.85) [32]
766	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	3/2013	12/2015 (6/2018) [11/2018]	2,514.88 (3,190.27) [3,190.27]	2,281.28 (675.39) [35]
767	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2019]	4,754.42 (-) [9,141.97]	840.87 (4,387.55) [12]

768	EASTERN REGION STRENGTHENING SCHEME -XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	0.00 (0.00) [0]
769	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (9/2018) [11/2018]	196.58 (225.28) [225.28]	148.92 (28.70) [33]
770	EASTERN REGION STRENGTHENING SCHEME XI	5/2016	11/2018 (-) [11/2018]	766.21 (-) [766.21]	375.34 (0.00) [0]
771	EASTERN REGION STRENGTHENING SCHEME XIV	5/2016	11/2018 (-) [11/2018]	167.01 (-) [167.01]	97.53 (0.00) [0]
772	EASTERN REGION STRENGTHENING SCHEME-III	7/2010	11/2012 (9/2018) [10/2018]	1,272.80 (1,731.10) [1,731.10]	1,461.65 (458.30) [71]
773	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (12/2018) [12/2018]	1,364.52 (1,891.41) [1,891.41]	1,202.20 (526.89) [32]
774	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2019) [6/2019]	522.29 (550.18) [550.18]	433.43 (27.89) [31]
775	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	481.12 (0.00) [0]
776	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [6/2019]	235.53 (-) [235.53]	20.09 (0.00) [0]
777	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [2/2019]	322.30 (-) [322.30]	103.28 (0.00) [0]
778	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2018]	197.40 (-) [197.40]	74.71 (0.00) [9]
779	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	5/2016	5/2019 (-) [5/2019]	3,519.59 (-) [3,519.59]	1,861.40 (0.00) [0]
780	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	4/2015	4/2018 (9/2018) [12/2018]	3,705.61 (-) [3,705.61]	2,518.90 (0.00) [8]
781	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C	7/2015	7/2018 (-) [12/2018]	2,247.37 (-) [2,247.37]	1,420.89 (0.00) [5]
782	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	552.21 (0.00) [0]
783	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	3,710.05 (0.00) [0]
784	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	321.99 (0.00) [0]
785	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	79.31 (0.00) [0]
786	INSTALLATION OF STATCOMS IN WESTERN REGION	3/2015	9/2017 (9/2018) [11/2018]	1,071.24 (-) [1,071.24]	630.56 (0.00) [14]
787	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2019]	5,111.33 (-) [6,652.57]	802.18 (1,541.24) [12]
788	NORTH- EAST NORTH WESTERN INTERCONNECTOR I	2/2009	8/2013	11,130.19	12,714.20

	PROJECT		(3/2022) [3/2022]	(13,762.80) [13,762.80]	(2,632.61) [103]
789	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	6/2016 (9/2018) [12/2018]	539.82 (-) [539.82]	419.63 (0.00) [30]
790	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA	3/2017	3/2019 (-) [3/2019]	162.31 (-) [162.31]	22.42 (0.00) [0]
791	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN	7/2016	3/2019 (-) [3/2019]	333.17 (-) [333.17]	250.73 (0.00) [0]
792	PROVISION OF SERIES REACTORS IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	177.52 (-) [177.52]	76.98 (0.00) [0]
793	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	431.89 (-) [431.89]	191.76 (0.00) [0]
794	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	25.85 (0.00) [0]
795	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [3/2019]	562.25 (-) [562.25]	26.40 (0.00) [0]
796	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [4/2019]	3,654.00 (-) [3,654.00]	2,591.63 (0.00) [0]
797	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [4/2019]	608.24 (-) [608.24]	354.00 (0.00) [0]
798	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [6/2019]	203.28 (260.03) [260.03]	181.16 (56.75) [23]
799	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [12/2019]	379.95 (-) [379.95]	21.82 (0.00) [0]
800	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [6/2019]	337.75 (-) [337.75]	16.10 (0.00) [0]
801	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	1/2016	7/2018 (-) [10/2018]	1,455.47 (-) [1,455.47]	1,028.69 (0.00) [3]
802	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	8/2014 (9/2018) [12/2018]	297.33 (534.02) [534.02]	426.98 (236.69) [52]
803	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (12/2018) [12/2018]	487.49 (639.46) [639.46]	499.90 (151.97) [54]
804	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2018) [2/2019]	4,824.12 (5,071.94) [5,071.94]	4,538.37 (247.82) [76]
805	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	3/2015	12/2015 (-) [9/2018]	955.00 (-) [1,364.00]	1,190.30 (409.00) [33]
806	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (9/2018) [11/2018]	268.80 (340.88) [340.88]	229.40 (72.08) [8]
807	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	2/2010	12/2012 (6/2018) [11/2018]	2,144.00 (2,932.88) [2,932.88]	2,654.96 (788.88) [71]
808	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019)	871.62 (-)	407.22 (0.00)

			[9/2019]	[871.62]	[23]
809	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [3/2019]	408.46 (-) [408.46]	139.34 (0.00) [2]
810	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (3/2019) [3/2019]	5,151.37 (-) [5,151.37]	2,716.40 (0.00) [12]
811	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (3/2019) [3/2019]	808.63 (-) [808.63]	332.96 (0.00) [14]
812	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [10/2018]	374.63 (-) [374.63]	187.24 (0.00) [30]
813	WESTERN REGION STRENGTHENING SCHEME-XVI	7/2016	7/2018 (-) [10/2018]	150.99 (-) [150.99]	88.66 (0.00) [3]
814	WESTERN REGION STRENGTHENING SCHEME XVII	2/2017	9/2019 (-) [9/2019]	204.12 (-) [204.12]	89.17 (0.00) [0]
815	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (-) [2/2020]	195.05 (-) [195.05]	55.10 (0.00) [0]
	<u>Railways</u>				
816	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	550.04 (0.00) [0]
817	AMBALA CANTT-DHAPER PH-1 WITH NEW MM OF DHAPER-CHANDIGARH	4/2010	/ (-) [0/0]	338.54 (-) [338.54]	212.64 (0.00) [0]
818	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [0/0]	288.35 (-) [238.36]	281.82 (-49.99) [0]
819	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [0/0]	450.55 (-) [251.05]	19.71 (-199.50) [0]
820	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (704.31) [704.31]	119.69 (0.00) [0]
821	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [2,154.83]	2.46 (1,231.60) [0]
822	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [0/0]	175.80 (-) [173.91]	148.10 (-1.89) [0]
823	CALICUT-MANGALORE (DL) (SR)	2/1996	/ (-) [0/0]	240.00 (-) [579.37]	537.30 (339.37) [0]
824	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	229.95 (1,211.86) [0]
825	CHANDIGARH-BADDI NL	4/2007	/ (-) [0/0]	328.14 (-) [1,540.00]	45.20 (1,211.86) [0]
826	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [0/0]	337.96 (-) [186.89]	69.96 (-151.07) [0]
827	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,350.00]	2.27 (1,826.48) [0]
828	CHHAPRA-BALLIA UP	3/2013	1/2019 (-)	295.00 (-)	174.83 (182.31)

			[1/2019]	[477.31]	[0]
829	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [871.56]	97.82 (627.78) [0]
830	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [0/0]	236.21 (-) [1,395.63]	98.43 (1,159.42) [0]
831	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2019) [3/2022]	1,347.26 (-) [1,347.26]	593.72 (0.00) [0]
832	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2019) [3/2022]	1,640.04 (-) [1,640.04]	599.20 (0.00) [0]
833	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [0/0]	365.17 (-) [528.34]	99.67 (163.17) [0]
834	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR	4/2013	/ (-) [0/0]	1,239.00 (-) [1,239.00]	0.00 (0.00) [0]
835	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [0/0]	336.91 (-) [336.91]	143.18 (0.00) [0]
836	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (12/2012) [6/2016]	584.41 (-) [1,005.23]	1,069.44 (420.82) [0]
837	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [12/2022]	2,030.50 (-) [2,030.50]	10.34 (0.00) [-]
838	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (3/2024) [3/2024]	651.00 (-) [1,009.00]	7.96 (358.00) [108]
839	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
840	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	14.62 (134.08) [0]
841	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (-) [4/2020]	511.86 (-) [1,756.00]	967.96 (1,244.14) [0]
842	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
843	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	4/1986	3/1994 (-) [0/0]	158.77 (274.56) [634.48]	629.43 (475.71) [0]
844	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [3/2022]	2,912.96 (-) [3,845.60]	1.92 (932.64) [0]
845	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [3/2020]	678.54 (-) [678.54]	0.00 (0.00) [12]
846	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2020]	542.18 (-) [693.90]	310.26 (151.72) [0]
847	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [0/0]	172.03 (-) [260.60]	14.50 (88.57) [0]
848	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [718.54]	274.46 (488.51) [0]

849	HOTGI-KUDGI-GADAG	3/2015	3/2019 (3/2021) [3/2021]	1,614.59 (1,614.59) [1,614.59]	641.23 (0.00) [24]
850	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [11/2018]	157.94 (-) [157.94]	50.50 (0.00) [0]
851	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [0/0]	166.89 (-) [166.89]	246.00 (0.00) [0]
852	JAKHAL-MANSA DOUBLING ON SPR SECTION	4/2008	/ (-) [0/0]	162.96 (-) [162.96]	153.31 (0.00) [0]
853	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [3/2016]	625.00 (-) [845.58]	0.00 (220.58) [0]
854	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	3/2002	6/2007 (-) [0/0]	625.30 (408.76) [876.10]	841.57 (250.80) [0]
855	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (3/2023) [3/2024]	2,206.29 (-) [1,996.94]	215.72 (-209.35) [120]
856	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [0/0]	563.51 (-) [1,813.59]	332.87 (1,250.08) [0]
857	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [0/0]	174.56 (-) [160.97]	70.86 (-13.59) [0]
858	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	4/1999	/ (-) [0/0]	744.71 (-) [1,126.79]	751.05 (382.08) [0]
859	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	4/2010	3/2017 (-) [0/0]	423.66 (-) [720.59]	529.28 (296.93) [0]
860	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2021]	2,063.03 (-) [2,063.03]	343.70 (0.00) [0]
861	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (3/2024) [3/2023]	1,856.95 (1,856.95) [1,955.27]	225.85 (98.32) [0]
862	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (346.15) [457.08]	343.65 (186.94) [0]
863	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [0/0]	318.50 (-) [852.80]	147.81 (534.30) [0]
864	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	972.82 (5,845.65) [178]
865	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [3/2019]	120.70 (-) [1,800.00]	103.10 (1,679.30) [0]
866	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [0/0]	278.66 (-) [1,255.98]	147.21 (977.32) [0]
867	MIRAJ-LONDA	3/2015	/ (3/2021) [3/2021]	1,830.00 (1,190.92) [1,190.92]	182.68 (-639.08) [-]
868	MM FROM BURAMARA-CHAKULIA	4/2008	0/0 (12/2024) [12/2024]	466.48 (-) [1,000.00]	0.83 (533.52) [-]
869	MONIGRAM- NIMTITA	4/2012	/	250.93	189.85

			(-) [0/0]	(-) [259.23]	(8.30) [0]
870	MUNEERABAD-MAHABOONNAGAR(NL),SCR	4/1997	3/2000 (3/2019) [12/2023]	1,723.00 (236.41) [3,501.83]	719.03 (1,778.83) [285]
871	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	123.11 (246.16) [0]
872	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [0/0]	450.00 (-) [2,100.00]	968.28 (1,650.00) [0]
873	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [0/0]	115.27 (-) [857.30]	31.99 (742.03) [0]
874	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	64.09 (228.78) [0]
875	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [0/0]	241.52 (374.00) [394.28]	148.33 (152.76) [0]
876	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2019]	1,798.00 (-) [1,798.00]	0.00 (0.00) [0]
877	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [3/2018]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
878	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [12/2020]	1,180.19 (-) [3,040.00]	3,036.52 (1,859.81) [144]
879	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [3/2020]	600.00 (-) [685.99]	3.38 (85.99) [0]
880	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [0/0]	261.38 (-) [332.14]	343.42 (70.76) [0]
881	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2022]	915.98 (-) [2,142.49]	291.74 (1,226.51) [0]
882	PLASSEY-JIAGANJ DOUBLING	4/2011	3/2015 (-) [0/0]	248.07 (-) [234.41]	148.00 (-13.66) [0]
883	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [0/0]	299.60 (-) [269.60]	1.12 (-30.00) [0]
884	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	3/1998	/ (-) [0/0]	280.00 (-) [1,122.00]	834.87 (842.00) [0]
885	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [2,878.97]	182.36 (796.22) [0]
886	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	970.34 (-) [2,062.20]	674.76 (1,091.86) [-]
887	SAINTHIA-TARAPITH 3RD LINE	4/2011	/ (-) [0/0]	193.44 (-) [186.64]	166.25 (-6.80) [0]
888	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE	4/2010	/ (-) [0/0]	268.52 (-) [268.52]	78.81 (0.00) [0]
889	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-)	297.47 (-)	52.10 (-144.45)

			[0/0]	[153.02]	[0]
890	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2020]	136.55 (-) [534.24]	143.74 (397.69) [48]
891	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (12/2023) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
892	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [0/0]	23.56 (-) [1,330.73]	9.31 (1,307.17) [0]
893	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [0/0]	365.17 (-) [365.67]	1.76 (0.50) [0]
894	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
895	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/ (-) [0/0]	876.00 (-) [876.00]	0.00 (0.00) [0]
896	YELAHANKA-PENUKONDA	5/2015	3/2020 (3/2020) [3/2022]	860.43 (860.43) [958.00]	469.91 (97.57) [24]
	<u>Road Transport And Highways</u>				
897	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,489.54 (0.00) [0]
898	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	2,294.94 (1,016.78) [0]
899	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
900	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [0/0]	604.00 (-) [604.00]	423.83 (0.00) [0]
901	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [7/2019]	754.00 (-) [754.00]	1,363.43 (0.00) [76]
902	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	0.00 (0.00) [-]
903	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,675.28 (0.00) [0]
904	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,136.31 (0.00) [69]
905	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	/ (-) [0/0]	789.83 (-) [789.83]	109.77 (0.00) [0]
	<u>Telecommunications</u>				
906	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
907	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
908	DIMAPUR-TIZIT NL	4/2013	3/2020 (-)	4,274.00 (-)	0.00 (0.00)

			[3/2020]	[4,274.00]	[0]
909	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [12/2021]	2,326.52 (2,446.57) [3,000.00]	655.38 (673.48) [81]
	Road Transport And Highways				
910	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [9/2018]	239.30 (-) [239.30]	0.00 (0.00) [0]
911	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2018]	285.68 (-) [285.68]	0.00 (0.00) [0]
912	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [9/2018]	282.98 (-) [282.98]	0.00 (0.00) [0]
913	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2018]	387.00 (-) [387.00]	0.00 (0.00) [0]
914	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [9/2018]	500.09 (-) [500.09]	0.00 (0.00) [0]
915	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
916	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	339.57 (-) [339.57]	0.00 (0.00) [0]
917	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [9/2018]	315.03 (-) [315.03]	0.00 (0.00) [0]
918	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [9/2018]	240.64 (-) [240.64]	0.00 (0.00) [0]
919	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	215.12 (-) [215.12]	0.00 (0.00) [0]
920	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [9/2018]	215.79 (-) [215.79]	0.00 (0.00) [0]
921	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [9/2018]	272.89 (-) [272.89]	0.00 (0.00) [0]
922	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]
923	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [9/2018]	251.97 (-) [251.97]	0.00 (0.00) [0]
924	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [9/2018]	237.72 (-) [237.72]	0.00 (0.00) [0]
925	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
926	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
927	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
928	WIDENING OF 2(TWO) LANING OF LONGLENG- CHANTONGYA ROAD, MON-TAMLU-MERANGKONG	12/2010	2/2011 (-)	1,296.00 (-)	0.00 (0.00)

	ROAD, PHEK- PFUTSERO ROA		[0/0]	[1,296.00]	[0]
	<u>ODISHA</u>				
	<u>Coal</u>				
929	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	234.48 (0.00) [108]
930	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2019]	172.08 (-) [172.08]	264.26 (0.00) [108]
931	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2021]	479.15 (-) [479.15]	104.48 (0.00) [24]
932	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	363.95 (0.00) [36]
933	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	413.85 (0.00) [0]
934	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2020]	479.53 (-) [479.53]	239.22 (0.00) [84]
935	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2021]	337.66 (-) [337.66]	44.91 (0.00) [24]
936	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2019]	457.77 (-) [457.77]	581.54 (0.00) [72]
937	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	33.53 (0.00) [24]
938	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2018]	302.96 (-) [302.96]	302.96 (0.00) [0]
939	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	689.20 (0.00) [0]
	<u>Mines</u>				
940	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	95.59 (0.00) [0]
941	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (11/2020) [11/2020]	355.00 (355.00) [355.00]	31.92 (0.00) [0]
942	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.00 (0.00) [0]
943	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	300.68 (0.00) [0]
	<u>Petroleum</u>				
944	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	14.96 (0.00) [0]
945	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	1.51 (0.00) [0]
946	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (243.53) [243.53]	29.47 (0.00) [0]
947	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-)	181.20 (-)	12.65 (0.00)

			[7/2022]	[181.20]	[0]
948	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	597.57 (0.00) [0]
949	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	7/2021 (-) [7/2021]	4,807.08 (-) [4,807.08]	19.10 (0.00) [0]
950	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [1/2019]	429.00 (-) [429.00]	232.84 (0.00) [0]
951	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	33.57 (0.00) [0]
952	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (12/2018) [12/2018]	3,150.00 (-) [3,150.00]	2,189.60 (0.00) [15]
	<u>Power</u>				
953	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	8/2018 (6/2019) [6/2019]	12,532.44 (-) [13,740.53]	8,027.68 (1,208.09) [10]
954	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [4/2019]	844.64 (-) [844.64]	303.70 (0.00) [0]
	<u>Railways</u>				
955	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [942.95]	879.77 (0.00) [24]
956	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2022]	810.28 (843.04) [843.04]	73.71 (32.76) [17]
957	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2020]	1,172.92 (-) [1,172.92]	210.71 (0.00) [15]
958	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
959	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2020]	5,200.00 (-) [5,200.00]	0.00 (0.00) [0]
960	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (9/2009) [3/2019]	1,185.64 (-) [1,844.47]	1,277.02 (658.83) [15]
961	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	1,547.38 (1,547.38) [1,547.38]	183.12 (0.00) [0]
962	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2021]	701.61 (-) [810.02]	83.66 (108.41) [28]
963	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2018]	133.41 (207.00) [385.00]	370.38 (251.59) [117]
964	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2021]	2,923.13 (-) [3,791.66]	1,088.86 (868.53) [147]
965	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2022]	2,361.74 (2,361.74) [2,361.74]	77.20 (0.00) [0]
966	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [3/2022]	969.83 (-) [969.83]	348.22 (0.00) [24]
967	RUPSA BANGRIPOSI 90 KM WITH MM FOR	4/1995	12/2021	524.43	184.09

	UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO		(12/2024) [12/2024]	(-) [939.00]	(414.57) [36]
968	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	180.78 (82.22) [0]
969	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2021]	948.04 (-) [970.00]	918.32 (21.96) [12]
970	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2020]	1,111.99 (1,539.28) [1,539.28]	742.32 (427.29) [13]
971	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (245.00) [1,202.70]	618.94 (0.00) [82]
972	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (1,928.07) [1,928.07]	564.41 (1,117.29) [21]
973	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (2,735.00) [2,335.67]	243.95 (0.00) [0]
<u>Road Transport And Highways</u>					
974	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [0/0]	1,282.94 (-) [1,282.94]	0.00 (0.00) [0]
975	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [0]
976	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
977	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [0/0]	319.80 (320.00) [320.00]	0.00 (0.20) [0]
978	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [0/0]	319.80 (-) [319.80]	0.00 (0.00) [0]
979	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [0/0]	1,069.65 (-) [1,069.65]	0.00 (0.00) [0]
980	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [10/2015]	1,410.00 (-) [1,410.00]	1,555.96 (0.00) [0]
981	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [0/0]	1,008.96 (-) [1,008.96]	0.00 (0.00) [0]
982	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [0/0]	564.66 (-) [564.66]	0.00 (0.00) [0]
983	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [11/2020]	476.56 (-) [476.56]	0.00 (0.00) [40]
984	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
985	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [0/0]	953.09 (-) [953.09]	0.00 (0.00) [0]
986	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [0/0]	668.86 (-) [668.86]	0.00 (0.00) [0]
987	REHABILITATION AND UP-GRADATION OF EXISTING 2-	1/2018	/	614.48	0.00

	LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG		(-) [0/0]	(-) [614.48]	(0.00) [0]
988	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	0.00 (0.00) [0]
989	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
990	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [0/0]	503.88 (-) [503.88]	0.00 (0.00) [0]
991	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2020]	1,288.07 (-) [1,420.00]	0.00 (131.93) [0]
992	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
993	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
994	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
995	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	0.00 (-0.05) [0]
996	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
997	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	0.00 (0.04) [0]
998	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
999	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1000	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,613.62 (0.00) [0]
1001	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	3/2014	5/2016 (-) [0/0]	162.51 (163.00) [163.00]	0.00 (0.49) [0]
1002	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	0.00 (0.50) [0]
1003	WIDENING AND STRENGTHENING OF EXISTING SINGLE TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [240.00]	0.00 (0.09) [0]
1004	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [327.00]	0.00 (0.37) [0]
1005	WIDENING OF EXISTING SINGLE TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [11/2018]	157.30 (157.00) [157.00]	0.00 (-0.30) [5]
1006	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	0.00 (0.00) [0]
1007	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900	12/2011	8/2015 (-)	191.08 (-)	0.00 (0.00)

	(BERHMAPUR-TAPTA		[0/0]	[191.08]	[0]
1008	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [0/0]	226.31 (226.00) [226.00]	0.00 (-0.31) [0]
	<u>Steel</u>				
1009	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (-) [2/2019]	3,127.30 (-) [3,127.30]	2,426.76 (0.00) [10]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1010	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	23.51 (0.00) [0]
1011	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	28.31 (0.00) [0]
	<u>Health And Family Welfare</u>				
1012	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [6/2020]	703.00 (-) [703.00]	276.91 (0.00) [0]
1013	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [12/2018]	152.95 (-) [152.95]	58.52 (0.00) [10]
	<u>Railways</u>				
1014	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	4/2009	/ (-) [0/0]	396.04 (-) [369.00]	186.27 (-27.04) [0]
1015	QADIAN-BEAS	4/2011	/ (-) [0/0]	205.22 (-) [205.22]	1.59 (0.00) [0]
	<u>Road Transport And Highways</u>				
1016	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	/ (-) [0/0]	573.96 (605.00) [605.00]	209.74 (31.04) [0]
1017	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	/ (-) [0/0]	486.74 (-) [486.74]	189.39 (0.00) [0]
1018	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (-) [1,169.61]	120.68 (0.00) [-]
1019	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	/ (-) [0/0]	463.65 (546.00) [463.65]	280.16 (0.00) [0]
1020	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	/ (-) [0/0]	483.38 (-) [483.38]	65.76 (0.00) [0]
1021	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	/ (-) [0/0]	616.36 (-) [616.36]	68.58 (0.00) [0]
1022	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	299.81 (0.00) [0]
1023	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [889.24]	389.64 (0.00) [0]
1024	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [9/2019]	1,388.34 (-) [1,388.34]	72.07 (0.00) [0]
1025	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	/ (-) [0/0]	312.79 (-) [312.79]	17.57 (0.00) [0]

1026	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	7/2014	/ (-) [0/0]	319.80 (-) [319.80]	102.55 (0.00) [0]
1027	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	0.00 (1.73) [1]
1028	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	99.86 (0.00) [0]
1029	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	/ (-) [0/0]	578.38 (-) [578.38]	128.53 (0.00) [0]
1030	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [4/2019]	447.29 (-) [447.29]	17.60 (0.00) [16]
1031	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [0/0]	261.76 (-) [261.76]	0.00 (0.00) [0]
1032	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [11/2018]	479.00 (-) [479.00]	391.33 (0.00) [-]
1033	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	/ (-) [4/2019]	273.06 (-) [273.06]	17.85 (0.00) [-]
1034	JALANDHAR - AMRITSAR	1/2014	1/2016 (-) [0/0]	523.85 (-) [523.85]	170.68 (0.00) [0]
1035	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	/ (-) [0/0]	435.90 (-) [435.90]	31.02 (0.00) [0]
1036	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	/ (-) [0/0]	279.68 (-) [279.68]	25.28 (0.00) [0]
1037	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	/ (-) [0/0]	899.21 (-) [899.21]	25.08 (0.00) [0]
1038	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	26.92 (0.00) [0]
	<u>Urban Development</u>				
1039	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (8/2018) [11/2018]	388.00 (-) [388.00]	379.31 (0.00) [18]
1040	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	9/2018 (-) [9/2018]	430.00 (-) [430.00]	0.00 (0.00) [0]
1041	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (6/2019) [6/2019]	294.00 (-) [294.00]	112.23 (0.00) [2]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1042	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (3/2017) [12/2020]	12,320.00 (-) [12,320.00]	9,760.00 (0.00) [48]
	<u>Coal</u>				
1043	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	173.06 (0.00) [0]
1044	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	8.71 (0.00) [0]

	Petroleum				
1045	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1046	LPG BP PROJECT JODHPUR	3/2018	/ (-) [0/0]	229.80 (-) [229.80]	69.04 (0.00) [0]
	Power				
1047	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [1/2019]	1,429.38 (-) [1,429.38]	743.82 (0.00) [0]
1048	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	7/2015	11/2017 (10/2018) [11/2018]	307.18 (-) [307.18]	206.21 (0.00) [12]
	Railways				
1049	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,103.04]	2.32 (229.33) [0]
1050	AJMER-BANGURGRAM	4/2011	11/2019 (-) [11/2019]	213.39 (-) [244.02]	171.82 (30.63) [0]
1051	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]
1052	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2019]	242.09 (-) [349.00]	248.23 (106.91) [0]
1053	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2019]	246.08 (-) [348.55]	113.46 (102.47) [-6]
1054	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [2/2019]	410.08 (780.98) [795.01]	437.03 (384.93) [0]
1055	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	4/2008	3/2015 (-) [3/2020]	829.74 (-) [1,216.00]	687.70 (386.26) [60]
1056	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	4/2008	3/2014 (3/2019) [3/2019]	653.19 (-) [1,116.00]	756.73 (462.81) [60]
1057	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [8/2022]	808.85 (-) [808.85]	0.00 (0.00) [0]
1058	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [12/2019]	420.18 (295.02) [865.00]	65.19 (444.82) [-3]
1059	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [12/2019]	493.17 (-) [493.17]	407.32 (0.00) [21]
1060	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1061	RANI-MARWAR JN. PATCH DOUBLING	4/2012	11/2018 (-) [12/2018]	288.97 (-) [346.35]	282.12 (57.38) [1]
1062	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [10/2018]	236.93 (-) [294.90]	157.63 (57.97) [0]
	Road Transport And Highways				
1063	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [10/2018]	597.00 (-) [597.00]	596.06 (0.00) [12]

1064	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [1/2019]	320.30 (-) [320.30]	174.91 (0.00) [0]
1065	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [11/2018]	530.07 (-) [530.07]	556.02 (0.00) [27]
1066	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [11/2019]	688.70 (-) [688.70]	426.85 (0.00) [-]
1067	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1068	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [12/2018]	822.90 (-) [822.90]	647.00 (0.00) [8]
1069	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	0.00 (0.00) [0]
1070	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1071	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	0.00 (0.00) [0]
1072	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [6/2019]	763.23 (-) [763.23]	0.00 (0.00) [0]
1073	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	0.00 (0.00) [3]
1074	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	0.00 (0.00) [0]
1075	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (9/2017) [10/2018]	1,673.70 (-) [1,673.70]	3,079.44 (0.00) [84]
1076	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1077	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1078	PADI - DAHOD	11/2014	5/2017 (-) [10/2018]	279.14 (-) [279.14]	211.16 (0.00) [17]
1079	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	9/2015	3/2018 (-) [11/2018]	567.51 (-) [567.51]	42.79 (0.00) [8]
1080	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1081	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	1/1991	5/2016 (-) [0/0]	208.87 (-) [208.87]	206.78 (0.00) [0]
1082	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	10/2016 (-) [0/0]	269.26 (-) [269.26]	212.72 (0.00) [0]
1083	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1084	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF	9/2016	/	1,100.19	530.00

	NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I		(-) [12/2019]	(-) [1,100.19]	(0.00) [-]
1085	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/	1,239.82	475.69
			(-) [5/2020]	(-) [1,239.82]	(0.00) [-]
1086	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020	894.00	0.00
			(-) [4/2020]	(-) [894.00]	(0.00) [0]
1087	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016	425.19	274.20
			(-) [3/2019]	(-) [425.19]	(0.00) [30]
1088	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/	275.90	242.51
			(-) [10/2018]	(-) [275.90]	(0.00) [-]
1089	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018	331.46	232.15
			(-) [10/2018]	(-) [331.46]	(0.00) [0]
1090	TWO LANNING WITH PAVED SHOULDER OF SALASAR- NAGAU	6/2016	6/2019	637.18	535.30
			(-) [9/2019]	(-) [637.18]	(0.00) [3]
1091	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/	1,103.88	0.00
			(-) [0/0]	(-) [1,103.88]	(0.00) [0]
1092	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015	257.09	14.80
			(-) [0/0]	(-) [257.09]	(0.00) [0]
1093	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015	383.40	224.68
			(-) [6/2019]	(-) [383.40]	(0.00) [51]
1094	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015	269.22	33.24
			(-) [0/0]	(-) [269.22]	(0.00) [0]
1095	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018	621.43	0.00
			(-) [0/0]	(-) [621.43]	(0.00) [0]
	Urban Development				
1096	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017	189.00	0.00
			(-) [0/0]	(-) [189.00]	(0.00) [0]
1097	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019	549.31	152.99
			(-) [9/2019]	(-) [540.42]	(-8.89) [2]
	SIKKIM				
	Civil Aviation				
1098	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	1/2009	1/2011	309.46	546.69
			(-) [9/2018]	(-) [553.53]	(244.07) [92]
	Railways				
1099	SEVOK RANGPO, NEFR	4/2008	12/2015	1,339.48	385.84
			(-) [3/2020]	(-) [4,084.69]	(2,745.21) [51]
	Road Transport And Highways				
1100	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013	182.28	24.36
			(-) [0/0]	(-) [182.00]	(-0.28) [0]
1101	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013	151.59	0.00
			(-) [0/0]	(-) [151.59]	(0.00) [0]
1102	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013	166.27	0.00
			(-) [0/0]	(-) [166.27]	(0.00) [0]

1103	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
1104	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [11/2017]	290.05 (-) [290.05]	18.12 (0.00) [0]
1105	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
1106	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [6/2018]	264.84 (-) [264.84]	0.00 (0.00) [0]
1107	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1108	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	9,827.00 (0.00) [36]
1109	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [3/2019]	3,492.00 (5,677.00) [6,100.00]	5,687.52 (2,608.00) [102]
	<u>Coal</u>				
1110	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (9/2019) [9/2019]	1,458.17 (709.06) [709.06]	390.90 (-749.11) [51]
1111	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (10/2018) [12/2018]	5,907.11 (-) [5,907.11]	5,666.08 (0.00) [36]
1112	NEYVELI SOLAR POWER PROJECT 130 MW	5/2016	6/2017 (12/2017) [12/2017]	687.28 (759.19) [759.19]	758.30 (71.91) [0]
	<u>Petroleum</u>				
1113	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	0.17 (0.00) [0]
1114	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	465.00 (0.00) [0]
1115	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [5/2021]	466.43 (-) [466.43]	1.18 (0.00) [7]
1116	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [12/2020]	4,497.00 (-) [4,497.00]	283.91 (0.00) [24]
1117	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1118	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [4/2019]	390.52 (390.52) [390.52]	154.56 (0.00) [1]
1119	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [0/0]	678.00 (-) [678.00]	5.12 (0.00) [0]
1120	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	11.79 (0.00) [0]
1121	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.42 (0.00) [0]

	<u>Power</u>				
1122	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	9/2011	9/2014 (9/2018) [10/2018]	1,940.13 (2,702.65) [2,702.65]	2,529.92 (762.52) [49]
1123	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (9/2018) [12/2018]	1,779.29 (2,187.32) [2,534.00]	2,051.63 (754.71) [121]
1124	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [7/2019]	186.17 (-) [186.17]	50.27 (0.00) [0]
	<u>Railways</u>				
1125	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [3/2018]	257.00 (257.00) [257.00]	0.00 (0.00) [0]
1126	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [2/2019]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1127	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	4/1998	/ (-) [0/0]	271.24 (-) [520.00]	468.18 (248.76) [0]
1128	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	9/2006	/ (-) [0/0]	343.17 (-) [1,065.00]	1,049.68 (721.83) [0]
1129	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1130	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (3/2019) [3/2019]	495.74 (495.74) [734.01]	438.72 (238.27) [69]
1131	KARUR-SALEM(NL),SR	2/1997	/ (-) [0/0]	155.55 (-) [920.00]	856.94 (764.45) [0]
1132	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [3/2020]	760.00 (-) [1,182.31]	0.00 (422.31) [0]
1133	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION	2/1997	3/2015 (-) [0/0]	458.63 (-) [458.63]	0.92 (0.00) [0]
1134	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	73.45 (285.59) [-]
1135	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING	2/2003	3/2009 (-) [0/0]	199.55 (-) [330.32]	2.12 (130.77) [0]
1136	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.	2/2006	3/2012 (-) [0/0]	208.00 (-) [208.00]	3.58 (0.00) [0]
1137	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,700.00]	0.00 (0.00) [0]
1138	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2019]	724.69 (-) [2,072.50]	1,129.33 (1,347.81) [0]
1139	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.61 (661.00) [0]
1140	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [302.02]	304.07 (33.15) [0]
1141	TIDIVANAM-NAGARI (NL)	9/2006	/ (-)	582.83 (-)	236.09 (1,717.17)

			[0/0]	[2,300.00]	[0]
1142	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/	227.40	61.81
			(-)	(-)	(672.60)
			[0/0]	[900.00]	[0]
1143	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020	303.98	1,292.55
			(-)	(-)	(676.02)
			[3/2020]	[980.00]	[0]
1144	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024	1,567.00	0.00
			(-)	(-)	(0.00)
			[3/2026]	[1,567.00]	[24]
1145	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	2/2000	3/2014	200.84	394.26
			(-)	(-)	(0.00)
			[0/0]	[200.84]	[0]
1146	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	2/2005	3/2010	600.00	671.00
			(-)	(600.00)	(45.54)
			[0/0]	[645.54]	[0]
	<u>Road Transport And Highways</u>				
1147	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013	485.00	406.68
			(-)	(-)	(0.00)
			[12/2018]	[485.00]	[64]
1148	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	4/2012	4/2014	624.00	350.79
			(-)	(-)	(0.00)
			[12/2019]	[624.00]	[68]
1149	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017	244.27	0.00
			(-)	(-)	(0.00)
			[0/0]	[244.27]	[0]
1150	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017	1,227.87	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,227.87]	[0]
1151	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015	258.97	0.00
			(-)	(-)	(9.95)
			[0/0]	[268.92]	[0]
1152	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015	154.14	0.00
			(-)	(-)	(0.00)
			[0/0]	[154.14]	[0]
1153	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013	600.00	324.02
			(-)	(-)	(0.00)
			[0/0]	[600.00]	[0]
1154	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017	1,387.11	881.98
			(-)	(-)	(0.00)
			[5/2019]	[1,387.11]	[18]
1155	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/	1,166.26	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,166.26]	[0]
1156	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016	641.17	244.33
			(-)	(-)	(0.00)
			[4/2019]	[641.17]	[33]
1157	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017	1,176.37	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,176.37]	[0]
1158	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018	707.82	168.88
			(-)	(-)	(0.00)
			[6/2019]	[707.82]	[10]
1159	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020	848.45	5.00
			(-)	(-)	(0.00)
			[3/2020]	[848.45]	[0]
1160	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018	641.17	204.31
			(-)	(-)	(0.00)
			[0/0]	[641.17]	[0]
1161	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC	3/2015	7/2015	157.18	0.00
			(-)	(162.00)	(4.82)

	MO		[0/0]	[162.00]	[0]
1162	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/	379.90	0.00
			(-)	(-)	(0.00)
			[0/0]	[379.90]	[0]
1163	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013	1,250.00	1,329.17
			(-)	(-)	(0.00)
			[12/2018]	[1,250.00]	[60]
1164	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	11/2014	11/2016	563.92	186.50
			(-)	(-)	(0.00)
			[0/0]	[563.92]	[0]
1165	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017	401.11	273.89
			(-)	(-)	(0.00)
			[0/0]	[401.11]	[0]
1166	TRICHY - KARUR	3/2007	7/2008	516.00	627.37
			(-)	(-)	(0.00)
			[0/0]	[516.00]	[0]
1167	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013	374.00	237.00
			(-)	(-)	(0.00)
			[12/2018]	[374.00]	[67]
1168	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017	563.92	96.48
			(-)	(-)	(0.00)
			[6/2019]	[563.92]	[18]
	<u>Shipping And Ports</u>				
1169	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017	600.00	1.45
			(-)	(258.00)	(-342.10)
			[5/2020]	[257.90]	[29]
1170	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017	244.50	275.98
			(-)	(258.00)	(31.48)
			[0/0]	[275.98]	[0]
1171	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006	150.00	139.80
			(-)	(-)	(450.00)
			[0/0]	[600.00]	[0]
1172	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008	2,427.40	831.21
			(-)	(-)	(0.00)
			[0/0]	[2,427.40]	[0]
	<u>Urban Development</u>				
1173	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	209.00	52.00
			(-)	(-)	(0.00)
			[10/2019]	[209.00]	[0]
1174	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018	3,770.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[3,770.00]	[0]
1175	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015	14,600.00	16,352.77
			(-)	(-)	(4,458.00)
			[0/0]	[19,058.00]	[0]
1176	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/	348.77	0.00
			(-)	(-)	(0.00)
			[0/0]	[348.77]	[0]
1177	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	4/2014	9/2016	332.72	321.13
			(3/2018)	(-)	(9.28)
			[9/2018]	[342.00]	[24]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1178	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020	477.65	0.00
			(-)	(-)	(0.00)
			[3/2020]	[477.65]	[0]
1179	KOYAGUDEM OPENCASE PROJECT	10/2015	3/2018	426.79	0.00
			(-)	(-)	(0.00)
			[3/2019]	[426.79]	[12]
1180	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015	447.06	353.61
			(-)	(-)	(-9.55)

			[3/2021]	[437.51]	[72]
1181	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1182	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2019]	413.84 (-) [413.84]	0.00 (0.00) [0]
1183	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2019]	397.09 (-) [442.42]	79.96 (45.33) [0]
1184	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	146.45 (-33.01) [44]
1185	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	12.69 (-78.25) [72]
1186	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [3/2018]	181.19 (-) [181.19]	159.87 (0.00) [0]
1187	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	477.74 (70.65) [132]
1188	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	1.31 (186.52) [72]
1189	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2019]	430.45 (-) [415.37]	160.45 (-15.08) [36]
1190	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [3/2019]	365.01 (-) [365.01]	204.26 (0.00) [45]
1191	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2019]	209.78 (-) [209.78]	154.21 (0.00) [48]
1192	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (3/2024) [3/2024]	249.03 (448.86) [448.86]	186.91 (199.83) [144]
	<u>Power</u>				
1193	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	7/2020 (10/2020) [10/2020]	10,598.98 (-) [10,598.98]	2,555.03 (0.00) [3]
	<u>Railways</u>				
1194	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (3/2017) [12/2020]	632.68 (-) [816.55]	561.52 (183.87) [57]
1195	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	169.16 (0.00) [0]
1196	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	616.08 (-) [723.00]	0.00 (106.92) [0]
1197	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (-) [815.00]	3.69 (356.75) [0]
1198	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	0.00 (65.24) [0]
1199	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (3/2022) [3/2022]	1,160.48 (-) [1,160.47]	93.75 (-0.01) [144]
1200	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92

			(-) [0/0]	(2,911.84) [2,911.84]	(1,799.84) [0]
1201	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	/ (3/2017) [3/2017]	124.43 (926.23) [1,025.00]	1,018.51 (900.57) [0]
1202	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	197.87 (0.00) [0]
	<u>Road Transport And Highways</u>				
1203	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	3/2016 (-) [0/0]	340.00 (-) [340.00]	0.00 (0.00) [0]
1204	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [6/2019]	1,266.60 (-) [1,544.00]	1,407.12 (277.40) [33]
1205	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	3/2011	12/2015 (-) [0/0]	218.31 (-) [339.82]	208.28 (121.51) [0]
1206	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	0.00 (0.00) [0]
1207	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1208	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	0.00 (0.00) [0]
1209	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (-) [7/2019]	1,423.96 (-) [1,423.96]	502.66 (0.00) [8]
1210	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO	12/2013	3/2016 (-) [0/0]	158.65 (-) [158.65]	103.50 (0.00) [0]
1211	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	3/2016 (-) [0/0]	177.18 (-) [177.18]	40.51 (0.00) [0]
1212	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1213	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [313.27]	0.00 (17.80) [0]
1214	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	12/2016 (-) [0/0]	244.30 (-) [156.09]	0.00 (-88.21) [0]
1215	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW	12/2013	3/2016 (-) [0/0]	244.08 (-) [244.08]	38.32 (0.00) [0]
	<u>Urban Development</u>				
1216	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (-) [209.84]	6.61 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
1217	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
1218	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (1,942.00) [3,374.00]	3,015.98 (2,232.00) [60]

1219	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
1220	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (4,118.00) [1,733.20]	1,543.99 (838.20) [0]
	<u>Road Transport And Highways</u>				
1221	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	36.90 (0.00) [0]
1222	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				
1223	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1224	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1225	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Coal</u>				
1226	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	3/2018 (-) [3/2019]	1,131.28 (-) [1,131.28]	572.40 (0.00) [12]
1227	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	3,072.20 (0.80) [0]
	<u>Health And Family Welfare</u>				
1228	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [4/2020]	785.00 (-) [785.00]	39.35 (0.00) [0]
1229	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [0/0]	268.84 (-) [268.84]	18.50 (0.00) [0]
	<u>Petroleum</u>				
1230	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	1.47 (0.00) [0]
1231	AURAIYA PHULPUR PIPELINE PROJECT	7/2015	12/2018 (-) [12/2018]	1,427.94 (-) [800.00]	577.39 (-627.94) [0]
1232	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	168.63 (0.00) [0]
1233	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	89.65 (0.00) [0]
1234	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.00 (0.00) [0]
1235	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [8/2021]	318.80 (-) [318.80]	0.00 (0.00) [0]
	<u>Power</u>				
1236	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (2/2018) [3/2019]	195.42 (294.60) [294.60]	195.00 (99.18) [61]

1237	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW)	7/2013	12/2016 (-) [0/0]	3,363.12 (-) [3,363.12]	2,244.00 (0.00) [0]
1238	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	12/2016 (-) [8/2019]	9,750.89 (-) [9,750.89]	8,554.00 (0.00) [32]
1239	TANDA TPP STAGE-II (2X660 MW)	9/2014	3/2019 (9/2019) [9/2019]	9,188.98 (-) [9,188.98]	5,071.82 (0.00) [6]
	<u>Railways</u>				
1240	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	4/1999	12/2009 (-) [0/0]	108.00 (-) [432.72]	446.52 (324.72) [0]
1241	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1242	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [600.00]	0.00 (0.00) [0]
1243	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	8/2018 (-) [8/2018]	199.75 (-) [270.00]	259.93 (70.25) [0]
1244	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1245	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	868.67 (0.00) [3]
1246	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	/ (-) [3/2018]	195.64 (-) [474.30]	443.26 (278.66) [0]
1247	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [3/2022]	602.50 (-) [714.34]	0.00 (111.84) [-]
1248	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1249	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1250	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [245.39]	210.67 (125.39) [0]
1251	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	4/2013	/ (-) [0/0]	654.00 (-) [654.00]	0.00 (0.00) [0]
1252	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1253	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	4/1997	4/1999 (-) [0/0]	233.00 (-) [318.42]	317.61 (85.42) [0]
1254	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [1/2022]	213.00 (-) [213.35]	0.00 (0.35) [69]
1255	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1256	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2021]	528.57 (-) [528.57]	0.59 (0.00) [24]

1257	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [977.00]	939.56 (49.99) [12]
1258	MANDHANA - BRAHMAWART NEW LINE PROJECT.	4/1997	4/1999 (-) [12/2018]	609.04 (1,063.00) [1,807.88]	1,793.99 (1,198.84) [236]
1259	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	668.70 (668.00) [668.00]	0.00 (-0.70) [0]
1260	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [3/2023]	1,765.92 (-) [1,765.92]	228.15 (0.00) [0]
1261	MEERUT-MUZAFARNAGAR PATCH DL	4/2012	/ (-) [0/0]	377.44 (-) [377.44]	182.85 (0.00) [0]
1262	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1263	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,345.00]	0.00 (2.00) [0]
1264	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [10/2022]	622.50 (427.00) [426.74]	5.83 (-195.76) [66]
1265	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	238.38 (0.00) [12]
1266	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,295.42]	81.15 (0.00) [0]
1267	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	3/2014 (-) [12/2019]	1,177.96 (-) [1,177.96]	0.00 (0.00) [69]
1268	UNCHAHAAR-AMETHI	4/2012	/ (-) [0/0]	380.00 (-) [380.00]	4.12 (0.00) [0]
1269	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	4/2006	3/2010 (-) [0/0]	369.90 (-) [1,581.53]	618.19 (1,211.63) [0]
1270	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [3/2022]	943.60 (-) [943.60]	102.17 (0.00) [0]
<u>Road Transport And Highways</u>					
1271	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	230.47 (0.00) [0]
1272	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1273	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	420.32 (0.00) [0]
1274	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	595.31 (0.00) [0]
1275	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [9/2018]	291.36 (-) [291.36]	414.14 (0.00) [56]
1276	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	189.14 (0.00) [0]

1277	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,310.42 (0.00) [7]
1278	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/	1,120.57	0.00
			(-) [0/0]	(-) [1,120.57]	(0.00) [0]
1279	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/	1,668.00	253.54
			(-) [2/2020]	(-) [1,668.00]	(0.00) [-]
1280	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016	611.65	660.22
			(-) [0/0]	(-) [611.65]	(0.00) [0]
1281	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/	1,408.00	0.00
			(-) [7/2020]	(-) [1,408.00]	(0.00) [-]
1282	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/	1,737.00	0.00
			(-) [4/2020]	(-) [1,737.00]	(0.00) [-]
1283	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/	1,404.50	193.08
			(-) [0/0]	(-) [1,404.50]	(0.00) [0]
1284	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019	1,587.49	110.58
			(-) [4/2019]	(-) [1,587.49]	(0.00) [0]
1285	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/	1,396.74	105.56
			(-) [0/0]	(-) [1,396.74]	(0.00) [0]
1286	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019	1,657.20	1,910.00
			(-) [1/2019]	(-) [1,657.20]	(0.00) [0]
1287	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020	2,064.99	738.75
			(-) [3/2020]	(-) [2,447.00]	(382.01) [0]
1288	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/	207.00	0.00
			(-) [0/0]	(-) [207.00]	(0.00) [0]
1289	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019	676.73	409.11
			(-) [4/2019]	(-) [676.73]	(0.00) [0]
1290	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	3/2018	774.57	0.00
			(-) [0/0]	(-) [774.57]	(0.00) [0]
1291	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	1/2014	10/2016	397.04	0.00
			(-) [0/0]	(-) [397.04]	(0.00) [0]
1292	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	10/2013	3/2017	317.76	15.47
			(-) [0/0]	(-) [317.76]	(0.00) [0]
1293	BAREILY-SITAPUR (NH-24)	3/2011	9/2013	1,046.00	805.19
			(-) [9/2018]	(-) [1,046.00]	(0.00) [60]
1294	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	/	629.74	0.00
			(-) [0/0]	(-) [629.74]	(0.00) [0]
1295	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/	972.77	0.00
			(-) [0/0]	(-) [972.77]	(0.00) [0]
1296	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/	534.55	170.92
			(-) [0/0]	(-) [534.55]	(0.00) [0]
1297	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING	12/2017	/	305.00	0.00

	FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O		(-) [0/0]	(-) [305.00]	(0.00) [0]
1298	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/	1,117.84	0.00
			(-) [0/0]	(-) [1,117.84]	(0.00) [0]
1299	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/	450.68	264.99
			(-) [0/0]	(-) [450.68]	(0.00) [0]
1300	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016	282.41	0.00
			(-) [0/0]	(-) [282.41]	(0.00) [0]
1301	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	1/2016	5/2019	701.12	841.92
			(-) [5/2019]	(-) [701.12]	(0.00) [0]
1302	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019	1,081.57	708.59
			(-) [6/2019]	(-) [1,081.57]	(0.00) [0]
1303	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/	1,232.21	498.25
			(-) [0/0]	(-) [1,232.21]	(0.00) [0]
1304	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020	1,989.00	0.00
			(-) [5/2020]	(-) [1,989.00]	(0.00) [2]
1305	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018	785.78	839.63
			(-) [0/0]	(-) [785.78]	(0.00) [0]
1306	ETAWAH CHAKERI	3/2013	9/2015	1,573.00	1,898.25
			(-) [0/0]	(-) [1,573.00]	(0.00) [0]
1307	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/	670.50	0.00
			(-) [0/0]	(-) [670.50]	(0.00) [0]
1308	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/	809.07	0.00
			(-) [0/0]	(-) [809.07]	(0.00) [0]
1309	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/	925.40	0.00
			(-) [0/0]	(-) [925.40]	(0.00) [0]
1310	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018	667.00	394.53
			(-) [0/0]	(-) [667.00]	(0.00) [0]
1311	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018	667.00	321.86
			(-) [0/0]	(-) [667.00]	(0.00) [0]
1312	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018	1,027.53	374.12
			(-) [0/0]	(-) [1,027.53]	(0.00) [0]
1313	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	281.19
			(-) [0/0]	(-) [815.28]	(0.00) [0]
1314	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017	261.09	240.96
			(-) [0/0]	(-) [261.09]	(0.00) [0]
1315	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020	1,373.28	0.00
			(-) [11/2020]	(-) [1,373.28]	(0.00) [8]
1316	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020	1,184.71	0.00
			(-) [3/2020]	(-) [1,310.00]	(125.29) [0]
1317	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM	3/2016	4/2019	899.00	301.30
			(-)	(-)	(0.00)

	42.791		[4/2019]	[899.00]	[0]
1318	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,948.72 (0.00) [0]
1319	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	10/2016 (-) [0/0]	283.45 (-) [283.45]	0.00 (0.00) [0]
1320	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	391.80 (0.00) [0]
1321	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [1,025.80]	0.00 (0.00) [0]
1322	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [1,115.28]	0.00 (0.00) [0]
1323	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [445.89]	0.00 (0.00) [0]
1324	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1325	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	3/2017 (-) [0/0]	493.94 (-) [493.94]	0.00 (0.00) [0]
1326	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	10/2016 (-) [0/0]	227.74 (-) [227.74]	0.00 (0.00) [0]
1327	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1328	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1329	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1330	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	0.00 (0.00) [0]
	<u>Steel</u>				
1331	FORGED WHEEL PLANT	4/2014	9/2018 (-) [1/2019]	1,682.85 (-) [1,682.85]	647.10 (0.00) [4]
	<u>Telecommunications</u>				
1332	UP (EAST) ACCESS LOT1	11/2017	8/2018 (10/2018) [10/2018]	169.45 (-) [169.45]	78.34 (0.00) [2]
	<u>Urban Development</u>				
1333	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	0.00 (0.00) [0]
1334	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Petroleum</u>				
1335	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [2/2020]	160.10 (-) [160.10]	24.22 (0.00) [0]
	<u>Power</u>				

1336	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.17 (274.07) [0]
1337	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	118.79 (0.00) [0]
1338	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (-) [3,846.30]	3,666.44 (867.82) [93]
1339	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (12/2020) [5/2021]	1,657.00 (2,978.86) [4,401.90]	2,611.13 (2,744.90) [63]
1340	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2021]	2,491.58 (-) [4,105.30]	1,468.26 (1,613.72) [102]
	Railways				
1341	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	38.33 (126.80) [0]
1342	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1343	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [12/2024]	16,216.00 (-) [16,216.00]	893.22 (0.00) [0]
	Road Transport And Highways				
1344	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	0.00 (0.00) [0]
1345	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	0.00 (0.00) [0]
1346	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [7/2018]	605.84 (-) [605.84]	722.46 (0.00) [0]
1347	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [0/0]	1,443.00 (-) [1,443.00]	22.50 (0.00) [0]
1348	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	0.00 (0.00) [0]
1349	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1350	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [10/2019]	720.00 (-) [720.00]	138.57 (0.00) [-]
1351	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [7/2019]	478.51 (-) [478.00]	409.17 (-0.51) [69]
1352	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	0.00 (0.00) [0]
1353	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [284.00]	0.00 (0.49) [0]
1354	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	0.00 (0.00) [0]
1355	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE	12/2017	12/2019 (-)	200.34 (-)	0.00 (0.00)

	WITH PAVED S		[12/2019]	[200.34]	[0]
1356	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [6/2019]	282.08 (-) [282.08]	0.00 (0.00) [0]
1357	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	0.00 (0.00) [0]
1358	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	0.00 (0.00) [0]
1359	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	0.00 (0.00) [0]
1360	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1361	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	0.00 (0.00) [0]
	<u>Urban Development</u>				
1362	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Coal</u>				
1363	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	296.10 (0.00) [0]
1364	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2019]	2,661.73 (-) [2,661.73]	0.00 (0.00) [0]
1365	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1366	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	376.04 (0.00) [24]
	<u>Health And Family Welfare</u>				
1367	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [9/2018]	244.00 (-) [244.00]	214.62 (0.00) [0]
1368	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [0/0]	168.90 (-) [191.38]	191.38 (22.48) [0]
1369	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [0/0]	651.99 (-) [651.99]	19.50 (0.00) [0]
1370	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2019]	355.15 (-) [355.15]	71.50 (0.00) [0]
	<u>Petroleum</u>				
1371	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,712.00]	0.98 (0.00) [-15]
1372	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [9/2019]	2,934.40 (-) [2,934.40]	711.29 (0.00) [0]
1373	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	3/2014	9/2017 (6/2018) [6/2018]	3,076.00 (4,190.00) [4,190.00]	3,209.47 (1,114.00) [0]
1374	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020	1,740.00	17.48

			(-) [12/2020]	(-) [1,740.00]	(0.00) [0]
1375	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1376	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (12/2018) [12/2018]	694.00 (1,097.54) [694.00]	470.83 (0.00) [2]
1377	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [4/2020]	163.02 (-) [163.02]	32.34 (0.00) [0]
	<u>Power</u>				
1378	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (-) [11/2019]	454.11 (-) [454.11]	238.92 (0.00) [19]
1379	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,381.84]	371.98 (0.00) [29]
	<u>Railways</u>				
1380	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	4/1999	12/2012 (-) [0/0]	207.52 (-) [334.87]	334.76 (127.35) [0]
1381	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (1,966.70) [2,373.00]	484.43 (1,345.60) [324]
1382	BANKURA DAMODAR VALLEY RIVER 96 KM WITH MM FOR EXTENSION OF NEW LINE FROM BOWAICHANDI KHANA 24.	4/1998	3/2022 (-) [3/2022]	1,027.40 (-) [2,373.00]	481.65 (1,345.60) [0]
1383	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [0/0]	501.78 (-) [1,960.06]	724.30 (1,458.28) [0]
1384	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [0/0]	255.64 (-) [272.20]	82.49 (16.56) [0]
1385	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/ (-) [0/0]	289.64 (-) [760.00]	0.13 (470.36) [0]
1386	BOWAICHANDI-ARAMBAGH	4/2010	/ (3/2025) [3/2025]	267.37 (-) [620.00]	40.77 (352.63) [-]
1387	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [0/0]	573.78 (-) [268.52]	0.67 (-305.26) [0]
1388	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	4/2009	2/2012 (-) [0/0]	259.51 (-) [673.85]	145.41 (414.34) [0]
1389	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [4,874.58]	1,881.65 (0.00) [0]
1390	GHUTIASHARIF-CANNING (ER)	4/2009	12/2011 (-) [0/0]	193.08 (-) [683.88]	148.63 (490.80) [0]
1391	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1392	MM FROM PANSKURA-GHATAL NL	4/2011	0/0 (3/2030) [3/2030]	276.69 (-) [426.00]	0.00 (149.31) [-]
1393	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [3/2020]	221.42 (-) [726.00]	97.55 (504.58) [-]

1394	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (274.41) [614.00]	267.93 (316.68) [12]
1395	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	283.55 (-) [451.00]	457.51 (167.45) [0]
1396	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2021]	602.27 (-) [612.00]	18.38 (9.73) [-9]
1397	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1398	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (4,200.00) [2,913.50]	764.97 (-0.01) [108]
1399	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1400	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	1,804.86 (307.50) [108]
1401	PANDABESWAR-CHINPAI DOUBLING (ER)	4/2004	12/2010 (-) [0/0]	293.74 (-) [229.33]	140.60 (-64.41) [0]
1402	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (12/2021) [12/2021]	1,013.45 (1,013.45) [1,428.00]	484.48 (414.55) [0]
1403	TAMLUK DIGHA,LINE DOUBLING (SER)	3/1984	6/2005 (-) [0/0]	293.97 (-) [749.69]	0.00 (455.72) [0]
1404	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2019]	614.25 (-) [2,532.49]	841.36 (1,918.24) [0]
1405	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,544.30 (2,355.23) [0]
<u>Road Transport And Highways</u>					
1406	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [5/2019]	1,083.00 (-) [1,083.00]	105.70 (0.00) [11]
1407	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [0/0]	998.79 (-) [998.79]	1,822.70 (0.00) [0]
1408	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [0/0]	1,078.84 (-) [1,078.84]	2,310.60 (0.00) [0]
1409	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,614.84 (0.00) [0]
1410	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [12/2019]	361.15 (-) [361.15]	0.00 (0.00) [-]
1411	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [6/2018]	158.65 (-) [158.65]	0.00 (0.00) [0]
1412	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [11/2018]	229.37 (-) [229.37]	6.39 (0.00) [0]
1413	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [8/2018]	767.03 (-) [767.03]	123.31 (0.00) [0]

1414	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [0/0]	702.16 (-) [702.16]	441.57 (0.00) [0]
1415	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1416	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1417	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [1,665.00]	1,836.44 (0.00) [0]
	<u>Urban Development</u>				
1418	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [1/2019]	156.57 (-) [156.57]	143.14 (0.00) [29]
1419	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1420	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	81.75 (0.00) [15]
	Total			18,05,667.72 (4,19,117.15) [21,63,672.09]	7,83,503.00 (3,58,004.37)

North East Project Detail's

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.09.2018)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
1	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019 (-) [12/2018]	247.52 (-) [247.52]	131.32 (0.00) [-2]
	<u>Power</u>				
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (3/2019) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,788.96 (3,683.06) [111]
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,295.43 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
6	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
7	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
9	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
10	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	38.50 (0.00) [0]
13	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
14	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]

15	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]
16	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
17	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/	264.16	0.00
			(-) [0/0]	(-) [264.16]	(0.00) [0]
18	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016	334.22	0.00
			(-) [0/0]	(-) [334.22]	(0.00) [0]
19	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	0.00
			(-) [0/0]	(-) [434.06]	(0.00) [0]
20	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	0.00
			(-) [0/0]	(-) [284.09]	(0.00) [0]
21	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	0.00
			(-) [0/0]	(-) [195.23]	(0.00) [0]
22	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	0.00
			(-) [0/0]	(-) [203.36]	(0.00) [0]
23	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	0.00
			(-) [0/0]	(-) [194.66]	(0.00) [0]
24	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	0.00
			(-) [0/0]	(-) [198.22]	(0.00) [0]
25	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012	207.03	0.00
			(-) [0/0]	(-) [207.03]	(0.00) [0]
26	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010	165.00	0.00
			(-) [0/0]	(-) [165.00]	(0.00) [0]
27	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017	180.57	0.00
			(-) [0/0]	(-) [180.57]	(0.00) [0]
28	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017	168.32	0.00
			(-) [0/0]	(-) [168.32]	(0.00) [0]
29	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012	156.63	132.21
			(-) [0/0]	(276.00) [276.00]	(119.37) [0]
30	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011	305.49	0.00
			(-) [0/0]	(-) [305.49]	(0.00) [0]
31	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010	104.00	0.00
			(-) [0/0]	(-) [201.00]	(97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	174.00
			(-) [5/2021]	(-) [875.00]	(0.00) [0]
33	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	113.50
			(-) [0/0]	(-) [175.57]	(0.00) [0]
	<u>Petroleum</u>				
34	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013	2,465.15	2,105.18

			(3/2019) [3/2019]	(-) [2,378.89]	(-86.26) [72]
35	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2022]	557.00 (-) [557.00]	64.70 (0.00) [24]
36	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	241.91 (0.00) [0]
37	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
38	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	40.04 (127.41) [70]
39	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	190.66 (0.00) [0]
40	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	1.65 (0.00) [0]
41	DIESEL HYDROTREATOR	7/2015	1/2018 (-) [0/0]	1,031.37 (-) [1,031.37]	305.91 (0.00) [0]
42	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,098.69 (0.00) [0]
43	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	98.07 (-5.15) [0]
44	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	961.00 (328.65) [0]
	<u>Power</u>				
45	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [10/2018]	4,375.35 (8,150.00) [8,150.00]	7,154.15 (3,774.65) [85]
	<u>Railways</u>				
46	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (-) [551.00]	595.01 (237.00) [12]
47	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [12/2022]	2,232.32 (-) [2,232.00]	193.12 (-0.32) [9]
48	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [12/2019]	3,230.02 (4,857.00) [5,820.00]	5,224.22 (2,589.98) [140]
49	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	163.08 (-49.96) [0]
50	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (-) [398.93]	264.69 (152.86) [0]
51	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	538.17 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
52	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
53	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.)	11/2010	2/2011 (-)	470.20 (-)	0.00 (0.00)

	BASKA BAR		[0/0]	[470.20]	[0]
54	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]
55	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
56	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
57	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
58	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2018]	289.99 (-) [289.99]	0.00 (0.00) [0]
59	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
60	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
61	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
62	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [0/0]	217.61 (-) [309.56]	389.08 (91.95) [0]
63	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [0/0]	160.00 (-) [160.00]	198.82 (0.00) [0]
64	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
65	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
66	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
67	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
68	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [361.00]	410.32 (81.00) [0]
69	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
70	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
71	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [385.13]	209.80 (185.32) [0]
72	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [118]
73	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	245.83 (0.00) [114]

74	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [0/0]	208.00 (-) [208.00]	297.81 (0.00) [0]
75	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [0/0]	225.00 (-) [225.00]	312.79 (0.00) [0]
76	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [11/2017]	245.00 (-) [245.00]	214.88 (0.00) [0]
77	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
78	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
79	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2022]	4,454.17 (-) [13,809.00]	7,919.05 (9,354.83) [132]
	<u>Urban Development</u>				
80	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (11/2018) [11/2019]	216.69 (216.69) [216.69]	52.00 (0.00) [56]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
81	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [8/2019]	363.99 (-) [363.99]	71.00 (0.00) [15]
	<u>Railways</u>				
82	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	259.43 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
83	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
84	JORBAT - BARAPANI	1/2011	1/2014 (-) [11/2018]	536.00 (-) [536.00]	674.52 (0.00) [58]
85	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [3/2019]	479.20 (-) [479.20]	6.14 (0.00) [10]
86	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	<u>Urban Development</u>				
87	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	<u>MIZORAM</u>				
	<u>Railways</u>				
88	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,600.00]	2,318.33 (2,206.53) [81]
	<u>Road Transport And Highways</u>				
89	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
90	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN	8/2010	10/2010 (-)	193.69 (-)	0.00 (0.00)

	MULTI MOD		[0/0]	[193.69]	[0]
91	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
92	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
93	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [12/2021]	2,326.52 (2,446.57) [3,000.00]	655.38 (673.48) [81]
	<u>Road Transport And Highways</u>				
94	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [9/2018]	239.30 (-) [239.30]	0.00 (0.00) [0]
95	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2018]	285.68 (-) [285.68]	0.00 (0.00) [0]
96	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [9/2018]	282.98 (-) [282.98]	0.00 (0.00) [0]
97	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2018]	387.00 (-) [387.00]	0.00 (0.00) [0]
98	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [9/2018]	500.09 (-) [500.09]	0.00 (0.00) [0]
99	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
100	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	339.57 (-) [339.57]	0.00 (0.00) [0]
101	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [9/2018]	315.03 (-) [315.03]	0.00 (0.00) [0]
102	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [9/2018]	240.64 (-) [240.64]	0.00 (0.00) [0]
103	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	215.12 (-) [215.12]	0.00 (0.00) [0]
104	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [9/2018]	215.79 (-) [215.79]	0.00 (0.00) [0]
105	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [9/2018]	272.89 (-) [272.89]	0.00 (0.00) [0]
106	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]
107	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [9/2018]	251.97 (-) [251.97]	0.00 (0.00) [0]
108	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [9/2018]	237.72 (-) [237.72]	0.00 (0.00) [0]
109	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]

110	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
111	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
112	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Civil Aviation</u>				
113	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	1/2009	1/2011 (-) [9/2018]	309.46 (-) [553.53]	546.69 (244.07) [92]
	<u>Railways</u>				
114	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	385.84 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
115	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
116	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
117	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
118	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
119	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [11/2017]	290.05 (-) [290.05]	18.12 (0.00) [0]
120	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
121	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [6/2018]	264.84 (-) [264.84]	0.00 (0.00) [0]
122	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
123	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
124	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (1,942.00) [3,374.00]	3,015.98 (2,232.00) [60]
125	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
126	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (4,118.00) [1,733.20]	1,543.99 (838.20) [0]
	<u>Road Transport And Highways</u>				
127	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM	10/2014	3/2018 (-)	369.00 (-)	36.90 (0.00)

	55.00 IN THE S		[0/0]	[369.00]	[0]
128	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	Urban Development				
129	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
130	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
131	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			82,239.65 (31,932.96) [1,32,401.03]	59,683.64 (50,161.38)
