


**294th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 Crores and above)
April, 2010**



Atomic Reactor

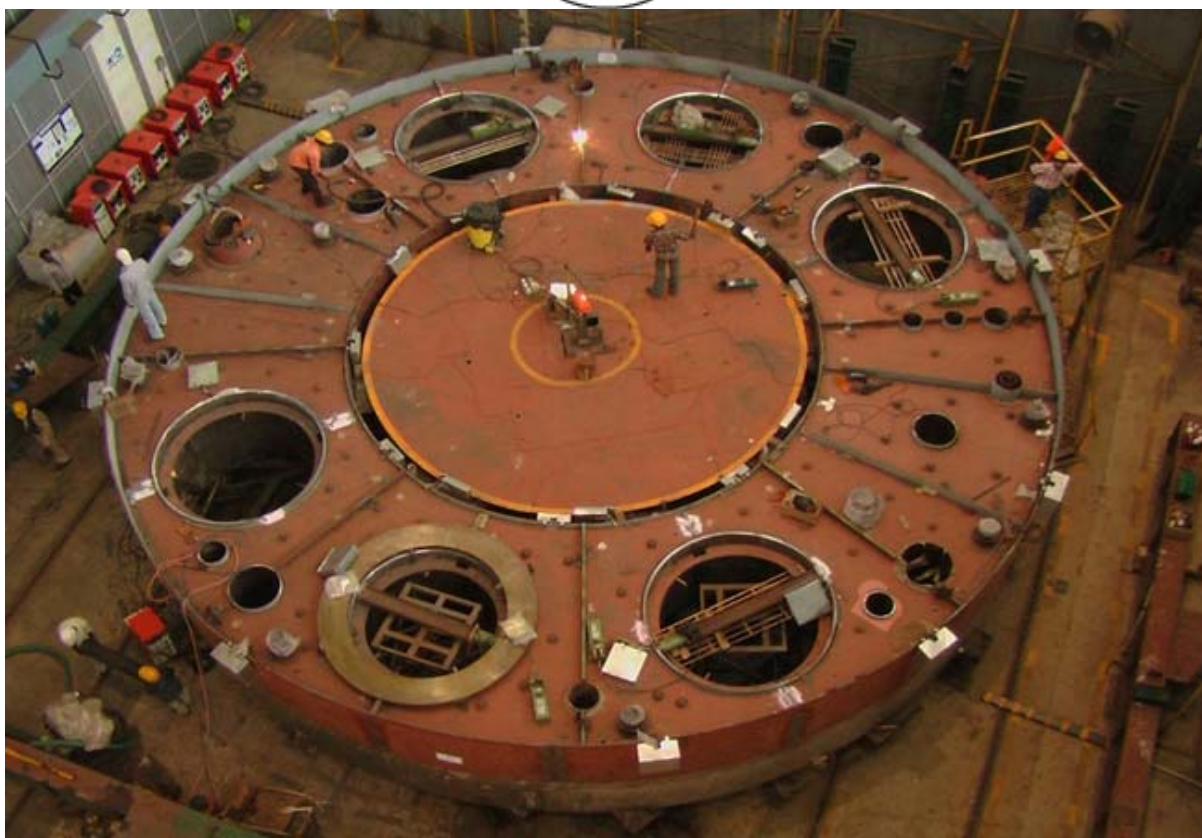

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Summary of Projects	6-15
Graph	16-25
Sector wise analysis of projects	26-51

EXECUTIVE SUMMARY

The 294th Flash Report for April' 2010, that contains information on the status of 578 projects in the Central Sector, each costing Rs. 150 Crores and above. First time, a report is prepared for the central sector projects costing Rs 150 Crores and above. During April' 2010, no project reported completion. However, 63 projects costing less than Rs 150 Crores have been dropped from the monitor of this Ministry. 22 new projects have been added during the month under reference. During April' 2010, two projects each from Steel and Shipping & Port Sectors have shown considerable improvement over the completion schedule reported earlier. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	135
2.	RAILWAYS	135
3.	POWER	85
4.	PETROLEUM	80
5.	COAL	38
6.	TELECOMMUNICATION	38
7.	STEEL	22
8.	SHIPPING & PORTS	22
9.	CIVIL AVIATION	8
10.	FERTILISERS	6
11.	ATOMIC ENERGY	4
12.	URBAN DEVELOPMENT	2
13.	MINES	1
14.	HEALTH & FW	1
15.	WATER RESOURCES	1
Total		578

2. Ninety one (91) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1 to 45 months in respect of projects relating to Atomic Energy, Civil Aviation, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports and Urban Development sectors.
3. In the **Atomic Energy sector**, Kaiga Units 3 and 4, Project (NPCIL) has shown additional delay of 4 months due to the continued problem of non availability of fuel. Kudankulam APP (NPCIL) has reported additional delay of 3 months due to slippage of commitment of M/s Atom Sroy Export (ASE), Russia.
4. In the **Civil Aviation Sector**, Construction of Integrated Passenger Terminal Building, NSCBI Airport, Kolkata has reported additional delays of 3 months due

to delay in shifting of effluent treatment plant (ETP) falling in the layout of Flyover and approach road.

5. In the **Coal sector**, 6 projects have reported additional delays in the range of 1-38 months. Barsingsar Lignite Mine, NLC, has reported additional delay of 3 months due to delay in preparation of tender documents and inadequate mobilization by the contractor. Block-B-OCP NCL (3.5 MTY) has reported additional delay of 12 months due to delay in supply of Hydraulic Shovel 9.5 m³-face, Hydraulic Shovel 9.5 m³ Backhoe and 160 mm Drill. Amlohri EPR (NCL) (6 MTY) has reported additional delay of 24 months due to delay in award of construction of combined Coal Handling Plant (CHP). Krishnashilla (NCL) (4MTY) has reported additional delay of 36 months due to delay in supply of 40 to 50 tonne hydraulic, cranes shovel 9.5 m³-Backhoe and 160 mm Drill. Jhanjra Longwall UG Phase II has reported additional delay of 38 months due to delay in tender process. Gevra Expansion OCP 25 MTY (SECL) has reported additional delay of 24 months, however, no specific reasons have been given by the project authority.
6. In the **Steel Sector**, 4 projects have reported additional delay in the range of 2-12 months while Power Plant-1 (Boiler-6) in Vishakhapatnam Steel Plant of RINL has reported improvement of 5 months over the completion schedule reported earlier. Expansion of Bokaro Steel Plant has reported additional delays of 2 months and no specific reason has been provided by the project authorities. Rebuilding of Coke Oven Battery No. 1 & 2, Expansion of Bhilai Steel Plant and Expansion of Rourkela Steel Plant have reported additional delay of 6 months, 6 months and 12 months respectively due to inadequate mobilization of resources by their contractors.
7. In the **Petroleum Sector**, 11 projects have reported additional delays in the range of 1-9 months. Development of B-193 Cluster Fields has reported additional delay of 1 month due to change in scope of work. Motor Spirit Quality (MSQ) Upgradation Project at Guwahati Refinery has reported additional delay of 1 month due to local constraints. Expansion of Panipat Refinery from 12 MMTPA to 15 MMTPA has suffered delay of 2 months due to shutdown of various units like Crude Distillation Unit(CDU),Vaccum Distillation Unit(VDU) and Delayed Cracker Unit (DCU). Additional Gas Processing Facility at Hazira has reported additional delay of 6 months due to late issue of Notice inviting tenders (NIT). Additional Gas processing units at (ONGC) Uran, Mumbai has reported additional delay of 9 months due to delay in tender process. MNW – NF Bridge Project at Hazira (ONGC) has reported additional delays of 7 months delayed due to adverse weather conditions. Installation of FCCV at Mumbai Refinery, MSQ Improvement project, Heera Reconstruction, Branch Pipeline from KSPL Viramgaon to Kandla and Development of C-Series Fields have reported additional delay of 6 months, 1 months, 5 months, 4 months and 5 months respectively, however, no specific reasons have been given by the concerned project authorities.
8. In the **Power Sector**, 16 projects have reported additional delay in the range of 3-21 months. SIPAT STPP Stage –I and Koldam HEP of (NTPC) have been delayed by a 2 months due to delay in commissioning of equipment. Farakka STPP Stage-III (NTPC) has reported additional delay of 3 months due to delay in erection schedule by M/s BHEL. Bongaigaon Thermal Power Project (NTPC) has reported additional delay of 3 months due to delay in slow progress by civil agency. Transmission system associated with Parbati HEP stage III, 543 CKM has reported additional delay of 7 months due to court cases. Chamara, Hydro Electric Project Stage III (NHPC) has reported additional delay of 4 months due to

violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. Nimoo Bazo Hydro Electric Project has reported additional delay of 4 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Western Region Transmission Strengthening Scheme has reported additional delay of 5 months to match with the linked generation project. Transmission System for Startup Power to DVC & Maithon RB Generation project (PGCIL) has report additional delay of 2 months due to delay in forest clearance. Parbati Hydro Electric Project Stage-III 4x130 MW (NHPC) has reported additional delay of 7 months due to delay in land acquisition for Sainj bypass and delay in award of E&M contract. BARH STPP, 3x660 MW has reported additional delay of 2 months due to delay in supply of material. MOUDA STPP (3x660 MW) of NTPC, Transmission system associated with Tuticorin JV TPS, and Koteswar HEP (THDC) have reported additional delay of 2 months, 19 months and 10 months, however, no specific reasons have been given by the concerned project authorities. Tehri Pumped Storage Plant has reported additional delay of 20 months due to delay in award of contract. Vishnugad-Pipalkoti Hydro Electric Project (THDCL) has reported additional delays of 21 months due to delay in acquisition of forest land.

9. In the **Road Transport and Highways Sector**, 26 projects have reported additional delay in the range of 1-24 months. However, the project authorities have not mentioned any specific reason for such delays.
10. In the **Railway Sector**, 7 projects have shown additional delays in the range of 3-45 months. Hajipur- Sugauli Via Vaishali New Line Project of ECR has reported additional delay of 45 months due to delay in land acquisition. Raichur- Guntakal of SCR has reported additional delay of 5 months due to delay in approval of Engineers Support Partnership (ESP) and land acquisition. Bardhaman-Katwa (GC), Bharuch – Samini- Dahej (GC), Rajatgarh- Barrang (LD), Sitamarhi- Raxaul-Narkataiganj (GC) and Conversion of 1500v DC Traction to 25 KV AC WR have reported additional delay of 3 months, 3 months, 9 months and 30 months respectively, however, no specific reasons have been given by the project authorities.
11. In the **Shipping & Ports Sector**, rail connectivity to ICTT at Vallarpadam project has shown considerable improvement over the completion schedule reported earlier.
12. In the **Urban Development Sector**, 2 Projects have reported additional delay of 1 – 6 months. Delhi MRTS Phase-II Project has reported additional delay of 1 month due to slow process of land acquisition. Bangalore Metro Rail Project has reported additional delays of 6 months but no specific reason has been reported by the concerned project authority.
13. Status as on 01.05.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the following tables.

(T.C.A. Anant)

Secretary to the Government of India
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	135	7
2	Road Transport & Highways	135	40
3	Power	85	16
4	Petroleum	80	11
5	Coal	38	6
6	Telecommunications	38	0
7	Steel	22	5
8	Shipping & Ports	22	1
9	Civil Aviation	8	1
10	Fertilisers	6	0
11	Atomic Energy	4	2
12	Urban Development	2	2
13	Mines	1	0
14	Health & Family Welfare	1	0
15	Water Resources	1	0
	Total	578	91


Summary of projects on the Flash Report for the month of April, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 100 Cr. & above) Previous Month	631
Number of Projects Completed/Dropped/Frozen Cost (Rs. 100 Cr. & above) in Previous Month	12
Number of Projects Dropped Cost (Less then Rs. 150 Cr.) in Current month	63
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	22
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	578

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 578 projects, 14 projects are ahead of schedule, 126 projects are on schedule and 268 projects are delayed. Of the balance, 124 projects do not have fixed dates of commissioning while 46 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

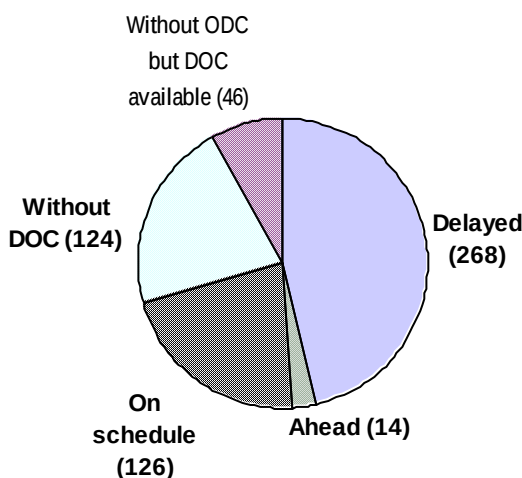

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 578 projects when sanctioned, was of the order of Rs. 610037.83 crore but this was subsequently revised to Rs. 671320.22 crore implying a cost overrun of 10.05%. The expenditure incurred on these projects till April, 2010 is Rs. 266362.34 crore, which is 39.68% of the revised cost of the projects.

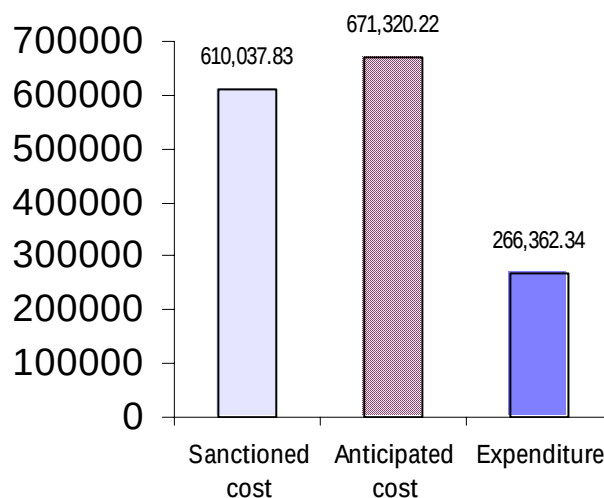

I. Project Added / Completed / Dropped / Frozen

No of Projects Cost (Rs. 100 Cr. & above) in Previous Month	631
No of Projects Completed/Dropped/Frozen Cost (Rs. 100 Cr. & above) in Previous Month	12
No of Projects Dropped Cost (Less then 150 Cr.) in Current Month	63
No of Projects Cost (Rs. 150 Cr. & above) added in Current Month	22
No of Projects Cost (Rs. 150 Cr. & above) in Current Month	578

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original	268	14	126	46	124	578	46.37
Latest Approved	323	20	132	42	64	578	55.88

III. (A) Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	487	534,342.09	578,001.93	221,450.63	38.30	43,659.84	8.20
Latest Approved	91	75,695.74	93,318.29	44,911.71	48.10	17,622.55	23.30
Total	578	610,037.83	671,320.22	266,362.34	39.68	61282.39	10.05

III. (B) Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	268	305,044.91	355,340.16	176,321.28	49.60	50,295.25	16.50
Latest Approved	323	50,564.09	377,407.03	194,336.23	51.50	326,842.94	646.40

IV. Additional Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Latest Approved	91	129,948.58	136,416.11	79,301.96	58.10	6,467.53	5.00
Total	91	129,948.58	136,416.11	79,301.96	58.13	6467.53	4.98

VI. List of projects added					
(Cost in Rs. crore)					
Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
Coal					
MANIKPUR OC EXPANTION	11/2009	321.42	3/2013	321.50	3/2014
Petroleum					
Additional Development of D-1 Field	1/2010	2,163.64	12/2011	2,163.64	12/2011
North Tapti Gas Field Development	1/2010	589.70	3/2011	755.56	3/2011
Construction of six Effluent Treatment Plants (ETP)	3/2009	234.78	9/2012	234.78	9/2012
Up-gradation of Konaban GGS and Pipeline Grid Project	7/2008	288.04	8/2012	288.04	8/2012
Power					
765KV System for central part of Northern Region Grid	11/2009	1,075.12	5/2012	1,075.12	5/2012
System Strengthening -XII of SR	2/2010	232.34	6/2012	232.34	6/2012
765KV System for Central part of Northern Region G	7/2009	1,736.36	6/2012	1,736.36	6/2012
Immsdiate evacuation system for NABINAGAR TPS	2/2010	215.86	6/2012	215.86	6/2012
Trans. System associated with PALLATANA GBPP & BPT	2/2010	2,144.00	12/2012	2,144.00	12/2012
Northern Region Transmission Strengthening Scheme	3/2012	965.58	11/2012	965.58	11/2012
Transm System for development of Pooling strn. in N	4/2010	4,404.57	1/2015	4,404.57	1/2015
System Strengthening -X of SR	12/2009	276.61	4/2012	276.61	4/2012
Transmission System of Vindhuachal -IV & Rihand -I	3/2010	4,672.99	11/2012	4,672.99	11/2012
MAUDA Transmission System	2/2010	469.38	10/2012	469.38	10/2012
System Strengthening in NR for SASAN & MUNDRA (UMPP)	12/2009	1,216.83	8/2012	1,216.83	8/2012
Fertilisers					
THAL AMMONIA REVAMP PROJECT	1/2009	488.75	3/2011	488.75	3/2011
PANIPATH - AMMONIA PLANT FEEDSTOCK PLANT	1/2010	1,292.84	10/2012	1,292.84	10/2012
CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ	9/2008	438.00	7/2011	438.00	7/2011
CAPACITY ENHANCEMENT OF VIJAIPUR-I	9/2008	325.00	7/2011	325.00	7/2011
BATHINDA - AMMONIA PLANT FEEDSTOCK PROJECT	1/2010	1,294.19	10/2012	1,294.19	10/2012
NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	1/2010	1,478.63	10/2012	1,478.63	10/2012

VII. Milestones (Cumulative due & achieved)

Total	1858
Achieved up to month	678

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL)	13,171.00	13,171.00	12/2008	03/2011	06/2011	3
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	03/2010	07/2010	4
<u>Civil Aviation</u>						
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	1,942.51	1,942.51	05/2011	05/2011	08/2011	3
<u>Coal</u>						
BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)	254.07	254.60	06/2009	02/2010	05/2010	3
BLOCK-B OCP NCL (3.5 MTY)	746.04	437.34	03/2012	03/2012	03/2013	12
GEVRA EXPANSION OCP (SECL) (25 MTY)	1,667.55	1,667.55	03/2010	03/2010	03/2012	24
AMLOHRI EPR (NCL) (6 MTY)	1,352.04	1,143.54	03/2014	03/2014	03/2016	24
KRISHNASHILA (NCL) (4MTY)	789.88	741.56	03/2010	03/2010	03/2013	36
JHANJRA LONGWAL UG PHASE II	287.18	287.17	11/2009	01/2012	03/2015	38
<u>Steel</u>						
POWER PLANT-I	462.00	350.00	12/2009	01/2011	08/2010	-5
EXPANSION OF BOKARO STEEL PLANT	3,316.00	3,534.00	N.A.	10/2011	12/2011	2
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	N.A.	10/2010	04/2011	6
EXPANSION OF BHILAI STEEL PLANT	5,185.00	6,146.00	N.A.	09/2012	03/2013	6
EXPENSION OF ROURKELA STEEL PLANT	6,133.00	8,128.00	02/2011	03/2012	03/2013	12
<u>Petroleum</u>						
LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI	638.90	1,030.00	04/2009	05/2010	06/2010	1
DEVELOPMENT OF B-193 CLUSTER FIELDS	3,248.78	5,633.44	03/2010	03/2012	04/2012	1
MSQ IMPROVMENT PROJECT	293.60	293.60	12/2009	06/2010	07/2010	1
EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA	1,007.83	1,060.00	12/2009	08/2010	10/2010	2
BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA	349.00	349.00	08/2011	08/2011	12/2011	4

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
DEVELOPMENT OF C-SERIES FIELDS	3,195.16	2,800.00	12/2008	05/2010	10/2010	5
HEERA RECONSTRUCTION	706.70	706.70	04/2010	04/2010	09/2010	5
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	06/2010	12/2010	6
ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA	370.11	370.11	04/2011	12/2011	06/2012	6
MNW-NF BRIDGE PROJECT	175.21	162.12	03/2009	05/2010	12/2010	7
ADDITIONAL GAS PROCESSING UNITS AT URAN	1,797.35	1,797.35	12/2011	12/2011	09/2012	9
Power						
SIPAT STPP STAGE - I (NTPC)	8,323.39	8,323.39	12/2009	10/2011	12/2011	2
BARH STPP(3X660MW) NTPC	8,692.97	8,692.97	11/2010	10/2013	12/2013	2
MOUDA STPP	5,459.28	6,010.89	02/2012	08/2012	10/2012	2
KOLDAM HEP (NTPC)	4,527.15	4,527.15	04/2009	12/2011	03/2012	3
CHAMERA, STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	08/2010	12/2010	4
NIMOO BAZGO HYDROELECTRIC PROJECT	611.01	611.02	08/2010	08/2010	12/2010	4
BONGAIGAON THERMAL POWER PROJECT	4,375.35	4,375.35	07/2011	11/2011	03/2012	4
WESTERN REGION STRENGTHENING SCHEME-II	5,221.23	5,221.23	07/2010	07/2010	12/2010	5
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G	290.49	290.49	04/2010	04/2010	09/2010	5
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	08/2010	02/2011	6
PARBATI H.E.P. STAGE -III (NHPC)	2,304.56	2,304.52	10/2010	11/2010	06/2011	7
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE	557.24	557.25	01/2010	11/2010	06/2011	7
KOTESHWAR HEP (THDC)	1,301.56	1,301.56	04/2005	12/2010	10/2011	10
TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS	353.57	353.57	07/2010	07/2010	02/2012	19
TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	1,657.60	07/2010	04/2013	12/2014	20
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	2,491.58	06/2013	06/2013	03/2015	21
Railways						
BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	200.80	200.80	N.A.	09/2010	12/2010	3
BARDHAMAN-KATWA (GC)	245.15	245.15	12/2010	12/2010	03/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
RAICHUR-GUNTAKAL(DL)(SCR)	136.62	221.90	12/2007	07/2010	12/2010	5
RAJATGARH-BARANG(LD),ECOR	166.16	243.40	N.A.	06/2010	12/2010	6
SITAMARHI-RAXAUL-NARKATIAGANJ (GC)	501.69	501.69	03/2010	06/2011	03/2012	9
CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	273.67	1,160.52	N.A.	06/2010	12/2012	30
HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	324.66	528.65	N.A.	06/2011	03/2015	45
Road Transport & Highways						
COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358	106.00	193.00	08/2006	04/2010	05/2010	1
PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57	276.00	276.00	04/2008	03/2010	04/2010	1
SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47	469.80	469.80	12/2008	03/2010	04/2010	1
SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI)	206.96	206.96	10/2008	03/2010	04/2010	1
NAGPUR-KONDHALI, NH-6(NHAI)	168.00	168.00	12/2008	04/2010	05/2010	1
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463	243.64	243.64	08/2009	04/2010	05/2010	1
PADALUR-TRICHY, NH-45	320.00	320.00	05/2009	03/2010	04/2010	1
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	03/2010	05/2010	2
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	263.00	263.00	02/2009	03/2010	05/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293	208.46	208.46	08/2009	04/2010	06/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418	205.92	205.92	08/2009	04/2010	06/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251	194.80	194.80	08/2009	04/2010	06/2010	2
MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7	360.42	360.42	11/2009	03/2010	05/2010	2
GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)	399.75	399.75	03/2005	03/2010	06/2010	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	227.00	227.00	10/2008	12/2010	03/2011	3
HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	280.00	280.00	02/2009	12/2010	03/2011	3
KOTA BYPASS,RJ-4, NH-76 (NHAI)	275.00	250.39	10/2008	06/2010	09/2010	3
SONAPUR TO GUWAHTI (AS-3)	245.00	245.00	03/2008	12/2010	03/2011	3
NALBARI TO BIJNI (AS-6)	225.00	225.00	06/2008	12/2010	03/2011	3
BANGALORE- NEELAMANGLALA NH-4	445.00	445.00	07/2010	03/2010	06/2010	3
ORAI TO JHANSI (UP-4),NH- 25, KM.170.0 TO KM.104.0	451.97	451.97	04/2008	06/2010	10/2010	4
MAIBANG TO LUNDING (AS- 27), KM.40.000 TO KM.60.500	200.00	200.00	04/2009	12/2010	04/2011	4
ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH)	295.00	295.00	08/2010	08/2010	12/2010	4
NALBARI TO BIJNI (AS-8)	200.00	200.00	06/2008	07/2010	01/2011	6
THRISSUR TO ANGAMALI (NH-47)	312.50	312.50	03/2009	06/2010	12/2010	6
DHARAMTUL TO SONAPUR,KM 205-183 (AS- 20)	160.00	160.00	05/2008	12/2010	06/2011	6
DELHI/ HARYANA BORDER TO ROHTAK	486.00	486.00	05/2010	05/2010	12/2010	7
SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	157.47	154.57	09/2007	06/2010	03/2011	9
DAKOBA TO NAGAON (NH- 36)(NHAI)	225.00	225.00	06/2008	12/2010	10/2011	10
BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	195.00	195.00	06/2008	12/2010	12/2011	12
BIJNI TO ASSAM /WB.BORDER (NH- 31.C)(2)(NHAI)	237.80	237.80	06/2008	12/2010	12/2011	12
NAGAON TO DHARAMTUL (AS-2)	264.72	264.72	06/2008	12/2010	12/2011	12
NALBARI T BIJNI (AS-7)	208.00	208.00	04/2008	12/2010	12/2011	12
DHARAMTUL TO SONAPUR (AS-19)	200.00	200.00	06/2008	12/2010	12/2011	12
GUWHATI TO NALBARI (AS- 4)	175.96	175.96	04/2008	12/2010	03/2012	15
GUWAHATI TO NALBARI (AS-5)	198.16	198.16	04/2008	12/2010	03/2012	15
CHAMBAL BRIDGE, NH-76 (RJ-5)	275.00	281.31	02/2010	12/2010	03/2012	15
HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54	212.00	212.00	09/2007	12/2010	12/2012	24

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
HARANGAJO TO MAIBANG, NH-54	196.00	196.00	07/2009	12/2010	12/2012	24
BRAHMPUTRA BRIDGE,NH NO-31	217.61	217.61	04/2010	12/2010	12/2012	24
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	11/2010	03/2010	-8
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT	8,118.00	8,676.00	06/2010	10/2010	11/2010	1
BANGALORE METRO RAIL PROJECT	6,395.00	6,395.00	12/2011	12/2011	06/2012	6
Number of projects reporting additional delay = 91						

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	23,236.29
Civil Aviation	8	5,142.67	5,081.67	5,142.67
Coal	38	24,083.43	25,126.65	26,097.33
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,091.51	4,091.51
Steel	22	44,741.86	44,741.86	52,147.80
Petroleum	80	156,343.74	159,491.05	175,218.57
Power	85	179,619.98	181,434.06	184,589.75
Health & Family Welfare	1	71.18	422.60	443.15
Railways	135	51,007.64	62,798.24	95,575.86
Road Transport & Highways	135	41,863.55	41,863.55	42,136.98
Shipping & Ports	22	24,047.63	24,047.63	24,630.99
Telecommunications	38	16,511.58	16,333.05	16,433.91
Urban Development	2	14,513.00	16,763.36	15,071.00
Water Resources	1	542.90	542.90	1,187.00
Grand total	578	589,880.37	610,037.83	671,320.22


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

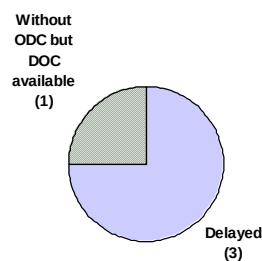

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 18410.25 Crores.

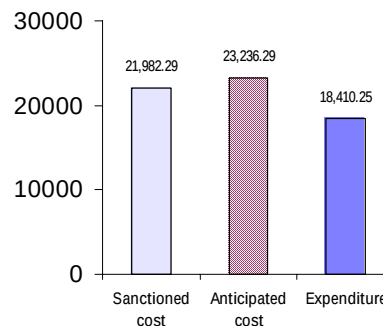


2. Sector: - Civil Aviation

Number of Projects	8
Number of Projects on schedule	3
Number of Projects Delayed	2
Number of Projects Wo_Doc_Original	2
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 3 projects are on schedule, 2 projects are delayed and 2 projects are original date of commissioning and 1 projects are Wo_Odc_original.

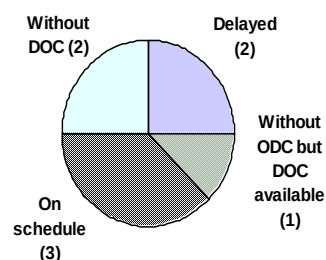

Investment Scenario

The total cost of implementation of 8 projects when sanctioned, was of the order of Rs. 5142.67 Crores but this was subsequently revised to Rs. 5142.67 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs 1688.49 Crores.

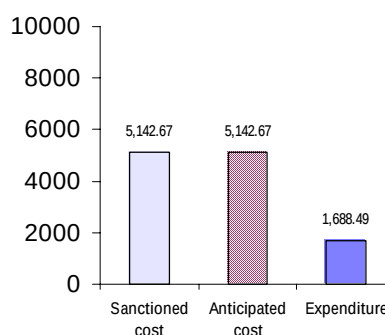


3. Sector: - Coal

Number of Projects	38
Number of Projects on schedule	12
Number of Projects Delayed	22
Number of Projects Ahead	3
Number of Projects Wo_ODC_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 38 projects, 12 projects are on schedule, 22 projects are delayed and 3 projects are ahead and 1 Project W_Odc_Original .

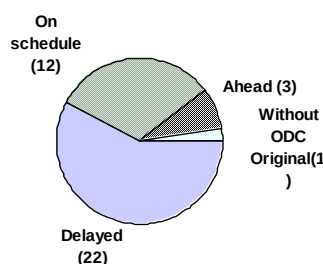

Investment Scenario

The total cost of implementation of 42 projects when sanctioned, was of the order of Rs. 24082.43 Crores but this was subsequently revised to Rs. 26097.33 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 8897.62 Crores

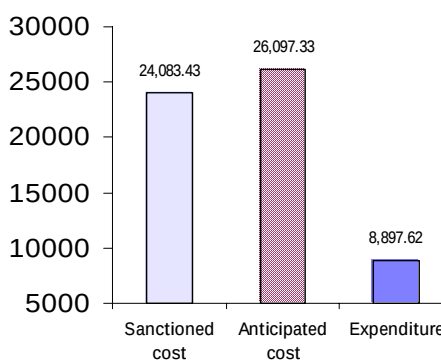


4. Sector: - Petroleum

Number of Projects	80
Number of Projects on schedule	31
Number of Projects Delayed	39
Number of Projects Ahead	5
Number of Projects Wo_Doc_Original	2
Number of Projects Without original date of commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 80 projects, 31 projects are on schedule, 39 projects are delayed and 5 projects are ahead and 2 projects are without date of commissioning and 3 Project is Without original date of commissioning.

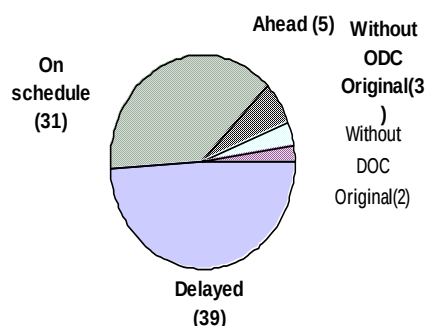

Investment Scenario

The total cost of implementation of 82 projects when sanctioned, was of the order of Rs. 156343.74 Crores but this was subsequently revised to Rs. 175218.57 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 52524.63 Crores.

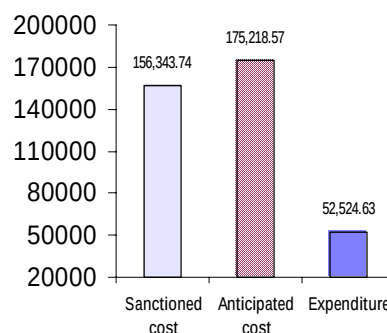


5. Sector: - Power


Number of Projects	85
Number of Projects on schedule	49
Number of Projects Delayed	34
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 85 projects, 49 projects are on schedule, 34 projects are delayed, 1 projects is without date of commissioning and 1 projects is with out original date of commissioning

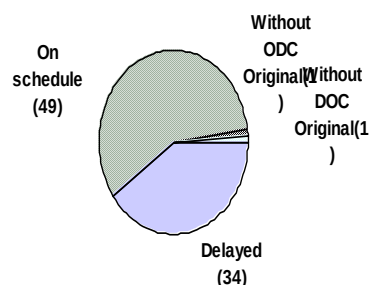

Investment Scenario

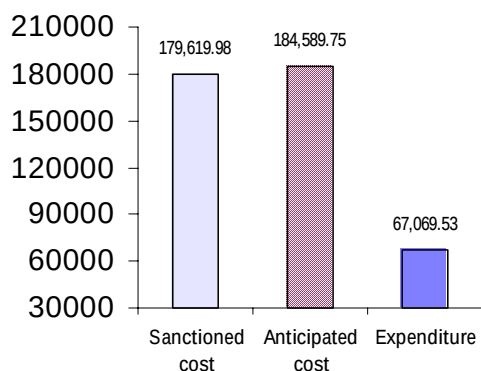


The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 179619.98 Crores but this was subsequently revised to Rs. 184589.75 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 67069.53 Crores.

6. Sector: - Railways

Number of Projects	135
Number of Projects on schedule	7
Number of Projects Delayed	36
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	51
Number of Projects Wo_Odc_Original	39


Brief Analysis

Project Status with out respect Original Schedule: Out of 135 projects, 7 projects are on schedule, 36 projects are delayed, 2 projects is ahead. 51 projects are Without date of commissioning and 39 projects are without original date of commissioning.

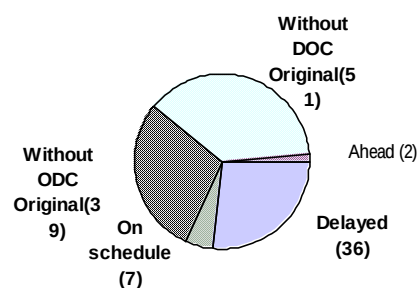

Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs. 51007.64 Crores but this was subsequently revised to Rs. 95575.86 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 32701.31 Crores.

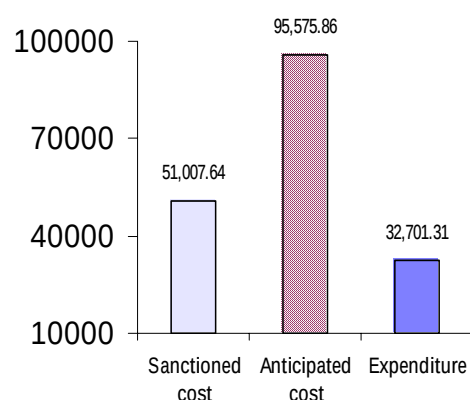


7. Sector: - Road Transport and Highways

Number of Projects	135
Number of Projects on schedule	10
Number of Projects Delayed	118
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 135 projects, 10 projects are on schedule, 118 projects are delayed, 2 projects are ahead and 5 projects is with out date of commissioning .

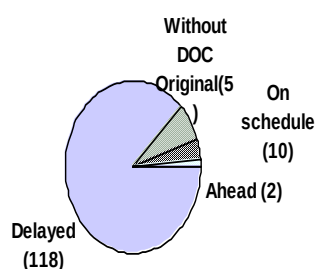

Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs 41863.55 Crores but this was subsequently revised to Rs. 42136.98 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 36235.78 Crores.

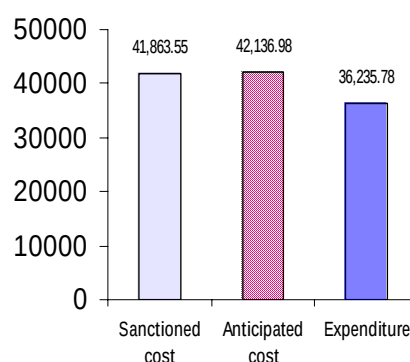


8. Sector: - Shipping and Ports

Number of Projects	22
Number of Projects on schedule	9
Number of Projects Delayed	8
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 9 projects are on schedule, 8 projects are delayed, 2 projects are ahead and 3 projects are without date of commissioning.



Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.24047.63 Crores but this was subsequently revised to Rs. 24630.99 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 4769.62 Crores.

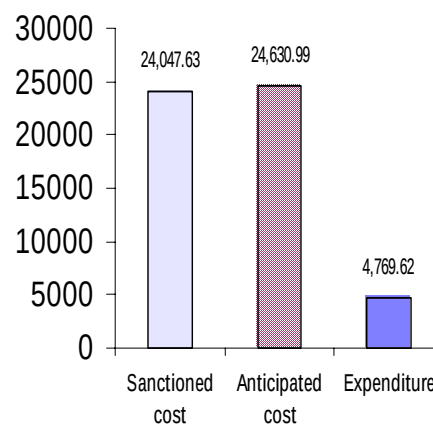


9. Sector: - Steel

Number of Projects	22
Number of Projects on schedule	1
Number of Projects Delayed	11
Number of Projects Wo_Odc_Original	10


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 1 projects are on schedule, 11 projects are delayed and 10 projects are Wo_Odc_Original.

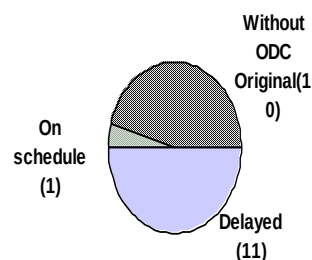

Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs.44741.86 Crores but this was subsequently revised to Rs. 52147.80 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs. 19762.23 Crores.

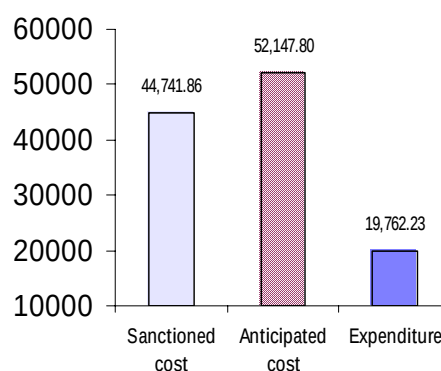


10. Sector: - Telecommunications

Number of Projects	38
Number of Projects Delayed	24
Number of Projects Wo_Doc_Original	14


Brief Analysis

Project Status with respect to Original Schedule: Out of 38 projects, 24 projects are delayed and 14 projects are with our date of commissioning.

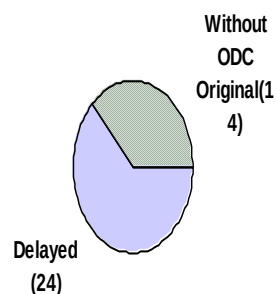

Investment Scenario

The total cost of implementation of 38 projects when sanctioned, was of the order of Rs 16511.58 Crores but this was subsequently revised to Rs. 16433.91 Crores. The expenditure incurred on these projects till Apr, 2010 is Rs 4469.52 Crores.

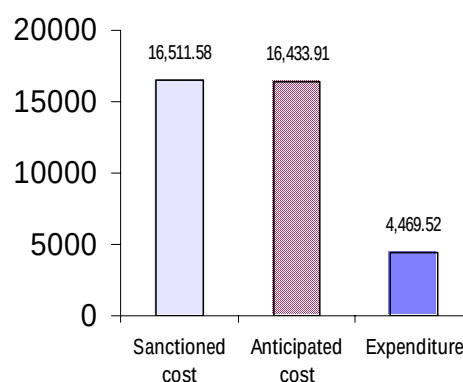

(Apr,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,531.00	10/2009 09/2007	07/2010	34(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	486.37	-	04/2011	-	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,977.00	12/2008	06/2011	30(O)	99/119
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,415.88	09/2010	09/2011	12(O)	8/80
Total			21,982.29	23,236.29	18,410.25				178/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	239.59	-	06/2010	-	1/24
6	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
7	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]	06/2009	213.35	213.35	112.00	09/2010	11/2010	2(O)	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]	08/2008	1,273.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
9	Extension of Secondary Runway(K2) - [N04000056]	08/2008	230.00	230.00	188.12	01/2011	01/2011	0(O)	0/0
10	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	579.26	05/2011	08/2011	3(O)	0/0
11	C/o new Airport-SH: E/W in cutting and filling geogrid - [N04000050]	01/2009	264.29	264.29	10.02	01/2011	-	-	0/0
12	GAGAN PROJECT - [N04000065]	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
Total			5,142.67	5,142.67	1,688.49				1/24
<u>Coal</u>									
13	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	473.97	03/2009	03/2010	12(O)	0/0
14	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07	254.60	215.84	06/2009	05/2010	11(O)	18/21
15	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,420.58	06/2009	09/2010	15(O)	32/26
16	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,958.95	06/2009	06/2011	24(O)	24/24
17	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	57.90	03/2010	03/2012	24(O)	0/4
18	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	993.52	03/2010	03/2012	24(O)	3/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66 341.63	341.63	101.57	03/2011 -	03/2012	12(O)	0/0
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	249.03	37.11	03/2012 -	03/2012	0(O)	0/36
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40 -	259.40	0.40	03/2012 -	03/2012	0(O)	0/0
22	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28 -	207.28	249.85	03/2012 -	03/2012	0(O)	0/0
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.57 -	418.57	37.00	03/2012 -	03/2012	0(O)	0/0
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]	03/2010	181.91 -	181.19	-	03/2012 -	03/2012	0(O)	0/0
25	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54 -	4,904.54	749.53	08/2012 -	08/2012	0(O)	0/0
26	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34 779.26	779.26	97.74	03/2013 -	09/2012	-6(O)	2/11
27	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63 -	453.63	47.19	- -	12/2012	-	0/50
28	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88 741.56	741.56	134.93	03/2010 -	03/2013	36(O)	0/1
29	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65 -	1,188.31	583.32	03/2011 03/2013	03/2013	0(R3)	0/4
30	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04 437.34	437.34	136.00	03/2012 -	03/2013	12(O)	0/1
31	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	706.40	12.15	07/2012 -	03/2013	8(O)	0/1
32	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78 -	467.78	11.29	03/2013 -	03/2013	0(O)	0/7
33	KANIHA OCP - [N06000035]	12/2007	457.77 -	457.77	48.96	03/2012 -	03/2013	12(O)	0/0
34	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93 -	479.53	175.35	03/2013 -	03/2013	0(O)	0/0
35	BINA EXTN. PROJ - [N06000019]	11/2006	168.97 -	168.97	-	03/2014 -	11/2013	-4(O)	1/1
36	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53 -	1,943.66	789.00	03/2010 -	03/2014	48(O)	2/6
37	CHURCHA UG - [N06000046]	06/2008	462.35 -	462.35	270.87	06/2014 -	03/2014	-3(O)	0/0
38	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08 -	153.82	3.14	03/2010 -	03/2014	48(O)	0/0
39	PENGANGA OC - [N06000066]	10/2008	339.77 -	339.77	-	03/2014 -	03/2014	0(O)	0/0
40	KARTALI (EAST) OC - [N06000076]	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/0
41	MANIKPUR OC EXPANTION - [N06000081]	11/2009	321.42 -	321.50	206.71	03/2013 -	03/2014	12(O)	0/0
42	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18 -	287.17	-	11/2009 01/2012	03/2015	38(R3)	0/0
43	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87 -	395.87	22.73	03/2013 -	03/2015	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
44	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
45	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
46	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
47	RKP OCP PHASE-I - [N06000079]	03/2010	201.58	209.78	0.18	03/2015	03/2015	0(O)	0/0
48	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04 1,143.54	1,143.54	-	03/2014	03/2016	24(O)	1/1
49	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	56.52	03/2014	03/2016	24(O)	0/0
50	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	12(O)	0/0
Total			24,083.43	26,097.33	8,897.62				83/201
<u>Fertilisers</u>									
51	THAL AMMONIA REVAMP PROJECT - [N08000003]	01/2009	488.75	488.75	17.28	03/2011	03/2011	0(O)	0/0
52	CAPACITY ENHANCEMENT OF VIJAIPUR-I - [N08000007]	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
53	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
54	PANIPATH - AMMONIA PLANT FEEDSTOCK PLANT - [N08000004]	01/2010	1,292.84	1,292.84	-	10/2012	10/2012	0(O)	0/0
55	BATHINDA - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000005]	01/2010	1,294.19	1,294.19	-	10/2012	10/2012	0(O)	0/0
56	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]	01/2010	1,478.63	1,478.63	-	10/2012	10/2012	0(O)	0/0
Total			5,317.41	5,317.41	17.28				0/0
<u>Mines</u>									
57	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
<u>Steel</u>									
58	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	164.48	08/2009	02/2010	6(O)	0/0
59	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	103.09	-	03/2010	-	0/0
60	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	527.00	-	04/2010	-	1/1
61	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	244.28	-	06/2010	-	0/1
62	BILADILLA IRON ORE DEPOSITE-11B - [N12000017]	01/2009	295.89	295.89	213.74	10/2009	06/2010	8(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
63	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	213.89	10/2009	06/2010	8(O)	2/21
64	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,031.35	-	06/2010	-	1/6
65	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	74.27	-	06/2010	-	0/1
66	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	42.02	06/2010	06/2010	0(O)	0/0
67	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	227.50	06/2009	07/2010	13(O)	0/0
68	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	84.40	12/2009	08/2010	8(O)	0/0
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	80.00	02/2010	08/2010	6(O)	0/0
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
71	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	165.99	-	04/2011	-	0/2
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	111.28	232.93	50.18	-	05/2011	-	0/1
73	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	6,203.00	10/2009	06/2011	20(O)	0/126
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
75	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	6,545.80	-	06/2011	-	0/6
76	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,534.00	932.87	-	12/2011	-	0/7
78	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	8,128.00	1,253.17	02/2011	03/2013	25(O)	0/0
79	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	6,146.00	1,474.84	-	03/2013	-	0/8
Total			44,741.86	52,147.80	19,762.23				4/180
Petroleum									
80	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	29/45
81	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.00	09/2009	12/2009	3(O)	0/0
82	MSQ UPGRADEATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	750.71	12/2009	01/2010	1(O)	0/0
83	SHORT TERM LOW COST MUMBAI REFINERY - [N16000082]	12/2006	390.00	230.00	164.51	01/2010	01/2010	0(O)	0/0
84	INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	186.58	12/2009	02/2010	2(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
85	CHAINSA-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77 -	565.00	382.13	09/2009 -	03/2010	6(O)	0/0
86	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13 -	396.13	52.34	10/2009 -	03/2010	5(O)	0/0
87	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71 639.11	639.11	520.92	12/2009 -	03/2010	3(O)	0/0
88	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82 -	405.82	277.56	12/2009 -	03/2010	3(O)	0/0
89	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31 -	3,860.00	3,114.04	11/2009 04/2010	04/2010	0(R3)	0/0
90	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	14,439.00 -	14,439.00	11,422.39	11/2009 11/2009	05/2010	6(R1)	61/101
91	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 350.00	389.00	347.92	06/2008 -	05/2010	23(O)	0/0
92	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60 -	289.60	198.16	05/2010 -	05/2010	0(O)	0/0
93	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46 -	643.46	425.28	- -	05/2010	-	0/2
94	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00 2,869.00	3,127.00	2,600.02	04/2009 12/2009	06/2010	6(R1)	31/36
95	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]	06/2006	1,431.91 -	1,675.72	1,359.95	09/2009 -	06/2010	9(O)	0/0
96	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30 -	2,305.30	1,966.04	06/2010 06/2010	06/2010	0(R1)	0/0
97	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90 1,030.00	1,030.00	673.52	04/2009 -	06/2010	14(O)	0/0
98	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00 -	325.00	195.40	02/2010 -	06/2010	4(O)	0/0
99	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00 -	300.00	179.95	02/2010 -	06/2010	4(O)	0/0
100	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00 -	1,492.00	840.77	04/2010 -	06/2010	2(O)	0/0
101	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92 -	1,493.49	651.43	06/2006 05/2008	07/2010	26(R1)	0/2
102	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60 -	293.60	161.38	12/2009 -	07/2010	7(O)	0/0
103	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80 3,941.41	3,941.41	-	12/2009 -	07/2010	7(O)	0/0
104	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00 -	6,898.00	5,182.82	01/2010 -	08/2010	7(O)	0/0
105	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70 -	706.70	218.16	04/2010 -	09/2010	5(O)	0/0
106	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]	06/2005	1,007.83 1,007.83	1,060.00	666.35	12/2009 12/2009	10/2010	10(R1)	18/49
107	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	2,800.00	2,448.39	12/2008 -	10/2010	22(O)	0/0
108	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07 -	1,816.07	8.66	10/2010 -	10/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
109	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	1.13	10/2010	10/2010	0(O)	0/0
110	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38	3,000.00	176.96	10/2010	10/2010	0(O)	0/0
111	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00	1,212.85	18.46	10/2011	10/2010	-12(O)	0/0
112	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009	12/2010	21(O)	0/0
113	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	577.01	09/2009	12/2010	15(O)	0/0
114	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00	224.00	68.02	12/2010	12/2010	0(O)	0/0
115	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40	605.40	183.47	12/2010	12/2010	0(R3)	12/17
116	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40	304.40	32.06	12/2010	12/2010	0(O)	0/0
117	CAPACITY AUGMENTATION OF AGRA& FERAZABAD REGION - [N16000074]	07/2009	199.57	199.57	-	01/2011	01/2011	0(O)	0/0
118	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	600.00	523.08	03/2007	03/2011	48(O)	3/3
119	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	1,200.00	988.06	03/2007	03/2011	48(O)	6/6
120	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90	219.22	145.95	03/2006	03/2011	60(O)	6/6
121	NORTH TAPTI GAS FIELD DEV. - [N16000085]	07/2008	589.70	589.70	-	03/2011	03/2011	0(O)	0/0
122	North Tapti Gas Field Development - [N16000096]	01/2010	589.70	755.56	-	03/2011	03/2011	0(O)	0/0
123	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75	8,061.42	3,898.92	06/2009	04/2011	22(O)	0/0
124	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93	1,061.78	9.91	11/2011	04/2011	-7(O)	0/0
125	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	41.56	04/2011	04/2011	0(O)	0/0
126	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,234.69	03/2005	05/2011	74(O)	0/0
127	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	330.40	0.35	05/2010	05/2011	12(O)	0/0
128	BNPL superlines(Uttranchal & Punjab) - [N16000091]	12/2009	540.92	540.92	-	05/2011	05/2011	0(O)	0/0
129	VKPL Upgradation and Laying of Superlines - [N16000092]	12/2009	463.32	463.32	-	05/2011	05/2011	0(O)	0/0
130	VKPL SPURLINE - [N16000093]	12/2009	463.32	463.32	-	06/2011	05/2011	-1(O)	0/0
131	BNPL SPURLINE - [N16000094]	12/2009	540.92	540.92	-	06/2011	05/2011	-1(O)	0/0
132	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	267.00	63.58	-	08/2011	-	0/1
133	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	53.67	09/2011	09/2011	0(O)	0/0
134	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	47.31	09/2011	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
135	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00 -	820.00	577.01	12/2011 -	12/2011	0(O)	0/0
136	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00 -	349.00	8.09	08/2011 -	12/2011	4(O)	0/0
137	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00 -	825.00	48.11	12/2011 -	12/2011	0(O)	0/0
138	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	06/2007	736.65 -	736.65	108.05	12/2011 -	12/2011	0(O)	0/0
139	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,163.64	-	12/2011 -	12/2011	0(O)	0/0
140	Additional Development of D-1 Field - [N16000097]	01/2010	2,163.64 -	2,163.64	-	12/2011 -	12/2011	0(O)	0/0
141	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT. - [N16000070]	07/2009	238.68 -	238.68	-	01/2012 -	01/2012	0(O)	0/0
142	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02 -	740.02	298.68	03/2010 03/2012	03/2012	0(R1)	0/0
143	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]	12/2009	1,492.33 -	1,492.33	18.75	06/2012 -	03/2012	-3(O)	0/0
144	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63 -	2,920.82	5.24	02/2009 09/2010	04/2012	19(R1)	0/0
145	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	0.61	03/2010 08/2010	04/2012	20(R1)	0/0
146	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29 -	6,326.40	599.85	05/2010 -	05/2012	24(O)	0/0
147	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21 -	1,436.21	-	07/2010 -	05/2012	22(O)	0/0
148	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11 -	370.11	8.53	04/2011 -	06/2012	14(O)	0/0
149	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]	07/2008	288.04 -	288.04	-	08/2012 -	08/2012	0(O)	0/0
150	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93 -	6,855.93	478.71	09/2012 -	09/2012	0(O)	0/0
151	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35 -	1,797.35	9.77	12/2011 -	09/2012	9(O)	0/0
152	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]	08/2009	1,793.00 -	1,793.00	7.12	09/2012 -	09/2012	0(O)	0/0
153	Construction of six Effluent Treatment Plants (ETP) - [N16000099]	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
154	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	29,777.00	3,239.47	03/2012 -	11/2012	8(O)	0/0
155	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00 -	3,032.00	-	12/2012 -	12/2012	0(O)	0/0
156	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43 -	4,543.43	-	12/2012 -	12/2012	0(O)	0/0
157	De-bottlenecking of SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1.00	- -	12/2012	-	0/0
158	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18 -	7,596.18	-	01/2013 -	01/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
159	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15 -	2,378.86	109.52	03/2013 -	03/2013	0(O)	0/0
	Total		156,343.74 -	175,218.57	52,524.63				166/268
Power									
160	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72 -	877.06	230.56	07/2006 -	03/2010	44(O)	2/5
161	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46 -	1,016.74	-	09/2007 -	05/2010	32(O)	8/36
162	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	756.41	12/2007 -	06/2010	30(O)	7/18
163	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	113.89	06/2010 -	06/2010	0(O)	0/0
164	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34 -	241.27	141.60	06/2008 -	08/2010	26(O)	8/20
165	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,962.37	02/2010 -	08/2010	6(O)	5/24
166	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]	06/2006	803.70 -	803.76	593.27	06/2009 -	09/2010	15(O)	1/20
167	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	279.24	09/2010 -	09/2010	0(O)	0/0
168	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	262.48	04/2010 -	09/2010	5(O)	0/0
169	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	135.08	09/2010 -	09/2010	0(O)	0/0
170	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	3,964.82	10/2010 -	10/2010	0(O)	11/40
171	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72 -	340.72	128.28	11/2010 -	11/2010	0(O)	0/0
172	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55 -	261.55	127.74	11/2010 -	11/2010	0(O)	0/0
173	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63 -	1,405.63	1,185.27	08/2010 -	12/2010	4(O)	0/0
174	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.G.R.) - [180100260]	12/2005	3,779.46 -	3,779.46	3,360.62	09/2009 -	12/2010	15(O)	15/30
175	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96 -	975.96	590.08	10/2009 -	12/2010	14(O)	2/20
176	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	611.02	452.20	08/2010 -	12/2010	4(O)	0/0
177	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23 -	5,221.23	2,307.00	07/2010 -	12/2010	5(O)	3/20
178	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76 -	417.76	254.31	12/2010 -	12/2010	0(O)	0/0
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36 -	408.36	284.85	12/2010 -	12/2010	0(O)	0/0
180	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89 -	230.89	27.61	01/2011 -	01/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
181	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	1,279.40	1,119.02	03/2007	02/2011	47(O)	1/25
182	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	1,108.36	11/2009	02/2011	15(O)	0/0
183	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	621.28	424.52	02/2011	02/2011	0(O)	0/1
184	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44	2,570.44	1,719.47	08/2010	02/2011	6(O)	13/26
185	URI-II - [N18000023]	10/2006	238.25	238.25	180.02	-	05/2011	-	0/0
186	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	2,981.71	05/2011	05/2011	0(O)	0/0
187	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	1,018.46	10/2010	06/2011	8(O)	0/0
188	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.25	340.11	01/2010	06/2011	17(O)	0/22
189	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	73.43	06/2011	06/2011	0(O)	0/0
190	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	103.45	06/2011	06/2011	0(O)	0/0
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	327.70	07/2011	07/2011	0(O)	0/0
192	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	184.39	07/2011	07/2011	0(O)	0/0
193	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	15.24	07/2011	07/2011	0(O)	0/0
194	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,307.03	719.10	09/2009	08/2011	23(O)	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	56.59	08/2011	08/2011	0(O)	0/0
196	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	1,896.65	1,566.40	11/2008	09/2011	34(O)	25/38
197	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	105.03	09/2011	09/2011	0(O)	0/0
198	KOTESHWAR HEP(THDC) - [180100184]	04/2000	1,301.56	1,301.56	1,811.87	04/2005	10/2011	78(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	161.39	11/2011	11/2011	0(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	57.33	11/2011	11/2011	0(O)	0/0
201	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	13.02	11/2011	11/2011	0(O)	0/0
202	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	32.29	11/2011	11/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
203	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,723.57	12/2009	12/2011	24(O)	33/56
204	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	623.44	17.06	01/2012	01/2012	0(O)	0/0
205	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	60.31	02/2012	02/2012	0(O)	0/0
206	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50	409.50	4.07	02/2012	02/2012	0(O)	0/0
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29	410.29	64.17	02/2012	02/2012	0(O)	0/0
208	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57	353.57	99.40	07/2010	02/2012	19(O)	0/0
209	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32	1,347.32	263.91	02/2012	02/2012	0(O)	0/0
210	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	3,155.09	04/2009	03/2012	35(O)	19/41
211	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03	2,047.03	814.02	01/2012	03/2012	2(O)	2/10
212	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	1,077.10	07/2011	03/2012	8(O)	0/0
213	System Strengthening -X of SR - [N18000086]	12/2009	276.61	276.61	14.34	04/2012	04/2012	0(O)	0/0
214	765KV System for central part of Northern Region Grid - [N18000079]	11/2009	1,075.12	1,075.12	78.26	05/2012	05/2012	0(O)	0/0
215	765KV System for Central part of Northern Region G - [N18000078]	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
216	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]	02/2010	215.86	215.86	10.12	06/2012	06/2012	0(O)	0/0
217	System Strengthening -XII of SR - [N18000085]	02/2010	232.34	232.34	4.42	06/2012	06/2012	0(O)	0/0
218	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]	12/2008	573.99	573.99	100.83	08/2012	08/2012	0(O)	0/0
219	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95	2,360.95	1,028.71	08/2012	08/2012	0(O)	0/0
220	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	2,064.78	08/2012	08/2012	0(O)	0/0
221	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83	1,216.83	63.19	08/2012	08/2012	0(O)	0/0
222	MOUDA STPP - [N18000048]	11/2007	5,459.28	6,010.89	1,050.60	02/2012	10/2012	8(O)	0/0
223	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	552.84	10/2012	10/2012	0(O)	0/0
224	MAUDA Transmission System - [N18000084]	02/2010	469.38	469.38	9.84	10/2012	10/2012	0(O)	0/0
225	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	722.71	11/2012	11/2012	0(O)	0/0
226	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	600.06	11/2012	11/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
227	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
228	Northern Region Transmission Strengthening Scheme - [N18000083]	03/2012	965.58	965.58	55.64	11/2012	11/2012	0(O)	0/0
229	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33	6,285.33	4,044.32	09/2010	12/2012	27(O)	2/11
230	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	6.09	12/2008 09/2010	12/2012	27(R1)	0/15
231	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	-	11/2011	12/2012	13(O)	6/34
232	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	871.50	12/2012	12/2012	0(O)	0/0
233	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]	02/2010	2,144.00	2,144.00	62.91	12/2012	12/2012	0(O)	0/0
234	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	2,797.59	09/2009	03/2013	42(O)	1/20
235	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	858.41	03/2013	03/2013	0(O)	5/31
236	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,136.40	05/2013	05/2013	0(O)	37/161
237	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	961.06	08/2013	08/2013	0(O)	0/0
238	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	1,058.37	08/2013	08/2013	0(O)	0/0
239	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,662.39	11/2010	12/2013	37(O)	15/51
240	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	245.32	07/2010	12/2014	53(O)	0/0
241	Transm System for development of Pooling str. in N - [N18000077]	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
242	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	104.27	06/2013	03/2015	21(O)	0/0
243	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	309.06	07/2014	01/2016	18(O)	0/0
244	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			179,619.98	184,589.75	67,069.53				221/775
<u>Health & Family Welfare</u>									
245	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	477.33	03/1999 03/2005	-	-	7/16
Total			71.18	443.15	477.33				7/16
<u>Railways</u>									
246	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38	700.00	97.09	- 03/2011	02/2011	-1(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
247	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	314.80	03/2009 03/2009	11/2009	8(R3)	0/0
248	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74 -	224.51	41.39	- -	12/2009	-	0/0
249	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44 -	209.57	188.22	03/2009 -	02/2010	11(O)	0/0
250	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	556.48	03/1995 -	03/2010	180(O)	0/0
251	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998 -	03/2010	144(O)	0/0
252	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 459.55	571.55	572.84	- -	03/2010	-	0/0
253	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	753.69	03/2001 -	03/2010	108(O)	0/0
254	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	393.37	03/2004 03/2005	03/2010	60(R1)	0/0
255	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 124.13	325.00	282.77	- -	03/2010	-	0/0
256	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	1,010.00	997.05	03/2003 -	03/2010	84(O)	0/0
257	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 -	665.00	583.93	- 11/2008	03/2010	16(R1)	0/0
258	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	502.14	477.09	- -	03/2010	-	0/0
259	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	746.02	06/2007 -	03/2010	33(O)	0/0
260	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	228.09	148.83	- -	03/2010	-	0/0
261	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 546.49	610.07	565.97	- 02/2009	03/2010	13(R1)	0/0
262	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	463.57	- 03/2009	03/2010	12(R1)	0/0
263	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 -	227.52	223.78	03/2008 03/2009	03/2010	12(R1)	0/0
264	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	-	- 03/2009	03/2010	12(R1)	0/0
265	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	-	03/2008 06/2008	03/2010	21(R3)	0/0
266	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	405.60	397.76	- -	03/2010	-	0/0
267	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	-	04/2003 03/2010	06/2010	3(R1)	0/0
268	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	798.33	12/2006 -	06/2010	42(O)	0/0
269	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
270	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	358.00	307.27	12/2006 12/2008	11/2010	23(R3)	0/0
271	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 -	273.00	-	- 03/2009	11/2010	20(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
272	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23	638.00	-	02/2015	11/2010	-51(O)	0/0
273	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)- PH-I - [220100164]	03/1996	401.81	495.44	266.10	03/2004	12/2010	81(O)	0/0
274	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00	721.90	676.33	-	12/2010	-	0/0
275	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96	762.33	224.67	-	12/2010	12(R1)	0/0
276	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16	243.40	194.64	-	12/2010	22(R1)	0/0
277	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62	221.90	108.80	12/2007	12/2010	9(R1)	0/0
278	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00	718.30	-	03/2008	12/2010	28(R1)	0/0
279	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73	399.50	260.00	03/2009	12/2010	24(R1)	0/0
280	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80	200.80	-	-	12/2010	-	0/0
281	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20	4,103.20	3,338.94	12/2010	12/2010	0(O)	0/0
282	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00	332.75	3.81	-	02/2011	-	0/0
283	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38	457.17	346.51	02/2010	02/2011	12(O)	0/0
284	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96	810.78	39.55	-	02/2011	-1(R3)	0/0
285	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66	375.21	191.13	-	03/2011	12(R1)	0/0
286	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90	488.76	273.74	06/1999	03/2011	141(O)	0/0
287	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78	456.45	247.29	06/2004	03/2011	81(O)	0/0
288	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00	925.00	433.30	05/2008	03/2011	34(O)	0/0
289	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00	214.09	131.70	12/2009	03/2011	15(O)	0/0
290	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50	306.00	341.81	-	03/2011	21(R3)	0/0
291	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36	371.36	234.34	-	03/2011	-	0/0
292	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92	168.80	70.43	-	03/2011	-	0/0
293	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01	348.78	3.32	-	03/2011	-	0/0
294	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00	329.70	-	03/2009	03/2011	15(R1)	0/0
295	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15	245.15	27.04	12/2010	03/2011	3(O)	0/0
296	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10	171.10	43.83	03/2011	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
297	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35	258.35	9.38	03/2011	03/2011	0(O)	0/0
298	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97	196.97	72.26	03/2011	03/2011	0(O)	0/0
299	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50	252.50	60.95	02/2010	11/2011	21(O)	0/0
300	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44	1,103.47	659.43	-	12/2011	-	0/0
301	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64	735.10	175.04	-	12/2011	27(R1)	0/0
302	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00	496.03	27.08	03/2010	12/2011	21(O)	0/0
303	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00	727.52	2.96	-	03/2012	-	0/0
304	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81	234.45	144.11	-	03/2012	-	0/0
305	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41	341.41	0.17	-	03/2012	-	0/0
306	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59	495.74	61.85	-	03/2012	-	0/0
307	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90	324.90	96.75	03/2010	03/2012	24(O)	0/0
308	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69	501.69	45.90	03/2010	03/2012	24(O)	0/0
309	TAMLUK DIGHA - [N22000097]	03/1984	293.97	293.97	311.22	06/2005	04/2012	82(O)	0/0
310	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77	540.96	471.60	03/1994	12/2012	225(O)	0/0
311	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67	1,160.52	475.75	-	12/2012	-	0/0
312	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	921.00	236.87	03/2009	12/2012	45(O)	0/0
313	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
314	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20	687.20	115.27	03/2010	12/2012	33(O)	0/0
315	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84	410.08	101.53	-	03/2013	-	0/0
316	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00	899.42	552.07	-	03/2013	-	0/0
317	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70	1,556.23	215.58	-	03/2013	-	0/0
318	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00	3,087.44	1,856.21	04/2008	03/2014	27(R1)	0/0
319	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00	1,502.29	484.37	12/2008	03/2014	63(O)	0/0
320	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00	531.81	87.12	-	03/2014	-	0/0
321	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00	546.47	0.78	-	03/2014	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
322	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	5,300.00	106.13	03/2014 -	03/2014	0(O)	0/0
323	AGARTALA SABROOM - [N22000099]	04/2008	813.34 -	813.34	13.89	03/2014 -	03/2014	0(O)	0/0
324	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34 -	619.34	0.68	04/2014 -	03/2014	-1(O)	0/0
325	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	0.30	- -	03/2015	-	0/0
326	SEVOK RANGPO - [N22000102]	04/2008	1,339.48 -	1,339.48	1.42	12/2015 -	12/2015	0(O)	0/0
327	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	2,492.53	189.83	03/2011 -	03/2016	60(O)	0/0
328	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 8,000.00	11,270.00	3.16	03/2001 -	12/2017	201(O)	0/0
329	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 407.78	617.63	341.96	- -	-	-	0/0
330	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53 320.66	464.50	487.70	03/1996 06/2009	-	-	0/0
331	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
332	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	232.09	- -	-	-	0/0
333	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 142.98	170.00	111.69	03/2002 03/2011	-	-	0/0
334	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
335	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	310.72	- -	-	-	0/0
336	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
337	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
338	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	274.41	- -	-	-	0/0
339	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	82.28	- -	-	-	0/0
340	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	357.81	- -	-	-	0/0
341	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	287.26	02/2009 -	-	-	0/0
342	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	337.82	49.53	- -	-	-	0/0
343	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 -	268.00	-	12/1999 03/2008	-	-	0/0
344	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
345	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	66.85	- -	-	-	0/0
346	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	89.61	03/2007 03/2007	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
347	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0
348	KODERMA-RANCHI VIA BARKAKHANA (NL), ECR - [220100222]	03/1999	491.19	1,099.20	540.09	07/2005	-	-	0/0
349	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	-	-	-	0/0
350	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	63.23	-	-	-	0/0
351	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00	497.63	477.14	-	-	-	0/0
352	BIDAR-GULBARGA, SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	126.85	-	-	-	0/0
353	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15	381.17	80.12	05/2009	-	-	0/0
354	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10	320.10	108.05	-	-	-	0/0
355	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23	162.87	0.04	-	-	-	0/0
356	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00	548.96	392.50	-	-	-	0/0
357	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00	695.00	9.41	-	-	-	0/0
358	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00	1,300.00	-	-	-	-	0/0
359	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	325.17	311.98	03/2005 12/2008	-	-	0/0
360	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91	459.91	36.40	-	-	-	0/0
361	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006	-	-	0/0
362	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]	04/2001	727.13 727.13	1,225.00	120.45	-	-	-	0/0
363	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67	165.67	0.15	-	-	-	0/0
364	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73	230.03	45.76	-	-	-	0/0
365	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	585.93	102.78	-	-	-	0/0
366	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45	573.12	555.49	-	-	-	0/0
367	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56	671.82	0.74	-	-	-	0/0
368	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92 261.70	261.70	0.08	02/2006	-	-	0/0
369	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]	09/2007	404.19 404.19	790.00	47.70	-	-	-	0/0
370	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 343.17	639.00	196.03	-	-	-	0/0
371	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00 170.00	255.96	111.77	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
372	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 125.00	227.40	12.71	- -	-	-	0/0
373	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	28.22	- -	-	-	0/0
374	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	24.40	- -	-	-	0/0
375	BHAKURA DAMODAR - [N22000098]	03/1998	282.70 -	325.17	24.32	07/2008 -	-	-	0/0
376	KISHANGANJ JALALGARH - [N22000101]	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
377	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]	04/1993	100.41 -	949.22	15.65	12/2009 -	-	-	0/0
378	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 254.07	676.00	307.38	- 12/2011	-	-	0/0
379	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	353.08 353.08	1,010.00	64.05	- 12/2012	12/2012	0(R3)	0/0
380	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	192.46	- 12/2012	-	-	0/0
	Total		51,007.64 -	95,575.86	32,701.31				0/0
<u>Road Transport & Highways</u>									
381	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00 -	310.00	-	04/2008 -	03/2010	23(O)	0/0
382	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93 -	440.93	641.40	12/2006 -	12/2009	36(O)	0/0
383	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39 -	534.39	716.15	05/2007 -	12/2009	31(O)	0/0
384	TOVARAMKURCHI-MADURAI,NH45B (NHAI) - [N24000054]	04/2000	263.00 -	263.00	317.74	08/2008 -	12/2009	16(O)	0/0
385	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80 -	402.80	453.70	03/2009 -	12/2009	9(O)	0/0
386	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00 -	450.00	876.61	07/2008 -	01/2010	18(O)	0/0
387	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00 -	556.00	568.50	03/2009 -	03/2010	12(O)	0/0
388	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00 -	261.00	286.30	08/2008 -	03/2010	19(O)	0/0
389	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00 -	230.00	164.23	06/2008 -	03/2010	21(O)	0/0
390	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40 -	372.40	399.29	07/2004 -	04/2010	69(O)	0/0
391	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00 -	276.00	360.00	04/2008 -	04/2010	24(O)	0/0
392	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80 -	469.80	665.80	12/2008 -	04/2010	16(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
393	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	04/2010	18(O)	0/0
394	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	636.10	05/2009	04/2010	11(O)	0/0
395	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	127.92	08/2006	05/2010	45(O)	0/0
396	MADURAI - KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	331.60	03/2008	05/2010	26(O)	0/0
397	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	204.68	01/2009	05/2010	16(O)	0/0
398	GONDE-VADAPE (THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	677.94	04/2009	05/2010	13(O)	0/0
399	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	383.28	02/2009	05/2010	15(O)	0/0
400	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]	03/2005	168.00	168.00	305.42	12/2008	05/2010	17(O)	0/0
401	HYDERABAD-BANGALORE SEC. (NS CORR. PH-II) [KM 418-463 - [N24000080]	12/2003	243.64	243.64	244.30	08/2009	05/2010	9(O)	0/0
402	MAHARASHTRA/AP BORDER TO ISLAM NAGAR, (NS-2/BOT/AP-6), NH-7 - [N24000093]	12/2003	360.42	360.42	476.00	11/2009	05/2010	6(O)	0/0
403	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	71.35	08/2004	06/2010	70(O)	0/0
404	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	452.03	03/2005	06/2010	63(O)	0/0
405	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	405.51	03/2005	06/2010	63(O)	0/0
406	PURNEA-GOYAKOTA SEC. (EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	244.30	07/2004	06/2010	71(O)	0/0
407	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	782.90	11/2007	06/2010	31(O)	0/0
408	GAGODHAR-GARAMORE (PK-IV, NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	423.50	11/2007	06/2010	31(O)	0/0
409	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	150.00	08/2005	06/2010	58(O)	0/0
410	MADURAI - KANNIAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.90	03/2008	06/2010	27(O)	0/0
411	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	560.71	03/2009	06/2010	15(O)	0/0
412	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	838.94	11/2010	06/2010	-5(O)	0/0
413	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	356.54	06/2008	06/2010	24(O)	0/0
414	DARBHANGA-MUZAFFARPUR (KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	386.96	06/2008	06/2010	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	155.20	07/2008	06/2010	23(O)	0/0
416	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	433.80	06/2008	06/2010	24(O)	0/0
417	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.44	06/2008	06/2010	24(O)	0/0
418	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	172.50	11/2008	06/2010	19(O)	0/0
419	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]	03/2005	280.00	280.00	550.82	06/2009	06/2010	12(O)	0/0
420	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]	04/2000	263.27	263.27	201.38	02/2004	06/2010	76(O)	0/0
421	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	30.89	04/2009	06/2010	14(O)	0/0
422	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	180.40	08/2009	06/2010	10(O)	0/0
423	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	208.10	09/2009	06/2010	9(O)	0/0
424	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	232.20	09/2008	06/2010	21(O)	0/0
425	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	187.70	08/2009	06/2010	10(O)	0/0
426	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	162.00	08/2009	06/2010	10(O)	0/0
427	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	403.39	06/2010	06/2010	0(O)	0/0
428	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]	12/2003	407.60	407.60	181.40	06/2010	06/2010	0(O)	0/0
429	BANGALORE-NEELAMANGALALA NH-4 - [N24000104]	03/2005	445.00	445.00	772.29	07/2010	06/2010	-1(O)	0/0
430	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	198.42	06/2010	06/2010	0(O)	0/0
431	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	67.03	08/2004	07/2010	71(O)	0/0
432	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	118.70	03/2008	07/2010	28(O)	0/0
433	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	90.26	03/2008	07/2010	28(O)	0/0
434	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.55	07/2010	07/2010	0(O)	0/0
435	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	441.95	07/2010	07/2010	0(O)	0/0
436	BANGALORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	831.21	07/2010	07/2010	0(O)	0/0
437	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	667.00	03/2010	07/2010	4(O)	0/0
438	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	177.44	06/2008	08/2010	26(O)	0/0
439	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	313.97	03/2005	09/2010	66(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
440	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	223.30	10/2008	09/2010	23(O)	0/0
441	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	232.40	09/2009	09/2010	12(O)	0/0
442	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	242.40	09/2009	09/2010	12(O)	0/0
443	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
444	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
445	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	-	10/2008	10/2010	24(O)	0/0
446	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	287.70	10/2008	10/2010	24(O)	0/0
447	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	348.10	10/2008	10/2010	24(O)	0/0
448	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	264.50	10/2008	10/2010	24(O)	0/0
449	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	292.12	10/2008	10/2010	24(O)	0/0
450	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	449.20	04/2008	10/2010	30(O)	0/0
451	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	178.00	10/2008	10/2010	24(O)	0/0
452	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	232.00	10/2009	10/2010	12(O)	0/0
453	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	418.89	03/2005	12/2010	69(O)	0/0
454	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	622.20	04/2007	12/2010	44(O)	0/0
455	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	277.40	09/2007	12/2010	39(O)	0/0
456	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	98.69	06/2005	12/2010	66(O)	0/0
457	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	291.00	05/2008	12/2010	31(O)	0/0
458	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	259.50	03/2008	12/2010	33(O)	0/0
459	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	28.10	04/2009	12/2010	20(O)	0/0
460	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
461	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	28.09	11/2008	12/2010	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
462	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	306.10	12/2008	12/2010	24(O)	0/0
463	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	282.20	12/2008	12/2010	24(O)	0/0
464	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	104.00	10/2008	12/2010	26(O)	0/0
465	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	108.10	10/2008	12/2010	26(O)	0/0
466	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	254.27	06/2009	12/2010	18(O)	0/0
467	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	12/2010	21(O)	0/0
468	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	253.60	12/2009	12/2010	12(O)	0/0
469	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
470	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	505.00	02/2010	12/2010	10(O)	0/0
471	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	0.41	02/2004	12/2010	82(O)	0/0
472	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	444.84	08/2010	12/2010	4(O)	0/0
473	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	287.00	05/2010	12/2010	7(O)	0/0
474	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	168.08	06/2008	01/2011	31(O)	0/0
475	TRICHY - DINDIGUL NH-45 - [N24000099]	03/2005	576.00	576.00	254.40	07/2010	01/2011	6(O)	0/0
476	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	526.99	01/2011	01/2011	0(O)	0/0
477	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	334.75	01/2011	01/2011	0(O)	0/0
478	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	108.10	09/2007	02/2011	41(O)	0/0
479	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	133.43	09/2007	03/2011	42(O)	0/0
480	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	195.53	07/2005	03/2011	68(O)	0/0
481	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	229.19	07/2005	03/2011	68(O)	0/0
482	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	166.62	10/2008	03/2011	29(O)	0/0
483	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	226.40	10/2008	03/2011	29(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
484	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	127.40	02/2009	03/2011	25(O)	0/0
485	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	147.14	09/2008	03/2011	30(O)	0/0
486	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00	198.00	110.90	11/2008	03/2011	28(O)	0/0
487	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	240.40	03/2008	03/2011	36(O)	0/0
488	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	129.40	06/2008	03/2011	33(O)	0/0
489	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	460.10	10/2009	03/2011	17(O)	0/0
490	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	118.00	09/2010	03/2011	6(O)	0/0
491	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	61.40	04/2009	04/2011	24(O)	0/0
492	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	517.38	05/2010	05/2011	12(O)	0/0
493	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	145.60	09/2007	06/2011	45(O)	0/0
494	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	53.32	09/2008	06/2011	33(O)	0/0
495	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
496	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0
497	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	65.53	05/2008	06/2011	37(O)	0/0
498	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	236.20	03/2010	06/2011	15(O)	0/0
499	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	145.54	04/2004	10/2011	90(O)	0/0
500	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00	225.00	170.70	06/2008	10/2011	40(O)	0/0
501	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00	195.00	88.52	06/2008	12/2011	42(O)	0/0
502	BIJNI TO ASSAM WB BORDER (NH-31.C)(2)(NHAI) - [240106293]	12/2003	237.80	237.80	98.64	06/2008	12/2011	42(O)	0/0
503	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	275.90	09/2008	12/2011	39(O)	0/0
504	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	167.00	06/2008	12/2011	42(O)	0/0
505	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	133.50	04/2008	12/2011	44(O)	0/0
506	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	131.10	06/2008	12/2011	42(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
507	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	93.26	04/2008	03/2012	47(O)	0/0
508	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	126.10	04/2008	03/2012	47(O)	0/0
509	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	177.32	02/2010	03/2012	25(O)	0/0
510	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
511	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	8.72	05/2010	08/2012	27(O)	0/0
512	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.11	09/2007	12/2012	63(O)	0/0
513	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.73	07/2009	12/2012	41(O)	0/0
514	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61	217.61	73.62	04/2010	12/2012	32(O)	0/0
515	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]	12/2003	300.00	300.00	-	10/2008	-	-	0/0
	Total		41,863.55	42,136.98	36,235.78				0/0
	Shipping & Ports								
516	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	406.28	03/2010	03/2010	0(O)	0/0
517	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	297.76	04/2009	03/2010	11(O)	0/0
518	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	181.80	06/2007 01/2009	06/2010	17(R1)	0/0
519	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	374.37	07/2010	07/2010	0(O)	0/0
520	DEV. & OPERATION OF AN INTERNATIONAL CONTAINER TRA - [N25000046]	11/2004	2,118.00	2,118.00	-	11/2004	08/2010	69(O)	0/0
521	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	814.65	10/2008	11/2010	25(O)	0/0
522	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	307.02	11/2010	11/2010	0(O)	0/0
523	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
524	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
525	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	99.84	12/2005	01/2011	61(O)	0/0
526	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	1,140.00	0.16	02/2011	02/2011	0(O)	0/0
527	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	755.50	-	03/2011	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
528	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	211.21	04/2011	04/2011	0(O)	0/0
529	Acquisition of two nos. of 120 B.P - [N25000042]	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
530	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	438.02	04/2011	12/2011	8(O)	0/0
531	Acquisition of Two nos. of 3060 DWT - [N25000043]	04/2009	2,770.32	2,770.42	1,108.12	09/2011	12/2011	3(O)	0/0
532	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
533	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]	03/2009	3,500.00	3,500.00	-	01/2012	01/2012	0(O)	0/0
534	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
535	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0
536	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
537	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]	03/2008	375.00	375.00	-	01/2009	-	-	0/0
	Total		24,047.63	24,630.99	4,769.62				0/0
	Telecommunications								
538	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
539	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
540	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	12/2009	20(O)	0/0
541	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0
542	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	422.85	12/2008	12/2009	12(O)	0/0
543	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	113.34	03/2009	12/2009	9(O)	0/0
544	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	470.24	12/2008	12/2009	12(O)	0/0
545	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	180.93	03/2009	12/2009	9(O)	0/0
546	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	12/2009	3(O)	0/0
547	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	169.33	12/2008	01/2010	13(O)	0/0
548	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	0.00	278.16	175.77	12/2008	01/2010	1(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
549	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	110.83	03/2009	01/2010	10(O)	0/0
550	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	336.81	64.50	01/2009	01/2010	12(O)	0/0
551	NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.24	12/2004	02/2010	62(O)	0/0
552	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007 12/2009	03/2010	3(R3)	0/0
553	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	94.13	10/2007 12/2009	03/2010	3(R3)	0/0
554	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	104.60	12/2009 12/2009	03/2010	3(R3)	0/0
555	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	161.35	02/2008	05/2010	27(O)	0/0
556	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	73.54	09/2009	06/2010	9(O)	0/0
557	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	10(O)	0/0
558	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53 2.00	180.53	25.97	12/2009	06/2010	6(O)	0/0
559	Execution of telecom network requirement of defence - [N26000065]	05/2006	1,077.00	1,077.00	841.00	03/2009	09/2010	18(O)	0/0
560	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
561	Implementation of FTTH, the state of the art Acces - [N26000073]	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
562	Procurement of DXC equipment - [N26000074]	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
563	Procurement of 24 F OF cable. - [N26000075]	02/2008	199.00	199.00	-	03/2010	11/2010	8(O)	0/0
564	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007 11/2009	12/2010	13(R3)	0/0
565	Procurement of 2.5G DWDM equipment - [N26000066]	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
566	Procurement of 10G (40 chl) DWDM equipment - [N26000067]	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
567	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
568	Procurement of STM-1 SDH equipment - [N26000069]	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
569	Procurement of STM-16 MADM equipment - [N26000070]	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
570	Procurement of STM-16 ADM equipment - [N26000071]	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
571	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
572	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	160.00	92.45	06/2006	-	-	0/0
573	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
574	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]	11/2008	350.00	350.00	-	-	-	-	0/0
575	CENTRALISED TRANSMISSION NMS - [N26000064]	08/2009	300.00	300.00	-	-	-	-	0/0
	Total		16,511.58	16,433.91	4,469.52				0/0
			-						
	<u>Urban Development</u>								
576	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00	8,676.00	13,719.69	06/2010	11/2010	5(O)	0/7
			8,605.36			-			
577	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	6,395.00	2,267.57	12/2011	06/2012	-3(R3)	0/1
			8,158.00			09/2012			
	Total		14,513.00	15,071.00	15,987.26				0/8
			-						
	<u>Water Resources</u>								
578	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-			
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			589,880.37	671,320.22	266,362.34				678/1858
