

**310<sup>th</sup> FLASH REPORT  
ON  
CENTRAL SECTOR PROJECTS  
(₹.150 Crores and above)  
August, 2011**



BCPL – Assam Gas Cracker



Government of India  
**Ministry of Statistics and Programme Implementation**  
**Infrastructure and Project Monitoring Division**  
Sardar Patel Bhavan, Sansad Marg  
New Delhi-110001  
Website: [www.cspm.gov.in](http://www.cspm.gov.in)

## Contents

|                                                                                      |       |
|--------------------------------------------------------------------------------------|-------|
| Executive Summary                                                                    | 1 -5  |
| Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11 | 6-12  |
| List of Delete Projects                                                              | 13    |
| Summary of Projects                                                                  | 14-24 |
| <b>Sector wise Trend and Graphicalf Analysis</b>                                     | 25-37 |
| Sector wise analysis of projects                                                     | 38-67 |
| Graph                                                                                | 68-78 |
| <b>Statewise Summary of All Ongoing Projects</b>                                     | 79    |
| <b>List of Abbreviations</b>                                                         | 80-81 |

## **EXECUTIVE SUMMARY**

The Flash Report for August 2011 (the 310<sup>th</sup> Flash Report) contains information on the status of the 553 projects in the Central Sector costing ₹ 150 Crores and above. During August 2011, seven projects have reported completion (which has now been dropped from the monitor of this Ministry).

While, the online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month, on account of continuous effort/persuasion by this Ministry, the, NHAI, MTNL and BSNL are not reporting online in spite of repeated requests. During August 2011, thirty-two (32) projects have reported additional delays, vis-à-vis the date of completion reported the previous month. The additional delays are in the range of 1 to 12 months, in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Civil Aviation and Atomic Energy Sectors.

| <b>S. No.</b> | <b>Sector</b>             | <b>Projects on monitor</b> | <b>Additional delays</b> |
|---------------|---------------------------|----------------------------|--------------------------|
| 1.            | RAILWAYS                  | 134                        | 2                        |
| 2.            | ROAD TRANSPORT & HIGHWAYS | 121                        | 12                       |
| 3.            | POWER                     | 83                         | 7                        |
| 4.            | PETROLEUM                 | 71                         | 5                        |
| 5.            | COAL                      | 46                         | 3                        |
| 6.            | TELECOMMUNICATION         | 40                         | 0                        |
| 7.            | SHIPPING & PORTS          | 26                         | 0                        |
| 8.            | STEEL                     | 12                         | 1                        |
| 9.            | FERTILISERS               | 6                          | 0                        |
| 10.           | CIVIL AVIATION            | 5                          | 1                        |
| 11.           | ATOMIC ENERGY             | 4                          | 1                        |
| 12.           | URBAN DEVELOPMENT         | 2                          | 0                        |
| 13.           | MINES                     | 1                          | 0                        |
| 14.           | WATER RESOURCES           | 1                          | 0                        |
| 15.           | PETROCHEMICALS            | 1                          | 0                        |
| <b>Total</b>  |                           | <b>553</b>                 | <b>32</b>                |

3. The total original cost of implementation of the 553 projects was about ₹ 6,14,127.75 Crores and their anticipated completion cost is likely to be ₹ 7,33,611.82 Crores, which reflects an overall cost overrun of 19.5%. The expenditure incurred on these projects till August, 2011 is ₹ 3,19,374.21 Crores, which is 43.5% of the revised cost of the projects .

4. Out of the 553 projects, 5 projects are ahead of schedule, 134 are on schedule, 243 projects are delayed and 118 projects have been sanctioned without any commissioning schedule/date. Further, in case of 53 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month under reference the projects reporting delays have marginally increased to 243 from 241 in July'2011. Out of 243 delayed projects, at the end of August, 2011, 50 projects had overall delay in the range of 1 to 12 months, 59 projects had delay in the range of 13 to 24 months, 101 projects had delay in the range of 25 to 60 months and 33 projects had delay of 61 months and above.

**The Sector-wise details of delays are as under:-**

i) In the **Coal sector**, 3 projects have reported additional delays in the range of 1 to 6 months. Adriyala Shaft Project SCCL has reported additional delay of six months (overall delay of 15 months) due to preparation of Revised Feasibility Report (RFR) in view of geological disturbance. TPS-II Expansion, NLC Project has an additional delay of 2 months due to delay in equipment erection. Barsingsar TPS, NLC has an additional delay of 1 month due to delay in commissioning.

ii) In the **Steel sector**, 700 TPD Air Separation Unit-4 at Oxygen Plant-II, Bhilai SAIL has reported an additional delay of one month due to retendering of the main package.

iii) In the **Petroleum Sector**, 5 projects have reported additional delays in the range of 1-7 months. Diesel Hydro Treatment Project, Dhaligaon, BRPL has reported additional delay of 1 month (overall delay of 23 months) due to law and order problems in the north - east. MSQ Quality up- Gradation Project at Bongaigaon Refinery, IOCL has reported additional delay of 1 month (over all delay of 21 months) due to modification of an existing running plant and delay by BHEL in delivery of accessories. Karanpur Moradabad Kashipur Rudrapur Pipeline Project. GAIL has reported additional delay of three months due to farmers and land owners are

demanding for re-routing the pipeline and high compensation is being demanded. Refrigerated LPG Storage at JNPT BPCL has reported an additional delay of two months due to delay in clearance from JNPT and Railway and ban on sand mining in Maharashtra. Paradip Refinery Project, IOCL has reported an additional delay of seven months due to law and order problems.

**iv) In the Power Sector,** 7 projects have reported additional delays in the range of 1-5 months. Chamera Stage-III, NHPC has reported an additional delay of one month (overall delay of 15 months) due to laxity treatment in LEG. Chutak Hydro Electric Project, NHPC has reported an additional delay of three month (over all delay of 12 months) due to delay in supply and erection of E&M components. Tehri Pumped Storage Plant (1000MW) THDCL has reported an additional delay of one month, for which no reason has been reported. Transmission System Associated with Parbati – III HEP PGCIL has reported an additional delay of one month due to delay in generation project and due to delay in forest clearance. Transmission System Associated with Barh Generation project, PGCIL has reported an additional delay of three months due to generation project delay. Northern Region System Strengthening Scheme – XII, PGCIL has reported an additional delay of four months due to severe ROW problem. Parbati HEP – II, (NHPC) has reported an additional delay of five months due to flash floods in Jigrai Nallah and contractual problems.

**v) In the Road Transport and Highways Sector,** 12 projects have reported additional delay in the range of 1-4 months. 6 projects have reported additional delay of one month each due to slow progress of work by the contractor. Vijayapur to Pathankot (J&K) NH-1A KM 16.35 to KM 50, NHAI and Vijayapur to Pathankot (NS-35/J&K) NH-1A KM 50 to KM 80, NHAI have reported an additional delay of 2 months each due to delay in utility shifting by the state departments. Sunakhala – Ganjam(GQ) KM 338 – KM 284 (NH-5), NHAI and Jhansi to Lalitpur, NH- 26, NHAI have reported an additional delay of 2 months each. Kotwa to Dewapur (10 LMNHP), NH-28 Ph. II KM 440 to KM 402, NHAI and Surat – Dahisar (Six Lane) KM 263 to KM 502, NHAI have reported an additional delay of 3 and 4 months respectively for which no specific reason has been reported by the project authority.

**vi)** In the **Railway Sector**, 2 projects have reported additional delays of 9 months each. Rail-cum- Road Bridge over River Brahmaputra Bridge NEFR has reported an additional delay of 9 months due to delay in tendering process. Sevok Rangpo, NEFR has reported an additional delay of 9 months due to delay in forest clearance and shifting location of Rangpo yard.

**vii)** In the **Civil Aviation Sector**, Construction of new Airport at Pakyong (Sikkim) Airport AAI has reported an additional delay of six months due to non availability of working days on account of heavy rainfall & earthquake.

**viii)** In the **Atomic Energy Sector**, Kudankulam APP, NPCIL has reported an additional delay of four months due to slippage of commitments by M/s ASE and agitation by the local people.

The status as on 01.09.2011 in respect of completion of projects costing ₹150 Crores and above in different sectors during 2011-12 is indicated in the Report.



(Pankaj Jain)  
Additional Secretary  
Ministry of Statistics & Programme Implementation

## EXECUTIVE SUMMARY

| Sl. No. | Sector                    | Projects on Monitor | Projects Additional Delayed |
|---------|---------------------------|---------------------|-----------------------------|
| 1       | Railways                  | 134                 | 2                           |
| 2       | Road Transport & Highways | 121                 | 12                          |
| 3       | Power                     | 83                  | 7                           |
| 4       | Petroleum                 | 71                  | 5                           |
| 5       | Coal                      | 46                  | 3                           |
| 6       | Telecommunications        | 40                  | 0                           |
| 7       | Shipping & Ports          | 26                  | 0                           |
| 8       | Steel                     | 12                  | 1                           |
| 9       | Fertilisers               | 6                   | 0                           |
| 10      | Civil Aviation            | 5                   | 1                           |
| 11      | Atomic Energy             | 4                   | 1                           |
| 12      | Urban Development         | 2                   | 0                           |
| 13      | Mines                     | 1                   | 0                           |
| 14      | Petrochemicals            | 1                   | 0                           |
| 15      | Water Resources           | 1                   | 0                           |
|         | Total                     | 553                 | 32                          |

# ANNEXURE-I

## Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

| Sl. No.                              | Project Name                                                                                                       | Original Cost (Rs. Crore) | Original Date Of Commissioning | Cumulative Expenditure (Rs. Crore) |
|--------------------------------------|--------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| <b>April,2011</b>                    |                                                                                                                    |                           |                                |                                    |
| <u>Civil Aviation</u>                |                                                                                                                    |                           |                                |                                    |
| 1                                    | Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]                                | 230.00                    | 01/2011                        | 241.28                             |
| <u>Petroleum</u>                     |                                                                                                                    |                           |                                |                                    |
| 2                                    | SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]              | 396.13                    | 10/2009                        | 106.22                             |
| 3                                    | Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]      | 605.40                    | 12/2010                        | 408.90                             |
| <u>Power</u>                         |                                                                                                                    |                           |                                |                                    |
| 4                                    | Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]                                           | 2,570.44                  | 08/2010                        | 1,896.00                           |
| <u>Railways</u>                      |                                                                                                                    |                           |                                |                                    |
| 5                                    | GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]                                              | 458.45                    | -                              | 555.49                             |
| <u>Road Transport &amp; Highways</u> |                                                                                                                    |                           |                                |                                    |
| 6                                    | MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]   | 323.36                    | 03/2008                        | 189.90                             |
| <u>Shipping &amp; Ports</u>          |                                                                                                                    |                           |                                |                                    |
| 7                                    | ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]                          | 1,108.12                  | 04/2011                        | 1,238.88                           |
| <b>May,2011</b>                      |                                                                                                                    |                           |                                |                                    |
| <u>Civil Aviation</u>                |                                                                                                                    |                           |                                |                                    |
| 8                                    | CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]               | 213.35                    | 09/2010                        | 60.89                              |
| <u>Power</u>                         |                                                                                                                    |                           |                                |                                    |
| 9                                    | TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037] | 290.49                    | 04/2010                        | 346.80                             |
| <u>Railways</u>                      |                                                                                                                    |                           |                                |                                    |
| 10                                   | DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]                                             | 180.73                    | 12/2006                        | 352.32                             |
| 11                                   | HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]                                                            | 106.64                    | 03/2007                        | 147.32                             |

**Month wise List of Completed Project Costing Rs. 150 Crore and above during  
2011-2012**

| Sl. No. | Project Name                                                                                                     | Original Cost (Rs. Crore) | Original Date Of Commissioning | Cumulative Expenditure (Rs. Crore) |
|---------|------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| 12      | SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]                                                 | 46.00                     | -                              | 244.16                             |
|         | <u>Road Transport &amp; Highways</u>                                                                             |                           |                                |                                    |
| 13      | GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]         | 579.00                    | 04/2009                        | 765.90                             |
| 14      | NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]                                  | 230.00                    | 06/2008                        | 312.00                             |
| 15      | KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]                  | 549.00                    | 05/2010                        | 815.00                             |
|         | June,2011                                                                                                        |                           |                                |                                    |
|         | <u>Petroleum</u>                                                                                                 |                           |                                |                                    |
| 16      | CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]                        | 2,591.80                  | 12/2009                        | 3,265.10                           |
|         | <u>Power</u>                                                                                                     |                           |                                |                                    |
| 17      | KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]                      | 260.34                    | 06/2008                        | 184.25                             |
| 18      | EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]       | 803.70                    | 06/2009                        | 667.01                             |
| 19      | TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]        | 276.61                    | 06/2011                        | 199.16                             |
|         | <u>Railways</u>                                                                                                  |                           |                                |                                    |
| 20      | VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]                                                      | 175.00                    | -                              | 538.69                             |
|         | <u>Road Transport &amp; Highways</u>                                                                             |                           |                                |                                    |
| 21      | PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191] | 205.73                    | 07/2004                        | 247.70                             |
| 22      | MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]    | 239.00                    | 07/2005                        | 317.60                             |
| 23      | BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]                     | 565.00                    | 07/2010                        | 1,080.00                           |
|         | July,2011                                                                                                        |                           |                                |                                    |
|         | <u>Steel</u>                                                                                                     |                           |                                |                                    |
| 24      | REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]                | 172.78                    | 01/2010                        | 131.95                             |
|         | <u>Petroleum</u>                                                                                                 |                           |                                |                                    |

**Month wise List of Completed Project Costing Rs. 150 Crore and above during  
2011-2012**

| Sl. No.                              | Project Name                                                                                                     | Original Cost<br>(Rs. Crore) | Original Date<br>Of<br>Commissioning | Cumulative<br>Expenditure<br>(Rs. Crore) |
|--------------------------------------|------------------------------------------------------------------------------------------------------------------|------------------------------|--------------------------------------|------------------------------------------|
| 25                                   | C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]               | 900.92                       | 05/2008                              | 774.32                                   |
| 26                                   | COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]                  | 1,512.00                     | 04/2011                              | 846.61                                   |
| 27                                   | Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]                              | 2,553.28                     | 05/2011                              | 3,614.84                                 |
| <u>Railways</u>                      |                                                                                                                  |                              |                                      |                                          |
| 28                                   | SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]                                                    | 437.40                       | 03/2004                              | 544.35                                   |
| <u>Road Transport &amp; Highways</u> |                                                                                                                  |                              |                                      |                                          |
| 29                                   | IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203] | 210.00                       | 04/2007                              | 672.97                                   |
| 30                                   | KURALI-KIRATPUR, NH-21(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000087]                                       | 309.00                       | 06/2010                              | 553.56                                   |
| <b>August,2011</b>                   |                                                                                                                  |                              |                                      |                                          |
| <u>Power</u>                         |                                                                                                                  |                              |                                      |                                          |
| 31                                   | EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]        | 262.10                       | 09/2010                              | 164.00                                   |
| <u>Railways</u>                      |                                                                                                                  |                              |                                      |                                          |
| 32                                   | AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]                                         | 262.00                       | -                                    | 548.54                                   |
| <u>Road Transport &amp; Highways</u> |                                                                                                                  |                              |                                      |                                          |
| 33                                   | AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]           | 193.00                       | 10/2008                              | 338.70                                   |
| 34                                   | MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256] | 359.00                       | 03/2009                              | 870.60                                   |
| <u>Telecommunications</u>            |                                                                                                                  |                              |                                      |                                          |
| 35                                   | NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]                                       | 312.86                       | 02/2008                              | 204.43                                   |
| <u>Urban Development</u>             |                                                                                                                  |                              |                                      |                                          |
| 36                                   | DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]                                          | 8,676.00                     | 06/2010                              | 18,304.30                                |

# ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2011-2012

| Sl. No.               | Project Name                                                                                         | Original Cost (Rs. Crore) | Original Date Of Commissioning | Cumulative Expenditure (Rs. Crore) |
|-----------------------|------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| May,2011              |                                                                                                      |                           |                                |                                    |
| <u>Civil Aviation</u> |                                                                                                      |                           |                                |                                    |
| 1                     | D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056] | 535.00                    | 06/2010                        | 143.97                             |
| August,2011           |                                                                                                      |                           |                                |                                    |
| <u>Steel</u>          |                                                                                                      |                           |                                |                                    |
| 2                     | EXPENSION OF ROURKELA STEEL PLANT(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N16000049]             | 6,133.00                  | 02/2011                        | 1,253.17                           |

## Summary of projects in the Flash Report for the month of August, 2011


### I. Project Implementation - Current Status:

|                                                                               |     |
|-------------------------------------------------------------------------------|-----|
| Number of Projects in Previous Month                                          | 565 |
| Number of Projects completed/dropped/frozen in Previous Month                 | 7   |
| Number of Projects completed/dropped/frozen in Current Month                  | 7   |
| Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month | 2   |

Number of Projects in Current Month **553**

### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 553 projects, 5 projects are ahead of schedule, 134 projects are on schedule and 243 projects are delayed. Of the balance, 118 projects do not have fixed dates of commissioning while 53 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

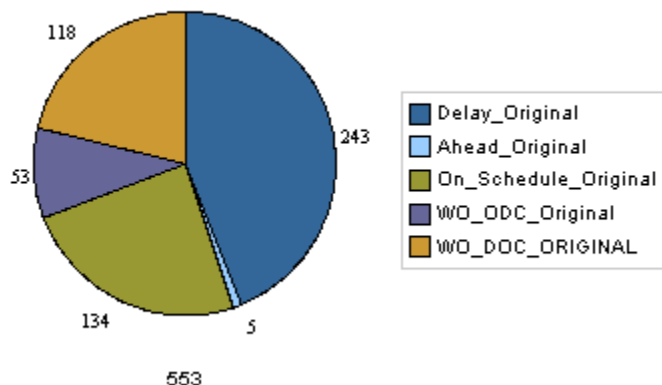

### III. Investment Scenario

**The Total Original cost of implementation of 553 projects when sanctioned, was of the order of Rs. 614127.75 crore but this was subsequently revised to Rs. 733611.82 crore implying a cost overrun of 19.5%. The expenditure incurred on these projects till August, 2011 is Rs. 319374.21 crore, which is 43.5% of the revised cost of the projects.**

Figures are in Rs. Crore

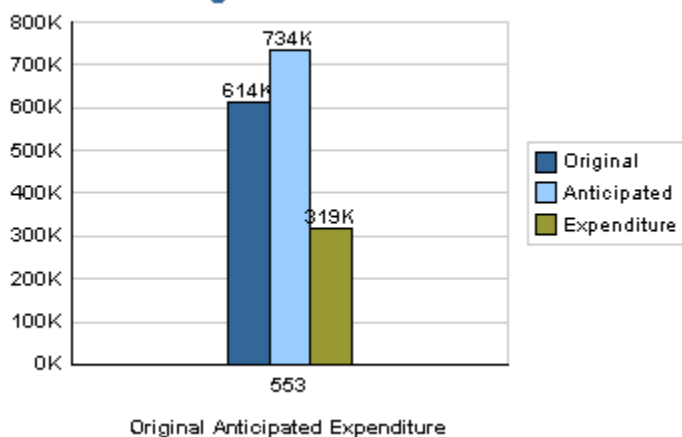

## I. Project Added / Completed / Dropped / Frozen

|                                                                               |     |
|-------------------------------------------------------------------------------|-----|
| No of Projects in Previous Month                                              | 565 |
| No of Projects Completed/Dropped/Frozen in Previous Month                     | 7   |
| No of Projects Completed/Dropped/Frozen in Current Month                      | 7   |
| No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month | 2   |
| No of Projects added in Current Month                                         | 0   |
| No of Projects in Current Month                                               | 553 |

## II. Project status

| With Respect To          | Number of Projects |       |             |                               |               | Total | Delay (%) |
|--------------------------|--------------------|-------|-------------|-------------------------------|---------------|-------|-----------|
|                          | Delayed            | Ahead | On schedule | Without ODC but DOC available | Without D.O.C |       |           |
| Original ( Date )        | 243                | 5     | 134         | 53                            | 118           | 553   | 43.94     |
| Latest Approved ( Date ) | 256                | 9     | 169         | 38                            | 83            | 553   | 46.29     |

## III. (A) Project cost

| (All Cost/ Expenditure in Rs. crore ) |                 |            |             |             |       |              |       |
|---------------------------------------|-----------------|------------|-------------|-------------|-------|--------------|-------|
| With Respect to                       | No. of Projects | Cost       |             |             |       | Cost overrun |       |
|                                       |                 | Sanctioned | Anticipated | Expenditure | %     | ( Crore)     | %     |
| Original ( OCE )                      | 443             | 480,400.39 | 516,847.62  | 214,788.20  | 41.60 | 36,447.23    | 7.60  |
| Latest Approved ( RCE )               | 110             | 189,723.01 | 216,764.20  | 104,586.01  | 48.20 | 27,041.19    | 14.30 |
| Total ( RCE )                         | 553             | 670,123.40 | 733,611.82  | 319,374.21  | 43.53 | 63488.42     | 9.47  |
| Original Cost of All Projects         |                 |            |             |             |       |              |       |
| Original Cost                         | 553             | 614,127.75 | 733,611.82  | 319,374.21  | 43.50 | 119,484.07   | 19.50 |

## III. (B) Delayed Project cost

| (All Cost/ Expenditure in Rs. crore ) |                 |            |             |             |       |              |       |
|---------------------------------------|-----------------|------------|-------------|-------------|-------|--------------|-------|
| With Respect to                       | No. of Projects | Cost       |             |             |       | Cost overrun |       |
|                                       |                 | Sanctioned | Anticipated | Expenditure | %     | ( Crore)     | %     |
| Original (OCE)                        | 243             | 313,783.31 | 379,159.99  | 200,831.11  | 53.00 | 65,376.68    | 20.80 |
| Latest Approved (RCE)                 | 256             | 301,825.59 | 346,139.65  | 193,862.43  | 56.00 | 44,314.06    | 14.70 |

## IV. Additional Delayed Project cost

| (All Cost/ Expenditure in Rs. crore ) |                 |            |             |             |       |              |       |
|---------------------------------------|-----------------|------------|-------------|-------------|-------|--------------|-------|
| With Respect to                       | No. of Projects | Cost       |             |             |       | Cost overrun |       |
|                                       |                 | Sanctioned | Anticipated | Expenditure | %     | ( Crore)     | %     |
| Latest Approved                       | 32              | 68,734.62  | 78,861.71   | 46,403.89   | 58.80 | 10,127.09    | 14.70 |

### Extent of cost overrun in projects with respect to original schedule

| S.No. | Sector                    | No. of Projects | Total cost (Rs. Cr.) |                  |                  | Projects with cost overrun |               |                  |             |
|-------|---------------------------|-----------------|----------------------|------------------|------------------|----------------------------|---------------|------------------|-------------|
|       |                           |                 | Original             | Anticipated cost | Cost overrun (%) | No .                       | Original cost | Anticipated cost | % Incr Base |
| 1     | Atomic Energy             | 4               | 29,228.3             | 34,066.3         | 16.6             | 2                          | 16,663.0      | 21,501.0         | 29.0        |
| 2     | Civil Aviation            | 5               | 4,123.2              | 5,202.6          | 26.2             | 2                          | 3,215.5       | 4,340.0          | 35.0        |
| 3     | Coal                      | 46              | 26,631.7             | 30,018.7         | 12.7             | 12                         | 13,742.8      | 17,727.6         | 29.0        |
| 4     | Fertilisers               | 6               | 5,317.4              | 5,317.4          | 0.0              | 0                          | 0.0           | 0.0              | 0.0         |
| 5     | Mines                     | 1               | 4,091.5              | 4,401.8          | 7.6              | 1                          | 4,091.5       | 4,401.8          | 7.6         |
| 6     | Steel                     | 12              | 34,591.7             | 55,969.9         | 61.8             | 9                          | 32,641.2      | 54,039.4         | 65.6        |
| 7     | Petrochemicals            | 1               | 5,460.6              | 5,460.6          | 0.0              | 0                          | 0.0           | 0.0              | 0.0         |
| 8     | Petroleum                 | 71              | 153,918.1            | 161,693.9        | 5.1              | 15                         | 21,740.3      | 37,650.3         | 73.2        |
| 9     | Power                     | 83              | 180,012.2            | 186,096.0        | 3.4              | 11                         | 25,563.8      | 32,102.3         | 25.6        |
| 10    | Railways                  | 134             | 65,810.6             | 131,493.8        | 99.8             | 101                        | 36,932.9      | 102,672.9        | 178.0       |
| 11    | Road Transport & Highways | 121             | 59,725.9             | 61,189.3         | 2.5              | 11                         | 3,482.9       | 5,515.4          | 58.4        |
| 12    | Shipping & Ports          | 26              | 18,451.4             | 19,434.9         | 5.3              | 11                         | 6,524.5       | 7,709.1          | 18.2        |
| 13    | Telecommunications        | 40              | 19,713.1             | 20,297.7         | 3.0              | 5                          | 2,114.4       | 2,781.7          | 31.6        |
| 14    | Urban Development         | 2               | 6,509.2              | 11,782.1         | 81.0             | 2                          | 6,509.2       | 11,782.1         | 81.0        |
| 15    | Water Resources           | 1               | 542.9                | 1,187.0          | 118.6            | 1                          | 542.9         | 1,187.0          | 118.6       |
| Total |                           | 553             | 614,127.8            | 733,611.8        | 19.5             | 183                        | 173,764.8     | 303,410.4        | 74.6        |

### Extent of the time overrun in projects with respect to original schedule

| S. No | Sector                    | No. of Projects | Total cost (Rs. Cr.) |                  |                  | Projects with time overrun |               |                  |                |
|-------|---------------------------|-----------------|----------------------|------------------|------------------|----------------------------|---------------|------------------|----------------|
|       |                           |                 | Original             | Anticipated cost | Cost overrun (%) | No.                        | Original cost | Anticipated cost | Range (Months) |
| 1     | Atomic Energy             | 4               | 29,228.3             | 34,066.3         | 16.6             | 3                          | 28,122.0      | 32,960.0         | 11 - 43        |
| 2     | Civil Aviation            | 5               | 4,123.2              | 5,202.6          | 26.2             | 3                          | 3,524.9       | 4,604.3          | 10 - 23        |
| 3     | Coal                      | 46              | 26,631.7             | 30,018.7         | 12.7             | 17                         | 11,824.7      | 14,752.2         | 9 - 48         |
| 4     | Fertilisers               | 6               | 5,317.4              | 5,317.4          | 0.0              | 3                          | 2,241.6       | 2,241.6          | 1 - 8          |
| 5     | Mines                     | 1               | 4,091.5              | 4,401.8          | 7.6              | 0                          | 0.0           | 0.0              | -              |
| 6     | Steel                     | 12              | 34,591.7             | 55,969.9         | 61.8             | 1                          | 8,692.0       | 12,291.0         | 36 - 36        |
| 7     | Petrochemicals            | 1               | 5,460.6              | 5,460.6          | 0.0              | 0                          | 0.0           | 0.0              | -              |
| 8     | Petroleum                 | 71              | 153,918.1            | 161,693.9        | 5.1              | 34                         | 77,116.8      | 87,160.4         | 2 - 120        |
| 9     | Power                     | 83              | 180,012.2            | 186,096.0        | 3.4              | 47                         | 110,291.7     | 116,088.8        | 2 - 90         |
| 10    | Railways                  | 134             | 65,810.6             | 131,493.8        | 99.8             | 27                         | 22,964.0      | 52,749.0         | 2 - 213        |
| 11    | Road Transport & Highways | 121             | 59,725.9             | 61,189.3         | 2.5              | 91                         | 32,618.0      | 33,261.4         | 1 - 106        |
| 12    | Shipping & Ports          | 26              | 18,451.4             | 19,434.9         | 5.3              | 12                         | 8,569.7       | 9,394.8          | 2 - 93         |
| 13    | Telecommunications        | 40              | 19,713.1             | 20,297.7         | 3.0              | 3                          | 880.0         | 860.4            | 17 - 54        |
| 14    | Urban Development         | 2               | 6,509.2              | 11,782.1         | 81.0             | 1                          | 6,395.0       | 11,609.0         | 15 - 15        |
| 15    | Water Resources           | 1               | 542.9                | 1,187.0          | 118.6            | 1                          | 542.9         | 1,187.0          | 60 - 60        |
| Total |                           | 553             | 614,127.8            | 733,611.8        | 19.5             | 243                        | 313,783.3     | 379,160.0        |                |

### Extent of time & cost overrun in projects with respect to original schedule

| S No. | Sector                    | No. of projects | Total Cost (Rs. Cr.) |                  |                 | Projects with time & cost overrun |           |                  |                |
|-------|---------------------------|-----------------|----------------------|------------------|-----------------|-----------------------------------|-----------|------------------|----------------|
|       |                           |                 | Original             | Anticipated Cost | Cost overrun(%) | No.                               | Original  | Anticipated cost | Range (Months) |
| 1     | Atomic Energy             | 4               | 29,228.29            | 34,066.29        | 16.55           | 2                                 | 16,663.00 | 21,501.00        | 16- 43         |
| 2     | Civil Aviation            | 5               | 4,123.24             | 5,202.62         | 26.18           | 2                                 | 3,215.51  | 4,340.00         | 10- 11         |
| 3     | Coal                      | 46              | 26,631.65            | 30,018.68        | 12.72           | 7                                 | 6,813.24  | 10,338.47        | 9- 48          |
| 4     | Fertilisers               | 6               | 5,317.41             | 5,317.41         | 0.00            | 0                                 | 0.00      | 0.00             | 0- 0           |
| 5     | Mines                     | 1               | 4,091.51             | 4,401.76         | 7.58            | 1                                 | 4,091.51  | 4,401.76         | 30- 30         |
| 6     | Steel                     | 12              | 34,591.72            | 55,969.91        | 61.80           | 1                                 | 8,692.00  | 12,291.00        | 36- 36         |
| 7     | Petrochemicals            | 1               | 5,460.61             | 5,460.61         | 0.00            | 0                                 | 0.00      | 0.00             | 0- 0           |
| 8     | Petroleum                 | 71              | 153,918.05           | 161,693.92       | 5.05            | 15                                | 21,740.26 | 37,650.31        | 3- 120         |
| 9     | Power                     | 83              | 180,012.22           | 186,095.99       | 3.38            | 10                                | 24,967.32 | 31,154.36        | 3- 90          |
| 10    | Railways                  | 134             | 65,810.63            | 131,493.76       | 99.81           | 20                                | 11,259.02 | 41,392.68        | 12- 213        |
| 11    | Road Transport & Highways | 121             | 59,725.85            | 61,189.26        | 2.45            | 10                                | 2,374.90  | 3,227.40         | 19- 92         |
| 12    | Shipping & Ports          | 26              | 18,451.36            | 19,434.85        | 5.33            | 7                                 | 3,728.52  | 4,751.17         | 6- 93          |
| 13    | Telecommunications        | 40              | 19,713.13            | 20,297.68        | 2.97            | 3                                 | 1,104.24  | 1,256.16         | 17- 23         |
| 14    | Urban Development         | 2               | 6,509.18             | 11,782.08        | 81.01           | 1                                 | 6,395.00  | 11,609.00        | 15- 15         |
| 15    | Water Resources           | 1               | 542.90               | 1,187.00         | 118.64          | 1                                 | 542.90    | 1,187.00         | 60- 60         |
| Total |                           | 553             | 614127.75            | 733611.82        | 19.46           | 80                                | 111587.42 | 185100.31        |                |

## V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore )

| Project                                                      | DOA     | Original |         | Now anticipated |         | Final       |
|--------------------------------------------------------------|---------|----------|---------|-----------------|---------|-------------|
|                                                              |         | Cost     | DOC     | Cost            | DOC     | Expenditure |
| <u>Railways</u>                                              |         |          |         |                 |         |             |
| AJMER-UDAIPUR-CHITTAURGARH (GC),NWR                          | 09/1996 | 262.00   | N.A.    | 567.23          | N.A.    | 548.54      |
| <u>Road Transport &amp; Highways</u>                         |         |          |         |                 |         |             |
| AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2           | 12/2003 | 193.00   | 10/2008 | 193.00          | 09/2011 | 338.70      |
| MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 | 03/2005 | 359.00   | 03/2009 | 359.00          | 08/2011 | 870.60      |
| <u>Power</u>                                                 |         |          |         |                 |         |             |
| EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER           | 09/2007 | 262.10   | 09/2010 | 262.10          | 08/2011 | 164.00      |
| <u>Steel</u>                                                 |         |          |         |                 |         |             |
| EXPENSION OF ROURKELA STEEL PLANT                            | 09/2008 | 6,133.00 | 02/2011 | 11,812.00       | 03/2013 | 1,253.17    |
| <u>Telecommunications</u>                                    |         |          |         |                 |         |             |
| NIB-II PROJECT RURAL BROADBAND                               | 12/2007 | 312.86   | 02/2008 | 353.00          | N.A.    | 204.43      |
| <u>Urban Development</u>                                     |         |          |         |                 |         |             |
| DELHI MRTS PHASE-II PROJECT                                  | 08/2005 | 8,676.00 | 06/2010 | 18,894.36       | 06/2011 | 18,304.30   |

## VI. List of projects added

(All Cost in Rs. crore )

| Project | DOA | Original |     | Anticipated |     |
|---------|-----|----------|-----|-------------|-----|
|         |     | Cost     | DOC | Cost        | DOC |

## VII. Milestones (Cumulative due & achieved)

|                      |      |
|----------------------|------|
| Total                | 2291 |
| Achieved up to month | 948  |

## VIII. List of projects reporting additional delays


| Project name                                                                | Cost ( Rs. Crore) |             | DOC reported |            |            | Delay       |
|-----------------------------------------------------------------------------|-------------------|-------------|--------------|------------|------------|-------------|
|                                                                             | Original          | Anticipated | Original     | Last month | This month | (in months) |
| <u>Atomic Energy</u>                                                        |                   |             |              |            |            |             |
| KUDANKULAM APP (NPCIL)<br>NPCIL                                             | 13,171.00         | 15,824.00   | 12/2008      | 03/2012    | 07/2012    | 4           |
| <u>Civil Aviation</u>                                                       |                   |             |              |            |            |             |
| C/o new Airport at<br>Pakyong(Sikkim) Airport AAI                           | 309.40            | 264.29      | 01/2011      | 06/2012    | 12/2012    | 6           |
| <u>Coal</u>                                                                 |                   |             |              |            |            |             |
| BARSINGSAR TPS<br>(2X125MW) (NLC) NLC                                       | 1,114.18          | 1,626.09    | 06/2009      | 08/2011    | 09/2011    | 1           |
| TPS-II EXPANSION (1470MW<br>TO 1970MW) (NLC) NLC                            | 2,030.78          | 2,453.57    | 06/2009      | 03/2012    | 05/2012    | 2           |
| ADRIYALA SHAFT PROJECT<br>SCCL                                              | 212.34            | 779.26      | 03/2013      | 06/2013    | 12/2013    | 6           |
| <u>Steel</u>                                                                |                   |             |              |            |            |             |
| 700TPD ARI SEPARATION<br>UNIT-4 AT OXYGEN PLANT-<br>II, BHILLAI SAIL        | 111.28            | 232.93      | N.A.         | 08/2011    | 10/2011    | 2           |
| <u>Petroleum</u>                                                            |                   |             |              |            |            |             |
| DIESEL HYDRO TREATMENT<br>PROJECT,BRPL DHALIGAON<br>BRPL                    | 1,431.91          | 1,690.13    | 09/2009      | 07/2011    | 08/2011    | 1           |
| MSQ QUALITY UP<br>GRADATION PROJECT AT<br>BONGAIGAON REF IOCL               | 293.60            | 261.75      | 12/2009      | 08/2011    | 09/2011    | 1           |
| REFRIGERATED LPG<br>STORAGE AT JNPT BPCL                                    | 304.40            | 304.40      | 06/2010      | 07/2011    | 09/2011    | 2           |
| KARANPUR MORADABAD-<br>KASHIPUR-RUDRAPUR<br>PIPELINE PROJECT PHASE-<br>GAIL | 238.68            | 204.00      | 01/2012      | 10/2011    | 01/2012    | 3           |
| PARADIP REFINERY<br>PROJECT IOCL                                            | 29,777.00         | 29,777.00   | 11/2012      | 11/2012    | 06/2013    | 7           |
| <u>Power</u>                                                                |                   |             |              |            |            |             |
| CHAMERA,STAGE-III (NHPC)<br>NHPC                                            | 1,405.63          | 1,405.63    | 08/2010      | 10/2011    | 11/2011    | 1           |
| TEHRI PUMPED STORAGE<br>PLANT(1000MW) THDCL                                 | 1,657.00          | 2,978.86    | 07/2010      | 01/2016    | 02/2016    | 1           |
| TRANSMISSION SYSTEM<br>ASSOCIATED WITH<br>PARBATI-III HEP PGCIL             | 557.24            | 639.52      | 01/2010      | 11/2011    | 12/2011    | 1           |

## VIII. List of projects reporting additional delays


| Project name                                                                | Cost ( Rs. Crore) |             | DOC reported |            |            | Delay<br>(in months) |
|-----------------------------------------------------------------------------|-------------------|-------------|--------------|------------|------------|----------------------|
|                                                                             | Original          | Anticipated | Original     | Last month | This month |                      |
| TRANSMISSION SY.<br>ASSOCIATED WITH BARH<br>GENER. PROJECT(P.GR.)<br>PGCIL  | 3,779.46          | 3,725.13    | 09/2009      | 12/2011    | 03/2012    | 3                    |
| CHUTAK HYDRO-ELECTRIC<br>PROJECT (NHPC) NHPC                                | 621.28            | 621.28      | 02/2011      | 11/2011    | 02/2012    | 3                    |
| NORTHERN REGION<br>SYSTEM STRENGTHENING<br>SCHEME-XIII PGCIL                | 317.69            | 317.69      | 11/2011      | 11/2011    | 03/2012    | 4                    |
| PARBATI HEP (NHPC) II<br>NHPC                                               | 3,919.59          | 3,919.59    | 09/2009      | 07/2014    | 12/2014    | 5                    |
| <u>Railways</u>                                                             |                   |             |              |            |            |                      |
| RAIL-CUM-ROAD BRIDGE<br>OVER RIVER<br>BRAHAMAPUTRA BRIDG<br>NEFR            | 1,000.00          | 3,230.01    | 04/2008      | 03/2014    | 12/2014    | 9                    |
| SEVOK RANGPO, NEFR<br>NEFR                                                  | 1,339.48          | 3,380.57    | 12/2015      | 03/2015    | 12/2015    | 9                    |
| <u>Road Transport &amp; Highways</u>                                        |                   |             |              |            |            |                      |
| GAGODHAR-<br>GARAMORE(PK-IV,NH15) KM<br>245 TO 281.3 AND 308 TO<br>254 NHAI | 412.78            | 479.54      | 11/2007      | 08/2011    | 09/2011    | 1                    |
| AYODHYA - LUCKNOW<br>(LMNHP-II) KM.93.075 TO<br>KM.45, NH-28 NHAI           | 217.00            | 217.00      | 10/2008      | 08/2011    | 09/2011    | 1                    |
| MADURAI-ARUPKOTTAI-<br>TUTICORIN, KM.138.8 TO<br>KM.264.5, NH-45 B NHAI     | 629.00            | 629.00      | 11/2010      | 08/2011    | 09/2011    | 1                    |
| TRICHY - DINDIGUAL NH-45<br>NHAI                                            | 576.00            | 576.00      | 07/2010      | 08/2011    | 09/2011    | 1                    |
| PONDICHERY - TINDIVANAU<br>NH-66 NHAI                                       | 285.00            | 285.00      | 07/2010      | 08/2011    | 09/2011    | 1                    |
| BALASORE BHADRAK<br>(REVIVED) KM 136.5 - 199.14<br>NH-5 NHAI                | 228.70            | 228.70      | 02/2004      | 08/2011    | 09/2011    | 1                    |
| SUNAKHALA-GANJAM (GQ)<br>KM.338-KM.284 (NH-5) NHAI                          | 225.00            | 241.53      | 04/2004      | 10/2011    | 12/2011    | 2                    |
| JHANSI TO LALITPUR, NH-26<br>NHAI                                           | 276.09            | 276.09      | 09/2009      | 08/2011    | 10/2011    | 2                    |
| VIJAYAPUR TO PATHANKOT<br>(J&K) NH-1A KM.16.35 TO<br>KM.50.00 NHAI          | 193.09            | 166.30      | 03/2008      | 09/2011    | 12/2011    | 3                    |
| VIJAYAPUR TO PATHANKOT<br>(NS-35/J&K) NH-1A KM.50 TO<br>KM.80 NHAI          | 166.27            | 193.10      | 03/2008      | 09/2011    | 12/2011    | 3                    |
| KOTWA TO DEWAPUR(10<br>LMNHP),NH-28 PHASE-II,<br>KM.440 TO KM.402 NHAI      | 240.00            | 240.00      | 10/2008      | 12/2011    | 03/2012    | 3                    |



## Trend and Graphical Analysis of All Projects

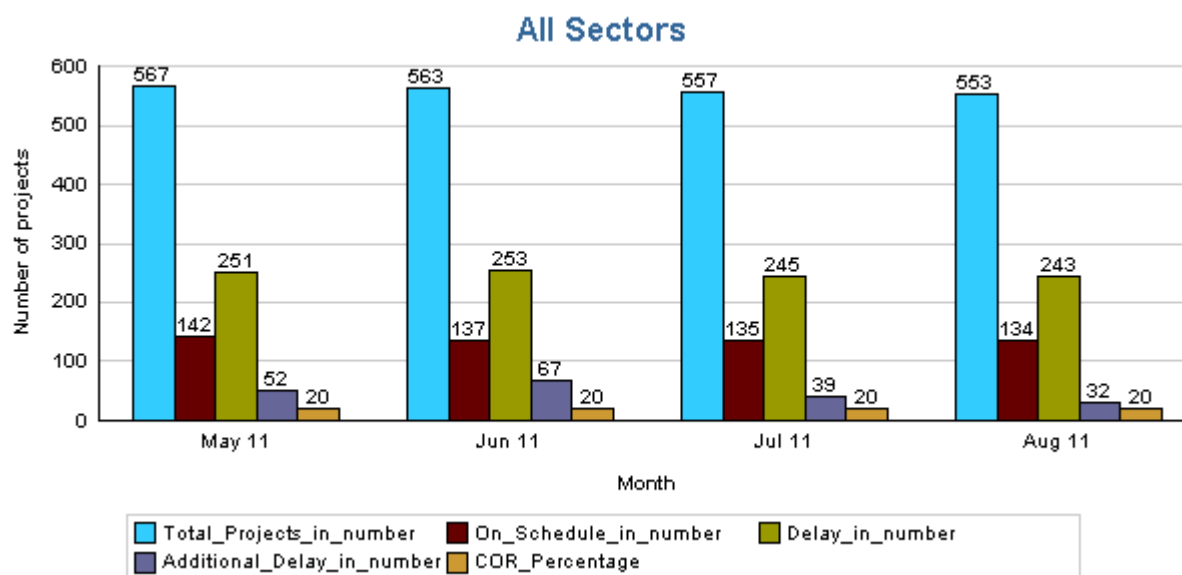


### All Sectors Break-up of 243 Delayed projects in August 2011

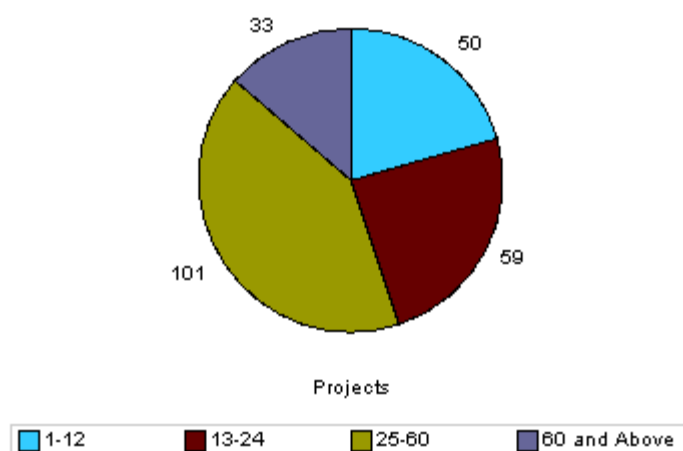


## Trend and Graphical Analysis

### Urban Development Sector

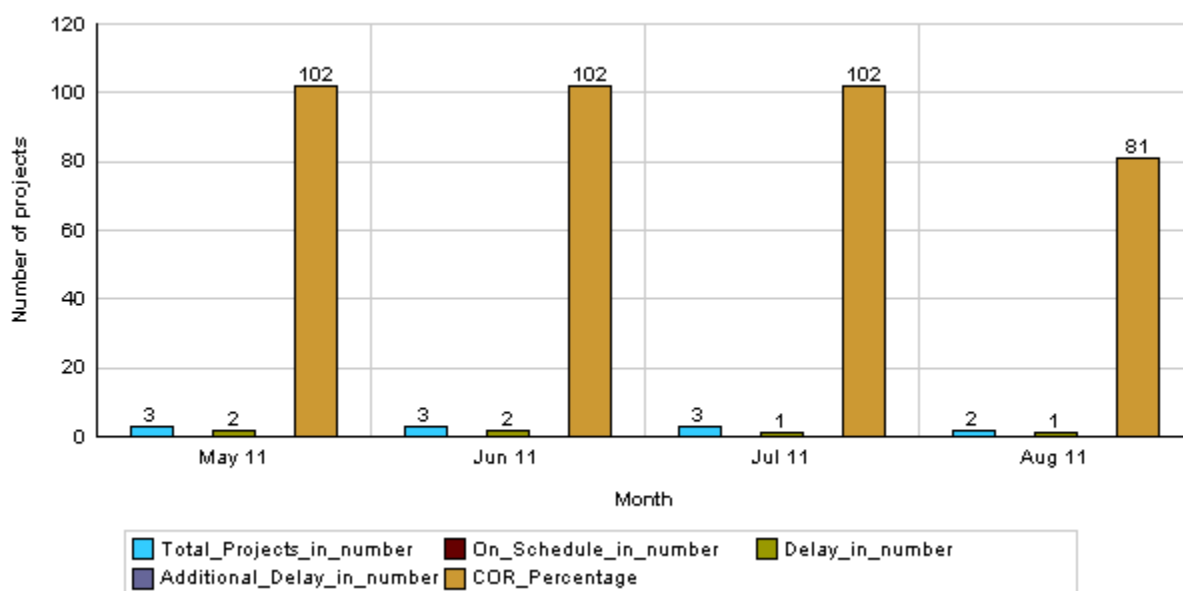


**Urban Development Sector Sector Break-up of 1 Delayed projects in August 2011**

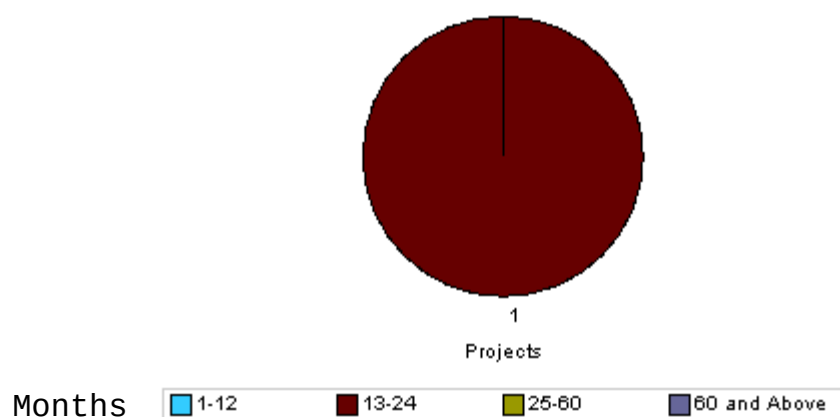


## Trend and Graphical Analysis


### Telecommunications Sector

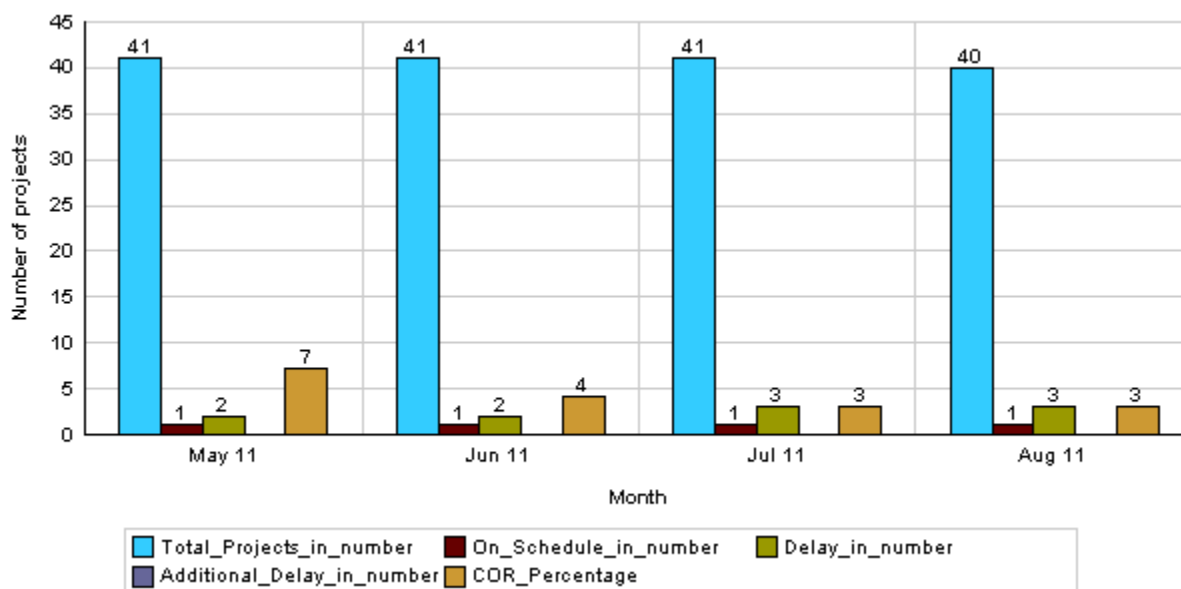


**Telecommunications Sector Break-up of 3 Delayed projects in August 2011**

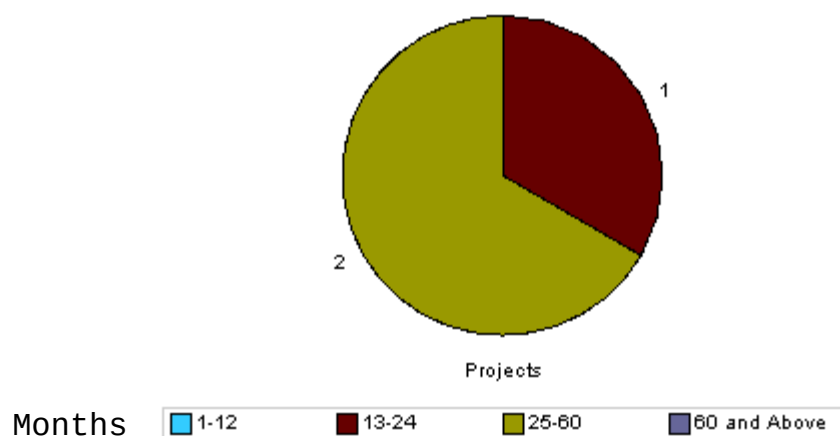


## Trend and Graphical Analysis Shipping and Ports Sector

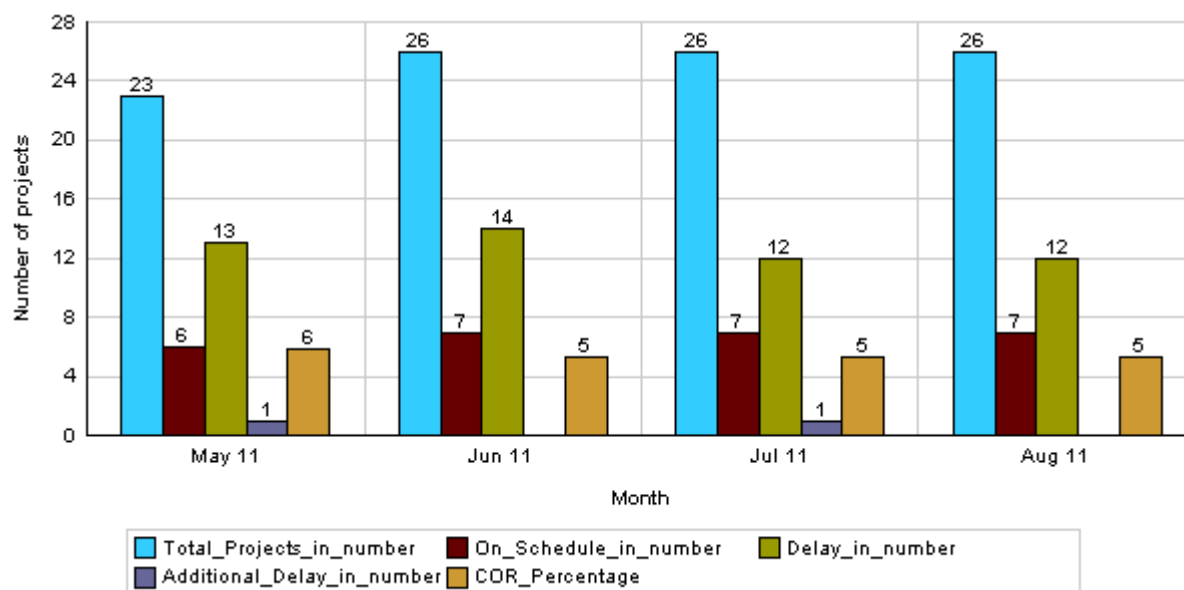


**Sector Break-up of 12 Delayed projects in August 2011**

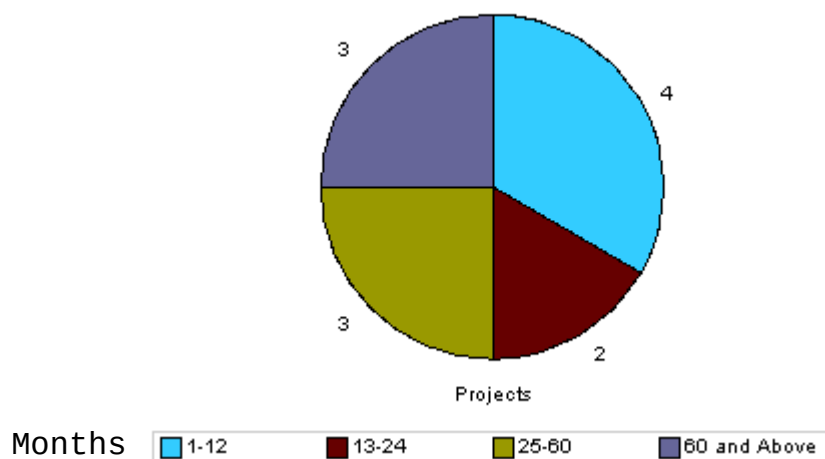

## Trend and Graphical Analysis Road Transport and Highways Sector

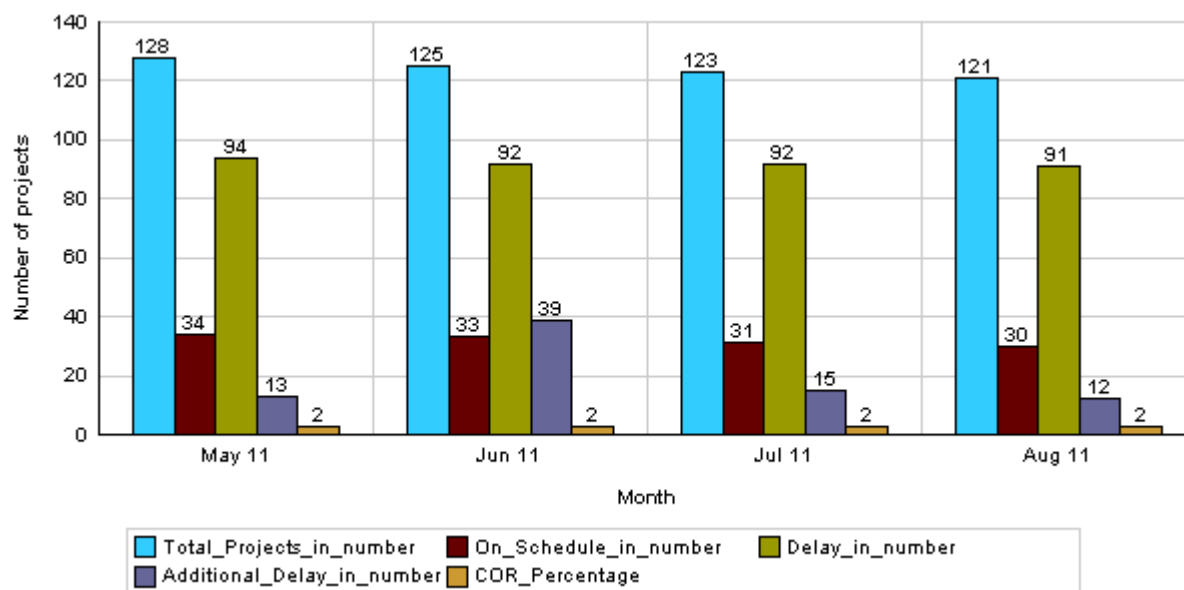


**Sector Break-up of 91 Delayed projects in August 2011**

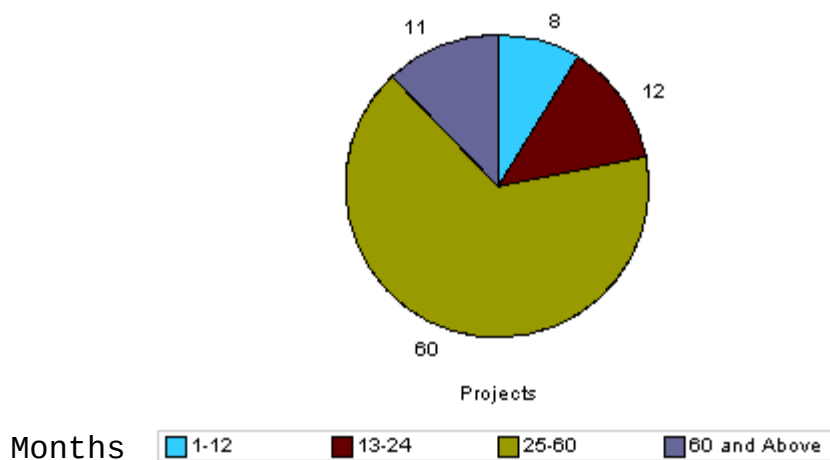


## Trend and Graphical Analysis

### Railways Sector

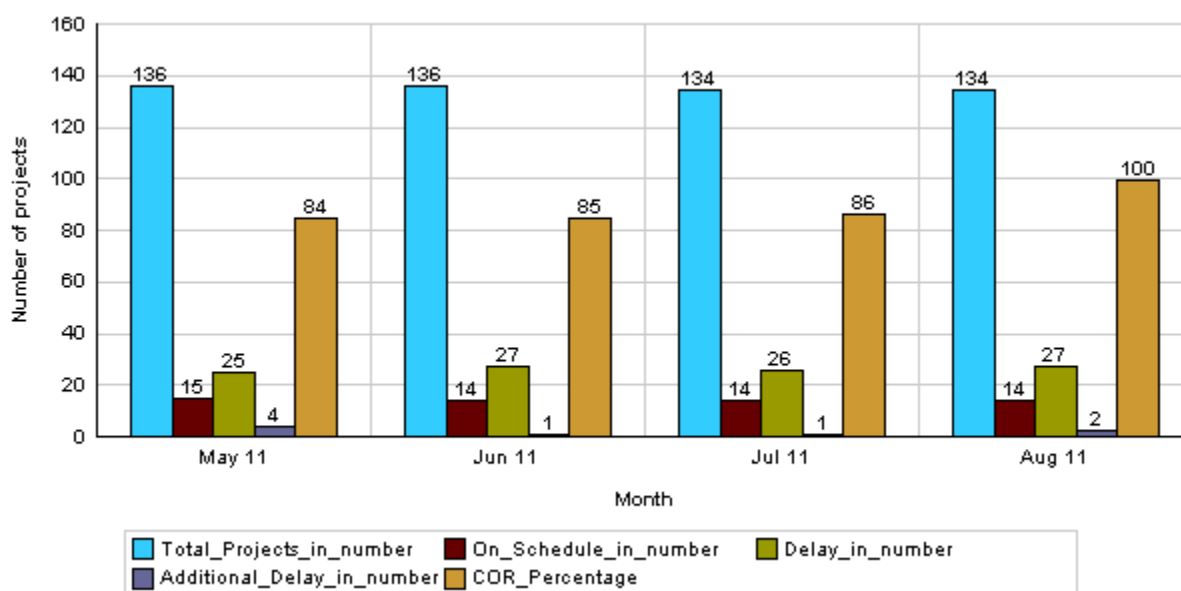


**Railways Sector Break-up of 27 Delayed projects in August 2011**

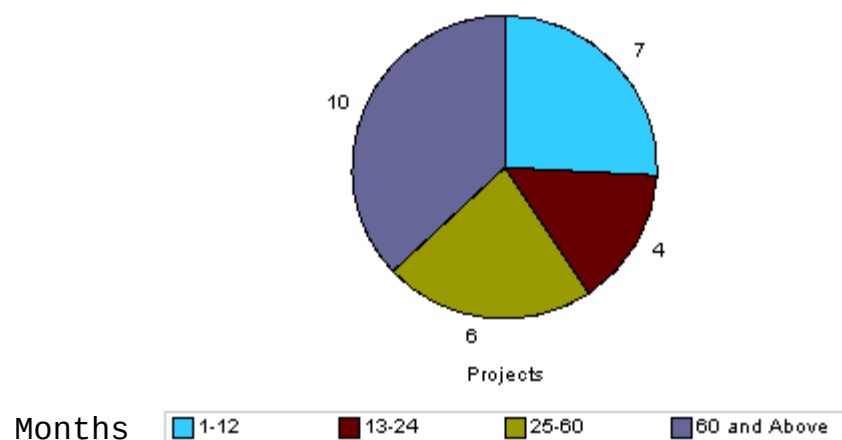


## Trend and Graphical Analysis

### Power Sector

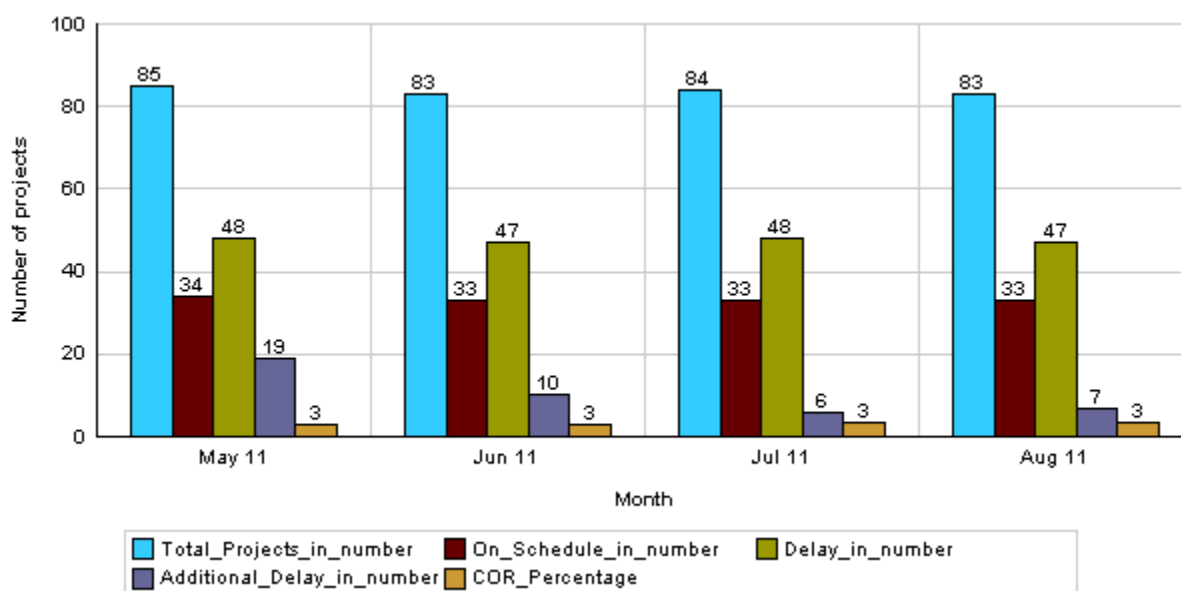


### **Power Sector Sector Break-up of 47 Delayed projects in August 2011**

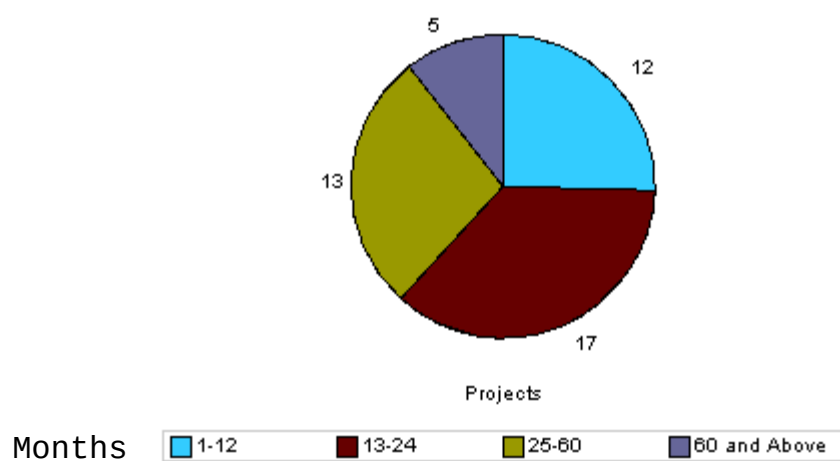


## Trend and Graphical Analysis

### Petroleum Sector

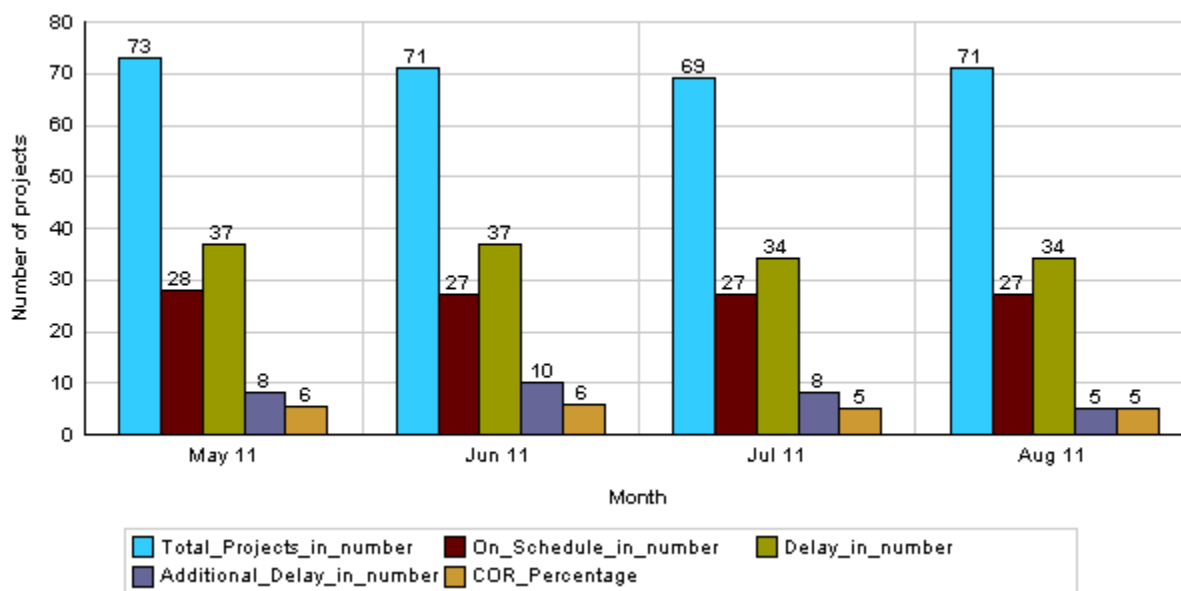


**Petroleum Sector Sector Break-up of 34 Delayed projects in August 2011**

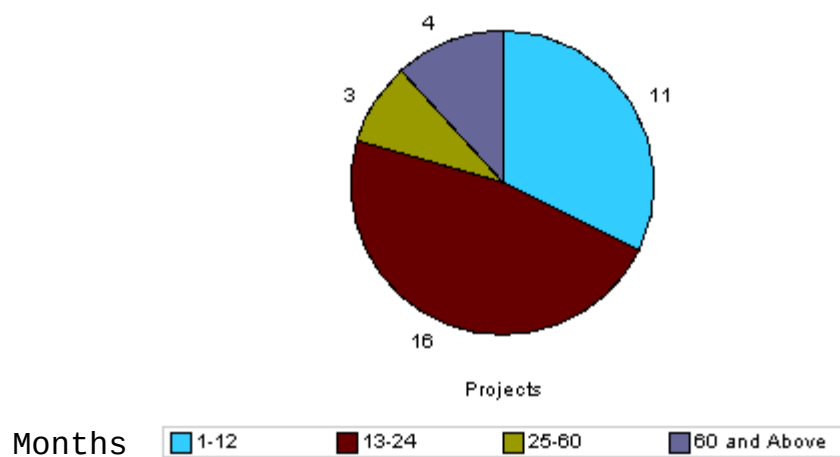


## Trend and Graphical Analysis

### Steel Sector

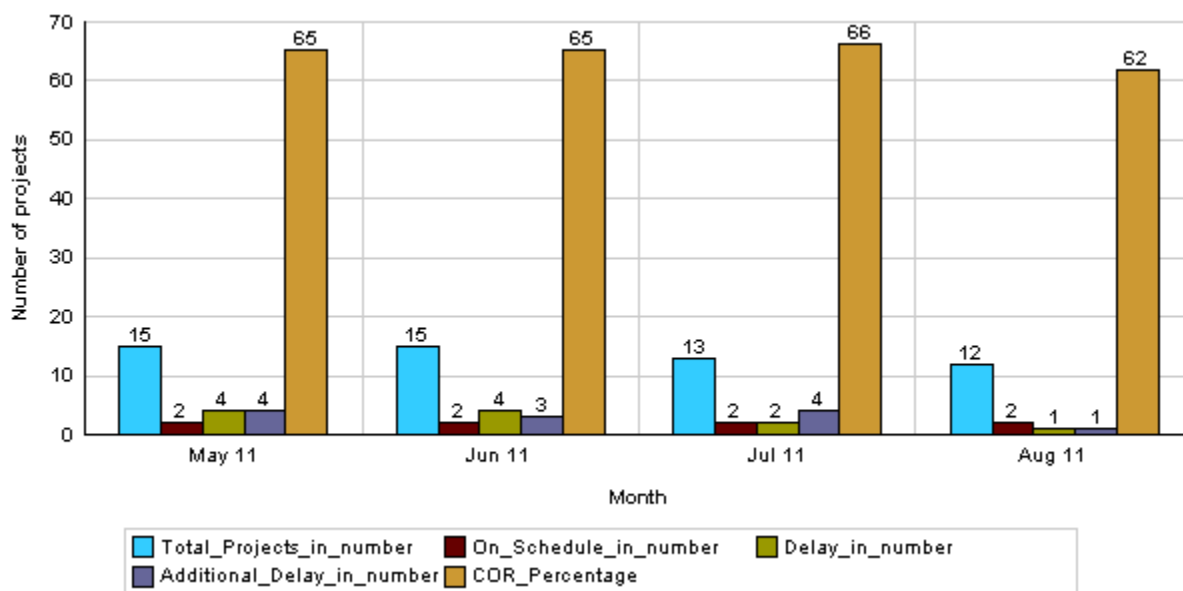


### Steel Sector Break-up of 1 Delayed projects in August 2011

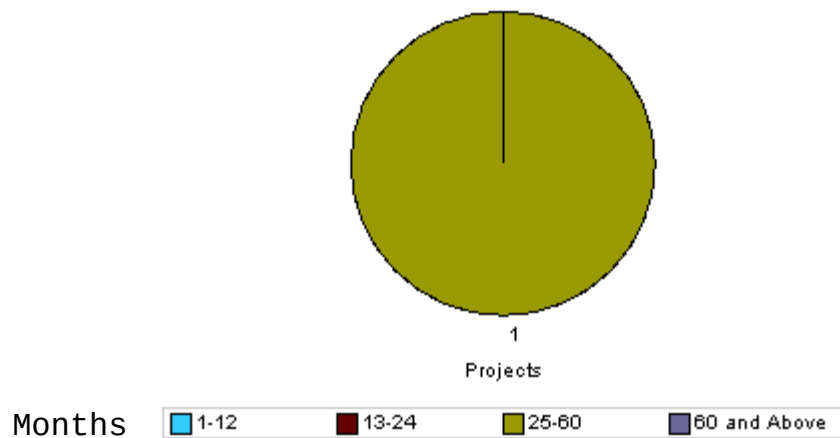


## Trend and Graphical Analysis

### Fertilisers Sector

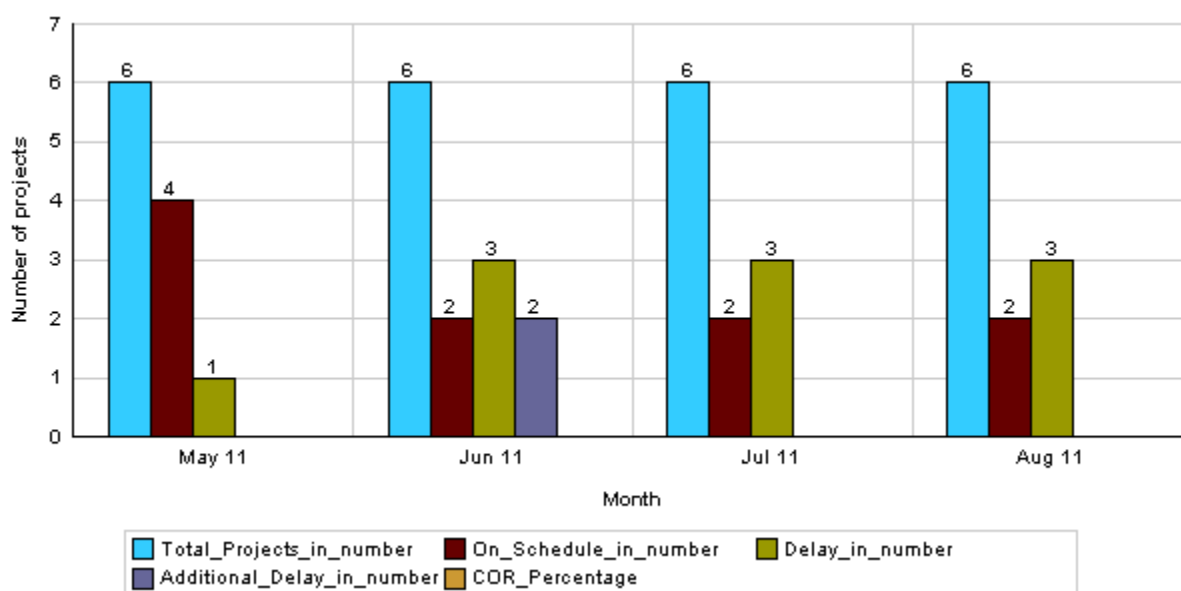


### Fertilisers Sector Sector Break-up of 3 Delayed projects in August 2011

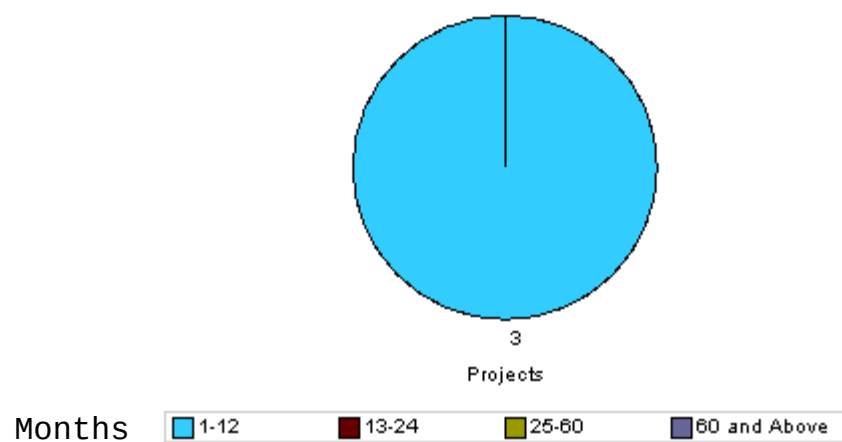


## Trend and Graphical Analysis

### Coal Sector

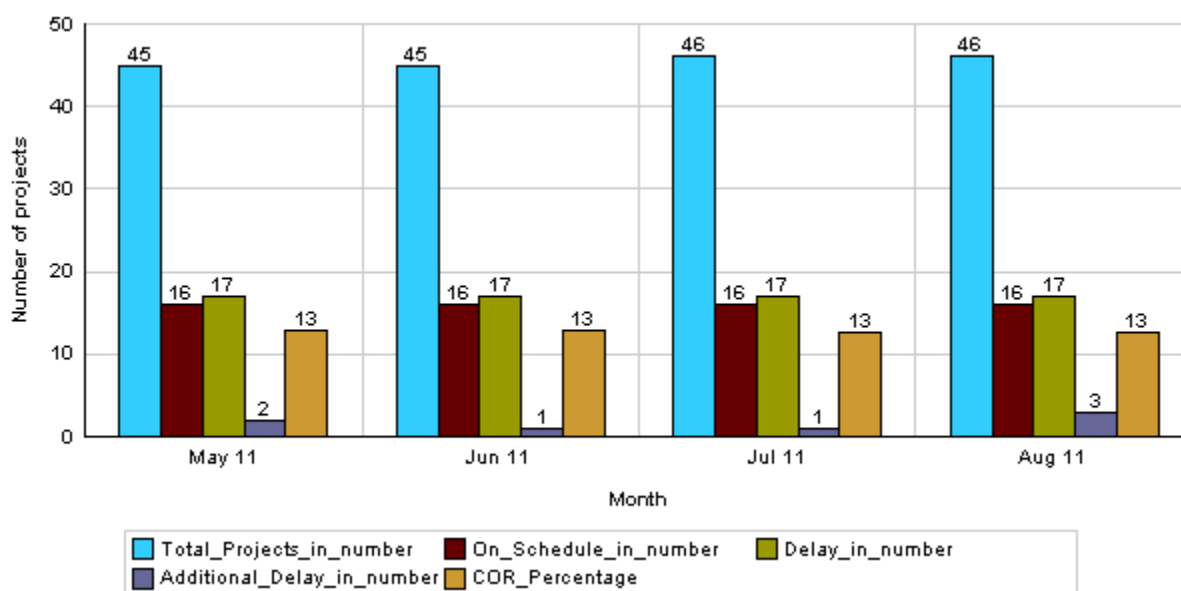


**Coal Sector Sector Break-up of 17 Delayed projects in August 2011**

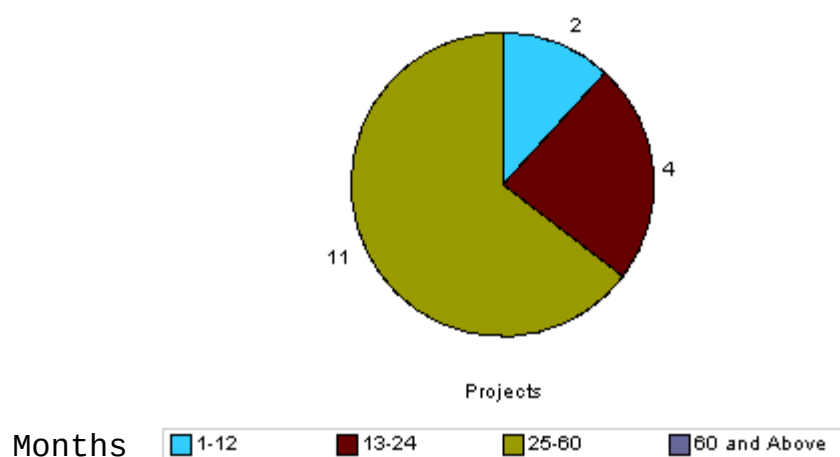


## Trend and Graphical Analysis

### Civil Aviation Sector

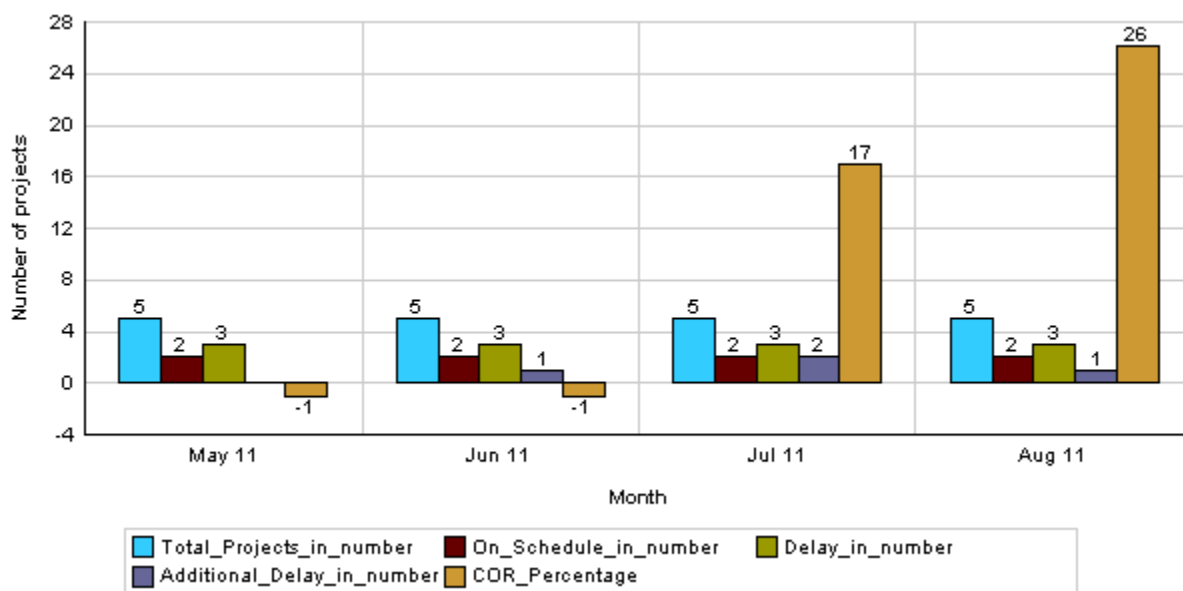


**Civil Aviation Sector Sector Break-up of 3 Delayed projects in August 2011**

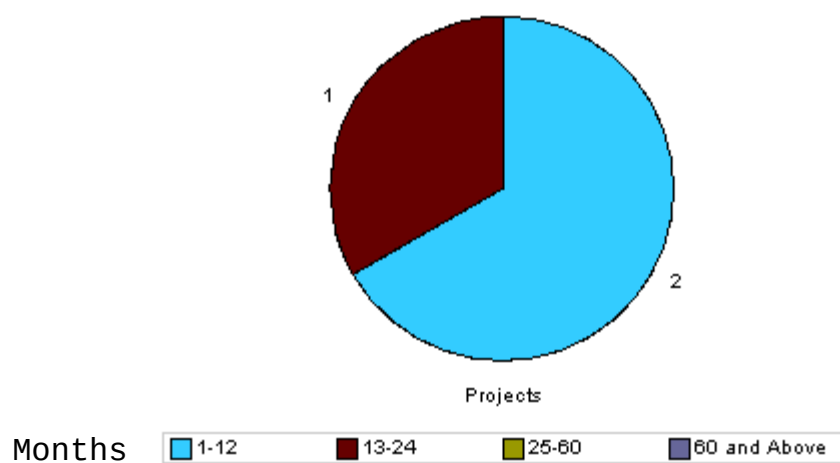


## Trend and Graphical Analysis

### Atomic Energy Sector

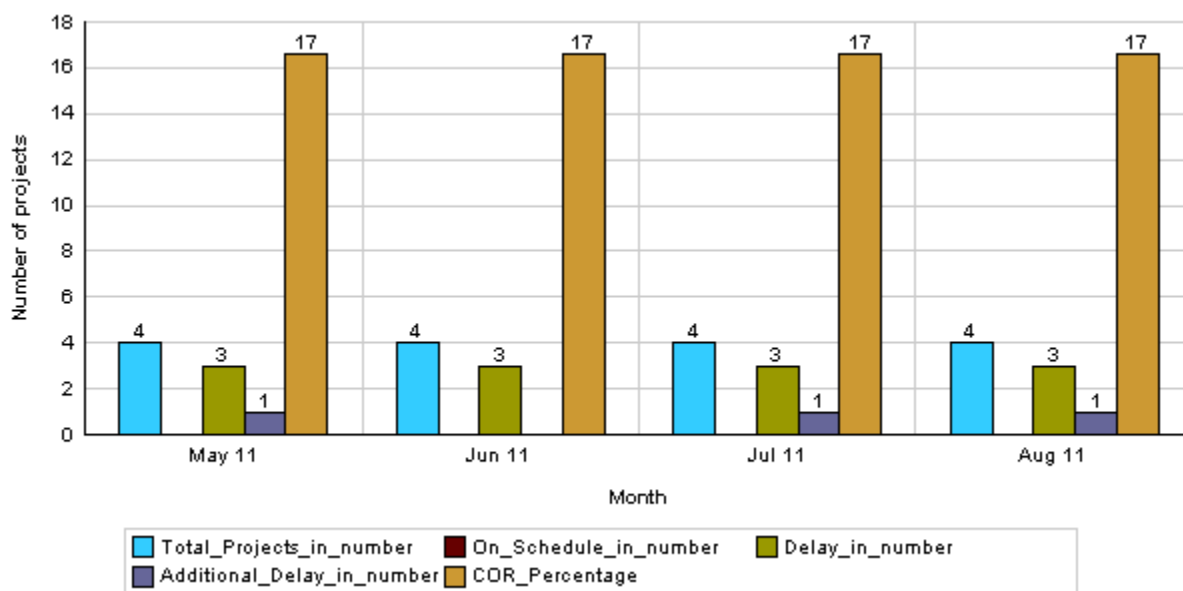

### Atomic Energy Sector Sector Break-up of 3 Delayed projects in August 2011

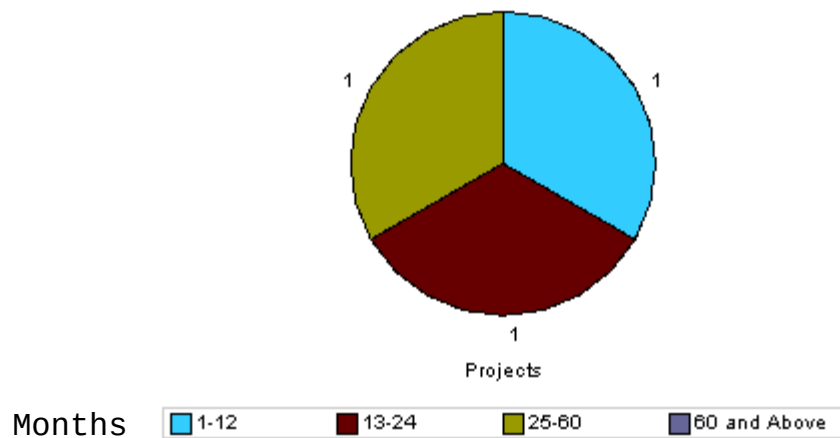

## Sectorwise analysis of projects

| Sector                    | Number of projects | Cost (Rs. Crore)  |                   |                   |
|---------------------------|--------------------|-------------------|-------------------|-------------------|
|                           |                    | Original          | Latest            | Anticipated       |
| Atomic Energy             | 4                  | 29,228.29         | 29,228.29         | 34,066.29         |
| Civil Aviation            | 5                  | 4,123.24          | 4,865.24          | 5,202.62          |
| Coal                      | 46                 | 26,631.65         | 27,880.90         | 30,018.68         |
| Fertilisers               | 6                  | 5,317.41          | 5,317.41          | 5,317.41          |
| Mines                     | 1                  | 4,091.51          | 4,401.76          | 4,401.76          |
| Steel                     | 12                 | 34,591.72         | 55,677.65         | 55,969.91         |
| Petrochemicals            | 1                  | 5,460.61          | 5,460.61          | 5,460.61          |
| Petroleum                 | 71                 | 153,918.05        | 165,567.75        | 161,693.92        |
| Power                     | 83                 | 180,012.22        | 182,573.64        | 186,095.99        |
| Railways                  | 134                | 65,810.63         | 83,737.39         | 131,493.76        |
| Road Transport & Highways | 121                | 59,725.85         | 59,725.85         | 61,189.26         |
| Shipping & Ports          | 26                 | 18,451.36         | 18,830.67         | 19,434.85         |
| Telecommunications        | 40                 | 19,713.13         | 19,745.26         | 20,297.68         |
| Urban Development         | 2                  | 6,509.18          | 6,568.08          | 11,782.08         |
| Water Resources           | 1                  | 542.90            | 542.90            | 1,187.00          |
| <b>Grand total</b>        | <b>553</b>         | <b>614,127.75</b> | <b>670,123.40</b> | <b>733,611.82</b> |

(Aug,2011)

| S.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
|      | <u>Atomic Energy</u>                                                                     |                  |                         |                  |                   |                       |             |                                             |                            |
| 1    | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu         | 09/2003          | 3,492.00 -              | 5,677.00         | 3,178.67          | 09/2010 -             | 01/2012     | 16(O)                                       | 8/80                       |
| 2    | URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh      | 09/2007          | 1,106.29 -              | 1,106.29         | 1,000.70          | - 04/2011             | 04/2012     | 12(R3)                                      | 0/1                        |
| 3    | KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu                                     | 12/2001          | 13,171.00 -             | 15,824.00        | 13,994.00         | 12/2008 -             | 07/2012     | 43(O)                                       | 61/119                     |
| 4    | KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat                           | 10/2009          | 11,459.00 -             | 11,459.00        | 959.00            | 12/2015 05/2016       | 11/2016     | 6(R1)                                       | 0/70                       |
|      | <b>Total</b>                                                                             |                  | 29,228.29 -             | 34,066.29        | 19,132.37         |                       |             |                                             | 69/270                     |
|      | <u>Civil Aviation</u>                                                                    |                  |                         |                  |                   |                       |             |                                             |                            |
| 5    | D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu            | 08/2008          | 1,273.00 2,015.00       | 2,015.00         | 928.46            | 01/2011 -             | 12/2011     | 11(O)                                       | 0/0                        |
| 6    | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal           | 08/2008          | 1,942.51 -              | 2,325.00         | 1,333.00          | 05/2011 -             | 03/2012     | 10(O)                                       | 0/0                        |
| 7    | Construction of New International Terminal Building - [N04000069]AAI,Goa                 | 05/2010          | 204.73 -                | 204.73           | 39.57             | 05/2012 -             | 05/2012     | 0(O)                                        | 0/0                        |
| 8    | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim                       | 01/2009          | 309.40 -                | 264.29           | 147.16            | 01/2011 -             | 12/2012     | 23(O)                                       | 0/0                        |
| 9    | GAGAN PROJECT - [N04000065]AAI,Multi State                                               | 09/2008          | 393.60 -                | 393.60           | 323.65            | 06/2013 -             | 06/2013     | 0(O)                                        | 0/0                        |
|      | <b>Total</b>                                                                             |                  | 4,123.24 -              | 5,202.62         | 2,771.84          |                       |             |                                             | 0/0                        |
|      | <u>Coal</u>                                                                              |                  |                         |                  |                   |                       |             |                                             |                            |
| 10   | BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan                                | 12/2004          | 1,114.18 1,626.09       | 1,626.09         | 1,640.49          | 06/2009 -             | 09/2011     | 27(O)                                       | 59/26                      |
| 11   | KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa                             | 01/2005          | 302.96 -                | 302.96           | 83.72             | 03/2010 -             | 03/2012     | 24(O)                                       | 9/11                       |
| 12   | ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]JCL,Jharkhand                                  | 04/2006          | 471.66 341.63           | 341.63           | 101.43            | 03/2011 03/2012       | 03/2012     | 0(R3)                                       | 0/2                        |
| 13   | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh | 10/2007          | 259.40 -                | 259.40           | 1.51              | 03/2012 03/2012       | 03/2012     | 0(R3)                                       | 0/1                        |
| 14   | BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa                             | 12/2007          | 172.08 -                | 172.08           | 93.78             | - -                   | 03/2012     | -                                           | 4/4                        |
| 15   | ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Orissa                            | 08/2008          | 207.28 -                | 207.28           | 67.14             | - -                   | 03/2012     | -                                           | 5/7                        |

| S.No | Project                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                       |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                     | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 16   | RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh           | 12/2009          | 418.97<br>-             | 418.97           | 77.15             | 03/2012<br>-          | 03/2012     | 0(O)                                        | 28/27                      |
| 17   | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh    | 03/2010          | 181.19<br>-             | 181.19           | 21.20             | 03/2012<br>-          | 03/2012     | 0(O)                                        | 10/34                      |
| 18   | TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu | 10/2004          | 2,030.78<br>2,453.57    | 2,453.57         | 2,249.78          | 06/2009<br>-          | 05/2012     | 35(O)                                       | 60/24                      |
| 19   | TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu           | 05/2008          | 4,904.54<br>4,909.54    | 4,909.54         | 1,973.76          | -<br>-                | 10/2012     | -                                           | 0/6                        |
| 20   | KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhy Pradesh              | 05/2006          | 789.88<br>741.62        | 741.62           | 139.06            | 03/2010<br>03/2013    | 03/2013     | 0(R3)                                       | 0/2                        |
| 21   | KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh       | 06/2006          | 737.65<br>-             | 1,188.31         | 569.71            | -<br>-                | 03/2013     | -                                           | 0/8                        |
| 22   | KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa                   | 12/2007          | 457.77<br>-             | 457.77           | 105.37            | -<br>-                | 03/2013     | -                                           | 6/11                       |
| 23   | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Orissa            | 11/2008          | 475.93<br>-             | 479.63           | 66.93             | -<br>-                | 03/2013     | -                                           | 5/7                        |
| 24   | Purnadih OCP - [N06000085]JCL,Jharkhandd                              | 07/2008          | 210.98<br>-             | 210.98           | 24.25             | 03/2013<br>-          | 03/2013     | 0(O)                                        | 0/2                        |
| 25   | ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh               | 09/2006          | 212.34<br>779.26        | 779.26           | 196.17            | 03/2013<br>09/2012    | 12/2013     | 15(R3)                                      | 2/22                       |
| 26   | GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh     | 07/2005          | 1,667.55<br>-           | 2,675.67         | 1,258.36          | 03/2010<br>-          | 03/2014     | 48(O)                                       | 3/15                       |
| 27   | DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh  | 07/2005          | 1,268.53<br>-           | 1,943.66         | 1,070.26          | 03/2010<br>-          | 03/2014     | 48(O)                                       | 2/13                       |
| 28   | BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State                | 11/2006          | 168.97<br>-             | 168.97           | 183.63            | 03/2014<br>-          | 03/2014     | 0(O)                                        | 1/2                        |
| 29   | CHURCHA RO UG (1.35MTY) - [N06000046]SECL,Chhatisgarh                 | 06/2008          | 462.35<br>-             | 462.35           | 253.86            | -<br>-                | 03/2014     | -                                           | 0/4                        |
| 30   | RAJMAHAL OC EXP. - [N06000056]ECL,Multi State                         | 02/2006          | 50.08<br>153.82         | 153.82           | 19.49             | 03/2011<br>-          | 03/2014     | 36(O)                                       | 0/3                        |
| 31   | KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh            | 07/2008          | 178.44<br>-             | 178.44           | -                 | 03/2014<br>-          | 03/2014     | 0(O)                                        | 0/1                        |
| 32   | MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh        | 11/2009          | 321.42<br>-             | 321.50           | 203.09            | -<br>-                | 03/2014     | -                                           | 0/5                        |
| 33   | Churi Benti UG - [N06000083]JCL,Jharkhandd                            | 06/2007          | 163.51<br>-             | 163.51           | 33.57             | 03/2011<br>03/2012    | 03/2014     | 24(R3)                                      | 0/2                        |
| 34   | North Urimari OCP - [N06000084]JCL,Jharkhandd                         | 12/2007          | 179.87<br>-             | 179.87           | 66.45             | 03/2012<br>03/2012    | 03/2014     | 24(R3)                                      | 0/2                        |
| 35   | Tapin OCP - [N06000086]JCL,Jharkhandd                                 | 08/2008          | 264.68<br>-             | 264.68           | 76.05             | 03/2012<br>03/2013    | 03/2014     | 12(R3)                                      | 0/2                        |
| 36   | KARMA OCP - [N06000088]JCL,Jharkhandd                                 | 06/2009          | 162.46<br>-             | 162.46           | 26.19             | 03/2014<br>-          | 03/2014     | 0(O)                                        | 0/0                        |
| 37   | PENGANGA OC - [N06000066]WCL,Orissa                                   | 10/2008          | 339.77<br>-             | 339.77           | 0.65              | -<br>-                | 10/2014     | -                                           | 1/1                        |

| S.No               | Project                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|--------------------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|                    |                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1                  | 2                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 38                 | BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh                         | 06/2006          | 746.04<br>535.10        | 535.10           | 139.84            | 03/2012<br>-          | 03/2015     | 36(O)                                       | 0/2                        |
| 39                 | JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal                               | 11/2006          | 287.18<br>-             | 287.17           | -                 | 03/2011<br>-          | 03/2015     | 48(O)                                       | 1/5                        |
| 40                 | GOPAL PRASAD OCP - [N06000042]MCL,Orissa                                          | 02/2008          | 395.87<br>-             | 395.87           | 58.42             | -<br>-                | 03/2015     | -                                           | 2/12                       |
| 41                 | PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh                                 | 07/2008          | 448.32<br>-             | 448.32           | -                 | 03/2015<br>-          | 03/2015     | 0(O)                                        | 0/1                        |
| 42                 | KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State                                  | 12/2008          | 453.63<br>-             | 453.63           | 67.70             | 12/2012<br>-          | 03/2015     | 27(O)                                       | 11/44                      |
| 43                 | Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh                             | 09/2008          | 203.82<br>-             | 203.82           | -                 | 03/2015<br>-          | 03/2015     | 0(O)                                        | 0/1                        |
| 44                 | JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh                          | 09/2008          | 152.43<br>-             | 152.43           | -                 | 03/2015<br>-          | 03/2015     | 0(O)                                        | 0/1                        |
| 45                 | RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal                                     | 03/2010          | 209.78<br>-             | 209.78           | 18.17             | 03/2015<br>-          | 03/2015     | 0(O)                                        | 4/31                       |
| 46                 | Kistaram OCP - [N06000089]SCCL,Andhra Pradesh                                     | 11/2010          | 242.29<br>-             | 242.29           | -                 | 03/2015<br>-          | 03/2015     | 0(O)                                        | 0/28                       |
| 47                 | AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh                         | 05/2006          | 1,352.04<br>1,143.54    | 1,143.54         | 206.07            | 03/2014<br>-          | 03/2016     | 24(O)                                       | 1/2                        |
| 48                 | MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd                                       | 07/2006          | 469.78<br>706.40        | 706.40           | 16.21             | 07/2012<br>03/2014    | 03/2016     | 24(R3)                                      | 0/2                        |
| 49                 | TALABIRA OCP - [N06000043]MCL,Orissa                                              | 03/2008          | 447.72<br>-             | 447.72           | 35.20             | -<br>-                | 03/2016     | -                                           | 1/12                       |
| 50                 | AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh            | 11/2009          | 198.59<br>-             | 198.59           | 89.33             | 03/2016<br>-          | 03/2016     | 0(O)                                        | 0/1                        |
| 51                 | Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd                                      | 12/2009          | 510.85<br>-             | 510.85           | 290.44            | 03/2016<br>-          | 03/2016     | 0(O)                                        | 0/2                        |
| 52                 | BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa                          | 12/2007          | 490.00<br>-             | 490.10           | 88.19             | -<br>-                | 03/2017     | -                                           | 6/12                       |
| 53                 | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh | 06/2011          | 1,131.28<br>1,131.28    | 1,131.28         | -                 | 03/2018<br>-          | 03/2018     | 0(O)                                        | 0/0                        |
| 54                 | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh                   | 10/2006          | 249.03<br>-             | 249.03           | 40.04             | 03/2012<br>03/2012    | -           | -                                           | 13/42                      |
| 55                 | JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh                           | 03/2013          | 467.78<br>-             | 467.78           | 12.31             | 03/2013<br>03/2013    | 03/2013     | 0(R3)                                       | 0/83                       |
| Total              |                                                                                   |                  | 26,631.65<br>-          | 30,018.68        | 11,664.97         |                       |             |                                             | 234/525                    |
| <b>Fertilisers</b> |                                                                                   |                  |                         |                  |                   |                       |             |                                             |                            |
| 56                 | THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana                              | 01/2009          | 488.75<br>-             | 488.75           | 168.14            | -<br>11/2011          | 11/2011     | 0(R3)                                       | 2/22                       |
| 57                 | CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh         | 09/2008          | 325.00<br>-             | 325.00           | 84.31             | 07/2011<br>-          | 11/2011     | 4(O)                                        | 0/0                        |

| S.No         | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|--------------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|              |                                                                                              |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1            | 2                                                                                            | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 58           | CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL, Madhya Pradesh          | 09/2008          | 438.00<br>-             | 438.00           | 105.79            | 07/2011<br>-          | 03/2012     | 8(O)                                        | 0/0                        |
| 59           | PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL, Haryana                | 01/2010          | 1,292.84<br>-           | 1,292.84         | 175.88            | 01/2013<br>-          | 01/2013     | 0(O)                                        | 0/5                        |
| 60           | BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL, Punjab                 | 01/2010          | 1,294.19<br>-           | 1,294.19         | 177.02            | 01/2013<br>-          | 01/2013     | 0(O)                                        | 0/5                        |
| 61           | NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL, Punjab                            | 01/2010          | 1,478.63<br>-           | 1,478.63         | 223.57            | 12/2012<br>-          | 01/2013     | 1(O)                                        | 0/8                        |
| Total        |                                                                                              |                  | 5,317.41<br>-           | 5,317.41         | 934.71            |                       |             |                                             | 2/40                       |
| <u>Mines</u> |                                                                                              |                  |                         |                  |                   |                       |             |                                             |                            |
| 62           | SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa     | 10/2004          | 4,091.51<br>4,401.76    | 4,401.76         | 4,096.00          | 12/2008<br>01/2011    | 06/2011     | 5(R3)                                       | 117/110                    |
| Total        |                                                                                              |                  | 4,091.51<br>-           | 4,401.76         | 4,096.00          |                       |             |                                             | 117/110                    |
| <u>Steel</u> |                                                                                              |                  |                         |                  |                   |                       |             |                                             |                            |
| 63           | 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Chhatisgarh      | 07/2007          | 111.28<br>232.93        | 232.93           | 168.27            | -<br>-                | 10/2011     | -                                           | 0/1                        |
| 64           | 330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh                      | 07/2007          | 260.00<br>-             | 350.00           | 220.10            | -<br>-                | 11/2011     | -                                           | 1/2                        |
| 65           | EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand                                 | 01/2008          | 3,316.00<br>6,325.00    | 6,325.00         | 2,109.69          | -<br>12/2011          | 12/2011     | 0(R3)                                       | 0/11                       |
| 66           | 67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh         | 07/2007          | 230.00<br>-             | 343.58           | 229.59            | -<br>-                | 12/2011     | -                                           | 2/3                        |
| 67           | Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC, Chhatisgarh                         | 01/2007          | 295.89<br>607.17        | 607.17           | 290.68            | -<br>12/2011          | 03/2012     | 3(R3)                                       | 18/21                      |
| 68           | Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State                      | 05/2008          | 480.00<br>-             | 460.00           | 127.39            | -<br>05/2012          | 05/2012     | 0(R3)                                       | 1/2                        |
| 69           | EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal                                | 02/2008          | 14,443.00<br>16,408.00  | 16,408.00        | 11,272.00         | -<br>12/2011          | 06/2012     | 6(R3)                                       | 1/14                       |
| 70           | EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh | 10/2005          | 8,692.00<br>12,291.00   | 12,291.00        | 8,719.80          | 10/2009<br>10/2012    | 10/2012     | 0(R3)                                       | 47/59                      |
| 71           | COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh                           | 08/2007          | 108.00<br>-             | 216.68           | 44.44             | -<br>10/2012          | 10/2012     | 0(R3)                                       | 3/4                        |
| 72           | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh                               | 09/2008          | 5,185.00<br>17,265.00   | 17,265.00        | 3,212.16          | -<br>03/2013          | 03/2013     | 0(R3)                                       | 2/20                       |
| 73           | 1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka                                 | 04/2011          | 572.00<br>-             | 572.00           | -                 | 04/2013<br>-          | 04/2013     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                 |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                               | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 74   | 7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka                  | 02/2011          | 898.55                  | 898.55           | -                 | 05/2013               | 05/2013     | 0(O)                                        | 0/0                        |
|      | Total                                                                           |                  | 34,591.72               | 55,969.91        | 26,394.12         | -                     |             |                                             | 75/137                     |
|      |                                                                                 |                  | -                       |                  |                   |                       |             |                                             |                            |
|      | <u>Petrochemicals</u>                                                           |                  |                         |                  |                   |                       |             |                                             |                            |
| 75   | ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam                               | 04/2006          | 5,460.61                | 5,460.61         | 2,719.00          | -                     | 04/2012     | -                                           | 0/30                       |
|      | Total                                                                           |                  | 5,460.61                | 5,460.61         | 2,719.00          | -                     |             |                                             | 0/30                       |
|      |                                                                                 |                  | -                       |                  |                   |                       |             |                                             |                            |
|      | <u>Petroleum</u>                                                                |                  |                         |                  |                   |                       |             |                                             |                            |
| 76   | North Tapti Gas Field Development - [N16000096]ONGC,Multi State                 | 07/2008          | 589.70                  | 755.76           | 520.63            | 03/2011               | 06/2011     | 1(R3)                                       | 0/0                        |
|      |                                                                                 |                  | 755.76                  |                  |                   | 05/2011               |             |                                             |                            |
| 77   | Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar | 06/2009          | 613.54                  | 727.88           | 671.52            | 12/2010               | 06/2011     | 6(O)                                        | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 78   | DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam           | 06/2006          | 1,431.91                | 1,690.13         | -                 | 09/2009               | 08/2011     | 23(O)                                       | 0/0                        |
|      |                                                                                 |                  | 1,646.39                |                  |                   | -                     |             |                                             |                            |
| 79   | CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu     | 01/2008          | 224.00                  | 299.00           | 240.00            | 02/2011               | 08/2011     | 0(R3)                                       | 0/0                        |
|      |                                                                                 |                  | 299.00                  |                  |                   | 08/2011               |             |                                             |                            |
| 80   | MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam      | 04/2008          | 293.60                  | 261.75           | 230.97            | 12/2009               | 09/2011     | 21(O)                                       | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 81   | DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State        | 11/2007          | 4,429.38                | 2,340.00         | 2,200.48          | 10/2010               | 09/2011     | 0(R2)                                       | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | 09/2011               |             |                                             |                            |
| 82   | DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra    | 03/2009          | 3,284.00                | 3,284.00         | -                 | 09/2011               | 09/2011     | 0(O)                                        | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 83   | REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra                  | 06/2008          | 304.40                  | 304.40           | 245.01            | 06/2010               | 09/2011     | 2(R3)                                       | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | 07/2011               |             |                                             |                            |
| 84   | HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra      | 09/2006          | 2,305.30                | 3,005.30         | 2,416.96          | 06/2010               | 10/2011     | 16(R3)                                      | 0/0                        |
|      |                                                                                 |                  | 700.00                  |                  |                   | 06/2010               |             |                                             |                            |
| 85   | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                    | 08/2006          | 3,195.16                | 2,800.00         | 2,520.91          | 12/2008               | 11/2011     | 35(R3)                                      | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | 12/2008               |             |                                             |                            |
| 86   | BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State                   | 11/2007          | 1,816.07                | 1,385.00         | -                 | 10/2010               | 12/2011     | 0(R3)                                       | 0/1                        |
|      |                                                                                 |                  | -                       |                  |                   | 12/2011               |             |                                             |                            |
| 87   | COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State        | 11/2007          | 1,167.00                | 798.00           | 631.81            | 04/2011               | 12/2011     | 0(R3)                                       | 0/2                        |
|      |                                                                                 |                  | 1,167.00                |                  |                   | 12/2011               |             |                                             |                            |
| 88   | BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat         | 02/2009          | 250.00                  | 250.00           | 197.53            | 03/2013               | 12/2011     | -15(R1)                                     | 0/0                        |
|      |                                                                                 |                  | 349.00                  |                  |                   | 03/2013               |             |                                             |                            |
| 89   | HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra                              | 05/2008          | 706.70                  | 706.70           | 626.78            | 04/2010               | 12/2011     | 20(O)                                       | 0/0                        |
|      |                                                                                 |                  | -                       |                  |                   | -                     |             |                                             |                            |

| S.No | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                           |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                         | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 90   | NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra                                       | 05/2008          | 305.08                  | 305.08           | 250.40            | 04/2011               | 12/2011     | 8(O)                                        | 0/0                        |
| 91   | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State             | 06/2007          | 736.65                  | 736.65           | 210.39            | 09/2011               | 12/2011     | 3(O)                                        | 0/0                        |
| 92   | EURO-IV DHD - [N16000109]CPCL,Tamil Nadu                                                  | 09/2008          | 2,615.69                | 2,615.69         | 1,632.03          | 05/2011               | 12/2011     | 7(O)                                        | 0/116                      |
| 93   | CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat              | 02/2009          | 267.00                  | 267.00           | 171.46            | 09/2012               | 12/2011     | -9(O)                                       | 0/0                        |
| 94   | KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State | 07/2009          | 238.68                  | 204.00           | 111.00            | 01/2012               | 01/2012     | 0(O)                                        | 1/8                        |
| 95   | MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka                           | 08/2008          | 12,412.00<br>12,160.26  | 12,160.26        | 6,378.01          | 01/2012               | 01/2012     | 0(O)                                        | 0/0                        |
| 96   | MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra                                       | 05/2008          | 175.21                  | 162.12           | 58.26             | 03/2009<br>02/2012    | 02/2012     | 0(R3)                                       | 0/0                        |
| 97   | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra      | 01/2007          | 740.02                  | 740.02           | 412.78            | 03/2010<br>03/2012    | 03/2012     | 0(R1)                                       | 0/0                        |
| 98   | KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State          | 06/2009          | 348.00                  | 261.00           | 149.85            | 03/2012<br>08/2012    | 03/2012     | -5(R3)                                      | 7/12                       |
| 99   | VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State    | 12/2009          | 463.32                  | 330.47           | 138.07            | 06/2011<br>03/2012    | 03/2012     | 0(R3)                                       | 3/9                        |
| 100  | SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State         | 05/2011          | 616.00                  | 616.00           | -                 | 03/2012               | 03/2012     | 0(O)                                        | 0/0                        |
| 101  | INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State                      | 04/2003          | 429.82<br>2,218.01      | 2,218.01         | 1,237.61          | 04/2006<br>05/2011    | 05/2012     | 12(R3)                                      | 0/0                        |
| 102  | CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra                     | 01/2007          | 2,853.29<br>6,326.40    | 6,326.40         | 3,535.29          | 05/2010<br>05/2012    | 05/2012     | 0(R3)                                       | 0/0                        |
| 103  | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                          | 01/2007          | 2,323.40<br>2,920.82    | 2,920.82         | 1,173.84          | 09/2010<br>03/2012    | 05/2012     | 2(R3)                                       | 0/0                        |
| 104  | REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra                       | 05/2008          | 333.40<br>837.54        | 656.51           | 20.10             | 05/2010<br>04/2012    | 05/2012     | 1(R3)                                       | 0/0                        |
| 105  | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                           | 06/2007          | 1,436.21<br>1,456.96    | 1,436.21         | 82.57             | 07/2010<br>05/2012    | 05/2012     | 0(R3)                                       | 0/0                        |
| 106  | CDU/VDU-II - [N16000110]CPCL,Tamil Nadu                                                   | 03/2010          | 333.99                  | 333.99           | 47.33             | 05/2012               | 05/2012     | 0(O)                                        | 11/36                      |
| 107  | DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra                         | 06/2007          | 3,248.78<br>5,633.44    | 5,633.44         | 1,366.95          | 08/2010<br>03/2012    | 06/2012     | 3(R3)                                       | 0/0                        |
| 108  | ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State                                | 01/2010          | 2,163.64                | 2,163.64         | 485.72            | 06/2012               | 06/2012     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                 |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                               | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 109  | INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa      | 12/2009          | 1,492.33                | 1,492.33         | 670.65            | 06/2012               | 06/2012     | 0(O)                                        | 6/9                        |
| 110  | Polypropylene unit - [N16000113]Mangalore Refin,Karnataka                       | 05/2009          | 1,803.78                | 1,803.78         | 400.94            | 07/2012               | 06/2012     | -1(O)                                       | 0/0                        |
| 111  | Wind Power Project - [N16000119]ONGC,Rajasthan                                  | 07/2010          | 1,106.00                | 1,106.00         | -                 | 06/2012               | 06/2012     | 0(O)                                        | 0/0                        |
| 112  | ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat          | 02/2008          | 370.11                  | 370.11           | 67.89             | 04/2011               | 07/2012     | 15(O)                                       | 0/0                        |
| 113  | BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State             | 12/2009          | 540.92                  | 460.70           | 146.19            | 06/2011<br>07/2012    | 07/2012     | 0(R3)                                       | 7/9                        |
| 114  | DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State         | 06/2009          | 4,543.43<br>4,508.38    | 2,500.00         | 1,047.00          | 03/2012<br>08/2012    | 08/2012     | 0(R3)                                       | 11/10                      |
| 115  | Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura | 07/2008          | 288.04<br>288.04        | 288.04           | 105.00            | 08/2012               | 08/2012     | 0(O)                                        | 0/0                        |
| 116  | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra            | 01/2009          | 7,133.39                | 6,855.93         | 2,263.80          | 09/2012               | 09/2012     | 0(O)                                        | 0/0                        |
| 117  | PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State          | 08/2009          | 1,793.00                | 1,793.00         | 421.76            | 09/2012<br>09/2012    | 09/2012     | 0(R3)                                       | 0/15                       |
| 118  | Construction of 6 ETPs - [N16000117]ONGC,Gujarat                                | 03/2009          | 302.26                  | 302.26           | 15.78             | 09/2012               | 09/2012     | 0(O)                                        | 0/0                        |
| 119  | ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra           | 10/2008          | 1,797.35                | 1,797.35         | 72.19             | 12/2011               | 01/2013     | 13(O)                                       | 0/0                        |
| 120  | Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh  | 07/2010          | 1,000.00                | 1,000.00         | 25.63             | 01/2013               | 01/2013     | 0(O)                                        | 12/18                      |
| 121  | Development of SB-14 field - [N16000116]ONGC,Multi State                        | 01/2011          | 410.44                  | 410.44           | -                 | 11/2012               | 01/2013     | 2(O)                                        | 0/0                        |
| 122  | BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana           | 11/2009          | 341.50                  | 341.50           | 16.71             | 02/2013               | 02/2013     | 0(O)                                        | 15/42                      |
| 123  | IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam                                 | 09/2001          | 113.90<br>438.85        | 438.85           | 231.94            | 03/2006<br>03/2013    | 03/2013     | 0(R3)                                       | 6/6                        |
| 124  | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra              | 10/2007          | 5,713.03<br>8,813.41    | 8,813.41         | 6,767.50          | 05/2010<br>03/2013    | 03/2013     | 0(R3)                                       | 0/0                        |
| 125  | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam                       | 03/2009          | 2,465.15                | 2,378.86         | 359.46            | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 126  | Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State   | 01/2010          | 723.64                  | 723.64           | -                 | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 127  | Development of Cluster-7 Fields - [N16000104]ONGC,Multi State                   | 03/2010          | 3,241.03                | 3,241.03         | -                 | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 128  | Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State                | 08/2010          | 372.11                  | 372.11           | -                 | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |

| S.No  | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original /Revised (in months) | Milestones Achieved/ Total |         |
|-------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|--------------------------------------------|----------------------------|---------|
|       |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                            |                            |         |
| 1     | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                          | 10                         |         |
| 129   | HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra      | 04/2008          | 825.00<br>1,827.00      | 1,827.00         | -                 | 12/2011<br>04/2013    | 04/2013     | 0(R3)                                      | 0/203                      |         |
| 130   | PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa                                   | 02/2009          | 29,777.00<br>-          | 29,777.00        | 8,953.92          | 11/2012<br>06/2013    | 06/2013     | 0(R3)                                      | 107/100                    |         |
| 131   | DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra    | 12/2009          | 1,584.00<br>-           | 1,584.00         | -                 | -<br>-                | 08/2013     | -                                          | 0/0                        |         |
| 132   | Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State     | 11/2010          | 331.20<br>-             | 331.20           | -                 | 08/2013<br>-          | 08/2013     | 0(O)                                       | 0/0                        |         |
| 133   | Wax Project - [N16000101]NRL,Assam                                                  | 06/2010          | 576.60<br>-             | 576.60           | 13.77             | 12/2013<br>12/2013    | 12/2013     | 0(R3)                                      | 0/0                        |         |
| 134   | Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State                   | 06/2010          | 2,523.00<br>-           | 2,523.00         | -                 | 01/2014<br>-          | 01/2014     | 0(O)                                       | 0/0                        |         |
| 135   | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam            | 06/2010          | 202.94<br>-             | 202.94           | -                 | 01/2014<br>-          | 01/2014     | 0(O)                                       | 0/0                        |         |
| 136   | PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State         | 08/2010          | 8,140.00<br>-           | 8,140.00         | 183.00            | 02/2014<br>-          | 02/2014     | 0(O)                                       | 0/0                        |         |
| 137   | IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam                                | 09/2001          | 345.10<br>663.69        | 663.69           | 592.78            | 03/2007<br>03/2014    | 03/2014     | 0(R3)                                      | 3/3                        |         |
| 138   | Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat                                   | 11/2010          | 1,916.10<br>-           | 1,916.10         | -                 | 12/2014<br>-          | 12/2014     | 0(O)                                       | 0/0                        |         |
| 139   | Ankleswar Redevelopment - [N16000122]ONGC,Gujarat                                   | 11/2010          | 2,189.63<br>-           | 2,189.63         | -                 | 12/2014<br>-          | 12/2014     | 0(O)                                       | 0/0                        |         |
| 140   | Mehesana Redevelopment - [N16000121]ONGC,Gujarat                                    | 11/2010          | 3,823.00<br>-           | 3,823.00         | -                 | 04/2015<br>-          | 04/2015     | 0(O)                                       | 0/0                        |         |
| 141   | IOR GELEKI (ONGCL) - [160100216]ONGC,Assam                                          | 09/2001          | 390.09<br>1,674.11      | 1,674.11         | 1,375.28          | 03/2007<br>03/2017    | 03/2017     | 0(R3)                                      | 6/6                        |         |
| 142   | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana                          | 11/2007          | 281.07<br>-             | 281.07           | 3.29              | 10/2010<br>-          | -           | -                                          | 0/0                        |         |
| 143   | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra     | 03/2011          | 861.79<br>-             | 861.79           | -                 | 05/2013<br>-          | -           | -                                          | 0/0                        |         |
| 144   | RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh | 01/2009          | 756.00<br>-             | 756.00           | 711.47            | 09/2011<br>-          | 12/2011     | 3(O)                                       | 0/0                        |         |
| 145   | DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh     | 03/2009          | 3,597.00<br>2,730.00    | 2,730.00         | 696.82            | 09/2011<br>03/2012    | -           | -                                          | 0/0                        |         |
| 146   | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State            | 07/2009          | 7,596.18<br>6,652.22    | 6,652.22         | 1.63              | 01/2013<br>-          | -           | -                                          | 0/0                        |         |
| Total |                                                                                     |                  | 153,918.05              | 161,693.92       | 53,108.66         |                       |             |                                            |                            | 195/605 |

Power

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 147  | TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State       | 12/2008          | 204.07                  | 204.07           | 112.43            | 06/2011               | 08/2011     | 2(O)                                        | 0/0                        |
| 148  | TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K                  | 10/2006          | 238.25                  | 227.03           | 211.35            | 05/2011<br>05/2011    | 09/2011     | 4(R3)                                       | 0/0                        |
| 149  | EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State                | 12/2007          | 227.52                  | 227.52           | 132.86            | 06/2010               | 09/2011     | 15(O)                                       | 0/0                        |
| 150  | CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.                              | 08/2005          | 1,405.63                | 1,405.63         | 1,651.81          | 08/2010               | 11/2011     | 15(O)                                       | 0/0                        |
| 151  | URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K                                   | 08/2005          | 1,724.79                | 1,724.79         | 1,522.71          | 11/2009               | 12/2011     | 25(O)                                       | 0/0                        |
| 152  | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.  | 07/2006          | 557.24                  | 639.52           | 465.15            | 01/2010               | 12/2011     | 23(O)                                       | 0/22                       |
| 153  | WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan                  | 07/2006          | 5,221.23                | 4,978.56         | 2,925.54          | 07/2010               | 12/2011     | 17(O)                                       | 3/20                       |
| 154  | TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State            | 04/2008          | 297.37                  | 297.37           | 295.61            | 07/2011               | 12/2011     | 5(O)                                        | 0/0                        |
| 155  | CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K                         | 08/2006          | 621.28                  | 621.28           | 680.28            | 02/2011               | 02/2012     | 12(O)                                       | 0/1                        |
| 156  | WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State                 | 02/2009          | 664.96                  | 664.96           | 304.39            | 02/2012               | 02/2012     | 0(O)                                        | 0/0                        |
| 157  | WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State         | 02/2009          | 409.50                  | 409.50           | 58.53             | 02/2012               | 02/2012     | 0(O)                                        | 0/0                        |
| 158  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan        | 02/2009          | 210.79                  | 210.79           | 144.56            | 08/2011               | 02/2012     | 6(O)                                        | 0/0                        |
| 159  | TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State           | 02/2009          | 353.57                  | 353.57           | 206.98            | 07/2010<br>02/2012    | 02/2012     | 0(R3)                                       | 0/0                        |
| 160  | SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State           | 03/2009          | 196.10                  | 196.10           | 72.09             | 07/2011               | 02/2012     | 7(O)                                        | 0/0                        |
| 161  | KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal                                   | 04/2000          | 1,301.56                | 2,283.69         | 2,481.22          | 04/2005               | 03/2012     | 83(O)                                       | 6/11                       |
| 162  | SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh                            | 12/2003          | 8,323.39                | 8,323.39         | 7,284.00          | 12/2009               | 03/2012     | 27(O)                                       | 33/60                      |
| 163  | PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.                      | 10/2005          | 2,304.52                | 2,304.52         | 1,534.06          | 10/2010               | 03/2012     | 17(O)                                       | 0/0                        |
| 164  | TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar | 12/2005          | 3,779.46                | 3,725.13         | 3,483.30          | 09/2009               | 03/2012     | 30(O)                                       | 15/30                      |
| 165  | EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State                 | 10/2006          | 975.96                  | 894.26           | 690.07            | 10/2009               | 03/2012     | 29(O)                                       | 2/20                       |

| S.No | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                           |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                         | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 166  | SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh                                  | 08/2007          | 5,103.39                | 5,038.53         | 4,060.00          | -                     | 03/2012     | -                                           | 0/6                        |
| 167  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State           | 02/2009          | 317.69                  | 317.69           | 54.29             | 11/2011               | 03/2012     | 4(O)                                        | 0/0                        |
| 168  | System Strengthening -X of SR - [N18000086]PGCIL,Multi State                              | 12/2009          | 276.61                  | 276.61           | 74.44             | 04/2012               | 04/2012     | 0(O)                                        | 0/0                        |
| 169  | TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal          | 10/2003          | 768.92                  | 768.92           | 1,349.12          | 03/2007               | 05/2012     | 62(O)                                       | 1/25                       |
| 170  | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State         | 11/2009          | 1,075.12                | 1,075.12         | 259.61            | 05/2012               | 05/2012     | 0(O)                                        | 0/0                        |
| 171  | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State         | 07/2009          | 1,736.36                | 1,736.36         | 339.20            | 06/2012               | 06/2012     | 0(O)                                        | 0/0                        |
| 172  | IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar                    | 02/2010          | 215.86                  | 215.86           | 116.80            | 06/2012               | 06/2012     | 0(O)                                        | 0/0                        |
| 173  | System Strengthening -XII of SR - [N18000085]PGCIL,Multi State                            | 02/2010          | 232.34                  | 232.34           | 10.68             | 06/2012               | 06/2012     | 0(O)                                        | 0/0                        |
| 174  | SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State          | 08/2008          | 2,360.95                | 2,360.95         | 1,663.54          | 08/2012               | 08/2012     | 0(O)                                        | 0/0                        |
| 175  | 765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State         | 08/2008          | 7,075.33                | 7,075.33         | 3,908.90          | 08/2012               | 08/2012     | 0(O)                                        | 0/0                        |
| 176  | System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State       | 12/2009          | 1,216.83                | 1,216.83         | 353.12            | 08/2012               | 08/2012     | 0(O)                                        | 0/0                        |
| 177  | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State | 10/2008          | 4,824.12                | 4,824.12         | 1,950.27          | 10/2012               | 10/2012     | 0(O)                                        | 0/0                        |
| 178  | MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra                                  | 02/2010          | 469.38                  | 469.38           | 166.77            | 10/2012               | 10/2012     | 0(O)                                        | 0/0                        |
| 179  | INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State    | 10/2010          | 160.32                  | 160.32           | 11.32             | 10/2012               | 10/2012     | 0(O)                                        | 0/0                        |
| 180  | NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K                                 | 08/2006          | 611.02                  | 611.02           | 657.77            | 08/2010               | 11/2012     | 27(O)                                       | 0/0                        |
| 181  | MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra                                           | 11/2008          | 5,459.28                | 6,010.89         | 2,790.00          | 08/2012               | 11/2012     | 3(O)                                        | 2/16                       |
| 182  | TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State         | 03/2010          | 4,672.99                | 4,672.99         | 312.54            | 11/2012               | 11/2012     | 0(O)                                        | 0/0                        |
| 183  | NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State          | 03/2010          | 965.58                  | 965.58           | 245.19            | 11/2012               | 11/2012     | 0(O)                                        | 0/0                        |
| 184  | EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State                     | 07/2010          | 1,272.80                | 1,272.80         | 86.61             | 11/2012               | 11/2012     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 185  | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal                  | 09/2005          | 1,061.38                | 1,061.38         | 1,007.32          | 09/2009               | 12/2012     | 39(O)                                       | 0/0                        |
| 186  | KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu                 | 05/2005          | 1,779.29                | 1,946.85         | 1,727.35          | 11/2008               | 12/2012     | 49(O)                                       | 25/38                      |
| 187  | LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC, Uttaranchal                           | 06/2006          | 2,895.10                | 2,895.10         | 685.00            | 11/2011               | 12/2012     | 13(O)                                       | 6/34                       |
| 188  | TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State  | 12/2008          | 7,031.88                | 7,031.88         | 2,538.06          | 12/2012               | 12/2012     | 0(O)                                        | 0/0                        |
| 189  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State   | 02/2009          | 509.66                  | 509.66           | 245.77            | 11/2011               | 12/2012     | 13(O)                                       | 0/0                        |
| 190  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, Multi State     | 02/2009          | 410.29                  | 410.29           | 128.49            | 02/2012               | 12/2012     | 10(O)                                       | 0/0                        |
| 191  | VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC, Madhya Pradesh                  | 01/2009          | 5,915.00                | 5,915.00         | 2,135.00          | 10/2012               | 12/2012     | 2(O)                                        | 2/15                       |
| 192  | RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh             | 01/2009          | 6,230.81                | 6,230.81         | 2,003.00          | 10/2012               | 12/2012     | 2(O)                                        | 3/16                       |
| 193  | Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL, Multi State  | 02/2010          | 2,144.00                | 2,144.00         | 306.84            | 12/2012               | 12/2012     | 0(O)                                        | 0/0                        |
| 194  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL, Multi State      | 10/2010          | 182.68                  | 182.68           | 25.54             | 01/2013               | 01/2013     | 0(O)                                        | 0/0                        |
| 195  | Transmission system for transfer of power from Gen. - [N18000098]PGCIL, Multi State | 05/2010          | 250.03                  | 250.03           | 18.25             | 01/2013               | 01/2013     | 0(O)                                        | 0/0                        |
| 196  | KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.                                   | 10/2002          | 4,527.15                | 4,527.15         | 3,777.00          | 04/2009               | 03/2013     | 47(O)                                       | 19/9                       |
| 197  | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra               | 12/2007          | 477.69                  | 477.69           | 340.11            | 09/2010               | 03/2013     | 30(O)                                       | 0/0                        |
| 198  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State      | 02/2009          | 520.48                  | 520.48           | 259.63            | 11/2011               | 03/2013     | 16(O)                                       | 0/0                        |
| 199  | 765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL, Multi State  | 02/2009          | 1,347.32                | 1,347.32         | 842.45            | 02/2012               | 03/2013     | 13(O)                                       | 0/0                        |
| 200  | TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Orissa       | 09/2010          | 2,074.86                | 2,074.86         | 123.63            | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 201  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL, Multi State    | 08/2010          | 1,677.57                | 1,677.57         | 76.35             | 04/2013               | 04/2013     | 0(O)                                        | 0/0                        |
| 202  | SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL, Multi State  | 08/2010          | 170.36                  | 170.36           | 8.71              | 04/2013               | 04/2013     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 203  | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura                              | 07/2009          | 421.01<br>623.44        | 623.44           | 68.22             | 01/2012<br>-          | 07/2013     | 18(O)                                       | 0/0                        |
| 204  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State           | 07/2010          | 752.64<br>-             | 752.64           | 44.90             | 07/2013<br>-          | 07/2013     | 0(O)                                        | 0/0                        |
| 205  | TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV - [N18000102]PGCIL,Maharashtra         | 07/2011          | 181.93<br>-             | 181.93           | -                 | 07/2013<br>-          | 07/2013     | 0(O)                                        | 0/0                        |
| 206  | PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.                    | 12/2008          | 573.99<br>-             | 573.99           | 205.89            | 08/2013<br>08/2013    | 08/2013     | 0(R3)                                       | 10/17                      |
| 207  | TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh      | 12/2010          | 779.21<br>-             | 779.21           | 71.18             | 08/2013<br>-          | 08/2013     | 0(O)                                        | 0/0                        |
| 208  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State          | 12/2010          | 209.78<br>-             | 209.78           | 15.15             | 08/2013<br>-          | 08/2013     | 0(O)                                        | 0/0                        |
| 209  | Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh              | 12/2010          | 1,719.52<br>-           | 1,719.52         | 125.67            | 08/2013<br>-          | 08/2013     | 0(O)                                        | 0/0                        |
| 210  | RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.                                       | 01/2007          | 2,047.03<br>-           | 2,047.03         | 1,317.70          | 01/2012<br>-          | 09/2013     | 20(O)                                       | 2/10                       |
| 211  | TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State            | 02/2009          | 184.19<br>-             | 184.19           | 127.76            | 11/2011<br>-          | 09/2013     | 22(O)                                       | 0/0                        |
| 212  | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam                                 | 01/2008          | 4,375.35<br>-           | 4,375.35         | 2,242.00          | 06/2011<br>-          | 10/2013     | 28(O)                                       | 0/29                       |
| 213  | BARH STPP STAGE -II - [N18000047]NTPC,                                                   | 02/2008          | 7,341.04<br>-           | 7,341.04         | 2,588.00          | -<br>-                | 10/2013     | -                                           | 2/18                       |
| 214  | Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State | 03/2011          | 1,585.12<br>-           | 1,585.12         | 57.33             | 11/2013<br>-          | 11/2013     | 0(O)                                        | 0/0                        |
| 215  | TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa             | 12/2010          | 2,743.19<br>-           | 2,743.19         | 216.21            | 12/2013<br>-          | 12/2013     | 0(O)                                        | 0/0                        |
| 216  | TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram                                   | 07/1998          | 368.72<br>913.63        | 913.63           | 247.90            | 07/2006<br>01/2014    | 01/2014     | 0(R3)                                       | 2/5                        |
| 217  | TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State          | 03/2011          | 2,569.25<br>-           | 2,569.25         | -                 | 03/2014<br>-          | 03/2014     | 0(O)                                        | 0/0                        |
| 218  | TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal                     | 11/2006          | 2,978.48<br>-           | 2,978.48         | 1,133.00          | 03/2013<br>-          | 06/2014     | 15(O)                                       | 5/13                       |
| 219  | SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.                             | 09/2003          | 6,285.33<br>-           | 6,285.33         | 5,056.36          | 09/2010<br>-          | 08/2014     | 47(O)                                       | 2/11                       |
| 220  | BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar                                 | 12/2003          | 8,692.97<br>-           | 8,693.00         | 6,070.00          | 12/2009<br>-          | 09/2014     | 57(O)                                       | 15/70                      |
| 221  | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State        | 02/2009          | 11,130.19<br>-          | 11,130.19        | 2,877.41          | 08/2013<br>-          | 09/2014     | 13(O)                                       | 0/0                        |

| S.No            | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|-----------------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|                 |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1               | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 222             | PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.                             | 09/2002          | 3,919.59                | 3,919.59         | 3,265.14          | 09/2009               | 12/2014     | 63(O)                                       | 1/20                       |
| 223             | TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal | 04/2010          | 4,404.57                | 4,404.57         | -                 | 01/2015               | 01/2015     | 0(O)                                        | 0/0                        |
| 224             | KISHANGANGA HEP - [N18000031]NHPC,J & K                                          | 07/2007          | 2,238.67                | 3,642.04         | 923.91            | 07/2014               | 01/2016     | 18(O)                                       | 0/0                        |
| 225             | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal                | 07/2006          | 1,657.00                | 2,978.86         | 261.82            | 07/2010               | 02/2016     | 67(O)                                       | 1/1                        |
| 226             | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal        | 08/2008          | 2,491.58                | 3,422.44         | 168.98            | 07/2014               | 05/2016     | 22(O)                                       | 0/7                        |
| 227             | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.          | 12/2004          | 2,496.90                | 2,496.90         | 1,554.07          | 05/2013<br>06/2016    | 06/2016     | 0(R3)                                       | 79/22                      |
| 228             | KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka               | 03/2005          | 596.45                  | 947.96           | 829.36            | 12/2007<br>12/2009    | -           | -                                           | 14/18                      |
| 229             | WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State            | 04/2008          | 230.89                  | 230.89           | 92.04             | 01/2011               | 10/2011     | 9(O)                                        | 0/1                        |
| Total           |                                                                                  |                  | 180,012.22              | 186,095.99       | 88,475.61         |                       |             |                                             | 250/565                    |
| <u>Railways</u> |                                                                                  |                  |                         |                  |                   |                       |             |                                             |                            |
| 230             | RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat                            | 04/2006          | 196.97                  | 196.97           | 174.05            | 03/2011               | 03/2011     | 0(O)                                        | 0/0                        |
| 231             | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala                            | 10/1998          | 550.00                  | 550.00           | 70.95             | -                     | 03/2012     | -                                           | 0/0                        |
| 232             | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State                          | 02/1996          | 240.00                  | 579.37           | 593.76            | -                     | 07/2011     | -                                           | 0/0                        |
| 233             | PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat                      | 04/2005          | 148.61                  | 227.52           | 258.71            | 03/2008<br>03/2009    | 10/2010     | 19(R1)                                      | 0/0                        |
| 234             | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa                               | 04/1999          | 166.16                  | 243.40           | 233.07            | -<br>02/2009          | 12/2010     | 22(R1)                                      | 0/0                        |
| 235             | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa               | 04/2000          | 133.41                  | 211.90           | 187.38            | -<br>03/2009          | 12/2010     | 21(R1)                                      | 0/0                        |
| 236             | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh                       | 04/2003          | 136.62                  | 221.90           | 154.91            | 12/2007<br>03/2010    | 12/2010     | 9(R1)                                       | 0/0                        |
| 237             | ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh        | 04/2003          | 230.73                  | 399.50           | 294.87            | 03/2009<br>12/2008    | 12/2010     | 24(R1)                                      | 0/0                        |
| 238             | BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat                   | 09/2005          | 200.80                  | 200.80           | 253.23            | -<br>-                | 12/2010     | -                                           | 0/0                        |
| 239             | BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh                               | 04/1997          | 151.52                  | 273.00           | 298.28            | -<br>03/2009          | 03/2011     | 24(R1)                                      | 0/0                        |
| 240             | PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State      | 04/2005          | 240.00                  | 329.70           | 258.52            | 03/2009<br>12/2009    | 03/2011     | 15(R1)                                      | 0/0                        |

| S.No | Project                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                               |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                             | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 241  | MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra     | 04/2003          | 3,125.20<br>4,501.80    | 4,501.80         | 4,246.71          | -<br>12/2010          | 06/2011     | 6(R3)                                       | 0/1                        |
| 242  | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa                         | 04/1994          | 355.38<br>470.21        | 700.00           | 161.90            | -<br>-                | 08/2011     | -                                           | 0/0                        |
| 243  | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa                         | 04/1993          | 100.00<br>142.90        | 208.68           | 182.17            | 03/2002<br>-          | 09/2011     | 114(O)                                      | 0/0                        |
| 244  | PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal                      | 09/2007          | 252.50<br>-             | 252.50           | 162.23            | 02/2010<br>-          | 11/2011     | 21(O)                                       | 0/0                        |
| 245  | GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State                             | 04/1985          | 158.77<br>432.46        | 540.96           | 558.55            | 03/1994<br>-          | 12/2011     | 213(O)                                      | 0/0                        |
| 246  | NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh                  | 03/1996          | 155.74<br>164.36        | 822.57           | 486.71            | 02/2009<br>-          | 12/2011     | 34(O)                                       | 0/0                        |
| 247  | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa                              | 04/1996          | 301.64<br>-             | 735.10           | -                 | -<br>09/2009          | 12/2011     | 27(R1)                                      | 0/0                        |
| 248  | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa                         | 04/2005          | 726.96<br>810.78        | 810.78           | 78.54             | -<br>-                | 12/2011     | -                                           | 0/0                        |
| 249  | Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka | 04/2007          | 482.00<br>-             | 482.70           | 224.65            | 03/2013<br>-          | 12/2011     | -15(O)                                      | 0/0                        |
| 250  | KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh                 | 03/1997          | 395.00<br>1,062.36      | 1,577.46         | 1,154.15          | -<br>-                | 02/2012     | -                                           | 0/0                        |
| 251  | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal       | 04/2000          | 157.96<br>762.33        | 762.33           | 409.84            | -<br>12/2009          | 02/2012     | 26(R1)                                      | 0/0                        |
| 252  | Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal              | 04/2009          | 259.51<br>-             | 259.51           | 62.43             | 12/2011<br>-          | 02/2012     | 2(O)                                        | 0/0                        |
| 253  | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State    | 03/1984          | 520.00<br>637.46        | 637.46           | 542.72            | 03/1995<br>-          | 03/2012     | 204(O)                                      | 0/0                        |
| 254  | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh        | 12/1994          | 124.43<br>407.78        | 725.90           | 502.72            | -<br>-                | 03/2012     | -                                           | 0/0                        |
| 255  | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand                  | 04/1995          | 184.00<br>254.07        | 675.00           | 453.79            | -<br>12/2011          | 03/2012     | 3(R3)                                       | 0/0                        |
| 256  | KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka           | 04/1996          | 157.00<br>262.82        | 262.82           | 203.03            | -<br>03/2012          | 03/2012     | 0(R3)                                       | 0/0                        |
| 257  | MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar                          | 04/1997          | 100.00<br>322.29        | 411.22           | 421.85            | -<br>-                | 03/2012     | -                                           | 0/0                        |
| 258  | JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar               | 04/1997          | 233.00<br>335.77        | 903.56           | 552.79            | -<br>-                | 03/2012     | -                                           | 0/0                        |
| 259  | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar      | 04/1996          | 114.01<br>283.95        | 427.89           | 336.91            | -<br>03/2011          | 03/2012     | 12(R3)                                      | 0/0                        |
| 260  | HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar   | 04/2003          | 98.74<br>224.51         | 337.30           | 191.22            | -<br>-                | 03/2012     | -                                           | 0/0                        |

| S.No | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                    |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                  | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 261  | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar           | 03/2005          | 470.09<br>1,417.97      | 1,417.97         | 914.08            | -<br>-                | 03/2012     | -                                           | 0/0                        |
| 262  | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh                  | 09/2006          | 324.90<br>-             | 324.90           | 187.13            | 03/2010<br>-          | 03/2012     | 24(O)                                       | 0/0                        |
| 263  | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr. | 09/1996          | 156.00<br>-             | 254.29           | 178.89            | -<br>-                | 03/2012     | -                                           | 0/0                        |
| 264  | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh   | 02/2008          | 171.10<br>-             | 171.10           | 136.84            | 03/2012<br>-          | 03/2012     | 0(O)                                        | 0/0                        |
| 265  | ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh                    | 12/2004          | 129.17<br>-             | 220.00           | 217.49            | 03/2011<br>-          | 03/2012     | 12(O)                                       | 0/0                        |
| 266  | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal                      | 03/1984          | 293.97<br>-             | 723.27           | 378.13            | 06/2005<br>07/2011    | 03/2012     | 8(R3)                                       | 0/0                        |
| 267  | Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan      | 04/2007          | 643.36<br>-             | 803.39           | 786.86            | 03/2011<br>-          | 03/2012     | 12(O)                                       | 0/0                        |
| 268  | Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand                                | 04/2008          | 167.73<br>-             | 167.73           | 36.04             | 03/2012<br>-          | 03/2012     | 0(O)                                        | 0/0                        |
| 269  | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal                      | 04/1974          | 31.42<br>154.30         | 499.16           | 142.91            | 03/2007<br>03/2007    | 06/2012     | 63(R1)                                      | 0/0                        |
| 270  | NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State                             | 03/1981          | 37.68<br>450.00         | 730.00           | 325.04            | -<br>07/2012          | 07/2012     | 0(R3)                                       | 0/0                        |
| 271  | CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra               | 07/1996          | 273.67<br>1,160.52      | 1,302.12         | 571.52            | -<br>-                | 12/2012     | -                                           | 0/0                        |
| 272  | CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab                       | 07/1998          | 248.44<br>576.27        | 1,104.40         | 793.10            | 12/2012<br>-          | 12/2012     | 0(O)                                        | 0/0                        |
| 273  | BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal                          | 03/1998          | 111.90<br>-             | 1,211.22         | 387.79            | 03/2005<br>12/2008    | 12/2012     | 48(R1)                                      | 0/0                        |
| 274  | JIND-SONEPAT (NL),NR - [220100280](NR),Haryana                                     | 01/2004          | 190.81<br>238.56        | 401.83           | 334.70            | -<br>03/2012          | 12/2012     | 9(R3)                                       | 0/0                        |
| 275  | KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar                                       | 04/2002          | 323.41<br>-             | 341.41           | 233.20            | -<br>-                | 12/2012     | -                                           | 0/0                        |
| 276  | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar                    | 04/2002          | 921.00<br>-             | 981.00           | 528.45            | 03/2009<br>-          | 12/2012     | 45(O)                                       | 0/0                        |
| 277  | PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar                                | 04/2001          | 624.47<br>-             | 1,389.98         | 957.77            | 10/2007<br>-          | 12/2012     | 62(O)                                       | 0/0                        |
| 278  | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh                      | 09/2007          | 687.20<br>-             | 687.20           | 339.93            | 03/2010<br>-          | 12/2012     | 33(O)                                       | 0/0                        |
| 279  | Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal     | 04/1999          | 207.52<br>-             | 207.52           | 103.56            | 12/2012<br>-          | 12/2012     | 0(O)                                        | 0/0                        |
| 280  | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan                             | 02/1997          | 151.84<br>410.08        | 410.08           | 149.04            | -<br>-                | 03/2013     | -                                           | 0/0                        |
| 281  | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State        | 03/1998          | 280.00<br>-             | 1,029.00         | 684.77            | -<br>-                | 03/2013     | -                                           | 0/0                        |

| S.No | Project                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 282  | Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh                    | 04/2008          | 603.04                  | 603.04           | 45.14             | 03/2012               | 03/2013     | 12(O)                                       | 0/0                        |
| 283  | Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat                       | 04/2008          | 394.13                  | 394.13           | 0.49              | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 284  | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu     | 04/2006          | 495.74                  | 495.74           | 135.49            | -                     | 06/2013     | 0(R3)                                       | 0/0                        |
| 285  | Ghutiasharif-Canning (ER) - [N22000117]ER, West Bengal                            | 04/2009          | 189.97                  | 189.97           | 58.46             | 12/2011               | 11/2013     | 23(O)                                       | 0/0                        |
| 286  | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh                  | 04/2005          | 383.79                  | 585.93           | 173.04            | -                     | 12/2013     | -                                           | 0/0                        |
| 287  | Katakhal to Bhairabi - [N22000126]NEFR, Assam                                     | 04/1998          | 227.90                  | 223.01           | 83.45             | 12/2012               | 12/2013     | 12(O)                                       | 0/0                        |
| 288  | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam       | 04/1996          | 1,676.31                | 4,091.33         | 2,776.44          | 03/2009               | 12/2013     | 57(O)                                       | 0/0                        |
| 289  | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State | 04/2000          | 733.00                  | 1,655.80         | 808.72            | 12/2008               | 03/2014     | 63(O)                                       | 0/0                        |
| 290  | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State | 01/2004          | 915.70                  | 1,717.29         | 702.69            | -                     | 03/2014     | -                                           | 0/0                        |
| 291  | AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura                             | 04/2008          | 813.34                  | 1,141.76         | 206.44            | 03/2014               | 03/2014     | 0(O)                                        | 0/0                        |
| 292  | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram                             | 04/2008          | 619.34                  | 2,393.49         | 3.61              | 04/2014               | 03/2014     | -1(O)                                       | 0/0                        |
| 293  | Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR, Rajasthan    | 04/2008          | 653.19                  | 653.19           | 6.72              | 03/2014               | 03/2014     | 0(O)                                        | 0/0                        |
| 294  | Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR, Rajasthan    | 04/2008          | 516.23                  | 516.23           | 70.08             | 03/2014               | 03/2014     | 0(O)                                        | 0/0                        |
| 295  | Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat        | 04/2008          | 1,389.62                | 1,389.62         | 171.04            | 03/2014               | 03/2014     | 0(O)                                        | 0/0                        |
| 296  | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh             | 04/2006          | 325.00                  | 369.90           | 97.35             | 03/2010               | 06/2014     | 0(R3)                                       | 0/0                        |
| 297  | RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR, Assam       | 09/1997          | 1,000.00                | 3,230.01         | 2,215.96          | 04/2008               | 12/2014     | 9(R3)                                       | 0/0                        |
| 298  | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar                    | 04/2003          | 324.66                  | 324.66           | 165.33            | -                     | 03/2015     | -                                           | 0/0                        |
| 299  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP, Maharashtra       | 04/2008          | 5,300.00                | 5,300.00         | 278.51            | 03/2014               | 03/2015     | 12(O)                                       | 0/0                        |
| 300  | Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR, Rajasthan          | 04/2008          | 829.74                  | 829.74           | -                 | 03/2015               | 03/2015     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 301  | New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland    | 04/2006          | 850.00<br>-             | 850.00           | 8.44              | 03/2015<br>-          | 03/2015     | 0(O)                                        | 0/0                        |
| 302  | SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim                                      | 04/2008          | 1,339.48<br>-           | 3,380.57         | 52.63             | 12/2015<br>-          | 12/2015     | 0(O)                                        | 0/0                        |
| 303  | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur                    | 04/2003          | 727.56<br>727.53        | 3,056.85         | 463.33            | 03/2011<br>03/2014    | 03/2016     | 24(R3)                                      | 0/0                        |
| 304  | New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal | 04/2010          | 2,069.60<br>-           | 2,069.60         | 0.21              | 03/2014<br>-          | 03/2016     | 24(O)                                       | 0/0                        |
| 305  | New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal | 04/2010          | 3,951.98<br>-           | 3,951.98         | 1.42              | 03/2016<br>-          | 03/2016     | 0(O)                                        | 0/0                        |
| 306  | New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal         | 04/2010          | 2,619.02<br>-           | 2,619.02         | 23.10             | 03/2016<br>-          | 03/2016     | 0(O)                                        | 0/0                        |
| 307  | New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal | 04/2010          | 2,397.72<br>-           | 2,397.72         | 0.02              | 03/2016<br>-          | 06/2016     | 3(O)                                        | 0/0                        |
| 308  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K                      | 03/1995          | 2,500.00<br>8,000.00    | 20,000.00        | 7,189.29          | 03/2001<br>-          | 12/2017     | 201(O)                                      | 0/0                        |
| 309  | VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State                               | 04/1990          | 155.66<br>-             | 356.87           | 148.75            | -<br>03/2010          | -           | -                                           | 0/0                        |
| 310  | RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat        | 04/1992          | 112.53<br>320.66        | 464.50           | 509.57            | 03/1996<br>06/2009    | -           | -                                           | 0/0                        |
| 311  | New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal | 04/1983          | 36.80<br>274.41         | 415.23           | 234.54            | -<br>-                | -           | -                                           | 0/0                        |
| 312  | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh | 04/1995          | 304.00<br>-             | 968.60           | -                 | 12/2012<br>-          | -           | -                                           | 0/0                        |
| 313  | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra                     | 02/1997          | 353.08<br>462.67        | 1,010.00         | 96.07             | -<br>-                | -           | -                                           | 0/0                        |
| 314  | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka         | 02/1997          | 295.00<br>-             | 412.91           | 468.64            | -<br>-                | -           | -                                           | 0/0                        |
| 315  | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State                         | 02/1997          | 386.30<br>-             | 1,038.00         | 551.55            | 03/1998<br>-          | -           | -                                           | 0/0                        |
| 316  | KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu                                    | 02/1997          | 155.55<br>-             | 945.73           | 599.07            | -<br>-                | -           | -                                           | 0/0                        |
| 317  | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka                                  | 04/1995          | 227.00<br>-             | 997.58           | 64.29             | -<br>-                | -           | -                                           | 0/0                        |
| 318  | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State                     | 04/1997          | 218.24<br>377.32        | 497.47           | 91.37             | -<br>-                | -           | -                                           | 0/0                        |
| 319  | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh                       | 07/1998          | 125.00<br>-             | 363.26           | 0.27              | 07/2008<br>-          | -           | -                                           | 0/0                        |

| S.No | Project                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                              | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 320  | KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd              | 03/1999          | 491.19<br>1,099.20      | 1,099.20         | 1,058.38          | 07/2005<br>-          | -           | -                                           | 0/0                        |
| 321  | GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka                              | 02/1998          | 242.42<br>369.70        | 554.55           | 254.82            | -<br>05/2009          | -           | -                                           | 0/0                        |
| 322  | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar                   | 04/1997          | 78.23<br>-              | 162.87           | 86.40             | -<br>-                | -           | -                                           | 0/0                        |
| 323  | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State           | 03/2002          | 409.00<br>625.30        | 847.76           | 813.24            | 06/2007<br>-          | -           | -                                           | 0/0                        |
| 324  | REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh                        | 06/2000          | 168.34<br>-             | 296.20           | 303.99            | 04/2003<br>03/2010    | -           | -                                           | 0/0                        |
| 325  | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu             | 09/1995          | 100.00<br>-             | 548.96           | 472.21            | -<br>-                | -           | -                                           | 0/0                        |
| 326  | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh                 | 12/2001          | 330.00<br>-             | 695.00           | 9.44              | -<br>-                | -           | -                                           | 0/0                        |
| 327  | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State                     | 04/2000          | 138.00<br>519.67        | 607.09           | 323.19            | -<br>12/2012          | -           | -                                           | 0/0                        |
| 328  | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka                  | 02/1999          | 138.00<br>-             | 901.62           | 0.29              | -<br>-                | -           | -                                           | 0/0                        |
| 329  | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd                          | 04/2002          | 459.91<br>-             | 418.17           | 73.52             | -<br>-                | -           | -                                           | 0/0                        |
| 330  | RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh                   | 04/2001          | 727.13<br>727.13        | 1,225.00         | 210.24            | -<br>-                | -           | -                                           | 0/0                        |
| 331  | RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa                             | 02/1996          | 57.94<br>-              | 173.49           | 171.65            | 03/1998<br>08/2005    | -           | -                                           | 0/0                        |
| 332  | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa                       | 04/1998          | 183.23<br>-             | 638.00           | -                 | 02/2015<br>-          | -           | -                                           | 0/0                        |
| 333  | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh             | 04/2006          | 378.56<br>671.82        | 791.60           | 0.76              | -<br>-                | -           | -                                           | 0/0                        |
| 334  | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd                      | 03/1997          | 186.92<br>-             | 261.70           | 20.18             | 02/2006<br>-          | -           | -                                           | 0/0                        |
| 335  | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh            | 07/2006          | 743.00<br>-             | 732.80           | 306.37            | 03/2008<br>06/2008    | -           | -                                           | 0/0                        |
| 336  | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu | 09/2007          | 404.19<br>-             | 900.00           | 187.89            | -<br>-                | -           | -                                           | 0/0                        |
| 337  | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu   | 09/2006          | 343.17<br>-             | 900.00           | 408.50            | -<br>-                | -           | -                                           | 0/0                        |
| 338  | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu               | 09/2006          | 125.00<br>-             | 227.40           | 21.00             | -<br>-                | -           | -                                           | 0/0                        |
| 339  | TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu                               | 09/2006          | 456.00<br>-             | 582.83           | 83.97             | -<br>-                | -           | -                                           | 0/0                        |

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 340  | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar             | 09/2006          | 300.00<br>300.00        | 529.88           | 35.45             | -<br>-                | -           | -                                           | 0/0                        |
| 341  | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                                 | 04/2008          | 282.92<br>-             | 359.86           | 0.71              | -<br>-                | -           | -                                           | 0/0                        |
| 342  | Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat             | 04/2006          | 117.36<br>196.95        | 196.95           | 168.88            | 03/2011<br>-          | -           | -                                           | 0/0                        |
| 343  | AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra                                    | 06/1994          | 120.90<br>284.27        | 488.76           | 451.87            | 06/1999<br>03/2011    | -           | -                                           | 0/0                        |
| 344  | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra        | 03/1996          | 401.81<br>495.44        | 495.44           | 166.58            | 03/2004<br>-          | -           | -                                           | 0/0                        |
| 345  | KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka                                    | 04/1995          | 65.94<br>281.20         | 302.23           | 325.44            | -<br>03/2011          | -           | -                                           | 0/0                        |
| 346  | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd                                   | 04/1997          | 194.07<br>-             | 456.45           | 267.31            | 06/2004<br>04/2005    | -           | -                                           | 0/0                        |
| 347  | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State                    | 09/1998          | 925.00<br>-             | 925.00           | 504.78            | 05/2008<br>03/2011    | -           | -                                           | 0/0                        |
| 348  | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh              | 04/1999          | 108.00<br>214.09        | 227.42           | 249.52            | 12/2009<br>03/2011    | -           | -                                           | 0/0                        |
| 349  | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar                                   | 09/2001          | 100.00<br>492.98        | 1,015.84         | 720.23            | -<br>12/2010          | -           | -                                           | 0/0                        |
| 350  | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh | 03/2002          | 381.17<br>863.23        | 863.23           | 401.26            | -<br>-                | -           | -                                           | 0/0                        |
| 351  | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State                   | 04/1999          | 323.40<br>-             | 522.56           | 414.70            | -<br>-                | -           | -                                           | 0/1                        |
| 352  | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal        | 03/2000          | 907.69<br>1,032.76      | 3,176.10         | 3,062.38          | 12/2006<br>08/2010    | -           | -                                           | 0/0                        |
| 353  | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State                                | 04/1998          | 92.63<br>108.91         | 228.09           | 230.26            | -<br>02/2011          | -           | -                                           | 0/0                        |
| 354  | REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana                                        | 01/2004          | 149.38<br>330.23        | 475.28           | 469.93            | 02/2010<br>02/2011    | -           | -                                           | 0/0                        |
| 355  | KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd                                   | 04/1996          | 371.36<br>-             | 452.35           | 367.76            | -<br>-                | -           | -                                           | 0/0                        |
| 356  | SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan                            | 04/2001          | 143.92<br>258.60        | 258.60           | 234.79            | -<br>03/2011          | -           | -                                           | 0/0                        |
| 357  | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar                                  | 04/2003          | 218.19<br>-             | 218.19           | 131.48            | -<br>-                | -           | -                                           | 0/0                        |
| 358  | HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State                                 | 04/2005          | 230.03<br>-             | 230.03           | 131.75            | -<br>-                | -           | -                                           | 0/0                        |
| 359  | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State       | 12/2006          | 170.00<br>170.00        | 435.87           | 359.02            | -<br>03/2011          | -           | -                                           | 0/0                        |
| 360  | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam             | 09/2006          | 200.00<br>-             | 384.04           | 76.53             | -<br>-                | -           | -                                           | 0/0                        |

| S.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 361  | BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal                                     | 04/2007          | 245.15                  | 245.15           | 160.33            | 12/2010<br>03/2011    | -           | -                                           | 0/0                        |
| 362  | Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal                            | 04/2004          | 225.68                  | 225.68           | 129.37            | -<br>12/2010          | -           | -                                           | 0/0                        |
| 363  | Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat               | 04/2008          | 318.24                  | 468.62           | 2.07              | 03/2012               | -           | -                                           | 0/0                        |
|      | Total                                                                                    |                  | 65,810.63               | 131,493.76       | 54,467.84         |                       |             |                                             | 0/2                        |
|      |                                                                                          |                  | -                       |                  |                   |                       |             |                                             |                            |
|      | <b>Road Transport &amp; Highways</b>                                                     |                  |                         |                  |                   |                       |             |                                             |                            |
| 364  | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka                     | 04/2000          | 241.00                  | 196.65           | 149.93            | 08/2004               | 09/2011     | 85(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 365  | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka                | 04/2000          | 318.00                  | 207.56           | 160.48            | 08/2004               | 09/2011     | 85(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 366  | HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal                    | 04/2000          | 273.00                  | 522.00           | 475.55            | 03/2005               | 09/2011     | 78(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 367  | GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat   | 12/2003          | 412.78                  | 479.54           | 436.46            | 11/2007               | 09/2011     | 46(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 368  | AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh   | 12/2003          | 217.00                  | 217.00           | 352.26            | 10/2008               | 09/2011     | 35(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 369  | MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu | 03/2005          | 629.00                  | 629.00           | 910.04            | 11/2010               | 09/2011     | 10(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 370  | LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh        | 12/2003          | 225.00                  | 225.00           | 254.49            | 10/2008               | 09/2011     | 35(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 371  | RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar                                   | 12/2003          | 340.00                  | 340.00           | 561.31            | 06/2008               | 09/2011     | 39(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 372  | THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala                                    | 12/2003          | 312.50                  | 312.50           | 602.56            | 03/2009               | 09/2011     | 30(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 373  | ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal                        | 12/2003          | 221.82                  | 221.82           | 241.98            | 11/2008               | 09/2011     | 34(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 374  | TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu                                    | 03/2005          | 576.00                  | 576.00           | 657.66            | 07/2010               | 09/2011     | 14(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 375  | PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu                               | 03/2005          | 285.00                  | 285.00           | 359.10            | 07/2010               | 09/2011     | 14(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 376  | NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka           | 03/2005          | 441.00                  | 441.00           | 908.83            | 07/2010               | 09/2011     | 14(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 377  | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa               | 04/2000          | 228.70                  | 228.70           | 165.14            | 02/2004               | 09/2011     | 91(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 378  | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh                      | 03/2005          | 190.00                  | 190.00           | 227.03            | 01/2009               | 10/2011     | 33(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |
| 379  | DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam                                   | 12/2003          | 225.00                  | 225.00           | 254.16            | 06/2008               | 10/2011     | 40(O)                                       | 0/0                        |
|      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                             |                            |

| S.No | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 380  | NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra                                  | 03/2005          | 168.00                  | 168.00           | 385.27            | 12/2008               | 10/2011     | 34(O)                                       | 0/0                        |
| 381  | JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh                                  | 12/2003          | 276.09                  | 276.09           | 295.27            | 09/2009               | 10/2011     | 25(O)                                       | 0/0                        |
| 382  | END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh           | 01/2008          | 464.00                  | 464.00           | 419.88            | 01/2011               | 10/2011     | 9(O)                                        | 0/0                        |
| 383  | Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu                                        | 04/2009          | 353.37                  | 353.37           | 198.71            | 10/2011               | 10/2011     | 0(O)                                        | 0/0                        |
| 384  | KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan                                | 12/2003          | 275.00                  | 250.39           | 277.08            | 10/2008               | 11/2011     | 37(O)                                       | 0/0                        |
| 385  | SAGAR BY PASS, KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh             | 12/2003          | 151.30                  | 151.30           | 172.23            | 10/2008               | 11/2011     | 37(O)                                       | 0/0                        |
| 386  | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana                      | 05/2009          | 1,108.00                | 2,288.00         | 2,610.80          | 11/2011               | 11/2011     | 0(O)                                        | 0/0                        |
| 387  | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa                        | 04/2000          | 225.00                  | 241.53           | 77.54             | 04/2004               | 12/2011     | 92(O)                                       | 0/0                        |
| 388  | AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh            | 04/2000          | 367.49                  | 367.49           | 453.68            | 03/2005               | 12/2011     | 81(O)                                       | 0/0                        |
| 389  | GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh | 12/2003          | 275.00                  | 275.00           | 296.55            | 09/2007               | 12/2011     | 51(O)                                       | 0/0                        |
| 390  | HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh              | 03/2005          | 220.00                  | 220.00           | 239.26            | 09/2007               | 12/2011     | 51(O)                                       | 0/0                        |
| 391  | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh  | 12/2003          | 155.00                  | 201.66           | 88.13             | 09/2008               | 12/2011     | 39(O)                                       | 0/0                        |
| 392  | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam          | 12/2003          | 230.00                  | 230.00           | 203.38            | 06/2005               | 12/2011     | 78(O)                                       | 0/0                        |
| 393  | VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K            | 12/2003          | 193.09                  | 166.30           | 179.19            | 03/2008               | 12/2011     | 45(O)                                       | 0/0                        |
| 394  | VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K            | 12/2003          | 166.27                  | 193.10           | 147.71            | 03/2008               | 12/2011     | 45(O)                                       | 0/0                        |
| 395  | GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh | 12/2003          | 227.00                  | 227.00           | 394.13            | 10/2008               | 12/2011     | 38(O)                                       | 0/0                        |
| 396  | ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh         | 12/2003          | 340.68                  | 340.68           | 353.85            | 03/2008               | 12/2011     | 45(O)                                       | 0/0                        |
| 397  | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam             | 12/2003          | 280.00                  | 280.00           | 224.96            | 02/2009               | 12/2011     | 34(O)                                       | 0/0                        |

| S.No | Project                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                                 |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                               | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 398  | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam                      | 12/2003          | 200.00<br>-             | 200.00           | 78.90             | 04/2009<br>-          | 12/2011     | 32(O)                                       | 0/0                        |
| 399  | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam                             | 12/2003          | 195.00<br>-             | 195.00           | 172.21            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 400  | KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh                                | 12/2003          | 242.00<br>-             | 242.00           | 393.21            | 12/2008<br>-          | 12/2011     | 36(O)                                       | 0/0                        |
| 401  | UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh                          | 12/2003          | 227.00<br>-             | 227.00           | 363.24            | 12/2008<br>-          | 12/2011     | 36(O)                                       | 0/0                        |
| 402  | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                            | 12/2003          | 237.80<br>-             | 237.80           | 197.55            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 403  | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar                                     | 12/2003          | 332.94<br>-             | 332.94           | 289.08            | 09/2008<br>-          | 12/2011     | 39(O)                                       | 0/0                        |
| 404  | LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh                                | 12/2003          | 198.00<br>-             | 198.00           | 187.06            | 11/2008<br>-          | 12/2011     | 37(O)                                       | 0/0                        |
| 405  | RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh  | 12/2003          | 251.03<br>-             | 251.03           | 276.03            | 10/2008<br>-          | 12/2011     | 38(O)                                       | 0/0                        |
| 406  | RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh | 12/2003          | 229.91<br>-             | 229.91           | 223.12            | 10/2008<br>-          | 12/2011     | 38(O)                                       | 0/0                        |
| 407  | JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar                                           | 12/2003          | 340.00<br>-             | 340.00           | 426.99            | 09/2008<br>-          | 12/2011     | 39(O)                                       | 0/0                        |
| 408  | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam                                                 | 12/2003          | 200.00<br>-             | 200.00           | 255.34            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 409  | SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh                                                 | 03/2005          | 322.00<br>-             | 322.00           | 553.66            | 06/2009<br>-          | 12/2011     | 30(O)                                       | 0/0                        |
| 410  | NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka                                     | 04/2000          | 196.50<br>-             | 196.50           | 233.50            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 411  | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam                                              | 12/2003          | 264.72<br>-             | 264.72           | 246.10            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 412  | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam                                               | 12/2003          | 245.00<br>-             | 245.00           | 476.19            | 03/2008<br>-          | 12/2011     | 45(O)                                       | 0/0                        |
| 413  | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam                                                 | 12/2003          | 225.00<br>-             | 225.00           | 165.57            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 414  | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam                                                  | 12/2003          | 208.00<br>-             | 208.00           | 206.17            | 04/2008<br>-          | 12/2011     | 44(O)                                       | 0/0                        |
| 415  | DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,Assam                                | 12/2003          | 160.00<br>-             | 160.00           | 121.62            | 05/2008<br>-          | 12/2011     | 43(O)                                       | 0/0                        |
| 416  | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                            | 12/2003          | 200.00<br>-             | 200.00           | 188.95            | 06/2008<br>-          | 12/2011     | 42(O)                                       | 0/0                        |
| 417  | THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI,Tamil Nadu                                      | 03/2005          | 280.00<br>-             | 280.00           | 580.67            | 06/2009<br>-          | 12/2011     | 30(O)                                       | 0/0                        |

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 418  | GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh     | 12/2003          | 600.24<br>-             | 600.24           | 692.67            | 10/2009<br>-          | 12/2011     | 26(O)                                       | 0/0                        |
| 419  | KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar             | 12/2003          | 418.04<br>-             | 418.04           | 322.97            | 03/2010<br>-          | 12/2011     | 21(O)                                       | 0/0                        |
| 420  | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh                          | 12/2003          | 355.06<br>-             | 355.06           | 294.66            | 09/2009<br>-          | 12/2011     | 27(O)                                       | 0/0                        |
| 421  | SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu                | 03/2005          | 941.00<br>-             | 941.00           | 1,901.00          | 01/2011<br>-          | 12/2011     | 11(O)                                       | 0/0                        |
| 422  | PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab                                       | 12/2003          | 229.00<br>-             | 284.00           | 338.97            | 05/2010<br>-          | 12/2011     | 19(O)                                       | 0/0                        |
| 423  | ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State           | 02/2008          | 295.00<br>-             | 295.00           | 624.25            | 08/2010<br>-          | 12/2011     | 16(O)                                       | 0/0                        |
| 424  | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana                              | 04/2007          | 486.00<br>-             | 486.00           | 525.47            | 05/2010<br>-          | 12/2011     | 19(O)                                       | 0/0                        |
| 425  | Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State                | 02/2009          | 1,693.75<br>-           | 1,693.75         | 2,492.60          | 08/2011<br>-          | 12/2011     | 4(O)                                        | 0/0                        |
| 426  | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                      | 03/2005          | 516.00<br>-             | 516.00           | 594.18            | 07/2010<br>-          | 01/2012     | 18(O)                                       | 0/0                        |
| 427  | Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh                           | 02/2010          | 390.56<br>-             | 390.56           | 389.36            | 02/2012<br>-          | 02/2012     | 0(O)                                        | 0/0                        |
| 428  | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam               | 12/2003          | 157.47<br>-             | 154.57           | 177.48            | 09/2007<br>-          | 03/2012     | 54(O)                                       | 0/0                        |
| 429  | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar    | 12/2003          | 240.00<br>-             | 240.00           | 263.77            | 10/2008<br>-          | 03/2012     | 41(O)                                       | 0/0                        |
| 430  | SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhy Pradesh | 12/2003          | 203.43<br>-             | 203.43           | 207.85            | 10/2008<br>-          | 03/2012     | 41(O)                                       | 0/0                        |
| 431  | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam                                      | 12/2003          | 175.96<br>-             | 175.96           | 117.25            | 04/2008<br>-          | 03/2012     | 47(O)                                       | 0/0                        |
| 432  | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam                                     | 12/2003          | 198.16<br>-             | 198.16           | 176.97            | 04/2008<br>-          | 03/2012     | 47(O)                                       | 0/0                        |
| 433  | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam                                     | 12/2003          | 217.61<br>-             | 217.61           | 147.12            | 04/2010<br>-          | 03/2012     | 23(O)                                       | 0/0                        |
| 434  | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                               | 12/2003          | 275.00<br>-             | 281.31           | 178.85            | 02/2010<br>-          | 03/2012     | 25(O)                                       | 0/0                        |
| 435  | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala                 | 03/2005          | 557.00<br>-             | 557.00           | 930.92            | 02/2010<br>-          | 05/2012     | 27(O)                                       | 0/0                        |
| 436  | Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra                                      | 11/2009          | 1,110.00<br>-           | 1,110.00         | 1,204.90          | 05/2012<br>-          | 05/2012     | 0(O)                                        | 0/0                        |
| 437  | Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan                                    | 11/2009          | 795.00<br>-             | 795.00           | 804.29            | 05/2012<br>-          | 05/2012     | 0(O)                                        | 0/0                        |
| 438  | Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh                          | 08/2010          | 388.00<br>-             | 388.00           | 340.53            | 05/2012<br>-          | 05/2012     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                               |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                             | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 439  | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar           | 12/2003          | 300.00                  | 300.00           | 165.54            | 10/2008               | 06/2012     | 44(O)                                       | 0/0                        |
| 440  | GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh                                      | 12/2003          | 300.93                  | 300.93           | 294.11            | 10/2009               | 06/2012     | 32(O)                                       | 0/0                        |
| 441  | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State                                           | 12/2003          | 604.00                  | 604.00           | 412.17            | 12/2009               | 06/2012     | 30(O)                                       | 0/0                        |
| 442  | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State              | 12/2003          | 232.45                  | 232.45           | 159.55            | 09/2010               | 06/2012     | 21(O)                                       | 0/0                        |
| 443  | MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra                                     | 12/2009          | 835.00                  | 835.00           | 396.69            | 06/2012               | 06/2012     | 0(O)                                        | 0/0                        |
| 444  | Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State                            | 04/2009          | 1,673.70                | 1,673.70         | 1,526.60          | 10/2011               | 06/2012     | 8(O)                                        | 0/0                        |
| 445  | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra                   | 03/2005          | 940.00                  | 940.00           | 323.19            | 07/2012               | 07/2012     | 0(O)                                        | 0/0                        |
| 446  | PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab                               | 12/2003          | 284.00                  | 359.00           | 119.35            | 05/2008               | 08/2012     | 51(O)                                       | 0/0                        |
| 447  | Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh          | 05/2009          | 572.30                  | 572.30           | 506.79            | 10/2011               | 08/2012     | 10(O)                                       | 0/0                        |
| 448  | LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh | 12/2003          | 407.60                  | 407.60           | 184.35            | 06/2010               | 10/2012     | 28(O)                                       | 0/0                        |
| 449  | LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh             | 12/2003          | 263.17                  | 263.17           | 233.29            | 09/2009               | 10/2012     | 37(O)                                       | 0/0                        |
| 450  | Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra               | 04/2010          | 1,170.52                | 1,170.52         | 4.41              | 06/2011               | 10/2012     | 16(O)                                       | 0/0                        |
| 451  | Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat                 | 03/2010          | 1,509.10                | 1,509.10         | 813.90            | 09/2012               | 10/2012     | 1(O)                                        | 0/0                        |
| 452  | Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh                      | 04/2010          | 1,740.00                | 1,740.00         | 1,005.10          | 10/2012               | 10/2012     | 0(O)                                        | 0/0                        |
| 453  | WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra                         | 02/2011          | 193.45                  | 193.45           | 29.04             | 11/2012               | 11/2012     | 0(O)                                        | 0/0                        |
| 454  | UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka                         | 11/2010          | 680.00                  | 680.00           | -                 | 11/2012               | 11/2012     | 0(O)                                        | 0/0                        |
| 455  | SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal                                     | 12/2003          | 225.00                  | 225.00           | 175.62            | 07/2008               | 12/2012     | 53(O)                                       | 0/0                        |
| 456  | GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa                                         | 04/2000          | 263.27                  | 263.27           | 250.29            | 02/2004               | 12/2012     | 106(O)                                      | 0/0                        |
| 457  | Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan                                                 | 06/2010          | 792.06                  | 792.06           | 389.32            | 12/2012               | 12/2012     | 0(O)                                        | 0/0                        |
| 458  | Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd                                                | 08/2010          | 625.07                  | 625.07           | 665.96            | 01/2013               | 01/2013     | 0(O)                                        | 0/0                        |

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 459  | Bijapur-Hungund Section - [N24000137]NHAI, Karnataka                                 | 09/2010          | 748.00                  | 748.00           | 958.73            | 09/2010               | 03/2013     | 30(O)                                       | 0/0                        |
| 460  | Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka       | 09/2010          | 946.00                  | 946.00           | -                 | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 461  | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu | 09/2010          | 852.00                  | 852.00           | 303.83            | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 462  | KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka                           | 09/2010          | 671.00                  | 671.00           | 173.17            | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 463  | PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra                                     | 10/2010          | 1,724.55                | 1,724.55         | 107.56            | 03/2013               | 03/2013     | 0(O)                                        | 0/0                        |
| 464  | Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh                            | 10/2010          | 1,175.00                | 1,175.00         | 138.67            | 04/2013               | 04/2013     | 0(O)                                        | 0/0                        |
| 465  | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh     | 11/2010          | 1,585.00                | 1,585.00         | 198.67            | 05/2013               | 05/2013     | 0(O)                                        | 0/0                        |
| 466  | DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka                                        | 12/2010          | 453.00                  | 453.00           | 122.73            | 05/2013               | 05/2013     | 0(O)                                        | 0/0                        |
| 467  | INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh                                 | 11/2010          | 325.00                  | 325.00           | 138.67            | 05/2013               | 05/2013     | 0(O)                                        | 0/0                        |
| 468  | AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh       | 12/2003          | 348.16                  | 348.16           | 117.69            | 09/2007               | 06/2013     | 69(O)                                       | 0/0                        |
| 469  | AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab                                         | 05/2010          | 705.00                  | 705.00           | 834.69            | 11/2012               | 06/2013     | 7(O)                                        | 0/0                        |
| 470  | MURADABAD-BAREILY - [N24000154]NHAI, Uttar Pradesh                                   | 04/2010          | 1,267.00                | 1,267.00         | -                 | 06/2013               | 06/2013     | 0(O)                                        | 0/0                        |
| 471  | BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka                                   | 12/2010          | 480.00                  | 480.00           | -                 | 06/2013               | 06/2013     | 0(O)                                        | 0/0                        |
| 472  | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam         | 12/2003          | 199.81                  | 385.13           | 30.37             | 04/2009               | 07/2013     | 51(O)                                       | 0/0                        |
| 473  | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam        | 12/2003          | 155.04                  | 280.13           | 39.26             | 11/2008               | 07/2013     | 56(O)                                       | 0/0                        |
| 474  | DEOLI-KOTA - [N24000148]NHAI, Rajasthan                                              | 01/2011          | 953.00                  | 593.00           | 67.10             | 07/2013               | 07/2013     | 0(O)                                        | 0/0                        |
| 475  | CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka                                | 03/2011          | 839.00                  | 839.00           | -                 | 08/2013               | 08/2013     | 0(O)                                        | 0/0                        |
| 476  | New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu          | 09/2010          | 1,655.00                | 1,655.00         | 4.34              | 09/2013               | 09/2013     | 0(O)                                        | 0/0                        |
| 477  | 4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka        | 03/2011          | 359.00                  | 359.00           | 0.99              | 09/2013               | 09/2013     | 0(O)                                        | 0/0                        |
| 478  | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala             | 02/2010          | 617.00                  | 617.00           | 154.52            | 08/2012               | 10/2013     | 14(O)                                       | 0/0                        |
| 479  | Talegaon-amravati - [N24000140]NHAI, Maharashtra                                     | 11/2009          | 567.00                  | 567.00           | 10.04             | 11/2013               | 11/2013     | 0(O)                                        | 0/0                        |

| S.No                        | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|-----------------------------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|                             |                                                                                           |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1                           | 2                                                                                         | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 480                         | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam         | 12/2003          | 167.64<br>-             | 167.64           | 40.71             | 11/2008<br>-          | 12/2013     | 61(O)                                       | 0/0                        |
| 481                         | HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam                      | 12/2003          | 212.00<br>-             | 212.00           | 40.29             | 09/2007<br>-          | 12/2013     | 75(O)                                       | 0/0                        |
| 482                         | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam                                       | 12/2003          | 196.00<br>-             | 196.00           | 27.94             | 07/2009<br>-          | 12/2013     | 53(O)                                       | 0/0                        |
| 483                         | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State                                    | 02/2011          | 2,498.76<br>-           | 2,498.76         | -                 | 08/2014<br>-          | 08/2014     | 0(O)                                        | 0/0                        |
| 484                         | PANIPAT-ROHTAK - [N24000151]NHAI,Haryana                                                  | 04/2011          | 807.00<br>-             | 807.00           | 300.12            | 10/2014<br>-          | 10/2014     | 0(O)                                        | 0/0                        |
| Total                       |                                                                                           |                  | 59,725.85<br>-          | 61,189.26        | 43,561.18         |                       |             |                                             | 0/0                        |
| <b>Shipping &amp; Ports</b> |                                                                                           |                  |                         |                  |                   |                       |             |                                             |                            |
| 485                         | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala     | 03/2007          | 245.67<br>-             | 298.17           | 294.07            | 04/2009<br>-          | 02/2011     | 22(O)                                       | 0/0                        |
| 486                         | Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka      | 06/2006          | 230.00<br>-             | 272.50           | 219.00            | 12/2010<br>-          | 06/2011     | 6(O)                                        | 0/0                        |
| 487                         | MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK,Tamil Nadu                              | 10/2004          | 196.25<br>-             | 196.25           | -                 | 06/2006<br>09/2011    | 09/2011     | 0(R2)                                       | 0/0                        |
| 488                         | ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala              | 12/2010          | 241.50<br>-             | 241.50           | 48.10             | 09/2011<br>-          | 09/2011     | 0(O)                                        | 0/0                        |
| 489                         | ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat     | 01/2002          | 165.00<br>165.00        | 165.00           | 121.41            | 12/2005<br>01/2008    | 10/2011     | 45(R3)                                      | 0/0                        |
| 490                         | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra        | 10/2007          | 359.44<br>-             | 359.44           | 351.81            | 04/2011<br>06/2011    | 11/2011     | 5(R3)                                       | 0/0                        |
| 491                         | Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra                        | 04/2009          | 290.85<br>305.00        | 305.00           | 86.46             | 06/2011<br>01/2012    | 01/2012     | 0(R3)                                       | 0/0                        |
| 492                         | ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra        | 11/2007          | 1,061.96<br>1,077.60    | 1,082.06         | 360.80            | 03/2012<br>-          | 03/2012     | 0(O)                                        | 0/0                        |
| 493                         | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala         | 03/2009          | 3,500.00<br>-           | 3,500.00         | -                 | 01/2012<br>-          | 03/2012     | 2(O)                                        | 0/0                        |
| 494                         | Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat | 06/2010          | 277.00<br>-             | 277.00           | 0.04              | 03/2012<br>-          | 03/2012     | 0(O)                                        | 0/0                        |
| 495                         | Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra                   | 04/2009          | 277.03<br>280.00        | 277.03           | 55.40             | 12/2011<br>05/2012    | 05/2012     | 0(R3)                                       | 0/0                        |

|       |                                                                                             |                  |                         |                  |                   | Date of Commissioning |             | Delay w.r.t. Original /Revised (in months) | Milestones Achieved/ Total |     |
|-------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|--------------------------------------------|----------------------------|-----|
| S.No  | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Original / Revised    | Anticipated |                                            |                            |     |
| 1     | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                          | 10                         |     |
| 496   | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra | 11/2007          | 1,228.00<br>-           | 1,460.00         | 568.86            | 12/2010<br>-          | 09/2012     | 21(O)                                      | 0/0                        |     |
| 497   | ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra          | 08/2008          | 1,066.91<br>-           | 968.35           | 222.91            | 09/2012<br>-          | 09/2012     | 0(O)                                       | 0/0                        |     |
| 498   | Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh     | 02/2010          | 444.10<br>-             | 444.10           | -                 | 06/2010<br>-          | 11/2012     | 29(O)                                      | 0/0                        |     |
| 499   | Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra   | 08/2010          | 612.72<br>627.64        | 627.64           | 83.51             | 12/2012<br>-          | 12/2012     | 0(O)                                       | 0/0                        |     |
| 500   | C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat           | 04/2005          | 882.00<br>-             | 1,060.00         | 0.16              | 02/2011<br>-          | 03/2013     | 25(O)                                      | 0/0                        |     |
| 501   | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat               | 12/2005          | 702.00<br>-             | 755.50           | -                 | 03/2011<br>-          | 03/2013     | 24(O)                                      | 0/0                        |     |
| 502   | SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala            | 03/2008          | 375.00<br>272.50        | 272.50           | -                 | 01/2009<br>-          | 05/2013     | 52(O)                                      | 0/0                        |     |
| 503   | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu           | 10/2002          | 150.00<br>600.00        | 600.00           | 67.00             | 03/2006<br>-          | 12/2013     | 93(O)                                      | 0/0                        |     |
| 504   | Acquistion of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra    | 10/2010          | 1,028.10<br>1,012.23    | 1,028.10         | 202.04            | 12/2013<br>-          | 12/2013     | 0(O)                                       | 0/0                        |     |
| 505   | Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra   | 10/2010          | 966.46<br>-             | 994.82           | 189.92            | 02/2014<br>-          | 02/2014     | 0(O)                                       | 0/0                        |     |
| 506   | DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra      | 10/2005          | 800.00<br>-             | 800.00           | 5.92              | 10/2008<br>-          | -           | -                                          | 0/0                        |     |
| 507   | DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa                         | 12/2005          | 154.84<br>-             | 253.36           | -                 | 12/2007<br>01/2009    | -           | -                                          | 0/0                        |     |
| 508   | DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu                        | 09/2006          | 399.13<br>-             | 399.13           | -                 | 08/2010<br>-          | -           | -                                          | 0/0                        |     |
| 509   | DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu                    | 09/2006          | 370.00<br>-             | 370.00           | -                 | 08/2010<br>-          | -           | -                                          | 0/0                        |     |
| 510   | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu                       | 06/2005          | 2,427.40<br>-           | 2,427.40         | 821.39            | 10/2008<br>-          | -           | -                                          | 0/0                        |     |
| Total |                                                                                             |                  | 18,451.36               | 19,434.85        | 3,698.80          |                       |             |                                            |                            | 0/0 |

Telecommunications

| S.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 511  | GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra            | 09/2008          | 1,799.94 -              | 1,799.94         | 251.53            | 09/2009 -             | 02/2010     | 5(O)                                        | 0/0                        |
| 512  | Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State | 12/2007          | 952.88 -                | 952.88           | -                 | 03/2010 -             | 10/2010     | 7(O)                                        | 0/0                        |
| 513  | GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana                         | 01/2008          | 192.48 -                | 192.48           | 119.41            | 03/2009 -             | 02/2011     | 23(O)                                       | 0/0                        |
| 514  | GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab                | 02/2008          | 373.94 -                | 373.94           | 199.63            | 12/2008 -             | 02/2011     | 26(O)                                       | 0/0                        |
| 515  | GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa                | 11/2007          | 277.34 -                | 377.54           | 308.13            | 03/2009 -             | 02/2011     | 23(O)                                       | 0/0                        |
| 516  | UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal                | 01/2009          | 149.15 158.72           | 158.72           | 76.55             | 06/2009 -             | 02/2011     | 20(O)                                       | 0/0                        |
| 517  | Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam                           | 06/2007          | 336.81 -                | 336.81           | 155.71            | 01/2009 -             | 02/2011     | 25(O)                                       | 0/0                        |
| 518  | GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar                 | 10/2007          | 366.00 -                | 366.00           | 226.39            | 10/2008 -             | 02/2011     | 28(O)                                       | 0/0                        |
| 519  | GSM equipment of 1900000Lines (2G) 401700 lines 3( - [N26000091]BSNL,Tamil Nadu            | 01/2009          | 760.20 -                | 1,100.00         | 813.60            | - 03/2011             | 02/2011     | -1(R3)                                      | 0/1                        |
| 520  | GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh       | 01/2009          | 922.91 -                | 922.91           | 346.90            | 01/2010 -             | 02/2011     | 13(O)                                       | 0/0                        |
| 521  | GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala               | 01/2009          | 848.70 -                | 848.70           | 675.35            | 01/2010 -             | 02/2011     | 13(O)                                       | 0/0                        |
| 522  | GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu            | 01/2009          | 315.19 -                | 315.19           | 132.24            | 01/2010 -             | 02/2011     | 13(O)                                       | 0/0                        |
| 523  | GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan             | 06/2007          | 601.49 -                | 601.49           | 495.72            | 12/2008 -             | 03/2011     | 27(O)                                       | 0/0                        |
| 524  | GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh           | 05/2007          | 335.91 -                | 335.91           | 182.45            | 03/2009 -             | 03/2011     | 24(O)                                       | 0/0                        |
| 525  | GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab                 | 09/2008          | 241.49 -                | 241.49           | 112.61            | 09/2009 -             | 03/2011     | 18(O)                                       | 0/0                        |
| 526  | GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh         | 10/2008          | 336.84 -                | 336.84           | 35.75             | 10/2009 -             | 03/2011     | 17(O)                                       | 0/0                        |
| 527  | GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal          | 02/2008          | 584.33 -                | 584.33           | 398.08            | 02/2009 -             | 03/2011     | 25(O)                                       | 0/0                        |

| S.No | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|      |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1    | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 528  | GSM equipment of 1867000Lines (2G) 383000 lines 3( - [N26000089]BSNL,Gujarat        | 08/2008          | 868.00<br>-             | 868.00           | 362.62            | 08/2009<br>-          | 03/2011     | 19(O)                                       | 0/0                        |
| 529  | GSM equipment of 1625000Lines (2G) 325000 lines 3( - [N26000090]BSNL,Madhya pradesh | 11/2009          | 916.70<br>-             | 916.70           | 280.72            | 11/2010<br>-          | 03/2011     | 4(O)                                        | 0/0                        |
| 530  | GSM equipment of 1700000Lines (2G) 234100 lines 3( - [N26000092]BSNL,Karnataka      | 10/2008          | 677.75<br>719.90        | 719.90           | 461.56            | 10/2009<br>-          | 03/2011     | 17(O)                                       | 0/0                        |
| 531  | CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi                      | 12/2005          | 249.00<br>229.41        | 229.41           | 66.20             | 02/2007<br>-          | 08/2011     | 54(O)                                       | 0/0                        |
| 532  | CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra                    | 01/2006          | 247.00<br>-             | 247.00           | 75.89             | 02/2007<br>-          | 08/2011     | 54(O)                                       | 0/0                        |
| 533  | FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra                         | 04/2010          | 389.86<br>-             | 389.86           | 3.06              | 09/2011<br>-          | 09/2011     | 0(O)                                        | 0/0                        |
| 534  | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State           | 10/2009          | 384.00<br>-             | 384.00           | 20.90             | 10/2010<br>-          | 03/2012     | 17(O)                                       | 0/0                        |
| 535  | PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State               | 11/2003          | 250.00<br>-             | 425.51           | 80.47             | 12/2005<br>-          | -           | -                                           | 0/0                        |
| 536  | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra     | 06/2006          | 231.38<br>-             | 168.30           | -                 | 10/2007<br>-          | -           | -                                           | 0/0                        |
| 537  | MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State                     | 11/2008          | 350.00<br>-             | 350.00           | -                 | -<br>-                | -           | -                                           | 0/0                        |
| 538  | Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State   | 05/2006          | 1,077.00<br>-           | 1,077.00         | -                 | 03/2009<br>-          | -           | -                                           | 0/0                        |
| 539  | Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State                    | 08/2006          | 424.00<br>-             | 424.00           | -                 | 03/2009<br>-          | -           | -                                           | 0/0                        |
| 540  | Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State            | 08/2006          | 590.10<br>-             | 590.10           | -                 | 03/2009<br>-          | -           | -                                           | 0/0                        |
| 541  | Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State      | 12/2007          | 545.50<br>-             | 545.50           | -                 | 03/2010<br>-          | -           | -                                           | 0/0                        |
| 542  | Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State                    | 02/2007          | 154.03<br>-             | 154.03           | -                 | 03/2010<br>-          | -           | -                                           | 0/0                        |
| 543  | Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State                  | 03/2008          | 355.92<br>-             | 355.92           | -                 | 03/2010<br>-          | -           | -                                           | 0/0                        |
| 544  | Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State                   | 02/2007          | 477.00<br>-             | 477.00           | -                 | 03/2010<br>-          | -           | -                                           | 0/0                        |
| 545  | Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State    | 12/2007          | 152.65<br>-             | 152.65           | -                 | 03/2010<br>-          | -           | -                                           | 0/0                        |
| 546  | Procurement of DXC equipment - [N26000074]BSNL,Multi State                          | 02/2008          | 229.00<br>-             | 229.00           | -                 | 03/2010<br>-          | -           | -                                           | 0/0                        |

| S.No               | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original / Revised (in months) | Milestones Achieved/ Total |
|--------------------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|---------------------------------------------|----------------------------|
|                    |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                             |                            |
| 1                  | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                           | 10                         |
| 547                | GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh | 02/2009          | 625.53                  | 625.53           | -                 | 02/2010               | -           | -                                           | 0/0                        |
| 548                | GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh    | 09/2009          | 624.75                  | 624.75           | -                 | 09/2010               | -           | -                                           | 0/0                        |
| 549                | GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal     | 06/2008          | 170.23                  | 170.23           | -                 | 06/2009               | -           | -                                           | 0/0                        |
| 550                | GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd    | 03/2008          | 328.13                  | 328.12           | 164.58            | 03/2009               | -           | -                                           | 0/0                        |
|                    | <b>Total</b>                                                                        |                  | 19,713.13               | 20,297.68        | 6,046.05          |                       |             |                                             | 0/1                        |
|                    |                                                                                     |                  | -                       |                  |                   |                       |             |                                             |                            |
|                    | <b>Urban Development</b>                                                            |                  |                         |                  |                   |                       |             |                                             |                            |
| 551                | BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka                            | 05/2006          | 6,395.00                | 11,609.00        | 2,267.57          | 12/2011               | 03/2013     | 15(O)                                       | 6/6                        |
| 552                | C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra    | 11/2006          | 114.18<br>173.08        | 173.08           | -                 | 04/2009               | -           | -                                           | 0/0                        |
|                    | <b>Total</b>                                                                        |                  | 6,509.18                | 11,782.08        | 2,267.57          |                       |             |                                             | 6/6                        |
|                    |                                                                                     |                  | -                       |                  |                   |                       |             |                                             |                            |
|                    | <b>Water Resources</b>                                                              |                  |                         |                  |                   |                       |             |                                             |                            |
| 553                | PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam                                       | 01/2001          | 542.90                  | 1,187.00         | 35.49             | 12/2007               | 12/2012     | 60(O)                                       | 0/0                        |
|                    | <b>Total</b>                                                                        |                  | 542.90                  | 1,187.00         | 35.49             |                       |             |                                             | 0/0                        |
|                    |                                                                                     |                  | -                       |                  |                   |                       |             |                                             |                            |
| <b>Grand Total</b> |                                                                                     |                  | 614,127.75              | 733,611.82       | 319,374.21        |                       |             |                                             | 948/2291                   |

## Sector wise current status of projects on the Flash Report

### Urban Development

#### I. Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

#### II. Brief Analysis


**Project Status with respect to Original Schedule: Out of 2 projects, 1 project are delayed .1 project do not have fixed dates of commissioning.**

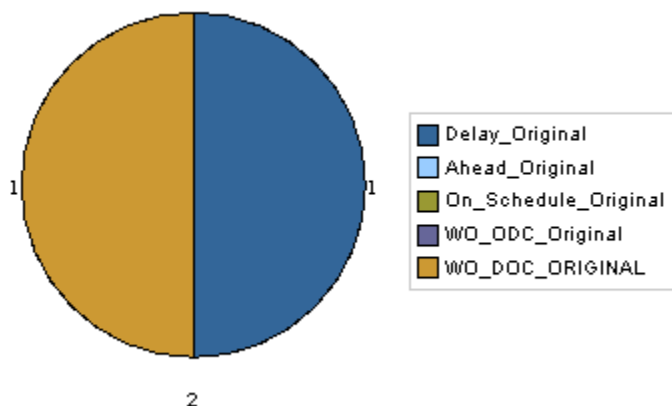

#### III. Investment Scenario

**The Total Original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 6509.18 crore but this was subsequently revised to Rs. 11782.08 crore implying a cost overrun of 81%. The expenditure incurred on these projects till August, 2011 is Rs. 2267.57 crore, which is 19.2% of the revised cost of the projects.**

Figures are in Rs. Crore

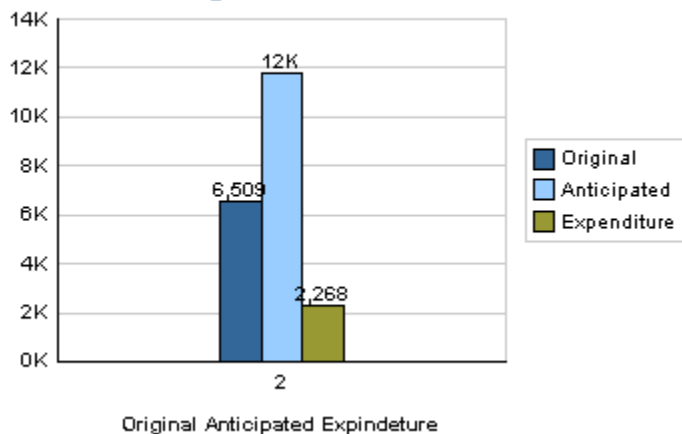

## Sector wise current status of projects on the Flash Report

### Telecommunications


#### I. Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 40 |
| Number of Projects On Schedule | 1  |
| Number of Projects Delayed     | 3  |

Number of Projects Without Date Of Commissioning 36

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 40 projects, 1 project are on schedule and 3 projects are delayed .36 projects do not have fixed dates of commissioning.

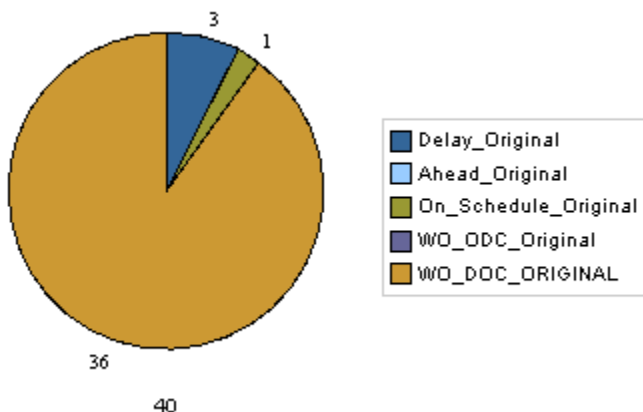

#### III. Investment Scenario

**The Total Original cost of implementation of 40 projects when sanctioned, was of the order of Rs. 19713.13 crore but this was subsequently revised to Rs. 20297.68 crore implying a cost overrun of 3%. The expenditure incurred on these projects till August, 2011 is Rs. 6046.05 crore, which is 29.8% of the revised cost of the projects.**

Figures are in Rs. Crore

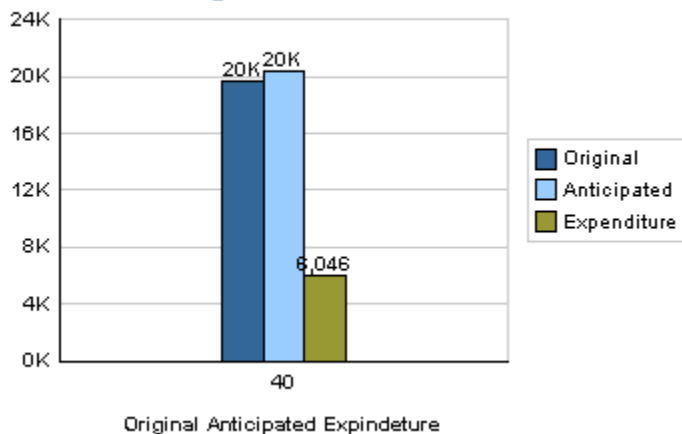

## Sector wise current status of projects on the Flash Report

### Shipping & Ports


#### I. Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 26 |
| Number of Projects On Schedule | 7  |
| Number of Projects Delayed     | 12 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 7 |
|--------------------------------------------------|---|

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 26 projects, 7 projects are on schedule and 12 projects are delayed .7 projects do not have fixed dates of commissioning.

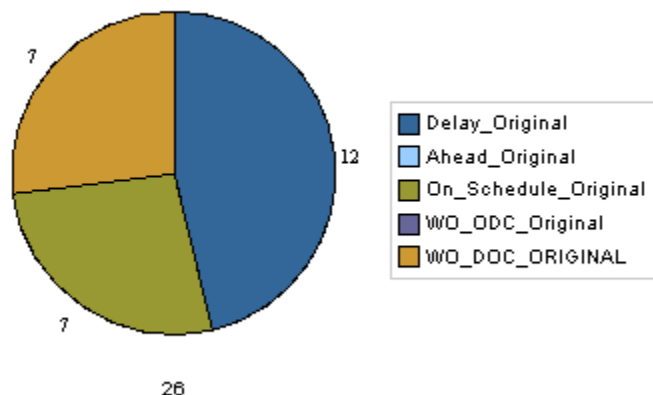

#### III. Investment Scenario

The Total Original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 18451.36 crore but this was subsequently revised to Rs. 19434.85 crore implying a cost overrun of 5.3%. The expenditure incurred on these projects till August, 2011 is Rs. 3698.8 crore, which is 19% of the revised cost of the projects.

Figures are in Rs. Crore

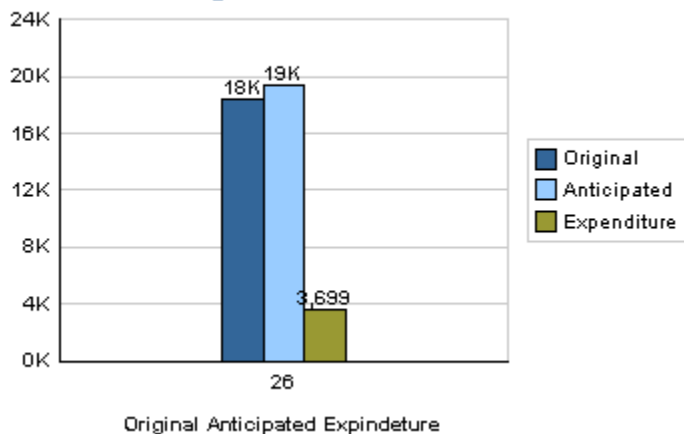

## Sector wise current status of projects on the Flash Report


### Road Transport & Highways

#### I. Current Status:

|                                |     |
|--------------------------------|-----|
| Number of Projects             | 121 |
| Number of Projects On Schedule | 30  |
| Number of Projects Delayed     | 91  |

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 121 projects, 30 projects are on schedule and 91 projects are delayed.

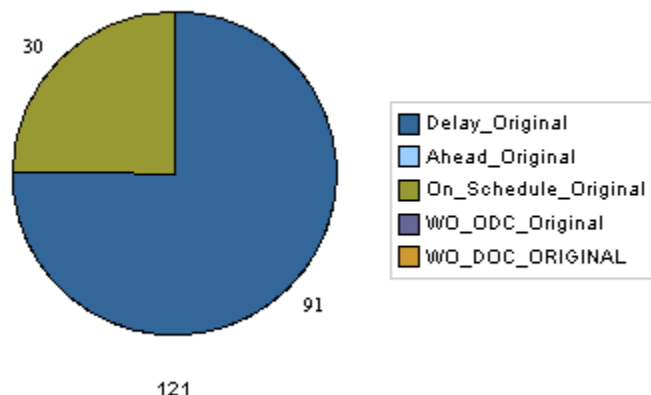

#### III. Investment Scenario

The Total Original cost of implementation of 121 projects when sanctioned, was of the order of Rs. 59725.85 crore but this was subsequently revised to Rs. 61189.26 crore implying a cost overrun of 2.5%. The expenditure incurred on these projects till August, 2011 is Rs. 43561.18 crore, which is 71.2% of the revised cost of the projects.

Figures are in Rs. Crore

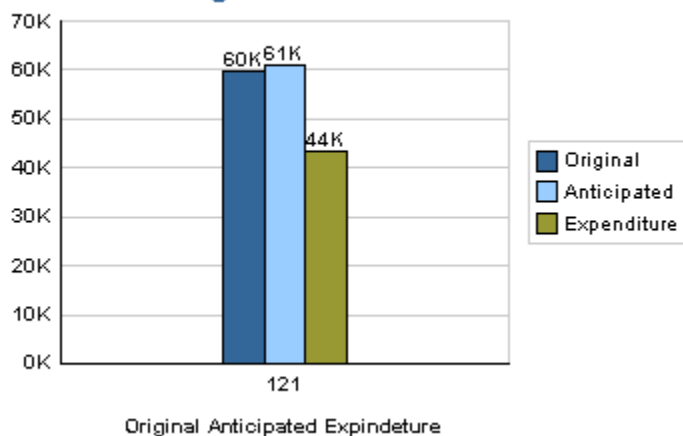

## Sector wise current status of projects on the Flash Report


### Railways

#### I. Current Status:

|                                                           |     |
|-----------------------------------------------------------|-----|
| Number of Projects                                        | 134 |
| Number of Projects On Schedule                            | 14  |
| Number of Projects Delayed                                | 27  |
| Number of Projects Ahead                                  | 2   |
| Number of Projects Without Original Date of Commissioning | 26  |
| Number of Projects Without Date Of Commissioning          | 65  |

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 134 projects, 2 projects are ahead of schedule, 14 projects are on schedule and 27 projects are delayed .65 projects do not have fixed dates of commissioning.26 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

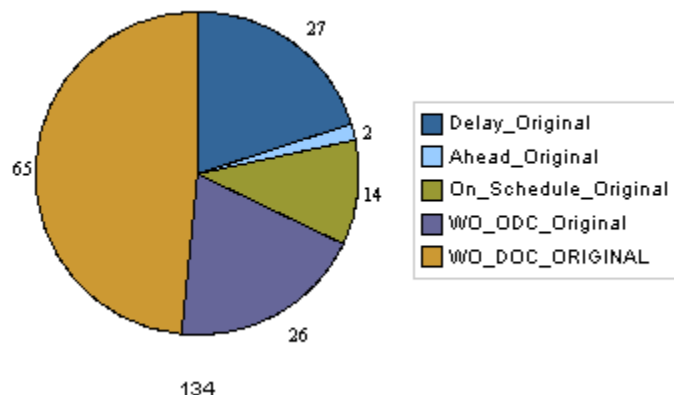

#### III. Investment Scenario

**The Total Original cost of implementation of 134 projects when sanctioned, was of the order of Rs. 65810.63 crore but this was subsequently revised to Rs. 131493.76 crore implying a cost overrun of 99.8%. The expenditure incurred on these projects till August, 2011 is Rs. 54467.84 crore, which is 41.4% of the revised cost of the projects.**

Figures are in Rs. Crore

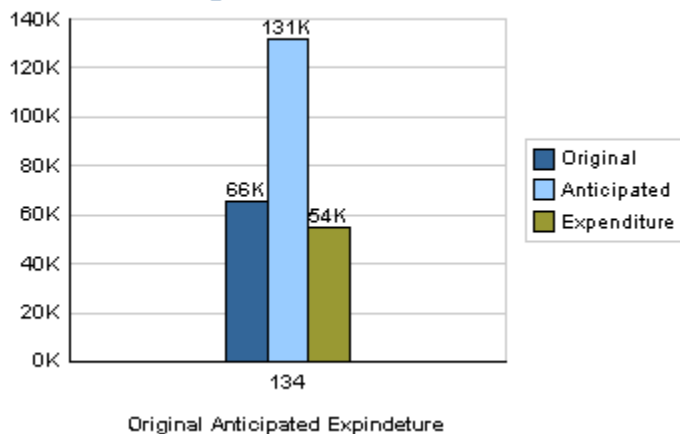

## Sector wise current status of projects on the Flash Report

### Power


#### I. Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 83 |
| Number of Projects On Schedule | 33 |
| Number of Projects Delayed     | 47 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 2 |
| Number of Projects Without Date Of Commissioning          | 1 |


#### II. Brief Analysis

Project Status with respect to Original Schedule: Out of 83 projects, 33 projects are on schedule and 47 projects are delayed .1 project do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

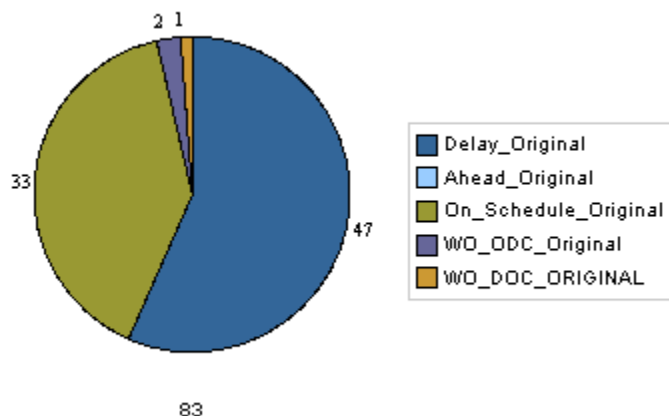

#### III. Investment Scenario

The Total Original cost of implementation of 83 projects when sanctioned, was of the order of Rs. 180012.22 crore but this was subsequently revised to Rs. 186095.99 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till August, 2011 is Rs. 88475.61 crore, which is 47.5% of the revised cost of the projects.

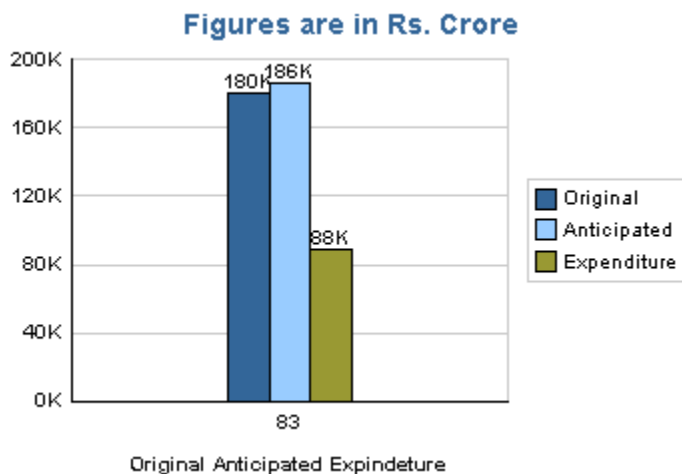

## Sector wise current status of projects on the Flash Report


### Petroleum

#### I. Current Status:

|                                                           |    |
|-----------------------------------------------------------|----|
| Number of Projects                                        | 71 |
| Number of Projects On Schedule                            | 27 |
| Number of Projects Delayed                                | 34 |
| Number of Projects Ahead                                  | 3  |
| Number of Projects Without Original Date of Commissioning | 1  |
| Number of Projects Without Date Of Commissioning          | 6  |

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 71 projects, 3 projects are ahead of schedule, 27 projects are on schedule and 34 projects are delayed .6 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

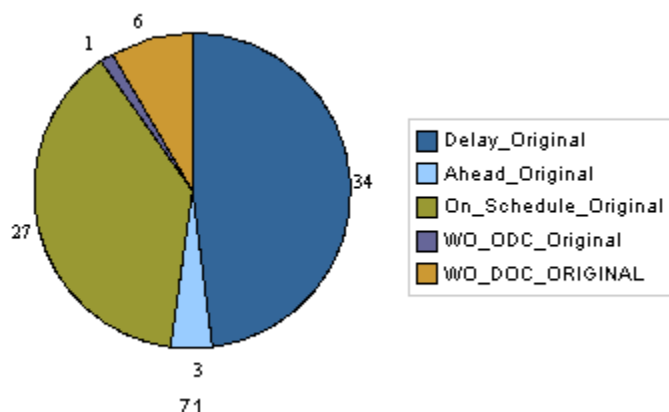

#### III. Investment Scenario

The Total Original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 153918.05 crore but this was subsequently revised to Rs. 161693.92 crore implying a cost overrun of 5.1%. The expenditure incurred on these projects till August, 2011 is Rs. 53108.66 crore, which is 32.8% of the revised cost of the projects.

Figures are in Rs. Crore

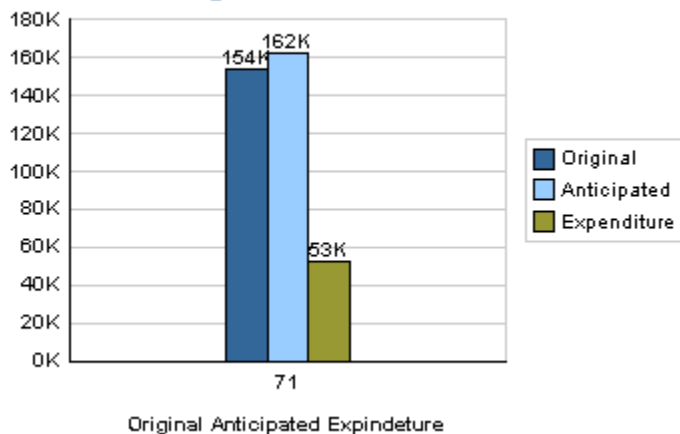

## Sector wise current status of projects on the Flash Report

### Steel


#### I. Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 12 |
| Number of Projects On Schedule | 2  |
| Number of Projects Delayed     | 1  |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 9 |
|-----------------------------------------------------------|---|

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 12 projects, 2 projects are on schedule and 1 project are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

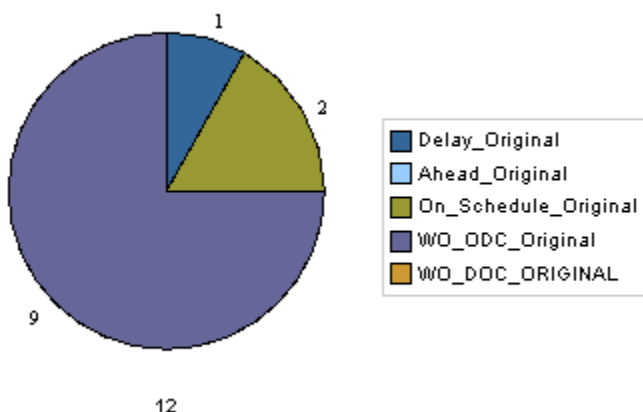

#### III. Investment Scenario

The Total Original cost of implementation of 12 projects when sanctioned, was of the order of Rs. 34591.72 crore but this was subsequently revised to Rs. 55969.91 crore implying a cost overrun of 61.8%. The expenditure incurred on these projects till August, 2011 is Rs. 26394.12 crore, which is 47.2% of the revised cost of the projects.

Figures are in Rs. Crore

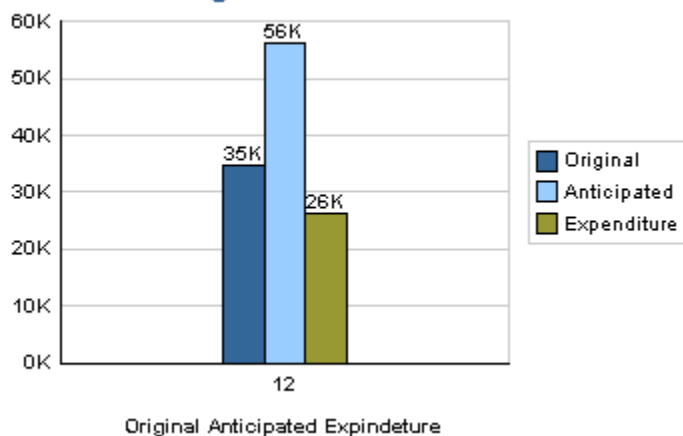

## Sector wise current status of projects on the Flash Report

### Fertilisers


#### I. Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 6 |
| Number of Projects On Schedule | 2 |
| Number of Projects Delayed     | 3 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 1 |
|-----------------------------------------------------------|---|

#### II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

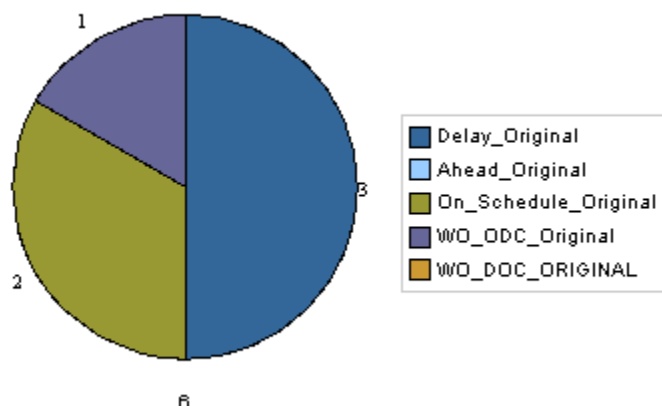

#### III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till August, 2011 is Rs. 934.71 crore, which is 17.6% of the revised cost of the projects.

Figures are in Rs. Crore

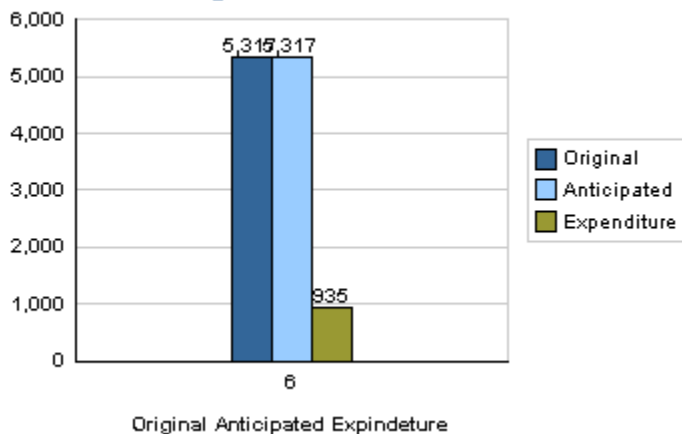

## Sector wise current status of projects on the Flash Report

### Coal


#### I. Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 46 |
| Number of Projects On Schedule | 16 |
| Number of Projects Delayed     | 17 |

|                                                           |    |
|-----------------------------------------------------------|----|
| Number of Projects Without Original Date of Commissioning | 12 |
| Number of Projects Without Date Of Commissioning          | 1  |

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 46 projects, 16 projects are on schedule and 17 projects are delayed .1 project do not have fixed dates of commissioning.12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

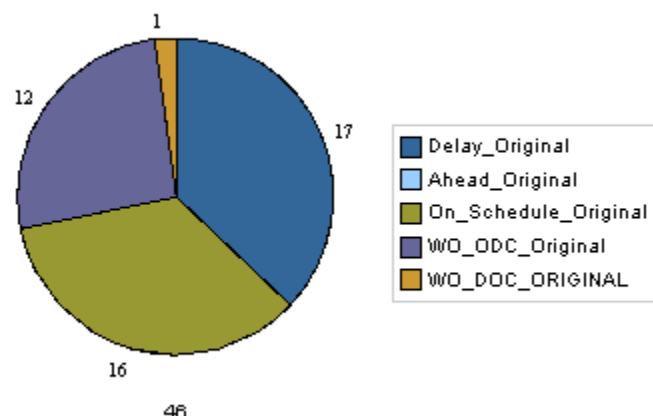

#### III. Investment Scenario

**The Total Original cost of implementation of 46 projects when sanctioned, was of the order of Rs. 26631.65 crore but this was subsequently revised to Rs. 30018.68 crore implying a cost overrun of 12.7%. The expenditure incurred on these projects till August, 2011 is Rs. 11664.97 crore, which is 38.9% of the revised cost of the projects.**

Figures are in Rs. Crore

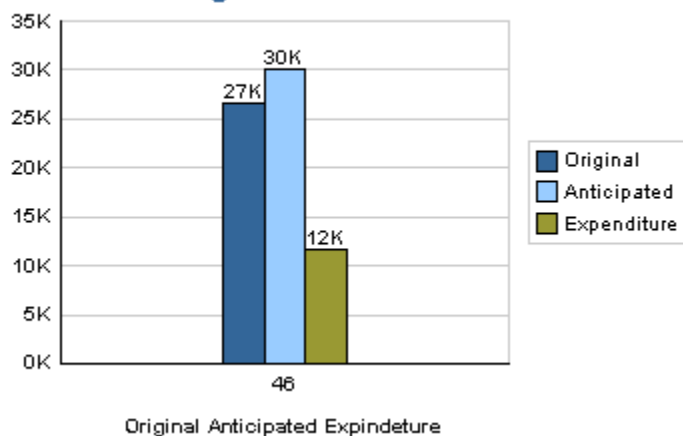

## Sector wise current status of projects on the Flash Report


### Civil Aviation

#### I. Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 5 |
| Number of Projects On Schedule | 2 |
| Number of Projects Delayed     | 3 |

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 5 projects, 2 projects are on schedule and 3 projects are delayed.

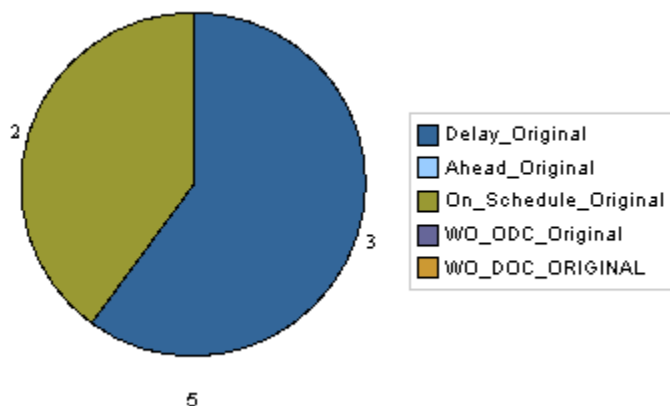

#### III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4123.24 crore but this was subsequently revised to Rs. 5202.62 crore implying a cost overrun of 26.2%. The expenditure incurred on these projects till August, 2011 is Rs. 2771.84 crore, which is 53.3% of the revised cost of the projects.

Figures are in Rs. Crore

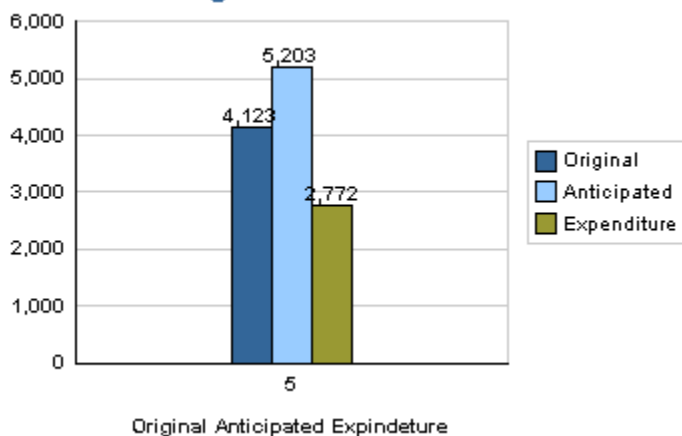

## Sector wise current status of projects on the Flash Report


### Atomic Energy

#### I. Current Status:

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects                                        | 4 |
| Number of Projects Delayed                                | 3 |
| Number of Projects Without Original Date of Commissioning | 1 |

#### II. Brief Analysis


**Project Status with respect to Original Schedule:** Out of 4 projects, 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

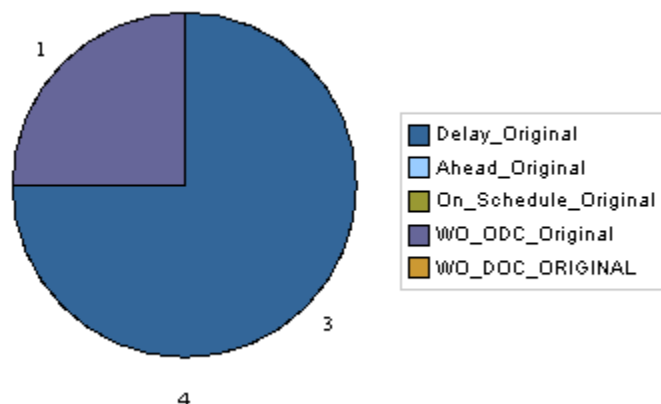

#### III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till August, 2011 is Rs. 19132.37 crore, which is 56.2% of the revised cost of the projects.

Figures are in Rs. Crore

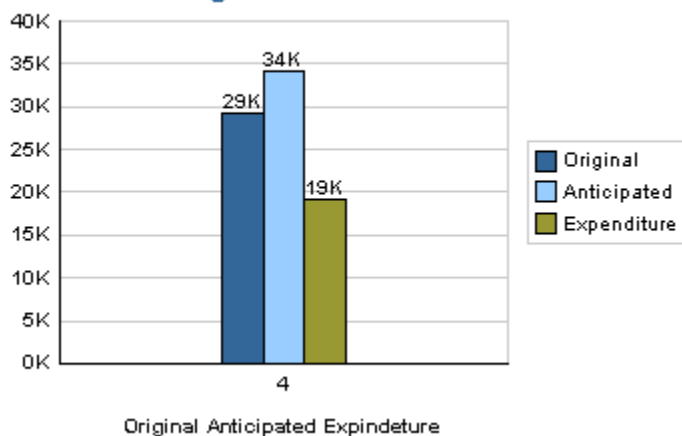

# *ANNEXURES*

**CENTRAL PROJECTS AS ON 01.09.2011**

| <b>SN</b>    | <b>STATE</b>   | <b>NO OF PROJECTS</b> | <b>COST ORIGINAL</b> | <b>COST ANTICIPATED</b> | <b>CUMMULATIVE EXPENDITURE</b> |
|--------------|----------------|-----------------------|----------------------|-------------------------|--------------------------------|
| 1            | Andhra Pradesh | 30                    | 30608.05             | 36641.91                | 20653.49                       |
| 2            | Arunachal Pr.  | 4                     | 9512.22              | 9610.51                 | 6995.21                        |
| 3            | Assam          | 38                    | 24189.38             | 32032.81                | 16697.27                       |
| 4            | Bihar          | 26                    | 27168.57             | 31861.52                | 20461.54                       |
| 5            | Chhatisgarh    | 19                    | 22504.78             | 37937.78                | 15657.71                       |
| 6            | Delhi          | 1                     | 249.00               | 229.41                  | 66.20                          |
| 7            | Goa            | 1                     | 204.73               | 204.73                  | 39.57                          |
| 8            | Gujarat        | 23                    | 28271.24             | 29230.35                | 4684.29                        |
| 9            | Haryana        | 10                    | 5337.83              | 7054.75                 | 4724.45                        |
| 10           | Himachal Pr.   | 6                     | 14761.16             | 14843.44                | 12010.86                       |
| 11           | J & K          | 8                     | 8293.37              | 27185.56                | 11512.21                       |
| 12           | Jharkhandd     | 18                    | 8758.17              | 13349.17                | 5851.80                        |
| 13           | Karnataka      | 27                    | 31565.39             | 39116.07                | 14805.96                       |
| 14           | Kerala         | 9                     | 7247.37              | 7197.37                 | 2776.47                        |
| 15           | Madhya pradesh | 23                    | 16926.11             | 17158.42                | 5998.29                        |
| 16           | Maharashtra    | 52                    | 72470.80             | 87647.63                | 35840.69                       |
| 17           | Manipur        | 1                     | 727.56               | 3056.85                 | 463.33                         |
| 18           | Mizoram        | 2                     | 988.06               | 3307.12                 | 251.51                         |
| 19           | Multi State    | 102                   | 124295.06            | 126950.18               | 40374.27                       |
| 20           | Nagaland       | 1                     | 850.00               | 850.00                  | 8.44                           |
| 21           | Orissa         | 27                    | 46642.14             | 48868.07                | 16475.62                       |
| 22           | Punjab         | 8                     | 4854.69              | 5840.65                 | 2798.94                        |
| 23           | Rajasthan      | 16                    | 14282.03             | 14705.92                | 8170.44                        |
| 24           | Sikkim         | 2                     | 1648.88              | 3644.86                 | 199.79                         |
| 25           | Tamil Nadu     | 32                    | 42609.48             | 52170.64                | 35223.27                       |
| 26           | Tripura        | 3                     | 1522.39              | 2053.24                 | 379.66                         |
| 27           | Uttar Pradesh  | 30                    | 17616.31             | 19751.41                | 9858.80                        |
| 28           | Uttaranchal    | 7                     | 11682.65             | 14927.07                | 4824.74                        |
| 29           | West Bengal    | 27                    | 38340.33             | 46184.38                | 21569.39                       |
| <b>TOTAL</b> |                | <b>553</b>            | <b>614127.75</b>     | <b>733611.82</b>        | <b>319374.21</b>               |

### List of Projects in which Expenditure is more than cost

| SN | PROJ_TITLE                                                                      | SECTOR        | AGENCY | DOA     | COST ORIGINAL | COST REVISED | CUMMULATIVE EXPENDITURE |
|----|---------------------------------------------------------------------------------|---------------|--------|---------|---------------|--------------|-------------------------|
| 1  | KUDANKULAM APP (NPCIL)                                                          | Atomic Energy | NPCIL  | 12/2001 | 13171.00      | 0.00         | 13994.00                |
| 2  | BINA EXTN. PROJ(6.0 Mtpa)                                                       | Coal          | NCL    | 11/2006 | 168.97        | 0.00         | 183.63                  |
| 3  | BARSINGSAR TPS (2X125MW) (NLC)                                                  | Coal          | NLC    | 12/2004 | 1114.18       | 1626.09      | 1640.49                 |
| 4  | Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya             | Petroleum     | HPCL   | 06/2009 | 613.54        | 0.00         | 671.52                  |
| 5  | HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT                                    | Petroleum     | ONGC   | 09/2006 | 2305.30       | 700.00       | 2416.96                 |
| 6  | CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)                                            | Power         | NHPC   | 08/2006 | 621.28        | 0.00         | 680.28                  |
| 7  | TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)                     | Power         | NHPC   | 10/2003 | 768.92        | 0.00         | 1349.12                 |
| 8  | CHAMERA,STAGE-III (NHPC)                                                        | Power         | NHPC   | 08/2005 | 1405.63       | 0.00         | 1651.81                 |
| 9  | NIMOO BAZGO HYDROELECTRIC PROJECT                                               | Power         | NHPC   | 08/2006 | 611.02        | 0.00         | 657.77                  |
| 10 | KOTESHWAR HEP(THDC)                                                             | Power         | THDCL  | 04/2000 | 1301.56       | 0.00         | 2481.22                 |
| 11 | JIND-SONEPAT (NL),NR                                                            | Railways      | (NR)   | 01/2004 | 190.81        | 238.56       | 334.70                  |
| 12 | REWARI-ROHTAK (NL),NR                                                           | Railways      | (NR)   | 01/2004 | 149.38        | 330.23       | 469.93                  |
| 13 | JALANDHAR-PATHANKOT-JAMMUTAWI (LD),NR                                           | Railways      | (NR)   | 03/2002 | 409.00        | 625.30       | 813.24                  |
| 14 | CHANDIGARH-LUDHIANA(NEW BG LINE),NR                                             | Railways      | (NR)   | 07/1998 | 248.44        | 576.27       | 793.10                  |
| 15 | AMRAVATI-NARKHER NL(CR)                                                         | Railways      | CR     | 06/1994 | 120.90        | 284.27       | 451.87                  |
| 16 | LANJHIGARH-JUNAGARH NL(ECOR)                                                    | Railways      | ECOR   | 04/1993 | 100.00        | 142.90       | 182.17                  |
| 17 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR                               | Railways      | ECR    | 04/1996 | 114.01        | 283.95       | 336.91                  |
| 18 | PATNA GANGA BRIDGE (NL), ECR                                                    | Railways      | ECR    | 04/2001 | 624.47        | 0.00         | 957.77                  |
| 19 | MUZAFFARPUR-SITAMARHI(NL),ECR                                                   | Railways      | ECR    | 04/1997 | 100.00        | 322.29       | 421.85                  |
| 20 | JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR                                        | Railways      | ECR    | 04/1997 | 233.00        | 335.77       | 552.79                  |
| 21 | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)                                           | Railways      | ECR    | 04/1997 | 78.23         | 0.00         | 86.40                   |
| 22 | MANDARHILL-DUMKA-RAMPURHAT (NL),ER                                              | Railways      | ER     | 04/1995 | 184.00        | 254.07       | 453.79                  |
| 23 | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) | Railways      | M RTP  | 03/2000 | 907.69        | 1032.76      | 3062.38                 |
| 24 | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR                                      | Railways      | NCR    | 04/1999 | 108.00        | 214.09       | 249.52                  |
| 25 | GUNA-ETAWAH(NCR), NL                                                            | Railways      | NCR    | 04/1985 | 158.77        | 432.46       | 558.55                  |

| SN | PROJ TITLE                                                                          | SECTOR   | AGENCY | DOA     | COST ORIGINAL | COST REVISED | CUMMULATIVE EXPENDITURE |
|----|-------------------------------------------------------------------------------------|----------|--------|---------|---------------|--------------|-------------------------|
| 26 | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project              | Railways | NEFR   | 04/1996 | 1676.31       | 0.00         | 2776.44                 |
| 27 | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR                    | Railways | NEFR   | 09/1996 | 156.00        | 0.00         | 178.89                  |
| 28 | RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR | Railways | NEFR   | 09/1997 | 1000.00       | 1500.00      | 2215.96                 |
| 29 | KATIHAR - JOGBANI (GC)(NEFR)                                                        | Railways | NEFR   | 09/2001 | 100.00        | 492.98       | 720.23                  |
| 30 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR                              | Railways | NEFR   | 04/2000 | 733.00        | 0.00         | 808.72                  |
| 31 | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR                                  | Railways | NEFR   | 12/2006 | 170.00        | 170.00       | 359.02                  |
| 32 | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                                             | Railways | NER    | 04/1999 | 323.40        | 0.00         | 414.70                  |
| 33 | KANPUR-KASGANJ-MATHURA(GC),NER                                                      | Railways | NER    | 03/1997 | 395.00        | 1062.36      | 1154.15                 |
| 34 | Sadulpur-Bikaner and Ratangarh-Degana Gauge Conversion (NWR)                        | Railways | NWR    | 04/2007 | 643.36        | 0.00         | 786.86                  |
| 35 | ELECTRIFICATION OF MORADABAD-ROZA                                                   | Railways | RE     | 12/2004 | 129.17        | 0.00         | 217.49                  |
| 36 | BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION                                                | Railways | RVNL   | 09/2005 | 200.80        | 0.00         | 253.23                  |
| 37 | PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)                                       | Railways | RVNL   | 04/2005 | 240.00        | 0.00         | 258.52                  |
| 38 | RAJATGARH-BARANG(LD),ECOR                                                           | Railways | RVNL   | 04/1999 | 166.16        | 0.00         | 233.07                  |
| 39 | BILASPUR-URKURA (DL)                                                                | Railways | RVNL   | 04/1997 | 151.52        | 0.00         | 298.28                  |
| 40 | RENIGUNTA-GUNTAKAL(RE)                                                              | Railways | RVNL   | 06/2000 | 168.34        | 0.00         | 303.99                  |
| 41 | RAICHUR-GUNTAKAL(DL)(SCR)                                                           | Railways | RVNL   | 04/2003 | 136.62        | 0.00         | 154.91                  |
| 42 | GADWAL - RAICHUR (NL), SCR                                                          | Railways | SCR    | 04/1998 | 92.63         | 108.91       | 230.26                  |
| 43 | NANDYAL-YERRAGUNTLA(NL),SCR                                                         | Railways | SCR    | 03/1996 | 155.74        | 164.36       | 486.71                  |
| 44 | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                                              | Railways | SCR    | 12/1994 | 124.43        | 407.78       | 502.72                  |
| 45 | GONDIA-JABALPUR(GC),(SECR)                                                          | Railways | SECR   | 02/1997 | 386.30        | 0.00         | 551.55                  |
| 46 | TAMLUK DIGHA,LINE DOUBLING (SER)                                                    | Railways | SER    | 03/1984 | 293.97        | 0.00         | 378.13                  |
| 47 | BANKURA - DAMODAR (GC) (SER)                                                        | Railways | SER    | 03/1998 | 111.90        | 0.00         | 387.79                  |
| 48 | RANCHI-LOHARDAGA(GC),SER                                                            | Railways | SER    | 04/1997 | 194.07        | 0.00         | 267.31                  |
| 49 | RUPSA-BANGRIPOSI (GC)(SER)                                                          | Railways | SER    | 02/1996 | 57.94         | 0.00         | 171.65                  |
| 50 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE                                   | Railways | SR     | 09/2006 | 343.17        | 0.00         | 408.50                  |

| SN | PROJ TITLE                                                                | SECTOR                    | AGENCY | DOA     | COST ORIGINAL | COST REVISED | CUMMULATIVE EXPENDITURE |
|----|---------------------------------------------------------------------------|---------------------------|--------|---------|---------------|--------------|-------------------------|
| 51 | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)                           | Railways                  | SR     | 03/1998 | 280.00        | 0.00         | 684.77                  |
| 52 | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)                                   | Railways                  | SR     | 09/1995 | 100.00        | 0.00         | 472.21                  |
| 53 | KARUR-SALEM(NL),SR                                                        | Railways                  | SR     | 02/1997 | 155.55        | 0.00         | 599.07                  |
| 54 | CALICUT-MANGALORE (DL) (SR)                                               | Railways                  | SR     | 02/1996 | 240.00        | 0.00         | 593.76                  |
| 55 | KOTTUR-HARIHAR(NL),(SWR)                                                  | Railways                  | SWR    | 04/1995 | 65.94         | 281.20       | 325.44                  |
| 56 | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR                             | Railways                  | SWR    | 02/1997 | 295.00        | 0.00         | 468.64                  |
| 57 | PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)                                       | Railways                  | WR     | 04/2005 | 148.61        | 0.00         | 258.71                  |
| 58 | RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR) | Railways                  | WR     | 04/1992 | 112.53        | 320.66       | 509.57                  |
| 59 | Hazaribagh-Ranchi                                                         | Road Transport & Highways | NHAI   | 08/2010 | 625.07        | 0.00         | 665.96                  |
| 60 | Kishangarh-Ajmer-Beawer                                                   | Road Transport & Highways | NHAI   | 11/2009 | 795.00        | 0.00         | 804.29                  |
| 61 | Pune-sholapur,pkg1                                                        | Road Transport & Highways | NHAI   | 11/2009 | 1110.00       | 0.00         | 1204.90                 |
| 62 | HALDIA PORT (PORT CONNECTIVITY) (NH-41)                                   | Road Transport & Highways | NHAI   | 04/2000 | 273.00        | 0.00         | 475.55                  |
| 63 | NEW MANGALORE PORT NH-17 AND 48                                           | Road Transport & Highways | NHAI   | 04/2000 | 196.50        | 0.00         | 233.50                  |
| 64 | GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR                      | Road Transport & Highways | NHAI   | 12/2003 | 600.24        | 0.00         | 692.67                  |
| 65 | JHANSI TO LALITPUR, NH-26                                                 | Road Transport & Highways | NHAI   | 12/2003 | 276.09        | 0.00         | 295.27                  |
| 66 | MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B               | Road Transport & Highways | NHAI   | 03/2005 | 629.00        | 0.00         | 910.04                  |
| 67 | SITAPUR-LUCKNOW                                                           | Road Transport & Highways | NHAI   | 03/2005 | 322.00        | 0.00         | 553.66                  |
| 68 | THRISSUR TO ANGAMALI (NH-47)                                              | Road Transport & Highways | NHAI   | 12/2003 | 312.50        | 0.00         | 602.56                  |
| 69 | SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI)                    | Road Transport & Highways | NHAI   | 12/2003 | 203.43        | 0.00         | 207.85                  |

| SN | PROJ TITLE                                                   | SECTOR                    | AGENCY | DOA     | COST ORIGINAL | COST REVISED | CUMMULATIVE EXPENDITURE |
|----|--------------------------------------------------------------|---------------------------|--------|---------|---------------|--------------|-------------------------|
| 70 | RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)  | Road Transport & Highways | NHAI   | 12/2003 | 251.03        | 0.00         | 276.03                  |
| 71 | RINGBUNDS TO JHAJHANPUR (BR-6)                               | Road Transport & Highways | NHAI   | 12/2003 | 340.00        | 0.00         | 561.31                  |
| 72 | JHAJHARPUR TO DARBANGA (BR-7)                                | Road Transport & Highways | NHAI   | 12/2003 | 340.00        | 0.00         | 426.99                  |
| 73 | NALBARI TO BIJNI (AS-8)                                      | Road Transport & Highways | NHAI   | 12/2003 | 200.00        | 0.00         | 255.34                  |
| 74 | SONAPUR TO GUWAHTI (AS-3)                                    | Road Transport & Highways | NHAI   | 12/2003 | 245.00        | 0.00         | 476.19                  |
| 75 | ASSAM/WB BORDER TO GAIRKATTA (WB-1)                          | Road Transport & Highways | NHAI   | 12/2003 | 221.82        | 0.00         | 241.98                  |
| 76 | NH CONNECTIVITY TO ICTT VALLARPADAEU NH - SH                 | Road Transport & Highways | NHAI   | 03/2005 | 557.00        | 0.00         | 930.92                  |
| 77 | PATHANKOT BHOGPUR NH-1A                                      | Road Transport & Highways | NHAI   | 12/2003 | 229.00        | 0.00         | 338.97                  |
| 78 | AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)              | Road Transport & Highways | NHAI   | 04/2000 | 367.49        | 0.00         | 453.68                  |
| 79 | GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24   | Road Transport & Highways | NHAI   | 12/2003 | 275.00        | 0.00         | 296.55                  |
| 80 | HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24                 | Road Transport & Highways | NHAI   | 03/2005 | 220.00        | 0.00         | 239.26                  |
| 81 | GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 | Road Transport & Highways | NHAI   | 12/2003 | 412.78        | 0.00         | 436.46                  |
| 82 | AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28       | Road Transport & Highways | NHAI   | 12/2003 | 217.00        | 0.00         | 352.26                  |
| 83 | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402  | Road Transport & Highways | NHAI   | 12/2003 | 240.00        | 0.00         | 263.77                  |
| 84 | GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00    | Road Transport & Highways | NHAI   | 12/2003 | 227.00        | 0.00         | 394.13                  |
| 85 | ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0            | Road Transport & Highways | NHAI   | 12/2003 | 340.68        | 0.00         | 353.85                  |

| SN  | PROJ_TITLE                                              | SECTOR                    | AGENCY | DOA     | COST ORIGINAL | COST REVISED | CUMMULATIVE EXPENDITURE |
|-----|---------------------------------------------------------|---------------------------|--------|---------|---------------|--------------|-------------------------|
| 86  | AURANG-RAIPUR, NH-6, KM.232 TO KM.281                   | Road Transport & Highways | NHAI   | 03/2005 | 190.00        | 0.00         | 227.03                  |
| 87  | DAKOBA TO NAGAON (NH-36)(NHAI)                          | Road Transport & Highways | NHAI   | 12/2003 | 225.00        | 0.00         | 254.16                  |
| 88  | KASIA TO GORAKHPUR (NH-28)(NHAI)                        | Road Transport & Highways | NHAI   | 12/2003 | 242.00        | 0.00         | 393.21                  |
| 89  | UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)                  | Road Transport & Highways | NHAI   | 12/2003 | 227.00        | 0.00         | 363.24                  |
| 90  | KOTA BYPASS,RJ-4, NH-76 (NHAI)                          | Road Transport & Highways | NHAI   | 12/2003 | 275.00        | 0.00         | 277.08                  |
| 91  | LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)        | Road Transport & Highways | NHAI   | 12/2003 | 225.00        | 0.00         | 254.49                  |
| 92  | SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)           | Road Transport & Highways | NHAI   | 12/2003 | 151.30        | 0.00         | 172.23                  |
| 93  | NAGPUR-KONDHALI,NH-6(NHAI)                              | Road Transport & Highways | NHAI   | 03/2005 | 168.00        | 0.00         | 385.27                  |
| 94  | THANJAUR-TRICHY,NH-67(NHAI)                             | Road Transport & Highways | NHAI   | 03/2005 | 280.00        | 0.00         | 580.67                  |
| 95  | TRICHY - DINDIGUAL NH-45                                | Road Transport & Highways | NHAI   | 03/2005 | 576.00        | 0.00         | 657.66                  |
| 96  | PONDICHERY - TINDIVANAU NH-66                           | Road Transport & Highways | NHAI   | 03/2005 | 285.00        | 0.00         | 359.10                  |
| 97  | TRICHY - KORUR NH-67                                    | Road Transport & Highways | NHAI   | 03/2005 | 516.00        | 0.00         | 594.18                  |
| 98  | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68               | Road Transport & Highways | NHAI   | 03/2005 | 941.00        | 0.00         | 1901.00                 |
| 99  | NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI | Road Transport & Highways | NHAI   | 03/2005 | 441.00        | 0.00         | 908.83                  |
| 100 | ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH)          | Road Transport & Highways | NHAI   | 02/2008 | 295.00        | 0.00         | 624.25                  |
| 101 | DELHI/ HARYANA BORDER TO ROHTAK                         | Road Transport & Highways | NHAI   | 04/2007 | 486.00        | 0.00         | 525.47                  |

| SN  | PROJ_TITLE                                                                              | SECTOR                    | AGENCY | DOA     | COST ORIGINAL | COST REVISED | CUMMULATIVE EXPENDITURE |
|-----|-----------------------------------------------------------------------------------------|---------------------------|--------|---------|---------------|--------------|-------------------------|
| 102 | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)                                             | Road Transport & Highways | NHAI   | 05/2009 | 1108.00       | 0.00         | 2610.80                 |
| 103 | AMRITSAR-PATHANKOT                                                                      | Road Transport & Highways | NHAI   | 05/2010 | 705.00        | 0.00         | 834.69                  |
| 104 | Surat- Dahisar(Six Lane) Km 263 to Km 502                                               | Road Transport & Highways | NHAI   | 02/2009 | 1693.75       | 0.00         | 2492.60                 |
| 105 | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275                                        | Road Transport & Highways | NHAI   | 12/2003 | 157.47        | 0.00         | 177.48                  |
| 106 | Bijapur-Hungund Section                                                                 | Road Transport & Highways | NHAI   | 09/2010 | 748.00        | 0.00         | 958.73                  |
| 107 | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST                           | Shipping & Ports          | RVNL   | 03/2007 | 245.67        | 0.00         | 294.07                  |
| 108 | GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle | Telecommunications        | BSNL   | 01/2009 | 760.20        | 0.00         | 813.60                  |
| 109 | GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1                               | Telecommunications        | BSNL   | 11/2007 | 277.34        | 0.00         | 308.13                  |

## List of project Without Original Date of Commissioning

(Aug,2011)

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
|      | <u>Atomic Energy</u>                                                                   |                  |                         |                  |                   |                       |             |                                   |                            |
| 1    | URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh    | 09/2007          | 1,106.29                | 1,106.29         | 1,000.70          | -<br>04/2011          | 04/2012     | 12(R3)                            | 0/1                        |
|      | <b>Total</b>                                                                           |                  | 1,106.29                | 1,106.29         | 1,000.70          |                       |             |                                   | 0/1                        |
|      | <u>Coal</u>                                                                            |                  |                         |                  |                   |                       |             |                                   |                            |
| 2    | BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa                           | 12/2007          | 172.08                  | 172.08           | 93.78             | -<br>-                | 03/2012     | -                                 | 4/4                        |
| 3    | ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Orissa                          | 08/2008          | 207.28                  | 207.28           | 67.14             | -<br>-                | 03/2012     | -                                 | 5/7                        |
| 4    | TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu                            | 05/2008          | 4,904.54<br>4,909.54    | 4,909.54         | 1,973.76          | -<br>-                | 10/2012     | -                                 | 0/6                        |
| 5    | KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh                        | 06/2006          | 737.65                  | 1,188.31         | 569.71            | -<br>-                | 03/2013     | -                                 | 0/8                        |
| 6    | KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa                                    | 12/2007          | 457.77                  | 457.77           | 105.37            | -<br>-                | 03/2013     | -                                 | 6/11                       |
| 7    | HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Orissa                             | 11/2008          | 475.93                  | 479.63           | 66.93             | -<br>-                | 03/2013     | -                                 | 5/7                        |
| 8    | CHURCHA RO UG (1.35MTY) - [N06000046]SECL,Chhatisgarh                                  | 06/2008          | 462.35                  | 462.35           | 253.86            | -<br>-                | 03/2014     | -                                 | 0/4                        |
| 9    | MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh                         | 11/2009          | 321.42                  | 321.50           | 203.09            | -<br>-                | 03/2014     | -                                 | 0/5                        |
| 10   | PENGANGA OC - [N06000066]WCL,Orissa                                                    | 10/2008          | 339.77                  | 339.77           | 0.65              | -<br>-                | 10/2014     | -                                 | 1/1                        |
| 11   | GOPAL PRASAD OCP - [N06000042]MCL,Orissa                                               | 02/2008          | 395.87                  | 395.87           | 58.42             | -<br>-                | 03/2015     | -                                 | 2/12                       |
| 12   | TALABIRA OCP - [N06000043]MCL,Orissa                                                   | 03/2008          | 447.72                  | 447.72           | 35.20             | -<br>-                | 03/2016     | -                                 | 1/12                       |
| 13   | BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa                               | 12/2007          | 490.00                  | 490.10           | 88.19             | -<br>-                | 03/2017     | -                                 | 6/12                       |
|      | <b>Total</b>                                                                           |                  | 9,412.38                | 9,871.92         | 3,516.10          |                       |             |                                   | 30/89                      |
|      | <u>Fertilisers</u>                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 14   | THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana                                   | 01/2009          | 488.75                  | 488.75           | 168.14            | -<br>11/2011          | 11/2011     | 0(R3)                             | 2/22                       |
|      | <b>Total</b>                                                                           |                  | 488.75                  | 488.75           | 168.14            |                       |             |                                   | 2/22                       |
|      | <u>Steel</u>                                                                           |                  |                         |                  |                   |                       |             |                                   |                            |
| 15   | 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh | 07/2007          | 111.28<br>232.93        | 232.93           | 168.27            | -<br>-                | 10/2011     | -                                 | 0/1                        |

## List of project Without Original Date of Commissioning

(Aug,2011)

| S.No                  | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|-----------------------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                       |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                     | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 16                    | 330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh              | 07/2007          | 260.00<br>-             | 350.00           | 220.10            | -<br>-                | 11/2011     | -                                 | 1/2                        |
| 17                    | EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand                         | 01/2008          | 3,316.00<br>6,325.00    | 6,325.00         | 2,109.69          | -<br>12/2011          | 12/2011     | 0(R3)                             | 0/11                       |
| 18                    | 67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh | 07/2007          | 230.00<br>-             | 343.58           | 229.59            | -<br>-                | 12/2011     | -                                 | 2/3                        |
| 19                    | Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC, Chhatisgarh                 | 01/2007          | 295.89<br>607.17        | 607.17           | 290.68            | -<br>12/2011          | 03/2012     | 3(R3)                             | 18/21                      |
| 20                    | Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State              | 05/2008          | 480.00<br>-             | 460.00           | 127.39            | -<br>05/2012          | 05/2012     | 0(R3)                             | 1/2                        |
| 21                    | EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal                        | 02/2008          | 14,443.00<br>16,408.00  | 16,408.00        | 11,272.00         | -<br>12/2011          | 06/2012     | 6(R3)                             | 1/14                       |
| 22                    | COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh                   | 08/2007          | 108.00<br>-             | 216.68           | 44.44             | -<br>10/2012          | 10/2012     | 0(R3)                             | 3/4                        |
| 23                    | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh                       | 09/2008          | 5,185.00<br>17,265.00   | 17,265.00        | 3,212.16          | -<br>03/2013          | 03/2013     | 0(R3)                             | 2/20                       |
| Total                 |                                                                                      |                  | 24,429.17<br>-          | 42,208.36        | 17,674.32         |                       |             |                                   | 28/78                      |
| <u>Petrochemicals</u> |                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 24                    | ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam                                   | 04/2006          | 5,460.61<br>-           | 5,460.61         | 2,719.00          | -<br>-                | 04/2012     | -                                 | 0/30                       |
| Total                 |                                                                                      |                  | 5,460.61<br>-           | 5,460.61         | 2,719.00          |                       |             |                                   | 0/30                       |
| <u>Petroleum</u>      |                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 25                    | DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra    | 12/2009          | 1,584.00<br>-           | 1,584.00         | -                 | -<br>-                | 08/2013     | -                                 | 0/0                        |
| Total                 |                                                                                      |                  | 1,584.00<br>-           | 1,584.00         | .00               |                       |             |                                   | 0/0                        |
| <u>Power</u>          |                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 26                    | SIMHADRI STPP STAGE -II - [N18000032]NTPC, Andhra Pradesh                            | 08/2007          | 5,103.39<br>-           | 5,038.53         | 4,060.00          | -<br>-                | 03/2012     | -                                 | 0/6                        |
| 27                    | BARH STPP STAGE -II - [N18000047]NTPC,                                               | 02/2008          | 7,341.04<br>-           | 7,341.04         | 2,588.00          | -<br>-                | 10/2013     | -                                 | 2/18                       |
| Total                 |                                                                                      |                  | 12,444.43<br>-          | 12,379.57        | 6,648.00          |                       |             |                                   | 2/24                       |
| <u>Railways</u>       |                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 28                    | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala                               | 10/1998          | 550.00<br>-             | 550.00           | 70.95             | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 29                    | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, Orissa                               | 04/1994          | 355.38<br>470.21        | 700.00           | 161.90            | -<br>-                | 08/2011     | -                                 | 0/0                        |
| 30                    | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa                                    | 04/1996          | 301.64<br>-             | 735.10           | -                 | -<br>09/2009          | 12/2011     | 27(R1)                            | 0/0                        |

## List of project Without Original Date of Commissioning

(Aug,2011)

| S.No | Project                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 31   | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa                             | 04/2005          | 726.96<br>810.78        | 810.78           | 78.54             | -<br>-                | 12/2011     | -                                 | 0/0                        |
| 32   | KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh                     | 03/1997          | 395.00<br>1,062.36      | 1,577.46         | 1,154.15          | -<br>-                | 02/2012     | -                                 | 0/0                        |
| 33   | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal           | 04/2000          | 157.96<br>762.33        | 762.33           | 409.84            | -<br>12/2009          | 02/2012     | 26(R1)                            | 0/0                        |
| 34   | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh            | 12/1994          | 124.43<br>407.78        | 725.90           | 502.72            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 35   | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd                     | 04/1995          | 184.00<br>254.07        | 675.00           | 453.79            | -<br>12/2011          | 03/2012     | 3(R3)                             | 0/0                        |
| 36   | KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka                | 04/1996          | 157.00<br>262.82        | 262.82           | 203.03            | -<br>03/2012          | 03/2012     | 0(R3)                             | 0/0                        |
| 37   | MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar                              | 04/1997          | 100.00<br>322.29        | 411.22           | 421.85            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 38   | JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar                   | 04/1997          | 233.00<br>335.77        | 903.56           | 552.79            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 39   | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar          | 04/1996          | 114.01<br>283.95        | 427.89           | 336.91            | -<br>03/2011          | 03/2012     | 12(R3)                            | 0/0                        |
| 40   | HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar       | 04/2003          | 98.74<br>224.51         | 337.30           | 191.22            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 41   | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar          | 03/2005          | 470.09<br>1,417.97      | 1,417.97         | 914.08            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 42   | CONSTRUCTION OF NEW LINE FROM HARMATHITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr. | 09/1996          | 156.00<br>-             | 254.29           | 178.89            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 43   | NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State                            | 03/1981          | 37.68<br>450.00         | 730.00           | 325.04            | -<br>07/2012          | 07/2012     | 0(R3)                             | 0/0                        |
| 44   | CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra              | 07/1996          | 273.67<br>1,160.52      | 1,302.12         | 571.52            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 45   | JIND-SONEPAT (NL),NR - [220100280](NR),Haryana                                    | 01/2004          | 190.81<br>238.56        | 401.83           | 334.70            | -<br>03/2012          | 12/2012     | 9(R3)                             | 0/0                        |
| 46   | KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar                                      | 04/2002          | 323.41<br>-             | 341.41           | 233.20            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 47   | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan                            | 02/1997          | 151.84<br>410.08        | 410.08           | 149.04            | -<br>-                | 03/2013     | -                                 | 0/0                        |
| 48   | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State       | 03/1998          | 280.00<br>-             | 1,029.00         | 684.77            | -<br>-                | 03/2013     | -                                 | 0/0                        |
| 49   | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTTP,Tamil Nadu     | 04/2006          | 495.74<br>495.74        | 495.74           | 135.49            | -<br>06/2013          | 06/2013     | 0(R3)                             | 0/0                        |
| 50   | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh                   | 04/2005          | 383.79<br>-             | 585.93           | 173.04            | -<br>-                | 12/2013     | -                                 | 0/0                        |

## List of project Without Original Date of Commissioning

(Aug,2011)

| S.No Project |                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 51           | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State | 01/2004          | 915.70<br>-             | 1,717.29         | 702.69            | -<br>-                | 03/2014     | -                                 | 0/0                        |
| 52           | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar                    | 04/2003          | 324.66<br>-             | 324.66           | 165.33            | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 53           | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State                       | 04/2000          | 138.00<br>519.67        | 607.09           | 323.19            | -<br>12/2012          | -           | -                                 | 0/0                        |
|              | Total                                                                            |                  | 7,639.51<br>-           | 18,496.77        | 9,428.67          |                       |             |                                   | 0/0                        |
| Grand Total  |                                                                                  |                  | 62,565.14               | 91,596.27        | 41,154.93         |                       |             |                                   | 62/244                     |

## List of project Without Date of Commissioning

Aug,2011)

| S.No             | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                  |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <u>Coal</u>      |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 1                | SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, Andhra Pradesh                         | 10/2006          | 249.03<br>-             | 249.03           | 40.04             | 03/2012<br>03/2012    | -           | -                                 | 13/42                      |
|                  | <b>Total</b>                                                                             |                  | 249.03<br>-             | 249.03           | 40.04             |                       |             |                                   | 13/42                      |
| <u>Mines</u>     |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 2                | SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa | 10/2004          | 4,091.51<br>4,401.76    | 4,401.76         | 4,096.00          | 12/2008<br>01/2011    | 06/2011     | 5(R3)                             | 117/110                    |
|                  | <b>Total</b>                                                                             |                  | 4,091.51<br>-           | 4,401.76         | 4,096.00          |                       |             |                                   | 117/110                    |
| <u>Petroleum</u> |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 3                | North Tapti Gas Field Development - [N16000096]ONGC, Multi State                         | 07/2008          | 589.70<br>755.76        | 755.76           | 520.63            | 03/2011<br>05/2011    | 06/2011     | 1(R3)                             | 0/0                        |
| 4                | Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar         | 06/2009          | 613.54<br>-             | 727.88           | 671.52            | 12/2010<br>-          | 06/2011     | 6(O)                              | 0/0                        |
| 5                | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana                              | 11/2007          | 281.07<br>-             | 281.07           | 3.29              | 10/2010<br>-          | -           | -                                 | 0/0                        |
| 6                | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra         | 03/2011          | 861.79<br>-             | 861.79           | -                 | 05/2013<br>-          | -           | -                                 | 0/0                        |
| 7                | DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh         | 03/2009          | 3,597.00<br>2,730.00    | 2,730.00         | 696.82            | 09/2011<br>03/2012    | -           | -                                 | 0/0                        |
| 8                | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State                | 07/2009          | 7,596.18<br>6,652.22    | 6,652.22         | 1.63              | 01/2013<br>-          | -           | -                                 | 0/0                        |
|                  | <b>Total</b>                                                                             |                  | 13,539.28<br>-          | 12,008.72        | 1,893.89          |                       |             |                                   | 0/0                        |
| <u>Power</u>     |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 9                | KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka                      | 03/2005          | 596.45<br>1,007.16      | 947.96           | 829.36            | 12/2007<br>12/2009    | -           | -                                 | 14/18                      |
|                  | <b>Total</b>                                                                             |                  | 596.45<br>-             | 947.96           | 829.36            |                       |             |                                   | 14/18                      |
| <u>Railways</u>  |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 10               | RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat                                   | 04/2006          | 196.97<br>-             | 196.97           | 174.05            | 03/2011<br>-          | 03/2011     | 0(O)                              | 0/0                        |
| 11               | CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State                                 | 02/1996          | 240.00<br>-             | 579.37           | 593.76            | -<br>-                | 07/2011     | -                                 | 0/0                        |
| 12               | PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR, Gujarat                             | 04/2005          | 148.61<br>-             | 227.52           | 258.71            | 03/2008<br>03/2009    | 10/2010     | 19(R1)                            | 0/0                        |
| 13               | RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa                                     | 04/1999          | 166.16<br>-             | 243.40           | 233.07            | -<br>02/2009          | 12/2010     | 22(R1)                            | 0/0                        |

## List of project Without Date of Commissioning

Aug,2011)

| S.No | Project                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 14   | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa               | 04/2000          | 133.41<br>207.00        | 211.90           | 187.38            | -<br>03/2009          | 12/2010     | 21(R1)                            | 0/0                        |
| 15   | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh                       | 04/2003          | 136.62<br>-             | 221.90           | 154.91            | 12/2007<br>03/2010    | 12/2010     | 9(R1)                             | 0/0                        |
| 16   | ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh        | 04/2003          | 230.73<br>399.73        | 399.50           | 294.87            | 03/2009<br>12/2008    | 12/2010     | 24(R1)                            | 0/0                        |
| 17   | BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL, Gujarat                    | 09/2005          | 200.80<br>-             | 200.80           | 253.23            | -<br>-                | 12/2010     | -                                 | 0/0                        |
| 18   | BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh                               | 04/1997          | 151.52<br>-             | 273.00           | 298.28            | -<br>03/2009          | 03/2011     | 24(R1)                            | 0/0                        |
| 19   | PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State      | 04/2005          | 240.00<br>-             | 329.70           | 258.52            | 03/2009<br>12/2009    | 03/2011     | 15(R1)                            | 0/0                        |
| 20   | MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP, Maharashtra        | 04/2003          | 3,125.20<br>4,501.80    | 4,501.80         | 4,246.71          | -<br>12/2010          | 06/2011     | 6(R3)                             | 0/1                        |
| 21   | VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State                              | 04/1990          | 155.66<br>-             | 356.87           | 148.75            | -<br>03/2010          | -           | -                                 | 0/0                        |
| 22   | RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR, Gujarat        | 04/1992          | 112.53<br>320.66        | 464.50           | 509.57            | 03/1996<br>06/2009    | -           | -                                 | 0/0                        |
| 23   | New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal | 04/1983          | 36.80<br>274.41         | 415.23           | 234.54            | -<br>-                | -           | -                                 | 0/0                        |
| 24   | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh | 04/1995          | 304.00<br>-             | 968.60           | -                 | 12/2012<br>-          | -           | -                                 | 0/0                        |
| 25   | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra                     | 02/1997          | 353.08<br>462.67        | 1,010.00         | 96.07             | -<br>-                | -           | -                                 | 0/0                        |
| 26   | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka        | 02/1997          | 295.00<br>-             | 412.91           | 468.64            | -<br>-                | -           | -                                 | 0/0                        |
| 27   | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State                         | 02/1997          | 386.30<br>-             | 1,038.00         | 551.55            | 03/1998<br>-          | -           | -                                 | 0/0                        |
| 28   | KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu                                   | 02/1997          | 155.55<br>-             | 945.73           | 599.07            | -<br>-                | -           | -                                 | 0/0                        |
| 29   | HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka                                 | 04/1995          | 227.00<br>-             | 997.58           | 64.29             | -<br>-                | -           | -                                 | 0/0                        |
| 30   | MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State                    | 04/1997          | 218.24<br>377.32        | 497.47           | 91.37             | -<br>-                | -           | -                                 | 0/0                        |
| 31   | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh                       | 07/1998          | 125.00<br>-             | 363.26           | 0.27              | 07/2008<br>-          | -           | -                                 | 0/0                        |
| 32   | KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand                | 03/1999          | 491.19<br>1,099.20      | 1,099.20         | 1,058.38          | 07/2005<br>-          | -           | -                                 | 0/0                        |
| 33   | GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka                               | 02/1998          | 242.42<br>369.70        | 554.55           | 254.82            | -<br>05/2009          | -           | -                                 | 0/0                        |
| 34   | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, Bihar                     | 04/1997          | 78.23<br>-              | 162.87           | 86.40             | -<br>-                | -           | -                                 | 0/0                        |

## List of project Without Date of Commissioning

Aug,2011)

| S.No Project |                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|---------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                 |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                               | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 35           | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State            | 03/2002          | 409.00<br>625.30        | 847.76           | 813.24            | 06/2007<br>-          | -           | -                                 | 0/0                        |
| 36           | REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh                         | 06/2000          | 168.34<br>-             | 296.20           | 303.99            | 04/2003<br>03/2010    | -           | -                                 | 0/0                        |
| 37           | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu              | 09/1995          | 100.00<br>-             | 548.96           | 472.21            | -<br>-                | -           | -                                 | 0/0                        |
| 38           | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh                  | 12/2001          | 330.00<br>-             | 695.00           | 9.44              | -<br>-                | -           | -                                 | 0/0                        |
| 39           | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka                   | 02/1999          | 138.00<br>-             | 901.62           | 0.29              | -<br>-                | -           | -                                 | 0/0                        |
| 40           | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand                            | 04/2002          | 459.91<br>-             | 418.17           | 73.52             | -<br>-                | -           | -                                 | 0/0                        |
| 41           | RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh                   | 04/2001          | 727.13<br>727.13        | 1,225.00         | 210.24            | -<br>-                | -           | -                                 | 0/0                        |
| 42           | RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa                              | 02/1996          | 57.94<br>-              | 173.49           | 171.65            | 03/1998<br>08/2005    | -           | -                                 | 0/0                        |
| 43           | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa                        | 04/1998          | 183.23<br>-             | 638.00           | -                 | 02/2015<br>-          | -           | -                                 | 0/0                        |
| 44           | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh              | 04/2006          | 378.56<br>671.82        | 791.60           | 0.76              | -<br>-                | -           | -                                 | 0/0                        |
| 45           | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand                        | 03/1997          | 186.92<br>-             | 261.70           | 20.18             | 02/2006<br>-          | -           | -                                 | 0/0                        |
| 46           | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh             | 07/2006          | 743.00<br>-             | 732.80           | 306.37            | 03/2008<br>06/2008    | -           | -                                 | 0/0                        |
| 47           | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu  | 09/2007          | 404.19<br>-             | 900.00           | 187.89            | -<br>-                | -           | -                                 | 0/0                        |
| 48           | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu    | 09/2006          | 343.17<br>-             | 900.00           | 408.50            | -<br>-                | -           | -                                 | 0/0                        |
| 49           | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu                | 09/2006          | 125.00<br>-             | 227.40           | 21.00             | -<br>-                | -           | -                                 | 0/0                        |
| 50           | TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu                                | 09/2006          | 456.00<br>-             | 582.83           | 83.97             | -<br>-                | -           | -                                 | 0/0                        |
| 51           | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar      | 09/2006          | 300.00<br>300.00        | 529.88           | 35.45             | -<br>-                | -           | -                                 | 0/0                        |
| 52           | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                          | 04/2008          | 282.92<br>-             | 359.86           | 0.71              | -<br>-                | -           | -                                 | 0/0                        |
| 53           | Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat      | 04/2006          | 117.36<br>196.95        | 196.95           | 168.88            | 03/2011<br>-          | -           | -                                 | 0/0                        |
| 54           | AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra                             | 06/1994          | 120.90<br>284.27        | 488.76           | 451.87            | 06/1999<br>03/2011    | -           | -                                 | 0/0                        |
| 55           | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra | 03/1996          | 401.81<br>495.44        | 495.44           | 166.58            | 03/2004<br>-          | -           | -                                 | 0/0                        |
| 56           | KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka                             | 04/1995          | 65.94<br>281.20         | 302.23           | 325.44            | -<br>03/2011          | -           | -                                 | 0/0                        |

## List of project Without Date of Commissioning

Aug,2011)

| S.No                        | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|-----------------------------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                             |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                           | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 57                          | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd                                   | 04/1997          | 194.07                  | 456.45           | 267.31            | 06/2004<br>04/2005    | -           | -                                 | 0/0                        |
| 58                          | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State                    | 09/1998          | 925.00                  | 925.00           | 504.78            | 05/2008<br>03/2011    | -           | -                                 | 0/0                        |
| 59                          | AGRA-ETAHAWH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh             | 04/1999          | 108.00<br>214.09        | 227.42           | 249.52            | 12/2009<br>03/2011    | -           | -                                 | 0/0                        |
| 60                          | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar                                   | 09/2001          | 100.00<br>492.98        | 1,015.84         | 720.23            | -<br>12/2010          | -           | -                                 | 0/0                        |
| 61                          | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh | 03/2002          | 381.17<br>863.23        | 863.23           | 401.26            | -<br>-                | -           | -                                 | 0/0                        |
| 62                          | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State                   | 04/1999          | 323.40                  | 522.56           | 414.70            | -<br>-                | -           | -                                 | 0/1                        |
| 63                          | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal        | 03/2000          | 907.69<br>1,032.76      | 3,176.10         | 3,062.38          | 12/2006<br>08/2010    | -           | -                                 | 0/0                        |
| 64                          | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State                                | 04/1998          | 92.63<br>108.91         | 228.09           | 230.26            | -<br>02/2011          | -           | -                                 | 0/0                        |
| 65                          | REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana                                        | 01/2004          | 149.38<br>330.23        | 475.28           | 469.93            | 02/2010<br>02/2011    | -           | -                                 | 0/0                        |
| 66                          | KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd                                   | 04/1996          | 371.36                  | 452.35           | 367.76            | -<br>-                | -           | -                                 | 0/0                        |
| 67                          | SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan                            | 04/2001          | 143.92<br>258.60        | 258.60           | 234.79            | -<br>03/2011          | -           | -                                 | 0/0                        |
| 68                          | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar                                  | 04/2003          | 218.19                  | 218.19           | 131.48            | -<br>-                | -           | -                                 | 0/0                        |
| 69                          | HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State                                 | 04/2005          | 230.03                  | 230.03           | 131.75            | -<br>-                | -           | -                                 | 0/0                        |
| 70                          | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State       | 12/2006          | 170.00<br>170.00        | 435.87           | 359.02            | -<br>03/2011          | -           | -                                 | 0/0                        |
| 71                          | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam             | 09/2006          | 200.00                  | 384.04           | 76.53             | -<br>-                | -           | -                                 | 0/0                        |
| 72                          | BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal                                   | 04/2007          | 245.15                  | 245.15           | 160.33            | 12/2010<br>03/2011    | -           | -                                 | 0/0                        |
| 73                          | Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal                          | 04/2004          | 225.68                  | 225.68           | 129.37            | -<br>12/2010          | -           | -                                 | 0/0                        |
| 74                          | Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat             | 04/2008          | 318.24                  | 468.62           | 2.07              | 03/2012               | -           | -                                 | 0/0                        |
|                             | <b>Total</b>                                                                           |                  | 19,954.25               | 39,994.78        | 23,262.86         |                       |             |                                   | 0/2                        |
| <b>Shipping &amp; Ports</b> |                                                                                        |                  |                         |                  |                   |                       |             |                                   |                            |
| 75                          | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala  | 03/2007          | 245.67                  | 298.17           | 294.07            | 04/2009               | 02/2011     | 22(O)                             | 0/0                        |
| 76                          | Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka   | 06/2006          | 230.00                  | 272.50           | 219.00            | 12/2010               | 06/2011     | 6(O)                              | 0/0                        |

## List of project Without Date of Commissioning

Aug,2011)

| S.No                      | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|---------------------------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                           |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                         | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 77                        | DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra     | 10/2005          | 800.00<br>-             | 800.00           | 5.92              | 10/2008<br>-          | -           | -                                 | 0/0                        |
| 78                        | DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa                        | 12/2005          | 154.84<br>-             | 253.36           | -                 | 12/2007<br>01/2009    | -           | -                                 | 0/0                        |
| 79                        | DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu                       | 09/2006          | 399.13<br>-             | 399.13           | -                 | 08/2010<br>-          | -           | -                                 | 0/0                        |
| 80                        | DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu                   | 09/2006          | 370.00<br>-             | 370.00           | -                 | 08/2010<br>-          | -           | -                                 | 0/0                        |
| 81                        | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu                      | 06/2005          | 2,427.40<br>-           | 2,427.40         | 821.39            | 10/2008<br>-          | -           | -                                 | 0/0                        |
| Total                     |                                                                                            |                  | 4,627.04<br>-           | 4,820.56         | 1,340.38          |                       |             |                                   | 0/0                        |
| <u>Telecommunications</u> |                                                                                            |                  |                         |                  |                   |                       |             |                                   |                            |
| 82                        | GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra            | 09/2008          | 1,799.94<br>-           | 1,799.94         | 251.53            | 09/2009<br>-          | 02/2010     | 5(O)                              | 0/0                        |
| 83                        | Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State | 12/2007          | 952.88<br>-             | 952.88           | -                 | 03/2010<br>-          | 10/2010     | 7(O)                              | 0/0                        |
| 84                        | GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana                         | 01/2008          | 192.48<br>-             | 192.48           | 119.41            | 03/2009<br>-          | 02/2011     | 23(O)                             | 0/0                        |
| 85                        | GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab                | 02/2008          | 373.94<br>-             | 373.94           | 199.63            | 12/2008<br>-          | 02/2011     | 26(O)                             | 0/0                        |
| 86                        | GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa                | 11/2007          | 277.34<br>-             | 377.54           | 308.13            | 03/2009<br>-          | 02/2011     | 23(O)                             | 0/0                        |
| 87                        | UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal                | 01/2009          | 149.15<br>158.72        | 158.72           | 76.55             | 06/2009<br>-          | 02/2011     | 20(O)                             | 0/0                        |
| 88                        | Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam                           | 06/2007          | 336.81<br>-             | 336.81           | 155.71            | 01/2009<br>-          | 02/2011     | 25(O)                             | 0/0                        |
| 89                        | GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar                 | 10/2007          | 366.00<br>-             | 366.00           | 226.39            | 10/2008<br>-          | 02/2011     | 28(O)                             | 0/0                        |
| 90                        | GSM equipment of 1900000Lines (2G) 401700 lines 3( - [N26000091]BSNL,Tamil Nadu            | 01/2009          | 760.20<br>-             | 1,100.00         | 813.60            | -<br>03/2011          | 02/2011     | -1(R3)                            | 0/1                        |
| 91                        | GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh       | 01/2009          | 922.91<br>-             | 922.91           | 346.90            | 01/2010<br>-          | 02/2011     | 13(O)                             | 0/0                        |
| 92                        | GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala               | 01/2009          | 848.70<br>-             | 848.70           | 675.35            | 01/2010<br>-          | 02/2011     | 13(O)                             | 0/0                        |
| 93                        | GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu            | 01/2009          | 315.19<br>-             | 315.19           | 132.24            | 01/2010<br>-          | 02/2011     | 13(O)                             | 0/0                        |

## List of project Without Date of Commissioning

Aug,2011)

| S.No | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 94   | GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan      | 06/2007          | 601.49                  | 601.49           | 495.72            | 12/2008               | 03/2011     | 27(O)                             | 0/0                        |
| 95   | GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh    | 05/2007          | 335.91                  | 335.91           | 182.45            | 03/2009               | 03/2011     | 24(O)                             | 0/0                        |
| 96   | GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab          | 09/2008          | 241.49                  | 241.49           | 112.61            | 09/2009               | 03/2011     | 18(O)                             | 0/0                        |
| 97   | GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh  | 10/2008          | 336.84                  | 336.84           | 35.75             | 10/2009               | 03/2011     | 17(O)                             | 0/0                        |
| 98   | GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal   | 02/2008          | 584.33                  | 584.33           | 398.08            | 02/2009               | 03/2011     | 25(O)                             | 0/0                        |
| 99   | GSM equipment of 1867000Lines (2G) 383000 lines 3(-) [N26000089]BSNL,Gujarat        | 08/2008          | 868.00                  | 868.00           | 362.62            | 08/2009               | 03/2011     | 19(O)                             | 0/0                        |
| 100  | GSM equipment of 1625000Lines (2G) 325000 lines 3(-) [N26000090]BSNL,Madhya pradesh | 11/2009          | 916.70                  | 916.70           | 280.72            | 11/2010               | 03/2011     | 4(O)                              | 0/0                        |
| 101  | GSM equipment of 1700000Lines (2G) 234100 lines 3(-) [N26000092]BSNL,Karnataka      | 10/2008          | 677.75<br>719.90        | 719.90           | 461.56            | 10/2009               | 03/2011     | 17(O)                             | 0/0                        |
| 102  | PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State               | 11/2003          | 250.00                  | 425.51           | 80.47             | 12/2005               | -           | -                                 | 0/0                        |
| 103  | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra     | 06/2006          | 231.38                  | 168.30           | -                 | 10/2007               | -           | -                                 | 0/0                        |
| 104  | MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State                     | 11/2008          | 350.00                  | 350.00           | -                 | -                     | -           | -                                 | 0/0                        |
| 105  | Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State   | 05/2006          | 1,077.00                | 1,077.00         | -                 | 03/2009               | -           | -                                 | 0/0                        |
| 106  | Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State                    | 08/2006          | 424.00                  | 424.00           | -                 | 03/2009               | -           | -                                 | 0/0                        |
| 107  | Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State            | 08/2006          | 590.10                  | 590.10           | -                 | 03/2009               | -           | -                                 | 0/0                        |
| 108  | Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State      | 12/2007          | 545.50                  | 545.50           | -                 | 03/2010               | -           | -                                 | 0/0                        |
| 109  | Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State                    | 02/2007          | 154.03                  | 154.03           | -                 | 03/2010               | -           | -                                 | 0/0                        |
| 110  | Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State                  | 03/2008          | 355.92                  | 355.92           | -                 | 03/2010               | -           | -                                 | 0/0                        |
| 111  | Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State                   | 02/2007          | 477.00                  | 477.00           | -                 | 03/2010               | -           | -                                 | 0/0                        |
| 112  | Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State    | 12/2007          | 152.65                  | 152.65           | -                 | 03/2010               | -           | -                                 | 0/0                        |

## List of project Without Date of Commissioning

Aug,2011)

| S.No Project             |                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------------------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                          |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                        | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 113                      | Procurement of DXC equipment - [N26000074]BSNL,Multi State                          | 02/2008          | 229.00                  | 229.00           | -                 | 03/2010               | -           | -                                 | 0/0                        |
| 114                      | GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh | 02/2009          | 625.53                  | 625.53           | -                 | 02/2010               | -           | -                                 | 0/0                        |
| 115                      | GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh    | 09/2009          | 624.75                  | 624.75           | -                 | 09/2010               | -           | -                                 | 0/0                        |
| 116                      | GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal     | 06/2008          | 170.23                  | 170.23           | -                 | 06/2009               | -           | -                                 | 0/0                        |
| 117                      | GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd    | 03/2008          | 328.13                  | 328.12           | 164.58            | 03/2009               | -           | -                                 | 0/0                        |
| Total                    |                                                                                     |                  | 18,443.27               | 19,047.41        | 5,880.00          |                       |             |                                   | 0/1                        |
| <u>Urban Development</u> |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 118                      | C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra    | 11/2006          | 114.18                  | 173.08           | -                 | 04/2009               | -           | -                                 | 0/0                        |
| Total                    |                                                                                     |                  | 114.18                  | 173.08           | .00               |                       |             |                                   | 0/0                        |
| Grand Total              |                                                                                     |                  | 61,615.01               | 81,643.30        | 37,342.53         |                       |             |                                   | 144/173                    |

## List of Delay Project

Aug,2011)

| S.No                  | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|-----------------------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                       |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                     | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <u>Atomic Energy</u>  |                                                                                  |                  |                         |                  |                   |                       |             |                                   |                            |
| 1                     | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu | 09/2003          | 3,492.00 -              | 5,677.00         | 3,178.67          | 09/2010 -             | 01/2012     | 16(O)                             | 8/80                       |
| 2                     | KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu                             | 12/2001          | 13,171.00 -             | 15,824.00        | 13,994.00         | 12/2008 -             | 07/2012     | 43(O)                             | 61/119                     |
| 3                     | KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat                   | 10/2009          | 11,459.00 -             | 11,459.00        | 959.00            | 12/2015 05/2016       | 11/2016     | 6(R1)                             | 0/70                       |
| Total                 |                                                                                  |                  | 28,122.00 -             | 32,960.00        | 18,131.67         |                       |             |                                   | 69/269                     |
| <u>Civil Aviation</u> |                                                                                  |                  |                         |                  |                   |                       |             |                                   |                            |
| 4                     | D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu    | 08/2008          | 1,273.00 2,015.00       | 2,015.00         | 928.46            | 01/2011 -             | 12/2011     | 11(O)                             | 0/0                        |
| 5                     | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal   | 08/2008          | 1,942.51 -              | 2,325.00         | 1,333.00          | 05/2011 -             | 03/2012     | 10(O)                             | 0/0                        |
| 6                     | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim               | 01/2009          | 309.40 -                | 264.29           | 147.16            | 01/2011 -             | 12/2012     | 23(O)                             | 0/0                        |
| Total                 |                                                                                  |                  | 3,524.91 -              | 4,604.29         | 2,408.62          |                       |             |                                   | 0/0                        |
| <u>Coal</u>           |                                                                                  |                  |                         |                  |                   |                       |             |                                   |                            |
| 7                     | BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan                        | 12/2004          | 1,114.18 1,626.09       | 1,626.09         | 1,640.49          | 06/2009 -             | 09/2011     | 27(O)                             | 59/26                      |
| 8                     | KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa                     | 01/2005          | 302.96 -                | 302.96           | 83.72             | 03/2010 -             | 03/2012     | 24(O)                             | 9/11                       |
| 9                     | ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd                         | 04/2006          | 471.66 341.63           | 341.63           | 101.43            | 03/2011 03/2012       | 03/2012     | 0(R3)                             | 0/2                        |
| 10                    | TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu            | 10/2004          | 2,030.78 2,453.57       | 2,453.57         | 2,249.78          | 06/2009 -             | 05/2012     | 35(O)                             | 60/24                      |
| 11                    | KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh                        | 05/2006          | 789.88 741.62           | 741.62           | 139.06            | 03/2010 03/2013       | 03/2013     | 0(R3)                             | 0/2                        |
| 12                    | ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh                          | 09/2006          | 212.34 779.26           | 779.26           | 196.17            | 03/2013 09/2012       | 12/2013     | 15(R3)                            | 2/22                       |
| 13                    | GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh                | 07/2005          | 1,667.55 -              | 2,675.67         | 1,258.36          | 03/2010 -             | 03/2014     | 48(O)                             | 3/15                       |
| 14                    | DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh             | 07/2005          | 1,268.53 -              | 1,943.66         | 1,070.26          | 03/2010 -             | 03/2014     | 48(O)                             | 2/13                       |
| 15                    | RAJMAHAL OC EXP. - [N06000056]ECL,Multi State                                    | 02/2006          | 50.08 153.82            | 153.82           | 19.49             | 03/2011 -             | 03/2014     | 36(O)                             | 0/3                        |
| 16                    | Churi Benti UG - [N06000083]CCL,Jharkhandd                                       | 06/2007          | 163.51 -                | 163.51           | 33.57             | 03/2011 03/2012       | 03/2014     | 24(R3)                            | 0/2                        |

## List of Delay Project

Aug,2011)

| S.No | Project                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 17   | North Urimari OCP -<br>[N06000084]CCL,Jharkhandd                                                  | 12/2007          | 179.87                  | 179.87           | 66.45             | 03/2012<br>03/2012    | 03/2014     | 24(R3)                            | 0/2                        |
| 18   | Tapin OCP -<br>[N06000086]CCL,Jharkhandd                                                          | 08/2008          | 264.68                  | 264.68           | 76.05             | 03/2012<br>03/2013    | 03/2014     | 12(R3)                            | 0/2                        |
| 19   | BLOCK-B OCP NCL (3.5 MTY) -<br>[N06000009]NCL,Madhya pradesh                                      | 06/2006          | 746.04<br>535.10        | 535.10           | 139.84            | 03/2012<br>-          | 03/2015     | 36(O)                             | 0/2                        |
| 20   | JHANJRA R-VI SEAM PSLW -<br>[N06000020]ECL,West Bengal                                            | 11/2006          | 287.18                  | 287.17           | -                 | 03/2011<br>-          | 03/2015     | 48(O)                             | 1/5                        |
| 21   | KAKATIYA LAONGWALL -<br>[N06000048]SCCL,Multi State                                               | 12/2008          | 453.63                  | 453.63           | 67.70             | 12/2012<br>-          | 03/2015     | 27(O)                             | 11/44                      |
| 22   | AMLOHRI EPR (NCL) (6 MTY) -<br>[N06000010]NCL,Madhya pradesh                                      | 05/2006          | 1,352.04<br>1,143.54    | 1,143.54         | 206.07            | 03/2014<br>-          | 03/2016     | 24(O)                             | 1/2                        |
| 23   | MAGADH OC (CCL) -<br>[N06000015]CCL,Jharkhandd                                                    | 07/2006          | 469.78<br>706.40        | 706.40           | 16.21             | 07/2012<br>03/2014    | 03/2016     | 24(R3)                            | 0/2                        |
|      | <b>Total</b>                                                                                      |                  | <b>11,824.69</b>        | <b>14,752.18</b> | <b>7,364.65</b>   |                       |             |                                   | <b>148/179</b>             |
|      |                                                                                                   |                  | -                       |                  |                   |                       |             |                                   |                            |
|      | <b>Fertilisers</b>                                                                                |                  |                         |                  |                   |                       |             |                                   |                            |
| 24   | CAPACITY ENHANCEMENT OF<br>VIJAI PUR-I PLANTS -<br>[N08000007]NFL,Madhya pradesh                  | 09/2008          | 325.00                  | 325.00           | 84.31             | 07/2011<br>-          | 11/2011     | 4(O)                              | 0/0                        |
| 25   | CAPACITY ENHANCEMENT OF<br>AMMONIA AND UREA PLANT VIJ -<br>[N08000008]NFL,Madhya pradesh          | 09/2008          | 438.00                  | 438.00           | 105.79            | 07/2011<br>-          | 03/2012     | 8(O)                              | 0/0                        |
| 26   | NANGAL - AMMONIA PLANT<br>FEEDSTOCK PROJECT -<br>[N08000006]NFL,Punjab                            | 01/2010          | 1,478.63                | 1,478.63         | 223.57            | 12/2012<br>-          | 01/2013     | 1(O)                              | 0/8                        |
|      | <b>Total</b>                                                                                      |                  | <b>2,241.63</b>         | <b>2,241.63</b>  | <b>413.67</b>     |                       |             |                                   | <b>0/8</b>                 |
|      |                                                                                                   |                  | -                       |                  |                   |                       |             |                                   |                            |
|      | <b>Steel</b>                                                                                      |                  |                         |                  |                   |                       |             |                                   |                            |
| 27   | EXPANSION OF RINL/VSP FROM 3<br>MTPY-6.3 MTPY OF LIQUID STEEL -<br>[120100067]RINL,Andhra Pradesh | 10/2005          | 8,692.00<br>12,291.00   | 12,291.00        | 8,719.80          | 10/2009<br>10/2012    | 10/2012     | 0(R3)                             | 47/59                      |
|      | <b>Total</b>                                                                                      |                  | <b>8,692.00</b>         | <b>12,291.00</b> | <b>8,719.80</b>   |                       |             |                                   | <b>47/59</b>               |
|      |                                                                                                   |                  | -                       |                  |                   |                       |             |                                   |                            |
|      | <b>Petroleum</b>                                                                                  |                  |                         |                  |                   |                       |             |                                   |                            |
| 28   | DIESEL HYDRO TREATMENT<br>PROJECT,BRPL DHALIGAON -<br>[N16000009]BRPL,Assam                       | 06/2006          | 1,431.91<br>1,646.39    | 1,690.13         | -                 | 09/2009<br>-          | 08/2011     | 23(O)                             | 0/0                        |
| 29   | CONSTRUCTION OF NEW TERMINAL<br>AT ENNORE CHENNAI -<br>[N16000066]HPCL,Tamil Nadu                 | 01/2008          | 224.00<br>299.00        | 299.00           | 240.00            | 02/2011<br>08/2011    | 08/2011     | 0(R3)                             | 0/0                        |
| 30   | MSQ QUALITY UP GRADATION<br>PROJECT AT BONGAIGAON REF -<br>[N16000040]IOCL,Assam                  | 04/2008          | 293.60                  | 261.75           | 230.97            | 12/2009<br>-          | 09/2011     | 21(O)                             | 0/0                        |
| 31   | DAHEJ-VIJAYPUR PIPE LINE<br>PROJECT(PHASE-II) -<br>[N16000052]GAIL,Multi State                    | 11/2007          | 4,429.38                | 2,340.00         | 2,200.48          | 10/2010<br>09/2011    | 09/2011     | 0(R2)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 32   | REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra                             | 06/2008          | 304.40                  | 304.40           | 245.01            | 06/2010<br>07/2011    | 09/2011     | 2(R3)                             | 0/0                        |
| 33   | HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra                 | 09/2006          | 2,305.30<br>700.00      | 3,005.30         | 2,416.96          | 06/2010<br>06/2010    | 10/2011     | 16(R3)                            | 0/0                        |
| 34   | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                               | 08/2006          | 3,195.16                | 2,800.00         | 2,520.91          | 12/2008<br>12/2008    | 11/2011     | 35(R3)                            | 0/0                        |
| 35   | BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State                              | 11/2007          | 1,816.07                | 1,385.00         | -                 | 10/2010<br>12/2011    | 12/2011     | 0(R3)                             | 0/1                        |
| 36   | COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State                   | 11/2007          | 1,167.00<br>1,167.00    | 798.00           | 631.81            | 04/2011<br>12/2011    | 12/2011     | 0(R3)                             | 0/2                        |
| 37   | HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra                                         | 05/2008          | 706.70                  | 706.70           | 626.78            | 04/2010<br>-          | 12/2011     | 20(O)                             | 0/0                        |
| 38   | NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra                                        | 05/2008          | 305.08                  | 305.08           | 250.40            | 04/2011<br>-          | 12/2011     | 8(O)                              | 0/0                        |
| 39   | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State              | 06/2007          | 736.65                  | 736.65           | 210.39            | 09/2011<br>-          | 12/2011     | 3(O)                              | 0/0                        |
| 40   | EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu                                                  | 09/2008          | 2,615.69                | 2,615.69         | 1,632.03          | 05/2011<br>-          | 12/2011     | 7(O)                              | 0/116                      |
| 41   | MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra                                        | 05/2008          | 175.21                  | 162.12           | 58.26             | 03/2009<br>02/2012    | 02/2012     | 0(R3)                             | 0/0                        |
| 42   | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra       | 01/2007          | 740.02                  | 740.02           | 412.78            | 03/2010<br>03/2012    | 03/2012     | 0(R1)                             | 0/0                        |
| 43   | VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State | 12/2009          | 463.32                  | 330.47           | 138.07            | 06/2011<br>03/2012    | 03/2012     | 0(R3)                             | 3/9                        |
| 44   | INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State                       | 04/2003          | 429.82<br>2,218.01      | 2,218.01         | 1,237.61          | 04/2006<br>05/2011    | 05/2012     | 12(R3)                            | 0/0                        |
| 45   | CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra                      | 01/2007          | 2,853.29<br>6,326.40    | 6,326.40         | 3,535.29          | 05/2010<br>05/2012    | 05/2012     | 0(R3)                             | 0/0                        |
| 46   | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                           | 01/2007          | 2,323.40<br>2,920.82    | 2,920.82         | 1,173.84          | 09/2010<br>03/2012    | 05/2012     | 2(R3)                             | 0/0                        |
| 47   | REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra                        | 05/2008          | 333.40<br>837.54        | 656.51           | 20.10             | 05/2010<br>04/2012    | 05/2012     | 1(R3)                             | 0/0                        |
| 48   | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                            | 06/2007          | 1,436.21<br>1,456.96    | 1,436.21         | 82.57             | 07/2010<br>05/2012    | 05/2012     | 0(R3)                             | 0/0                        |
| 49   | DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra                          | 06/2007          | 3,248.78<br>5,633.44    | 5,633.44         | 1,366.95          | 08/2010<br>03/2012    | 06/2012     | 3(R3)                             | 0/0                        |
| 50   | ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat                     | 02/2008          | 370.11                  | 370.11           | 67.89             | 04/2011<br>-          | 07/2012     | 15(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No                | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|---------------------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                     |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                   | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 51                  | BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State                 | 12/2009          | 540.92<br>-             | 460.70           | 146.19            | 06/2011<br>07/2012    | 07/2012     | 0(R3)                             | 7/9                        |
| 52                  | DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State             | 06/2009          | 4,543.43<br>4,508.38    | 2,500.00         | 1,047.00          | 03/2012<br>08/2012    | 08/2012     | 0(R3)                             | 11/10                      |
| 53                  | ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra               | 10/2008          | 1,797.35<br>-           | 1,797.35         | 72.19             | 12/2011<br>-          | 01/2013     | 13(O)                             | 0/0                        |
| 54                  | Development of SB-14 field - [N16000116]ONGC,Multi State                            | 01/2011          | 410.44<br>-             | 410.44           | -                 | 11/2012<br>-          | 01/2013     | 2(O)                              | 0/0                        |
| 55                  | IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam                                     | 09/2001          | 113.90<br>438.85        | 438.85           | 231.94            | 03/2006<br>03/2013    | 03/2013     | 0(R3)                             | 6/6                        |
| 56                  | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra                  | 10/2007          | 5,713.03<br>8,813.41    | 8,813.41         | 6,767.50          | 05/2010<br>03/2013    | 03/2013     | 0(R3)                             | 0/0                        |
| 57                  | HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra      | 04/2008          | 825.00<br>1,827.00      | 1,827.00         | -                 | 12/2011<br>04/2013    | 04/2013     | 0(R3)                             | 0/203                      |
| 58                  | PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa                                   | 02/2009          | 29,777.00<br>-          | 29,777.00        | 8,953.92          | 11/2012<br>06/2013    | 06/2013     | 0(R3)                             | 107/100                    |
| 59                  | IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam                                | 09/2001          | 345.10<br>663.69        | 663.69           | 592.78            | 03/2007<br>03/2014    | 03/2014     | 0(R3)                             | 3/3                        |
| 60                  | IOR GELEKI (ONGCL) - [160100216]ONGC,Assam                                          | 09/2001          | 390.09<br>1,674.11      | 1,674.11         | 1,375.28          | 03/2007<br>03/2017    | 03/2017     | 0(R3)                             | 6/6                        |
| 61                  | RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh | 01/2009          | 756.00<br>-             | 756.00           | 711.47            | 09/2011<br>-          | 12/2011     | 3(O)                              | 0/0                        |
| <b>Total</b>        |                                                                                     |                  | 77,116.76<br>-          | 87,160.36        | 39,197.37         |                       |             |                                   | 143/465                    |
| <b><u>Power</u></b> |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 62                  | TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State      | 12/2008          | 204.07<br>-             | 204.07           | 112.43            | 06/2011<br>-          | 08/2011     | 2(O)                              | 0/0                        |
| 63                  | TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K                  | 10/2006          | 238.25<br>-             | 227.03           | 211.35            | 05/2011<br>05/2011    | 09/2011     | 4(R3)                             | 0/0                        |
| 64                  | EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State               | 12/2007          | 227.52<br>-             | 227.52           | 132.86            | 06/2010<br>-          | 09/2011     | 15(O)                             | 0/0                        |
| 65                  | CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.                             | 08/2005          | 1,405.63<br>-           | 1,405.63         | 1,651.81          | 08/2010<br>-          | 11/2011     | 15(O)                             | 0/0                        |
| 66                  | URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K                                  | 08/2005          | 1,724.79<br>-           | 1,724.79         | 1,522.71          | 11/2009<br>-          | 12/2011     | 25(O)                             | 0/0                        |
| 67                  | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr. | 07/2006          | 557.24<br>-             | 639.52           | 465.15            | 01/2010<br>-          | 12/2011     | 23(O)                             | 0/22                       |
| 68                  | WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan                 | 07/2006          | 5,221.23<br>-           | 4,978.56         | 2,925.54          | 07/2010<br>-          | 12/2011     | 17(O)                             | 3/20                       |

## List of Delay Project

Aug,2011)

| S.No Project |                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 69           | TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State            | 04/2008          | 297.37<br>-             | 297.37           | 295.61            | 07/2011<br>-          | 12/2011     | 5(O)                              | 0/0                        |
| 70           | CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K                         | 08/2006          | 621.28<br>-             | 621.28           | 680.28            | 02/2011<br>-          | 02/2012     | 12(O)                             | 0/1                        |
| 71           | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan        | 02/2009          | 210.79<br>-             | 210.79           | 144.56            | 08/2011<br>-          | 02/2012     | 6(O)                              | 0/0                        |
| 72           | TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State           | 02/2009          | 353.57<br>-             | 353.57           | 206.98            | 07/2010<br>02/2012    | 02/2012     | 0(R3)                             | 0/0                        |
| 73           | SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State           | 03/2009          | 196.10<br>-             | 196.10           | 72.09             | 07/2011<br>-          | 02/2012     | 7(O)                              | 0/0                        |
| 74           | KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal                                   | 04/2000          | 1,301.56<br>-           | 2,283.69         | 2,481.22          | 04/2005<br>-          | 03/2012     | 83(O)                             | 6/11                       |
| 75           | SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh                            | 12/2003          | 8,323.39<br>-           | 8,323.39         | 7,284.00          | 12/2009<br>-          | 03/2012     | 27(O)                             | 33/60                      |
| 76           | PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.                      | 10/2005          | 2,304.52<br>-           | 2,304.52         | 1,534.06          | 10/2010<br>-          | 03/2012     | 17(O)                             | 0/0                        |
| 77           | TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar | 12/2005          | 3,779.46<br>-           | 3,725.13         | 3,483.30          | 09/2009<br>-          | 03/2012     | 30(O)                             | 15/30                      |
| 78           | EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State                 | 10/2006          | 975.96<br>-             | 894.26           | 690.07            | 10/2009<br>-          | 03/2012     | 29(O)                             | 2/20                       |
| 79           | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State      | 02/2009          | 317.69<br>-             | 317.69           | 54.29             | 11/2011<br>-          | 03/2012     | 4(O)                              | 0/0                        |
| 80           | TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal     | 10/2003          | 768.92<br>-             | 768.92           | 1,349.12          | 03/2007<br>-          | 05/2012     | 62(O)                             | 1/25                       |
| 81           | NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K                            | 08/2006          | 611.02<br>-             | 611.02           | 657.77            | 08/2010<br>-          | 11/2012     | 27(O)                             | 0/0                        |
| 82           | MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra                                      | 11/2008          | 5,459.28<br>-           | 6,010.89         | 2,790.00          | 08/2012<br>-          | 11/2012     | 3(O)                              | 2/16                       |
| 83           | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal                    | 09/2005          | 1,061.38<br>-           | 1,061.38         | 1,007.32          | 09/2009<br>-          | 12/2012     | 39(O)                             | 0/0                        |
| 84           | KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu                   | 05/2005          | 1,779.29<br>-           | 1,946.85         | 1,727.35          | 11/2008<br>-          | 12/2012     | 49(O)                             | 25/38                      |
| 85           | LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal                             | 06/2006          | 2,895.10<br>-           | 2,895.10         | 685.00            | 11/2011<br>-          | 12/2012     | 13(O)                             | 6/34                       |
| 86           | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State     | 02/2009          | 509.66<br>-             | 509.66           | 245.77            | 11/2011<br>-          | 12/2012     | 13(O)                             | 0/0                        |
| 87           | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State       | 02/2009          | 410.29<br>-             | 410.29           | 128.49            | 02/2012<br>-          | 12/2012     | 10(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                    |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                  | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 88   | VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC, Madhya Pradesh                 | 01/2009          | 5,915.00<br>-           | 5,915.00         | 2,135.00          | 10/2012<br>-          | 12/2012     | 2(O)                              | 2/15                       |
| 89   | RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh            | 01/2009          | 6,230.81<br>-           | 6,230.81         | 2,003.00          | 10/2012<br>-          | 12/2012     | 2(O)                              | 3/16                       |
| 90   | KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.                                  | 10/2002          | 4,527.15<br>-           | 4,527.15         | 3,777.00          | 04/2009<br>-          | 03/2013     | 47(O)                             | 19/9                       |
| 91   | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra              | 12/2007          | 477.69<br>-             | 477.69           | 340.11            | 09/2010<br>-          | 03/2013     | 30(O)                             | 0/0                        |
| 92   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State     | 02/2009          | 520.48<br>-             | 520.48           | 259.63            | 11/2011<br>-          | 03/2013     | 16(O)                             | 0/0                        |
| 93   | 765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL, Multi State | 02/2009          | 1,347.32<br>-           | 1,347.32         | 842.45            | 02/2012<br>-          | 03/2013     | 13(O)                             | 0/0                        |
| 94   | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura                       | 07/2009          | 421.01<br>623.44        | 623.44           | 68.22             | 01/2012<br>-          | 07/2013     | 18(O)                             | 0/0                        |
| 95   | RAMPUR HEP (412 MW) - [N18000024]SJVN, Himachal Pr.                                | 01/2007          | 2,047.03<br>-           | 2,047.03         | 1,317.70          | 01/2012<br>-          | 09/2013     | 20(O)                             | 2/10                       |
| 96   | TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State     | 02/2009          | 184.19<br>-             | 184.19           | 127.76            | 11/2011<br>-          | 09/2013     | 22(O)                             | 0/0                        |
| 97   | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, Assam                          | 01/2008          | 4,375.35<br>-           | 4,375.35         | 2,242.00          | 06/2011<br>-          | 10/2013     | 28(O)                             | 0/29                       |
| 98   | TUIRIAL HE PROJECT (NEEPCO) - [180100165]NEEPCO, Mizoram                           | 07/1998          | 368.72<br>913.63        | 913.63           | 247.90            | 07/2006<br>01/2014    | 01/2014     | 0(R3)                             | 2/5                        |
| 99   | TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal              | 11/2006          | 2,978.48<br>-           | 2,978.48         | 1,133.00          | 03/2013<br>-          | 06/2014     | 15(O)                             | 5/13                       |
| 100  | SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.                      | 09/2003          | 6,285.33<br>-           | 6,285.33         | 5,056.36          | 09/2010<br>-          | 08/2014     | 47(O)                             | 2/11                       |
| 101  | BARH STTP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar                          | 12/2003          | 8,692.97<br>-           | 8,693.00         | 6,070.00          | 12/2009<br>-          | 09/2014     | 57(O)                             | 15/70                      |
| 102  | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State | 02/2009          | 11,130.19<br>-          | 11,130.19        | 2,877.41          | 08/2013<br>-          | 09/2014     | 13(O)                             | 0/0                        |
| 103  | PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.                              | 09/2002          | 3,919.59<br>-           | 3,919.59         | 3,265.14          | 09/2009<br>-          | 12/2014     | 63(O)                             | 1/20                       |
| 104  | KISHANGANGA HEP - [N18000031]NHPC, J & K                                           | 07/2007          | 2,238.67<br>3,642.04    | 3,642.04         | 923.91            | 07/2014<br>-          | 01/2016     | 18(O)                             | 0/0                        |
| 105  | TEHRI PUMPED STORAGE PLANT (1000MW) - [N18000010]THDCL, Uttaranchal                | 07/2006          | 1,657.00<br>-           | 2,978.86         | 261.82            | 07/2010<br>-          | 02/2016     | 67(O)                             | 1/1                        |
| 106  | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttaranchal         | 08/2008          | 2,491.58<br>2,491.58    | 3,422.44         | 168.98            | 07/2014<br>-          | 05/2016     | 22(O)                             | 0/7                        |
| 107  | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.           | 12/2004          | 2,496.90<br>-           | 2,496.90         | 1,554.07          | 05/2013<br>06/2016    | 06/2016     | 0(R3)                             | 79/22                      |

## List of Delay Project

Aug,2011)

| S.No                   | Project                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost  | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------------|-------------------------------------------------------------------------------|------------------|-------------------------|-------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                        |                                                                               |                  |                         |                   |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                      | 2                                                                             | 3                | 4                       | 5                 | 6                 | 7                     | 8           | 9                                 | 10                         |
| 108                    | WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State         | 04/2008          | 230.89<br>-             | 230.89            | 92.04             | 01/2011<br>-          | 10/2011     | 9(O)                              | 0/1                        |
|                        | <b>Total</b>                                                                  |                  | <b>110,291.71</b><br>-  | <b>116,088.83</b> | <b>67,302.63</b>  |                       |             |                                   | <b>224/506</b>             |
| <u><b>Railways</b></u> |                                                                               |                  |                         |                   |                   |                       |             |                                   |                            |
| 109                    | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa                         | 04/1993          | 100.00<br>142.90        | 208.68            | 182.17            | 03/2002<br>-          | 09/2011     | 114(O)                            | 0/0                        |
| 110                    | PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal                      | 09/2007          | 252.50<br>-             | 252.50            | 162.23            | 02/2010<br>-          | 11/2011     | 21(O)                             | 0/0                        |
| 111                    | GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State                             | 04/1985          | 158.77<br>432.46        | 540.96            | 558.55            | 03/1994<br>-          | 12/2011     | 213(O)                            | 0/0                        |
| 112                    | NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh                  | 03/1996          | 155.74<br>164.36        | 822.57            | 486.71            | 02/2009<br>-          | 12/2011     | 34(O)                             | 0/0                        |
| 113                    | Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal              | 04/2009          | 259.51<br>-             | 259.51            | 62.43             | 12/2011<br>-          | 02/2012     | 2(O)                              | 0/0                        |
| 114                    | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State    | 03/1984          | 520.00<br>637.46        | 637.46            | 542.72            | 03/1995<br>-          | 03/2012     | 204(O)                            | 0/0                        |
| 115                    | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh             | 09/2006          | 324.90<br>-             | 324.90            | 187.13            | 03/2010<br>-          | 03/2012     | 24(O)                             | 0/0                        |
| 116                    | ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh               | 12/2004          | 129.17<br>-             | 220.00            | 217.49            | 03/2011<br>-          | 03/2012     | 12(O)                             | 0/0                        |
| 117                    | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal                 | 03/1984          | 293.97<br>-             | 723.27            | 378.13            | 06/2005<br>07/2011    | 03/2012     | 8(R3)                             | 0/0                        |
| 118                    | Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan | 04/2007          | 643.36<br>-             | 803.39            | 786.86            | 03/2011<br>-          | 03/2012     | 12(O)                             | 0/0                        |
| 119                    | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal                 | 04/1974          | 31.42<br>154.30         | 499.16            | 142.91            | 03/2007<br>03/2007    | 06/2012     | 63(R1)                            | 0/0                        |
| 120                    | BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal                     | 03/1998          | 111.90<br>-             | 1,211.22          | 387.79            | 03/2005<br>12/2008    | 12/2012     | 48(R1)                            | 0/0                        |
| 121                    | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar               | 04/2002          | 921.00<br>-             | 981.00            | 528.45            | 03/2009<br>-          | 12/2012     | 45(O)                             | 0/0                        |
| 122                    | PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar                           | 04/2001          | 624.47<br>-             | 1,389.98          | 957.77            | 10/2007<br>-          | 12/2012     | 62(O)                             | 0/0                        |
| 123                    | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh                 | 09/2007          | 687.20<br>-             | 687.20            | 339.93            | 03/2010<br>-          | 12/2012     | 33(O)                             | 0/0                        |
| 124                    | Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh                 | 04/2008          | 603.04<br>-             | 603.04            | 45.14             | 03/2012<br>-          | 03/2013     | 12(O)                             | 0/0                        |
| 125                    | Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal                         | 04/2009          | 189.97<br>-             | 189.97            | 58.46             | 12/2011<br>-          | 11/2013     | 23(O)                             | 0/0                        |
| 126                    | Katakhal to Bhairabi - [N22000126]NEFR,Assam                                  | 04/1998          | 227.90<br>-             | 223.01            | 83.45             | 12/2012<br>-          | 12/2013     | 12(O)                             | 0/0                        |
| 127                    | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam    | 04/1996          | 1,676.31<br>-           | 4,091.33          | 2,776.44          | 03/2009<br>-          | 12/2013     | 57(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No                                        | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|---------------------------------------------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                                             |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                                           | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 128                                         | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State         | 04/2000          | 733.00<br>-             | 1,655.80         | 808.72            | 12/2008<br>-          | 03/2014     | 63(O)                             | 0/0                        |
| 129                                         | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh                     | 04/2006          | 325.00<br>-             | 369.90           | 97.35             | 03/2010<br>06/2014    | 06/2014     | 0(R3)                             | 0/0                        |
| 130                                         | RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam               | 09/1997          | 1,000.00<br>1,500.00    | 3,230.01         | 2,215.96          | 04/2008<br>03/2014    | 12/2014     | 9(R3)                             | 0/0                        |
| 131                                         | MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra               | 04/2008          | 5,300.00<br>-           | 5,300.00         | 278.51            | 03/2014<br>-          | 03/2015     | 12(O)                             | 0/0                        |
| 132                                         | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur                            | 04/2003          | 727.56<br>727.53        | 3,056.85         | 463.33            | 03/2011<br>03/2014    | 03/2016     | 24(R3)                            | 0/0                        |
| 133                                         | New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal         | 04/2010          | 2,069.60<br>-           | 2,069.60         | 0.21              | 03/2014<br>-          | 03/2016     | 24(O)                             | 0/0                        |
| 134                                         | New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal         | 04/2010          | 2,397.72<br>-           | 2,397.72         | 0.02              | 03/2016<br>-          | 06/2016     | 3(O)                              | 0/0                        |
| 135                                         | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K                              | 03/1995          | 2,500.00<br>8,000.00    | 20,000.00        | 7,189.29          | 03/2001<br>-          | 12/2017     | 201(O)                            | 0/0                        |
|                                             | <b>Total</b>                                                                             |                  | 22,964.01<br>-          | 52,749.03        | 19,938.15         |                       |             |                                   | 0/0                        |
| <b><u>Road Transport &amp; Highways</u></b> |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 136                                         | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka                     | 04/2000          | 241.00<br>-             | 196.65           | 149.93            | 08/2004<br>-          | 09/2011     | 85(O)                             | 0/0                        |
| 137                                         | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka                | 04/2000          | 318.00<br>-             | 207.56           | 160.48            | 08/2004<br>-          | 09/2011     | 85(O)                             | 0/0                        |
| 138                                         | HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal                    | 04/2000          | 273.00<br>-             | 522.00           | 475.55            | 03/2005<br>-          | 09/2011     | 78(O)                             | 0/0                        |
| 139                                         | GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat   | 12/2003          | 412.78<br>-             | 479.54           | 436.46            | 11/2007<br>-          | 09/2011     | 46(O)                             | 0/0                        |
| 140                                         | AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh   | 12/2003          | 217.00<br>-             | 217.00           | 352.26            | 10/2008<br>-          | 09/2011     | 35(O)                             | 0/0                        |
| 141                                         | MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu | 03/2005          | 629.00<br>-             | 629.00           | 910.04            | 11/2010<br>-          | 09/2011     | 10(O)                             | 0/0                        |
| 142                                         | LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh        | 12/2003          | 225.00<br>-             | 225.00           | 254.49            | 10/2008<br>-          | 09/2011     | 35(O)                             | 0/0                        |
| 143                                         | RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar                                   | 12/2003          | 340.00<br>-             | 340.00           | 561.31            | 06/2008<br>-          | 09/2011     | 39(O)                             | 0/0                        |
| 144                                         | THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala                                    | 12/2003          | 312.50<br>-             | 312.50           | 602.56            | 03/2009<br>-          | 09/2011     | 30(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No Project |                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 145          | ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal                          | 12/2003          | 221.82                  | 221.82           | 241.98            | 11/2008               | 09/2011     | 34(O)                             | 0/0                        |
| 146          | TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu                                      | 03/2005          | 576.00                  | 576.00           | 657.66            | 07/2010               | 09/2011     | 14(O)                             | 0/0                        |
| 147          | PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu                                 | 03/2005          | 285.00                  | 285.00           | 359.10            | 07/2010               | 09/2011     | 14(O)                             | 0/0                        |
| 148          | NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka             | 03/2005          | 441.00                  | 441.00           | 908.83            | 07/2010               | 09/2011     | 14(O)                             | 0/0                        |
| 149          | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa                 | 04/2000          | 228.70                  | 228.70           | 165.14            | 02/2004               | 09/2011     | 91(O)                             | 0/0                        |
| 150          | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh                        | 03/2005          | 190.00                  | 190.00           | 227.03            | 01/2009               | 10/2011     | 33(O)                             | 0/0                        |
| 151          | DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam                                     | 12/2003          | 225.00                  | 225.00           | 254.16            | 06/2008               | 10/2011     | 40(O)                             | 0/0                        |
| 152          | NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra                                  | 03/2005          | 168.00                  | 168.00           | 385.27            | 12/2008               | 10/2011     | 34(O)                             | 0/0                        |
| 153          | JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh                                  | 12/2003          | 276.09                  | 276.09           | 295.27            | 09/2009               | 10/2011     | 25(O)                             | 0/0                        |
| 154          | END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh            | 01/2008          | 464.00                  | 464.00           | 419.88            | 01/2011               | 10/2011     | 9(O)                              | 0/0                        |
| 155          | KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan                                | 12/2003          | 275.00                  | 250.39           | 277.08            | 10/2008               | 11/2011     | 37(O)                             | 0/0                        |
| 156          | SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh              | 12/2003          | 151.30                  | 151.30           | 172.23            | 10/2008               | 11/2011     | 37(O)                             | 0/0                        |
| 157          | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa                        | 04/2000          | 225.00                  | 241.53           | 77.54             | 04/2004               | 12/2011     | 92(O)                             | 0/0                        |
| 158          | AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh            | 04/2000          | 367.49                  | 367.49           | 453.68            | 03/2005               | 12/2011     | 81(O)                             | 0/0                        |
| 159          | GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh | 12/2003          | 275.00                  | 275.00           | 296.55            | 09/2007               | 12/2011     | 51(O)                             | 0/0                        |
| 160          | HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh              | 03/2005          | 220.00                  | 220.00           | 239.26            | 09/2007               | 12/2011     | 51(O)                             | 0/0                        |
| 161          | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh  | 12/2003          | 155.00                  | 201.66           | 88.13             | 09/2008               | 12/2011     | 39(O)                             | 0/0                        |
| 162          | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam          | 12/2003          | 230.00                  | 230.00           | 203.38            | 06/2005               | 12/2011     | 78(O)                             | 0/0                        |
| 163          | VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K            | 12/2003          | 193.09                  | 166.30           | 179.19            | 03/2008               | 12/2011     | 45(O)                             | 0/0                        |
| 164          | VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K            | 12/2003          | 166.27                  | 193.10           | 147.71            | 03/2008               | 12/2011     | 45(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No | Project                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                                |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                              | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 165  | GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh      | 12/2003          | 227.00<br>-             | 227.00           | 394.13            | 10/2008<br>-          | 12/2011     | 38(O)                             | 0/0                        |
| 166  | ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh              | 12/2003          | 340.68<br>-             | 340.68           | 353.85            | 03/2008<br>-          | 12/2011     | 45(O)                             | 0/0                        |
| 167  | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam                 | 12/2003          | 280.00<br>-             | 280.00           | 224.96            | 02/2009<br>-          | 12/2011     | 34(O)                             | 0/0                        |
| 168  | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam                     | 12/2003          | 200.00<br>-             | 200.00           | 78.90             | 04/2009<br>-          | 12/2011     | 32(O)                             | 0/0                        |
| 169  | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam                            | 12/2003          | 195.00<br>-             | 195.00           | 172.21            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 170  | KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh                               | 12/2003          | 242.00<br>-             | 242.00           | 393.21            | 12/2008<br>-          | 12/2011     | 36(O)                             | 0/0                        |
| 171  | UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh                         | 12/2003          | 227.00<br>-             | 227.00           | 363.24            | 12/2008<br>-          | 12/2011     | 36(O)                             | 0/0                        |
| 172  | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                           | 12/2003          | 237.80<br>-             | 237.80           | 197.55            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 173  | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar                                    | 12/2003          | 332.94<br>-             | 332.94           | 289.08            | 09/2008<br>-          | 12/2011     | 39(O)                             | 0/0                        |
| 174  | LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh                               | 12/2003          | 198.00<br>-             | 198.00           | 187.06            | 11/2008<br>-          | 12/2011     | 37(O)                             | 0/0                        |
| 175  | RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh  | 12/2003          | 251.03<br>-             | 251.03           | 276.03            | 10/2008<br>-          | 12/2011     | 38(O)                             | 0/0                        |
| 176  | RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh | 12/2003          | 229.91<br>-             | 229.91           | 223.12            | 10/2008<br>-          | 12/2011     | 38(O)                             | 0/0                        |
| 177  | JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar                                          | 12/2003          | 340.00<br>-             | 340.00           | 426.99            | 09/2008<br>-          | 12/2011     | 39(O)                             | 0/0                        |
| 178  | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam                                                | 12/2003          | 200.00<br>-             | 200.00           | 255.34            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 179  | SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh                                                | 03/2005          | 322.00<br>-             | 322.00           | 553.66            | 06/2009<br>-          | 12/2011     | 30(O)                             | 0/0                        |
| 180  | NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka                                    | 04/2000          | 196.50<br>-             | 196.50           | 233.50            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 181  | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam                                             | 12/2003          | 264.72<br>-             | 264.72           | 246.10            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 182  | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam                                              | 12/2003          | 245.00<br>-             | 245.00           | 476.19            | 03/2008<br>-          | 12/2011     | 45(O)                             | 0/0                        |
| 183  | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam                                                | 12/2003          | 225.00<br>-             | 225.00           | 165.57            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 184  | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam                                                 | 12/2003          | 208.00<br>-             | 208.00           | 206.17            | 04/2008<br>-          | 12/2011     | 44(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No Project |                                                                                         | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                         |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                       | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 185          | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam                         | 12/2003          | 160.00                  | 160.00           | 121.62            | 05/2008               | 12/2011     | 43(O)                             | 0/0                        |
| 186          | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                    | 12/2003          | 200.00                  | 200.00           | 188.95            | 06/2008               | 12/2011     | 42(O)                             | 0/0                        |
| 187          | THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu                                | 03/2005          | 280.00                  | 280.00           | 580.67            | 06/2009               | 12/2011     | 30(O)                             | 0/0                        |
| 188          | GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh      | 12/2003          | 600.24                  | 600.24           | 692.67            | 10/2009               | 12/2011     | 26(O)                             | 0/0                        |
| 189          | KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar              | 12/2003          | 418.04                  | 418.04           | 322.97            | 03/2010               | 12/2011     | 21(O)                             | 0/0                        |
| 190          | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh                            | 12/2003          | 355.06                  | 355.06           | 294.66            | 09/2009               | 12/2011     | 27(O)                             | 0/0                        |
| 191          | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu                  | 03/2005          | 941.00                  | 941.00           | 1,901.00          | 01/2011               | 12/2011     | 11(O)                             | 0/0                        |
| 192          | PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab                                        | 12/2003          | 229.00                  | 284.00           | 338.97            | 05/2010               | 12/2011     | 19(O)                             | 0/0                        |
| 193          | ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State            | 02/2008          | 295.00                  | 295.00           | 624.25            | 08/2010               | 12/2011     | 16(O)                             | 0/0                        |
| 194          | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana                               | 04/2007          | 486.00                  | 486.00           | 525.47            | 05/2010               | 12/2011     | 19(O)                             | 0/0                        |
| 195          | Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State                 | 02/2009          | 1,693.75                | 1,693.75         | 2,492.60          | 08/2011               | 12/2011     | 4(O)                              | 0/0                        |
| 196          | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                       | 03/2005          | 516.00                  | 516.00           | 594.18            | 07/2010               | 01/2012     | 18(O)                             | 0/0                        |
| 197          | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam                | 12/2003          | 157.47                  | 154.57           | 177.48            | 09/2007               | 03/2012     | 54(O)                             | 0/0                        |
| 198          | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar     | 12/2003          | 240.00                  | 240.00           | 263.77            | 10/2008               | 03/2012     | 41(O)                             | 0/0                        |
| 199          | SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh | 12/2003          | 203.43                  | 203.43           | 207.85            | 10/2008               | 03/2012     | 41(O)                             | 0/0                        |
| 200          | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam                                       | 12/2003          | 175.96                  | 175.96           | 117.25            | 04/2008               | 03/2012     | 47(O)                             | 0/0                        |
| 201          | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam                                      | 12/2003          | 198.16                  | 198.16           | 176.97            | 04/2008               | 03/2012     | 47(O)                             | 0/0                        |
| 202          | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam                                      | 12/2003          | 217.61                  | 217.61           | 147.12            | 04/2010               | 03/2012     | 23(O)                             | 0/0                        |
| 203          | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                                | 12/2003          | 275.00                  | 281.31           | 178.85            | 02/2010               | 03/2012     | 25(O)                             | 0/0                        |
| 204          | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala                  | 03/2005          | 557.00                  | 557.00           | 930.92            | 02/2010               | 05/2012     | 27(O)                             | 0/0                        |
| 205          | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar     | 12/2003          | 300.00                  | 300.00           | 165.54            | 10/2008               | 06/2012     | 44(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No Project |                                                                                               | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|-----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                               |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                             | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 206          | GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh                                      | 12/2003          | 300.93                  | 300.93           | 294.11            | 10/2009               | 06/2012     | 32(O)                             | 0/0                        |
| 207          | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State                                           | 12/2003          | 604.00                  | 604.00           | 412.17            | 12/2009               | 06/2012     | 30(O)                             | 0/0                        |
| 208          | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State              | 12/2003          | 232.45                  | 232.45           | 159.55            | 09/2010               | 06/2012     | 21(O)                             | 0/0                        |
| 209          | Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State                            | 04/2009          | 1,673.70                | 1,673.70         | 1,526.60          | 10/2011               | 06/2012     | 8(O)                              | 0/0                        |
| 210          | PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab                               | 12/2003          | 284.00                  | 359.00           | 119.35            | 05/2008               | 08/2012     | 51(O)                             | 0/0                        |
| 211          | Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh          | 05/2009          | 572.30                  | 572.30           | 506.79            | 10/2011               | 08/2012     | 10(O)                             | 0/0                        |
| 212          | LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh | 12/2003          | 407.60                  | 407.60           | 184.35            | 06/2010               | 10/2012     | 28(O)                             | 0/0                        |
| 213          | LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh             | 12/2003          | 263.17                  | 263.17           | 233.29            | 09/2009               | 10/2012     | 37(O)                             | 0/0                        |
| 214          | Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra               | 04/2010          | 1,170.52                | 1,170.52         | 4.41              | 06/2011               | 10/2012     | 16(O)                             | 0/0                        |
| 215          | Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat                 | 03/2010          | 1,509.10                | 1,509.10         | 813.90            | 09/2012               | 10/2012     | 1(O)                              | 0/0                        |
| 216          | SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal                                     | 12/2003          | 225.00                  | 225.00           | 175.62            | 07/2008               | 12/2012     | 53(O)                             | 0/0                        |
| 217          | GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa                                         | 04/2000          | 263.27                  | 263.27           | 250.29            | 02/2004               | 12/2012     | 106(O)                            | 0/0                        |
| 218          | Bijapur-Hungund Section - [N24000137]NHAI,Karnataka                                           | 09/2010          | 748.00                  | 748.00           | 958.73            | 09/2010               | 03/2013     | 30(O)                             | 0/0                        |
| 219          | AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh                  | 12/2003          | 348.16                  | 348.16           | 117.69            | 09/2007               | 06/2013     | 69(O)                             | 0/0                        |
| 220          | AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab                                                   | 05/2010          | 705.00                  | 705.00           | 834.69            | 11/2012               | 06/2013     | 7(O)                              | 0/0                        |
| 221          | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam                   | 12/2003          | 199.81                  | 385.13           | 30.37             | 04/2009               | 07/2013     | 51(O)                             | 0/0                        |
| 222          | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam                  | 12/2003          | 155.04                  | 280.13           | 39.26             | 11/2008               | 07/2013     | 56(O)                             | 0/0                        |
| 223          | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala                       | 02/2010          | 617.00                  | 617.00           | 154.52            | 08/2012               | 10/2013     | 14(O)                             | 0/0                        |
| 224          | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam             | 12/2003          | 167.64                  | 167.64           | 40.71             | 11/2008               | 12/2013     | 61(O)                             | 0/0                        |
| 225          | HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam                          | 12/2003          | 212.00                  | 212.00           | 40.29             | 09/2007               | 12/2013     | 75(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                              |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                            | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 226  | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam                                         | 12/2003          | 196.00                  | 196.00           | 27.94             | 07/2009               | 12/2013     | 53(O)                             | 0/0                        |
|      | <b>Total</b>                                                                                 |                  | 32,618.03               | 33,261.44        | 33,637.40         | -                     |             |                                   | 0/0                        |
|      | <b>Shipping &amp; Ports</b>                                                                  |                  |                         |                  |                   |                       |             |                                   |                            |
| 227  | MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK, Tamil Nadu                                 | 10/2004          | 196.25                  | 196.25           | -                 | 06/2006<br>09/2011    | 09/2011     | 0(R2)                             | 0/0                        |
| 228  | ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat       | 01/2002          | 165.00<br>165.00        | 165.00           | 121.41            | 12/2005<br>01/2008    | 10/2011     | 45(R3)                            | 0/0                        |
| 229  | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra          | 10/2007          | 359.44                  | 359.44           | 351.81            | 04/2011<br>06/2011    | 11/2011     | 5(R3)                             | 0/0                        |
| 230  | Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra                          | 04/2009          | 290.85<br>305.00        | 305.00           | 86.46             | 06/2011<br>01/2012    | 01/2012     | 0(R3)                             | 0/0                        |
| 231  | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala           | 03/2009          | 3,500.00                | 3,500.00         | -                 | 01/2012               | 03/2012     | 2(O)                              | 0/0                        |
| 232  | Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST, Maharashtra                     | 04/2009          | 277.03<br>280.00        | 277.03           | 55.40             | 12/2011<br>05/2012    | 05/2012     | 0(R3)                             | 0/0                        |
| 233  | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra | 11/2007          | 1,228.00                | 1,460.00         | 568.86            | 12/2010               | 09/2012     | 21(O)                             | 0/0                        |
| 234  | Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh     | 02/2010          | 444.10                  | 444.10           | -                 | 06/2010               | 11/2012     | 29(O)                             | 0/0                        |
| 235  | C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST, Gujarat           | 04/2005          | 882.00                  | 1,060.00         | 0.16              | 02/2011               | 03/2013     | 25(O)                             | 0/0                        |
| 236  | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat               | 12/2005          | 702.00                  | 755.50           | -                 | 03/2011               | 03/2013     | 24(O)                             | 0/0                        |
| 237  | SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST, Kerala            | 03/2008          | 375.00<br>272.50        | 272.50           | -                 | 01/2009               | 05/2013     | 52(O)                             | 0/0                        |
| 238  | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP., Tamil Nadu          | 10/2002          | 150.00<br>600.00        | 600.00           | 67.00             | 03/2006               | 12/2013     | 93(O)                             | 0/0                        |
|      | <b>Total</b>                                                                                 |                  | 8,569.67                | 9,394.82         | 1,251.10          |                       |             |                                   | 0/0                        |
|      | <b>Telecommunications</b>                                                                    |                  |                         |                  |                   |                       |             |                                   |                            |
| 239  | CONVERGENT BILLING AND CRM-MTNL (DELHI) - [N26000011]MTNL, Delhi                             | 12/2005          | 249.00<br>229.41        | 229.41           | 66.20             | 02/2007               | 08/2011     | 54(O)                             | 0/0                        |
| 240  | CONVERGENT BILLING AND CRM (MUMBAI) - [N26000016]MTNL, Maharashtra                           | 01/2006          | 247.00                  | 247.00           | 75.89             | 02/2007               | 08/2011     | 54(O)                             | 0/0                        |

## List of Delay Project

Aug,2011)

| S.No Project |                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|----------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 241          | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State | 10/2009          | 384.00                  | 384.00           | 20.90             | 10/2010               | 03/2012     | 17(O)                             | 0/0                        |
|              | Total                                                                      |                  | 880.00                  | 860.41           | 162.99            |                       |             |                                   | 0/0                        |
|              |                                                                            |                  | -                       |                  |                   |                       |             |                                   |                            |
|              | <u>Urban Development</u>                                                   |                  |                         |                  |                   |                       |             |                                   |                            |
| 242          | BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka                  | 05/2006          | 6,395.00                | 11,609.00        | 2,267.57          | 12/2011               | 03/2013     | 15(O)                             | 6/6                        |
|              | Total                                                                      |                  | 6,395.00                | 11,609.00        | 2,267.57          |                       |             |                                   | 6/6                        |
|              |                                                                            |                  | -                       |                  |                   |                       |             |                                   |                            |
|              | <u>Water Resources</u>                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 243          | PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam                             | 01/2001          | 542.90                  | 1,187.00         | 35.49             | 12/2007               | 12/2012     | 60(O)                             | 0/0                        |
|              | Total                                                                      |                  | 542.90                  | 1,187.00         | 35.49             |                       |             |                                   | 0/0                        |
|              |                                                                            |                  | -                       |                  |                   |                       |             |                                   |                            |
| Grand Total  |                                                                            |                  | 313,783.31              | 379,159.99       | 200,831.11        |                       |             |                                   | 637/1492                   |

## List of Projects Without Milestones

Aug,2011)

| S.No                  | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|-----------------------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                       |                                                                                    |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                     | 2                                                                                  | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <u>Civil Aviation</u> |                                                                                    |                  |                         |                  |                   |                       |             |                                   |                            |
| 1                     | D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu      | 08/2008          | 1,273.00<br>2,015.00    | 2,015.00         | 928.46            | 01/2011<br>-          | 12/2011     | 11(O)                             | 0/0                        |
| 2                     | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal     | 08/2008          | 1,942.51<br>-           | 2,325.00         | 1,333.00          | 05/2011<br>-          | 03/2012     | 10(O)                             | 0/0                        |
| 3                     | Construction of New International Terminal Building - [N04000069]AAI,Goa           | 05/2010          | 204.73<br>-             | 204.73           | 39.57             | 05/2012<br>-          | 05/2012     | 0(O)                              | 0/0                        |
| 4                     | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim                 | 01/2009          | 309.40<br>-             | 264.29           | 147.16            | 01/2011<br>-          | 12/2012     | 23(O)                             | 0/0                        |
| 5                     | GAGAN PROJECT - [N04000065]AAI,Multi State                                         | 09/2008          | 393.60<br>-             | 393.60           | 323.65            | 06/2013<br>-          | 06/2013     | 0(O)                              | 0/0                        |
|                       | <b>Total</b>                                                                       |                  | 4,123.24<br>-           | 5,202.62         | 2,771.84          |                       |             |                                   | 0/0                        |
| <u>Coal</u>           |                                                                                    |                  |                         |                  |                   |                       |             |                                   |                            |
| 6                     | KARMA OCP - [N06000088]JCL,Jharkhandd                                              | 06/2009          | 162.46<br>-             | 162.46           | 26.19             | 03/2014<br>-          | 03/2014     | 0(O)                              | 0/0                        |
| 7                     | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh  | 06/2011          | 1,131.28<br>1,131.28    | 1,131.28         | -                 | 03/2018<br>-          | 03/2018     | 0(O)                              | 0/0                        |
|                       | <b>Total</b>                                                                       |                  | 1,293.74<br>-           | 1,293.74         | 26.19             |                       |             |                                   | 0/0                        |
| <u>Fertilisers</u>    |                                                                                    |                  |                         |                  |                   |                       |             |                                   |                            |
| 8                     | CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh          | 09/2008          | 325.00<br>-             | 325.00           | 84.31             | 07/2011<br>-          | 11/2011     | 4(O)                              | 0/0                        |
| 9                     | CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh | 09/2008          | 438.00<br>-             | 438.00           | 105.79            | 07/2011<br>-          | 03/2012     | 8(O)                              | 0/0                        |
|                       | <b>Total</b>                                                                       |                  | 763.00<br>-             | 763.00           | 190.10            |                       |             |                                   | 0/0                        |
| <u>Steel</u>          |                                                                                    |                  |                         |                  |                   |                       |             |                                   |                            |
| 10                    | 1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka                        | 04/2011          | 572.00<br>-             | 572.00           | -                 | 04/2013<br>-          | 04/2013     | 0(O)                              | 0/0                        |
| 11                    | 7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka                     | 02/2011          | 898.55<br>-             | 898.55           | -                 | 05/2013<br>-          | 05/2013     | 0(O)                              | 0/0                        |
|                       | <b>Total</b>                                                                       |                  | 1,470.55<br>-           | 1,470.55         | .00               |                       |             |                                   | 0/0                        |
| <u>Petroleum</u>      |                                                                                    |                  |                         |                  |                   |                       |             |                                   |                            |
| 12                    | North Tapti Gas Field Development - [N16000096]ONGC,Multi State                    | 07/2008          | 589.70<br>755.76        | 755.76           | 520.63            | 03/2011<br>05/2011    | 06/2011     | 1(R3)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 13   | Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar      | 06/2009          | 613.54<br>-             | 727.88           | 671.52            | 12/2010<br>-          | 06/2011     | 6(O)                              | 0/0                        |
| 14   | DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam                | 06/2006          | 1,431.91<br>1,646.39    | 1,690.13         | -                 | 09/2009<br>-          | 08/2011     | 23(O)                             | 0/0                        |
| 15   | CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu          | 01/2008          | 224.00<br>299.00        | 299.00           | 240.00            | 02/2011<br>08/2011    | 08/2011     | 0(R3)                             | 0/0                        |
| 16   | MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam           | 04/2008          | 293.60<br>-             | 261.75           | 230.97            | 12/2009<br>-          | 09/2011     | 21(O)                             | 0/0                        |
| 17   | DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State             | 11/2007          | 4,429.38<br>-           | 2,340.00         | 2,200.48          | 10/2010<br>09/2011    | 09/2011     | 0(R2)                             | 0/0                        |
| 18   | DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra         | 03/2009          | 3,284.00<br>-           | 3,284.00         | -                 | 09/2011<br>-          | 09/2011     | 0(O)                              | 0/0                        |
| 19   | REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra                       | 06/2008          | 304.40<br>-             | 304.40           | 245.01            | 06/2010<br>07/2011    | 09/2011     | 2(R3)                             | 0/0                        |
| 20   | HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra           | 09/2006          | 2,305.30<br>700.00      | 3,005.30         | 2,416.96          | 06/2010<br>06/2010    | 10/2011     | 16(R3)                            | 0/0                        |
| 21   | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                         | 08/2006          | 3,195.16<br>-           | 2,800.00         | 2,520.91          | 12/2008<br>12/2008    | 11/2011     | 35(R3)                            | 0/0                        |
| 22   | BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat              | 02/2009          | 250.00<br>349.00        | 250.00           | 197.53            | 03/2013<br>03/2013    | 12/2011     | -15(R1)                           | 0/0                        |
| 23   | HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra                                   | 05/2008          | 706.70<br>-             | 706.70           | 626.78            | 04/2010<br>-          | 12/2011     | 20(O)                             | 0/0                        |
| 24   | NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra                                  | 05/2008          | 305.08<br>-             | 305.08           | 250.40            | 04/2011<br>-          | 12/2011     | 8(O)                              | 0/0                        |
| 25   | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State        | 06/2007          | 736.65<br>-             | 736.65           | 210.39            | 09/2011<br>-          | 12/2011     | 3(O)                              | 0/0                        |
| 26   | CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat         | 02/2009          | 267.00<br>-             | 267.00           | 171.46            | 09/2012<br>-          | 12/2011     | -9(O)                             | 0/0                        |
| 27   | MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka                      | 08/2008          | 12,412.00<br>12,160.26  | 12,160.26        | 6,378.01          | 01/2012<br>-          | 01/2012     | 0(O)                              | 0/0                        |
| 28   | MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra                                  | 05/2008          | 175.21<br>-             | 162.12           | 58.26             | 03/2009<br>02/2012    | 02/2012     | 0(R3)                             | 0/0                        |
| 29   | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra | 01/2007          | 740.02<br>-             | 740.02           | 412.78            | 03/2010<br>03/2012    | 03/2012     | 0(R1)                             | 0/0                        |
| 30   | SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State    | 05/2011          | 616.00<br>-             | 616.00           | -                 | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 31   | INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State                 | 04/2003          | 429.82<br>2,218.01      | 2,218.01         | 1,237.61          | 04/2006<br>05/2011    | 05/2012     | 12(R3)                            | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 32   | CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra            | 01/2007          | 2,853.29<br>6,326.40    | 6,326.40         | 3,535.29          | 05/2010<br>05/2012    | 05/2012     | 0(R3)                             | 0/0                        |
| 33   | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                 | 01/2007          | 2,323.40<br>2,920.82    | 2,920.82         | 1,173.84          | 09/2010<br>03/2012    | 05/2012     | 2(R3)                             | 0/0                        |
| 34   | REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra              | 05/2008          | 333.40<br>837.54        | 656.51           | 20.10             | 05/2010<br>04/2012    | 05/2012     | 1(R3)                             | 0/0                        |
| 35   | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                  | 06/2007          | 1,436.21<br>1,456.96    | 1,436.21         | 82.57             | 07/2010<br>05/2012    | 05/2012     | 0(R3)                             | 0/0                        |
| 36   | DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra                | 06/2007          | 3,248.78<br>5,633.44    | 5,633.44         | 1,366.95          | 08/2010<br>03/2012    | 06/2012     | 3(R3)                             | 0/0                        |
| 37   | ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State                       | 01/2010          | 2,163.64<br>-           | 2,163.64         | 485.72            | 06/2012<br>-          | 06/2012     | 0(O)                              | 0/0                        |
| 38   | Polypropylene unit - [N16000113]Mangalore Refin,Karnataka                        | 05/2009          | 1,803.78<br>-           | 1,803.78         | 400.94            | 07/2012<br>-          | 06/2012     | -1(O)                             | 0/0                        |
| 39   | Wind Power Project - [N16000119]ONGC,Rajasthan                                   | 07/2010          | 1,106.00<br>-           | 1,106.00         | -                 | 06/2012<br>-          | 06/2012     | 0(O)                              | 0/0                        |
| 40   | ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat           | 02/2008          | 370.11<br>-             | 370.11           | 67.89             | 04/2011<br>-          | 07/2012     | 15(O)                             | 0/0                        |
| 41   | Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura  | 07/2008          | 288.04<br>288.04        | 288.04           | 105.00            | 08/2012<br>-          | 08/2012     | 0(O)                              | 0/0                        |
| 42   | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra             | 01/2009          | 7,133.39<br>-           | 6,855.93         | 2,263.80          | 09/2012<br>-          | 09/2012     | 0(O)                              | 0/0                        |
| 43   | Construction of 6 ETPs - [N16000117]ONGC,Gujarat                                 | 03/2009          | 302.26<br>-             | 302.26           | 15.78             | 09/2012<br>-          | 09/2012     | 0(O)                              | 0/0                        |
| 44   | ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra            | 10/2008          | 1,797.35<br>-           | 1,797.35         | 72.19             | 12/2011<br>-          | 01/2013     | 13(O)                             | 0/0                        |
| 45   | Development of SB-14 field - [N16000116]ONGC,Multi State                         | 01/2011          | 410.44<br>-             | 410.44           | -                 | 11/2012<br>-          | 01/2013     | 2(O)                              | 0/0                        |
| 46   | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra               | 10/2007          | 5,713.03<br>8,813.41    | 8,813.41         | 6,767.50          | 05/2010<br>03/2013    | 03/2013     | 0(R3)                             | 0/0                        |
| 47   | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam                        | 03/2009          | 2,465.15<br>-           | 2,378.86         | 359.46            | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 48   | Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State    | 01/2010          | 723.64<br>-             | 723.64           | -                 | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 49   | Development of Cluster-7 Fields - [N16000104]ONGC,Multi State                    | 03/2010          | 3,241.03<br>-           | 3,241.03         | -                 | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 50   | Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State                 | 08/2010          | 372.11<br>-             | 372.11           | -                 | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 51   | DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra | 12/2009          | 1,584.00<br>-           | 1,584.00         | -                 | -<br>-                | 08/2013     | -                                 | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No                | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|---------------------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                     |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                   | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 52                  | Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State     | 11/2010          | 331.20<br>-             | 331.20           | -                 | 08/2013<br>-          | 08/2013     | 0(O)                              | 0/0                        |
| 53                  | Wax Project - [N16000101]NRL,Assam                                                  | 06/2010          | 576.60<br>-             | 576.60           | 13.77             | 12/2013<br>12/2013    | 12/2013     | 0(R3)                             | 0/0                        |
| 54                  | Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State                   | 06/2010          | 2,523.00<br>-           | 2,523.00         | -                 | 01/2014<br>-          | 01/2014     | 0(O)                              | 0/0                        |
| 55                  | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam            | 06/2010          | 202.94<br>-             | 202.94           | -                 | 01/2014<br>-          | 01/2014     | 0(O)                              | 0/0                        |
| 56                  | PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State         | 08/2010          | 8,140.00<br>-           | 8,140.00         | 183.00            | 02/2014<br>-          | 02/2014     | 0(O)                              | 0/0                        |
| 57                  | Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat                                   | 11/2010          | 1,916.10<br>-           | 1,916.10         | -                 | 12/2014<br>-          | 12/2014     | 0(O)                              | 0/0                        |
| 58                  | Ankleswar Redevelopment - [N16000122]ONGC,Gujarat                                   | 11/2010          | 2,189.63<br>-           | 2,189.63         | -                 | 12/2014<br>-          | 12/2014     | 0(O)                              | 0/0                        |
| 59                  | Mehesana Redevelopment - [N16000121]ONGC,Gujarat                                    | 11/2010          | 3,823.00<br>-           | 3,823.00         | -                 | 04/2015<br>-          | 04/2015     | 0(O)                              | 0/0                        |
| 60                  | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana                          | 11/2007          | 281.07<br>-             | 281.07           | 3.29              | 10/2010<br>-          | -           | -                                 | 0/0                        |
| 61                  | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra     | 03/2011          | 861.79<br>-             | 861.79           | -                 | 05/2013<br>-          | -           | -                                 | 0/0                        |
| 62                  | RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh | 01/2009          | 756.00<br>-             | 756.00           | 711.47            | 09/2011<br>-          | 12/2011     | 3(O)                              | 0/0                        |
| 63                  | DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh     | 03/2009          | 3,597.00<br>2,730.00    | 2,730.00         | 696.82            | 09/2011<br>03/2012    | -           | -                                 | 0/0                        |
| 64                  | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State            | 07/2009          | 7,596.18<br>6,652.22    | 6,652.22         | 1.63              | 01/2013<br>-          | -           | -                                 | 0/0                        |
| <b>Total</b>        |                                                                                     |                  | 105,773.03<br>-         | 113,797.59       | 36,916.71         |                       |             |                                   | 0/0                        |
| <b><u>Power</u></b> |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 65                  | TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State      | 12/2008          | 204.07<br>-             | 204.07           | 112.43            | 06/2011<br>-          | 08/2011     | 2(O)                              | 0/0                        |
| 66                  | TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K                  | 10/2006          | 238.25<br>-             | 227.03           | 211.35            | 05/2011<br>05/2011    | 09/2011     | 4(R3)                             | 0/0                        |
| 67                  | EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State               | 12/2007          | 227.52<br>-             | 227.52           | 132.86            | 06/2010<br>-          | 09/2011     | 15(O)                             | 0/0                        |
| 68                  | CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.                             | 08/2005          | 1,405.63<br>-           | 1,405.63         | 1,651.81          | 08/2010<br>-          | 11/2011     | 15(O)                             | 0/0                        |
| 69                  | URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K                                  | 08/2005          | 1,724.79<br>-           | 1,724.79         | 1,522.71          | 11/2009<br>-          | 12/2011     | 25(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                           |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                         | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 70   | TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State                 | 04/2008          | 297.37<br>-             | 297.37           | 295.61            | 07/2011<br>-          | 12/2011     | 5(O)                              | 0/0                        |
| 71   | WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State                      | 02/2009          | 664.96<br>-             | 664.96           | 304.39            | 02/2012<br>-          | 02/2012     | 0(O)                              | 0/0                        |
| 72   | WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State              | 02/2009          | 409.50<br>-             | 409.50           | 58.53             | 02/2012<br>-          | 02/2012     | 0(O)                              | 0/0                        |
| 73   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan             | 02/2009          | 210.79<br>-             | 210.79           | 144.56            | 08/2011<br>-          | 02/2012     | 6(O)                              | 0/0                        |
| 74   | TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State                | 02/2009          | 353.57<br>-             | 353.57           | 206.98            | 07/2010<br>02/2012    | 02/2012     | 0(R3)                             | 0/0                        |
| 75   | SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State                | 03/2009          | 196.10<br>-             | 196.10           | 72.09             | 07/2011<br>-          | 02/2012     | 7(O)                              | 0/0                        |
| 76   | PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.                           | 10/2005          | 2,304.52<br>-           | 2,304.52         | 1,534.06          | 10/2010<br>-          | 03/2012     | 17(O)                             | 0/0                        |
| 77   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State           | 02/2009          | 317.69<br>-             | 317.69           | 54.29             | 11/2011<br>-          | 03/2012     | 4(O)                              | 0/0                        |
| 78   | System Strengthening -X of SR - [N18000086]PGCIL,Multi State                              | 12/2009          | 276.61<br>-             | 276.61           | 74.44             | 04/2012<br>-          | 04/2012     | 0(O)                              | 0/0                        |
| 79   | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State         | 11/2009          | 1,075.12<br>-           | 1,075.12         | 259.61            | 05/2012<br>-          | 05/2012     | 0(O)                              | 0/0                        |
| 80   | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State         | 07/2009          | 1,736.36<br>-           | 1,736.36         | 339.20            | 06/2012<br>-          | 06/2012     | 0(O)                              | 0/0                        |
| 81   | IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar                    | 02/2010          | 215.86<br>-             | 215.86           | 116.80            | 06/2012<br>-          | 06/2012     | 0(O)                              | 0/0                        |
| 82   | System Strengthening -XII of SR - [N18000085]PGCIL,Multi State                            | 02/2010          | 232.34<br>-             | 232.34           | 10.68             | 06/2012<br>-          | 06/2012     | 0(O)                              | 0/0                        |
| 83   | SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State         | 08/2008          | 2,360.95<br>-           | 2,360.95         | 1,663.54          | 08/2012<br>-          | 08/2012     | 0(O)                              | 0/0                        |
| 84   | 765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State         | 08/2008          | 7,075.33<br>-           | 7,075.33         | 3,908.90          | 08/2012<br>-          | 08/2012     | 0(O)                              | 0/0                        |
| 85   | System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State       | 12/2009          | 1,216.83<br>-           | 1,216.83         | 353.12            | 08/2012<br>-          | 08/2012     | 0(O)                              | 0/0                        |
| 86   | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State | 10/2008          | 4,824.12<br>-           | 4,824.12         | 1,950.27          | 10/2012<br>-          | 10/2012     | 0(O)                              | 0/0                        |
| 87   | MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra                                  | 02/2010          | 469.38<br>-             | 469.38           | 166.77            | 10/2012<br>-          | 10/2012     | 0(O)                              | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 88   | INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State | 10/2010          | 160.32<br>-             | 160.32           | 11.32             | 10/2012<br>-          | 10/2012     | 0(O)                              | 0/0                        |
| 89   | NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K                              | 08/2006          | 611.02<br>-             | 611.02           | 657.77            | 08/2010<br>-          | 11/2012     | 27(O)                             | 0/0                        |
| 90   | TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State      | 03/2010          | 4,672.99<br>-           | 4,672.99         | 312.54            | 11/2012<br>-          | 11/2012     | 0(O)                              | 0/0                        |
| 91   | NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State       | 03/2010          | 965.58<br>-             | 965.58           | 245.19            | 11/2012<br>-          | 11/2012     | 0(O)                              | 0/0                        |
| 92   | EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State                  | 07/2010          | 1,272.80<br>-           | 1,272.80         | 86.61             | 11/2012<br>-          | 11/2012     | 0(O)                              | 0/0                        |
| 93   | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal                      | 09/2005          | 1,061.38<br>-           | 1,061.38         | 1,007.32          | 09/2009<br>-          | 12/2012     | 39(O)                             | 0/0                        |
| 94   | TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State      | 12/2008          | 7,031.88<br>-           | 7,031.88         | 2,538.06          | 12/2012<br>-          | 12/2012     | 0(O)                              | 0/0                        |
| 95   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State       | 02/2009          | 509.66<br>-             | 509.66           | 245.77            | 11/2011<br>-          | 12/2012     | 13(O)                             | 0/0                        |
| 96   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State         | 02/2009          | 410.29<br>-             | 410.29           | 128.49            | 02/2012<br>-          | 12/2012     | 10(O)                             | 0/0                        |
| 97   | Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State      | 02/2010          | 2,144.00<br>-           | 2,144.00         | 306.84            | 12/2012<br>-          | 12/2012     | 0(O)                              | 0/0                        |
| 98   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State          | 10/2010          | 182.68<br>-             | 182.68           | 25.54             | 01/2013<br>-          | 01/2013     | 0(O)                              | 0/0                        |
| 99   | Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State     | 05/2010          | 250.03<br>-             | 250.03           | 18.25             | 01/2013<br>-          | 01/2013     | 0(O)                              | 0/0                        |
| 100  | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra                   | 12/2007          | 477.69<br>-             | 477.69           | 340.11            | 09/2010<br>-          | 03/2013     | 30(O)                             | 0/0                        |
| 101  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State          | 02/2009          | 520.48<br>-             | 520.48           | 259.63            | 11/2011<br>-          | 03/2013     | 16(O)                             | 0/0                        |
| 102  | 765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State      | 02/2009          | 1,347.32<br>-           | 1,347.32         | 842.45            | 02/2012<br>-          | 03/2013     | 13(O)                             | 0/0                        |
| 103  | TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa           | 09/2010          | 2,074.86<br>-           | 2,074.86         | 123.63            | 03/2013<br>-          | 03/2013     | 0(O)                              | 0/0                        |
| 104  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State        | 08/2010          | 1,677.57<br>-           | 1,677.57         | 76.35             | 04/2013<br>-          | 04/2013     | 0(O)                              | 0/0                        |
| 105  | SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State      | 08/2010          | 170.36<br>-             | 170.36           | 8.71              | 04/2013<br>-          | 04/2013     | 0(O)                              | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No                   | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                        |                                                                                           |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                      | 2                                                                                         | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 106                    | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura                              | 07/2009          | 421.01<br>623.44        | 623.44           | 68.22             | 01/2012<br>-          | 07/2013     | 18(O)                             | 0/0                        |
| 107                    | NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, Multi State           | 07/2010          | 752.64<br>-             | 752.64           | 44.90             | 07/2013<br>-          | 07/2013     | 0(O)                              | 0/0                        |
| 108                    | TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV - [N18000102]PGCIL, Maharashtra         | 07/2011          | 181.93<br>-             | 181.93           | -                 | 07/2013<br>-          | 07/2013     | 0(O)                              | 0/0                        |
| 109                    | TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL, Andhra Pradesh      | 12/2010          | 779.21<br>-             | 779.21           | 71.18             | 08/2013<br>-          | 08/2013     | 0(O)                              | 0/0                        |
| 110                    | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL, Multi State          | 12/2010          | 209.78<br>-             | 209.78           | 15.15             | 08/2013<br>-          | 08/2013     | 0(O)                              | 0/0                        |
| 111                    | Establishment of pooling stations at Rajgarh - [N18000092]PGCIL, Chhatisgarh              | 12/2010          | 1,719.52<br>-           | 1,719.52         | 125.67            | 08/2013<br>-          | 08/2013     | 0(O)                              | 0/0                        |
| 112                    | TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State            | 02/2009          | 184.19<br>-             | 184.19           | 127.76            | 11/2011<br>-          | 09/2013     | 22(O)                             | 0/0                        |
| 113                    | Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State | 03/2011          | 1,585.12<br>-           | 1,585.12         | 57.33             | 11/2013<br>-          | 11/2013     | 0(O)                              | 0/0                        |
| 114                    | TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa             | 12/2010          | 2,743.19<br>-           | 2,743.19         | 216.21            | 12/2013<br>-          | 12/2013     | 0(O)                              | 0/0                        |
| 115                    | TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State          | 03/2011          | 2,569.25<br>-           | 2,569.25         | -                 | 03/2014<br>-          | 03/2014     | 0(O)                              | 0/0                        |
| 116                    | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State        | 02/2009          | 11,130.19<br>-          | 11,130.19        | 2,877.41          | 08/2013<br>-          | 09/2014     | 13(O)                             | 0/0                        |
| 117                    | TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal         | 04/2010          | 4,404.57<br>-           | 4,404.57         | -                 | 01/2015<br>-          | 01/2015     | 0(O)                              | 0/0                        |
| 118                    | KISHANGANGA HEP - [N18000031]NHPC, J & K                                                  | 07/2007          | 2,238.67<br>3,642.04    | 3,642.04         | 923.91            | 07/2014<br>-          | 01/2016     | 18(O)                             | 0/0                        |
|                        | <b>Total</b>                                                                              |                  | 82,497.84<br>-          | 84,092.42        | 26,907.32         |                       |             |                                   | 0/0                        |
| <b><u>Railways</u></b> |                                                                                           |                  |                         |                  |                   |                       |             |                                   |                            |
| 119                    | RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat                                    | 04/2006          | 196.97<br>-             | 196.97           | 174.05            | 03/2011<br>-          | 03/2011     | 0(O)                              | 0/0                        |
| 120                    | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala                                    | 10/1998          | 550.00<br>-             | 550.00           | 70.95             | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 121                    | CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State                                  | 02/1996          | 240.00<br>-             | 579.37           | 593.76            | -<br>-                | 07/2011     | -                                 | 0/0                        |
| 122                    | PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR, Gujarat                              | 04/2005          | 148.61<br>-             | 227.52           | 258.71            | 03/2008<br>03/2009    | 10/2010     | 19(R1)                            | 0/0                        |
| 123                    | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Orissa                                       | 04/1999          | 166.16<br>-             | 243.40           | 233.07            | -<br>02/2009          | 12/2010     | 22(R1)                            | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|-------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                               |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                             | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 124  | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa            | 04/2000          | 133.41<br>207.00        | 211.90           | 187.38            | -<br>03/2009          | 12/2010     | 21(R1)                            | 0/0                        |
| 125  | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh                    | 04/2003          | 136.62<br>-             | 221.90           | 154.91            | 12/2007<br>03/2010    | 12/2010     | 9(R1)                             | 0/0                        |
| 126  | ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh     | 04/2003          | 230.73<br>399.73        | 399.50           | 294.87            | 03/2009<br>12/2008    | 12/2010     | 24(R1)                            | 0/0                        |
| 127  | BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat                 | 09/2005          | 200.80<br>-             | 200.80           | 253.23            | -<br>-                | 12/2010     | -                                 | 0/0                        |
| 128  | BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh                            | 04/1997          | 151.52<br>-             | 273.00           | 298.28            | -<br>03/2009          | 03/2011     | 24(R1)                            | 0/0                        |
| 129  | PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State   | 04/2005          | 240.00<br>-             | 329.70           | 258.52            | 03/2009<br>12/2009    | 03/2011     | 15(R1)                            | 0/0                        |
| 130  | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa                         | 04/1994          | 355.38<br>470.21        | 700.00           | 161.90            | -<br>-                | 08/2011     | -                                 | 0/0                        |
| 131  | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa                         | 04/1993          | 100.00<br>142.90        | 208.68           | 182.17            | 03/2002<br>-          | 09/2011     | 114(O)                            | 0/0                        |
| 132  | PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal                      | 09/2007          | 252.50<br>-             | 252.50           | 162.23            | 02/2010<br>-          | 11/2011     | 21(O)                             | 0/0                        |
| 133  | GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State                             | 04/1985          | 158.77<br>432.46        | 540.96           | 558.55            | 03/1994<br>-          | 12/2011     | 213(O)                            | 0/0                        |
| 134  | NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh                  | 03/1996          | 155.74<br>164.36        | 822.57           | 486.71            | 02/2009<br>-          | 12/2011     | 34(O)                             | 0/0                        |
| 135  | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa                              | 04/1996          | 301.64<br>-             | 735.10           | -                 | -<br>09/2009          | 12/2011     | 27(R1)                            | 0/0                        |
| 136  | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa                         | 04/2005          | 726.96<br>810.78        | 810.78           | 78.54             | -<br>-                | 12/2011     | -                                 | 0/0                        |
| 137  | Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka | 04/2007          | 482.00<br>-             | 482.70           | 224.65            | 03/2013<br>-          | 12/2011     | -15(O)                            | 0/0                        |
| 138  | KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh                 | 03/1997          | 395.00<br>1,062.36      | 1,577.46         | 1,154.15          | -<br>-                | 02/2012     | -                                 | 0/0                        |
| 139  | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal       | 04/2000          | 157.96<br>762.33        | 762.33           | 409.84            | -<br>12/2009          | 02/2012     | 26(R1)                            | 0/0                        |
| 140  | Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal              | 04/2009          | 259.51<br>-             | 259.51           | 62.43             | 12/2011<br>-          | 02/2012     | 2(O)                              | 0/0                        |
| 141  | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State    | 03/1984          | 520.00<br>637.46        | 637.46           | 542.72            | 03/1995<br>-          | 03/2012     | 204(O)                            | 0/0                        |
| 142  | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh        | 12/1994          | 124.43<br>407.78        | 725.90           | 502.72            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 143  | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand                  | 04/1995          | 184.00<br>254.07        | 675.00           | 453.79            | -<br>12/2011          | 03/2012     | 3(R3)                             | 0/0                        |
| 144  | KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka           | 04/1996          | 157.00<br>262.82        | 262.82           | 203.03            | -<br>03/2012          | 03/2012     | 0(R3)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 145  | MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194] ECR, Bihar                              | 04/1997          | 100.00<br>322.29        | 411.22           | 421.85            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 146  | JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240] ECR, Bihar                   | 04/1997          | 233.00<br>335.77        | 903.56           | 552.79            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 147  | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002] ECR, Bihar           | 04/1996          | 114.01<br>283.95        | 427.89           | 336.91            | -<br>03/2011          | 03/2012     | 12(R3)                            | 0/0                        |
| 148  | HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052] WS&PU, Bihar       | 04/2003          | 98.74<br>224.51         | 337.30           | 191.22            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 149  | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053] WS&PU, Bihar           | 03/2005          | 470.09<br>1,417.97      | 1,417.97         | 914.08            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 150  | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075] RVNL, Chhatisgarh                  | 09/2006          | 324.90<br>-             | 324.90           | 187.13            | 03/2010<br>-          | 03/2012     | 24(O)                             | 0/0                        |
| 151  | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083] NEFR, Arunachal Pr. | 09/1996          | 156.00<br>-             | 254.29           | 178.89            | -<br>-                | 03/2012     | -                                 | 0/0                        |
| 152  | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094] RE, Uttar Pradesh   | 02/2008          | 171.10<br>-             | 171.10           | 136.84            | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 153  | ELECTRIFICATION OF MORADABAD-ROZA - [N22000095] RE, Uttar Pradesh                    | 12/2004          | 129.17<br>-             | 220.00           | 217.49            | 03/2011<br>-          | 03/2012     | 12(O)                             | 0/0                        |
| 154  | TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097] SER, West Bengal                     | 03/1984          | 293.97<br>-             | 723.27           | 378.13            | 06/2005<br>07/2011    | 03/2012     | 8(R3)                             | 0/0                        |
| 155  | Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106] NWR, Rajasthan      | 04/2007          | 643.36<br>-             | 803.39           | 786.86            | 03/2011<br>-          | 03/2012     | 12(O)                             | 0/0                        |
| 156  | Tinpahar - Sahibganj (ER) - [N22000115] ER, Jharkhand                                | 04/2008          | 167.73<br>-             | 167.73           | 36.04             | 03/2012<br>-          | 03/2012     | 0(O)                              | 0/0                        |
| 157  | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208] SER, West Bengal                      | 04/1974          | 31.42<br>154.30         | 499.16           | 142.91            | 03/2007<br>03/2007    | 06/2012     | 63(R1)                            | 0/0                        |
| 158  | NANGALDAM-TALWARA(NL), NR - [220100188] (NR), Multi State                            | 03/1981          | 37.68<br>450.00         | 730.00           | 325.04            | -<br>07/2012          | 07/2012     | 0(R3)                             | 0/0                        |
| 159  | CONV.OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233] RE, Maharashtra              | 07/1996          | 273.67<br>1,160.52      | 1,302.12         | 571.52            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 160  | CHANDIGARH-LUDHIANA(NEW BG LINE), NR - [220100241] (NR), Punjab                      | 07/1998          | 248.44<br>576.27        | 1,104.40         | 793.10            | 12/2012<br>-          | 12/2012     | 0(O)                              | 0/0                        |
| 161  | BANKURA - DAMODAR (GC) (SER) - [220100277] SER, West Bengal                          | 03/1998          | 111.90<br>-             | 1,211.22         | 387.79            | 03/2005<br>12/2008    | 12/2012     | 48(R1)                            | 0/0                        |
| 162  | JIND-SONEPAT (NL), NR - [220100280] (NR), Haryana                                    | 01/2004          | 190.81<br>238.56        | 401.83           | 334.70            | -<br>03/2012          | 12/2012     | 9(R3)                             | 0/0                        |
| 163  | KOSI BRIDGE (NL), ECR - [220100304] ECR, Bihar                                       | 04/2002          | 323.41<br>-             | 341.41           | 233.20            | -<br>-                | 12/2012     | -                                 | 0/0                        |
| 164  | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307] ECR, Bihar                    | 04/2002          | 921.00<br>-             | 981.00           | 528.45            | 03/2009<br>-          | 12/2012     | 45(O)                             | 0/0                        |
| 165  | PATNA GANGA BRIDGE (NL), ECR - [220100308] ECR, Bihar                                | 04/2001          | 624.47<br>-             | 1,389.98         | 957.77            | 10/2007<br>-          | 12/2012     | 62(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No Project |                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 166          | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh                    | 09/2007          | 687.20                  | 687.20           | 339.93            | 03/2010               | 12/2012     | 33(O)                             | 0/0                        |
| 167          | Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal   | 04/1999          | 207.52                  | 207.52           | 103.56            | 12/2012               | 12/2012     | 0(O)                              | 0/0                        |
| 168          | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan                            | 02/1997          | 151.84<br>410.08        | 410.08           | 149.04            | -                     | 03/2013     | -                                 | 0/0                        |
| 169          | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State      | 03/1998          | 280.00                  | 1,029.00         | 684.77            | -                     | 03/2013     | -                                 | 0/0                        |
| 170          | Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh                    | 04/2008          | 603.04                  | 603.04           | 45.14             | 03/2012               | 03/2013     | 12(O)                             | 0/0                        |
| 171          | Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat                       | 04/2008          | 394.13                  | 394.13           | 0.49              | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 172          | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu     | 04/2006          | 495.74<br>495.74        | 495.74           | 135.49            | -<br>06/2013          | 06/2013     | 0(R3)                             | 0/0                        |
| 173          | Ghutiasharif-Canning (ER) - [N22000117]ER, West Bengal                            | 04/2009          | 189.97                  | 189.97           | 58.46             | 12/2011               | 11/2013     | 23(O)                             | 0/0                        |
| 174          | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh                  | 04/2005          | 383.79                  | 585.93           | 173.04            | -                     | 12/2013     | -                                 | 0/0                        |
| 175          | Katakhal to Bhairabi - [N22000126]NEFR, Assam                                     | 04/1998          | 227.90                  | 223.01           | 83.45             | 12/2012               | 12/2013     | 12(O)                             | 0/0                        |
| 176          | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam       | 04/1996          | 1,676.31                | 4,091.33         | 2,776.44          | 03/2009               | 12/2013     | 57(O)                             | 0/0                        |
| 177          | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State | 04/2000          | 733.00                  | 1,655.80         | 808.72            | 12/2008               | 03/2014     | 63(O)                             | 0/0                        |
| 178          | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State | 01/2004          | 915.70                  | 1,717.29         | 702.69            | -                     | 03/2014     | -                                 | 0/0                        |
| 179          | AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura                             | 04/2008          | 813.34                  | 1,141.76         | 206.44            | 03/2014               | 03/2014     | 0(O)                              | 0/0                        |
| 180          | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram                             | 04/2008          | 619.34                  | 2,393.49         | 3.61              | 04/2014               | 03/2014     | -1(O)                             | 0/0                        |
| 181          | Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR, Rajasthan    | 04/2008          | 653.19                  | 653.19           | 6.72              | 03/2014               | 03/2014     | 0(O)                              | 0/0                        |
| 182          | Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR, Rajasthan    | 04/2008          | 516.23                  | 516.23           | 70.08             | 03/2014               | 03/2014     | 0(O)                              | 0/0                        |
| 183          | Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat        | 04/2008          | 1,389.62                | 1,389.62         | 171.04            | 03/2014               | 03/2014     | 0(O)                              | 0/0                        |
| 184          | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh             | 04/2006          | 325.00                  | 369.90           | 97.35             | 03/2010<br>06/2014    | 06/2014     | 0(R3)                             | 0/0                        |
| 185          | RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR, Assam       | 09/1997          | 1,000.00<br>1,500.00    | 3,230.01         | 2,215.96          | 04/2008<br>03/2014    | 12/2014     | 9(R3)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                  |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 186  | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar                    | 04/2003          | 324.66                  | 324.66           | 165.33            | -                     | 03/2015     | -                                 | 0/0                        |
| 187  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra       | 04/2008          | 5,300.00                | 5,300.00         | 278.51            | 03/2014               | 03/2015     | 12(O)                             | 0/0                        |
| 188  | Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan          | 04/2008          | 829.74                  | 829.74           | -                 | 03/2015               | 03/2015     | 0(O)                              | 0/0                        |
| 189  | New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland    | 04/2006          | 850.00                  | 850.00           | 8.44              | 03/2015               | 03/2015     | 0(O)                              | 0/0                        |
| 190  | SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim                                      | 04/2008          | 1,339.48                | 3,380.57         | 52.63             | 12/2015               | 12/2015     | 0(O)                              | 0/0                        |
| 191  | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur                    | 04/2003          | 727.56<br>727.53        | 3,056.85         | 463.33            | 03/2011<br>03/2014    | 03/2016     | 24(R3)                            | 0/0                        |
| 192  | New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal | 04/2010          | 2,069.60                | 2,069.60         | 0.21              | 03/2014               | 03/2016     | 24(O)                             | 0/0                        |
| 193  | New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal | 04/2010          | 3,951.98                | 3,951.98         | 1.42              | 03/2016               | 03/2016     | 0(O)                              | 0/0                        |
| 194  | New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal         | 04/2010          | 2,619.02                | 2,619.02         | 23.10             | 03/2016               | 03/2016     | 0(O)                              | 0/0                        |
| 195  | New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal | 04/2010          | 2,397.72                | 2,397.72         | 0.02              | 03/2016               | 06/2016     | 3(O)                              | 0/0                        |
| 196  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K                      | 03/1995          | 2,500.00<br>8,000.00    | 20,000.00        | 7,189.29          | 03/2001               | 12/2017     | 201(O)                            | 0/0                        |
| 197  | VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State                               | 04/1990          | 155.66                  | 356.87           | 148.75            | -<br>03/2010          | -           | -                                 | 0/0                        |
| 198  | RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat        | 04/1992          | 112.53<br>320.66        | 464.50           | 509.57            | 03/1996<br>06/2009    | -           | -                                 | 0/0                        |
| 199  | New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal | 04/1983          | 36.80<br>274.41         | 415.23           | 234.54            | -<br>-                | -           | -                                 | 0/0                        |
| 200  | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh | 04/1995          | 304.00                  | 968.60           | -                 | 12/2012               | -           | -                                 | 0/0                        |
| 201  | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra                     | 02/1997          | 353.08<br>462.67        | 1,010.00         | 96.07             | -<br>-                | -           | -                                 | 0/0                        |
| 202  | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka         | 02/1997          | 295.00                  | 412.91           | 468.64            | -<br>-                | -           | -                                 | 0/0                        |
| 203  | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State                         | 02/1997          | 386.30                  | 1,038.00         | 551.55            | 03/1998               | -           | -                                 | 0/0                        |
| 204  | KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu                                    | 02/1997          | 155.55                  | 945.73           | 599.07            | -<br>-                | -           | -                                 | 0/0                        |
| 205  | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka                                  | 04/1995          | 227.00                  | 997.58           | 64.29             | -<br>-                | -           | -                                 | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                              | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 206  | MUNEERABAD-<br>MAHABOONAGAR(NL),SCR -<br>[220100205]SCR,Multi State                  | 04/1997          | 218.24<br>377.32        | 497.47           | 91.37             | -<br>-                | -           | -                                 | 0/0                        |
| 207  | MACHERLA-NALGONDA(NL)(SCR) -<br>[220100220]SCR,Andhra Pradesh                        | 07/1998          | 125.00<br>-             | 363.26           | 0.27              | 07/2008<br>-          | -           | -                                 | 0/0                        |
| 208  | KODERMA-RANCHI VIA BARKAKANA<br>(NL),ECR -<br>[220100222]ECR,Jharkhandd              | 03/1999          | 491.19<br>1,099.20      | 1,099.20         | 1,058.38          | 07/2005<br>-          | -           | -                                 | 0/0                        |
| 209  | GULBARGA-BIDAR,SCR(NL) -<br>[220100254]SCR,Karnataka                                 | 02/1998          | 242.42<br>369.70        | 554.55           | 254.82            | -<br>05/2009          | -           | -                                 | 0/0                        |
| 210  | KHAGARIA-KUSHESHWAR ASTHAN<br>(NL) (ECR) - [220100257]ECR,Bihar                      | 04/1997          | 78.23<br>-              | 162.87           | 86.40             | -<br>-                | -           | -                                 | 0/0                        |
| 211  | JALANDHAR-PATHANKOT-JAMMU-<br>TAWI (LD),NR - [220100258](NR),Multi<br>State          | 03/2002          | 409.00<br>625.30        | 847.76           | 813.24            | 06/2007<br>-          | -           | -                                 | 0/0                        |
| 212  | REINGUNTA-GUNTAKAL(RE) -<br>[220100260]RVNL,Andhra Pradesh                           | 06/2000          | 168.34<br>-             | 296.20           | 303.99            | 04/2003<br>03/2010    | -           | -                                 | 0/0                        |
| 213  | TIRUCHIRAPPALI-NAGORE-<br>KARAIKKAL(SR)(GC) -<br>[220100262]SR,Tamil Nadu            | 09/1995          | 100.00<br>-             | 548.96           | 472.21            | -<br>-                | -           | -                                 | 0/0                        |
| 214  | KOTLPALLI-NARASAPUR (NL) (SCR) -<br>[220100265]SCR,Andhra Pradesh                    | 12/2001          | 330.00<br>-             | 695.00           | 9.44              | -<br>-                | -           | -                                 | 0/0                        |
| 215  | DEOGHAR - SULTANGANJ (INL), ER -<br>[220100273]ER,Multi State                        | 04/2000          | 138.00<br>519.67        | 607.09           | 323.19            | -<br>12/2012          | -           | -                                 | 0/0                        |
| 216  | BANGLORE - SATYAMANGALAM<br>(NL)(SWR) -<br>[220100274]SWR,Karnataka                  | 02/1999          | 138.00<br>-             | 901.62           | 0.29              | -<br>-                | -           | -                                 | 0/0                        |
| 217  | KODERMA-TILAIYA (NL), ECR -<br>[220100305]ECR,Jharkhandd                             | 04/2002          | 459.91<br>-             | 418.17           | 73.52             | -<br>-                | -           | -                                 | 0/0                        |
| 218  | RAMGANJMUUNDI-BHOPAL (NL),WCR -<br>[220100314]WCR,Madhya pradesh                     | 04/2001          | 727.13<br>727.13        | 1,225.00         | 210.24            | -<br>-                | -           | -                                 | 0/0                        |
| 219  | RUPSA-BANGRIPOSI (GC)(SER) -<br>[220100323]SER,Orissa                                | 02/1996          | 57.94<br>-              | 173.49           | 171.65            | 03/1998<br>08/2005    | -           | -                                 | 0/0                        |
| 220  | SUKINDA ROAD - ANGUL (NL)(ECOR)<br>- [220100325]RVNL,Orissa                          | 04/1998          | 183.23<br>-             | 638.00           | -                 | 02/2015<br>-          | -           | -                                 | 0/0                        |
| 221  | MANOHARABAD-KOTHPALL NEW<br>LINE(SCR) - [N22000032]SCR,Andhra<br>Pradesh             | 04/2006          | 378.56<br>671.82        | 791.60           | 0.76              | -<br>-                | -           | -                                 | 0/0                        |
| 222  | GOELKERA-MANOHARPUR,(LD)(SER)<br>- [N22000045]SER,Jharkhandd                         | 03/1997          | 186.92<br>-             | 261.70           | 20.18             | 02/2006<br>-          | -           | -                                 | 0/0                        |
| 223  | OBULAVARIPALLE-<br>KRISHNAPATNAM(RVNL) -<br>[N22000049]RVNL,Andhra Pradesh           | 07/2006          | 743.00<br>-             | 732.80           | 306.37            | 03/2008<br>06/2008    | -           | -                                 | 0/0                        |
| 224  | MAYLADUTHURAI-THIRUVARUR-<br>KARAIKUDI-THIRU 'PONDI'-A -<br>[N22000079]SR,Tamil Nadu | 09/2007          | 404.19<br>-             | 900.00           | 187.89            | -<br>-                | -           | -                                 | 0/0                        |
| 225  | DINDIGUL-POLLACHI-PALGHAT-<br>POLLACHI AND COIMBATORE -<br>[N22000080]SR,Tamil Nadu  | 09/2006          | 343.17<br>-             | 900.00           | 408.50            | -<br>-                | -           | -                                 | 0/0                        |
| 226  | TINDIVANAM-GINGEE-<br>TIRUVANNAMALAI (NL) -<br>[N22000084]SR,Tamil Nadu              | 09/2006          | 125.00<br>-             | 227.40           | 21.00             | -<br>-                | -           | -                                 | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                        |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                      | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 227  | TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu                                       | 09/2006          | 456.00                  | 582.83           | 83.97             | -                     | -           | -                                 | 0/0                        |
| 228  | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar             | 09/2006          | 300.00<br>300.00        | 529.88           | 35.45             | -                     | -           | -                                 | 0/0                        |
| 229  | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                                 | 04/2008          | 282.92                  | 359.86           | 0.71              | -                     | -           | -                                 | 0/0                        |
| 230  | Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat             | 04/2006          | 117.36<br>196.95        | 196.95           | 168.88            | 03/2011               | -           | -                                 | 0/0                        |
| 231  | AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra                                    | 06/1994          | 120.90<br>284.27        | 488.76           | 451.87            | 06/1999<br>03/2011    | -           | -                                 | 0/0                        |
| 232  | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra        | 03/1996          | 401.81<br>495.44        | 495.44           | 166.58            | 03/2004               | -           | -                                 | 0/0                        |
| 233  | KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka                                    | 04/1995          | 65.94<br>281.20         | 302.23           | 325.44            | -<br>03/2011          | -           | -                                 | 0/0                        |
| 234  | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand                                    | 04/1997          | 194.07                  | 456.45           | 267.31            | 06/2004<br>04/2005    | -           | -                                 | 0/0                        |
| 235  | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State                    | 09/1998          | 925.00                  | 925.00           | 504.78            | 05/2008<br>03/2011    | -           | -                                 | 0/0                        |
| 236  | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh              | 04/1999          | 108.00<br>214.09        | 227.42           | 249.52            | 12/2009<br>03/2011    | -           | -                                 | 0/0                        |
| 237  | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar                                   | 09/2001          | 100.00<br>492.98        | 1,015.84         | 720.23            | -<br>12/2010          | -           | -                                 | 0/0                        |
| 238  | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh | 03/2002          | 381.17<br>863.23        | 863.23           | 401.26            | -<br>-                | -           | -                                 | 0/0                        |
| 239  | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal        | 03/2000          | 907.69<br>1,032.76      | 3,176.10         | 3,062.38          | 12/2006<br>08/2010    | -           | -                                 | 0/0                        |
| 240  | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State                                | 04/1998          | 92.63<br>108.91         | 228.09           | 230.26            | -<br>02/2011          | -           | -                                 | 0/0                        |
| 241  | REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana                                        | 01/2004          | 149.38<br>330.23        | 475.28           | 469.93            | 02/2010<br>02/2011    | -           | -                                 | 0/0                        |
| 242  | KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand                                    | 04/1996          | 371.36                  | 452.35           | 367.76            | -                     | -           | -                                 | 0/0                        |
| 243  | SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan                            | 04/2001          | 143.92<br>258.60        | 258.60           | 234.79            | -<br>03/2011          | -           | -                                 | 0/0                        |
| 244  | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar                                  | 04/2003          | 218.19                  | 218.19           | 131.48            | -                     | -           | -                                 | 0/0                        |
| 245  | HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State                                 | 04/2005          | 230.03                  | 230.03           | 131.75            | -                     | -           | -                                 | 0/0                        |
| 246  | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State       | 12/2006          | 170.00<br>170.00        | 435.87           | 359.02            | -<br>03/2011          | -           | -                                 | 0/0                        |
| 247  | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam             | 09/2006          | 200.00                  | 384.04           | 76.53             | -                     | -           | -                                 | 0/0                        |
| 248  | BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal                                   | 04/2007          | 245.15                  | 245.15           | 160.33            | 12/2010<br>03/2011    | -           | -                                 | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No                                 | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------------------------------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                                      |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                                    | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 249                                  | Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal                            | 04/2004          | 225.68                  | 225.68           | 129.37            | -                     | -           | -                                 | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | 12/2010               |             |                                   |                            |
| 250                                  | Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat               | 04/2008          | 318.24                  | 468.62           | 2.07              | 03/2012               | -           | -                                 | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| Total                                |                                                                                          |                  | 62,362.03               | 126,469.40       | 49,806.43         |                       |             |                                   | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   |                       |             |                                   |                            |
| <u>Road Transport &amp; Highways</u> |                                                                                          |                  |                         |                  |                   |                       |             |                                   |                            |
| 251                                  | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka                     | 04/2000          | 241.00                  | 196.65           | 149.93            | 08/2004               | 09/2011     | 85(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 252                                  | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka                | 04/2000          | 318.00                  | 207.56           | 160.48            | 08/2004               | 09/2011     | 85(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 253                                  | HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal                    | 04/2000          | 273.00                  | 522.00           | 475.55            | 03/2005               | 09/2011     | 78(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 254                                  | GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat   | 12/2003          | 412.78                  | 479.54           | 436.46            | 11/2007               | 09/2011     | 46(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 255                                  | AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh   | 12/2003          | 217.00                  | 217.00           | 352.26            | 10/2008               | 09/2011     | 35(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 256                                  | MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu | 03/2005          | 629.00                  | 629.00           | 910.04            | 11/2010               | 09/2011     | 10(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 257                                  | LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh        | 12/2003          | 225.00                  | 225.00           | 254.49            | 10/2008               | 09/2011     | 35(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 258                                  | RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar                                   | 12/2003          | 340.00                  | 340.00           | 561.31            | 06/2008               | 09/2011     | 39(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 259                                  | THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala                                    | 12/2003          | 312.50                  | 312.50           | 602.56            | 03/2009               | 09/2011     | 30(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 260                                  | ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal                        | 12/2003          | 221.82                  | 221.82           | 241.98            | 11/2008               | 09/2011     | 34(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 261                                  | TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu                                    | 03/2005          | 576.00                  | 576.00           | 657.66            | 07/2010               | 09/2011     | 14(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 262                                  | PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu                               | 03/2005          | 285.00                  | 285.00           | 359.10            | 07/2010               | 09/2011     | 14(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 263                                  | NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka           | 03/2005          | 441.00                  | 441.00           | 908.83            | 07/2010               | 09/2011     | 14(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 264                                  | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa               | 04/2000          | 228.70                  | 228.70           | 165.14            | 02/2004               | 09/2011     | 91(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 265                                  | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh                      | 03/2005          | 190.00                  | 190.00           | 227.03            | 01/2009               | 10/2011     | 33(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 266                                  | DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam                                   | 12/2003          | 225.00                  | 225.00           | 254.16            | 06/2008               | 10/2011     | 40(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |
| 267                                  | NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra                                 | 03/2005          | 168.00                  | 168.00           | 385.27            | 12/2008               | 10/2011     | 34(O)                             | 0/0                        |
|                                      |                                                                                          |                  | -                       |                  |                   | -                     |             |                                   |                            |

## List of Projects Without Milestones

Aug,2011)

| S.No Project |                                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                             |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                           | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 268          | JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh                                  | 12/2003          | 276.09                  | 276.09           | 295.27            | 09/2009               | 10/2011     | 25(O)                             | 0/0                        |
| 269          | END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh            | 01/2008          | 464.00                  | 464.00           | 419.88            | 01/2011               | 10/2011     | 9(O)                              | 0/0                        |
| 270          | Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu                                        | 04/2009          | 353.37                  | 353.37           | 198.71            | 10/2011               | 10/2011     | 0(O)                              | 0/0                        |
| 271          | KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan                                 | 12/2003          | 275.00                  | 250.39           | 277.08            | 10/2008               | 11/2011     | 37(O)                             | 0/0                        |
| 272          | SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh              | 12/2003          | 151.30                  | 151.30           | 172.23            | 10/2008               | 11/2011     | 37(O)                             | 0/0                        |
| 273          | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana                      | 05/2009          | 1,108.00                | 2,288.00         | 2,610.80          | 11/2011               | 11/2011     | 0(O)                              | 0/0                        |
| 274          | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa                        | 04/2000          | 225.00                  | 241.53           | 77.54             | 04/2004               | 12/2011     | 92(O)                             | 0/0                        |
| 275          | AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh            | 04/2000          | 367.49                  | 367.49           | 453.68            | 03/2005               | 12/2011     | 81(O)                             | 0/0                        |
| 276          | GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh | 12/2003          | 275.00                  | 275.00           | 296.55            | 09/2007               | 12/2011     | 51(O)                             | 0/0                        |
| 277          | HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh              | 03/2005          | 220.00                  | 220.00           | 239.26            | 09/2007               | 12/2011     | 51(O)                             | 0/0                        |
| 278          | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh  | 12/2003          | 155.00                  | 201.66           | 88.13             | 09/2008               | 12/2011     | 39(O)                             | 0/0                        |
| 279          | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam          | 12/2003          | 230.00                  | 230.00           | 203.38            | 06/2005               | 12/2011     | 78(O)                             | 0/0                        |
| 280          | VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K            | 12/2003          | 193.09                  | 166.30           | 179.19            | 03/2008               | 12/2011     | 45(O)                             | 0/0                        |
| 281          | VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K            | 12/2003          | 166.27                  | 193.10           | 147.71            | 03/2008               | 12/2011     | 45(O)                             | 0/0                        |
| 282          | GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh  | 12/2003          | 227.00                  | 227.00           | 394.13            | 10/2008               | 12/2011     | 38(O)                             | 0/0                        |
| 283          | ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh          | 12/2003          | 340.68                  | 340.68           | 353.85            | 03/2008               | 12/2011     | 45(O)                             | 0/0                        |
| 284          | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam             | 12/2003          | 280.00                  | 280.00           | 224.96            | 02/2009               | 12/2011     | 34(O)                             | 0/0                        |
| 285          | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam                 | 12/2003          | 200.00                  | 200.00           | 78.90             | 04/2009               | 12/2011     | 32(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                                |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                              | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 286  | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam                            | 12/2003          | 195.00<br>-             | 195.00           | 172.21            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 287  | KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh                               | 12/2003          | 242.00<br>-             | 242.00           | 393.21            | 12/2008<br>-          | 12/2011     | 36(O)                             | 0/0                        |
| 288  | UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh                         | 12/2003          | 227.00<br>-             | 227.00           | 363.24            | 12/2008<br>-          | 12/2011     | 36(O)                             | 0/0                        |
| 289  | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                           | 12/2003          | 237.80<br>-             | 237.80           | 197.55            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 290  | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar                                    | 12/2003          | 332.94<br>-             | 332.94           | 289.08            | 09/2008<br>-          | 12/2011     | 39(O)                             | 0/0                        |
| 291  | LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh                               | 12/2003          | 198.00<br>-             | 198.00           | 187.06            | 11/2008<br>-          | 12/2011     | 37(O)                             | 0/0                        |
| 292  | RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh  | 12/2003          | 251.03<br>-             | 251.03           | 276.03            | 10/2008<br>-          | 12/2011     | 38(O)                             | 0/0                        |
| 293  | RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh | 12/2003          | 229.91<br>-             | 229.91           | 223.12            | 10/2008<br>-          | 12/2011     | 38(O)                             | 0/0                        |
| 294  | JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar                                          | 12/2003          | 340.00<br>-             | 340.00           | 426.99            | 09/2008<br>-          | 12/2011     | 39(O)                             | 0/0                        |
| 295  | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam                                                | 12/2003          | 200.00<br>-             | 200.00           | 255.34            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 296  | SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh                                                | 03/2005          | 322.00<br>-             | 322.00           | 553.66            | 06/2009<br>-          | 12/2011     | 30(O)                             | 0/0                        |
| 297  | NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka                                    | 04/2000          | 196.50<br>-             | 196.50           | 233.50            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 298  | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam                                             | 12/2003          | 264.72<br>-             | 264.72           | 246.10            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 299  | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam                                              | 12/2003          | 245.00<br>-             | 245.00           | 476.19            | 03/2008<br>-          | 12/2011     | 45(O)                             | 0/0                        |
| 300  | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam                                                | 12/2003          | 225.00<br>-             | 225.00           | 165.57            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 301  | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam                                                 | 12/2003          | 208.00<br>-             | 208.00           | 206.17            | 04/2008<br>-          | 12/2011     | 44(O)                             | 0/0                        |
| 302  | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam                                | 12/2003          | 160.00<br>-             | 160.00           | 121.62            | 05/2008<br>-          | 12/2011     | 43(O)                             | 0/0                        |
| 303  | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                           | 12/2003          | 200.00<br>-             | 200.00           | 188.95            | 06/2008<br>-          | 12/2011     | 42(O)                             | 0/0                        |
| 304  | THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu                                       | 03/2005          | 280.00<br>-             | 280.00           | 580.67            | 06/2009<br>-          | 12/2011     | 30(O)                             | 0/0                        |
| 305  | GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh             | 12/2003          | 600.24<br>-             | 600.24           | 692.67            | 10/2009<br>-          | 12/2011     | 26(O)                             | 0/0                        |
| 306  | KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar                     | 12/2003          | 418.04<br>-             | 418.04           | 322.97            | 03/2010<br>-          | 12/2011     | 21(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No Project |                                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                          |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                        | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 307          | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh                             | 12/2003          | 355.06                  | 355.06           | 294.66            | 09/2009               | 12/2011     | 27(O)                             | 0/0                        |
| 308          | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu                   | 03/2005          | 941.00                  | 941.00           | 1,901.00          | 01/2011               | 12/2011     | 11(O)                             | 0/0                        |
| 309          | PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab                                         | 12/2003          | 229.00                  | 284.00           | 338.97            | 05/2010               | 12/2011     | 19(O)                             | 0/0                        |
| 310          | ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State            | 02/2008          | 295.00                  | 295.00           | 624.25            | 08/2010               | 12/2011     | 16(O)                             | 0/0                        |
| 311          | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana                                | 04/2007          | 486.00                  | 486.00           | 525.47            | 05/2010               | 12/2011     | 19(O)                             | 0/0                        |
| 312          | Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State                 | 02/2009          | 1,693.75                | 1,693.75         | 2,492.60          | 08/2011               | 12/2011     | 4(O)                              | 0/0                        |
| 313          | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                        | 03/2005          | 516.00                  | 516.00           | 594.18            | 07/2010               | 01/2012     | 18(O)                             | 0/0                        |
| 314          | Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh                             | 02/2010          | 390.56                  | 390.56           | 389.36            | 02/2012               | 02/2012     | 0(O)                              | 0/0                        |
| 315          | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam                 | 12/2003          | 157.47                  | 154.57           | 177.48            | 09/2007               | 03/2012     | 54(O)                             | 0/0                        |
| 316          | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar      | 12/2003          | 240.00                  | 240.00           | 263.77            | 10/2008               | 03/2012     | 41(O)                             | 0/0                        |
| 317          | SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya pradesh | 12/2003          | 203.43                  | 203.43           | 207.85            | 10/2008               | 03/2012     | 41(O)                             | 0/0                        |
| 318          | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam                                       | 12/2003          | 175.96                  | 175.96           | 117.25            | 04/2008               | 03/2012     | 47(O)                             | 0/0                        |
| 319          | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam                                      | 12/2003          | 198.16                  | 198.16           | 176.97            | 04/2008               | 03/2012     | 47(O)                             | 0/0                        |
| 320          | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI, Assam                                      | 12/2003          | 217.61                  | 217.61           | 147.12            | 04/2010               | 03/2012     | 23(O)                             | 0/0                        |
| 321          | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                                 | 12/2003          | 275.00                  | 281.31           | 178.85            | 02/2010               | 03/2012     | 25(O)                             | 0/0                        |
| 322          | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala                   | 03/2005          | 557.00                  | 557.00           | 930.92            | 02/2010               | 05/2012     | 27(O)                             | 0/0                        |
| 323          | Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra                                        | 11/2009          | 1,110.00                | 1,110.00         | 1,204.90          | 05/2012               | 05/2012     | 0(O)                              | 0/0                        |
| 324          | Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan                                      | 11/2009          | 795.00                  | 795.00           | 804.29            | 05/2012               | 05/2012     | 0(O)                              | 0/0                        |
| 325          | Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh                            | 08/2010          | 388.00                  | 388.00           | 340.53            | 05/2012               | 05/2012     | 0(O)                              | 0/0                        |
| 326          | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar      | 12/2003          | 300.00                  | 300.00           | 165.54            | 10/2008               | 06/2012     | 44(O)                             | 0/0                        |
| 327          | GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya pradesh                                | 12/2003          | 300.93                  | 300.93           | 294.11            | 10/2009               | 06/2012     | 32(O)                             | 0/0                        |
| 328          | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State                                     | 12/2003          | 604.00                  | 604.00           | 412.17            | 12/2009               | 06/2012     | 30(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|---------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                                   |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                                 | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 329  | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State                 | 12/2003          | 232.45                  | 232.45           | 159.55            | 09/2010               | 06/2012     | 21(O)                             | 0/0                        |
| 330  | MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra                                        | 12/2009          | 835.00                  | 835.00           | 396.69            | 06/2012               | 06/2012     | 0(O)                              | 0/0                        |
| 331  | Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State                               | 04/2009          | 1,673.70                | 1,673.70         | 1,526.60          | 10/2011               | 06/2012     | 8(O)                              | 0/0                        |
| 332  | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra                      | 03/2005          | 940.00                  | 940.00           | 323.19            | 07/2012               | 07/2012     | 0(O)                              | 0/0                        |
| 333  | PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab                                  | 12/2003          | 284.00                  | 359.00           | 119.35            | 05/2008               | 08/2012     | 51(O)                             | 0/0                        |
| 334  | Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh              | 05/2009          | 572.30                  | 572.30           | 506.79            | 10/2011               | 08/2012     | 10(O)                             | 0/0                        |
| 335  | LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya pradesh | 12/2003          | 407.60                  | 407.60           | 184.35            | 06/2010               | 10/2012     | 28(O)                             | 0/0                        |
| 336  | LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh                 | 12/2003          | 263.17                  | 263.17           | 233.29            | 09/2009               | 10/2012     | 37(O)                             | 0/0                        |
| 337  | Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra                  | 04/2010          | 1,170.52                | 1,170.52         | 4.41              | 06/2011               | 10/2012     | 16(O)                             | 0/0                        |
| 338  | Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat                   | 03/2010          | 1,509.10                | 1,509.10         | 813.90            | 09/2012               | 10/2012     | 1(O)                              | 0/0                        |
| 339  | Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh                         | 04/2010          | 1,740.00                | 1,740.00         | 1,005.10          | 10/2012               | 10/2012     | 0(O)                              | 0/0                        |
| 340  | WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, Maharashtra                          | 02/2011          | 193.45                  | 193.45           | 29.04             | 11/2012               | 11/2012     | 0(O)                              | 0/0                        |
| 341  | UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka                            | 11/2010          | 680.00                  | 680.00           | -                 | 11/2012               | 11/2012     | 0(O)                              | 0/0                        |
| 342  | SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal                                        | 12/2003          | 225.00                  | 225.00           | 175.62            | 07/2008               | 12/2012     | 53(O)                             | 0/0                        |
| 343  | GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa                                          | 04/2000          | 263.27                  | 263.27           | 250.29            | 02/2004               | 12/2012     | 106(O)                            | 0/0                        |
| 344  | Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan                                                    | 06/2010          | 792.06                  | 792.06           | 389.32            | 12/2012               | 12/2012     | 0(O)                              | 0/0                        |
| 345  | Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand                                                    | 08/2010          | 625.07                  | 625.07           | 665.96            | 01/2013               | 01/2013     | 0(O)                              | 0/0                        |
| 346  | Bijapur-Hungund Section - [N24000137]NHAI, Karnataka                                              | 09/2010          | 748.00                  | 748.00           | 958.73            | 09/2010               | 03/2013     | 30(O)                             | 0/0                        |
| 347  | Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka                    | 09/2010          | 946.00                  | 946.00           | -                 | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 348  | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu              | 09/2010          | 852.00                  | 852.00           | 303.83            | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                    |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                  | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 349  | KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka                         | 09/2010          | 671.00                  | 671.00           | 173.17            | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 350  | PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra                                   | 10/2010          | 1,724.55                | 1,724.55         | 107.56            | 03/2013               | 03/2013     | 0(O)                              | 0/0                        |
| 351  | Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh                          | 10/2010          | 1,175.00                | 1,175.00         | 138.67            | 04/2013               | 04/2013     | 0(O)                              | 0/0                        |
| 352  | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh   | 11/2010          | 1,585.00                | 1,585.00         | 198.67            | 05/2013               | 05/2013     | 0(O)                              | 0/0                        |
| 353  | DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka                                      | 12/2010          | 453.00                  | 453.00           | 122.73            | 05/2013               | 05/2013     | 0(O)                              | 0/0                        |
| 354  | INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh                               | 11/2010          | 325.00                  | 325.00           | 138.67            | 05/2013               | 05/2013     | 0(O)                              | 0/0                        |
| 355  | AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh     | 12/2003          | 348.16                  | 348.16           | 117.69            | 09/2007               | 06/2013     | 69(O)                             | 0/0                        |
| 356  | AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab                                       | 05/2010          | 705.00                  | 705.00           | 834.69            | 11/2012               | 06/2013     | 7(O)                              | 0/0                        |
| 357  | MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh                                | 04/2010          | 1,267.00                | 1,267.00         | -                 | 06/2013               | 06/2013     | 0(O)                              | 0/0                        |
| 358  | BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka                                 | 12/2010          | 480.00                  | 480.00           | -                 | 06/2013               | 06/2013     | 0(O)                              | 0/0                        |
| 359  | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam       | 12/2003          | 199.81                  | 385.13           | 30.37             | 04/2009               | 07/2013     | 51(O)                             | 0/0                        |
| 360  | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam      | 12/2003          | 155.04                  | 280.13           | 39.26             | 11/2008               | 07/2013     | 56(O)                             | 0/0                        |
| 361  | DEOLI-KOTA - [N24000148]NHAI, Rajasthan                                            | 01/2011          | 953.00                  | 593.00           | 67.10             | 07/2013               | 07/2013     | 0(O)                              | 0/0                        |
| 362  | CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka                              | 03/2011          | 839.00                  | 839.00           | -                 | 08/2013               | 08/2013     | 0(O)                              | 0/0                        |
| 363  | New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu        | 09/2010          | 1,655.00                | 1,655.00         | 4.34              | 09/2013               | 09/2013     | 0(O)                              | 0/0                        |
| 364  | 4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka      | 03/2011          | 359.00                  | 359.00           | 0.99              | 09/2013               | 09/2013     | 0(O)                              | 0/0                        |
| 365  | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala           | 02/2010          | 617.00                  | 617.00           | 154.52            | 08/2012               | 10/2013     | 14(O)                             | 0/0                        |
| 366  | Talegaon-amravati - [N24000140]NHAI, Maharashtra                                   | 11/2009          | 567.00                  | 567.00           | 10.04             | 11/2013               | 11/2013     | 0(O)                              | 0/0                        |
| 367  | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam | 12/2003          | 167.64                  | 167.64           | 40.71             | 11/2008               | 12/2013     | 61(O)                             | 0/0                        |
| 368  | HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam             | 12/2003          | 212.00                  | 212.00           | 40.29             | 09/2007               | 12/2013     | 75(O)                             | 0/0                        |
| 369  | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam                               | 12/2003          | 196.00                  | 196.00           | 27.94             | 07/2009               | 12/2013     | 53(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|      |                                                                                              |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1    | 2                                                                                            | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 370  | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State                                      | 02/2011          | 2,498.76                | 2,498.76         | -                 | 08/2014               | 08/2014     | 0(O)                              | 0/0                        |
| 371  | PANIPAT-ROHTAK - [N24000151]NHAI, Haryana                                                    | 04/2011          | 807.00                  | 807.00           | 300.12            | 10/2014               | 10/2014     | 0(O)                              | 0/0                        |
|      | <b>Total</b>                                                                                 |                  | 59,725.85               | 61,189.26        | 43,561.18         |                       |             |                                   | 0/0                        |
|      | <b>Shipping &amp; Ports</b>                                                                  |                  |                         |                  |                   |                       |             |                                   |                            |
| 372  | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala       | 03/2007          | 245.67                  | 298.17           | 294.07            | 04/2009               | 02/2011     | 22(O)                             | 0/0                        |
| 373  | Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST, Karnataka        | 06/2006          | 230.00                  | 272.50           | 219.00            | 12/2010               | 06/2011     | 6(O)                              | 0/0                        |
| 374  | MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK, Tamil Nadu                                | 10/2004          | 196.25                  | 196.25           | -                 | 06/2006<br>09/2011    | 09/2011     | 0(R2)                             | 0/0                        |
| 375  | ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP., Kerala                | 12/2010          | 241.50                  | 241.50           | 48.10             | 09/2011               | 09/2011     | 0(O)                              | 0/0                        |
| 376  | ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat       | 01/2002          | 165.00<br>165.00        | 165.00           | 121.41            | 12/2005<br>01/2008    | 10/2011     | 45(R3)                            | 0/0                        |
| 377  | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra          | 10/2007          | 359.44                  | 359.44           | 351.81            | 04/2011<br>06/2011    | 11/2011     | 5(R3)                             | 0/0                        |
| 378  | Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra                          | 04/2009          | 290.85<br>305.00        | 305.00           | 86.46             | 06/2011<br>01/2012    | 01/2012     | 0(R3)                             | 0/0                        |
| 379  | ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP., Maharashtra          | 11/2007          | 1,061.96<br>1,077.60    | 1,082.06         | 360.80            | 03/2012               | 03/2012     | 0(O)                              | 0/0                        |
| 380  | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala           | 03/2009          | 3,500.00                | 3,500.00         | -                 | 01/2012               | 03/2012     | 2(O)                              | 0/0                        |
| 381  | Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat   | 06/2010          | 277.00                  | 277.00           | 0.04              | 03/2012               | 03/2012     | 0(O)                              | 0/0                        |
| 382  | Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST, Maharashtra                     | 04/2009          | 277.03<br>280.00        | 277.03           | 55.40             | 12/2011<br>05/2012    | 05/2012     | 0(R3)                             | 0/0                        |
| 383  | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra | 11/2007          | 1,228.00                | 1,460.00         | 568.86            | 12/2010               | 09/2012     | 21(O)                             | 0/0                        |
| 384  | ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP., Maharashtra          | 08/2008          | 1,066.91                | 968.35           | 222.91            | 09/2012               | 09/2012     | 0(O)                              | 0/0                        |
| 385  | Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh     | 02/2010          | 444.10                  | 444.10           | -                 | 06/2010               | 11/2012     | 29(O)                             | 0/0                        |
| 386  | Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Maharashtra   | 08/2010          | 612.72<br>627.64        | 627.64           | 83.51             | 12/2012               | 12/2012     | 0(O)                              | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No                      | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|---------------------------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                           |                                                                                            |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                         | 2                                                                                          | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 387                       | C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat          | 04/2005          | 882.00<br>-             | 1,060.00         | 0.16              | 02/2011<br>-          | 03/2013     | 25(O)                             | 0/0                        |
| 388                       | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat              | 12/2005          | 702.00<br>-             | 755.50           | -                 | 03/2011<br>-          | 03/2013     | 24(O)                             | 0/0                        |
| 389                       | SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala           | 03/2008          | 375.00<br>272.50        | 272.50           | -                 | 01/2009<br>-          | 05/2013     | 52(O)                             | 0/0                        |
| 390                       | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu          | 10/2002          | 150.00<br>600.00        | 600.00           | 67.00             | 03/2006<br>-          | 12/2013     | 93(O)                             | 0/0                        |
| 391                       | Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra  | 10/2010          | 1,028.10<br>1,012.23    | 1,028.10         | 202.04            | 12/2013<br>-          | 12/2013     | 0(O)                              | 0/0                        |
| 392                       | Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra  | 10/2010          | 966.46<br>-             | 994.82           | 189.92            | 02/2014<br>-          | 02/2014     | 0(O)                              | 0/0                        |
| 393                       | DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra     | 10/2005          | 800.00<br>-             | 800.00           | 5.92              | 10/2008<br>-          | -           | -                                 | 0/0                        |
| 394                       | DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa                        | 12/2005          | 154.84<br>-             | 253.36           | -                 | 12/2007<br>01/2009    | -           | -                                 | 0/0                        |
| 395                       | DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu                       | 09/2006          | 399.13<br>-             | 399.13           | -                 | 08/2010<br>-          | -           | -                                 | 0/0                        |
| 396                       | DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu                   | 09/2006          | 370.00<br>-             | 370.00           | -                 | 08/2010<br>-          | -           | -                                 | 0/0                        |
| 397                       | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu                      | 06/2005          | 2,427.40<br>-           | 2,427.40         | 821.39            | 10/2008<br>-          | -           | -                                 | 0/0                        |
|                           | <b>Total</b>                                                                               |                  | 18,451.36<br>-          | 19,434.85        | 3,698.80          |                       |             |                                   | 0/0                        |
| <b>Telecommunications</b> |                                                                                            |                  |                         |                  |                   |                       |             |                                   |                            |
| 398                       | GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra            | 09/2008          | 1,799.94<br>-           | 1,799.94         | 251.53            | 09/2009<br>-          | 02/2010     | 5(O)                              | 0/0                        |
| 399                       | Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State | 12/2007          | 952.88<br>-             | 952.88           | -                 | 03/2010<br>-          | 10/2010     | 7(O)                              | 0/0                        |
| 400                       | GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana                         | 01/2008          | 192.48<br>-             | 192.48           | 119.41            | 03/2009<br>-          | 02/2011     | 23(O)                             | 0/0                        |
| 401                       | GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab                | 02/2008          | 373.94<br>-             | 373.94           | 199.63            | 12/2008<br>-          | 02/2011     | 26(O)                             | 0/0                        |
| 402                       | GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa                | 11/2007          | 277.34<br>-             | 377.54           | 308.13            | 03/2009<br>-          | 02/2011     | 23(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No Project |                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------|--------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|              |                                                                                      |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1            | 2                                                                                    | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 403          | UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal          | 01/2009          | 149.15<br>158.72        | 158.72           | 76.55             | 06/2009<br>-          | 02/2011     | 20(O)                             | 0/0                        |
| 404          | Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam                     | 06/2007          | 336.81<br>-             | 336.81           | 155.71            | 01/2009<br>-          | 02/2011     | 25(O)                             | 0/0                        |
| 405          | GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar           | 10/2007          | 366.00<br>-             | 366.00           | 226.39            | 10/2008<br>-          | 02/2011     | 28(O)                             | 0/0                        |
| 406          | GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh | 01/2009          | 922.91<br>-             | 922.91           | 346.90            | 01/2010<br>-          | 02/2011     | 13(O)                             | 0/0                        |
| 407          | GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala         | 01/2009          | 848.70<br>-             | 848.70           | 675.35            | 01/2010<br>-          | 02/2011     | 13(O)                             | 0/0                        |
| 408          | GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu      | 01/2009          | 315.19<br>-             | 315.19           | 132.24            | 01/2010<br>-          | 02/2011     | 13(O)                             | 0/0                        |
| 409          | GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan       | 06/2007          | 601.49<br>-             | 601.49           | 495.72            | 12/2008<br>-          | 03/2011     | 27(O)                             | 0/0                        |
| 410          | GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh     | 05/2007          | 335.91<br>-             | 335.91           | 182.45            | 03/2009<br>-          | 03/2011     | 24(O)                             | 0/0                        |
| 411          | GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab           | 09/2008          | 241.49<br>-             | 241.49           | 112.61            | 09/2009<br>-          | 03/2011     | 18(O)                             | 0/0                        |
| 412          | GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh   | 10/2008          | 336.84<br>-             | 336.84           | 35.75             | 10/2009<br>-          | 03/2011     | 17(O)                             | 0/0                        |
| 413          | GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal    | 02/2008          | 584.33<br>-             | 584.33           | 398.08            | 02/2009<br>-          | 03/2011     | 25(O)                             | 0/0                        |
| 414          | GSM equipment of 1867000Lines (2G) 383000 lines 3(-) [N26000089]BSNL,Gujarat         | 08/2008          | 868.00<br>-             | 868.00           | 362.62            | 08/2009<br>-          | 03/2011     | 19(O)                             | 0/0                        |
| 415          | GSM equipment of 1625000Lines (2G) 325000 lines 3(-) [N26000090]BSNL,Madhya pradesh  | 11/2009          | 916.70<br>-             | 916.70           | 280.72            | 11/2010<br>-          | 03/2011     | 4(O)                              | 0/0                        |
| 416          | GSM equipment of 1700000Lines (2G) 234100 lines 3(-) [N26000092]BSNL,Karnataka       | 10/2008          | 677.75<br>719.90        | 719.90           | 461.56            | 10/2009<br>-          | 03/2011     | 17(O)                             | 0/0                        |
| 417          | CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi                       | 12/2005          | 249.00<br>229.41        | 229.41           | 66.20             | 02/2007<br>-          | 08/2011     | 54(O)                             | 0/0                        |
| 418          | CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra                     | 01/2006          | 247.00<br>-             | 247.00           | 75.89             | 02/2007<br>-          | 08/2011     | 54(O)                             | 0/0                        |
| 419          | FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra                          | 04/2010          | 389.86<br>-             | 389.86           | 3.06              | 09/2011<br>-          | 09/2011     | 0(O)                              | 0/0                        |
| 420          | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State            | 10/2009          | 384.00<br>-             | 384.00           | 20.90             | 10/2010<br>-          | 03/2012     | 17(O)                             | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No                     | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|--------------------------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                          |                                                                                     |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                        | 2                                                                                   | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| 421                      | PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State               | 11/2003          | 250.00<br>-             | 425.51           | 80.47             | 12/2005<br>-          | -           | -                                 | 0/0                        |
| 422                      | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra     | 06/2006          | 231.38<br>-             | 168.30           | -                 | 10/2007<br>-          | -           | -                                 | 0/0                        |
| 423                      | MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State                     | 11/2008          | 350.00<br>-             | 350.00           | -                 | -<br>-                | -           | -                                 | 0/0                        |
| 424                      | Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State   | 05/2006          | 1,077.00<br>-           | 1,077.00         | -                 | 03/2009<br>-          | -           | -                                 | 0/0                        |
| 425                      | Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State                    | 08/2006          | 424.00<br>-             | 424.00           | -                 | 03/2009<br>-          | -           | -                                 | 0/0                        |
| 426                      | Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State            | 08/2006          | 590.10<br>-             | 590.10           | -                 | 03/2009<br>-          | -           | -                                 | 0/0                        |
| 427                      | Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State      | 12/2007          | 545.50<br>-             | 545.50           | -                 | 03/2010<br>-          | -           | -                                 | 0/0                        |
| 428                      | Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State                    | 02/2007          | 154.03<br>-             | 154.03           | -                 | 03/2010<br>-          | -           | -                                 | 0/0                        |
| 429                      | Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State                  | 03/2008          | 355.92<br>-             | 355.92           | -                 | 03/2010<br>-          | -           | -                                 | 0/0                        |
| 430                      | Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State                   | 02/2007          | 477.00<br>-             | 477.00           | -                 | 03/2010<br>-          | -           | -                                 | 0/0                        |
| 431                      | Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State    | 12/2007          | 152.65<br>-             | 152.65           | -                 | 03/2010<br>-          | -           | -                                 | 0/0                        |
| 432                      | Procurement of DXC equipment - [N26000074]BSNL,Multi State                          | 02/2008          | 229.00<br>-             | 229.00           | -                 | 03/2010<br>-          | -           | -                                 | 0/0                        |
| 433                      | GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh | 02/2009          | 625.53<br>-             | 625.53           | -                 | 02/2010<br>-          | -           | -                                 | 0/0                        |
| 434                      | GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh    | 09/2009          | 624.75<br>-             | 624.75           | -                 | 09/2010<br>-          | -           | -                                 | 0/0                        |
| 435                      | GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal     | 06/2008          | 170.23<br>-             | 170.23           | -                 | 06/2009<br>-          | -           | -                                 | 0/0                        |
| 436                      | GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd    | 03/2008          | 328.13<br>-             | 328.12           | 164.58            | 03/2009<br>-          | -           | -                                 | 0/0                        |
| <b>Total</b>             |                                                                                     |                  | 18,952.93<br>-          | 19,197.68        | 5,232.45          |                       |             |                                   | 0/0                        |
| <b>Urban Development</b> |                                                                                     |                  |                         |                  |                   |                       |             |                                   |                            |
| 437                      | C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra    | 11/2006          | 114.18<br>173.08        | 173.08           | -                 | 04/2009<br>-          | -           | -                                 | 0/0                        |
| <b>Total</b>             |                                                                                     |                  | 114.18<br>-             | 173.08           | .00               |                       |             |                                   | 0/0                        |

## List of Projects Without Milestones

Aug,2011)

| S.No Project           |                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumm. Expenditure | Date of Commissioning |             | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
|------------------------|------------------------------------------------|------------------|-------------------------|------------------|-------------------|-----------------------|-------------|-----------------------------------|----------------------------|
|                        |                                                |                  |                         |                  |                   | Original / Revised    | Anticipated |                                   |                            |
| 1                      | 2                                              | 3                | 4                       | 5                | 6                 | 7                     | 8           | 9                                 | 10                         |
| <u>Water Resources</u> |                                                |                  |                         |                  |                   |                       |             |                                   |                            |
| 438                    | PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam | 01/2001          | 542.90                  | 1,187.00         | 35.49             | 12/2007               | 12/2012     | 60(O)                             | 0/0                        |
|                        |                                                |                  | -                       |                  |                   | -                     |             |                                   |                            |
|                        | Total                                          |                  | 542.90                  | 1,187.00         | 35.49             |                       |             |                                   | 0/0                        |
|                        |                                                |                  | -                       |                  |                   |                       |             |                                   |                            |
| Grand Total            |                                                |                  | 356,070.65              | 434,271.19       | 169,146.51        |                       |             |                                   | 0/0                        |

## **Abbreviations used in the report**

|                |                                            |
|----------------|--------------------------------------------|
| <b>AAI</b>     | Airport Authority of India                 |
| <b>AERB</b>    | Atomic Energy Regulatory Board             |
| <b>AIBP</b>    | Accelerated Irrigation Benefit Programme   |
| <b>AIR</b>     | All India Radio                            |
| <b>APW</b>     | Active Process Water                       |
| <b>ATU</b>     | Atomic Treating Unit                       |
| <b>BCM</b>     | Billion Cubic Meter                        |
| <b>BHEL</b>    | Bharat Heavy Electricals Ltd.              |
| <b>BHPV</b>    | Bharat Heavy Plates & Vessel Ltd.          |
| <b>BLU</b>     | Boiler Light Up                            |
| <b>BOLT</b>    | Build , Operate, Lease & Transfer          |
| <b>BPST</b>    | Bureau of Parliamentary Studies & Training |
| <b>CCEA</b>    | Cabinet Committee on Economic Affairs      |
| <b>CCU</b>     | Catalytic Cracking Unit                    |
| <b>CDS</b>     | Crude Distribution System                  |
| <b>CDU</b>     | Crude Distillation Unit                    |
| <b>CEA</b>     | Central Electricity Authority              |
| <b>CEC</b>     | Central Empowered Committee                |
| <b>CHP</b>     | Coal Handling Plant                        |
| <b>CLW</b>     | Chittaranjan Locomotive Works              |
| <b>CMPDI</b>   | Central Mine Planning & Design Institute   |
| <b>COS</b>     | Committee of Secretaries                   |
| <b>CPP</b>     | Captive Power Plant                        |
| <b>CRIS</b>    | Centre for Railway Information System      |
| <b>CRL</b>     | Cochin Refinery Ltd.                       |
| <b>CSL</b>     | Cochin Shipyard Ltd.                       |
| <b>CTU</b>     | Crude Topping Unit                         |
| <b>DAE</b>     | Department of Atomic Energy                |
| <b>DB</b>      | Dumb Barges                                |
| <b>DCME</b>    | Digital Circuit Multiplexing Equipment     |
| <b>DGMS</b>    | Director General Mines Safety              |
| <b>DHDS</b>    | Diesel Hydro Desulphurisation project      |
| <b>DOC</b>     | Date of Commissioning                      |
| <b>DOT</b>     | Department of Telecommunication            |
| <b>DVC</b>     | Damodar Valley Corporation                 |
| <b>ECL</b>     | Eastern Coalfields Ltd.                    |
| <b>EIL</b>     | Engineers India Ltd.                       |
| <b>EMP</b>     | Environment Management Plan                |
| <b>EOT</b>     | Electrical Overhead travelling crane       |
| <b>ESP</b>     | Electrostatic Precipitator                 |
| <b>FCCU</b>    | Fluidised catalytic Cracker Unit           |
| <b>FE</b>      | Foreign Exchange                           |
| <b>FOIS</b>    | Freight Generation Information System      |
| <b>FPU</b>     | Feed Preparation Unit                      |
| <b>GAIL</b>    | Gas Authority of India Ltd.                |
| <b>GC</b>      | Gauge Conversion                           |
| <b>GDS</b>     | Gateway Digital Switch                     |
| <b>GIS</b>     | Gas Insulated Station                      |
| <b>GT</b>      | Gas Turbine                                |
| <b>GTPP</b>    | Gas Turbine Power Plant                    |
| <b>HCU</b>     | Hydro- cracker Unit                        |
| <b>HEC</b>     | Heavy Engineering Corporation              |
| <b>HEMM</b>    | Heavy Equipment & Mining Machinery         |
| <b>HEP</b>     | Hydro Electric Project                     |
| <b>HPCL</b>    | Hindustan Petrochemicals Ltd.              |
| <b>HRT</b>     | Head Race Tunnel                           |
| <b>HSCL</b>    | Hindustan Steel Construction Ltd.          |
| <b>HVDC</b>    | High Voltage Direct Current                |
| <b>IAAI</b>    | International Airport Authority of India   |
| <b>ICT</b>     | Inter Connecting Transformer               |
| <b>IDC</b>     | Interest During construction               |
| <b>IFFCO</b>   | Indian Farmer Fertilizer Co-operative      |
| <b>IMG</b>     | Inter Ministerial Group                    |
| <b>IOC</b>     | Indian Oil Corporation                     |
| <b>IPCL</b>    | Indian Petrochemicals Ltd.                 |
| <b>KV</b>      | Kilo Volts.                                |
| <b>L&amp;T</b> | Larsen & Toubro                            |
| <b>LEP</b>     | Life Extension Program                     |
| <b>LOI</b>     | Letter of Intent                           |

|                  |                                              |
|------------------|----------------------------------------------|
| <b>LPG</b>       | Liquified Petroleum Gas                      |
| <b>LSTK</b>      | Lump sum Turnkey contract                    |
| <b>MAMC</b>      | Minning & Allied Machinery Copn.             |
| <b>MFL</b>       | Madras Fertilizer Ltd.                       |
| <b>MGCL</b>      | Madras Gas Cracker Complex                   |
| <b>MIS</b>       | Management Information System                |
| <b>MMSCMD</b>    | Million Metric Standard Cubic Meter day      |
| <b>MMT</b>       | Million Metric Tonnes                        |
| <b>MOE&amp;F</b> | Ministry of Environment & Forest             |
| <b>MT</b>        | Metric Tonnes                                |
| <b>MTY</b>       | Metric Tonne per year                        |
| <b>MU</b>        | Million Unit                                 |
| <b>MW</b>        | Mega Watts                                   |
| <b>NALCO</b>     | National Aluminium Company                   |
| <b>NBCC</b>      | National Building Construction Copn.         |
| <b>NCL</b>       | Northern coalfields Ltd                      |
| <b>NEC</b>       | North East Council                           |
| <b>NEEPCO</b>    | North-Eastern Electric Power Corporation     |
| <b>NFL</b>       | National Fertilizer Ltd.                     |
| <b>NH</b>        | National Highway                             |
| <b>NHPC</b>      | National Hydro-Electric Power Corporation    |
| <b>NIRE</b>      | National Institute of Renewable Energy       |
| <b>NIT</b>       | Notice Inviting Tender                       |
| <b>NJPC</b>      | Nathpa Jhakri Power Corpn.                   |
| <b>NLC</b>       | Neyveli Lignite Corpn.                       |
| <b>NMDC</b>      | National Mineral Development Corpn.          |
| <b>NPC</b>       | Nuclear Power Corporation                    |
| <b>NRL</b>       | Numaligarh Refinery Ltd.                     |
| <b>OB</b>        | Over burden                                  |
| <b>OC</b>        | Opencast                                     |
| <b>OECE</b>      | Overseas Economic Co-operation Fund          |
| <b>ONGC</b>      | Oil & Natural Gas Commission                 |
| <b>OPGC</b>      | Orissa Power Generation Corporation          |
| <b>P &amp; M</b> | Plant & Machinery                            |
| <b>PERT</b>      | Project Evaluation & Review Technique        |
| <b>PHT</b>       | Primary Heat Transport                       |
| <b>PIB</b>       | Public Investment Board                      |
| <b>PSLW</b>      | Powered Support Longwall                     |
| <b>QRC</b>       | Quick Roll Changer                           |
| <b>RAPP</b>      | Rajasthan Atomic Power Plant                 |
| <b>RCE</b>       | Revised Cost Estimates                       |
| <b>RCF</b>       | Railway Coach Factory                        |
| <b>ROB</b>       | Road Over bridge                             |
| <b>ROH</b>       | Regular Overhauling                          |
| <b>RTU</b>       | Remote Terminal Unit                         |
| <b>SAIL</b>      | Steel Authority of India Ltd.                |
| <b>SCI</b>       | Shipping Corporation of India                |
| <b>SDH</b>       | Synchronous Digital Hierarchy                |
| <b>SG</b>        | Steam Generator                              |
| <b>SP</b>        | Self Propelled                               |
| <b>ST</b>        | Steam Turbine                                |
| <b>STPS</b>      | Super Thermal Power Station                  |
| <b>SSS</b>       | Sardar Swaran Singh                          |
| <b>SUR</b>       | Sulphur Recovery Unit                        |
| <b>SWSU</b>      | Sour Water Stripping Unit                    |
| <b>TBM</b>       | Tunnel Boring Machine                        |
| <b>TG</b>        | Turbo Generator                              |
| <b>TPA</b>       | Tonnes Per Annum                             |
| <b>TPS</b>       | Thermal Power Station                        |
| <b>TPY</b>       | Tonnes per year                              |
| <b>UG</b>        | Under Ground                                 |
| <b>ULDCS</b>     | Unified Load Despatch & Communication Scheme |
| <b>VDU</b>       | Vaccum Distillation Unit                     |
| <b>WHRB</b>      | Waste Heat Recovery Boiler                   |
