

**334<sup>th</sup> FLASH REPORT  
ON  
CENTRAL SECTOR PROJECTS  
(₹ 150 crore and above)  
August 2013**



DMRC - DELHI MRTS PHASE-III



Government of India  
**Ministry of Statistics and Programme Implementation**  
**Infrastructure and Project Monitoring Division**  
Sardar Patel Bhavan, Sansad Marg  
New Delhi-110001  
Website: [www.cspm.gov.in](http://www.cspm.gov.in)

## **Abbreviations used in the report**

|                |                                            |
|----------------|--------------------------------------------|
| <b>AAI</b>     | Airport Authority of India                 |
| <b>AERB</b>    | Atomic Energy Regulatory Board             |
| <b>AIBP</b>    | Accelerated Irrigation Benefit Programme   |
| <b>AIR</b>     | All India Radio                            |
| <b>APW</b>     | Active Process Water                       |
| <b>ATU</b>     | Atomic Treating Unit                       |
| <b>BCM</b>     | Billion Cubic Meter                        |
| <b>BHEL</b>    | Bharat Heavy Electricals Ltd.              |
| <b>BHPV</b>    | Bharat Heavy Plates & Vessel Ltd.          |
| <b>BLU</b>     | Boiler Light Up                            |
| <b>BOLT</b>    | Build , Operate, Lease & Transfer          |
| <b>BPST</b>    | Bureau of Parliamentary Studies & Training |
| <b>CCEA</b>    | Cabinet Committee on Economic Affairs      |
| <b>CCU</b>     | Catalytic Cracking Unit                    |
| <b>CDS</b>     | Crude Distribution System                  |
| <b>CDU</b>     | Crude Distillation Unit                    |
| <b>CEA</b>     | Central Electricity Authority              |
| <b>CEC</b>     | Central Empowered Committee                |
| <b>CHP</b>     | Coal Handling Plant                        |
| <b>CLW</b>     | Chittaranjan Locomotive Works              |
| <b>CMPDI</b>   | Central Mine Planning & Design Institute   |
| <b>COS</b>     | Committee of Secretaries                   |
| <b>COR</b>     | Cost Overrun                               |
| <b>CPP</b>     | Captive Power Plant                        |
| <b>CRIS</b>    | Centre for Railway Information System      |
| <b>CRL</b>     | Cochin Refinery Ltd.                       |
| <b>CSL</b>     | Cochin Shipyard Ltd.                       |
| <b>CTU</b>     | Crude Topping Unit                         |
| <b>DAE</b>     | Department of Atomic Energy                |
| <b>DB</b>      | Dumb Barges                                |
| <b>DCME</b>    | Digital Circuit Multiplexing Equipment     |
| <b>DGMS</b>    | Director General Mines Safety              |
| <b>DHDS</b>    | Diesel Hydro Desulphurisation project      |
| <b>DOA</b>     | Date of Approval                           |
| <b>DOC</b>     | Date of Commissioning                      |
| <b>DOT</b>     | Department of Telecommunication            |
| <b>DVC</b>     | Damodar Valley Corporation                 |
| <b>ECL</b>     | Eastern Coalfields Ltd.                    |
| <b>EIL</b>     | Engineers India Ltd.                       |
| <b>EMP</b>     | Environment Management Plan                |
| <b>EOT</b>     | Electrical Overhead travelling crane       |
| <b>ESP</b>     | Electrostatic Precipitator                 |
| <b>FCCU</b>    | Fluidised catalytic Cracker Unit           |
| <b>FE</b>      | Foreign Exchange                           |
| <b>FOIS</b>    | Freight Generation Information System      |
| <b>FPU</b>     | Feed Preparation Unit                      |
| <b>GAIL</b>    | Gas Authority of India Ltd.                |
| <b>GC</b>      | Gauge Conversion                           |
| <b>GDS</b>     | Gateway Digital Switch                     |
| <b>GIS</b>     | Gas Insulated Station                      |
| <b>GT</b>      | Gas Turbine                                |
| <b>GTPP</b>    | Gas Turbine Power Plant                    |
| <b>HCU</b>     | Hydro- cracker Unit                        |
| <b>HEC</b>     | Heavy Engineering Corporation              |
| <b>HEMM</b>    | Heavy Equipment & Mining Machinery         |
| <b>HEP</b>     | Hydro Electric Project                     |
| <b>HPCL</b>    | Hindustan Petrochemicals Ltd.              |
| <b>HRT</b>     | Head Race Tunnel                           |
| <b>HSCL</b>    | Hindustan Steel Construction Ltd.          |
| <b>HVDC</b>    | High Voltage Direct Current                |
| <b>IAAI</b>    | International Airport Authority of India   |
| <b>ICT</b>     | Inter Connecting Transformer               |
| <b>IDC</b>     | Interest During construction               |
| <b>IFFCO</b>   | Indian Farmer Fertilizer Co-operative      |
| <b>IMG</b>     | Inter Ministerial Group                    |
| <b>IOC</b>     | Indian Oil Corporation                     |
| <b>IPCL</b>    | Indian Petrochemicals Ltd.                 |
| <b>KV</b>      | Kilo Volts.                                |
| <b>L&amp;T</b> | Larsen & Toubro                            |
| <b>LEP</b>     | Life Extension Program                     |

|                  |                                              |
|------------------|----------------------------------------------|
| <b>LOI</b>       | Letter of Intent                             |
| <b>LPG</b>       | Liquified Petroleum Gas                      |
| <b>LSTK</b>      | Lump sum Turnkey contract                    |
| <b>MAMC</b>      | Minning & Allied Machinery Copn.             |
| <b>MFL</b>       | Madras Fertilizer Ltd.                       |
| <b>MGCL</b>      | Madras Gas Cracker Complex                   |
| <b>MIS</b>       | Management Information System                |
| <b>MMSCMD</b>    | Million Metric Standard Cubic Meter day      |
| <b>MMT</b>       | Million Metric Tonnes                        |
| <b>MOE&amp;F</b> | Ministry of Environment & Forest             |
| <b>MT</b>        | Metric Tonnes                                |
| <b>MTY</b>       | Metric Tonne per year                        |
| <b>MU</b>        | Million Unit                                 |
| <b>MW</b>        | Mega Watts                                   |
| <b>NAC</b>       | New Anticipated Cost                         |
| <b>NALCO</b>     | National Aluminium Company                   |
| <b>NBCC</b>      | National Building Construction Copn.         |
| <b>NCL</b>       | Northern coalfields Ltd                      |
| <b>NEC</b>       | North East Council                           |
| <b>NEEPCO</b>    | North-Eastern Electric Power Corporation     |
| <b>NFL</b>       | National Fertilizer Ltd.                     |
| <b>NH</b>        | National Highway                             |
| <b>NHPC</b>      | National Hydro-Electric Power Corporation    |
| <b>NIRE</b>      | National Institute of Renewable Energy       |
| <b>NIT</b>       | Notice Inviting Tender                       |
| <b>NJPC</b>      | Nathpa Jhakri Power Corpn.                   |
| <b>NLC</b>       | Neyveli Lignite Corpn.                       |
| <b>NMDC</b>      | National Mineral Development Corpn.          |
| <b>NPC</b>       | Nuclear Power Corporation                    |
| <b>NRL</b>       | Numaligarh Refinery Ltd.                     |
| <b>OB</b>        | Over burden                                  |
| <b>OC</b>        | Opencast                                     |
| <b>OECE</b>      | Overseas Economic Co-operation Fund          |
| <b>ONGC</b>      | Oil & Natural Gas Commission                 |
| <b>OPGC</b>      | Orissa Power Generation Corporation          |
| <b>P &amp; M</b> | Plant & Machinery                            |
| <b>PERT</b>      | Project Evaluation & Review Technique        |
| <b>PHT</b>       | Primary Heat Transport                       |
| <b>PIB</b>       | Public Investment Board                      |
| <b>PSLW</b>      | Powered Support Longwall                     |
| <b>QRC</b>       | Quick Roll Changer                           |
| <b>RAPP</b>      | Rajasthan Atomic Power Plant                 |
| <b>RCE</b>       | Revised Cost Estimates                       |
| <b>RCF</b>       | Railway Coach Factory                        |
| <b>ROB</b>       | Road Over bridge                             |
| <b>ROH</b>       | Regular Overhauling                          |
| <b>RTU</b>       | Remote Terminal Unit                         |
| <b>SAIL</b>      | Steel Authority of India Ltd.                |
| <b>SCI</b>       | Shipping Corporation of India                |
| <b>SDH</b>       | Synchronous Digital Hierarchy                |
| <b>SG</b>        | Steam Generator                              |
| <b>SP</b>        | Self Propelled                               |
| <b>ST</b>        | Steam Turbine                                |
| <b>STPS</b>      | Super Thermal Power Station                  |
| <b>SUR</b>       | Sulphur Recovery Unit                        |
| <b>SWSU</b>      | Sour Water Stripping Unit                    |
| <b>TBM</b>       | Tunnel Boring Machine                        |
| <b>TG</b>        | Turbo Generator                              |
| <b>TPA</b>       | Tonnes Per Annum                             |
| <b>TPS</b>       | Thermal Power Station                        |
| <b>TOR</b>       | Time Overrun                                 |
| <b>TPY</b>       | Tonnes per year                              |
| <b>UG</b>        | Under Ground                                 |
| <b>ULDSCS</b>    | Unified Load Despatch & Communication Scheme |
| <b>VDU</b>       | Vacuum Distillation Unit                     |
| <b>WHRB</b>      | Waste Heat Recovery Boiler                   |
| <b>WO_DOC</b>    | With out Date of Commissioning               |
| <b>WO_ODC</b>    | With out original Date of Commissioning      |

# Contents

|                                                                                      |         |
|--------------------------------------------------------------------------------------|---------|
| Executive Summary in English                                                         | 1 -9    |
| Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14 | 10-11   |
| Summary of Projects                                                                  | 12-29   |
| Trend and Graphical Analysis of Projects                                             | 30-42   |
| Sector wise analysis of projects                                                     | 43-43   |
| List of All Ongoing Projects                                                         | 44-72   |
| Sector wise Graph                                                                    | 73-83   |
| <b>ANNEXURE</b>                                                                      | 84-84   |
| Central Sector Projects                                                              | 85-85   |
| List of Projects Having Expenditure More than cost                                   | 86-91   |
| List of Projects Ahead of Schedule                                                   | 92-92   |
| List of Projects with out Original date of Commissioning                             | 93-94   |
| List of Projects with out date of Commissioning                                      | 95-104  |
| List of On schedule Projects Original Schedule                                       | 105-112 |
| List of Delayed Projects w.r.t Original Schedule                                     | 113-125 |
| List of Projects Having cost overrun w.r.t original                                  | 126-136 |
| List of Projects Having cost and time overrun w.r.t original                         | 137-141 |
| List of Projects without Milestones                                                  | 142-162 |
| List of Projects Ahead of Schedule w.r.t Latest Schedule                             | 163-163 |
| List of On schedule Projects w.r.t. Latest Schedule                                  | 164-172 |
| List of Delayed Projects w.r.t Latest Schedule                                       | 173-185 |



## कार्यकारी सारांश

अगस्त, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 741 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अगस्त, 2013 के दौरान 4 परियोजनाओं (विद्युत क्षेत्र की 1 तथा रेलवे क्षेत्र की 3) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 741 परियोजनाओं में से 291 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 44 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 44 परियोजनाओं में से, 15 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। रेलवे, पोत परिवहन तथा पत्तन, इस्पात, विद्युत, सड़क परिवहन एवं राजमार्ग तथा पेट्रोलियम क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 28 महीनों तक का अतिरिक्त विलंब हुआ है।

| क्र.सं.    | क्षेत्र                  | निगरानी के तहत आने वाली परियोजनाएं | नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं | रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं | अतिरिक्त विलंबित बड़ी परियोजनाएं |
|------------|--------------------------|------------------------------------|--------------------------------------------------|-------------------------------------------------------|----------------------------------|
| 1.         | रेलवे                    | 283                                | 34                                               | 2                                                     | 1                                |
| 2.         | सड़क परिवहन एवं राजमार्ग | 152                                | 100                                              | 19                                                    | 3                                |
| 3.         | विद्युत                  | 99                                 | 51                                               | 7                                                     | 5                                |
| 4.         | पेट्रोलियम               | 84                                 | 51                                               | 9                                                     | 4                                |
| 5.         | कोयला                    | 55                                 | 28                                               | 0                                                     | 0                                |
| 6.         | पोत परिवहन एवं पत्तन     | 19                                 | 2                                                | 3                                                     | 1                                |
| 7.         | इस्पात                   | 18                                 | 12                                               | 4                                                     | 1                                |
| 8.         | दूरसंचार                 | 13                                 | 6                                                | 0                                                     | 0                                |
| 9.         | नागर विमानन              | 8                                  | 2                                                | 0                                                     | 0                                |
| 10.        | परमाणु ऊर्जा             | 4                                  | 4                                                | 0                                                     | 0                                |
| 11.        | शहरी विकास               | 4                                  | 1                                                | 0                                                     | 0                                |
| 12.        | पेट्रोरसायन              | 1                                  | 0                                                | 0                                                     | 0                                |
| 13.        | जल संसाधन                | 1                                  | 0                                                | 0                                                     | 0                                |
| <b>कुल</b> |                          | <b>741</b>                         | <b>291</b>                                       | <b>44</b>                                             | <b>15</b>                        |

3. 741 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग `9,12,567.98 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत `10,87,065.02 करोड़ रुपए होने की संभावना है जो 1,74,497.04 करोड़ (मूल लागत का 19.10%) की समग्र लागत वृद्धि को दर्शाता है । अगस्त, 2013 तक इन परियोजनाओं पर किया गया व्यय ` 5,03,192.40 करोड़ है जो परियोजनाओं की अनुमानित लागत का 46.30% है । लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.08.2013 की स्थिति के अनुसार)**

| क्र. सं. | परियोजना                                                                        | क्षेत्र | अनुमोदन की तारीख | परियोजना की लागत ( करोड़) |         |          | लागत-वृद्धि (% में) |
|----------|---------------------------------------------------------------------------------|---------|------------------|---------------------------|---------|----------|---------------------|
|          |                                                                                 |         |                  | मूल                       | संशोधित | अनुमानित |                     |
| 1        | नांगल बांध तलवारा (एनएल), एनआर                                                  | रेलवे   | 03/1981          | 37.68                     | 450.00  | 1036.78  | 2651.54             |
| 2        | गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर | रेलवे   | 04/1983          | 36.80                     | 274.41  | 703.17   | 1810.79             |
| 3        | हावड़ा-आमता-चेपादंगा एनएल (एसईआर)                                               | रेलवे   | 04/1974          | 31.42                     | 393.46  | 535.40   | 1604.01             |
| 4        | बांकुरा-दामोदर (जीसी) (एसईआर)                                                   | रेलवे   | 03/1998          | 111.90                    | 1028.05 | 1423.98  | 1172.55             |
| 5        | रूपसा-बांगरीपोसी (जीसी) (एसईआर)                                                 | रेलवे   | 02/1996          | 57.94                     | 604.04  | 639.97   | 1004.54             |

**टिप्पणी:** परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.08.2013 की स्थिति के अनुसार)

| क्र. सं. | परियोजना                                         | क्षेत्र      | अनुमोदन की तारीख | परियोजना की लागत (₹ करोड़) |               |             |
|----------|--------------------------------------------------|--------------|------------------|----------------------------|---------------|-------------|
|          |                                                  |              |                  | मूल लागत                   | अनुमानित लागत | लागत-वृद्धि |
| 1        | उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर             | रेलवे        | 03/1995          | 2500.00                    | 20000.00      | 17500.00    |
| 2        | बंगलौर मेट्रो रेल परियोजना                       | शहरी विकास   | 05/2006          | 6395.00                    | 11609.00      | 5214.00     |
| 3        | सुबानश्री लोअर एचईपी (एनएचपीसी)                  | विद्युत      | 09/2003          | 6285.33                    | 10667.00      | 4381.67     |
| 4        | कुंडकुलम एपीपी (एनपीसीआईएल)                      | परमाणु ऊर्जा | 12/2001          | 13171.00                   | 17270.00      | 4099.00     |
| 5        | बोगीबिल एंड लिंक लाईन पर ब्रह्मपुत्र पुल एनईएफआर | रेलवे        | 09/1997          | 1000.00                    | 4996.65       | 3996.65     |

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 741 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 156 समय पर तथा 291 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 302 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 27 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 262 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 291 विलंबित परियोजनाओं में से, 70 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 73 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 74 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 68 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.08.2013 की स्थिति के अनुसार)

| क्र. सं. | परियोजना                                               | क्षेत्र | अनुमोदन की तारीख | शुरू करने की तारीख |          | समय-वृद्धि (महीने में) |
|----------|--------------------------------------------------------|---------|------------------|--------------------|----------|------------------------|
|          |                                                        |         |                  | मूल                | अनुमानित |                        |
| 1        | फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)            | रेलवे   | 03/1984          | 03/1995            | 03/2015  | 240                    |
| 2        | गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर) | रेलवे   | 04/1986          | 03/1994            | 10/2013  | 235                    |
| 3        | उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर                   | रेलवे   | 03/1995          | 03/2001            | 12/2017  | 201                    |
| 4        | बांकुरा-दामोदर (जीसी) (एसईआर)                          | रेलवे   | 03/1998          | 03/2005            | 12/2016  | 141                    |
| 5        | लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)                         | रेलवे   | 04/1993          | 03/2002            | 09/2013  | 138                    |

**टिप्पणी:** परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. समय एवं लागत वृद्धि के संबंध में गंभीर रूप से प्रभावित इन परियोजनाओं की समीक्षा में, रेल मंत्रालय ने सूचित किया है कि रेलवे परियोजनाओं हेतु परिव्यय बहुत ही कम है और वर्तमान स्फीति को निष्क्रिय करने हेतु अपर्याप्त है । इसके कारण रेलवे परियोजनाओं को पूरा करने से संबंधित लक्ष्यों को निश्चित करने की स्थिति में नहीं है । निधि की कमी ने रेलवे को वर्ष 2010-11 तथा 2011-12 में क्रमशः 2315 किमी तथा 2337 किमी की उपलब्धि के मुकाबले वर्ष 2013-14 हेतु लक्ष्य को कम करके 1525 किमी करने को विवश किया है ।

7. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, उपस्कर संस्थापना में विलंब, संरचना डिजाइन में परिवर्तन, भू वैज्ञानिक गतिविधियां, प्रौद्योगिकी का हस्तांतरण, कार्य-क्षेत्र में बदलाव, राज्य सरकार द्वारा जनोपयोगी सेवाओं को अन्यत्र ले जाने में विलंब, कार्यकारी एजेंसी के स्वामित्व में बदलाव, स्थान की कमी, वेन्डर द्वारा संग्रहण, कार्यों को प्रदान करने में विलंब, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

**बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.08.2013 की स्थिति के अनुसार)**

| क्र. सं. | परियोजना                                    | क्षेत्र | अनुमोदन की तारीख | परियोजना की लागत (रु. करोड़) |          | संचयी व्यय (रु. करोड़) | शुरू करने की तारीख |          | उपलब्धि |
|----------|---------------------------------------------|---------|------------------|------------------------------|----------|------------------------|--------------------|----------|---------|
|          |                                             |         |                  | मूल                          | अनुमानित |                        | मूल                | अनुमानित |         |
| 1        | हावड़ा-आमता-चंपादंगा एनएल (एससीआर)          | रेलवे   | 04/1974          | 31.42                        | 535.40   | 176.52                 | 03/2007            | 03/2015  | एन.आर.  |
| 2        | नांगल बांध तलवारा (एनएल), एनआर              | रेलवे   | 03/1981          | 37.68                        | 036.78   | 353.41                 | 07/2012            | एन.आर.   | एन.आर.  |
| 3        | इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन    | रेलवे   | 04/1983          | 36.80                        | 703.17   | 247.74                 | एन.आर.             | 03/2015  | एन.आर.  |
| 4        | फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस) | रेलवे   | 03/1984          | 0.00                         | 634.13   | 555.27                 | 03/1995            | 03/2013  | एन.आर.  |
| 5        | तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)       | रेलवे   | 03/1984          | 3.97                         | 4.47     | 433.89                 | 06/2005            | 06/2016  | एन.आर.  |

**टिप्पणी:** परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

एन.आर.: सूचित नहीं।

9. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं। पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

**बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.08.2013 की स्थिति के अनुसार)**

| क्र. सं. | परियोजना                                   | क्षेत्र | अनुमोदन की तारीख | परियोजना की लागत (₹ करोड़) |         | संचयी व्यय (₹ करोड़) |
|----------|--------------------------------------------|---------|------------------|----------------------------|---------|----------------------|
|          |                                            |         |                  | मूल                        | संशोधित |                      |
| 1        | लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)             | रेलवे   | 04/1993          | 100.00                     | 142.98  | 211.19               |
| 2        | अमरावती-नरखेर एनएल (सीआर)                  | रेलवे   | 06/1994          | 120.90                     | 284.27  | 541.95               |
| 3        | पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर) | रेलवे   | 12/1994          | 124.43                     | 495.68  | 597.99               |
| 4        | उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर       | रेलवे   | 03/1995          | 2500.00                    | 2500.00 | 8549.43              |
| 5        | कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)          | रेलवे   | 04/1995          | 65.94                      | 302.23  | 344.29               |

**टिप्पणी:** परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.08.2013 की स्थिति के अनुसार)

| क्र. सं. | परियोजना                                   | क्षेत्र | अनुमोदन की तारीख | परियोजना को शुरू करने की तारीख |         |          |
|----------|--------------------------------------------|---------|------------------|--------------------------------|---------|----------|
|          |                                            |         |                  | मूल                            | संशोधित | अनुमानित |
| 1        | नांगल बांध-तलवारा (एनएल), एनआर             | रेलवे   | 03/1981          | 07/2012                        | एन.आर.  | एन.आर.   |
| 2        | विरमगाम-भिल्डी (डब्ल्यूआर), जीसी           | रेलवे   | 04/1990          | एन.आर.                         | 03/2010 | एन.आर.   |
| 3        | अमरावती-नरखेर एनएल (सीआर)                  | रेलवे   | 06/1994          | 06/1999                        | 03/2011 | 03/2011  |
| 4        | पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर) | रेलवे   | 12/1994          | एन.आर.                         | एन.आर.  | 03/2012  |
| 5        | कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)          | रेलवे   | 04/1995          | एन.आर.                         | एन.आर.  | 12/2012  |

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

10. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

I. रेलवे क्षेत्र में 283 परियोजनाओं में से 34 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से एक परियोजना मेगा परियोजना है । । 'लुम्बडिंग -सिल्चर जिरीबाम, बदरपुर-बारईग्राम कुमर्ग, एन ई एफ आर' तथा 'चम्पाझारन-विमलगढ डबलिंग एक्सटेंशन, एसईआर' परियोजना के संबंध में प्रत्येक में क्रमशः निधि की कमी तथा खराब मौसम परिस्थितियों के कारण 9 माह के अतिरिक्त विलंब की सूचना दी गई है ।

II. पोत परिवहन तथा पत्तन क्षेत्र में 19 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1- 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से एक परियोजना मेगा परियोजना है । 'भारतीय पोत निगम द्वारा चार 82000 डीडब्ल्यूटी काम्सवमैक्स भारी जहाजों का अधिग्रहण', भारतीय पोत निगम द्वारा चार एंकर हैंडलिंग सह

आपूर्ति जहाजों का अधिग्रहण' तथा 'भारतीय मुम्बई पत्तन न्यास द्वारा दो ऑफशोर कन्टेनर बर्थस एण्ड टर्मिनल का निर्माण तथा विकास' परियोजनाओं के संबंध में क्रमशः 1,2 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

**III. इस्पात क्षेत्र** में 18 परियोजनाओं में से 12 परियोजनाएं विलंबित हैं। माह के दौरान 4 परियोजनाओं के संबंध में 1-3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 1 मेगा परियोजना है। 'तरल इस्पात का 3 एमटीपीवाई से 6.3 एमटीपीवाई तक आरआईएनएल/वीएसपी का विस्तार, आरआईएनएल' तथा '67.5 मेगावाट टीजी-5 आक्जीलरी सिस्टम इमरजेंसी पावर रिकवायरमेंट, आरआईएनएल', सेल के सम्बन्ध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना दी गई है; कोक ओवन बैटरी नं. 4 फेस- II, आरआईएनएल' तथा 'कच्चा माल हैंडलिंग संयंत्र (आरएमएचपी) में लौह अयस्क भण्डारण का संवर्धन, आरआईएनएल' परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

**IV विद्युत क्षेत्र** में, 99 परियोजनाओं में से 51 परियोजनाएं विलंबित हैं। माह के दौरान, 7 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 5 मेगा परियोजनाएं हैं। 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XX पीजीसीआईएल' परियोजना के संबंध में कार्यान्वयन एजेंसी में परिवर्तन के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'ओडिशा में फेस-1 जनरेशन परियोजना हेतु पारेषण प्रणाली, पीजीसीआईएल' तथा 'ओडिशा-सी में फेस-1 जनरेशन परियोजना हेतु पारेषण प्रणाली, पीजीसीआईएल' परियोजना वन संबंधी अनुमति में विलंब होने के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'एमबी टावर लिमिटेड की कनेक्टिविटी के लिए पारेषण प्रणाली, पीजीसीआईएल' परियोजना में आर ओ डब्ल्यू समस्या के कारण 2 माह के अतिरिक्त विलंब की सूचना दी है। 'पारबती आईपी-II, एनएचपीसी' में संविदा संबंधी मामलों के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'मध्य प्रदेश तथा छत्तीसगढ़ में आईपीपी जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' परियोजना में भूमि अधिग्रहण में विलम्ब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

**V पट्रोलियम क्षेत्र** में 84 परियोजनाओं में से 51 परियोजनाएं विलंबित हैं। माह के दौरान, 9 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 4 मेगा परियोजनाएं हैं। 'फ्लूडाइज्ड कैटालाइटिक क्रैकिंग यूनिट (एफसीसीयू) रिवैम्प, आईओसीएल' तथा विजाग में स्ट्रैटैजिक कूड आर्यल परियोजना, आईएसपीआरआई' के संबंध में ब्राउनफील्ड ऑपरेशन के कारण यूनिट के बंद होने से तथा बैलेंस बैंच को हटाने के दौरान भूवैज्ञानिक गतिविधियों के कारण प्रत्येक में 1 माह के विलंब अतिरिक्त विलंब की सूचना प्राप्त हुई है,



“सेन्ट्रल गैस गेदरिंग स्टेशन एण्ड आफटेक प्वाइन्ट, ओआईएन’ परियोजना के संबंध में ईपीसी ठेकेदार द्वारा ड्राइंग जारी करने में विलंब तथा बार-बार बन्द होने के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘गैस टर्बाइन जनरेशन सैट, ओआईएल’ परियोजना के संबंध में उपस्करों की आपूर्ति में विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘चबुआ तथा बागजाम में 2 एफजीएस का निर्माण, ओआईएल’ परियोजना के संबंध में भारी वर्षा के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘बी-46-कलस्टर फील्ड का विकास, ओएनजीसी’ परियोजना तथा पानीपत में बूटाडीन एक्सट्रैक्शन यूनिट, आईओसीएल’ प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘तत्काल आपूर्ति जहाज (आईएसवी) का निर्माण, ओएनजीसी’ तथा ‘मुम्बई हाई नॉर्थ डेवलपमेंट फेस 2, ओएनजीसी’ परियोजनाओं के संबंध में क्रमशः 2 तथा 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

**V. सड़क परिवहन तथा राजमार्ग क्षेत्र में 152 परियोजनाओं में से 100 विलंबित हैं । माह के दौरान, 19 परियोजनाओं के संबंध में 1-28 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 3 मेगा परियोजना है । ‘जयपुर-टोंक-देवली, एनएचएआई’ परियोजना के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘हावेरी-हरिहर(जीक्यू)340कि.मी.से 244.कि.मी.(एनएच-4), एनएचएआई’, ‘हरिहर-चित्रदुर्ग(जीक्यू)284कि.मी.से 207.कि.मी.(एनएच-4), एनएचएआई’ तथा ‘न्यू मंगलौर पोर्ट, एनएच-17 तथा 48, एनएचएआई’ परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘सुनाखला—गंजम (जीक्यू) 338कि.मी.से 284.कि.मी. (एनएच-5), एनएचएआई’ तथा ‘कोटा बाईपास,आरजे-4,एनएच76, एनएचएआई’ परियोजनाओं के संबंध में प्रत्येक में 3माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘गंजम-इच्छापुरम, एनएच-5, एनएचएआई’,‘बालासौर भद्रक136.5कि.मी.से199.14.कि.मी.एनएच-5,एनएचएआई’ तथा ‘अहमदाबाद से गोधरा को चार लेन बनाना, एनएचएआई’ परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, ‘सलेम-यू/उन्ड्रपेट(बीओटी-1/टीएन-06) एनएच-68, एनएचएआई’ तथा पिम्पलागांव-नासिक-गोन्ड, एनएच-3(एनएचडीपी-फेस-3), एनएचएआई’ परियोजनाओं के संबंध में प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘गोधरा से गुजरात/मध्य प्रदेश सीमा तक को चार लेन बनाना, एनएचएआई’ तथा ‘भुवनेश्वर से पुरी, एनएचएआई’ परियोजनाओं के संबंध में प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है;‘सोनपुर से गुवाहाटी(एएस-3), एनएचएआई’, ‘गाजियाबाद-अलीगढ़ एनएच-91,एनएचएआई’ तथा ‘चम्बल पुल, एनएच-76(आरजे-5), एनएचएआई’ परियोजनाओं के संबंध में क्रमशः7, 10 और 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘फरक्का-रायगंज को चार लेन बनाना, एनएचएआई तथा ‘ब्रह्मपुर-फरक्का को चार लेन बनाना, एनएचएआई’ परियोजनाओं के संबंध में प्रत्येक में 16 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; ‘रायगंज-दलकोला को चार लेन बनाना’, एनएचएआई’ के संबंध में 28 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । कार्यान्वयन एजेंसी ने इन परियोजनाओं में**

विलंब के लिए किसी विशेष कारण का कोई उल्लेख नहीं किया है । तथापि, इन परियोजनाओं में विलंब के सामान्य कारण-भूमि अधिग्रहण, वन तथा पर्यावरण संबंधी अनुमति में विलंब, जनोपयोगी सुविधाओं के अंतरण में विलंब, ठेकेदारों का घटिया कार्य निष्पादन, आदि हैं ।

11. दिनांक 31.08.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
12. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

## **EXECUTIVE SUMMARY**

1. The Flash Report for August 2013 contains information on the status of the 741 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During August 2013, 4 projects (1 project in Power and 3 projects in Railways Sectors) have reported completion.

2. During the reference month, out of 741 projects, 291 projects are delayed with respect to latest schedule and 44 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 44 projects, 15 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 28 months in respect of projects relating to Railways, Shipping & Ports, Steel, Power, Road Transport & Highways and Petroleum Sectors.

| S. No. | Sector                      | Projects on monitor | Delayed Projects w.r.t latest schedule | Additionally delayed during the month under report | Additionally delayed Mega Projects |
|--------|-----------------------------|---------------------|----------------------------------------|----------------------------------------------------|------------------------------------|
| 1.     | Railways                    | 283                 | 34                                     | 2                                                  | 1                                  |
| 2.     | Road Transport And Highways | 152                 | 100                                    | 19                                                 | 3                                  |
| 3.     | Power                       | 99                  | 51                                     | 7                                                  | 5                                  |
| 4.     | Petroleum                   | 84                  | 51                                     | 9                                                  | 4                                  |
| 5.     | Coal                        | 55                  | 28                                     | 0                                                  | 0                                  |
| 6.     | Shipping And Ports          | 19                  | 2                                      | 3                                                  | 1                                  |
| 7.     | Steel                       | 18                  | 12                                     | 4                                                  | 1                                  |
| 8.     | Telecommunications          | 13                  | 6                                      | 0                                                  | 0                                  |
| 9.     | Civil Aviation              | 8                   | 2                                      | 0                                                  | 0                                  |
| 10.    | Atomic Energy               | 4                   | 4                                      | 0                                                  | 0                                  |
| 11.    | Urban Development           | 4                   | 1                                      | 0                                                  | 0                                  |
| 12.    | Petrochemicals              | 1                   | 0                                      | 0                                                  | 0                                  |
| 13.    | Water Resources             | 1                   | 0                                      | 0                                                  | 0                                  |
| Total  |                             | 741                 | 291                                    | 44                                                 | 15                                 |

3. Total original cost of implementation of the 741 projects was about ₹ 9,12,567.98 crore and their anticipated completion cost is likely to be ₹ 10,87,065.02 crore, which reflects overall cost overruns of ₹ 1,74,497.04 crore (19.10 % of original cost). The expenditure incurred on these projects till August 2013 is ₹ 5,03,192.40 crore, which is 46.30 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

**LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-08 -2013)**

| SN | PROJECT                                                                 | SECTOR   | DATE OF APPROVAL | COST OF PROJECT (₹ ; crore) |         |             | COST OVERRUNS (in %) |
|----|-------------------------------------------------------------------------|----------|------------------|-----------------------------|---------|-------------|----------------------|
|    |                                                                         |          |                  | ORIGINAL                    | REVISED | ANTICIPATED |                      |
| 1  | NANGALDAM-TALWARA(NL),NR                                                | Railways | 03/1981          | 37.68                       | 450.00  | 1036.78     | 2651.54              |
| 2  | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR | Railways | 04/1983          | 36.80                       | 274.41  | 703.17      | 1810.79              |
| 3  | HOWRAH-AMTA-CHAMPADANGA NL (SER)                                        | Railways | 04/1974          | 31.42                       | 393.46  | 535.40      | 1604.01              |
| 4  | BANKURA - DAMODAR (GC) (SER)                                            | Railways | 03/1998          | 111.90                      | 1028.05 | 1423.98     | 1172.55              |
| 5  | RUPSA-BANGRIPOSI (GC) (SER)                                             | Railways | 02/1996          | 57.94                       | 604.04  | 639.97      | 1004.54              |

**N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.**

4. The 5 projects with maximum cost overruns in absolute term are as below:-

**LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-08-2013)**

| SN | PROJECT                                    | SECTOR            | DATE OF APPROVAL | COST OF PROJECT (₹ ; crore) |                  |              |
|----|--------------------------------------------|-------------------|------------------|-----------------------------|------------------|--------------|
|    |                                            |                   |                  | COST ORIGINAL               | COST ANTICIPATED | COST OVERRUN |
| 1  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR        | Railways          | 03/1995          | 2500.00                     | 20000.00         | 17500.00     |
| 2  | BANGALORE METRO RAIL PROJECT               | Urban Development | 05/2006          | 6395.00                     | 11609.00         | 5214.00      |
| 3  | SUBANSIRI LOWER H.E.P (NHPC)               | Power             | 09/2003          | 6285.33                     | 10667.00         | 4381.67      |
| 4  | KUDANKULAM APP (NPCIL)                     | Atomic Energy     | 12/2001          | 13171.00                    | 17270.00         | 4099.00      |
| 5  | BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR | Railways          | 09/1997          | 1000.00                     | 4996.65          | 3996.65      |

**N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.**

5. Out of the 741 projects, 5 projects are ahead of schedule, 156 are on schedule and 291 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 302 if delay is calculated on the basis of original schedule of completion. Further, 27 projects have been sanctioned without any commissioning schedule/date and for 262 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 291 delayed projects, 70 projects have overall delay in the range of 1 to 12 months, 79 projects have a delay in the range of 13 to 24 months, 74 projects have a delay in the range of 25 to 60 months and 68 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

**LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-08-2013)**

| SN | PROJECT                                           | SECTOR   | DATE OF APPROVAL | DATE OF COMMISSIONING |             | TIME OVERRUNS (in months) |
|----|---------------------------------------------------|----------|------------------|-----------------------|-------------|---------------------------|
|    |                                                   |          |                  | ORIGINAL              | ANTICIPATED |                           |
| 1  | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)      | Railways | 03/1984          | 03/1995               | 03/2015     | 240                       |
| 2  | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) | Railways | 04/1986          | 03/1994               | 10/2013     | 235                       |
| 3  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR               | Railways | 03/1995          | 03/2001               | 12/2017     | 201                       |
| 4  | BANKURA - DAMODAR (GC) (SER)                      | Railways | 03/1998          | 03/2005               | 12/2016     | 141                       |
| 5  | LANJHIGARH-JUNAGARH NL(ECOR)                      | Railways | 04/1993          | 03/2002               | 09/2013     | 138                       |

**N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.**

6. In a review of its severely affected projects in terms of time & cost overruns, Ministry of Railways has informed that outlay for Railway projects is very low of throw forward and is insufficient even to neutralize the prevailing inflation. Due to this, Railways is not in the position to fix the targets for completion of the projects. Paucity of funds has forced Railways to scale down the targets for 2013-14 to 1525 Km against the achievement of 2315 Km and 2337 Km in 2010-11 and 2011-12 respectively.

7. The brief reasons for time overruns as reported by various other project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, delay in equipment erection, change in structural design, geological surprises, transfer of technology, change in scope of work, delay in shifting of utility by State Government, change of ownership of executing agency, space constraint, mobilization by vendor, delay in award of works ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

**List of 5 Earliest Projects without Milestones (as on 31-08-2013)**

| SN | PROJECT                                      | SECTOR   | DATE OF APPROVAL | COST OF PROJECT<br>(₹ crore) |             | EXPENDITURE CUMMULATIVE<br>(₹ crore) | DATE OF COMMISSIONING |             | MILESTONES |
|----|----------------------------------------------|----------|------------------|------------------------------|-------------|--------------------------------------|-----------------------|-------------|------------|
|    |                                              |          |                  | ORIGINAL                     | ANTICIPATED |                                      | ORIGINAL              | ANTICIPATED |            |
| 1  | HOWRAH-AMTA-CHAMPADANGA NL (SER)             | Railways | 04/1974          | 31.42                        | 535.40      | 176.52                               | 03/2007               | 03/2015     | N.R.       |
| 2  | NANGALDAM-TALWARA(NL),NR                     | Railways | 03/1981          | 37.68                        | 1036.78     | 353.41                               | 07/2012               | N.R.        | N.R.       |
| 3  | NEW BG RLY LINE FROM EKLAKHI-BALURGHAT       | Railways | 04/1983          | 36.80                        | 703.17      | 247.74                               | N.R.                  | 03/2015     | N.R.       |
| 4  | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) | Railways | 03/1984          | 520.00                       | 634.13      | 555.27                               | 03/1995               | 03/2013     | N.R.       |
| 5  | TAMLUK DIGHA,LINE DOUBLING (SER)             | Railways | 03/1984          | 293.97                       | 1074.47     | 433.89                               | 06/2005               | 06/2016     | N.R.       |

**N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.**

**N.R.: Not Reported.**

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

**List of 5 Earliest Projects without Revised Cost Estimates (as on 31-08-2013)**

| SN | PROJECT                                | SECTOR   | DATE OF APPROVAL | COST OF PROJECT (₹; crore) |         | EXPENDITURE CUMMULATIVE (₹; crore) |
|----|----------------------------------------|----------|------------------|----------------------------|---------|------------------------------------|
|    |                                        |          |                  | ORIGINAL                   | REVISED |                                    |
| 1  | LANJHIGARH-JUNAGARH NL(ECOR)           | Railways | 04/1993          | 100.00                     | 142.98  | 211.19                             |
| 2  | AMRAVATI-NARKHER NL(CR)                | Railways | 06/1994          | 120.90                     | 284.27  | 541.95                             |
| 3  | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) | Railways | 12/1994          | 124.43                     | 495.68  | 597.99                             |
| 4  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR    | Railways | 03/1995          | 2500.00                    | 2500.00 | 8549.43                            |
| 5  | KOTTUR-HARIHAR(NL),(SWR)               | Railways | 04/1995          | 65.94                      | 302.23  | 344.29                             |

**N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.**

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

**List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.08.2013)**

| SN | PROJECT                                | SECTOR   | DATE OF APPROVAL | DATE OF COMMISSIONING |         |             |
|----|----------------------------------------|----------|------------------|-----------------------|---------|-------------|
|    |                                        |          |                  | ORIGINAL              | REVISED | ANTICIPATED |
| 1  | NANGALDAM-TALWARA(NL),NR               | Railways | 03/1981          | 07/2012               | N.R.    | N.R.        |
| 2  | VIRAMGAM-BHILDI(WR),GC                 | Railways | 04/1990          | N.R.                  | 03/2010 | N.R.        |
| 3  | AMRAVATI-NARKHER NL(CR)                | Railways | 06/1994          | 06/1999               | 03/2011 | 03/2011     |
| 4  | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) | Railways | 12/1994          | N.R.                  | N.R.    | 03/2012     |
| 5  | KOTTUR-HARIHAR(NL),(SWR)               | Railways | 04/1995          | N.R.                  | N.R.    | 12/2012     |

**N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.**

**N.R.: Not Reported.**

10. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Railways Sector**, out of 283 projects, 34 projects are delayed. During the month 2 projects have reported additional delays of 9 months each, out of which 1 is Mega project. The projects 'Lumding-Silchar Jiribam, Badarpur-Baraigram Kumarg, NEFR' and 'Champajharan-Bimalgarh Doubling Extension, SER' have reported additional delays of 9 months each due to fund constraints and bad weather conditions respectively.

ii) In the **Shipping & Ports Sector**, out of 19 projects, 2 projects are delayed. During the month 3 projects have reported additional delays in the range of 1-9 months, out of which 1 is Mega project. The projects 'Acquisition of 4 Nos of 82000 DWT Kamsavmax bulk carriers by Shipping Corporation of India', 'Acquisition of 4 No. of Anchor Handling cum Supply by Shipping Corporation of India' and 'Construction & Development of 2 Offshore Container Berths & Terminal by Mumbai Port Trust of India' have reported additional delays of 1, 2 and 9 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

iii) In the **Steel Sector**, out of 18 projects, 12 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-3 months, out of which 1 is Mega project. The projects 'Expansion of RINL/VSP from 3 MTPY-6.3 MTPY of liquid Steel, RINL' and '67.5 MW TG-5 Auxiliary System Emergency Power Requirement, RINL' SAIL' have reported additional delay of 1 month each; the projects 'Coke Oven Battery No. 4 Phase-II, RINL' and 'Augmentation of Iron Ore Storage in Raw Material Handling Plant (RMHP), RINL' have reported additional delays of 3 month each (however, no specific reasons have been reported by the project authority for the delay in these projects).

iv) In the **Power Sector**, out of 99 projects, 51 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-12 months, out of which 5 are Mega projects. The project 'Northern Region System Strengthening Scheme- XX, PGCIL' has reported additional delay of 1 month due to change of implementing agency; the projects 'Transmission System for Phase-I Generation Project in Odisha, PGCIL', 'Transmission System for Phase-I Generation Project in Odisha, PGCIL' and 'Transmission System for Phase-I Generation Project in Odisha-C, PGCIL' have reported additional delays of 2 months each due to delay in forest clearance; the project 'Transmission System for Connectivity of MB Power Limited, PGCIL' has reported additional delay of 2 months due to ROW problem; the project 'Parbati HEP – II, NHPC' has reported additional delay of 4 months due to delay in contractual issue; the project



‘Transmission System for IPP Generation Projects in Madhya Pradesh and Chhattisgarh, PGCIL’ has reported additional delay of 12 months due to delay in land acquisition.

**v)** In the **Petroleum Sector**, out of 84 projects, 51 projects are delayed. During the month 9 projects have reported additional delays in the range of 1-6 months, out of which 4 are Mega projects. The projects ‘Fluidized Catalytic Cracking Unit (FCCU) Revamp, IOCL’ and ‘Strategic Crude Oil Storage Project at Vizag, ISPRL’ have reported additional delay of 1 month each due to unit shut down because of brownfield operations and due to geology encountered during excavation of balance bench; the project ‘Central Gas Gathering Station and Offtake Point, OIL’ has reported additional delays of 3 months due to delay in release of drawings by EPC contractor and frequent bandhs; the project ‘Gas Turbine Generation Set, OIL’ has reported additional delay of 5 months due to delay in supply equipments; the project ‘Construction of 2 FGS in Chabua & Baghjan, OIL’ has reported additional delay of 6 months due to heavy rain; the projects ‘Development of B-46 Cluster Field, ONGC’ and ‘Butadiene Extraction Unit (BDEU) at Panipat, IOCL’ have reported additional delay of 1 month each; the projects ‘Construction of 23 Immediate Supply Vessels (ISV), ONGC’ and ‘Mumbai High North Development Phase-II, ONGC’ have reported additional delays of 2 and 6 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

**vi)** In the **Road Transport & Highways Sector**, out of 152 projects, 100 are delayed. During the month 19 projects have reported additional delays in the range of 1-28 months, out of which 3 are Mega projects. The project ‘Jaipur-Tonk-Deoli, NHAI’ has reported additional delay of 1 month; the projects ‘Haveri-Harihar (GQ) KM.340-KM.284 (NH-4), NHAI’ , ‘Harihar-Chitradurga (GQ) KM.284-KM.207 (NH-4), NHAI’ and ‘New Mangalore Port NH-17 and 48, NHAI’ have reported additional delays of 2 months each; the projects ‘Sunakhala-Ganjam (GQ) KM.338-KM.284 (NH-5), NHAI’ and ‘Kota Bypass, RJ-4, NH-76, NHAI’ have reported additional delays of 3 months each; the projects ‘Ganjam-Icchapurum, NH-5, NHAI’ , ‘Balasore Bhadrak KM 136.5 - 199.14 NH-5, NHAI’ and ‘4 Lanning of Ahmedabad to Godhara, NHAI’ have reported additional delays of 3 months each; the projects ‘Salem - U / Undrupet (BOT -1/TN-06) NH -68, NHAI’ and ‘Pimpalgaon-Nasik-Gonde, NH-3 (NHDP-PHASE-III), NHAI’ have reported additional delays of 4 months each; the projects ‘4 Lanning of Godhara to Gujarat/MP Border, NHAI’ and ‘Bhubaneswar to Puri, NHAI’ have reported additional delays of 4 months each; the projects ‘Sonapur to Guwahti (AS-3), NHAI’ , ‘Ghaziabad-Aligarh NH-91, NHAI’ and ‘Chambal Bridge, NH-76 (RJ-5), NHAI’ have reported additional delays of 7, 10 and 11 months respectively; the projects ‘4-Laning of Faraka-Raiganj, NHAI’ and ‘4-Laning of Brahmapore-Faraka, NHAI’ have reported additional delays of 16 months each;

the project '4-Laning of Raiganj-Dalkola, NHAI' has reported additional delay of 28 months. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, delay in shifting of utility, poor performance of contractor, etc.


11. The status as on 31.08.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

## EXECUTIVE SUMMARY

| Sl.No. | Sector                      | Projects on Monitor | Projects Additionally Delayed |
|--------|-----------------------------|---------------------|-------------------------------|
| 1      | Railways                    | 283                 | 2                             |
| 2      | Road Transport And Highways | 152                 | 19                            |
| 3      | Power                       | 99                  | 7                             |
| 4      | Petroleum                   | 84                  | 9                             |
| 5      | Coal                        | 55                  | 0                             |
| 6      | Shipping And Ports          | 19                  | 3                             |
| 7      | Steel                       | 18                  | 4                             |
| 8      | Telecommunications          | 13                  | 0                             |
| 9      | Civil Aviation              | 8                   | 0                             |
| 10     | Atomic Energy               | 4                   | 0                             |
| 11     | Urban Development           | 4                   | 0                             |
| 12     | Petrochemicals              | 1                   | 0                             |
| 13     | Water Resources             | 1                   | 0                             |
|        | Total                       | 741                 | 44                            |

Sectoral break up of on-going infrastructure projects.

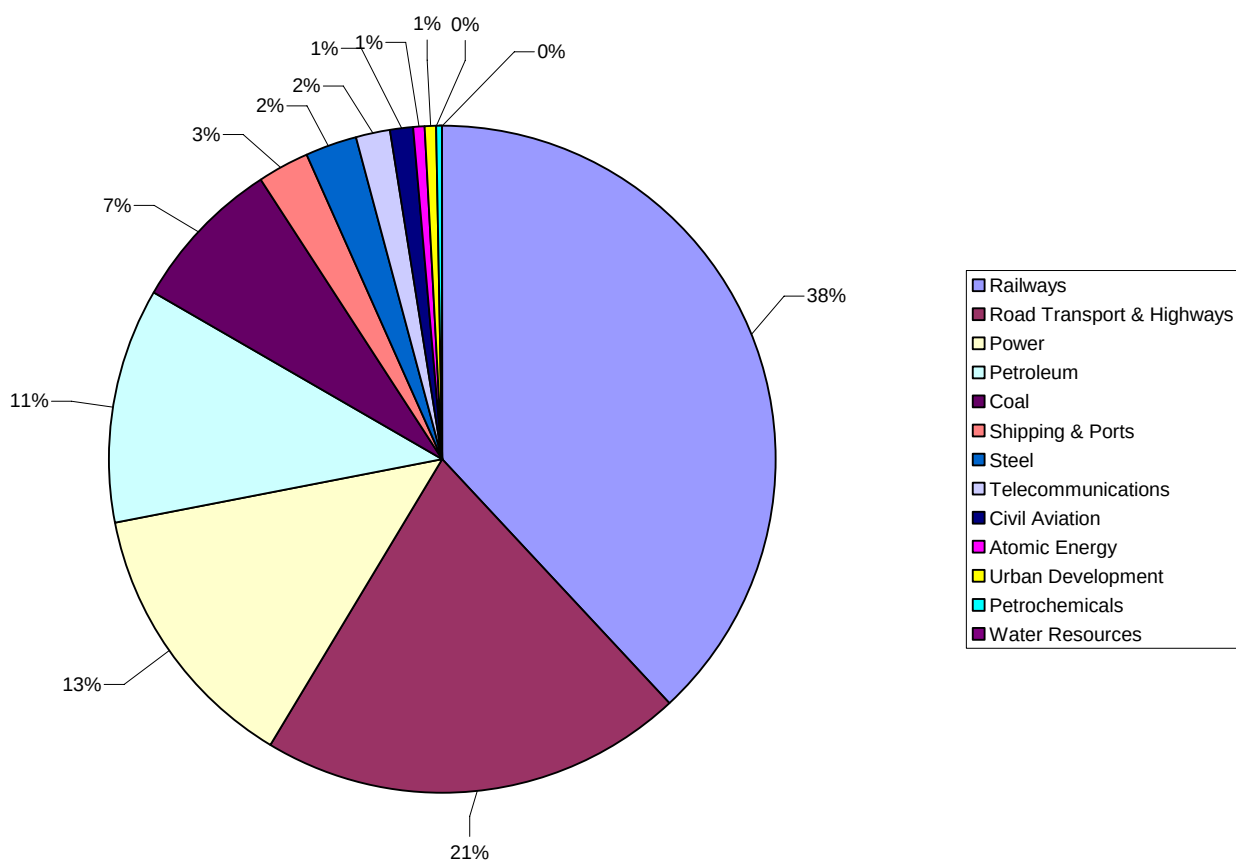

| Month wise List of Completed Projects Costing Rs. 150 crore and above during |                                                                                                           |                           |                                |                                    |
|------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------|---------------------------|--------------------------------|------------------------------------|
| 2013-2014                                                                    |                                                                                                           |                           |                                |                                    |
| Sl. No                                                                       | Project Name                                                                                              | Original Cost (Rs. crore) | Original Date of commissioning | Cumulative Expenditure (Rs. crore) |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | April,2013                                                                                                |                           |                                |                                    |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Power</u>                                                                                              |                           |                                |                                    |
| 1                                                                            | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]   | 209.78                    | 08/2013                        | 52.2                               |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Railways</u>                                                                                           |                           |                                |                                    |
| 2                                                                            | REINGUNTA-GUNTAKAL(RE)(RAIL VIKAS NIGAM LTD.) - [220100260]                                               | 168.34                    | 04/2003                        | 343.36                             |
| 3                                                                            | BILASPUR-URKURA (DL)(RAIL VIKAS NIGAM LTD.) - [220100321]                                                 | 151.52                    | -                              | 315                                |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | May,2013                                                                                                  |                           |                                |                                    |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Fertilisers</u>                                                                                        |                           |                                |                                    |
| 4                                                                            | NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT(NATIONAL FERTILISER LIMITED) - [N08000006]                       | 1,478.63                  | 01/2013                        | 1133                               |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Power</u>                                                                                              |                           |                                |                                    |
| 5                                                                            | 765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068] | 1,347.32                  | 02/2012                        | 1206.1                             |
| 6                                                                            | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078] | 1,736.36                  | 06/2012                        | 1240.75                            |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Road Transport And Highways</u>                                                                        |                           |                                |                                    |
| 7                                                                            | ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]     | 340.68                    | 03/2008                        | 400.56                             |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | June,2013                                                                                                 |                           |                                |                                    |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Railways</u>                                                                                           |                           |                                |                                    |
| 8                                                                            | PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000027]                        | 240.00                    | 03/2009                        | 334.59                             |
| 9                                                                            | PANSPURA-KHARAGPUR 3D LINE(RAIL VIKAS NIGAM LTD.) - [N22000076]                                           | 252.50                    | 02/2010                        | 249.36                             |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | July,2013                                                                                                 |                           |                                |                                    |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Petroleum</u>                                                                                          |                           |                                |                                    |
| 10                                                                           | North Tapti Gas Field Development(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]                    | 589.70                    | 03/2011                        | 912.53                             |
|                                                                              |                                                                                                           |                           |                                |                                    |
|                                                                              | <u>Power</u>                                                                                              |                           |                                |                                    |

# Month wise List of Completed Projects Costing Rs. 150 crore and above during

2013-2014

| Sl. No | Project Name                                                                                                       | Original Cost<br>(Rs. crore) | Original Date of<br>commissioning | Cumulative<br>Expenditure<br>(Rs. crore) |
|--------|--------------------------------------------------------------------------------------------------------------------|------------------------------|-----------------------------------|------------------------------------------|
| 11     | TEESTA LOW DAM STAGE III HYDROELECTRIC POWER<br>PROJE(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) -<br>[180100222]  | 768.92                       | 03/2007                           | 1467.53                                  |
| 12     | CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)(NATIONAL HYDRO-<br>ELECTRIC POWER CORPORATION) - [N18000007]                  | 621.26                       | 02/2011                           | 731.93                                   |
|        |                                                                                                                    |                              |                                   |                                          |
|        | August,2013                                                                                                        |                              |                                   |                                          |
| 13     | INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND<br>B(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000089] | 160.32                       | 10/2012                           | 87.63                                    |
|        |                                                                                                                    |                              |                                   |                                          |
|        | <u>Railways</u>                                                                                                    |                              |                                   |                                          |
| 14     | Madurai-Rameswaram-GC(SOUTHERN RAILWAY) - [N22000200]                                                              | 240.00                       | -                                 | 367.21                                   |
| 15     | Krishnanagar-Bethua Dahri doubling(EASTERN RAILWAYS) - [N22000226]                                                 | 151.65                       | 03/2015                           | 90.21                                    |
| 16     | Dharmavaram-Pakala GC(SAOUTH COST RAILWAY) - [N22000284]                                                           | 294.99                       | -                                 | 658.53                                   |
|        |                                                                                                                    |                              |                                   |                                          |
|        |                                                                                                                    |                              |                                   |                                          |
|        |                                                                                                                    |                              |                                   |                                          |


## Summary of projects in the Flash Report for the month of August, 2013

### Project Implementation - Current Status:

|                                                              |     |
|--------------------------------------------------------------|-----|
| Number of Projects in Previous Month                         | 694 |
| Number of Projects completed/dropped/frozen in Current Month | 4   |
| Number of Projects Added in Current Month                    | 51  |
| Number of Projects in Current Month                          | 741 |


### Brief Analysis

**Project Status with respect to Original Schedule:** Out of 741 projects, 4 projects are ahead of schedule, 146 projects are on schedule and 302 projects are delayed. Of the balance, 262 projects do not have fixed dates of commissioning while 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

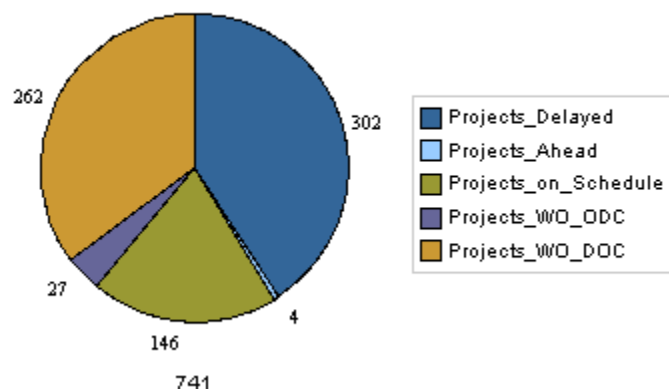

### Investment Scenario

The Total Original cost of implementation of 741 projects when sanctioned, was of the order of Rs. 912567.98 crore but this was subsequently revised to Rs. 1087065.02 crore implying a cost overrun of 19.1%. The expenditure incurred on these projects till August, 2013 is Rs. 503192.4 crore, which is 46.3% of the revised cost of the projects.

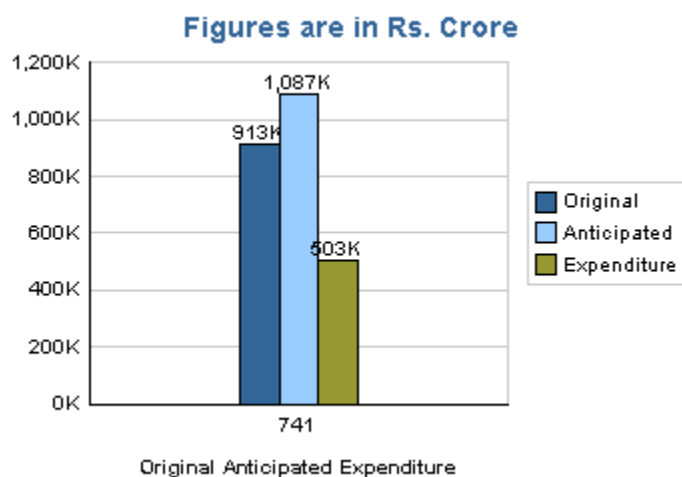

## Projects Added / Completed / Dropped / Frozen

|                                                          |     |
|----------------------------------------------------------|-----|
| No of Projects in Previous Month                         | 694 |
| No of Projects Completed/Dropped/Frozen in Current Month | 4   |
| No of Projects added in Current Month                    | 51  |
| No of Projects in Current Month                          | 741 |

| Project status           |         |       |             |                               |               |       |                      |
|--------------------------|---------|-------|-------------|-------------------------------|---------------|-------|----------------------|
| Number of Projects       |         |       |             |                               |               |       |                      |
| With Respect To          | Delayed | Ahead | On schedule | Without ODC but DOC available | Without D.O.C | Total | Delayed Projects (%) |
| Original ( Date )        | 302     | 4     | 146         | 27                            | 262           | 741   | 40.76                |
| Latest Approved ( Date ) | 291     | 5     | 156         | 27                            | 262           | 741   | 39.27                |

| Project cost                          |                 |                 |                  |                  |                               |            |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|------------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |            |       |
| Cost overrun                          |                 |                 |                  |                  |                               |            |       |
| With Respect to                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore   | %     |
| Original ( OCE )                      | 587             | 778,509.20      | 825,300.56       | 350,446.23       | 42.50                         | 46,791.36  | 6.00  |
| Latest Approved ( RCE )               | 154             | 203,300.63      | 261,764.46       | 152,746.17       | 58.40                         | 58,463.83  | 28.80 |
| Total ( RCE )                         | 741             | 981,809.83      | 1,087,065.02     | 503,192.40       | 46.29                         | 105255.19  | 10.72 |
| Original Cost of All Projects         |                 |                 |                  |                  |                               |            |       |
| Original Cost                         | 741             | 912,567.98      | 1,087,065.02     | 503,192.40       | 46.30                         | 174,497.04 | 19.10 |

| Delayed Project cost                  |                 |                 |                  |                  |                               |            |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|------------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |            |       |
| Cost overrun                          |                 |                 |                  |                  |                               |            |       |
| With Respect to                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore   | %     |
| Original (OCE)                        | 302             | 491,331.26      | 595,539.07       | 375,635.13       | 63.10                         | 104,207.81 | 21.20 |
| Latest Approved (RCE)                 | 291             | 510,862.54      | 572,713.21       | 365,629.96       | 63.80                         | 61,850.67  | 12.10 |

| Additional Delayed Project cost       |                 |                 |                  |                  |                               |          |       |
|---------------------------------------|-----------------|-----------------|------------------|------------------|-------------------------------|----------|-------|
| (All Cost/ Expenditure in Rs. crore ) |                 |                 |                  |                  |                               |          |       |
| Cost overrun                          |                 |                 |                  |                  |                               |          |       |
| With Respect to                       | No. of Projects | Sanctioned Cost | Anticipated Cost | Expenditure Cost | % cost w.r.t anticipated cost | Rs crore | %     |
| Latest Approved                       | 44              | 49,253.05       | 57,957.51        | 49,340.51        | 85.10                         | 8,704.46 | 17.70 |

## Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore )

|       |                             |                 |               |                  |                  | Projects with cost overrun |               |                  |                  |
|-------|-----------------------------|-----------------|---------------|------------------|------------------|----------------------------|---------------|------------------|------------------|
| Sl.No | Sector                      | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                        | Original Cost | Anticipated Cost | Cost overrun (%) |
| 1     | Atomic Energy               | 4               | 40,442.0      | 46,726.0         | 15.5             | 2                          | 16,663.0      | 22,947.0         | 37.7             |
| 2     | Civil Aviation              | 8               | 6,035.5       | 6,625.0          | 9.8              | 2                          | 3,750.5       | 4,340.0          | 15.7             |
| 3     | Coal                        | 55              | 38,127.1      | 41,212.5         | 8.1              | 7                          | 8,579.5       | 12,262.6         | 42.9             |
| 4     | Steel                       | 18              | 65,625.2      | 71,782.4         | 9.4              | 6                          | 24,028.9      | 30,216.1         | 25.7             |
| 5     | Petrochemicals              | 1               | 5,460.6       | 8,920.0          | 63.4             | 1                          | 5,460.6       | 8,920.0          | 63.4             |
| 6     | Petroleum                   | 84              | 184,108.8     | 198,495.5        | 7.8              | 24                         | 58,175.9      | 78,668.0         | 35.2             |
| 7     | Power                       | 99              | 254,014.6     | 273,611.0        | 7.7              | 20                         | 52,742.1      | 72,338.5         | 37.2             |
| 8     | Railways                    | 283             | 147,446.3     | 258,415.1        | 75.3             | 140                        | 62,375.6      | 173,538.9        | 178.2            |
| 9     | Road Transport And Highways | 152             | 105,203.5     | 107,142.2        | 1.8              | 11                         | 3,324.3       | 5,445.2          | 63.8             |
| 10    | Shipping And Ports          | 19              | 15,617.1      | 17,902.4         | 14.6             | 9                          | 8,629.0       | 11,218.5         | 30.0             |
| 11    | Telecommunications          | 13              | 5,699.2       | 5,527.9          | -3.0             | 3                          | 1,394.0       | 1,481.5          | 6.3              |
| 12    | Urban Development           | 4               | 44,245.2      | 49,518.1         | 11.9             | 2                          | 6,509.2       | 11,782.1         | 81.0             |
| 13    | Water Resources             | 1               | 542.9         | 1,187.0          | 118.6            | 1                          | 542.9         | 1,187.0          | 118.6            |
|       |                             |                 |               |                  |                  |                            |               |                  |                  |
| Total |                             | 741             | 912,568.0     | 1,087,065.0      | 19.1             | 228                        | 252,175.3     | 434,345.3        | 72.2             |



## Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

|              |                   |                 |                  |                    |                  | Projects with cost overrun |                  |                  |                  |
|--------------|-------------------|-----------------|------------------|--------------------|------------------|----------------------------|------------------|------------------|------------------|
| Sl.No        | State             | No. of Projects | Original Cost    | Anticipated Cost   | Cost overrun (%) | No.                        | Original Cost    | Anticipated Cost | Cost overrun (%) |
| 1            | Andhra Pradesh    | 46              | 37,404.6         | 45,444.3           | 21.5             | 15                         | 13,556.4         | 22,463.1         | 65.7             |
| 2            | Arunachal Pradesh | 4               | 9,512.2          | 17,330.3           | 82.2             | 4                          | 9,512.2          | 17,330.3         | 82.2             |
| 3            | Assam             | 41              | 24,155.5         | 38,429.7           | 59.1             | 14                         | 10,762.0         | 25,130.3         | 133.5            |
| 4            | Bihar             | 46              | 32,579.0         | 41,019.1           | 25.9             | 17                         | 13,347.2         | 21,803.6         | 63.4             |
| 5            | Goa               | 1               | 335.6            | 335.6              | 0.0              | 0                          | 0.0              | 0.0              | 0.0              |
| 6            | Gujarat           | 34              | 38,828.1         | 39,875.2           | 2.7              | 6                          | 2,776.3          | 4,230.6          | 52.4             |
| 7            | Haryana           | 10              | 4,741.4          | 6,424.0            | 35.5             | 2                          | 1,298.8          | 2,981.4          | 129.5            |
| 8            | Himachal Pradesh  | 6               | 14,402.5         | 20,285.8           | 40.8             | 5                          | 12,355.4         | 18,238.8         | 47.6             |
| 9            | Jammu and Kashmir | 9               | 14,305.7         | 33,912.6           | 137.1            | 5                          | 7,245.2          | 26,852.1         | 270.6            |
| 10           | Karnataka         | 37              | 53,868.0         | 63,787.7           | 18.4             | 12                         | 10,176.5         | 20,589.1         | 102.3            |
| 11           | Kerala            | 10              | 21,010.6         | 22,804.1           | 8.5              | 3                          | 4,295.7          | 6,089.2          | 41.8             |
| 12           | Madhya pradesh    | 22              | 31,749.1         | 32,975.5           | 3.9              | 5                          | 3,317.9          | 4,963.7          | 49.6             |
| 13           | Maharashtra       | 56              | 95,785.3         | 109,495.3          | 14.3             | 17                         | 33,052.5         | 49,221.5         | 48.9             |
| 14           | Manipur           | 1               | 727.6            | 4,453.5            | 512.1            | 1                          | 727.6            | 4,453.5          | 512.1            |
| 15           | Meghalaya         | 3               | 4,845.0          | 4,845.0            | 0.0              | 0                          | 0.0              | 0.0              | 0.0              |
| 16           | Mizoram           | 2               | 1,533.0          | 3,298.0            | 115.1            | 1                          | 619.3            | 2,384.3          | 285.0            |
| 17           | Nagaland          | 2               | 5,124.0          | 6,715.5            | 31.1             | 1                          | 850.0            | 2,441.5          | 187.2            |
| 18           | Odisha            | 31              | 56,321.5         | 63,614.3           | 12.9             | 13                         | 32,821.5         | 40,114.2         | 22.2             |
| 19           | Punjab            | 6               | 2,212.6          | 3,154.4            | 42.6             | 2                          | 532.4            | 1,474.2          | 176.9            |
| 20           | Rajasthan         | 25              | 25,256.6         | 25,682.6           | 1.7              | 7                          | 2,725.5          | 3,637.6          | 33.5             |
| 21           | Sikkim            | 2               | 1,648.9          | 3,690.0            | 123.8            | 1                          | 1,339.5          | 3,380.6          | 152.4            |
| 22           | Tamil Nadu        | 41              | 53,242.8         | 68,268.9           | 28.2             | 20                         | 30,760.3         | 45,786.4         | 48.8             |
| 23           | Tripura           | 5               | 2,669.4          | 4,358.5            | 63.3             | 3                          | 2,129.4          | 3,852.8          | 80.9             |
| 24           | Uttar Pradesh     | 30              | 22,605.7         | 27,184.9           | 20.3             | 10                         | 3,831.0          | 8,458.5          | 120.8            |
| 25           | West Bengal       | 34              | 48,504.9         | 60,026.9           | 23.8             | 16                         | 24,742.5         | 36,264.5         | 46.6             |
| 26           | Chandigarh        | 1               | 452.0            | 452.0              | 0.0              | 0                          | 0.0              | 0.0              | 0.0              |
| 27           | Delhi             | 6               | 38,669.3         | 38,649.7           | -0.1             | 0                          | 0.0              | 0.0              | 0.0              |
| 28           | Chhatisgarh       | 24              | 58,278.3         | 59,362.9           | 1.9              | 5                          | 1,396.8          | 2,481.4          | 77.6             |
| 29           | Jharkhand         | 26              | 15,873.2         | 20,137.5           | 26.9             | 8                          | 2,534.9          | 6,971.0          | 175.0            |
| 30           | Uttarakhand       | 6               | 7,844.0          | 10,199.3           | 30.0             | 4                          | 5,839.0          | 8,194.3          | 40.3             |
| 31           | Multi State       | 174             | 188,081.5        | 210,851.9          | 12.1             | 31                         | 19,629.6         | 44,556.7         | 127.0            |
|              |                   |                 |                  |                    |                  |                            |                  |                  |                  |
| <b>Total</b> |                   | <b>741</b>      | <b>912,568.0</b> | <b>1,087,065.0</b> | <b>19.1</b>      | <b>228</b>                 | <b>252,175.3</b> | <b>434,345.3</b> | <b>72.2</b>      |

## Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

|       |                             |                 |               |                  |                  | Projects with time overruns |               |                  |                            |
|-------|-----------------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|----------------------------|
| Sl.No | Sector                      | No. of Projects | Original Cost | Anticipated Cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | Atomic Energy               | 4               | 40,442.0      | 46,726.0         | 15.5             | 4                           | 40,442.0      | 46,726.0         | 3 - 66                     |
| 2     | Civil Aviation              | 8               | 6,035.5       | 6,625.0          | 9.8              | 2                           | 645.1         | 645.1            | 16 - 47                    |
| 3     | Coal                        | 55              | 38,127.1      | 41,212.5         | 8.1              | 28                          | 24,633.8      | 28,090.6         | 12 - 72                    |
| 4     | Steel                       | 18              | 65,625.2      | 71,782.4         | 9.4              | 14                          | 64,438.3      | 70,505.9         | 8 - 47                     |
| 5     | Petrochemicals              | 1               | 5,460.6       | 8,920.0          | 63.4             | 1                           | 5,460.6       | 8,920.0          | 20 - 20                    |
| 6     | Petroleum                   | 84              | 184,108.8     | 198,495.5        | 7.8              | 54                          | 132,039.2     | 147,186.9        | 1 - 94                     |
| 7     | Power                       | 99              | 254,014.6     | 273,611.0        | 7.7              | 51                          | 125,860.1     | 143,356.7        | 1 - 106                    |
| 8     | Railways                    | 283             | 147,446.3     | 258,415.1        | 75.3             | 36                          | 25,876.7      | 75,224.3         | 3 - 240                    |
| 9     | Road Transport And Highways | 152             | 105,203.5     | 107,142.2        | 1.8              | 100                         | 60,272.7      | 62,184.4         | 2 - 115                    |
| 10    | Shipping And Ports          | 19              | 15,617.1      | 17,902.4         | 14.6             | 5                           | 6,002.6       | 7,254.7          | 5 - 93                     |
| 11    | Telecommunications          | 13              | 5,699.2       | 5,527.9          | -3.0             | 6                           | 3,166.2       | 2,950.5          | 28 - 74                    |
| 12    | Urban Development           | 4               | 44,245.2      | 49,518.1         | 11.9             | 1                           | 2,494.0       | 2,494.0          | 8 - 8                      |
| 13    | Water Resources             | 1               | 542.9         | 1,187.0          | 118.6            | 0                           | 0.0           | 0.0              | -                          |
| Total |                             | 741             | 912,568.0     | 1,087,065.0      | 19.1             | 302                         | 491,331.3     | 595,539.1        |                            |

## Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

|       |                   |                 |               |                  |                  | Projects with time overruns |               |                  |                            |
|-------|-------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|----------------------------|
| Sl.No | State             | No. of Projects | Original Cost | Anticipated cost | Cost overrun (%) | No.                         | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | Andhra Pradesh    | 46              | 37,404.6      | 45,444.3         | 21.5             | 10                          | 16,303.5      | 20,388.9         | 4 - 47                     |
| 2     | Arunachal Pradesh | 4               | 9,512.2       | 17,330.3         | 82.2             | 3                           | 9,356.2       | 16,923.9         | 25 - 87                    |
| 3     | Assam             | 41              | 24,155.5      | 38,429.7         | 59.1             | 36                          | 22,277.8      | 35,722.7         | 3 - 105                    |
| 4     | Bihar             | 46              | 32,579.0      | 41,019.1         | 25.9             | 12                          | 20,814.3      | 25,494.6         | 2 - 98                     |
| 5     | Goa               | 1               | 335.6         | 335.6            | 0.0              | 1                           | 335.6         | 335.6            | 16 - 16                    |
| 6     | Gujarat           | 34              | 38,828.1      | 39,875.2         | 2.7              | 11                          | 24,987.1      | 25,008.7         | 4 - 24                     |
| 7     | Haryana           | 10              | 4,741.4       | 6,424.0          | 35.5             | 4                           | 2,216.6       | 3,396.6          | 7 - 50                     |
| 8     | Himachal Pradesh  | 6               | 14,402.5      | 20,285.8         | 40.8             | 4                           | 12,798.3      | 16,543.6         | 26 - 106                   |
| 9     | Jammu and Kashmir | 9               | 14,305.7      | 33,912.6         | 137.1            | 7                           | 13,038.7      | 32,618.8         | 10 - 181                   |
| 10    | Karnataka         | 37              | 53,868.0      | 63,787.7         | 18.4             | 12                          | 19,346.4      | 19,349.1         | 8 - 179                    |
| 11    | Kerala            | 10              | 21,010.6      | 22,804.1         | 8.5              | 5                           | 19,581.0      | 20,231.0         | 5 - 58                     |
| 12    | Madhya pradesh    | 22              | 31,749.1      | 32,975.5         | 3.9              | 10                          | 4,919.6       | 5,046.3          | 2 - 69                     |
| 13    | Maharashtra       | 56              | 95,785.3      | 109,495.3        | 14.3             | 26                          | 44,594.4      | 52,325.7         | 5 - 129                    |
| 14    | Manipur           | 1               | 727.6         | 4,453.5          | 512.1            | 1                           | 727.6         | 4,453.5          | 72 - 72                    |
| 15    | Meghalaya         | 3               | 4,845.0       | 4,845.0          | 0.0              | 0                           | 0.0           | 0.0              | -                          |
| 16    | Mizoram           | 2               | 1,533.0       | 3,298.0          | 115.1            | 2                           | 1,533.0       | 3,298.0          | 7 - 35                     |
| 17    | Nagaland          | 2               | 5,124.0       | 6,715.5          | 31.1             | 1                           | 850.0         | 2,441.5          | 24 - 24                    |
| 18    | Odisha            | 31              | 56,321.5      | 63,614.3         | 12.9             | 20                          | 52,044.1      | 55,413.4         | 4 - 138                    |
| 19    | Punjab            | 6               | 2,212.6       | 3,154.4          | 42.6             | 2                           | 989.0         | 1,064.0          | 13 - 64                    |
| 20    | Rajasthan         | 25              | 25,256.6      | 25,682.6         | 1.7              | 8                           | 16,423.9      | 15,977.6         | 3 - 64                     |
| 21    | Sikkim            | 2               | 1,648.9       | 3,690.0          | 123.8            | 2                           | 1,648.9       | 3,690.0          | 15 - 47                    |
| 22    | Tamil Nadu        | 41              | 53,242.8      | 68,268.9         | 28.2             | 15                          | 34,552.5      | 43,919.7         | 6 - 93                     |
| 23    | Tripura           | 5               | 2,669.4       | 4,358.5          | 63.3             | 3                           | 1,996.4       | 3,145.7          | 19 - 96                    |
| 24    | Uttar Pradesh     | 30              | 22,605.7      | 27,184.9         | 20.3             | 15                          | 14,533.6      | 17,278.5         | 9 - 84                     |
| 25    | West Bengal       | 34              | 48,504.9      | 60,026.9         | 23.8             | 10                          | 21,899.1      | 27,322.0         | 3 - 141                    |
| 26    | Chandigarh        | 1               | 452.0         | 452.0            | 0.0              | 0                           | 0.0           | 0.0              | -                          |
| 27    | Delhi             | 6               | 38,669.3      | 38,649.7         | -0.1             | 1                           | 2,494.0       | 2,494.0          | 8 - 8                      |
| 28    | Chhatisgarh       | 24              | 58,278.3      | 59,362.9         | 1.9              | 10                          | 25,204.4      | 25,515.7         | 4 - 59                     |
| 29    | Jharkhand         | 26              | 15,873.2      | 20,137.5         | 26.9             | 10                          | 9,422.6       | 9,529.2          | 9 - 60                     |
| 30    | Uttarakhand       | 6               | 7,844.0       | 10,199.3         | 30.0             | 4                           | 6,097.2       | 8,228.1          | 5 - 54                     |
| 31    | Multi State       | 174             | 188,081.5     | 210,851.9        | 12.1             | 57                          | 90,345.5      | 98,382.6         | 1 - 240                    |
|       |                   |                 |               |                  |                  |                             |               |                  |                            |
| Total |                   | 741             | 912,568.0     | 1,087,065.0      | 19.1             | 302                         | 491,331.3     | 595,539.1        |                            |

## Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

|       |                             |                 |               |                  |                  | Projects with time overruns |               |                  |                            |
|-------|-----------------------------|-----------------|---------------|------------------|------------------|-----------------------------|---------------|------------------|----------------------------|
| Sl.No | Sector                      | No. of Projects | Original Cost | Anticipated Cost | Cost overrun (%) | No.                         | Original cost | Anticipated Cost | Range of T.O.R (in months) |
| 1     | Atomic Energy               | 4               | 40,442.0      | 46,726.0         | 15.5             | 4                           | 40,442.0      | 46,726.0         | 3 - 66                     |
| 2     | Civil Aviation              | 8               | 6,035.5       | 6,625.0          | 9.8              | 2                           | 645.1         | 645.1            | 16 - 47                    |
| 3     | Coal                        | 55              | 38,127.1      | 41,212.5         | 8.1              | 28                          | 24,633.8      | 28,090.6         | 12 - 72                    |
| 4     | Steel                       | 18              | 65,625.2      | 71,782.4         | 9.4              | 12                          | 62,967.8      | 69,035.3         | 8 - 47                     |
| 5     | Petrochemicals              | 1               | 5,460.6       | 8,920.0          | 63.4             | 0                           | 0.0           | 0.0              | -                          |
| 6     | Petroleum                   | 84              | 184,108.8     | 198,495.5        | 7.8              | 51                          | 128,063.0     | 138,123.9        | 1 - 94                     |
| 7     | Power                       | 99              | 254,014.6     | 273,611.0        | 7.7              | 51                          | 125,860.1     | 143,356.7        | 1 - 106                    |
| 8     | Railways                    | 283             | 147,446.3     | 258,415.1        | 75.3             | 34                          | 25,361.7      | 73,496.8         | 3 - 240                    |
| 9     | Road Transport And Highways | 152             | 105,203.5     | 107,142.2        | 1.8              | 100                         | 60,272.7      | 62,184.4         | 2 - 115                    |
| 10    | Shipping And Ports          | 19              | 15,617.1      | 17,902.4         | 14.6             | 2                           | 4,728.0       | 5,610.0          | 19 - 48                    |
| 11    | Telecommunications          | 13              | 5,699.2       | 5,527.9          | -3.0             | 6                           | 3,166.2       | 2,950.5          | 28 - 74                    |
| 12    | Urban Development           | 4               | 44,245.2      | 49,518.1         | 11.9             | 1                           | 2,494.0       | 2,494.0          | 8 - 8                      |
| 13    | Water Resources             | 1               | 542.9         | 1,187.0          | 118.6            | 0                           | 0.0           | 0.0              | -                          |
| Total |                             | 741             | 912,568.0     | 1,087,065.0      | 19.1             | 291                         | 478,634.3     | 572,713.2        |                            |

## Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

|        |                             |                 |                      |                  |                  | Projects with cost overruns |                      |                  |                  |
|--------|-----------------------------|-----------------|----------------------|------------------|------------------|-----------------------------|----------------------|------------------|------------------|
| Sl.No. | Sector                      | No. of projects | Latest Approved Cost | Anticipated Cost | Cost overrun (%) | No.                         | Latest Approved Cost | Anticipated Cost | Cost overrun (%) |
| 1      | Atomic Energy               | 4               | 44,541.0             | 46,726.0         | 4.9              | 1                           | 3,492.0              | 5,677.0          | 62.6             |
| 2      | Civil Aviation              | 8               | 6,242.5              | 6,625.0          | 6.1              | 1                           | 1,942.5              | 2,325.0          | 19.7             |
| 3      | Coal                        | 55              | 40,988.6             | 41,212.5         | 0.5              | 5                           | 2,211.1              | 2,694.1          | 21.8             |
| 4      | Steel                       | 18              | 69,847.4             | 71,782.4         | 2.8              | 1                           | 14,443.0             | 16,408.0         | 13.6             |
| 5      | Petrochemicals              | 1               | 8,920.0              | 8,920.0          | 0.0              | 0                           | 0.0                  | 0.0              | 0.0              |
| 6      | Petroleum                   | 84              | 198,338.5            | 198,495.5        | 0.1              | 9                           | 32,985.2             | 37,291.3         | 13.1             |
| 7      | Power                       | 99              | 258,714.6            | 273,611.0        | 5.8              | 13                          | 43,181.0             | 58,077.4         | 34.5             |
| 8      | Railways                    | 283             | 180,813.0            | 258,415.1        | 42.9             | 110                         | 65,159.1             | 142,915.7        | 119.3            |
| 9      | Road Transport And Highways | 152             | 105,370.0            | 107,142.2        | 1.7              | 11                          | 3,324.3              | 5,445.2          | 63.8             |
| 10     | Shipping And Ports          | 19              | 17,488.0             | 17,902.4         | 2.4              | 5                           | 3,157.6              | 3,783.5          | 19.8             |
| 11     | Telecommunications          | 13              | 5,699.2              | 5,527.9          | -3.0             | 3                           | 1,394.0              | 1,481.5          | 6.3              |
| 12     | Urban Development           | 4               | 44,304.1             | 49,518.1         | 11.8             | 1                           | 6,395.0              | 11,609.0         | 81.5             |
| 13     | Water Resources             | 1               | 542.9                | 1,187.0          | 118.6            | 1                           | 542.9                | 1,187.0          | 118.6            |
|        |                             |                 |                      |                  |                  |                             |                      |                  |                  |
| Total  |                             | 741             | 981,809.8            | 1,087,065.0      | 10.7             | 161                         | 178,227.5            | 288,894.7        | 62.1             |

## Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

|        |                             |                 |               |                  |                  | Projects with time & cost overruns |               |                  |                            |
|--------|-----------------------------|-----------------|---------------|------------------|------------------|------------------------------------|---------------|------------------|----------------------------|
| Sl.No. | Sector                      | No. of projects | Original Cost | Anticipated Cost | Cost Overrun (%) | No.                                | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1      | Atomic Energy               | 4               | 40,442.00     | 46,726.00        | 15.54            | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 2      | Civil Aviation              | 8               | 6,035.46      | 6,624.95         | 9.77             | 1                                  | 1,808.00      | 2,015.00         | 13- 13                     |
| 3      | Coal                        | 55              | 38,127.05     | 41,212.50        | 8.09             | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 4      | Steel                       | 18              | 65,625.22     | 71,782.40        | 9.38             | 2                                  | 8,987.89      | 12,898.17        | 24- 47                     |
| 5      | Petrochemicals              | 1               | 5,460.61      | 8,920.00         | 63.35            | 1                                  | 5,460.61      | 8,920.00         | 20- 20                     |
| 6      | Petroleum                   | 84              | 184,108.78    | 198,495.51       | 7.81             | 11                                 | 20,683.33     | 35,008.63        | 20- 94                     |
| 7      | Power                       | 99              | 254,014.60    | 273,611.01       | 7.71             | 3                                  | 2,827.44      | 5,103.94         | 0- 79                      |
| 8      | Railways                    | 283             | 147,446.28    | 258,415.07       | 75.26            | 15                                 | 5,839.02      | 22,637.08        | 0- 141                     |
| 9      | Road Transport And Highways | 152             | 105,203.54    | 107,142.16       | 1.84             | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 10     | Shipping And Ports          | 19              | 15,617.12     | 17,902.42        | 14.63            | 5                                  | 5,400.70      | 6,860.25         | 10- 93                     |
| 11     | Telecommunications          | 13              | 5,699.24      | 5,527.92         | -3.01            | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 12     | Urban Development           | 4               | 44,245.18     | 49,518.08        | 11.92            | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 13     | Water Resources             | 1               | 542.90        | 1,187.00         | 118.64           | 0                                  | 0.00          | 0.00             | 0- 0                       |
| Total  |                             | 741             | 912567.98     | 1087065.02       | 19.12            | 38                                 | 51006.99      | 93443.07         |                            |

## Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

|        |                             |                 |               |                  |                  | Projects with time & cost overruns |               |                  |                            |
|--------|-----------------------------|-----------------|---------------|------------------|------------------|------------------------------------|---------------|------------------|----------------------------|
| Sl.No. | Sector                      | No. of projects | Original Cost | Anticipated Cost | Cost Overrun (%) | No.                                | Original Cost | Anticipated Cost | Range of T.O.R (in months) |
| 1      | Atomic Energy               | 4               | 40,442.00     | 46,726.00        | 15.54            | 2                                  | 16,663.00     | 22,947.00        | 54- 66                     |
| 2      | Civil Aviation              | 8               | 6,035.46      | 6,624.95         | 9.77             | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 3      | Coal                        | 55              | 38,127.05     | 41,212.50        | 8.09             | 5                                  | 7,938.86      | 11,573.95        | 19- 55                     |
| 4      | Steel                       | 18              | 65,625.22     | 71,782.40        | 9.38             | 5                                  | 23,768.89     | 29,866.43        | 14- 47                     |
| 5      | Petrochemicals              | 1               | 5,460.61      | 8,920.00         | 63.35            | 1                                  | 5,460.61      | 8,920.00         | 20- 20                     |
| 6      | Petroleum                   | 84              | 184,108.78    | 198,495.51       | 7.81             | 19                                 | 54,231.55     | 73,697.33        | 2- 94                      |
| 7      | Power                       | 99              | 254,014.60    | 273,611.01       | 7.71             | 15                                 | 43,928.85     | 61,425.37        | 10- 106                    |
| 8      | Railways                    | 283             | 147,446.28    | 258,415.07       | 75.26            | 31                                 | 22,259.81     | 71,612.36        | 9- 240                     |
| 9      | Road Transport And Highways | 152             | 105,203.54    | 107,142.16       | 1.84             | 10                                 | 3,158.01      | 5,252.10         | 25- 113                    |
| 10     | Shipping And Ports          | 19              | 15,617.12     | 17,902.42        | 14.63            | 3                                  | 4,878.00      | 6,210.00         | 19- 93                     |
| 11     | Telecommunications          | 13              | 5,699.24      | 5,527.92         | -3.01            | 2                                  | 1,065.85      | 1,089.32         | 34- 54                     |
| 12     | Urban Development           | 4               | 44,245.18     | 49,518.08        | 11.92            | 0                                  | 0.00          | 0.00             | 0- 0                       |
| 13     | Water Resources             | 1               | 542.90        | 1,187.00         | 118.64           | 0                                  | 0.00          | 0.00             | 0- 0                       |
| Total  |                             | 741             | 912567.98     | 1087065.02       | 19.12            | 93                                 | 183353.43     | 292593.86        |                            |

| List of projects completed/dropped/Frozen during current month |                                                         |         |          |         |                 |         | (All Cost /Expenditure in Rs. crore ) |
|----------------------------------------------------------------|---------------------------------------------------------|---------|----------|---------|-----------------|---------|---------------------------------------|
|                                                                |                                                         |         | Original |         | Now anticipated |         |                                       |
| Sl.No                                                          | Project                                                 | DOA     | Cost     | DOC     | Cost            | DOC     | Final Expenditure                     |
|                                                                | <u>Power</u>                                            |         |          |         |                 |         |                                       |
| 1                                                              | INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B | 10/2010 | 160.32   | 10/2012 | 160.32          | 08/2013 | 87.63                                 |
|                                                                |                                                         |         |          |         |                 |         |                                       |
|                                                                | <u>Railways</u>                                         |         |          |         |                 |         |                                       |
| 2                                                              | Madurai-Rameswaram-GC                                   | 04/1999 | 240.00   | N.A.    | 441.69          | N.A.    | 367.21                                |
| 3                                                              | Krishnanagar-Bethua Dahri doubling                      | 04/2009 | 151.65   | 03/2015 | 151.65          | 03/2015 | 90.21                                 |
| 4                                                              | Dharmavaram-Pakala GC                                   | 04/1997 | 294.99   | N.A.    | 704.11          | N.A.    | 658.53                                |
|                                                                |                                                         |         |          |         |                 |         |                                       |

| List of projects added |                                                           |        |          |         | (All Cost in Rs. crore ) |         |
|------------------------|-----------------------------------------------------------|--------|----------|---------|--------------------------|---------|
|                        |                                                           |        | Original |         | Anticipated              |         |
| Sl.No                  | Project                                                   | DOA    | Cost     | DOC     | Cost                     | DOC     |
|                        |                                                           |        |          |         |                          |         |
|                        | <u>Petroleum</u>                                          |        |          |         |                          |         |
| 1                      | Purchase of 2 Nos. of 2000 HP Drilling Rig                | 4/2010 | 270.00   | 12/2014 | 270.00                   | 12/2014 |
| 2                      | CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY | 8/2006 | 374.56   | 9/2012  | 374.56                   | 10/2016 |
|                        |                                                           |        |          |         |                          |         |
|                        | <u>Power</u>                                              |        |          |         |                          |         |
| 3                      | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV           | 9/2013 | 680.69   | 3/2016  | 680.69                   | 3/2016  |
| 4                      | Transmission System associated with Mauda Stage-II        | 9/2013 | 1,575.30 | 5/2016  | 1,575.30                 | 5/2016  |
|                        |                                                           |        |          |         |                          |         |
|                        | <u>Railways</u>                                           |        |          |         |                          |         |
| 5                      | PEN ROHA DOUBLING                                         | 4/2007 | 203.00   | /       | 203.00                   | -       |
| 6                      | PANVEL PEN DOUBLING                                       | 4/2006 | 191.00   | /       | 191.00                   | 12/2013 |
| 7                      | Tumkur-Chitradurga-Davengere NL                           | 4/2011 | 913.00   | /       | 913.00                   | -       |
| 8                      | Munirabad (gingera) -Raichur NL                           | 4/2007 | 179.65   | /       | 645.00                   | -       |
| 9                      | Bagalkot-Kudachi NL                                       | 4/2010 | 377.93   | /       | 377.93                   | -       |



| List of projects added |                                                              |        |          |        | (All Cost in Rs. crore) |         |
|------------------------|--------------------------------------------------------------|--------|----------|--------|-------------------------|---------|
|                        |                                                              |        | Original |        | Anticipated             |         |
| Sl.No                  | Project                                                      | DOA    | Cost     | DOC    | Cost                    | DOC     |
| 10                     | Manuguru-Ramagundam                                          | 4/2013 | 1,112.00 | /      | 1,112.00                | -       |
| 11                     | Kondapalli-Kothagudem                                        | 4/2013 | 723.00   | /      | 723.00                  | -       |
| 12                     | Kazipet-Vijayawada 3rd line with Electrification             | 4/2012 | 1,054.35 | /      | 1,054.35                | -       |
| 13                     | Akola-Khandwa GC Akola-Akot                                  | 4/2008 | 184.26   | /      | 2,000.00                | -       |
| 14                     | Bhadrachalam-Kovvur                                          | 4/2012 | 923.23   | /      | 923.23                  | -       |
| 15                     | Gudur-Durgarajapatnam                                        | 4/2011 | 283.54   | /      | 283.54                  | -       |
| 16                     | Meerut-Muzafarnagar Patch DL                                 | 4/2012 | 289.79   | /      | 289.79                  | -       |
| 17                     | ansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur M | 4/2009 | 396.04   | /      | 396.04                  | -       |
| 18                     | Grade Seperator at Dayabasti                                 | 4/1999 | 159.20   | /      | 159.20                  | -       |
| 19                     | Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareli    | 4/2013 | 654.00   | /      | 654.00                  | -       |
| 20                     | Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar                        | 4/2013 | 1,239.00 | /      | 1,239.00                | -       |
| 21                     | Rohtak-Meham Hansi                                           | 4/2012 | 287.00   | /      | 287.00                  | -       |
| 22                     | Bhanupali-Bilaspur Beri NL                                   | 4/2008 | 1,046.88 | /      | 2,966.99                | -       |
| 23                     | Deoband (Muzaffarnagar)- Roorkee NL                          | 4/2007 | 336.91   | /      | 336.91                  | -       |
| 24                     | Kolar-Chickbalapur GC                                        | 4/2006 | 287.99   | 1/1999 | 287.99                  | 12/2013 |
| 25                     | Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL           | 4/2013 | 558.00   | /      | 558.00                  | -       |
| 26                     | Srinivasa-pura-Madanapalli NL                                | 4/2013 | 296.00   | /      | 296.00                  | -       |
| 27                     | Shimoga-Harihar NL                                           | 4/2011 | 562.74   | /      | 562.74                  | -       |
| 28                     | Rayadurga-Tumkur NL                                          | 4/2007 | 970.34   | /      | 970.34                  | -       |
| 29                     | White Field-Kolar NL                                         | 4/2011 | 341.05   | /      | 341.05                  | -       |
| 30                     | Anand Vihar-Tilak Bridge 3rd and 4th line                    | 4/2012 | 295.68   | /      | 295.68                  | -       |
| 31                     | Cumbum-Proddatur                                             | 4/2013 | 829.00   | /      | 829.00                  | -       |
| 32                     | Mudkhed-Parbhani                                             | 4/2011 | 390.60   | /      | 390.60                  | -       |
| 33                     | Dharmavaram-Pakala GC                                        | 4/1997 | 294.99   | /      | 704.11                  | -       |
| 34                     | Akkannapet-Medak                                             | 4/2012 | 153.00   | /      | 153.00                  | -       |
| 35                     | Nadikude-Sri Kalahasti                                       | 4/2011 | 1,313.48 | /      | 1,313.48                | -       |
| 36                     | Bhadrachalam Road-Sattupalli                                 | 4/2010 | 337.49   | /      | 337.49                  | -       |
| 37                     | Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I               | 4/2008 | 2,050.00 | /      | 2,050.00                | -       |
| 38                     | Haridwar-Laksar                                              | 4/2012 | 219.83   | /      | 444.18                  | -       |
| 39                     | Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh  | 4/2010 | 338.54   | /      | 338.54                  | -       |
| 40                     | Jakhal-Mansa Doubling on SPR Section                         | 4/2008 | 165.65   | /      | 165.65                  | -       |
| 41                     | Hissar-Sirsa via Agroha and Fatehabad                        | 4/2013 | 400.00   | /      | 400.00                  | -       |
| 42                     | Yamunanagar-Chandigarh via Sadhaura Narayangarh              | 4/2013 | 876.00   | /      | 876.00                  | -       |
| 43                     | Unchahar-Amethi                                              | 4/2012 | 380.00   | /      | 380.00                  | -       |
| 44                     | Qadian-Beas                                                  | 4/2011 | 205.22   | /      | 205.22                  | -       |
| 45                     | Chandigarh-Baddi NL                                          | 4/2007 | 328.14   | /      | 328.14                  | -       |
| 46                     | Hospet-Hubli-Londa-Vascodagama DL                            | 4/2010 | 2,127.00 | /      | 2,127.00                | -       |
| 47                     | Gadag-Wadi NL                                                | 4/2013 | 1,117.00 | /      | 1,117.00                | -       |

| List of projects added |                                          |        |          |         | (All Cost in Rs. crore) |         |
|------------------------|------------------------------------------|--------|----------|---------|-------------------------|---------|
|                        |                                          |        | Original |         | Anticipated             |         |
| Sl.No                  | Project                                  | DOA    | Cost     | DOC     | Cost                    | DOC     |
| 48                     | Chikballa-pur-Gowribidanur NL            | 4/2013 | 327.25   | /       | 327.25                  | -       |
| 49                     | Monigram- Nimita                         | 4/2012 | 250.93   | /       | 250.93                  | -       |
| 50                     | Bazar Sau -Azimganj Jn. doubling         | 4/2012 | 255.64   | /       | 255.64                  | -       |
|                        |                                          |        |          |         |                         |         |
|                        | <u>Road Transport And Highways</u>       |        |          |         |                         |         |
| 51                     | WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 | 6/2013 | 1,287.95 | 11/2015 | 1,287.95                | 11/2015 |
|                        |                                          |        |          |         |                         |         |

| Milestones (Cumulative due & achieved) |      |  |
|----------------------------------------|------|--|
| Total                                  | 3786 |  |
| Achieved up to month                   | 1369 |  |
|                                        |      |  |


## List of projects reporting additional delays

|        |                                                                    | Cost ( Rs.crore) |             | DOC reported |            |            |                   |
|--------|--------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
| Sl. No | Project name                                                       | Original         | Anticipated | Original     | Last month | This month | Delay (in months) |
|        | <u>Steel</u>                                                       |                  |             |              |            |            |                   |
| 1      | EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL    | 8,692.00         | 12,291.00   | 10/2009      | 08/2013    | 09/2013    | 1                 |
| 2      | 67.5 MW TG-5 AUX. SYSTEM EMERGENCY POWER REQUIREMENT RINL          | 230.00           | 343.58      | 02/2011      | 08/2013    | 09/2013    | 1                 |
| 3      | COKE OVEN BATTERY NO. 4 PHASE-II RINL                              | 108.00           | 216.68      | 10/2012      | 09/2013    | 12/2013    | 3                 |
| 4      | Augmentation of Iron Ore Storage in RMHP RINL                      | 480.00           | 450.00      | 05/2012      | 09/2013    | 12/2013    | 3                 |
|        |                                                                    |                  |             |              |            |            |                   |
|        | <u>Petroleum</u>                                                   |                  |             |              |            |            |                   |
| 5      | DEVELOPMENT OF B-46 CLUSTER FIELD ONGC                             | 1,436.21         | 1,436.21    | 07/2010      | 02/2014    | 03/2014    | 1                 |
| 6      | Fluidized catalytic cracking unit(FCCU) revamp IOCL                | 1,000.00         | 1,000.00    | 01/2013      | 10/2013    | 11/2013    | 1                 |
| 7      | BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL                   | 341.50           | 341.50      | 02/2013      | 08/2013    | 09/2013    | 1                 |
| 8      | STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG ISPR                  | 672.00           | 1,038.00    | 10/2011      | 12/2013    | 01/2014    | 1                 |
| 9      | Construction of 23 Immediate Supply Vessels (ISV) ONGC             | 331.20           | 269.10      | 08/2013      | 01/2014    | 03/2014    | 2                 |
| 10     | CENTRAL GAS GATHERING STATION AND OFFTAKE POINT OIL                | 144.02           | 204.29      | 06/2012      | 09/2013    | 12/2013    | 3                 |
| 11     | GAS TURBINE GENERATION SET OIL                                     | 216.88           | 216.88      | 10/2011      | 07/2013    | 12/2013    | 5                 |
| 12     | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II ONGC                        | 7,133.39         | 6,855.93    | 09/2012      | 09/2013    | 03/2014    | 6                 |
| 13     | CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN OIL                      | 126.18           | 159.54      | 06/2012      | 09/2013    | 03/2014    | 6                 |
|        |                                                                    |                  |             |              |            |            |                   |
|        | <u>Power</u>                                                       |                  |             |              |            |            |                   |
| 14     | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX PGCIL               | 182.68           | 182.68      | 01/2013      | 09/2013    | 10/2013    | 1                 |
| 15     | TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI PGCIL           | 2,074.86         | 2,074.86    | 03/2013      | 03/2014    | 05/2014    | 2                 |
| 16     | TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR PGCIL           | 2,743.19         | 2,743.19    | 12/2013      | 03/2014    | 05/2014    | 2                 |
| 17     | TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C PGCIL             | 2,569.25         | 2,569.25    | 03/2014      | 03/2014    | 05/2014    | 2                 |
| 18     | TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED PGCIL     | 425.51           | 425.51      | 10/2013      | 10/2013    | 12/2013    | 2                 |
| 19     | PARBATI HEP (NHPC) II NHPC                                         | 3,919.59         | 5,366.00    | 09/2009      | 03/2018    | 07/2018    | 4                 |
| 20     | TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH PGCIL | 1,366.34         | 1,366.34    | 12/2013      | 12/2013    | 12/2014    | 12                |
|        |                                                                    |                  |             |              |            |            |                   |
|        | <u>Railways</u>                                                    |                  |             |              |            |            |                   |


## List of projects reporting additional delays

| Sl. No | Project name                                                       | Cost ( Rs.crore) |             | DOC reported |            |            | Delay (in months) |
|--------|--------------------------------------------------------------------|------------------|-------------|--------------|------------|------------|-------------------|
|        |                                                                    | Original         | Anticipated | Original     | Last month | This month |                   |
| 21     | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg NEFR            | 1,676.31         | 5,000.00    | 03/2009      | 03/2014    | 12/2014    | 9                 |
| 22     | Champajharan-Bimalgarh Doubling extension SER                      | 149.90           | 177.38      | 03/2015      | 03/2015    | 12/2015    | 9                 |
|        | <u>Road Transport And Highways</u>                                 |                  |             |              |            |            |                   |
| 23     | Jaipur-Tonk-Deoli NHAI                                             | 792.06           | 792.06      | 12/2012      | 08/2013    | 09/2013    | 1                 |
| 24     | Haveri-Harihar (GQ) KM.340-KM.284 (NH-4) NHAI                      | 241.00           | 196.65      | 08/2004      | 08/2013    | 10/2013    | 2                 |
| 25     | Harihar-Chitradurga (GQ) KM.284-KM.207 (NH-4) NHAI                 | 318.00           | 207.56      | 08/2004      | 08/2013    | 10/2013    | 2                 |
| 26     | NEW Mangalore Port NH-17 AND 48 NHAI                               | 196.50           | 196.50      | 06/2011      | 08/2013    | 10/2013    | 2                 |
| 27     | Sunakhala-Ganjam (GQ) KM.338-KM.284 (NH-5) NHAI                    | 225.00           | 241.53      | 04/2004      | 06/2013    | 09/2013    | 3                 |
| 28     | Kota Bypass,RJ-4, NH-76 (NHAI) NHAI                                | 275.00           | 250.39      | 10/2008      | 09/2013    | 12/2013    | 3                 |
| 29     | Ganjam-ICchapurum,NH-5(NHAI) NHAI                                  | 263.27           | 263.27      | 02/2004      | 06/2013    | 09/2013    | 3                 |
| 30     | Balasore Bhadrak (Revived) KM 136.5 - 199.14 NH-5 NHAI             | 228.70           | 228.70      | 02/2004      | 06/2013    | 09/2013    | 3                 |
| 31     | 4 Lanning of Ahmedabad to Godhara NHAI                             | 1,008.50         | 1,008.50    | 06/2013      | 09/2013    | 12/2013    | 3                 |
| 32     | Salem - U / Undrupet(BOT -1/TN-06) NH -68 NHAI                     | 941.00           | 941.00      | 01/2011      | 08/2013    | 12/2013    | 4                 |
| 33     | Pimpalgaon-Nasik-Gonde, NH-3 (NHDP-Phase-III) NHAI                 | 940.00           | 940.00      | 07/2012      | 08/2013    | 12/2013    | 4                 |
| 34     | 4 Lanning of Godhara to Gujarat/MP Border NHAI                     | 785.50           | 785.50      | 08/2013      | 08/2013    | 12/2013    | 4                 |
| 35     | Bhubaneswar to Puri NHAI                                           | 500.29           | 500.29      | 08/2013      | 08/2013    | 12/2013    | 4                 |
| 36     | Sonapur to Guwahati (AS-3) NHAI                                    | 245.00           | 245.00      | 03/2008      | 08/2013    | 03/2014    | 7                 |
| 37     | Ghaziabad-Aligarh NH-91 NHAI                                       | 1,141.00         | 1,141.00    | 08/2013      | 08/2013    | 06/2014    | 10                |
| 38     | Chambal Bridge, NH-76 (RJ-5) NHAI                                  | 275.00           | 281.31      | 02/2010      | 07/2014    | 06/2015    | 11                |
| 39     | 4-laning of Faraka-Raiganj NHAI                                    | 1,078.84         | 1,078.84    | 08/2013      | 08/2013    | 12/2014    | 16                |
| 40     | 4-laning of Brahmapore-Faraka NHAI                                 | 998.79           | 998.79      | 08/2013      | 08/2013    | 12/2014    | 16                |
| 41     | 4-laning of Raiganj-Dalkola NHAI                                   | 580.43           | 580.43      | 08/2013      | 08/2013    | 12/2015    | 28                |
|        | <u>Shipping And Ports</u>                                          |                  |             |              |            |            |                   |
| 42     | Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers SHIPP.   | 612.72           | 532.83      | 12/2012      | 10/2013    | 11/2013    | 1                 |
| 43     | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY SHIPP.          | 359.44           | 359.44      | 04/2011      | 09/2011    | 11/2011    | 2                 |
| 44     | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER MUMBAI PORT TRU | 1,228.00         | 1,460.00    | 12/2010      | 03/2014    | 12/2014    | 9                 |
| 44     |                                                                    |                  |             |              |            |            |                   |

## Graphical Presentation of All Projects w.r.t. Original Schedule

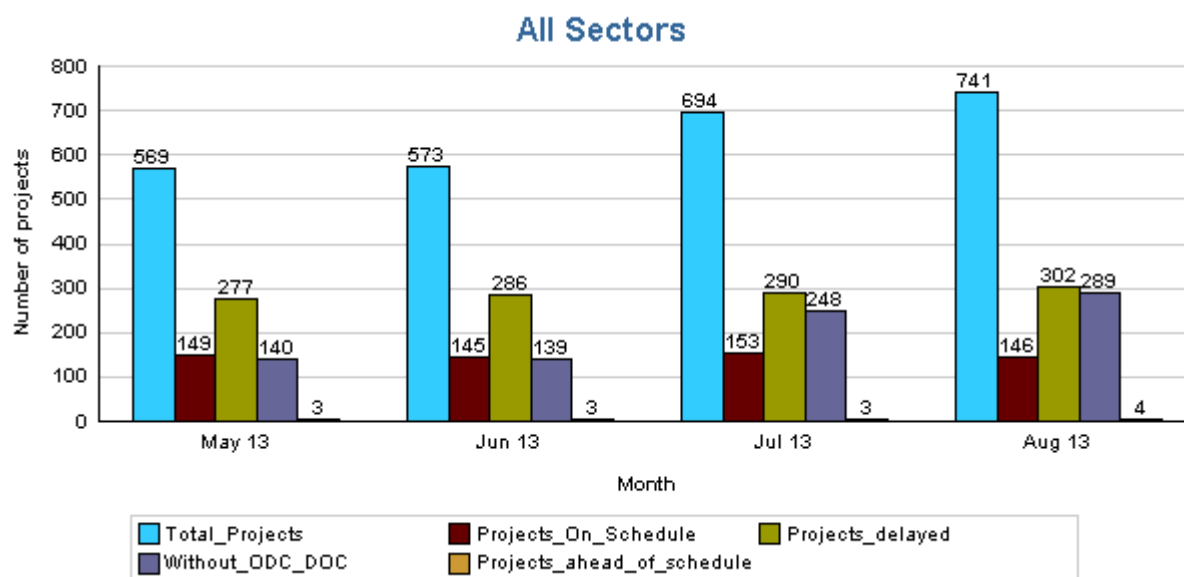


**Break-up of 302 Delayed projects in August 2013**

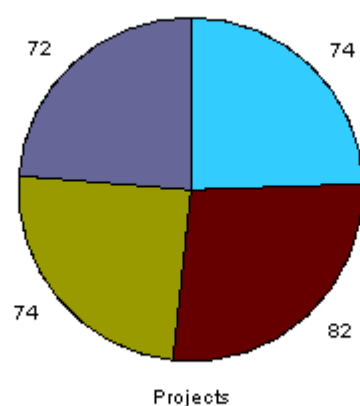


Delay in Months

| Delay in Months | 1-12 | 13-24 | 25-60 | 60 and Above |
|-----------------|------|-------|-------|--------------|
| Projects        | 74   | 82    | 74    | 72           |

## Graphical Presentation of All Projects w.r.t. Revised Schedule

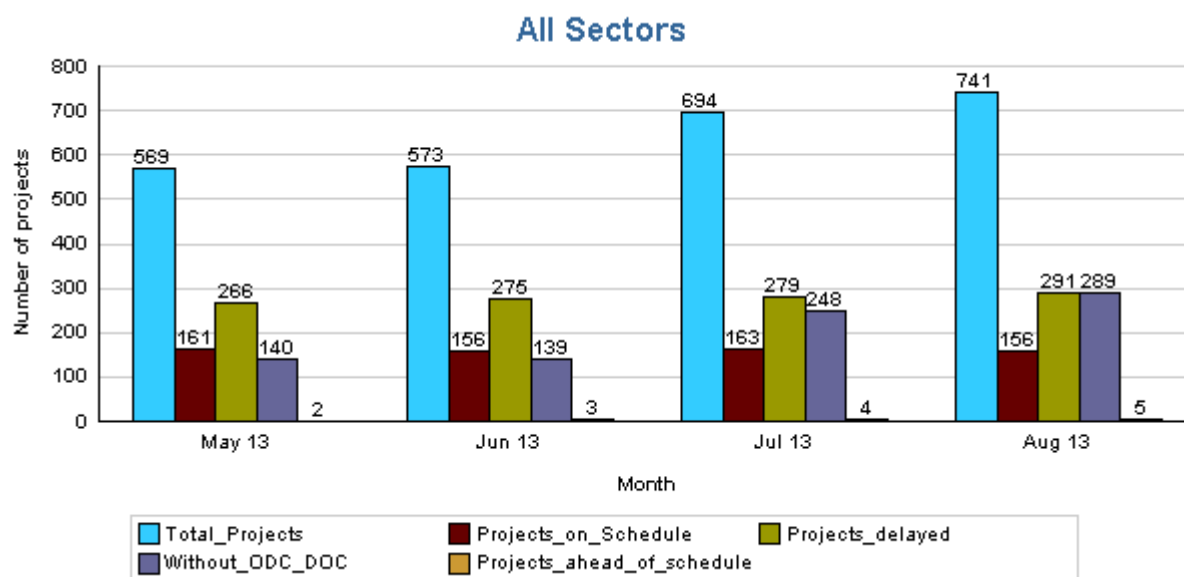


**Break-up of 291 Delayed projects in August 2013**

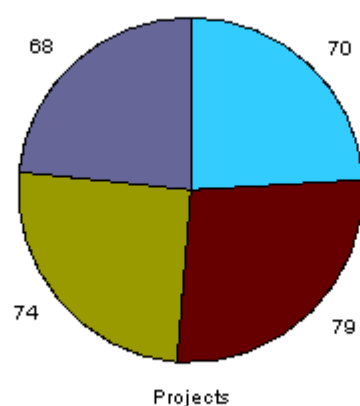


Delay in Months



## Graphical Presentation of Urban Development Sector

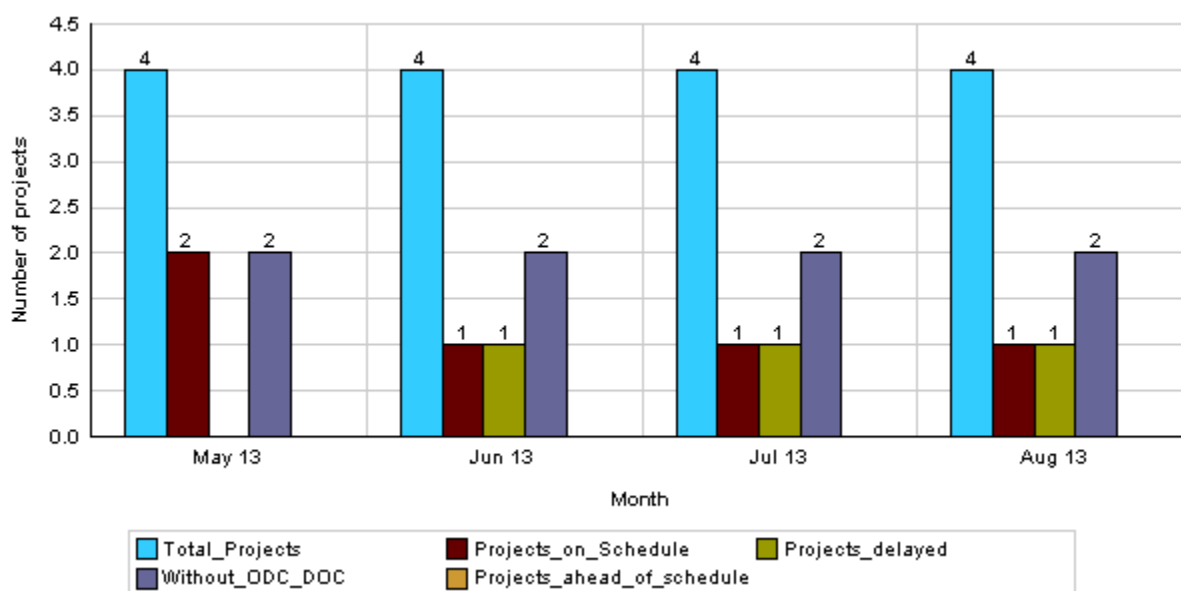


### Break-up of 1 Delayed projects in August 2013




Delay in Months



## Graphical Presentation of Telecommunications Sector

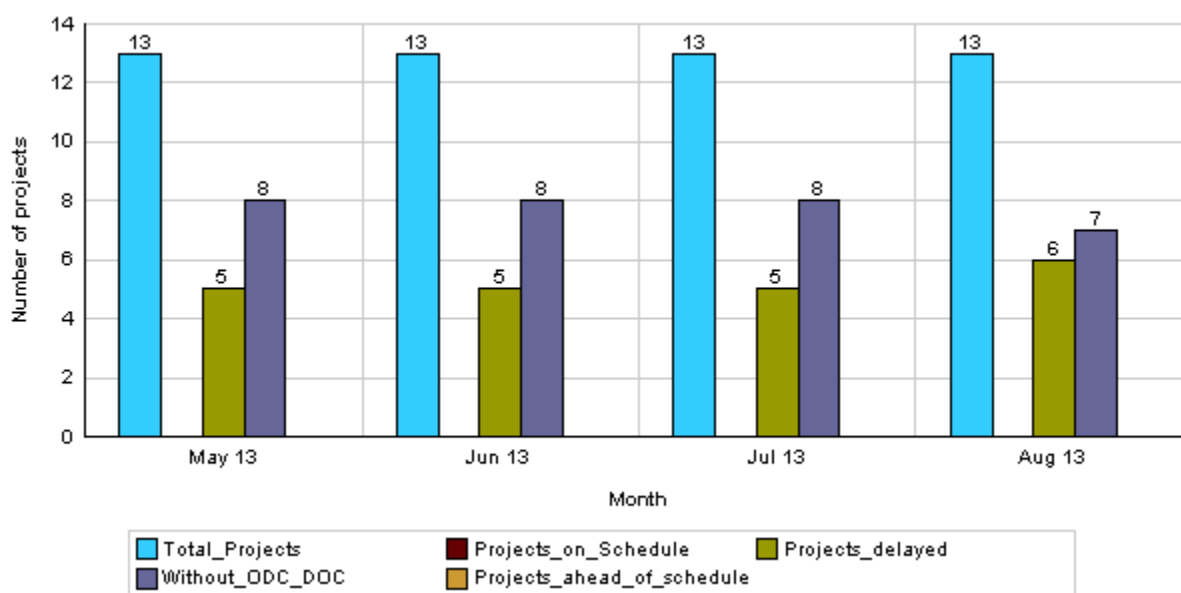

**Break-up of 6 Delayed projects in August 2013**

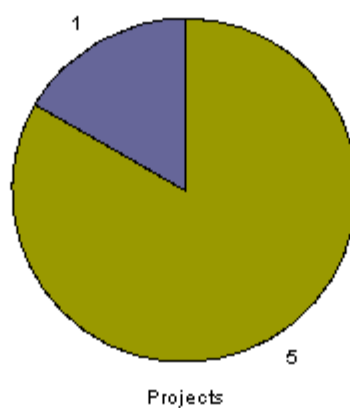


Delay in Months






## Graphical Presentation of Shipping And Ports Sector

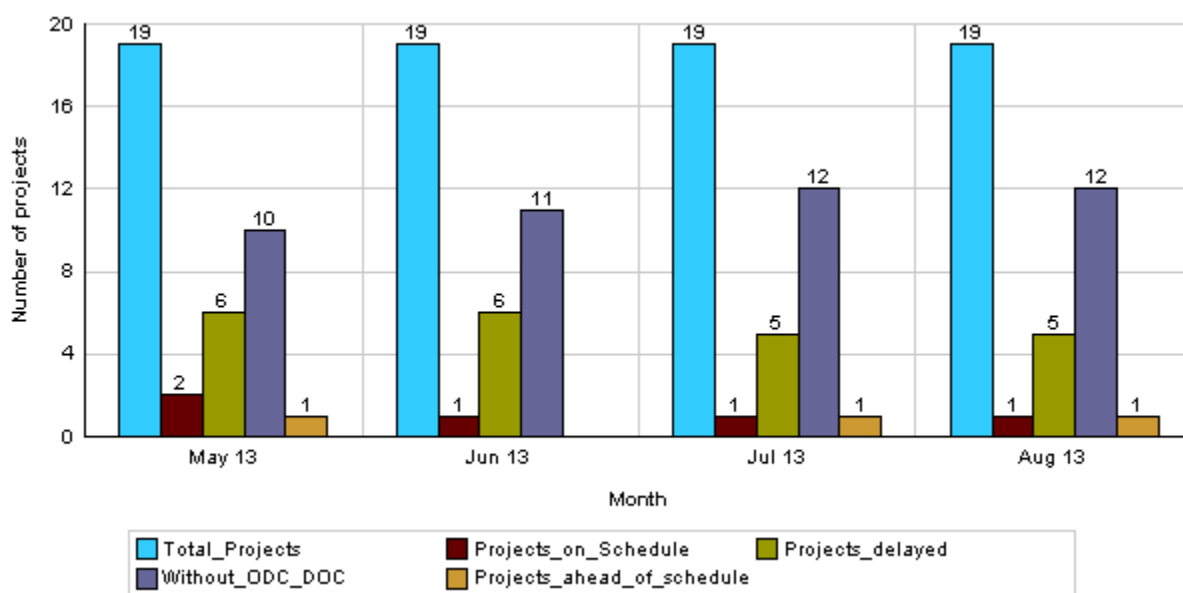


**Break-up of 5 Delayed projects in August 2013**

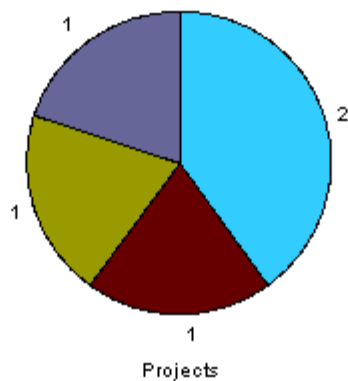


Delay in Months



## Graphical Presentation of Road Transport And Highways Sector

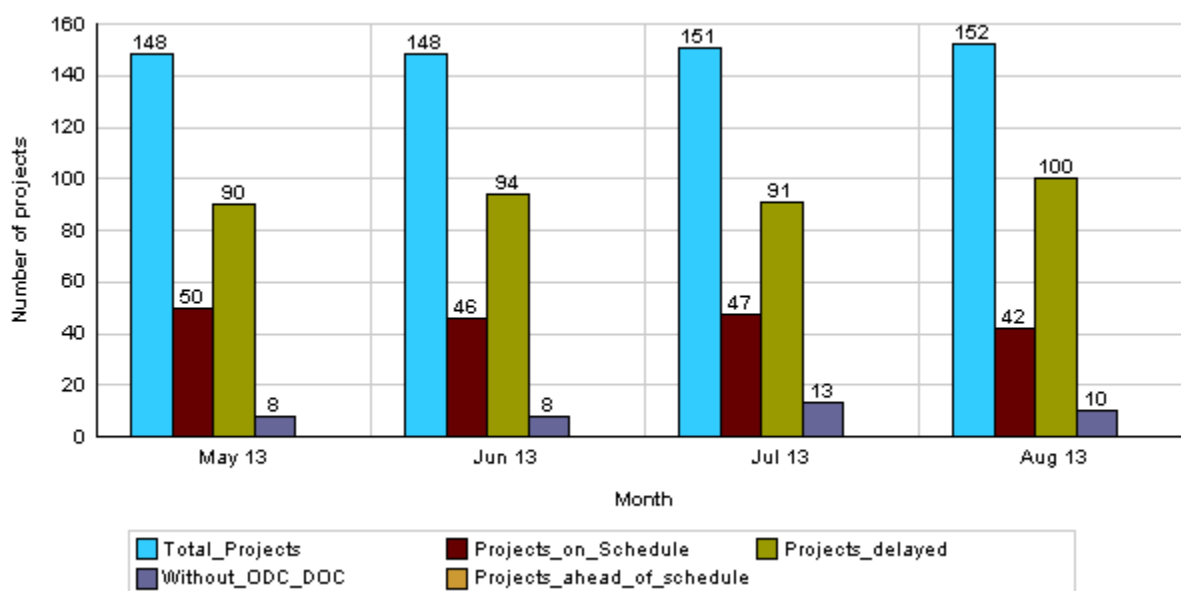


**Break-up of 100 Delayed projects in August 2013**

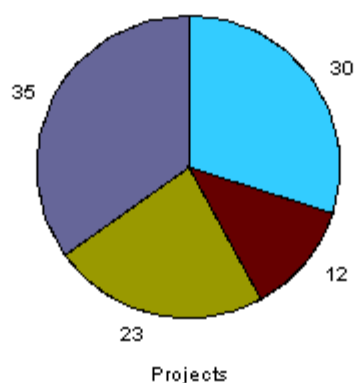


Delay in Months



## Graphical Presentation of Railways Sector

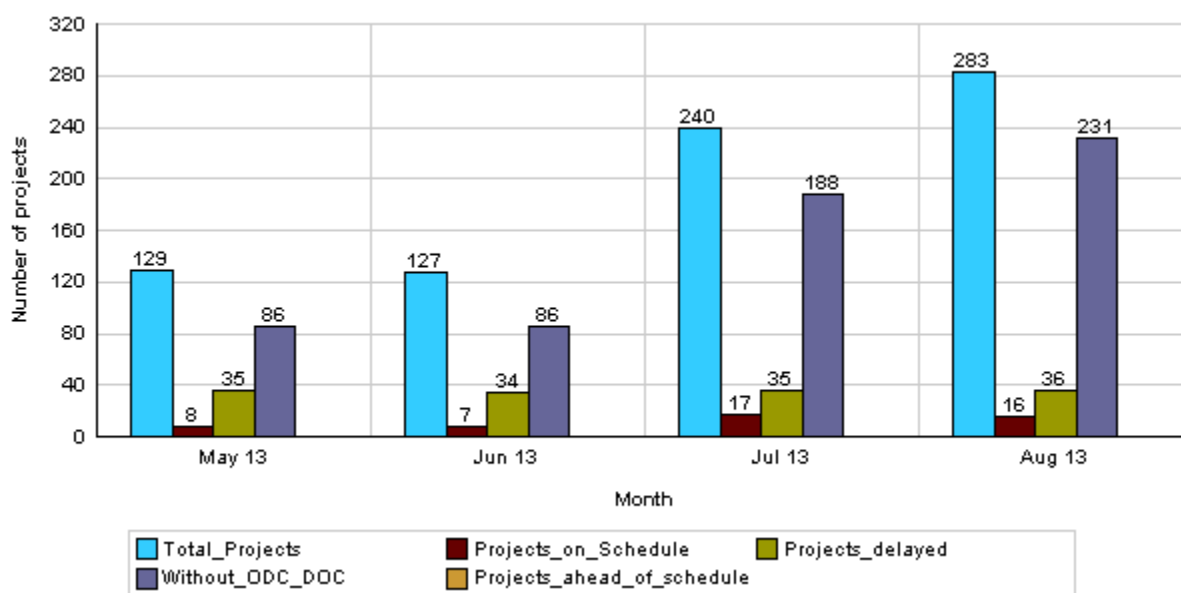


### Break-up of 36 Delayed projects in August 2013

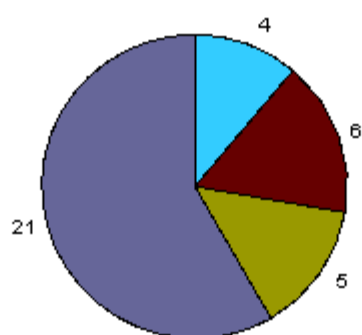


Delay in Months



## Graphical Presentation of Power Sector

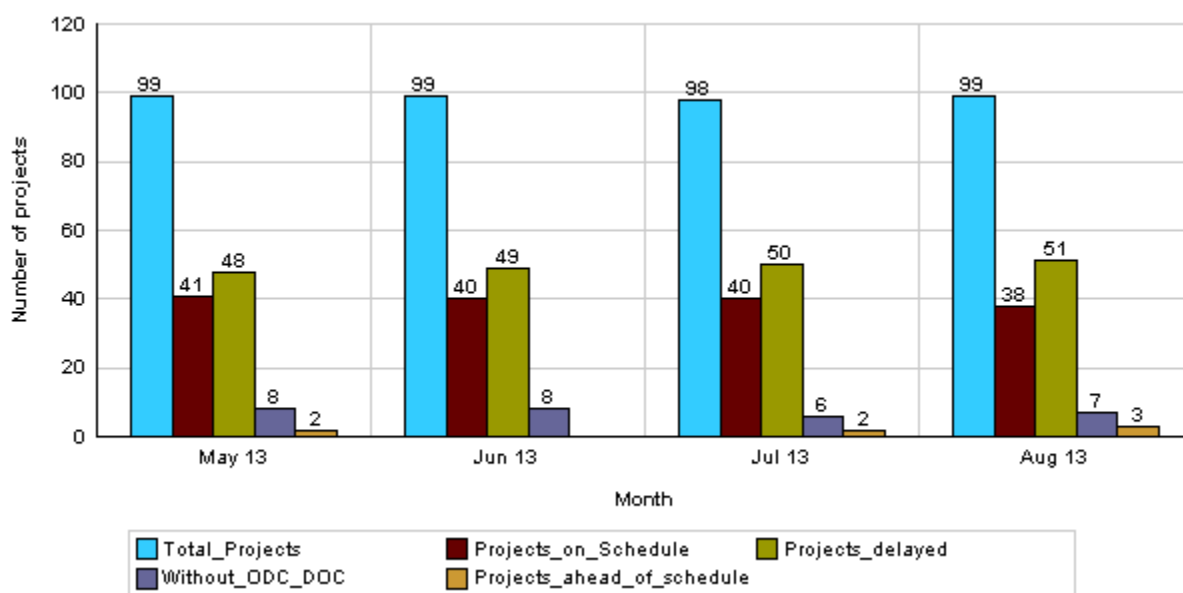


### Break-up of 51 Delayed projects in August 2013

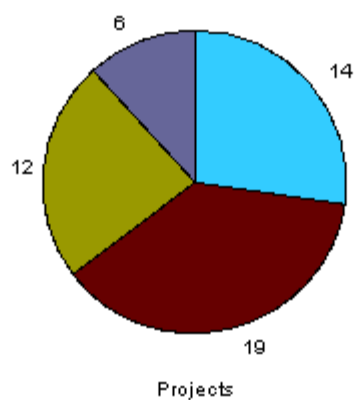


Delay in Months



## Graphical Presentation of Petroleum Sector

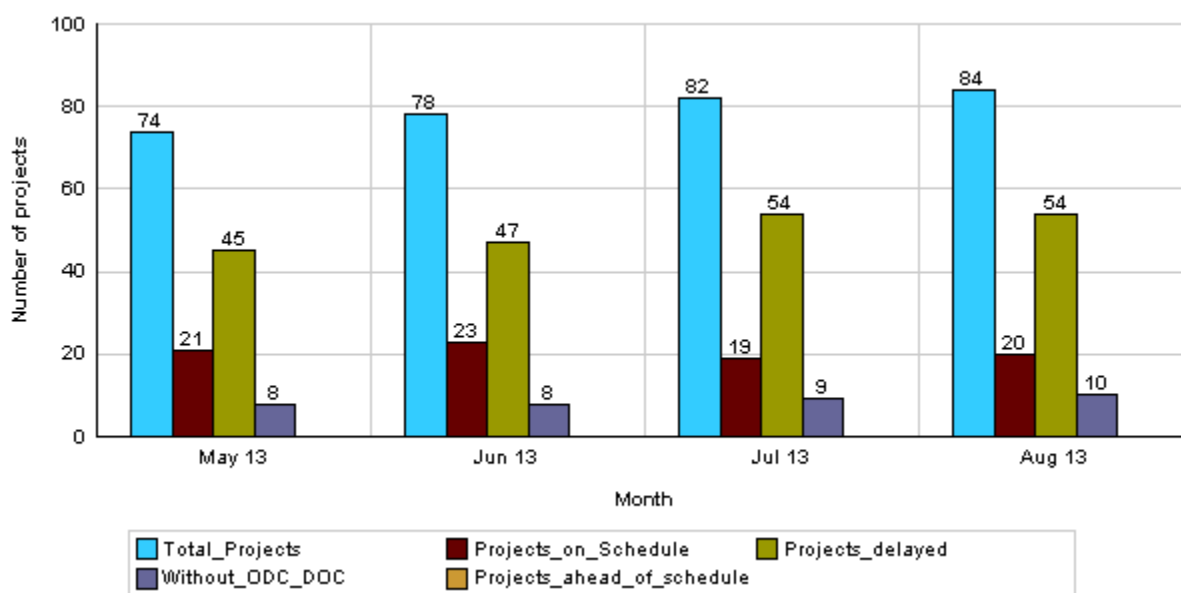


### Break-up of 54 Delayed projects in August 2013

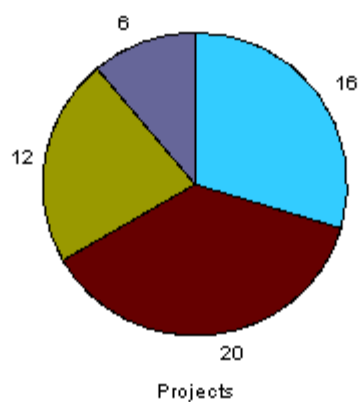


Delay in Months



## Graphical Presentation of Steel Sector

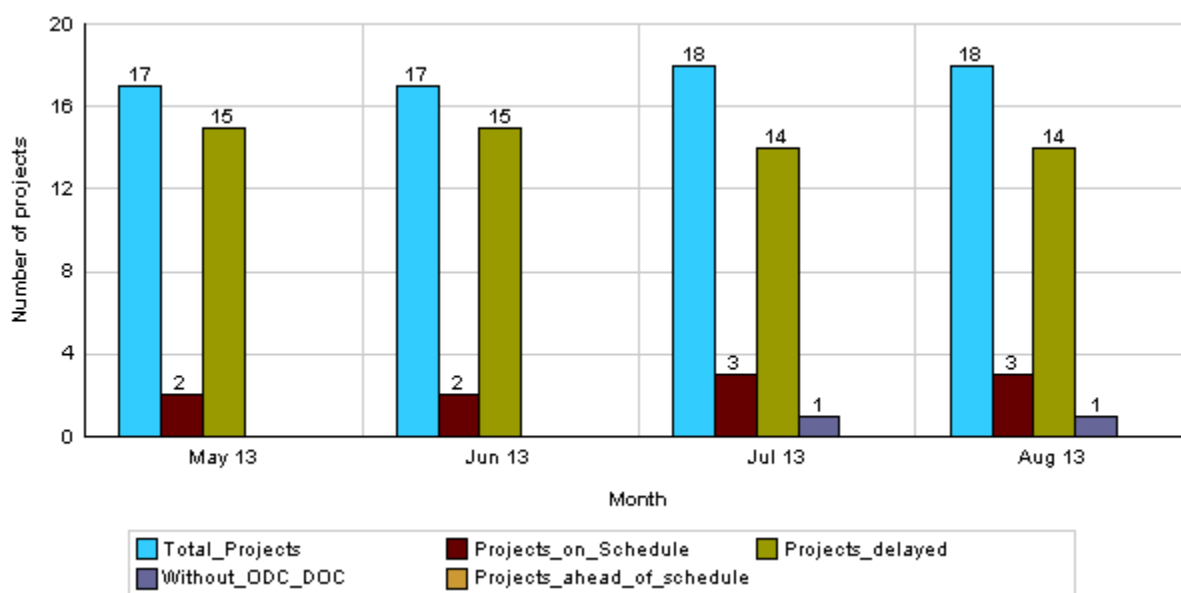


### Break-up of 14 Delayed projects in August 2013

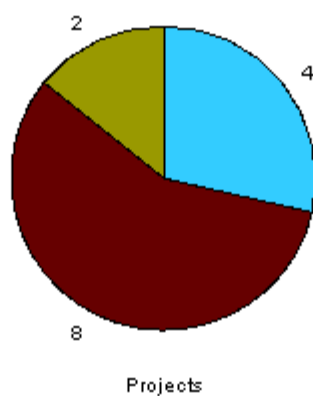


Delay in Months



## Graphical Presentation of Coal Sector

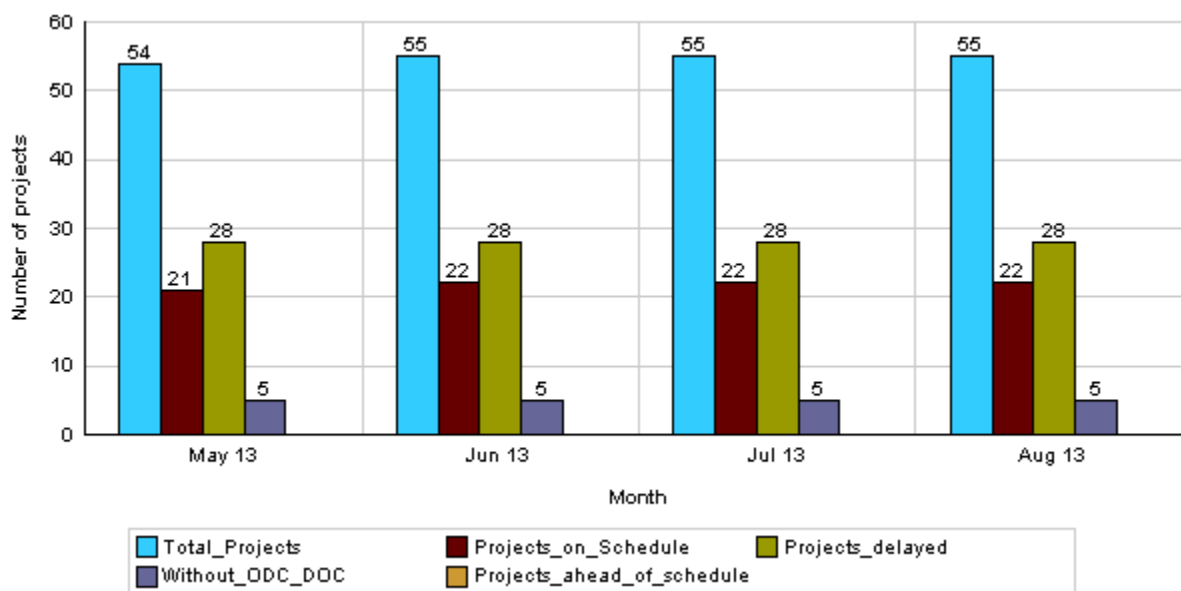


**Break-up of 28 Delayed projects in August 2013**

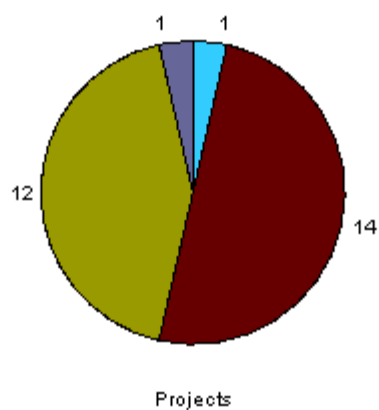

Delay in Months



## Graphical Presentation of Civil Aviation Sector

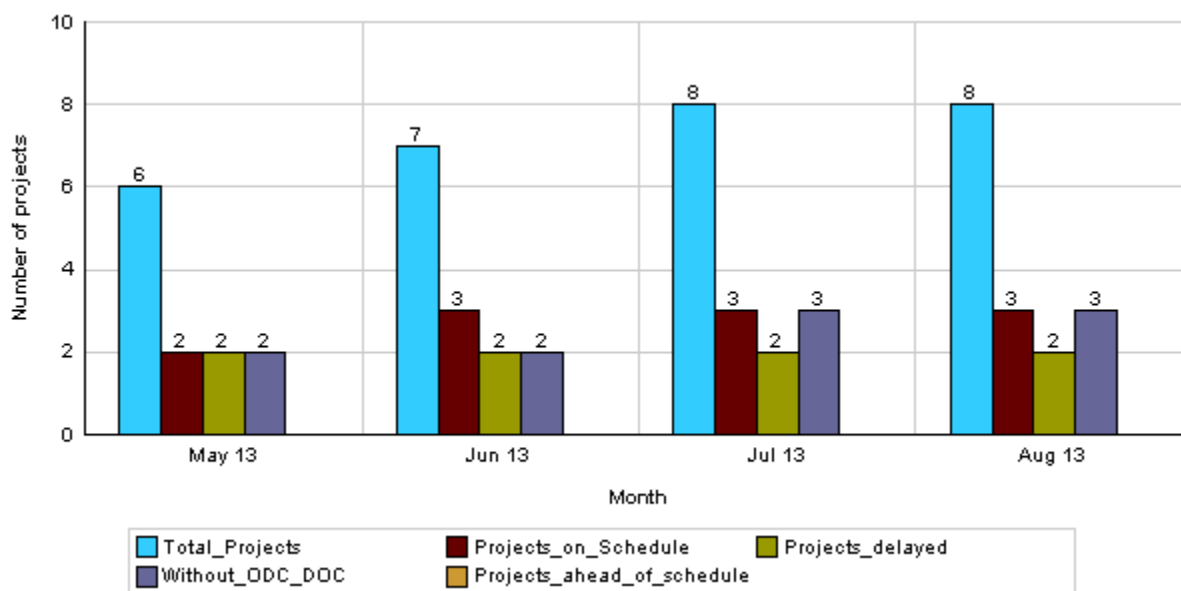

### Break-up of 2 Delayed projects in August 2013




Delay in Months






## Graphical Presentation of Atomic Energy Sector

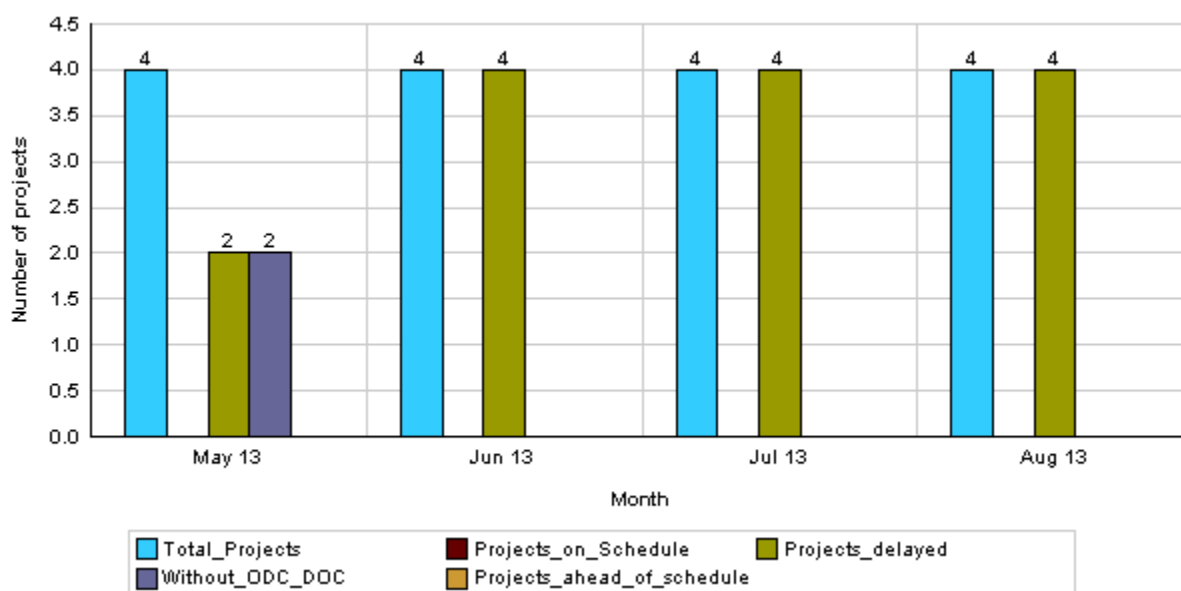

**Break-up of 4 Delayed projects in August 2013**

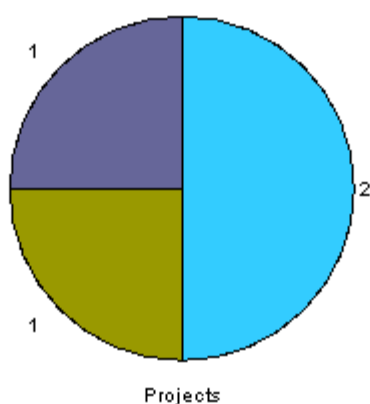

Delay in Months



| Sectorwise analysis of projects |                    |                  |            |              |                        |
|---------------------------------|--------------------|------------------|------------|--------------|------------------------|
|                                 |                    | Cost (Rs. crore) |            |              |                        |
| Sector                          | Number of projects | Original         | Latest     | Anticipated  | Cumulative Expenditure |
| Atomic Energy                   | 4                  | 40,442.00        | 44,541.00  | 46,726.00    | 26,373.60              |
| Civil Aviation                  | 8                  | 6,035.46         | 6,242.46   | 6,624.95     | 5,421.55               |
| Coal                            | 55                 | 38,127.05        | 40,988.64  | 41,212.50    | 15,401.75              |
| Steel                           | 18                 | 65,625.22        | 69,847.40  | 71,782.40    | 53,178.98              |
| Petrochemicals                  | 1                  | 5,460.61         | 8,920.00   | 8,920.00     | 4,510.51               |
| Petroleum                       | 84                 | 184,108.78       | 198,338.52 | 198,495.51   | 94,028.32              |
| Power                           | 99                 | 254,014.60       | 258,714.64 | 273,611.01   | 128,680.52             |
| Railways                        | 283                | 147,446.28       | 180,812.96 | 258,415.07   | 75,004.75              |
| Road Transport And Highways     | 152                | 105,203.54       | 105,370.04 | 107,142.16   | 83,521.87              |
| Shipping And Ports              | 19                 | 15,617.12        | 17,487.95  | 17,902.42    | 8,642.58               |
| Telecommunications              | 13                 | 5,699.24         | 5,699.24   | 5,527.92     | 1,970.85               |
| Urban Development               | 4                  | 44,245.18        | 44,304.08  | 49,518.08    | 6,421.63               |
| Water Resources                 | 1                  | 542.90           | 542.90     | 1,187.00     | 35.49                  |
|                                 |                    |                  |            |              |                        |
| Grand total                     | 741                | 912,567.98       | 981,809.83 | 1,087,065.02 | 503,192.40             |

(All Cost/ Expenditure in Rs. Crore)


## Sector Wise Details (Aug,2013)

|       |                                                                                           |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
|       |                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Atomic Energy</u>                                                                      |                  |                         |                  |                             |                       |             |                                            |                             |
| 1     | KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat                        | 10/2009          | 11,459.00 -             | 11,459.00        | 3,088.00                    | 12/2015 -             | 11/2016     | 11(O) -                                    | 0/70                        |
| 2     | KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu                                      | 12/2001          | 13,171.00 17,270.00     | 17,270.00        | 16,485.00                   | 12/2008 -             | 06/2014     | 66(O) -                                    | 39/106                      |
| 3     | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu          | 09/2003          | 3,492.00 -              | 5,677.00         | 4,681.60                    | 09/2010 -             | 03/2015     | 54(O) -                                    | 8/82                        |
| 4     | RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan          | 10/2009          | 12,320.00 -             | 12,320.00        | 2,119.00                    | 12/2016 -             | 03/2017     | 3(O) -                                     | 0/69                        |
|       | Total                                                                                     |                  | 40,442.00 -             | 46,726.00        | 26,373.60                   |                       |             |                                            | 47/327                      |
|       |                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Civil Aviation</u>                                                                     |                  |                         |                  |                             |                       |             |                                            |                             |
| 5     | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal            | 08/2008          | 1,942.51 -              | 2,325.00         | 2,472.95                    | 05/2011 -             | 03/2013     | -                                          | 0/0                         |
| 6     | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim                        | 01/2009          | 309.46 -                | 309.46           | 231.80                      | 01/2011 04/2013       | 12/2014     | 47(O) 20(R)                                | 0/0                         |
| 7     | Construction of New International Terminal Building - [N04000069]AAI,Goa                  | 05/2010          | 335.61 -                | 335.61           | 233.69                      | 05/2012 -             | 09/2013     | 16(O) -                                    | 0/0                         |
| 8     | D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu             | 08/2008          | 1,808.00 2,015.00       | 2,015.00         | 1,905.71                    | 01/2011 02/2012       | 02/2012     | -                                          | 0/0                         |
| 9     | DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Chandigarh            | 02/2011          | 452.00 -                | 452.00           | 127.08                      | 03/2015 -             | 03/2015     | 0(O) -                                     | 0/0                         |
| 10    | ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI - [N04000072]AAI,Multi State | 02/2010          | 344.28 -                | 344.28           | -                           | 03/2014 -             | 03/2014     | 0(O) -                                     | 0/0                         |
| 11    | GAGAN PROJECT - [N04000065]AAI,Multi State                                                | 09/2008          | 626.00 -                | 626.00           | 450.30                      | 06/2013 -             | 06/2013     | -                                          | 0/0                         |
| 12    | SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State   | 10/2012          | 217.60 -                | 217.60           | 0.02                        | 03/2015 -             | 03/2015     | 0(O) -                                     | 0/0                         |
|       | Total                                                                                     |                  | 6,035.46 -              | 6,624.95         | 5,421.55                    |                       |             |                                            | 0/0                         |
|       |                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Coal</u>                                                                               |                  |                         |                  |                             |                       |             |                                            |                             |
| 13    | ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh                                   | 12/2009          | 212.34 779.26           | 977.53           | 722.85                      | 03/2013 09/2012       | 10/2014     | 19(O) 25(R)                                | 18/22                       |
| 14    | AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh                      | 11/2009          | 150.59 -                | 198.59           | 89.13                       | 03/2016 -             | 03/2016     | 0(O) -                                     | 2/7                         |
| 15    | AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh                         | 12/2009          | 1,352.04 1,143.54       | 1,143.54         | 470.53                      | 03/2016 03/2016       | 03/2016     | 0(O) 0(R)                                  | 0/4                         |
| 16    | AMRAPALI OC - [N06000103]CCL,Jharkhand                                                    | 02/2012          | 858.11 -                | 858.11           | 49.33                       | 03/2020 -             | 03/2020     | 0(O) -                                     | 0/3                         |
| 17    | ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha                               | 08/2008          | 207.28 -                | 207.28           | 114.09                      | 03/2012 -             | 03/2014     | 24(O) -                                    | 5/6                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                   |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 18    | ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand                           | 12/2007          | 471.66<br>341.63        | 341.63           | 108.85                      | 03/2011<br>-          | 03/2014     | 36(O)<br>-                                 | 0/2                         |
| 19    | BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha                       | 12/2007          | 172.08<br>-             | 172.08           | 124.54                      | 03/2010<br>-          | 03/2015     | 60(O)<br>-                                 | 3/4                         |
| 20    | BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh                     | 04/2012          | 258.56<br>-             | 258.56           | 52.44                       | 03/2016<br>-          | 03/2016     | 0(O)<br>-                                  | 0/6                         |
| 21    | BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha                          | 12/2007          | 490.00<br>-             | 490.10           | 150.13                      | 03/2017<br>-          | 03/2017     | 0(O)<br>-                                  | 4/12                        |
| 22    | BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State                            | 11/2006          | 168.97<br>-             | 168.97           | 45.02                       | 03/2014<br>-          | 03/2014     | 0(O)<br>-                                  | 0/2                         |
| 23    | BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh                         | 06/2011          | 746.04<br>-             | 535.10           | 161.09                      | 03/2015<br>-          | 03/2015     | 0(O)<br>-                                  | 0/3                         |
| 24    | Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh                             | 09/2008          | 203.82<br>-             | 203.82           | -                           | 03/2015<br>-          | 03/2015     | 0(O)<br>-                                  | 1/6                         |
| 25    | CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh                               | 06/2008          | 462.35<br>-             | 462.35           | 266.91                      | 03/2014<br>-          | 03/2016     | 24(O)<br>-                                 | 2/8                         |
| 26    | Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand                              | 08/2007          | 163.51<br>-             | 163.51           | 35.12                       | 03/2011<br>-          | 03/2016     | 60(O)<br>-                                 | 0/2                         |
| 27    | DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh              | 12/2009          | 1,943.66<br>-           | 1,943.66         | 1,259.22                    | 03/2014<br>-          | 03/2016     | 24(O)<br>-                                 | 6/12                        |
| 28    | GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh              | 06/2010          | 2,675.67<br>-           | 2,675.67         | 1,419.31                    | 03/2014<br>-          | 03/2016     | 24(O)<br>-                                 | 10/15                       |
| 29    | GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha                                  | 02/2008          | 395.87<br>-             | 395.87           | 72.34                       | 03/2015<br>-          | 03/2015     | 0(O)<br>-                                  | 1/13                        |
| 30    | HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha                         | 11/2008          | 479.63<br>-             | 479.63           | 114.88                      | 03/2013<br>-          | 03/2015     | 24(O)<br>-                                 | 3/8                         |
| 31    | JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh                          | 09/2008          | 152.43<br>-             | 152.43           | -                           | 03/2015<br>-          | 03/2017     | 24(O)<br>-                                 | 1/7                         |
| 32    | JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh                       | 07/2011          | 447.06<br>-             | 447.06           | 14.02                       | 03/2015<br>-          | 03/2015     | 0(O)<br>-                                  | 4/31                        |
| 33    | JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh                           | 09/2007          | 467.78<br>-             | 467.78           | 12.31                       | 03/2013<br>-          | -           | -                                          | 6/83                        |
| 34    | JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal                               | 11/2006          | 287.18<br>-             | 287.17           | 0.92                        | 03/2011<br>-          | 03/2017     | 72(O)<br>-                                 | 0/2                         |
| 35    | KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh                                | 12/2008          | 453.63<br>-             | 453.63           | 87.53                       | 12/2012<br>-          | 03/2016     | 39(O)<br>-                                 | 9/44                        |
| 36    | KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,Andhra Pradesh                    | 07/2012          | 417.33<br>-             | 417.33           | 0.06                        | 07/2016<br>-          | 07/2016     | 0(O)<br>-                                  | 3/39                        |
| 37    | KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha                               | 12/2007          | 457.77<br>-             | 457.77           | 112.72                      | 03/2013<br>-          | 03/2015     | 24(O)<br>-                                 | 5/10                        |
| 38    | KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand                                     | 06/2009          | 162.46<br>-             | 162.46           | 40.64                       | 03/2014<br>-          | 03/2014     | 0(O)<br>-                                  | 0/2                         |
| 39    | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh                       | 07/2008          | 178.44<br>-             | 178.44           | -                           | 03/2014<br>-          | 03/2016     | 24(O)<br>-                                 | 1/7                         |
| 40    | KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh | 06/2011          | 1,131.28<br>-           | 1,131.28         | 4.88                        | 03/2018<br>-          | 03/2018     | 0(O)<br>-                                  | 0/4                         |
| 41    | KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh                          | 06/2011          | 789.88<br>-             | 741.62           | 372.96                      | 03/2013<br>-          | 03/2014     | 12(O)<br>-                                 | 0/2                         |
| 42    | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha                       | 01/2005          | 302.96<br>-             | 302.96           | 115.27                      | 03/2010<br>-          | 03/2014     | 48(O)<br>-                                 | 9/10                        |
| 43    | KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh                   | 06/2008          | 1,188.31<br>-           | 1,188.31         | 738.32                      | 03/2013<br>-          | 03/2013     | -                                          | 0/9                         |

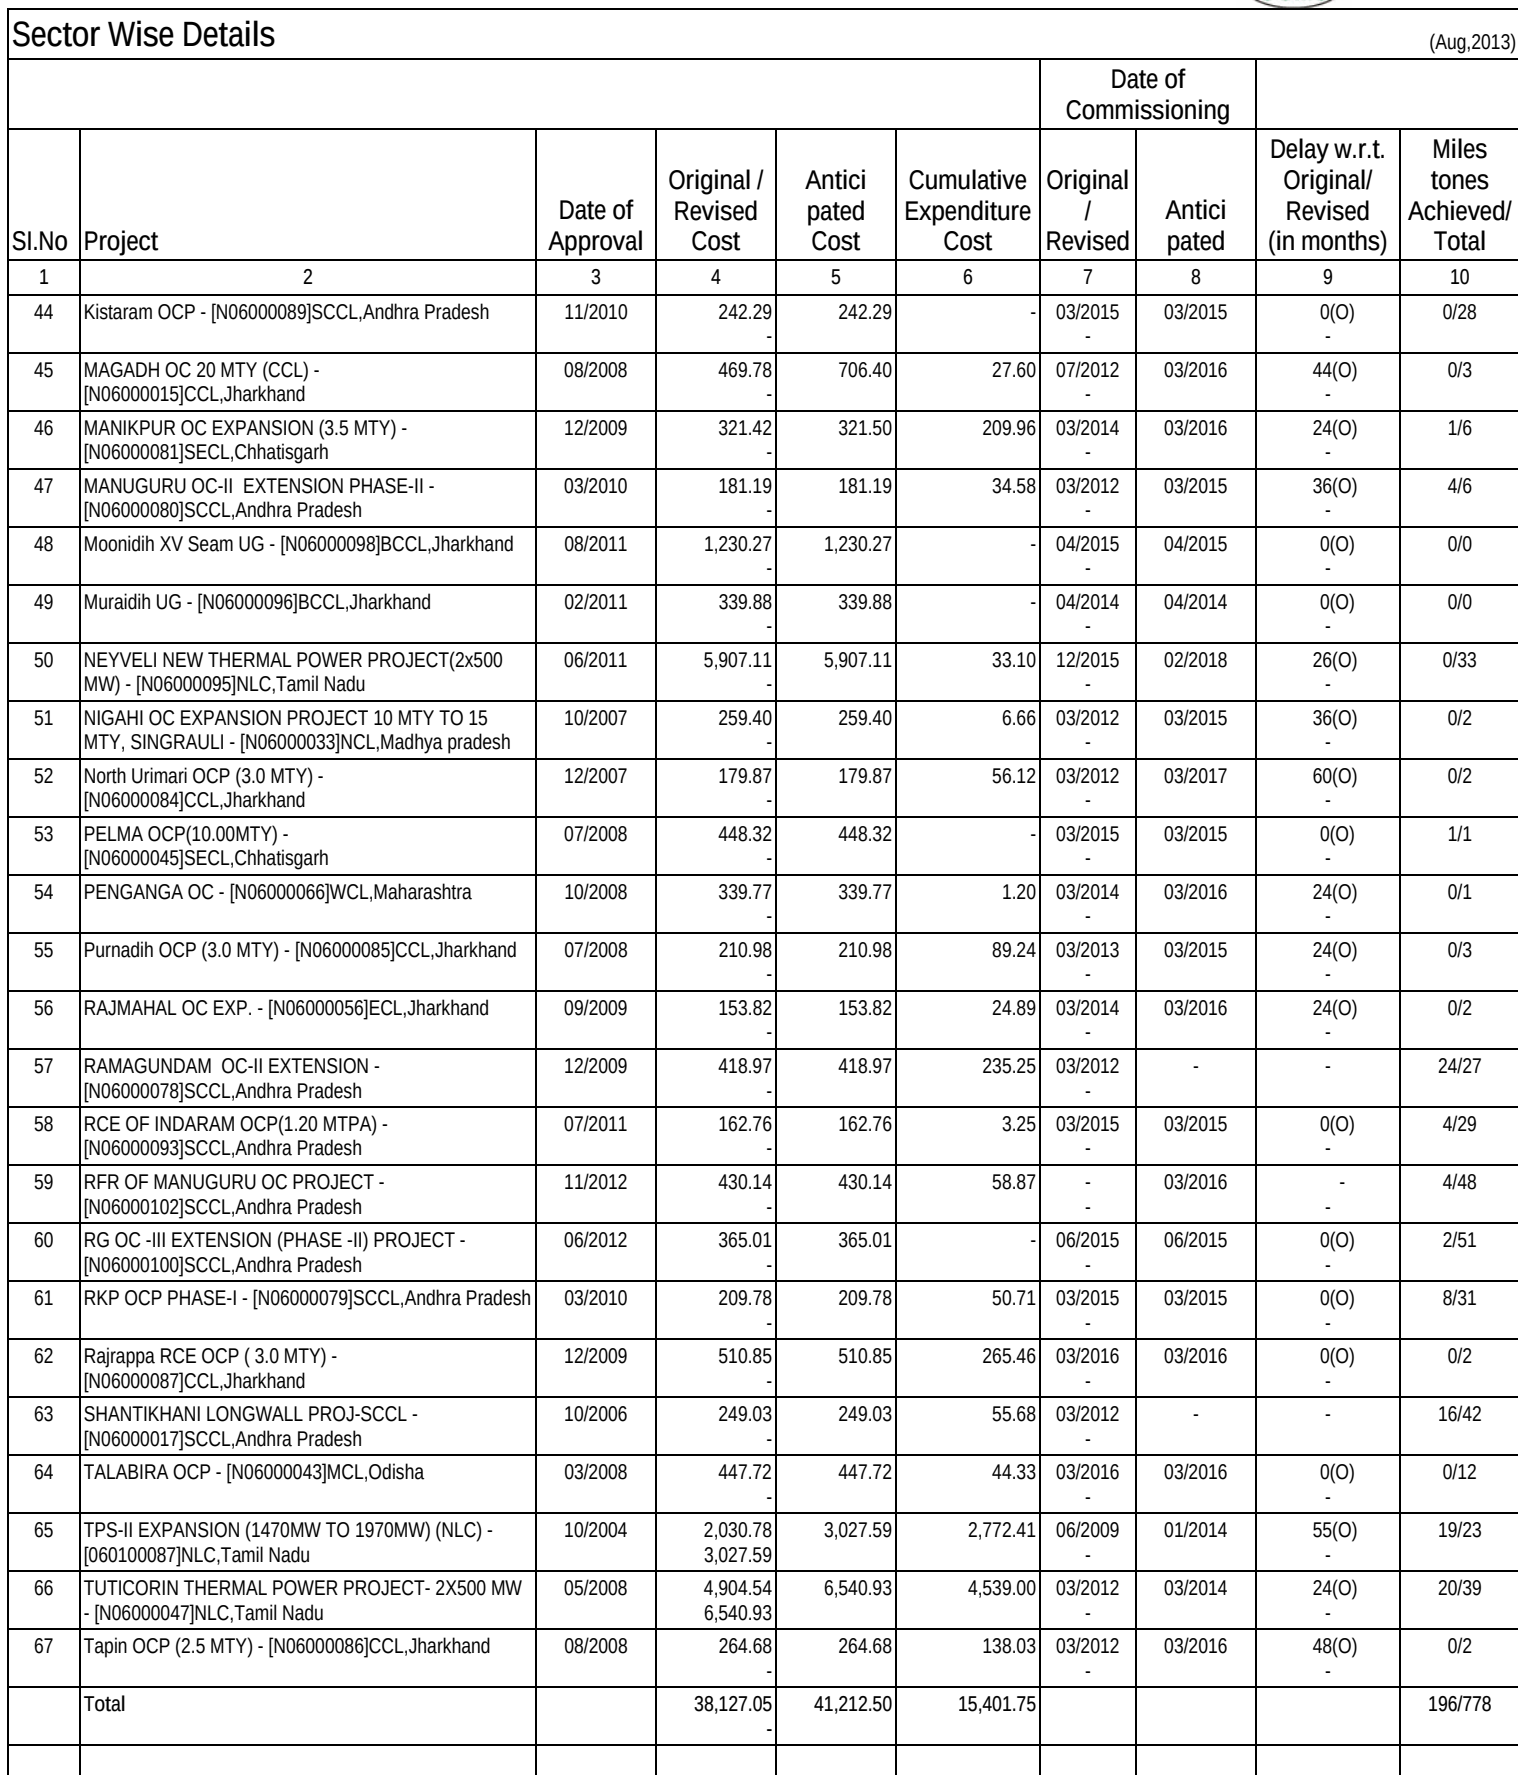

## Sector Wise Details

(Aug,2013)

|       |                                                                                             |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
|       | <u>Steel</u>                                                                                |                  |                         |                  |                             |                       |             |                                            |                             |
| 68    | 1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka                 | 04/2011          | 572.00 -                | 572.00           | 321.92                      | 04/2013<br>12/2013    | 12/2013     | 8(O)<br>0(R)                               | 17/19                       |
| 69    | 330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh                      | 07/2007          | 260.00<br>349.64        | 349.64           | 255.40                      | 08/2010<br>08/2010    | 06/2013     | -                                          | 1/1                         |
| 70    | 67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh            | 07/2007          | 230.00<br>343.58        | 343.58           | 278.77                      | 02/2011<br>02/2011    | 09/2013     | 31(O)<br>31(R)                             | 2/3                         |
| 71    | 7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka               | 02/2011          | 898.55 -                | 898.55           | 213.94                      | 05/2013<br>03/2014    | 03/2014     | 10(O)<br>0(R)                              | 12/21                       |
| 72    | Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State                      | 05/2008          | 480.00 -                | 450.00           | 278.90                      | 05/2012<br>05/2012    | 12/2013     | 19(O)<br>19(R)                             | 2/2                         |
| 73    | Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh                | 01/2007          | 295.89<br>607.17        | 607.17           | 353.13                      | 12/2011<br>03/2012    | 12/2013     | 24(O)<br>21(R)                             | 16/21                       |
| 74    | COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh                           | 08/2007          | 108.00<br>216.68        | 216.68           | 152.10                      | 10/2012<br>10/2012    | 12/2013     | 14(O)<br>14(R)                             | 3/4                         |
| 75    | Coke Oven Battery-5 - [N12000080]SAIL,West Bengal                                           | 03/2012          | 339.35 -                | 339.35           | 12.07                       | 06/2015<br>-          | 06/2015     | 0(O)<br>-                                  | 0/0                         |
| 76    | Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisga - [N12000078]SAIL,Chhatisgarh  | 07/2012          | 332.65 -                | 332.65           | 68.92                       | 08/2014<br>-          | 08/2014     | 0(O)<br>-                                  | 0/2                         |
| 77    | ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha                  | 11/2011          | 254.55 -                | 254.55           | 69.12                       | 11/2013<br>-          | 06/2015     | 19(O)<br>-                                 | 1/3                         |
| 78    | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh                               | 09/2008          | 17,265.00 -             | 17,265.00        | 10,284.01                   | 03/2013<br>-          | 09/2014     | 18(O)<br>-                                 | 23/32                       |
| 79    | EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand                                 | 01/2008          | 6,325.00 -              | 6,325.00         | 3,727.01                    | 12/2011<br>-          | 12/2013     | 24(O)<br>-                                 | 18/21                       |
| 80    | EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal                             | 06/2009          | 2,875.00 -              | 2,875.00         | 1,772.53                    | 12/2012<br>-          | 03/2014     | 15(O)<br>-                                 | 10/16                       |
| 81    | EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal                                | 02/2008          | 14,443.00 -             | 16,408.00        | 14,967.69                   | 12/2011<br>-          | 12/2013     | 24(O)<br>-                                 | 20/23                       |
| 82    | EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh | 10/2005          | 8,692.00<br>12,291.00   | 12,291.00        | 10,522.68                   | 10/2009<br>10/2012    | 09/2013     | 47(O)<br>11(R)                             | 66/67                       |
| 83    | Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha                                  | 09/2008          | 11,812.00 -             | 11,812.00        | 9,817.02                    | 03/2013<br>-          | 12/2013     | 9(O)<br>-                                  | 14/19                       |
| 84    | INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra             | 12/2011          | 187.33 -                | 187.33           | 80.31                       | 10/2013<br>-          | 06/2014     | 8(O)<br>-                                  | 0/3                         |
| 85    | Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha        | 01/2012          | 254.90 -                | 254.90           | 3.46                        | 12/2014<br>-          | 12/2014     | 0(O)<br>-                                  | 0/1                         |
|       | <b>Total</b>                                                                                |                  | 65,625.22 -             | 71,782.40        | 53,178.98                   |                       |             |                                            | 205/258                     |
|       |                                                                                             |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Petrochemicals</u>                                                                       |                  |                         |                  |                             |                       |             |                                            |                             |
| 86    | ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam                                           | 04/2006          | 5,460.61<br>8,920.00    | 8,920.00         | 4,510.51                    | 04/2012<br>12/2013    | 12/2013     | 20(O)<br>0(R)                              | 19/29                       |
|       | <b>Total</b>                                                                                |                  | 5,460.61 -              | 8,920.00         | 4,510.51                    |                       |             |                                            | 19/29                       |
|       |                                                                                             |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Petroleum</u>                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
| 87    | 102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan                                       | 07/2010          | 1,106.00 -              | 678.02           | 28.10                       | 06/2012<br>-          | 03/2014     | 21(O)<br>-                                 | 0/4                         |
| 88    | ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State                                  | 01/2010          | 2,163.64<br>2,331.62    | 2,331.62         | 1,557.08                    | 06/2012<br>-          | 05/2014     | 23(O)<br>-                                 | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                          |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 89    | ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra                    | 10/2008          | 1,797.35<br>-           | 977.00           | 773.81                      | 12/2011<br>-          | 11/2013     | 23(O)<br>-                                 | 0/5                         |
| 90    | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam                                | 03/2009          | 2,465.15<br>-           | 2,378.86         | 1,494.55                    | 03/2013<br>-          | 03/2014     | 12(O)<br>-                                 | 0/5                         |
| 91    | AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,Multi State             | 08/2011          | 586.00<br>-             | 586.00           | 56.49                       | 07/2015<br>-          | 08/2015     | 1(O)<br>-                                  | 0/0                         |
| 92    | Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat                                        | 11/2010          | 1,916.10<br>-           | 1,916.10         | 783.72                      | 12/2014<br>-          | 12/2016     | 24(O)<br>-                                 | 0/0                         |
| 93    | Ankleswar Redevelopment - [N16000122]ONGC,Gujarat                                        | 11/2010          | 2,189.63<br>-           | 2,189.63         | 1,039.14                    | 12/2014<br>-          | 12/2016     | 24(O)<br>-                                 | 0/0                         |
| 94    | BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State                      | 12/2009          | 540.92<br>-             | 540.92           | 327.67                      | 07/2012<br>07/2012    | -           | -                                          | 0/17                        |
| 95    | BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]OCL,Haryana                     | 11/2009          | 341.50<br>-             | 341.50           | 192.74                      | 02/2013<br>-          | 09/2013     | 7(O)<br>-                                  | 38/42                       |
| 96    | Butene-1 at Panipat - [N16000139]OCL,Haryana                                             | 02/2012          | 190.00<br>-             | 190.00           | 67.27                       | 03/2014<br>-          | 03/2014     | 0(O)<br>-                                  | 0/24                        |
| 97    | CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam                   | 08/2008          | 144.02<br>-             | 204.29           | 130.26                      | 06/2012<br>-          | 12/2013     | 18(O)<br>-                                 | 0/0                         |
| 98    | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State            | 06/2007          | 736.65<br>-             | 736.65           | 360.32                      | 09/2011<br>-          | 12/2014     | 39(O)<br>-                                 | 0/0                         |
| 99    | CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam                         | 08/2008          | 126.18<br>-             | 159.54           | 59.52                       | 06/2012<br>-          | 03/2014     | 21(O)<br>-                                 | 0/0                         |
| 100   | CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu              | 01/2008          | 224.00<br>394.00        | 394.00           | 312.61                      | -<br>-                | 03/2013     | -                                          | 18/19                       |
| 101   | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam                 | 06/2010          | 202.94<br>-             | 202.94           | 4.12                        | 01/2014<br>-          | 01/2015     | 12(O)<br>-                                 | 0/5                         |
| 102   | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra          | 03/2011          | 861.79<br>-             | 761.68           | 281.53                      | 05/2013<br>-          | 05/2014     | 12(O)<br>-                                 | 0/5                         |
| 103   | CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY - [N16000167]OIL,Multi State   | 08/2006          | 374.56<br>-             | 374.56           | -                           | 09/2012<br>-          | 10/2016     | 49(O)<br>-                                 | 0/0                         |
| 104   | Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan | 04/2011          | 152.89<br>-             | 152.89           | 118.41                      | 06/2013<br>-          | 06/2013     | -                                          | 0/0                         |
| 105   | Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State          | 11/2010          | 331.20<br>-             | 269.10           | 78.89                       | 08/2013<br>-          | 03/2014     | 7(O)<br>-                                  | 0/5                         |
| 106   | Construction of 6 ETps - [N16000117]ONGC,Gujarat                                         | 03/2009          | 302.26<br>-             | 240.95           | 98.72                       | 09/2012<br>-          | 12/2013     | 15(O)<br>-                                 | 0/0                         |
| 107   | Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]ONGC,Gujarat                | 10/2011          | 200.69<br>-             | 200.69           | 3.03                        | 07/2014<br>-          | 07/2014     | 0(O)<br>-                                  | 0/5                         |
| 108   | Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State            | 01/2010          | 723.64<br>-             | 723.64           | -                           | 03/2013<br>-          | 06/2016     | 39(O)<br>-                                 | 0/0                         |
| 109   | Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat             | 03/2009          | 234.78<br>234.78        | 317.64           | 96.88                       | 09/2012<br>-          | 09/2013     | 12(O)<br>-                                 | 0/5                         |
| 110   | Construction of three ETps, Mehsana - [N16000135]ONGC,Gujarat                            | 03/2012          | 260.74<br>-             | 260.74           | 0.52                        | 11/2014<br>-          | 11/2014     | 0(O)<br>-                                  | 0/5                         |
| 111   | DBPL-II - [N16000147]GAIL,Multi State                                                    | 06/2009          | 486.00<br>-             | 486.00           | 57.56                       | 09/2013<br>-          | 09/2013     | 0(O)<br>-                                  | 0/0                         |
| 112   | DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra          | 12/2009          | 1,584.00<br>-           | 1,584.00         | 448.17                      | -<br>-                | -           | -                                          | 0/0                         |
| 113   | DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State                                | 04/2003          | 429.82<br>2,735.65      | 2,735.65         | 2,184.00                    | 04/2006<br>06/2012    | 02/2014     | 94(O)<br>20(R)                             | 0/0                         |
| 114   | DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra                        | 06/2007          | 3,248.78<br>5,633.44    | 5,633.44         | 5,116.25                    | 08/2010<br>03/2012    | 05/2014     | 45(O)<br>26(R)                             | 0/10                        |

## Sector Wise Details

(Aug,2013)

|       |                                                                                  |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 115   | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                 | 01/2007          | 2,323.40<br>2,920.82    | 2,920.82         | 1,902.72                    | 09/2010<br>03/2012    | 12/2015     | 63(O)<br>45(R)                             | 0/0                         |
| 116   | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                  | 06/2007          | 1,436.21<br>1,456.96    | 1,436.21         | 1,100.32                    | 07/2010<br>05/2012    | 03/2014     | 44(O)<br>22(R)                             | 0/0                         |
| 117   | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                     | 08/2006          | 3,195.16<br>3,690.37    | 3,690.37         | 2,520.91                    | 12/2008<br>04/2013    | 03/2014     | 63(O)<br>11(R)                             | 0/0                         |
| 118   | DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra     | 03/2009          | 3,284.00<br>2,174.00    | 2,174.00         | 1,459.18                    | 09/2011<br>05/2012    | 09/2013     | 24(O)<br>16(R)                             | 6/76                        |
| 119   | DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh  | 03/2009          | 3,597.00<br>2,730.00    | 2,730.00         | 1,697.33                    | 09/2011<br>03/2012    | 08/2013     | 23(O)<br>17(R)                             | 56/59                       |
| 120   | Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State                 | 08/2010          | 372.11<br>-             | 372.11           | 234.31                      | 03/2013<br>-          | 12/2013     | 9(O)<br>-                                  | 0/5                         |
| 121   | Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra                 | 03/2012          | 2,592.17<br>-           | 2,592.17         | 11.90                       | 05/2014<br>-          | 05/2014     | 0(O)<br>-                                  | 0/9                         |
| 122   | Development of Cluster-7 Fields - [N16000104]ONGC,Multi State                    | 03/2010          | 3,241.03<br>6,638.94    | 6,638.94         | 1,451.42                    | 03/2013<br>11/2014    | 11/2014     | 20(O)<br>0(R)                              | 0/10                        |
| 123   | Development of SB-14 field - [N16000116]ONGC,Multi State                         | 01/2011          | 410.44<br>-             | 410.44           | 228.26                      | 11/2012<br>-          | 10/2013     | 11(O)<br>-                                 | 0/9                         |
| 124   | Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State                | 06/2010          | 2,523.00<br>-           | 2,523.00         | 957.44                      | 01/2014<br>-          | 05/2014     | 4(O)<br>-                                  | 0/9                         |
| 125   | Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State | 04/2012          | 600.17<br>-             | 600.17           | 80.56                       | 12/2014<br>-          | 12/2014     | 0(O)<br>-                                  | 0/8                         |
| 126   | Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu                  | 05/2013          | 711.00<br>-             | 711.00           | 0.87                        | -<br>-                | -           | -                                          | 0/0                         |
| 127   | Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh   | 07/2010          | 1,000.00<br>-           | 1,000.00         | 649.76                      | 01/2013<br>-          | 11/2013     | 10(O)<br>-                                 | 18/18                       |
| 128   | GAS TURBINE GENERATION SET - [N18000146]OIL,Assam                                | 07/2009          | 216.88<br>-             | 216.88           | 160.36                      | 10/2011<br>-          | 12/2013     | 26(O)<br>-                                 | 0/9                         |
| 129   | HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra | 04/2008          | 825.00<br>-             | 1,827.00         | -                           | 04/2013<br>-          | 09/2013     | 5(O)<br>-                                  | 0/167                       |
| 130   | Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra          | 03/2012          | 5,608.40<br>-           | 5,608.40         | 1,178.55                    | 05/2015<br>-          | 05/2015     | 0(O)<br>-                                  | 0/17                        |
| 131   | IOR GELEKI (ONGCL) - [160100216]ONGC,Assam                                       | 09/2001          | 390.09<br>1,674.11      | 1,674.11         | 1,727.24                    | 03/2007<br>03/2017    | 12/2013     | 81(O)<br>-39(R)                            | 6/6                         |
| 132   | IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam                             | 09/2001          | 345.10<br>663.69        | 750.00           | 729.07                      | 03/2007<br>03/2014    | 12/2013     | 81(O)<br>-3(R)                             | 3/3                         |
| 133   | IOR of B-173A Field - [N16000140]ONGC,Multi State                                | 01/2012          | 352.49<br>-             | 352.49           | 4.19                        | 03/2014<br>-          | 05/2014     | 2(O)<br>-                                  | 0/5                         |
| 134   | IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam                                  | 09/2001          | 113.90<br>438.85        | 438.85           | 432.22                      | 03/2006<br>03/2013    | 12/2013     | 93(O)<br>9(R)                              | 6/6                         |
| 135   | IREF - [N16000143]BPCL,Kerala                                                    | 01/1999          | 14,225.00<br>-          | 14,225.00        | 508.63                      | 12/2015<br>-          | 05/2016     | 5(O)<br>-                                  | 0/0                         |
| 136   | Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra             | 12/2011          | 2,059.63<br>2,665.65    | 2,665.65         | 246.35                      | 03/2015<br>-          | 03/2015     | 0(O)<br>-                                  | 0/12                        |
| 137   | Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra            | 12/2012          | 3,513.07<br>-           | 3,513.07         | -                           | 02/2016<br>-          | 02/2016     | 0(O)<br>-                                  | 0/0                         |
| 138   | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State         | 07/2009          | 7,596.18<br>-           | 7,596.18         | 13.30                       | 01/2013<br>-          | 12/2015     | 35(O)<br>-                                 | 0/0                         |
| 139   | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana                       | 11/2007          | 281.07<br>-             | 281.07           | 4.42                        | 10/2010<br>-          | 12/2014     | 50(O)<br>-                                 | 0/0                         |



## Sector Wise Details

(Aug,2013)

|       |                                                                                            |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 140   | KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State  | 07/2009          | 238.68 -                | 312.00           | 293.12                      | 01/2012 -             | 07/2013     | -                                          | 0/1                         |
| 141   | KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State           | 06/2009          | 2,915.00 -              | 2,300.00         | 1,236.09                    | 12/2012 -             | -           | -                                          | 0/21                        |
| 142   | MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka           | 11/2012          | 666.00 -                | 701.00           | 16.56                       | 11/2015 -             | 11/2015     | 0(O) -                                     | 0/0                         |
| 143   | MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka                            | 08/2008          | 12,412.00 -             | 12,160.26        | 10,486.51                   | 01/2012 -             | 10/2013     | 21(O) -                                    | 0/108                       |
| 144   | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra                       | 01/2009          | 7,133.39 -              | 6,855.93         | 5,308.52                    | 09/2012 -             | 03/2014     | 18(O) -                                    | 0/0                         |
| 145   | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra                         | 10/2007          | 5,713.03<br>8,813.41    | 8,813.41         | 7,204.61                    | 05/2010<br>03/2013    | 03/2014     | 46(O)<br>12(R)                             | 0/0                         |
| 146   | Mehesana Redevelopment - [N16000121]ONGC,Gujarat                                           | 11/2010          | 3,823.00 -              | 3,823.00         | 701.81                      | 04/2015 -             | 03/2017     | 23(O) -                                    | 0/0                         |
| 147   | Mounded Bullet - [N16000154]CPCL,Tamil Nadu                                                | 12/2012          | 279.00 -                | 279.00           | 279.00                      | 12/2014 -             | 12/2014     | 0(O) -                                     | 0/0                         |
| 148   | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra       | 01/2007          | 740.02 -                | 740.02           | 730.48                      | 03/2010<br>03/2012    | 12/2013     | 45(O)<br>21(R)                             | 0/0                         |
| 149   | PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State                         | 02/2011          | 913.00 -                | 913.00           | 35.31                       | 07/2015 -             | 07/2015     | 0(O) -                                     | 0/0                         |
| 150   | PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha                                          | 02/2009          | 29,777.00 -             | 32,710.00        | 22,957.00                   | 11/2012 -             | 04/2014     | 17(O) -                                    | 60/100                      |
| 151   | PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State                              | 08/2009          | 1,793.00 -              | 1,793.00         | 873.21                      | 09/2012 -             | -           | -                                          | 5/11                        |
| 152   | PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State                | 08/2010          | 8,140.00 -              | 8,140.00         | 5,177.12                    | 02/2014 -             | 02/2014     | 0(O) -                                     | 0/0                         |
| 153   | PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra | 08/2009          | 246.81<br>276.83        | 276.83           | 238.10                      | 04/2012<br>06/2013    | 12/2013     | 20(O)<br>6(R)                              | 0/0                         |
| 154   | Pipeline Replacement Project, Ahmedabad - [N16000159]ONGC,Gujarat                          | 09/2011          | 202.25 -                | 160.16           | -                           | 07/2016 -             | 07/2016     | 0(O) -                                     | 0/5                         |
| 155   | Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State                               | 04/2012          | 2,547.26 -              | 1,417.00         | 485.99                      | 05/2014 -             | 05/2014     | 0(O) -                                     | 0/5                         |
| 156   | Polypropylene unit - [N16000113]Mangalore Refin,Karnataka                                  | 05/2009          | 1,803.78 -              | 1,803.78         | 732.72                      | 07/2012 -             | 12/2013     | 17(O) -                                    | 0/31                        |
| 157   | Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]OIL,Multi State                    | 04/2010          | 270.00 -                | 270.00           | -                           | 12/2014 -             | 12/2014     | 0(O) -                                     | 0/0                         |
| 158   | RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh        | 01/2009          | 756.00<br>898.00        | 898.00           | 913.72                      | -<br>-                | 08/2013     | -<br>-                                     | 52/53                       |
| 159   | REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State                               | 02/2012          | 1,210.64 -              | 1,210.64         | 169.14                      | 11/2015 -             | 11/2015     | 0(O) -                                     | 6/25                        |
| 160   | Reconstruction of BPA and BPB Platforms - [N16000161]ONGC,Maharashtra                      | 03/2013          | 1,138.50 -              | 1,138.50         | -                           | 04/2015 -             | 04/2015     | 0(O) -                                     | 0/0                         |
| 161   | Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra                    | 01/1999          | 1,419.00 -              | 1,419.00         | 134.21                      | 12/2014 -             | 12/2014     | 0(O) -                                     | 0/0                         |
| 162   | SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka          | 07/2010          | 1,043.57 -              | 957.10           | 655.84                      | 04/2012 -             | 12/2013     | 20(O) -                                    | 0/0                         |
| 163   | STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka              | 01/2006          | 732.00<br>1,227.00      | 1,227.00         | 722.53                      | 10/2011 -             | 12/2013     | 26(O) -                                    | 0/0                         |
| 164   | STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh             | 01/2006          | 672.00<br>1,038.00      | 1,038.00         | 904.74                      | 10/2011 -             | 01/2014     | 27(O) -                                    | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                                |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 165   | Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State                                   | 10/2012          | 10,281.00<br>-          | 10,281.00        | 0.04                        | -<br>-                | 04/2015     | -<br>-                                     | 0/0                         |
| 166   | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam            | 09/2012          | 871.35<br>-             | 871.35           | 2.26                        | 03/2015<br>-          | 06/2015     | 3(O)<br>-                                  | 0/5                         |
| 167   | URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State                               | 11/2012          | 309.81<br>-             | 309.82           | 48.71                       | 08/2014<br>-          | 10/2014     | 2(O)<br>-                                  | 0/0                         |
| 168   | Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura                | 07/2008          | 288.04<br>288.04        | 253.66           | 199.40                      | 08/2012<br>-          | 03/2014     | 19(O)<br>-                                 | 0/5                         |
| 169   | VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State     | 12/2009          | 463.32<br>-             | 330.47           | 261.51                      | 03/2012<br>-          | 12/2013     | 21(O)<br>-                                 | 13/20                       |
| 170   | Wax Project - [N16000101]NRL,Assam                                                             | 06/2010          | 576.60<br>-             | 576.60           | 289.40                      | 12/2013<br>-          | 12/2013     | 0(O)<br>-                                  | 0/0                         |
|       | Total                                                                                          |                  | 184,108.78<br>-         | 198,495.51       | 94,028.32                   |                       |             |                                            | 287/974                     |
|       |                                                                                                |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Power</u>                                                                                   |                  |                         |                  |                             |                       |             |                                            |                             |
| 171   | 765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State              | 08/2008          | 7,075.33<br>-           | 7,075.33         | 5,883.09                    | 08/2012<br>-          | 03/2014     | 19(O)<br>-                                 | 0/11                        |
| 172   | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State              | 11/2009          | 1,075.12<br>-           | 1,075.12         | 838.25                      | 05/2012<br>-          | 12/2013     | 19(O)<br>-                                 | 0/8                         |
| 173   | AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State          | 12/2012          | 156.04<br>-             | 156.04           | -                           | 10/2014<br>-          | 10/2014     | 0(O)<br>-                                  | 0/7                         |
| 174   | BARH STPP STAGE -II - [N18000047]NTPC,Bihar                                                    | 02/2008          | 7,341.04<br>-           | 7,341.04         | 6,307.00                    | 08/2013<br>-          | 09/2014     | 13(O)<br>-                                 | 12/19                       |
| 175   | BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar                                       | 12/2003          | 8,692.97<br>-           | 8,693.00         | 8,627.00                    | 12/2009<br>-          | 02/2017     | 86(O)<br>-                                 | 26/52                       |
| 176   | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam                                       | 01/2008          | 4,375.35<br>-           | 4,375.35         | 4,002.00                    | 07/2011<br>-          | 10/2015     | 51(O)<br>-                                 | 5/28                        |
| 177   | COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State                                  | 03/2013          | 2,514.88<br>-           | 2,514.88         | -                           | 12/2015<br>-          | 12/2015     | 0(O)<br>-                                  | 0/20                        |
| 178   | COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh  | 06/2012          | 1,909.24<br>-           | 1,909.24         | 174.43                      | 06/2015<br>-          | 06/2015     | 0(O)<br>-                                  | 0/0                         |
| 179   | COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh | 08/2011          | 1,637.34<br>-           | 1,637.34         | 882.14                      | 08/2014<br>-          | 08/2014     | 0(O)<br>-                                  | 7/20                        |
| 180   | COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh | 03/2012          | 206.44<br>-             | 206.44           | 40.67                       | 06/2014<br>-          | 06/2014     | 0(O)<br>-                                  | 0/20                        |
| 181   | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC - [N18000143]PGCIL,Multi State              | 03/2013          | 514.20<br>-             | 514.20           | -                           | 06/2015<br>-          | 06/2015     | 0(O)<br>-                                  | 0/0                         |
| 182   | COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu                             | 01/2013          | 182.80<br>-             | 182.80           | 3.60                        | 10/2014<br>-          | 10/2014     | 0(O)<br>-                                  | 0/0                         |
| 183   | Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu               | 09/2011          | 1,940.13<br>-           | 1,940.13         | 1,000.05                    | 09/2014<br>-          | 09/2014     | 0(O)<br>-                                  | 7/20                        |
| 184   | EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State                           | 10/2006          | 975.96<br>-             | 975.96           | 885.07                      | 10/2009<br>-          | 12/2013     | 50(O)<br>-                                 | 5/15                        |
| 185   | EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State                          | 07/2010          | 1,272.80<br>-           | 1,272.80         | 709.36                      | 11/2012<br>-          | 09/2014     | 22(O)<br>-                                 | 2/13                        |
| 186   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State    | 03/2012          | 198.63<br>-             | 198.63           | -                           | 09/2014<br>-          | 09/2014     | 0(O)<br>-                                  | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                             |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|---------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                     | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                           | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 187   | ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh                  | 05/2011          | 1,961.87<br>-           | 1,961.87         | 1,101.84                    | 05/2014<br>-          | 05/2014     | 0(O)<br>-                                  | 1/11                        |
| 188   | Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh                 | 12/2010          | 1,719.52<br>-           | 1,719.52         | 1,259.49                    | 08/2013<br>-          | 12/2013     | 4(O)<br>-                                  | 1/12                        |
| 189   | Gadarwara Super Thermal Power Project Stage-I - [N18000151]NTPC,Madhya pradesh              | 02/2013          | 11,638.55<br>-          | 11,638.55        | 681.00                      | 09/2017<br>-          | 09/2017     | 0(O)<br>-                                  | 4/40                        |
| 190   | IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar                       | 12/2011          | 901.77<br>-             | 901.77           | 345.53                      | 08/2014<br>-          | 08/2014     | 0(O)<br>-                                  | 1/16                        |
| 191   | INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh | 08/2011          | 1,391.97<br>-           | 1,391.97         | 1,041.70                    | 12/2013<br>-          | 12/2013     | 0(O)<br>-                                  | 1/12                        |
| 192   | KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka                      | 03/2005          | 596.45<br>1,007.16      | 1,007.16         | 909.22                      | 12/2007<br>12/2009    | -           | -                                          | 2/11                        |
| 193   | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh                 | 12/2004          | 2,496.90<br>-           | 5,139.00         | 2,448.33                    | 05/2013<br>05/2013    | 03/2017     | 46(O)<br>46(R)                             | 7/22                        |
| 194   | KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir                                         | 07/2007          | 2,238.67<br>3,642.04    | 3,642.00         | 2,579.51                    | 01/2016<br>01/2016    | 11/2016     | 10(O)<br>10(R)                             | 0/4                         |
| 195   | KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh                                        | 10/2002          | 4,527.15<br>-           | 6,414.56         | 5,095.00                    | 04/2009<br>-          | 09/2014     | 65(O)<br>-                                 | 0/9                         |
| 196   | KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka                                              | 12/2011          | 15,166.19<br>-          | 15,166.19        | 1,775.00                    | 12/2016<br>-          | 12/2016     | 0(O)<br>-                                  | 15/17                       |
| 197   | KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu                         | 05/2005          | 1,779.29<br>2,159.07    | 2,159.07         | 1,870.74                    | 09/2008<br>-          | 03/2013     | -                                          | 15/23                       |
| 198   | LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh                                             | 11/2012          | 11,846.00<br>-          | 11,846.00        | 1,096.00                    | 05/2017<br>-          | 05/2017     | 0(O)<br>-                                  | 6/39                        |
| 199   | Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand                                       | 07/2012          | 1,527.00<br>-           | 1,527.00         | 113.03                      | 08/2017<br>-          | 08/2017     | 0(O)<br>-                                  | 0/15                        |
| 200   | MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra                                             | 11/2008          | 5,459.28<br>-           | 6,010.89         | 4,056.00                    | 08/2012<br>-          | 03/2013     | -                                          | 16/16                       |
| 201   | MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra                                            | 03/2012          | 7,921.47<br>-           | 7,921.47         | 1,139.00                    | 09/2016<br>-          | 09/2016     | 0(O)<br>-                                  | 14/14                       |
| 202   | NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir                       | 08/2006          | 611.01<br>-             | 936.00           | 874.31                      | 08/2010<br>01/2013    | 10/2013     | 38(O)<br>9(R)                              | 0/3                         |
| 203   | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State           | 02/2009          | 11,130.19<br>-          | 11,130.19        | 6,539.65                    | 08/2013<br>-          | 06/2015     | 22(O)<br>-                                 | 0/17                        |
| 204   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State              | 02/2009          | 410.29<br>-             | 410.29           | 266.57                      | 02/2012<br>-          | 12/2013     | 22(O)<br>-                                 | 1/13                        |
| 205   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State               | 02/2009          | 520.48<br>-             | 520.48           | 363.00                      | 11/2011<br>-          | 07/2014     | 32(O)<br>-                                 | 0/11                        |
| 206   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State            | 02/2009          | 509.66<br>-             | 509.66           | 380.93                      | 11/2011<br>-          | 12/2013     | 25(O)<br>-                                 | 1/14                        |
| 207   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State               | 10/2010          | 182.68<br>-             | 182.68           | 134.05                      | 01/2013<br>-          | 10/2013     | 9(O)<br>-                                  | 1/6                         |
| 208   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State              | 07/2010          | 752.64<br>-             | 752.64           | 313.52                      | 07/2013<br>-          | 03/2014     | 8(O)<br>-                                  | 1/11                        |
| 209   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State             | 08/2010          | 1,677.57<br>-           | 1,677.57         | 882.14                      | 04/2013<br>-          | 03/2015     | 23(O)<br>-                                 | 0/11                        |
| 210   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State             | 11/2011          | 723.63<br>-             | 723.63           | 188.04                      | 11/2014<br>-          | 11/2014     | 0(O)<br>-                                  | 1/12                        |
| 211   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,Multi State              | 09/2013          | 680.69<br>-             | 680.69           | -                           | 03/2016<br>-          | 03/2016     | 0(O)<br>-                                  | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                              |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 212   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State              | 09/2012          | 803.34 -                | 803.34           | 98.44                       | 03/2015 -             | 03/2015     | 0(O) -                                     | 0/15                        |
| 213   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State            | 09/2012          | 524.40 -                | 524.40           | 40.78                       | 04/2015 -             | 05/2015     | 1(O) -                                     | 0/16                        |
| 214   | NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State             | 03/2010          | 965.58 -                | 965.58           | 601.58                      | 11/2012 -             | 03/2014     | 16(O) -                                    | 0/11                        |
| 215   | PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh                          | 10/2005          | 2,304.56 -              | 2,716.00         | 2,169.15                    | 10/2010<br>01/2013    | 03/2014     | 41(O)<br>14(R)                             | 0/6                         |
| 216   | PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh                                     | 09/2002          | 3,919.59 -              | 5,366.00         | 4,027.33                    | 09/2009<br>07/2014    | 07/2018     | 106(O)<br>48(R)                            | 1/20                        |
| 217   | PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh                    | 12/2008          | 573.99<br>1,117.92      | 1,117.92         | 660.88                      | 08/2012<br>08/2013    | 09/2014     | 25(O)<br>13(R)                             | 17/22                       |
| 218   | RAMPUR HEP(412 MW) - [N18000024]SJVN,L Himachal Pradesh                                      | 01/2007          | 2,047.03 -              | 2,047.03         | 2,671.47                    | 01/2012 -             | 03/2014     | 26(O) -                                    | 0/28                        |
| 219   | RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh                       | 01/2009          | 6,230.81 -              | 6,230.81         | 4,468.00                    | 10/2012 -             | 11/2013     | 13(O) -                                    | 16/16                       |
| 220   | SOLAPUR STPP - [N18000133]NTPC,Maharashtra                                                   | 03/2012          | 9,395.18 -              | 9,395.18         | 1,608.00                    | 11/2016 -             | 11/2016     | 0(O) -                                     | 15/15                       |
| 221   | SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh                             | 09/2003          | 6,285.33 -              | 10,667.00        | 6,332.94                    | 09/2010<br>08/2014    | 12/2017     | 87(O)<br>40(R)                             | 11/11                       |
| 222   | SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State            | 08/2010          | 170.36 -                | 170.36           | 90.67                       | 04/2013 -             | 12/2013     | 8(O) -                                     | 4/15                        |
| 223   | SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State             | 08/2008          | 2,360.95<br>2,580.90    | 2,580.90         | 2,059.77                    | 08/2012 -             | 03/2014     | 19(O) -                                    | 0/5                         |
| 224   | SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State         | 09/2012          | 1,508.74 -              | 1,508.74         | 75.99                       | 06/2016 -             | 04/2015     | -14(O) -                                   | 0/20                        |
| 225   | SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State           | 09/2012          | 1,935.35 -              | 1,935.35         | 244.36                      | 12/2014 -             | 11/2014     | -1(O) -                                    | 0/0                         |
| 226   | SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh         | 03/2012          | 213.78 -                | 213.78           | -                           | 03/2014 -             | 03/2014     | 0(O) -                                     | 0/7                         |
| 227   | SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh             | 12/2011          | 1,746.65 -              | 1,746.65         | 157.92                      | 08/2014 -             | 08/2014     | 0(O) -                                     | 2/19                        |
| 228   | SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra  | 02/2012          | 1,310.85 -              | 1,310.85         | 427.43                      | 02/2015 -             | 02/2015     | 0(O) -                                     | 0/14                        |
| 229   | SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State            | 06/2012          | 1,263.26 -              | 1,263.26         | 243.28                      | 11/2014 -             | 11/2014     | 0(O) -                                     | 0/16                        |
| 230   | SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh | 01/2012          | 1,422.85 -              | 1,422.85         | 393.32                      | 01/2015 -             | 01/2015     | 0(O) -                                     | 3/19                        |
| 231   | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State                  | 12/2011          | 297.33 -                | 297.33           | 132.02                      | 08/2014 -             | 08/2014     | 0(O) -                                     | 7/20                        |
| 232   | SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State                           | 10/2011          | 487.49 -                | 487.49           | 181.51                      | 06/2014 -             | 06/2014     | 0(O) -                                     | 7/20                        |
| 233   | System Strengthening -XII of SR - [N18000085]PGCIL,Multi State                               | 02/2010          | 232.34 -                | 232.34           | 153.02                      | 06/2012 -             | 09/2013     | 15(O) -                                    | 0/3                         |
| 234   | System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State          | 12/2009          | 1,216.83 -              | 1,216.83         | 900.28                      | 08/2012 -             | 06/2014     | 22(O) -                                    | 0/11                        |
| 235   | TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand                         | 11/2006          | 2,978.48 -              | 3,846.30         | 1,880.00                    | 03/2013 -             | 03/2016     | 36(O) -                                    | 2/15                        |

## Sector Wise Details

(Aug,2013)

|       |                                                                                               |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 236   | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal                             | 09/2005          | 1,061.38 -              | 1,501.75         | 1,376.77                    | 09/2009<br>06/2013    | 11/2014     | 62(O)<br>17(R)                             | 0/0                         |
| 237   | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh                           | 07/2006          | 1,657.00<br>2,978.86    | 2,978.86         | 509.53                      | 07/2010<br>02/2016    | 02/2017     | 79(O)<br>12(R)                             | 1/10                        |
| 238   | TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat        | 01/2012          | 259.28 -                | 259.28           | 108.70                      | 01/2014 -             | 01/2014     | 0(O)<br>-                                  | 3/18                        |
| 239   | TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State             | 12/2011          | 2,422.66 -              | 2,422.66         | 470.84                      | 08/2014 -             | 08/2014     | 0(O)<br>-                                  | 2/19                        |
| 240   | TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - - [N18000129]PGCIL,Multi State  | 02/2012          | 3,201.44 -              | 3,201.44         | 912.30                      | 10/2014 -             | 09/2014     | -1(O)<br>-                                 | 2/18                        |
| 241   | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State     | 10/2008          | 4,824.12 -              | 4,824.12         | 3,504.41                    | 10/2012 -             | 06/2014     | 20(O)<br>-                                 | 0/11                        |
| 242   | TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State               | 03/2011          | 2,569.25 -              | 2,569.25         | 1,813.91                    | 03/2014 -             | 05/2014     | 2(O)<br>-                                  | 4/15                        |
| 243   | TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh | 02/2012          | 324.33 -                | 324.33           | 40.34                       | 08/2014 -             | 08/2014     | 0(O)<br>-                                  | 7/20                        |
| 244   | TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh | 02/2012          | 1,927.16 -              | 1,927.16         | 401.94                      | 10/2014 -             | 10/2014     | 0(O)<br>-                                  | 3/16                        |
| 245   | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh       | 07/2006          | 557.24<br>775.25        | 775.25           | 645.72                      | 01/2010 -             | 07/2013     | -                                          | 2/11                        |
| 246   | TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State                 | 02/2009          | 184.19 -                | 184.19           | 157.27                      | 11/2011 -             | 09/2013     | 22(O)<br>-                                 | 0/4                         |
| 247   | TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State             | 12/2008          | 7,031.88 -              | 7,031.88         | 4,572.72                    | 12/2012 -             | 09/2013     | 9(O)<br>-                                  | 0/9                         |
| 248   | TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat        | 12/2011          | 552.44 -                | 552.44           | 323.50                      | 02/2014 -             | 02/2014     | 0(O)<br>-                                  | 3/17                        |
| 249   | TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh    | 08/2011          | 425.51 -                | 425.51           | 322.97                      | 10/2013 -             | 12/2013     | 2(O)<br>-                                  | 2/13                        |
| 250   | TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra             | 07/2011          | 181.93 -                | 181.93           | 136.41                      | 07/2013 -             | 12/2013     | 5(O)<br>-                                  | 0/13                        |
| 251   | TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State   | 09/2011          | 1,366.34 -              | 1,366.34         | 768.46                      | 12/2013 -             | 12/2014     | 12(O)<br>-                                 | 2/13                        |
| 252   | TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand               | 10/2011          | 558.26 -                | 558.26           | 166.39                      | 11/2013 -             | 09/2014     | 10(O)<br>-                                 | 7/20                        |
| 253   | TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha                  | 09/2010          | 2,074.86 -              | 2,074.86         | 1,202.80                    | 03/2013 -             | 05/2014     | 14(O)<br>-                                 | 4/15                        |
| 254   | TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha                  | 12/2010          | 2,743.19 -              | 2,743.19         | 1,670.12                    | 12/2013 -             | 05/2014     | 5(O)<br>-                                  | 0/13                        |
| 255   | TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhattisgarh   | 11/2011          | 2,127.51 -              | 2,127.51         | 1,081.67                    | 07/2014 -             | 07/2014     | 0(O)<br>-                                  | 2/14                        |
| 256   | TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura                                   | 07/2009          | 421.01<br>623.44        | 960.79           | 618.62                      | -<br>-                | 05/2014     | -<br>-                                     | 10/29                       |
| 257   | TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram                             | 01/2011          | 913.63 -                | 913.63           | 451.94                      | 07/2014 -             | 02/2015     | 7(O)<br>-                                  | 1/16                        |
| 258   | Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State             | 02/2010          | 2,144.00 -              | 2,144.00         | 1,371.71                    | 12/2012 -             | 06/2014     | 18(O)<br>-                                 | 0/11                        |

# Sector Wise Details

(Aug,2013)

|       |                                                                                           |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 259   | Transm System for development of Pooling stn. in N - [N18000077]PGCIL,West Bengal         | 04/2010          | 4,404.57 -              | 4,404.57         | 388.61                      | 01/2015 -             | 01/2015     | 0(O) -                                     | 0/20                        |
| 260   | Transmission System associated with Mauda Stage-II - [N18000153]PGCIL,Multi State         | 09/2013          | 1,575.30 -              | 1,575.30         | -                           | 05/2016 -             | 05/2016     | 0(O) -                                     | 0/0                         |
| 261   | Transmission System of Vindhuchal -IV And Rihand - [N18000076]PGCIL,Multi State           | 03/2010          | 4,672.99 -              | 4,672.99         | 2,650.25                    | 11/2012 -             | 03/2015     | 28(O) -                                    | 0/15                        |
| 262   | Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State  | 03/2011          | 1,585.12 -              | 1,585.12         | 1,014.35                    | 11/2013 -             | 12/2014     | 13(O) -                                    | 5/16                        |
| 263   | Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State        | 05/2010          | 250.03 -                | 250.03           | 63.41                       | 01/2013 -             | 12/2014     | 23(O) -                                    | 5/18                        |
| 264   | URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir                            | 08/2005          | 1,729.29 -              | 2,081.00         | 2,035.18                    | 11/2009<br>02/2013    | 10/2013     | 47(O)<br>8(R)                              | 0/4                         |
| 265   | VINDHYACHAL STTP STAGE-V - [N18000134]NTPC,Madhya pradesh                                 | 12/2011          | 3,180.40 -              | 3,180.40         | 438.00                      | 08/2015 -             | 08/2015     | 0(O) -                                     | 11/12                       |
| 266   | VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh                         | 01/2009          | 5,915.00 -              | 5,915.00         | 3,401.00                    | 10/2012 -             | 03/2013     | -                                          | 15/15                       |
| 267   | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand                 | 08/2008          | 2,491.58 -              | 3,745.08         | 360.37                      | 07/2014 -             | 05/2016     | 22(O) -                                    | 1/1                         |
| 268   | WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra                      | 12/2007          | 477.69 -                | 477.69           | 446.89                      | 09/2010 -             | -           | -                                          | 0/5                         |
| 269   | WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh | 03/2012          | 9,569.76 -              | 9,569.76         | 829.02                      | 06/2015 -             | 06/2015     | 0(O) -                                     | 3/28                        |
|       | Total                                                                                     |                  | 254,014.60 -            | 273,611.01       | 128,680.52                  |                       |             |                                            | 332/1395                    |
|       |                                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Railways</u>                                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
| 270   | 3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra                             | 04/2011          | 182.06 -                | 182.06           | 0.98                        | - -                   | -           | -                                          | 0/0                         |
| 271   | AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura                                      | 04/2008          | 813.34<br>813.34        | 1,741.00         | 483.28                      | 03/2014 -             | 12/2015     | 21(O) -                                    | 0/0                         |
| 272   | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh                 | 04/1999          | 108.00<br>427.21        | 432.72           | 394.63                      | 12/2009<br>03/2011    | 10/2013     | 46(O)<br>31(R)                             | 0/0                         |
| 273   | AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra                              | 02/1997          | 353.08<br>514.68        | 2,820.00         | 137.80                      | - -                   | -           | -                                          | 0/0                         |
| 274   | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State          | 12/2006          | 170.00<br>170.00        | 435.87           | 411.28                      | 03/2011<br>03/2011    | 03/2011     | -                                          | 0/0                         |
| 275   | AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra                                       | 06/1994          | 120.90<br>663.10        | 725.00           | 558.94                      | 06/1999<br>03/2011    | 03/2011     | -                                          | 0/0                         |
| 276   | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh                      | 03/2013          | 307.00 -                | 307.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 277   | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala                                     | 10/1998          | 550.00<br>517.70        | 1,566.00         | 119.70                      | - -                   | -           | -                                          | 0/0                         |
| 278   | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh                     | 03/2012          | 160.89 -                | 199.75           | 30.57                       | - -                   | -           | -                                          | 0/0                         |
| 279   | Agartala-Akhaura NL - [N22000195]NEFR,Tripura                                             | 04/2012          | 252.00 -                | 252.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 280   | Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat                                              | 04/2012          | 567.18 -                | 567.18           | -                           | - -                   | -           | -                                          | 0/0                         |
| 281   | Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat                                | 04/2008          | 394.14<br>385.60        | 1,215.30         | 7.32                        | 03/2013 -             | 03/2013     | -                                          | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                         |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 282   | Ajmer-Bangurgram - [N22000155]NWR,Rajasthan                                             | 04/2011          | 213.39<br>-             | 218.39           | 16.48                       | -<br>-                | -           | -                                          | 0/0                         |
| 283   | Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan                               | 04/2013          | 822.00<br>-             | 822.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 284   | Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh                                      | 04/2012          | 153.00<br>-             | 153.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 285   | Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State                              | 04/2008          | 184.26<br>-             | 2,000.00         | 20.68                       | -<br>-                | -           | -                                          | 0/0                         |
| 286   | Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan                                      | 04/2013          | 242.09<br>-             | 242.09           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 287   | Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State | 04/2010          | 338.54<br>-             | 338.54           | 75.48                       | -<br>-                | -           | -                                          | 0/0                         |
| 288   | Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam                                | 04/2011          | 312.12<br>-             | 312.12           | 29.93                       | -<br>-                | 03/2015     | -<br>-                                     | 0/0                         |
| 289   | Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi                         | 04/2012          | 295.68<br>-             | 295.68           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 290   | Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar                                            | 04/2008          | 490.80<br>-             | 490.80           | 0.39                        | -<br>-                | -           | -                                          | 0/0                         |
| 291   | Araria-Supaul (NL) - [N22000177]ECR,Bihar                                               | 04/2008          | 304.41<br>-             | 304.41           | 0.19                        | -<br>-                | -           | -                                          | 0/0                         |
| 292   | Attippattu-Puttur - [N22000184]SR,Tamil Nadu                                            | 04/2008          | 446.87<br>-             | 527.00           | 2.86                        | -<br>-                | -           | -                                          | 0/0                         |
| 293   | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka                           | 02/1999          | 138.00<br>901.62        | 901.62           | 0.42                        | -<br>-                | -           | -                                          | 0/0                         |
| 294   | BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal                               | 03/1998          | 111.90<br>1,028.05      | 1,423.98         | 482.24                      | 03/2005<br>12/2008    | 12/2016     | 141(O)<br>96(R)                            | 0/0                         |
| 295   | BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal                                        | 04/2007          | 245.15<br>1,106.62      | 1,106.62         | 225.42                      | 12/2010<br>03/2011    | 03/2011     | -                                          | 0/0                         |
| 296   | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra         | 03/1996          | 401.81<br>495.44        | 1,814.48         | 250.13                      | 03/2004<br>12/2010    | 12/2014     | 129(O)<br>48(R)                            | 0/0                         |
| 297   | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram                                    | 04/2008          | 619.34<br>-             | 2,384.34         | 96.18                       | 04/2014<br>-          | 03/2017     | 35(O)<br>-                                 | 0/0                         |
| 298   | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh                           | 03/2008          | 195.64<br>-             | 195.64           | 67.64                       | -<br>-                | -           | -                                          | 0/0                         |
| 299   | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh                           | 09/2007          | 687.20<br>-             | 800.00           | 735.19                      | 03/2010<br>-          | 12/2015     | 69(O)<br>-                                 | 0/0                         |
| 300   | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam                    | 09/1997          | 1,000.00<br>1,500.00    | 4,996.19         | 2,836.11                    | 04/2008<br>03/2014    | 12/2015     | 92(O)<br>21(R)                             | 0/0                         |
| 301   | Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka                                          | 04/2010          | 377.93<br>-             | 377.93           | 10.33                       | -<br>-                | -           | -                                          | 0/0                         |
| 302   | Bandel-Boinchi 3rd line - [N22000221]ER,Multi State                                     | 04/2011          | 288.35<br>-             | 288.35           | 3.99                        | -<br>-                | -           | -                                          | 0/0                         |
| 303   | Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal          | 04/1999          | 207.52<br>207.52        | 207.52           | 177.60                      | 12/2012<br>-          | 12/2013     | 12(O)<br>-                                 | 0/0                         |
| 304   | Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan                             | 04/2012          | 246.08<br>-             | 246.08           | 0.11                        | -<br>-                | -           | -                                          | 0/0                         |
| 305   | Bariaipuri-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State         | 04/2007          | 450.55<br>-             | 450.55           | 9.35                        | -<br>-                | -           | -                                          | 0/0                         |
| 306   | Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal                            | 04/2012          | 255.64<br>-             | 255.64           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 307   | Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh                          | 04/2010          | 337.49<br>-             | 337.49           | -                           | -<br>-                | -           | -                                          | 0/0                         |



## Sector Wise Details

(Aug,2013)

|       |                                                                                          |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 308   | Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh                                    | 04/2012          | 923.23 -                | 923.23           | -                           | - -                   | -           | -                                          | 0/0                         |
| 309   | Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal                          | 04/2011          | 289.64 -                | 289.64           | 0.04                        | - -                   | -           | -                                          | 0/0                         |
| 310   | Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh                              | 04/2008          | 1,046.88 -              | 2,966.99         | 37.72                       | - -                   | -           | -                                          | 0/0                         |
| 311   | Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat               | 04/2006          | 117.36 196.95           | 196.95           | 190.89                      | 03/2011 -             | -           | -                                          | 0/0                         |
| 312   | Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat               | 04/2008          | 318.24 -                | 238.24           | 1.71                        | 03/2012 -             | -           | -                                          | 0/0                         |
| 313   | Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar                                            | 04/2008          | 326.20 -                | 326.20           | 1.69                        | - -                   | -           | -                                          | 0/0                         |
| 314   | Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State                                  | 04/2011          | 175.80 -                | 175.80           | 0.84                        | - -                   | -           | -                                          | 0/0                         |
| 315   | Bowaichandi-Arambagh - [N22000159]SER,West Bengal                                        | 04/2010          | 267.37 -                | 267.37           | 33.74                       | - -                   | -           | -                                          | 0/0                         |
| 316   | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State                                  | 02/1996          | 240.00 -                | 579.37           | 599.40                      | - -                   | 02/2012     | -                                          | 0/0                         |
| 317   | CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab                               | 07/1998          | 248.44 576.27           | 1,115.21         | 969.33                      | 12/2012 01/2013       | 04/2013     | -                                          | 0/0                         |
| 318   | CHHAPRA-BALLIA UP - [N22000134]NER,Multi State                                           | 03/2013          | 295.00 -                | 295.00           | 0.06                        | - -                   | -           | -                                          | 0/0                         |
| 319   | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar                 | 03/2005          | 470.09 1,417.97         | 1,417.97         | 1,011.09                    | - -                   | 03/2012     | -                                          | 0/0                         |
| 320   | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh                          | 04/2005          | 383.79 -                | 585.93           | 194.91                      | - -                   | 12/2013     | -                                          | 0/0                         |
| 321   | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State              | 03/2007          | 243.78 -                | 243.78           | 27.24                       | - -                   | -           | -                                          | 0/0                         |
| 322   | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh   | 09/1996          | 156.00 156.00           | 406.40           | 350.63                      | - -                   | 12/2013     | -                                          | 0/0                         |
| 323   | Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha                        | 04/2010          | 149.90 -                | 177.38           | 41.41                       | 03/2015 -             | 12/2015     | 9(O) -                                     | 0/0                         |
| 324   | Chandigarh-Baddi NL - [N22000296]NR,Multi State                                          | 04/2007          | 328.14 -                | 328.14           | 0.18                        | - -                   | -           | -                                          | 0/0                         |
| 325   | Chandpara-Bangaon doubling with exension to Chandb - [N22000242]ER,Multi State           | 04/2003          | 337.96 -                | 337.96           | 59.00                       | - -                   | -           | -                                          | 0/0                         |
| 326   | Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu  | 04/2007          | 247.00 -                | 951.24           | 516.64                      | - -                   | -           | -                                          | 0/0                         |
| 327   | Chengannur-Chingavanam - [N22000203]SR,Kerala                                            | 04/2006          | 191.72 -                | 191.72           | 80.62                       | - -                   | -           | -                                          | 0/0                         |
| 328   | Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu               | 04/1999          | 271.24 -                | 520.00           | 458.21                      | - -                   | -           | -                                          | 0/0                         |
| 329   | Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State                           | 04/2008          | 523.52 -                | 1,200.00         | 1.65                        | - -                   | -           | -                                          | 0/0                         |
| 330   | Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar                                         | 04/2006          | 285.07 -                | 378.56           | 104.59                      | - -                   | -           | -                                          | 0/0                         |
| 331   | Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka                                 | 04/2013          | 327.25 -                | 327.25           | -                           | - -                   | -           | -                                          | 0/0                         |
| 332   | Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka            | 04/2013          | 558.00 -                | 558.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 333   | Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER,Multi State | 04/2005          | 595.91 -                | 595.91           | 88.57                       | - -                   | -           | -                                          | 0/0                         |



## Sector Wise Details

(Aug,2013)

|       |                                                                                          |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 334   | Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State                                        | 04/2007          | 1,347.26<br>-           | 1,347.26         | 138.49                      | -<br>-                | -           | -                                          | 0/0                         |
| 335   | Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal      | 04/2009          | 573.78<br>-             | 573.78           | 166.84                      | -<br>-                | -           | -                                          | 0/0                         |
| 336   | Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura                     | 04/1999          | 895.00<br>-             | 1,151.00         | 944.78                      | 03/2007<br>-          | 03/2015     | 96(O)<br>-                                 | 0/0                         |
| 337   | Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu                          | 04/1999          | 198.68<br>-             | 556.64           | 266.14                      | -<br>-                | -           | -                                          | 0/0                         |
| 338   | Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh                                       | 04/2013          | 829.00<br>-             | 829.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 339   | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh         | 04/1995          | 304.00<br>-             | 968.60           | 130.98                      | 12/2012<br>-          | -           | -                                          | 0/0                         |
| 340   | DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar                                     | 04/2001          | 104.79<br>-             | 406.92           | 103.68                      | -<br>-                | -           | -                                          | 0/0                         |
| 341   | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan                                   | 02/1997          | 151.84<br>410.08        | 410.08           | 238.17                      | -<br>-                | 03/2014     | -<br>-                                     | 0/0                         |
| 342   | DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER,Multi State                                | 04/2000          | 138.00<br>607.09        | 607.09           | 499.64                      | 12/2012<br>12/2012    | 02/2013     | -                                          | 0/0                         |
| 343   | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu             | 09/2006          | 343.17<br>343.17        | 914.98           | 664.99                      | -<br>-                | 12/2012     | -                                          | 0/0                         |
| 344   | Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State             | 04/2007          | 1,640.04<br>-           | 1,640.04         | 151.33                      | -<br>-                | -           | -                                          | 0/0                         |
| 345   | Dakshin-barasal-lakshmikanthapur - [N22000116]ER,West Bengal                             | 04/2009          | 259.51<br>533.38        | 533.38           | 99.68                       | 12/2011<br>02/2012    | 02/2012     | -                                          | 0/0                         |
| 346   | Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164]SER,Jharkhand                       | 04/2010          | 309.44<br>-             | 388.67           | 42.01                       | 12/2015<br>-          | 12/2015     | 0(O)<br>-                                  | 0/0                         |
| 347   | Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER,Multi State | 04/2010          | 296.44<br>-             | 296.44           | 2.80                        | -<br>-                | -           | -                                          | 0/0                         |
| 348   | Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar                                    | 04/2005          | 366.73<br>-             | 366.73           | 3.81                        | -<br>-                | -           | -                                          | 0/0                         |
| 349   | Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State                        | 04/2013          | 1,239.00<br>-           | 1,239.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 350   | Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State                          | 04/2007          | 336.91<br>-             | 336.91           | 140.60                      | -<br>-                | -           | -                                          | 0/0                         |
| 351   | Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat                                              | 04/2012          | 376.59<br>-             | 376.59           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 352   | Dholpur-Sirmuttra with extension to Gangapurcity A - [N22000158]NCR,Multi State          | 04/2010          | 622.41<br>2,030.50      | 2,030.50         | 1.22                        | 02/2019<br>-          | 02/2019     | 0(O)<br>-                                  | 0/0                         |
| 353   | Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State                  | 04/2010          | 553.63<br>-             | 651.17           | 7.08                        | -<br>-                | -           | -                                          | 0/0                         |
| 354   | Dimapur-Tizit NL - [N22000196]NEFR,Nagaland                                              | 04/2013          | 4,274.00<br>-           | 4,274.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 355   | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal   | 03/2013          | 4,874.58<br>-           | 4,874.58         | -                           | 03/2016<br>-          | 03/2016     | 0(O)<br>-                                  | 0/0                         |
| 356   | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G* - [N22000094]RE,Uttar Pradesh         | 02/2008          | 171.10<br>224.89        | 246.44           | 141.55                      | 03/2012<br>12/2013    | 03/2014     | 24(O)<br>3(R)                              | 0/0                         |
| 357   | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh                                  | 09/2001          | 129.70<br>245.39        | 245.39           | 230.40                      | 12/2008<br>-          | 09/2014     | 69(O)<br>-                                 | 0/0                         |
| 358   | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu             | 04/2006          | 495.74<br>-             | 495.74           | 250.82                      | 06/2013<br>06/2013    | 12/2014     | 18(O)<br>18(R)                             | 0/0                         |

# Sector Wise Details

(Aug,2013)

|       |                                                                                         |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                 | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                       | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 359   | Ernakulam-Kumbalam - [N22000204]SR,Kerala                                               | 04/2010          | 189.24 -                | 189.24           | 1.88                        | - -                   | -           | -                                          | 0/0                         |
| 360   | Erode-Palani - [N22000199]SR,Tamil Nadu                                                 | 04/2008          | 288.57 -                | 603.22           | 1.31                        | - -                   | -           | -                                          | 0/0                         |
| 361   | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State              | 03/1984          | 520.00 835.04           | 835.04           | 602.18                      | 03/1995 -             | 03/2015     | 240(O) -                                   | 0/0                         |
| 362   | Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareli - [N22000270]NR,Uttar Pradesh | 04/2013          | 654.00 -                | 654.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 363   | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State                                 | 04/1998          | 92.63 228.09            | 270.00           | 281.00                      | 02/2011 02/2011       | 03/2013     | -                                          | 0/0                         |
| 364   | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand                                | 03/1997          | 186.92 261.70           | 261.70           | 110.96                      | 02/2006 -             | -           | -                                          | 0/0                         |
| 365   | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh  | 03/2002          | 381.17 863.23           | 863.23           | 719.19                      | - -                   | 03/2012     | -                                          | 0/0                         |
| 366   | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State                                | 02/1997          | 386.30 1,038.00         | 1,038.00         | 590.26                      | 03/1998 -             | -           | -                                          | 0/0                         |
| 367   | GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka                                       | 02/1998          | 242.42 369.70           | 832.00           | 354.21                      | - 05/2009             | 05/2009     | -                                          | 0/0                         |
| 368   | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State          | 04/1986          | 158.77 580.83           | 580.83           | 579.43                      | 03/1994 -             | 10/2013     | 235(O) -                                   | 0/0                         |
| 369   | Gadag-Wadi NL - [N22000299]SWR,Karnataka                                                | 04/2013          | 1,117.00 -              | 1,117.00         | -                           | - -                   | -           | -                                          | 0/0                         |
| 370   | Gaya-Chatra (NL) - [N22000169]ECOR,Multi State                                          | 04/2008          | 415.67 -                | 415.67           | 12.91                       | - -                   | -           | -                                          | 0/0                         |
| 371   | Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar                               | 04/2008          | 445.25 -                | 445.25           | 0.94                        | - -                   | -           | -                                          | 0/0                         |
| 372   | Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal                                   | 04/2009          | 189.97 611.03           | 611.03           | 130.61                      | 12/2011 11/2013       | 11/2013     | 23(O) 0(R)                                 | 0/0                         |
| 373   | Grade Seperator at Dayabasti - [N22000269]NR,Delhi                                      | 04/1999          | 159.20 -                | 159.20           | 49.08                       | - -                   | -           | -                                          | 0/0                         |
| 374   | Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh                                 | 04/2011          | 283.54 -                | 283.54           | 0.02                        | - -                   | -           | -                                          | 0/0                         |
| 375   | Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan                           | 04/2011          | 239.73 -                | 206.22           | 2.45                        | - -                   | -           | -                                          | 0/0                         |
| 376   | Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State             | 04/2011          | 1,176.09 3,845.60       | 3,845.60         | 1.52                        | 02/2020 -             | 02/2020     | 0(O) -                                     | 0/0                         |
| 377   | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar                           | 04/2003          | 324.66 528.65           | 528.65           | 190.53                      | - -                   | -           | -                                          | 0/0                         |
| 378   | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha                                        | 04/1996          | 301.64 -                | 1,185.64         | 240.58                      | - 09/2009             | -           | -                                          | 0/0                         |
| 379   | HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar             | 04/2003          | 98.74 224.51            | 337.30           | 222.07                      | - -                   | 03/2012     | -                                          | 0/0                         |
| 380   | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka                | 02/1997          | 295.00 412.91           | 412.91           | 672.78                      | - -                   | 01/2013     | -                                          | 0/0                         |
| 381   | HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State                                  | 04/2005          | 230.03 230.03           | 230.03           | 149.24                      | - -                   | 03/2014     | -                                          | 0/0                         |
| 382   | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal                           | 04/1974          | 31.42 393.46            | 535.40           | 177.85                      | 03/2007 03/2007       | 03/2015     | 96(O) 96(R)                                | 0/0                         |
| 383   | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka                                         | 04/1997          | 227.00 997.58           | 2,135.00         | 101.17                      | - -                   | -           | -                                          | 0/0                         |
| 384   | Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State         | 04/2000          | 157.17 -                | 157.17           | 75.86                       | - -                   | -           | -                                          | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                                |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                        | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                              | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 385   | Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar                                         | 04/2013          | 213.01 -                | 213.01           | -                           | -                     | -           | -                                          | 0/0                         |
| 386   | Hansdiha-Godda NL - [N22000236]ER,Multi State                                                  | 04/2011          | 267.09 -                | 267.09           | 0.10                        | -                     | -           | -                                          | 0/0                         |
| 387   | Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State                                   | 04/2010          | 172.03 -                | 172.03           | 2.61                        | -                     | -           | -                                          | 0/0                         |
| 388   | Haridwar-Laksar - [N22000289]NR,Uttarakhand                                                    | 04/2012          | 219.83 -                | 444.18           | -                           | -                     | -           | -                                          | 0/0                         |
| 389   | Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan                        | 04/2008          | 829.74 829.74           | 829.74           | 30.04                       | 03/2015 -             | 03/2015     | 0(O) -                                     | 0/0                         |
| 390   | Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana                                  | 04/2013          | 400.00 -                | 400.00           | -                           | -                     | -           | -                                          | 0/0                         |
| 391   | Hospet-Hubli-Londa-Vasco-dagama DL - [N22000297]SWR,Karnataka                                  | 04/2010          | 2,127.00 -              | 2,127.00         | 47.34                       | -                     | -           | -                                          | 0/0                         |
| 392   | Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State         | 04/2010          | 157.94 -                | 157.94           | 37.82                       | -                     | -           | -                                          | 0/0                         |
| 393   | Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State       | 04/2011          | 166.89 -                | 166.89           | -                           | -                     | -           | -                                          | 0/0                         |
| 394   | Hyderabad/Secunderabad Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP,Andhra Pradesh | 04/2012          | 632.68 -                | 816.55           | 0.40                        | 04/2012 -             | -           | -                                          | 0/0                         |
| 395   | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State                             | 03/2002          | 409.00 625.30           | 847.75           | 836.10                      | 06/2007 -             | 06/2007     | -                                          | 0/0                         |
| 396   | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar                               | 04/1997          | 233.00 501.69           | 1,043.56         | 712.97                      | 03/2012 08/2012       | -           | -                                          | 0/0                         |
| 397   | JIND-SONEPAT (NL),NR - [220100280]NR,Haryana                                                   | 01/2004          | 190.81 238.56           | 693.39           | 472.03                      | 03/2012 03/2012       | 12/2012     | -                                          | 0/0                         |
| 398   | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur                                  | 04/2003          | 727.56 727.53           | 4,453.50         | 1,595.53                    | 03/2011 03/2014       | 03/2017     | 72(O) 36(R)                                | 0/0                         |
| 399   | Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan                  | 04/2008          | 653.19 653.19           | 653.47           | 246.16                      | 03/2014 -             | 03/2014     | 0(O) -                                     | 0/0                         |
| 400   | Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State                               | 04/2008          | 165.65 -                | 165.65           | 131.01                      | -                     | -           | -                                          | 0/0                         |
| 401   | Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar            | 04/2009          | 470.00 -                | 470.00           | 34.32                       | -                     | -           | -                                          | 0/0                         |
| 402   | KADUR-CHIKMAGALUR-SAKLISHPUR (NL),(SWR) - [220100190]SWR,Karnataka                             | 04/1996          | 157.00 262.82           | 333.50           | 308.25                      | 03/2012 03/2012       | 03/2013     | -                                          | 0/0                         |
| 403   | KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh                                  | 03/1997          | 395.00 1,577.45         | 1,708.41         | 1,475.25                    | -                     | 03/2013     | -                                          | 0/0                         |
| 404   | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh      | 03/2013          | 643.00 -                | 643.00           | -                           | -                     | -           | -                                          | 0/0                         |
| 405   | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State                           | 04/1999          | 323.40 323.40           | 744.71           | 513.75                      | -                     | 03/2014     | -                                          | 1/1                         |
| 406   | KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu                                                  | 02/1997          | 155.55 155.00           | 775.36           | 754.44                      | -                     | 10/2012     | -                                          | 0/0                         |
| 407   | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar                                           | 09/2001          | 100.00 492.98           | 1,041.79         | 742.54                      | 12/2010 12/2010       | 03/2015     | 51(O) 51(R)                                | 0/0                         |
| 408   | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar                                   | 04/1997          | 78.23 162.87            | 162.87           | 122.54                      | -                     | -           | -                                          | 0/0                         |
| 409   | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha                             | 04/2000          | 133.41 207.00           | 276.00           | 254.02                      | 03/2009 03/2009       | 08/2014     | 65(O) 65(R)                                | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                          |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 410   | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha                                    | 04/1994          | 355.38<br>470.21        | 1,995.25         | 260.49                      | -<br>-                | 03/2014     | -<br>-                                     | 0/0                         |
| 411   | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                                   | 04/2008          | 282.92<br>282.92        | 359.86           | 1.22                        | -<br>-                | 03/2015     | -<br>-                                     | 0/0                         |
| 412   | KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand                                      | 04/1996          | 371.36<br>768.87        | 768.87           | 492.05                      | -<br>03/2010          | 03/2010     | -                                          | 0/0                         |
| 413   | KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand                         | 03/1999          | 491.19<br>2,957.21      | 2,957.21         | 1,604.44                    | 07/2005<br>-          | -           | -                                          | 0/0                         |
| 414   | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand                                     | 04/2002          | 459.91<br>418.17        | 418.17           | 167.82                      | -<br>-                | -           | -                                          | 0/0                         |
| 415   | KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar                                             | 04/2002          | 323.41<br>322.95        | 341.41           | 288.78                      | 03/2012<br>03/2013    | 03/2013     | -                                          | 0/0                         |
| 416   | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh                           | 12/2001          | 330.00<br>1,047.00      | 1,045.20         | 9.41                        | -<br>-                | -           | -                                          | 0/0                         |
| 417   | KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka                                      | 04/1995          | 65.94<br>302.23         | 302.23           | 354.49                      | -<br>-                | 12/2012     | -                                          | 0/0                         |
| 418   | Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State            | 04/2008          | 2,050.00<br>-           | 2,050.00         | 92.24                       | -<br>-                | -           | -                                          | 0/0                         |
| 419   | Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER,Multi State  | 04/2001          | 923.52<br>-             | 923.52           | 232.05                      | -<br>-                | -           | -                                          | 0/0                         |
| 420   | Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER,Multi State | 04/2010          | 174.56<br>-             | 174.56           | 44.71                       | -<br>-                | -           | -                                          | 0/0                         |
| 421   | Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra                                       | 04/2011          | 277.70<br>-             | 277.70           | 1.64                        | -<br>-                | -           | -                                          | 0/0                         |
| 422   | Katakhal to Bhairabi - [N22000126]NEFR,Assam                                             | 04/1998          | 227.90<br>227.90        | 223.01           | 125.93                      | 12/2012<br>-          | 03/2015     | 27(O)<br>-                                 | 0/0                         |
| 423   | Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State      | 04/2010          | 423.66<br>-             | 423.66           | 132.84                      | 03/2017<br>-          | 03/2017     | 0(O)<br>-                                  | 0/0                         |
| 424   | Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State          | 04/2012          | 1,054.35<br>-           | 1,054.35         | 0.18                        | -<br>-                | -           | -                                          | 0/0                         |
| 425   | Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka                                         | 04/2006          | 287.99<br>-             | 287.99           | 421.25                      | 01/1999<br>-          | 12/2013     | 179(O)<br>-                                | 0/0                         |
| 426   | Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh                                  | 04/2013          | 723.00<br>-             | 723.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 427   | Kumbalam-Turavur - [N22000191]SR,Kerala                                                  | 04/2011          | 252.96<br>-             | 252.96           | 1.48                        | -<br>-                | -           | -                                          | 0/0                         |
| 428   | Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar                                           | 04/2008          | 192.56<br>-             | 192.56           | 0.38                        | -<br>-                | -           | -                                          | 0/0                         |
| 429   | Kuruppanthara-Chingavanam - [N22000190]SR,Multi State                                    | 04/2007          | 270.14<br>-             | 270.14           | 6.69                        | -<br>-                | -           | -                                          | 0/0                         |
| 430   | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State                      | 09/1998          | 925.00<br>-             | 1,630.97         | 394.38                      | 05/2008<br>03/2011    | -           | -                                          | 0/0                         |
| 431   | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha                                    | 04/1993          | 100.00<br>142.98        | 227.94           | 229.30                      | 03/2002<br>-          | 09/2013     | 138(O)<br>-                                | 0/0                         |
| 432   | Lakshmikantapur-Namkhana subsequently MM for Namkh - [N22000216]ER,Multi State           | 04/1999          | 406.99<br>-             | 406.99           | 137.78                      | -<br>-                | -           | -                                          | 0/0                         |
| 433   | Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244]ER,Multi State | 04/2009          | 257.42<br>-             | 257.42           | 32.87                       | 03/2014<br>-          | 03/2014     | 0(O)<br>-                                  | 0/0                         |
| 434   | Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam                             | 04/2012          | 246.07<br>-             | 246.07           | 0.11                        | -<br>-                | -           | -                                          | 0/0                         |
| 435   | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam               | 04/1996          | 1,676.31<br>1,676.31    | 5,000.00         | 3,635.42                    | 03/2009<br>-          | 12/2014     | 69(O)<br>-                                 | 0/0                         |

# Sector Wise Details

(Aug,2013)

|       |                                                                                    |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                            | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                  | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 436   | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh                         | 07/1998          | 125.00<br>363.26        | 480.00           | 0.61                        | 07/2008<br>-          | 07/2008     | -                                          | 0/0                         |
| 437   | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar                              | 04/2003          | 218.19<br>218.19        | 472.00           | 177.85                      | -<br>-                | 02/2013     | -                                          | 0/0                         |
| 438   | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand                       | 04/1995          | 184.00<br>900.05        | 900.05           | 727.13                      | 12/2011<br>12/2011    | 03/2013     | -                                          | 0/0                         |
| 439   | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh                 | 04/2006          | 378.56<br>671.82        | 791.59           | 0.76                        | -<br>-                | -           | -                                          | 0/0                         |
| 440   | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar           | 04/1996          | 114.01<br>332.92        | 477.88           | 438.36                      | 03/2012<br>03/2013    | 03/2013     | -                                          | 0/0                         |
| 441   | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu     | 09/2007          | 404.19<br>404.19        | 1,383.45         | 349.12                      | -<br>-                | -           | -                                          | 0/0                         |
| 442   | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra              | 04/2008          | 5,300.00<br>5,300.00    | 6,220.15         | 1,294.74                    | 03/2014<br>03/2016    | 12/2016     | 33(O)<br>9(R)                              | 0/0                         |
| 443   | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State                       | 04/1997          | 218.24<br>377.32        | 645.00           | 248.11                      | -<br>-                | 03/2012     | -                                          | 0/0                         |
| 444   | Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu                                   | 04/2008          | 164.41<br>-             | 260.72           | 10.55                       | -<br>-                | -           | -                                          | 0/0                         |
| 445   | Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State                    | 04/2011          | 601.43<br>-             | 800.00           | 0.13                        | -<br>-                | -           | -                                          | 0/0                         |
| 446   | Magrahat-Diamond Harbour with MM Sangrampur-Krishna - [N22000243]ER,Multi State    | 04/2009          | 493.96<br>-             | 493.96           | 115.46                      | -<br>-                | -           | -                                          | 0/0                         |
| 447   | Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand                 | 04/2012          | 258.20<br>-             | 258.20           | -                           | -<br>-                | 03/2016     | -                                          | 0/0                         |
| 448   | Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh                              | 04/2013          | 1,112.00<br>-           | 1,112.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 449   | Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur - [N22000152]NWR,Rajasthan | 04/2013          | 456.00<br>-             | 965.16           | 557.35                      | -<br>-                | -           | -                                          | 0/0                         |
| 450   | Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh                         | 04/2012          | 289.79<br>-             | 289.79           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 451   | Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat                         | 04/2011          | 439.88<br>-             | 439.88           | 0.63                        | -<br>-                | -           | -                                          | 0/0                         |
| 452   | Monigram- Nimtita - [N22000301]ER,Multi State                                      | 04/2012          | 250.93<br>-             | 250.93           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 453   | Motihari-Sitamari (NL) - [N22000174]ECR,Bihar                                      | 04/2006          | 211.00<br>-             | 211.00           | 4.41                        | -<br>-                | -           | -                                          | 0/0                         |
| 454   | Mudkhed-Parbhani - [N22000283](SCR),Maharashtra                                    | 04/2011          | 390.60<br>-             | 390.60           | 0.63                        | -<br>-                | -           | -                                          | 0/0                         |
| 455   | Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka                         | 04/2007          | 179.65<br>-             | 645.00           | 248.11                      | -<br>-                | -           | -                                          | 0/0                         |
| 456   | Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State                             | 04/2011          | 165.82<br>-             | 165.82           | 0.25                        | -<br>-                | -           | -                                          | 0/0                         |
| 457   | Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar                                  | 04/2008          | 281.30<br>-             | 281.30           | 0.58                        | -<br>-                | -           | -                                          | 0/0                         |
| 458   | Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar                   | 04/2008          | 228.05<br>-             | 228.05           | 0.39                        | -<br>-                | -           | -                                          | 0/0                         |
| 459   | NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh                        | 03/1996          | 155.74<br>429.49        | 883.00           | 657.88                      | 02/2009<br>-          | 03/2012     | -                                          | 0/0                         |
| 460   | NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State                               | 03/1981          | 37.68<br>450.00         | 1,036.78         | 357.74                      | 07/2012<br>-          | -           | -                                          | 0/0                         |
| 461   | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar         | 09/2006          | 300.00<br>300.00        | 532.87           | 40.88                       | -<br>-                | -           | -                                          | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                  |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 462   | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam       | 09/2006          | 200.00<br>200.00        | 385.20           | 139.95                      | -<br>-                | 03/2015     | -<br>-                                     | 0/0                         |
| 463   | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State | 04/2000          | 733.00<br>733.00        | 2,350.00         | 1,477.35                    | 12/2008<br>-          | 03/2015     | 75(O)<br>-                                 | 0/0                         |
| 464   | Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State                         | 04/2010          | 169.82<br>-             | 169.82           | 32.10                       | -<br>-                | -           | -                                          | 0/0                         |
| 465   | Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh                         | 04/2011          | 1,313.48<br>-           | 1,313.48         | 0.10                        | -<br>-                | -           | -                                          | 0/0                         |
| 466   | Nawada-Laxmipur (NL) - [N22000167]SER,Bihar                                      | 04/2008          | 620.57<br>-             | 620.57           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 467   | New Alipur to Akra, MM for Budge Budge-Pujali NL, - [N22000240]ER,Multi State    | 04/2010          | 494.54<br>-             | 494.54           | 31.92                       | -<br>-                | -           | -                                          | 0/0                         |
| 468   | New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal | 04/1983          | 36.80<br>274.41         | 703.17           | 250.35                      | -<br>-                | 03/2015     | -<br>-                                     | 0/0                         |
| 469   | New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State            | 04/2010          | 242.22<br>-             | 242.22           | 37.72                       | -<br>-                | -           | -                                          | 0/0                         |
| 470   | New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya                | 04/2010          | 4,083.02<br>-           | 4,083.02         | 2.60                        | -<br>-                | -           | -                                          | 0/0                         |
| 471   | New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State                | 04/1999          | 175.43<br>-             | 247.75           | 145.43                      | -<br>-                | 03/2014     | -<br>-                                     | 0/0                         |
| 472   | New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State             | 04/2010          | 241.52<br>-             | 238.83           | 98.33                       | -<br>-                | -           | -                                          | 0/0                         |
| 473   | New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal           | 04/2010          | 221.42<br>-             | 221.42           | 21.44                       | -<br>-                | -           | -                                          | 0/0                         |
| 474   | New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State           | 04/2013          | 1,798.00<br>-           | 1,798.00         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 475   | New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal                        | 04/2011          | 209.77<br>-             | 209.77           | 20.93                       | -<br>-                | 03/2015     | -<br>-                                     | 0/0                         |
| 476   | New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal    | 04/2012          | 283.55<br>-             | 283.55           | 0.40                        | -<br>-                | 03/2015     | -<br>-                                     | 0/0                         |
| 477   | New Jalpaiguri-Siliguri-New Bongaigaon including B - [N22000209]NEFR,Multi State | 04/1999          | 523.17<br>-             | 1,393.44         | 1,032.88                    | -<br>-                | -           | -                                          | 0/0                         |
| 478   | New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland    | 04/2006          | 850.00<br>850.00        | 2,441.48         | 8.94                        | 03/2015<br>-          | 03/2017     | 24(O)<br>-                                 | 0/0                         |
| 479   | New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal         | 04/2010          | 2,619.02<br>-           | 2,913.51         | 324.72                      | 03/2016<br>-          | 03/2016     | 0(O)<br>-                                  | 0/0                         |
| 480   | New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal | 04/2010          | 2,069.60<br>-           | 2,298.42         | 58.94                       | 03/2014<br>-          | 03/2014     | 0(O)<br>-                                  | 0/0                         |
| 481   | New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal | 04/2010          | 3,951.98<br>-           | 3,951.98         | -                           | 03/2016<br>-          | 03/2016     | 0(O)<br>-                                  | 0/0                         |
| 482   | New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal | 04/2010          | 2,397.72<br>-           | 2,397.72         | 56.63                       | 03/2016<br>-          | 06/2016     | 3(O)<br>-                                  | 0/0                         |
| 483   | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh              | 07/2006          | 743.00<br>-             | 1,117.11         | 457.21                      | 03/2008<br>06/2008    | -           | -                                          | 0/0                         |
| 484   | PANVEL PEN DOUBLING - [N22000255]CR,Multi State                                  | 04/2006          | 191.00<br>-             | 191.00           | 195.08                      | -<br>-                | 12/2013     | -<br>-                                     | 0/0                         |
| 485   | PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar                              | 04/2001          | 624.47<br>2,921.00      | 2,921.00         | 1,854.28                    | 10/2007<br>12/2012    | 12/2015     | 98(O)<br>36(R)                             | 0/0                         |
| 486   | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh           | 12/1994          | 124.43<br>495.68        | 925.30           | 624.87                      | -<br>-                | 03/2012     | -                                          | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                  |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                          | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 487   | PEN ROHA DOUBLING - [N22000254]CR,Multi State                                    | 04/2007          | 203.00<br>-             | 203.00           | 154.83                      | -<br>-                | -           | -                                          | 0/0                         |
| 488   | Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat                                | 04/2013          | 1,266.89<br>-           | 1,266.89         | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 489   | Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal                    | 04/2004          | 225.68<br>293.74        | 293.74           | 139.20                      | 12/2010<br>12/2010    | 12/2010     | -                                          | 0/0                         |
| 490   | Pirpainti-Bhagalpur - [N22000222]ER,Multi State                                  | 04/2011          | 261.38<br>-             | 261.38           | 14.11                       | -<br>-                | -           | -                                          | 0/0                         |
| 491   | Pirpainti-Jasidih - [N22000219]ER,Multi State                                    | 04/2013          | 915.98<br>-             | 915.98           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 492   | Plassey-Jiaganj Doubling - [N22000220]ER,Multi State                             | 04/2011          | 248.07<br>-             | 248.07           | 8.91                        | 03/2015<br>-          | 03/2015     | 0(O)<br>-                                  | 0/0                         |
| 493   | Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State    | 04/2011          | 299.60<br>-             | 299.60           | 1.09                        | 03/2017<br>-          | 03/2017     | 0(O)<br>-                                  | 0/0                         |
| 494   | Pushkar-Merta - [N22000151]NWR,Rajasthan                                         | 04/2013          | 323.00<br>-             | 323.00           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 495   | QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State      | 03/1998          | 280.00<br>842.35        | 1,029.92         | 814.96                      | -<br>-                | 03/2013     | -                                          | 0/6                         |
| 496   | Qadian-Beas - [N22000295]NR,Punjab                                               | 04/2011          | 205.22<br>-             | 205.22           | 1.22                        | -<br>-                | -           | -                                          | 0/0                         |
| 497   | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh                       | 04/2003          | 136.62<br>-             | 289.93           | 264.04                      | 12/2007<br>03/2010    | -           | -                                          | 0/0                         |
| 498   | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar                  | 04/2002          | 921.00<br>2,363.00      | 2,363.00         | 1,146.14                    | 03/2009<br>12/2012    | 12/2014     | 69(O)<br>24(R)                             | 0/0                         |
| 499   | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha                               | 04/1999          | 166.16<br>-             | 288.00           | 281.73                      | 02/2009<br>02/2009    | 08/2014     | 66(O)<br>66(R)                             | 0/0                         |
| 500   | RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh                     | 04/2001          | 727.13<br>727.13        | 1,225.90         | 227.34                      | -<br>-                | -           | -                                          | 0/0                         |
| 501   | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand                              | 04/1997          | 194.07<br>194.07        | 596.00           | 347.58                      | 06/2004<br>-          | 12/2012     | -                                          | 0/0                         |
| 502   | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State | 01/2004          | 915.70<br>915.70        | 3,019.17         | 2,174.43                    | -<br>-                | 03/2014     | -<br>-                                     | 0/0                         |
| 503   | RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha                               | 02/1996          | 57.94<br>604.04         | 639.97           | 175.75                      | 03/1998<br>08/2005    | 08/2005     | -                                          | 0/0                         |
| 504   | Rajkot-Veraval,Wansjalai to Jataisar with new MM f - [N22000143]WR,Gujarat       | 04/1994          | 320.66<br>-             | 320.66           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 505   | Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka    | 04/2007          | 482.00<br>482.70        | 482.70           | 486.44                      | 03/2013<br>-          | 03/2014     | 12(O)<br>-                                 | 0/0                         |
| 506   | Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan                        | 04/2012          | 288.97<br>-             | 288.97           | -                           | -<br>-                | -           | -                                          | 0/0                         |
| 507   | Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And - [N22000153]NWR,Rajasthan     | 04/2010          | 739.65<br>-             | 872.22           | 788.94                      | -<br>-                | -           | -                                          | 0/0                         |
| 508   | Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State                  | 04/2012          | 2,082.75<br>-           | 2,082.75         | 9.85                        | -<br>-                | -           | -                                          | 0/0                         |
| 509   | Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh                    | 04/2008          | 603.04<br>603.04        | 1,421.25         | 252.84                      | 03/2012<br>-          | -           | -                                          | 0/0                         |
| 510   | Rayadurga-Tumkur NL - [N22000279]SWR,Multi State                                 | 04/2007          | 970.34<br>-             | 970.34           | 188.92                      | -<br>-                | -           | -                                          | 0/0                         |
| 511   | Rohtak-Meham Hansi - [N22000272]NR,Haryana                                       | 04/2012          | 287.00<br>-             | 287.00           | 0.04                        | -<br>-                | -           | -                                          | 0/0                         |
| 512   | Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra           | 04/2012          | 714.10<br>-             | 714.10           | 2.42                        | -<br>12/2017          | 12/2017     | -<br>0(R)                                  | 0/0                         |



# Sector Wise Details

(Aug,2013)

|       |                                                                                          |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                  | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 513   | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh                        | 09/2006          | 324.90 -                | 385.54           | -                           | 03/2010 -             | -           | -                                          | 0/0                         |
| 514   | SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim                                              | 04/2008          | 1,339.48 -              | 3,380.58         | 59.40                       | 12/2015 -             | 03/2017     | 15(O) -                                    | 0/0                         |
| 515   | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha                                 | 04/1998          | 183.23 -                | 818.29           | 103.44                      | 02/2015 -             | 02/2015     | 0(O) -                                     | 0/0                         |
| 516   | Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State                                   | 04/2011          | 193.44 -                | 193.44           | 12.34                       | - -                   | -           | -                                          | 0/0                         |
| 517   | Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar                                         | 04/1999          | 175.69 -                | 325.00           | 230.66                      | - -                   | -           | -                                          | 0/0                         |
| 518   | Sakri-Nirmali and Jhanjharpur-Laukahabazar and Sah - [N22000180]ECR,Bihar                | 04/2004          | 372.14 -                | 355.81           | 361.61                      | - -                   | -           | -                                          | 0/0                         |
| 519   | Santoshpur-Remount Road via Garden Reach-Metiabruze - [N22000248]ER,Multi State          | 04/2010          | 268.52 -                | 268.52           | 77.61                       | - -                   | -           | -                                          | 0/0                         |
| 520   | Shimoga-Harihar NL - [N22000278]SWR,Karnataka                                            | 04/2011          | 562.74 -                | 562.74           | 0.06                        | - -                   | -           | -                                          | 0/0                         |
| 521   | Sitamahi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar                        | 04/2008          | 678.62 -                | 678.62           | 14.36                       | - -                   | -           | -                                          | 0/0                         |
| 522   | Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State | 04/2000          | 297.47 -                | 297.47           | 51.70                       | - -                   | -           | -                                          | 0/0                         |
| 523   | Sondalia-Champapur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State   | 04/2010          | 277.28 -                | 277.28           | 33.48                       | - -                   | -           | -                                          | 0/0                         |
| 524   | Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State                               | 04/2013          | 296.00 -                | 296.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 525   | Sriperumbudur-Guduvanchery with spur to Irungattukkottai-Ava - [N22000186]SR,Tamil Nadu  | 04/2013          | 839.00 -                | 839.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 526   | Sultanganj-Katuria via Asarganj, Tarapur And Belha - [N22000217]ER,Multi State           | 04/2007          | 450.00 -                | 450.00           | 7.70                        | - -                   | -           | -                                          | 0/0                         |
| 527   | Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan            | 04/2008          | 516.23 516.23           | 516.23           | 401.08                      | 03/2014 -             | 03/2014     | 0(O) -                                     | 0/0                         |
| 528   | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha                                    | 04/2005          | 726.96 810.78           | 810.78           | 128.36                      | - -                   | -           | -                                          | 0/0                         |
| 529   | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal                            | 03/1984          | 293.97 1,025.39         | 1,074.47         | 447.00                      | 06/2005 07/2011       | 06/2016     | 132(O) 59(R)                               | 0/0                         |
| 530   | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal                  | 04/2000          | 157.96 1,188.91         | 1,188.91         | 639.92                      | - 12/2009             | 02/2012     | -                                          | 0/0                         |
| 531   | TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu                                         | 09/2006          | 456.00 456.00           | 582.83           | 189.37                      | - -                   | -           | -                                          | 0/0                         |
| 532   | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu                         | 09/2006          | 125.00 125.00           | 227.40           | 57.96                       | - -                   | -           | -                                          | 0/0                         |
| 533   | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu                       | 09/1995          | 100.00 100.00           | 800.00           | 546.50                      | - -                   | -           | -                                          | 0/0                         |
| 534   | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]JMRT,West Bengal          | 03/2000          | 907.69 3,156.32         | 3,176.10         | 3,451.00                    | 12/2006 08/2010       | 08/2010     | -                                          | 0/0                         |
| 535   | Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal                            | 04/2010          | 146.95 -                | 171.02           | 113.17                      | 06/2013 -             | -           | -                                          | 0/0                         |
| 536   | Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State                                | 04/2010          | 365.17 -                | 365.17           | 1.43                        | - -                   | -           | -                                          | 0/0                         |
| 537   | Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan                                            | 04/2013          | 236.39 -                | 236.93           | -                           | - -                   | -           | -                                          | 0/0                         |
| 538   | Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand                                      | 04/2008          | 167.73 167.73           | 167.73           | 47.70                       | 03/2012 -             | 02/2013     | -                                          | 0/0                         |



# Sector Wise Details

(Aug,2013)

|       |                                                                                              |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 539   | Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka                                   | 04/2011          | 913.00 -                | 913.00           | 0.46                        | - -                   | -           | -                                          | 0/0                         |
| 540   | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir                        | 03/1995          | 2,500.00 2,500.00       | 20,000.00        | 8,822.50                    | 11/2002 -             | 12/2017     | 181(O) -                                   | 0/0                         |
| 541   | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh                           | 04/2006          | 325.00 325.00           | 1,116.53         | 225.51                      | 03/2010 03/2017       | 03/2017     | 84(O) 0(R)                                 | 0/0                         |
| 542   | Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat                    | 04/2008          | 1,389.62 -              | 1,389.62         | 655.55                      | 03/2014 -             | 03/2014     | 0(O) -                                     | 0/0                         |
| 543   | Unchahar-Amethi - [N22000294]NR,Uttar Pradesh                                                | 04/2012          | 380.00 -                | 380.00           | 0.35                        | - -                   | -           | -                                          | 0/0                         |
| 544   | VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State                                           | 04/1990          | 155.66 356.87           | 548.01           | 181.84                      | - 03/2010             | -           | -                                          | 0/0                         |
| 545   | Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State                         | 04/2008          | 822.39 -                | 1,280.83         | 0.84                        | - -                   | -           | -                                          | 0/0                         |
| 546   | Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat                                             | 04/2011          | 446.00 -                | 685.17           | 12.96                       | - -                   | -           | -                                          | 0/0                         |
| 547   | Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat                                          | 04/2010          | 279.40 -                | 264.06           | 92.78                       | - -                   | 04/2014     | - -                                        | 0/0                         |
| 548   | Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra                                        | 04/2008          | 697.00 -                | 1,604.00         | 16.65                       | - -                   | -           | -                                          | 0/0                         |
| 549   | Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra                                     | 04/2012          | 297.85 -                | 297.85           | 1.07                        | - -                   | -           | -                                          | 0/0                         |
| 550   | White Field-Kolar NL - [N22000280]SWR,Karnataka                                              | 04/2011          | 341.05 -                | 341.05           | 0.18                        | - -                   | -           | -                                          | 0/0                         |
| 551   | Yamunanagar-Chandigarh via Sadhaura Narayangarh - [N22000293]NR,Multi State                  | 04/2013          | 876.00 -                | 876.00           | -                           | - -                   | -           | -                                          | 0/0                         |
| 552   | ansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur M - [N22000268]NR,Punjab          | 04/2009          | 396.04 -                | 396.04           | -                           | - -                   | -           | -                                          | 0/0                         |
|       | Total                                                                                        |                  | 147,446.28 -            | 258,415.07       | 75,004.75                   |                       |             |                                            | 1/7                         |
|       |                                                                                              |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Road Transport And Highways</u>                                                           |                  |                         |                  |                             |                       |             |                                            |                             |
| 553   | 2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh                                | 10/2012          | 250.50 -                | 250.50           | 131.40                      | 10/2014 -             | 10/2014     | 0(O) -                                     | 0/0                         |
| 554   | 2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh                               | 01/2013          | 373.47 -                | 373.47           | 38.90                       | 07/2014 -             | 07/2014     | 0(O) -                                     | 0/0                         |
| 555   | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar                                           | 05/2011          | 351.54 -                | 351.54           | 394.10                      | 05/2013 -             | 03/2014     | 10(O) -                                    | 0/0                         |
| 556   | 2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar                                  | 05/2011          | 511.54 -                | 511.54           | 631.80                      | 11/2013 -             | 11/2013     | 0(O) -                                     | 0/0                         |
| 557   | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State      | 04/2012          | 624.00 -                | 624.00           | 296.40                      | 04/2014 -             | 04/2014     | 0(O) -                                     | 0/0                         |
| 558   | 2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh | 10/2011          | 1,565.00 -              | 1,565.00         | 648.30                      | 10/2014 -             | 10/2014     | 0(O) -                                     | 0/0                         |
| 559   | 2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar                  | 07/2012          | 356.40 -                | 356.40           | -                           | 07/2014 -             | 07/2014     | 0(O) -                                     | 0/0                         |
| 560   | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh                     | 07/2012          | 291.36 -                | 291.36           | 86.37                       | 01/2014 -             | 01/2014     | 0(O) -                                     | 0/0                         |

# Sector Wise Details

(Aug,2013)

|       |                                                                                        |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                      | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 561   | 2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya                               | 02/2011          | 226.00 -                | 226.00           | 288.80                      | 02/2014 -             | 02/2014     | 0(O) -                                     | 0/0                         |
| 562   | 2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar                             | 05/2011          | 664.00 -                | 664.00           | 550.00                      | 02/2014 -             | 04/2014     | 2(O) -                                     | 0/0                         |
| 563   | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar                             | 10/2011          | 375.09 -                | 375.09           | 174.40                      | 04/2014 -             | 04/2014     | 0(O) -                                     | 0/0                         |
| 564   | 2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar                             | 12/2011          | 325.00 -                | 325.00           | 161.20                      | 05/2014 -             | 05/2014     | 0(O) -                                     | 0/0                         |
| 565   | 4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, Gujarat | 03/2012          | 828.00 -                | 828.00           | 470.50                      | 09/2014 -             | 09/2014     | 0(O) -                                     | 0/0                         |
| 566   | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State                                | 02/2011          | 2,498.76 -              | 2,498.76         | 1,734.00                    | 08/2014 -             | 07/2015     | 11(O) -                                    | 0/0                         |
| 567   | 4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat                           | 12/2010          | 1,008.50 -              | 1,008.50         | 1,346.00                    | 06/2013 -             | 12/2013     | 6(O) -                                     | 0/0                         |
| 568   | 4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka          | 03/2011          | 359.00 -                | 359.00           | 39.27                       | 09/2013 -             | 07/2014     | 10(O) -                                    | 0/0                         |
| 569   | 4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat                   | 03/2011          | 785.50 -                | 785.50           | 839.30                      | 08/2013 -             | 12/2013     | 4(O) -                                     | 0/0                         |
| 570   | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar                                   | 01/2011          | 575.00 -                | 575.00           | 714.40                      | 07/2013 -             | 12/2013     | 5(O) -                                     | 0/0                         |
| 571   | 4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand                              | 02/2012          | 398.00 -                | 398.00           | 437.90                      | 02/2014 -             | 02/2014     | 0(O) -                                     | 0/0                         |
| 572   | 4-laning of Brahampore-Faraka - [N24000203]NHAI, Multi State                           | 02/2011          | 998.79 -                | 998.79           | 1,202.00                    | 08/2013 -             | 12/2014     | 16(O) -                                    | 0/0                         |
| 573   | 4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State                              | 02/2011          | 1,078.84 -              | 1,078.84         | 1,226.00                    | 08/2013 -             | 12/2014     | 16(O) -                                    | 0/0                         |
| 574   | 4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State                             | 02/2011          | 580.43 -                | 580.43           | 280.10                      | 08/2013 -             | 12/2015     | 28(O) -                                    | 0/0                         |
| 575   | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, West Bengal                  | 04/2012          | 1,396.18 -              | 1,396.18         | 1,027.00                    | 09/2014 -             | 09/2014     | 0(O) -                                     | 0/0                         |
| 576   | AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh         | 12/2003          | 348.16 -                | 465.50           | 237.20                      | 09/2007 -             | 03/2014     | 78(O) -                                    | 0/0                         |
| 577   | AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, Gujarat                               | 01/2013          | 2,125.24 -              | 2,125.24         | 30.80                       | 12/2015 -             | 12/2015     | 0(O) -                                     | 0/0                         |
| 578   | AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab                                           | 05/2010          | 705.00 -                | 705.00           | 2,124.00                    | 11/2012 -             | 12/2013     | 13(O) -                                    | 0/0                         |
| 579   | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh                   | 03/2005          | 190.00 -                | 190.00           | 264.60                      | 01/2009 -             | 12/2013     | 59(O) -                                    | 0/0                         |
| 580   | Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh                          | 02/2010          | 390.56 -                | 390.56           | 772.40                      | 02/2012 -             | 06/2013     | -                                          | 0/0                         |
| 581   | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha            | 04/2000          | 228.70 -                | 228.70           | 194.51                      | 02/2004 -             | 09/2013     | 115(O) -                                   | 0/0                         |
| 582   | BAREILY-SITAPUR - [N24000200]NHAI, Uttar Pradesh                                       | 03/2011          | 1,046.00 -              | 1,046.00         | 352.90                      | 09/2013 -             | 09/2013     | 0(O) -                                     | 0/0                         |
| 583   | BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan                                      | 12/2011          | 2,388.00 -              | 2,388.00         | 1,306.00                    | 06/2014 -             | 06/2014     | 0(O) -                                     | 0/0                         |
| 584   | BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka                                     | 12/2010          | 480.00 -                | 480.00           | 563.30                      | -                     | 10/2013     | -                                          | 2/2                         |
| 585   | BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh                                        | 10/2011          | 209.00 -                | 209.00           | 34.38                       | 01/2013 -             | 10/2013     | 9(O) -                                     | 0/0                         |
| 586   | BHUBANESWAR TO PURI - [N24000195]NHAI, Odisha                                          | 03/2011          | 500.29 -                | 500.29           | 509.00                      | 08/2013 -             | 12/2013     | 4(O) -                                     | 0/0                         |

# Sector Wise Details

(Aug,2013)

|       |                                                                                           |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                   | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                         | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 587   | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                      | 12/2003          | 237.80<br>-             | 237.80           | 287.50                      | 06/2008<br>-          | 03/2014     | 69(O)<br>-                                 | 0/0                         |
| 588   | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam                       | 12/2003          | 195.00<br>-             | 195.00           | 250.10                      | 06/2008<br>-          | 03/2014     | 69(O)<br>-                                 | 0/0                         |
| 589   | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam         | 12/2003          | 230.00<br>-             | 230.00           | 239.20                      | 06/2005<br>-          | 03/2014     | 105(O)<br>-                                | 0/0                         |
| 590   | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam                                        | 12/2003          | 217.61<br>-             | 217.61           | 290.00                      | 04/2010<br>-          | 11/2014     | 55(O)<br>-                                 | 0/0                         |
| 591   | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                                  | 12/2003          | 275.00<br>-             | 281.31           | 180.10                      | 02/2010<br>-          | 06/2015     | 64(O)<br>-                                 | 0/0                         |
| 592   | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu       | 09/2010          | 852.00<br>-             | 852.00           | 834.00                      | 03/2013<br>-          | 12/2013     | 9(O)<br>-                                  | 0/0                         |
| 593   | CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka                                      | 03/2011          | 839.00<br>-             | 839.00           | 665.60                      | -<br>-                | 12/2013     | -<br>-                                     | 0/1                         |
| 594   | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh           | 11/2010          | 1,585.00<br>-           | 1,585.00         | 957.80                      | 05/2013<br>-          | 09/2013     | 4(O)<br>-                                  | 0/0                         |
| 595   | Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu                                       | 04/2009          | 353.37<br>-             | 353.37           | 417.20                      | 10/2011<br>-          | 03/2014     | 29(O)<br>-                                 | 0/0                         |
| 596   | Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh      | 05/2009          | 572.30<br>-             | 572.30           | 832.90                      | 10/2011<br>-          | 06/2014     | 32(O)<br>-                                 | 0/0                         |
| 597   | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar       | 12/2003          | 300.00<br>-             | 300.00           | 176.80                      | 10/2008<br>-          | 06/2014     | 68(O)<br>-                                 | 0/0                         |
| 598   | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State                         | 10/2012          | 1,928.22<br>-           | 1,928.22         | 302.60                      | 04/2015<br>-          | 04/2015     | 0(O)<br>-                                  | 0/0                         |
| 599   | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana                                 | 04/2007          | 486.00<br>-             | 486.00           | 653.40                      | 05/2010<br>-          | 10/2013     | 41(O)<br>-                                 | 0/0                         |
| 600   | DEOLI-KOTA - [N24000148]NHAI,Rajasthan                                                    | 01/2011          | 593.00<br>-             | 593.00           | 566.40                      | 07/2013<br>-          | 10/2013     | 3(O)<br>-                                  | 0/0                         |
| 601   | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu           | 06/2011          | 600.00<br>-             | 600.00           | 75.85                       | 06/2013<br>-          | 12/2013     | 6(O)<br>-                                  | 0/0                         |
| 602   | DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka                                              | 12/2010          | 453.00<br>-             | 453.00           | 713.90                      | -<br>-                | 09/2013     | -<br>-                                     | 1/1                         |
| 603   | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                      | 12/2003          | 200.00<br>-             | 200.00           | 253.60                      | 06/2008<br>-          | 12/2013     | 66(O)<br>-                                 | 0/0                         |
| 604   | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam                           | 12/2003          | 160.00<br>-             | 160.00           | 207.20                      | 05/2008<br>-          | 12/2013     | 67(O)<br>-                                 | 0/0                         |
| 605   | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State          | 12/2003          | 232.45<br>-             | 232.45           | 304.30                      | 09/2010<br>-          | 08/2014     | 47(O)<br>-                                 | 0/0                         |
| 606   | Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu                                             | 09/2011          | 485.00<br>-             | 485.00           | 317.00                      | 08/2013<br>-          | 02/2015     | 18(O)<br>-                                 | 0/0                         |
| 607   | ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh                                            | 03/2013          | 1,573.00<br>-           | 1,573.00         | 15.05                       | 09/2015<br>-          | 09/2015     | 0(O)<br>-                                  | 0/0                         |
| 608   | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar                               | 12/2003          | 332.94<br>-             | 332.94           | 470.20                      | 09/2008<br>-          | 12/2013     | 63(O)<br>-                                 | 0/0                         |
| 609   | FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State                   | 02/2013          | 1,232.00<br>-           | 1,232.00         | 150.70                      | 08/2015<br>-          | 08/2015     | 0(O)<br>-                                  | 0/0                         |
| 610   | FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala                   | 04/2011          | 682.00<br>-             | 682.00           | 143.60                      | 10/2013<br>-          | 11/2015     | 25(O)<br>-                                 | 0/0                         |
| 611   | Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra           | 04/2010          | 1,170.52<br>-           | 1,170.52         | 4.41                        | 06/2011<br>-          | 12/2013     | 30(O)<br>-                                 | 0/0                         |
| 612   | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh | 12/2003          | 155.00<br>-             | 201.66           | 143.60                      | 09/2008<br>-          | 03/2014     | 66(O)<br>-                                 | 0/0                         |

# Sector Wise Details

(Aug,2013)

|       |                                                                                     |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                             | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                   | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 613   | GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha                               | 04/2000          | 263.27 -                | 263.27           | 276.46                      | 02/2004 -             | 09/2013     | 115(O) -                                   | 0/0                         |
| 614   | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh                             | 02/2011          | 1,141.00 -              | 1,141.00         | 1,264.00                    | 08/2013 -             | 06/2014     | 10(O) -                                    | 0/0                         |
| 615   | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam                                  | 12/2003          | 198.16 -                | 198.16           | 272.30                      | 04/2008 -             | 03/2014     | 71(O) -                                    | 0/0                         |
| 616   | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam                                   | 12/2003          | 175.96 -                | 175.96           | 211.60                      | 04/2008 -             | 03/2014     | 71(O) -                                    | 0/0                         |
| 617   | GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh                            | 12/2003          | 300.93 -                | 300.93           | 302.70                      | 10/2009 -             | 06/2013     | -                                          | 0/0                         |
| 618   | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State                                 | 12/2003          | 604.00 -                | 604.00           | 495.40                      | 12/2009 -             | 12/2014     | 60(O) -                                    | 0/0                         |
| 619   | Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat      | 03/2010          | 1,509.10 -              | 1,509.10         | 2,080.00                    | 09/2012 -             | 12/2013     | 15(O) -                                    | 0/0                         |
| 620   | Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State                  | 04/2009          | 1,673.70 -              | 1,673.70         | 2,839.00                    | 10/2011 -             | 12/2013     | 26(O) -                                    | 0/0                         |
| 621   | HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh        | 03/2005          | 220.00 -                | 220.00           | 284.20                      | 09/2007 -             | 11/2013     | 74(O) -                                    | 0/0                         |
| 622   | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam      | 12/2003          | 280.00 -                | 280.00           | 322.50                      | 02/2009 03/2014       | 05/2014     | 63(O) 2(R)                                 | 0/0                         |
| 623   | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam                                 | 12/2003          | 196.00 -                | 363.74           | 155.90                      | 07/2009 -             | 05/2014     | 58(O) -                                    | 0/0                         |
| 624   | HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam                | 12/2003          | 212.00 -                | 386.10           | 68.94                       | 09/2007 -             | 04/2014     | 79(O) -                                    | 0/0                         |
| 625   | HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand                | 11/2011          | 478.00 -                | 478.00           | 270.80                      | 10/2013 -             | 03/2014     | 5(O) -                                     | 0/0                         |
| 626   | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka           | 04/2000          | 318.00 -                | 207.56           | 196.42                      | 08/2004 -             | 10/2013     | 110(O) -                                   | 0/0                         |
| 627   | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka                | 04/2000          | 241.00 -                | 196.65           | 203.44                      | 08/2004 07/2010       | 10/2013     | 110(O) 39(R)                               | 0/0                         |
| 628   | Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand                                       | 08/2010          | 625.07 -                | 625.07           | 947.60                      | 01/2013 -             | 10/2013     | 9(O) -                                     | 0/0                         |
| 629   | Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka       | 09/2010          | 946.00 -                | 946.00           | 1,790.00                    | -                     | 10/2013     | -                                          | 3/3                         |
| 630   | INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh                                 | 11/2010          | 325.00 -                | 325.00           | 518.70                      | 05/2013 -             | 02/2014     | 9(O) -                                     | 0/0                         |
| 631   | Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh                            | 10/2010          | 1,175.00 -              | 1,175.00         | 138.67                      | 04/2013 -             | 12/2013     | 8(O) -                                     | 0/0                         |
| 632   | JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan                                          | 08/2010          | 267.81 -                | 267.81           | 648.30                      | 02/2013 -             | 09/2013     | 7(O) -                                     | 0/0                         |
| 633   | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir              | 07/2010          | 1,813.76 -              | 1,813.76         | -                           | 07/2013 -             | 06/2014     | 11(O) -                                    | 0/0                         |
| 634   | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh                        | 12/2003          | 355.06 -                | 355.06           | 507.30                      | 09/2009 -             | 12/2013     | 51(O) -                                    | 0/0                         |
| 635   | JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya                                       | 01/2011          | 536.00 -                | 536.00           | 513.80                      | 01/2014 -             | 01/2014     | 0(O) -                                     | 0/0                         |
| 636   | Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan                                       | 06/2010          | 792.06 -                | 792.06           | 1,972.00                    | 12/2012 -             | 09/2013     | 9(O) -                                     | 0/0                         |
| 637   | KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan                          | 12/2003          | 275.00 -                | 250.39           | 280.40                      | 10/2008 -             | 12/2013     | 62(O) -                                    | 0/0                         |
| 638   | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar | 12/2003          | 240.00 -                | 240.00           | 295.00                      | 10/2008 -             | 12/2013     | 62(O) -                                    | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                                   |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|---------------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                           | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                                 | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 639   | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, West Bengal                                             | 02/2012          | 702.16 -                | 702.16           | 463.54                      | 07/2014 -             | 07/2014     | 0(O) -                                     | 0/0                         |
| 640   | KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka                                        | 09/2010          | 671.00 -                | 671.00           | 929.60                      | - -                   | 06/2014     | - -                                        | 2/3                         |
| 641   | Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan                                              | 11/2009          | 795.00 -                | 795.00           | 1,127.00                    | 05/2012 -             | 09/2013     | 16(O) -                                    | 0/0                         |
| 642   | LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH-7 - [N24000094]NHAI, Madhya Pradesh | 12/2003          | 407.60 -                | 407.60           | 186.50                      | 06/2010 -             | 12/2013     | 42(O) -                                    | 0/0                         |
| 643   | LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh                | 12/2003          | 263.17 -                | 263.17           | 233.80                      | 09/2009 -             | 09/2014     | 60(O) -                                    | 0/0                         |
| 644   | LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh                                               | 07/1999          | 635.90 -                | 635.90           | 214.20                      | 07/2012 -             | 07/2014     | 24(O) -                                    | 0/0                         |
| 645   | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam                     | 12/2003          | 155.04 -                | 280.13           | 123.00                      | 11/2008 -             | 06/2014     | 67(O) -                                    | 0/0                         |
| 646   | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam                      | 12/2003          | 199.81 -                | 385.13           | 91.97                       | 04/2009 -             | 12/2014     | 68(O) -                                    | 0/0                         |
| 647   | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam                | 12/2003          | 167.64 -                | 167.64           | 66.16                       | 11/2008 -             | 12/2014     | 73(O) -                                    | 0/0                         |
| 648   | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam                       | 12/2003          | 200.00 -                | 200.00           | 164.50                      | 04/2009 -             | 12/2014     | 68(O) -                                    | 0/0                         |
| 649   | MURADABAD-BAREILY - [N24000154]NHAI, Uttar Pradesh                                                | 04/2010          | 1,267.00 -              | 1,267.00         | 1,857.00                    | 06/2013 -             | 03/2014     | 9(O) -                                     | 0/0                         |
| 650   | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State                                             | 09/2011          | 754.00 -                | 754.00           | 515.60                      | 03/2013 -             | 03/2014     | 12(O) -                                    | 0/0                         |
| 651   | Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar                                                    | 05/2011          | 511.54 -                | 511.54           | 65.78                       | 11/2013 -             | 11/2013     | 0(O) -                                     | 0/0                         |
| 652   | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam                                               | 12/2003          | 264.72 -                | 264.72           | 301.10                      | 06/2008 -             | 12/2013     | 66(O) -                                    | 0/0                         |
| 653   | NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra                                        | 03/2005          | 168.00 -                | 168.00           | 457.30                      | 12/2008 -             | 03/2014     | 63(O) -                                    | 0/0                         |
| 654   | NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra                                            | 04/2012          | 484.19 -                | 484.19           | 282.80                      | 10/2014 -             | 10/2014     | 0(O) -                                     | 0/0                         |
| 655   | NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam                                                   | 12/2003          | 208.00 -                | 208.00           | 303.90                      | 04/2008 -             | 05/2014     | 73(O) -                                    | 0/0                         |
| 656   | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam                                                  | 12/2003          | 225.00 -                | 225.00           | 264.70                      | 06/2008 -             | 09/2013     | 63(O) -                                    | 0/0                         |
| 657   | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam                                                  | 12/2003          | 200.00 -                | 200.00           | 286.90                      | 06/2008 -             | 12/2013     | 66(O) -                                    | 0/0                         |
| 658   | NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir                                               | 06/2010          | 2,159.00 -              | 2,159.00         | -                           | 06/2015 -             | 05/2016     | 11(O) -                                    | 0/0                         |
| 659   | NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka                                      | 04/2000          | 196.50<br>363.00        | 196.50           | 284.40                      | 06/2011<br>06/2011    | 10/2013     | 28(O)<br>28(R)                             | 0/2                         |
| 660   | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala                           | 03/2005          | 557.00 -                | 557.00           | 1,128.00                    | 02/2010 -             | 12/2014     | 58(O) -                                    | 0/0                         |
| 661   | NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha                                                   | 07/2011          | 586.00 -                | 586.00           | 237.60                      | 01/2014 -             | 12/2014     | 11(O) -                                    | 0/0                         |
| 662   | New 4 Lane elevated road from Chennai airport - [N24000139]NHAI, Tamil Nadu                       | 09/2010          | 1,655.00 -              | 1,655.00         | 393.70                      | 09/2013 -             | 09/2013     | 0(O) -                                     | 0/0                         |
| 663   | PANIKHOLI-RIMOLI - [N24000197]NHAI, Odisha                                                        | 03/2012          | 1,410.00 -              | 1,410.00         | 153.80                      | 09/2014 -             | 10/2015     | 13(O) -                                    | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                               |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|-----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                       | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                             | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 664   | PANIPAT-ROHTAK - [N24000151]NHAI,Haryana                                                      | 04/2011          | 807.00<br>-             | 807.00           | 1,318.00                    | 10/2014<br>-          | 10/2014     | 0(O)<br>-                                  | 0/0                         |
| 665   | PANVEL-INDAPUR - [N24000216]NHAI,Multi State                                                  | 12/2011          | 942.69<br>-             | 942.69           | 196.20                      | 06/2014<br>-          | 06/2014     | 0(O)<br>-                                  | 0/0                         |
| 666   | PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab                         | 12/2003          | 284.00<br>-             | 359.00           | 315.50                      | 05/2008<br>-          | 09/2013     | 64(O)<br>-                                 | 0/0                         |
| 667   | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar                                | 09/2011          | 574.00<br>-             | 574.00           | 646.10                      | 03/2014<br>-          | 03/2014     | 0(O)<br>-                                  | 0/0                         |
| 668   | PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar                                                    | 08/2010          | 671.30<br>-             | 671.30           | 625.90                      | 02/2013<br>-          | 10/2013     | 8(O)<br>-                                  | 0/0                         |
| 669   | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra                   | 03/2005          | 940.00<br>-             | 940.00           | 1,325.00                    | 07/2012<br>-          | 12/2013     | 17(O)<br>-                                 | 0/0                         |
| 670   | PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra                                               | 10/2010          | 1,724.55<br>-           | 1,724.55         | 1,193.00                    | 03/2013<br>-          | 04/2014     | 13(O)<br>-                                 | 0/0                         |
| 671   | PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra                                            | 09/2011          | 835.00<br>-             | 835.00           | 388.20                      | 01/2014<br>-          | 01/2014     | 0(O)<br>-                                  | 0/0                         |
| 672   | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana                         | 05/2009          | 1,108.00<br>-           | 2,288.00         | 3,465.90                    | 11/2011<br>-          | 12/2013     | 25(O)<br>-                                 | 0/0                         |
| 673   | Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra                                             | 11/2009          | 1,110.00<br>-           | 1,110.00         | 1,802.00                    | 05/2012<br>-          | 10/2013     | 17(O)<br>-                                 | 0/0                         |
| 674   | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir                  | 07/2010          | 1,987.00<br>-           | 1,987.00         | 944.00                      | 07/2015<br>-          | 06/2016     | 11(O)<br>-                                 | 0/0                         |
| 675   | RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh | 12/2003          | 251.03<br>-             | 251.03           | 337.80                      | 10/2008<br>-          | 03/2014     | 65(O)<br>-                                 | 0/0                         |
| 676   | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State                                         | 12/2012          | 1,479.00<br>-           | 1,479.00         | 190.40                      | 06/2015<br>-          | 06/2015     | 0(O)<br>-                                  | 0/0                         |
| 677   | REENGUS SIKAR - [N24000227]NHAI,Rajasthan                                                     | 03/2012          | 333.51<br>-             | 333.51           | 227.90                      | 09/2014<br>-          | 09/2014     | 0(O)<br>-                                  | 0/0                         |
| 678   | ROHTAK-BAWAL - [N24000169]NHAI,Haryana                                                        | 05/2011          | 650.00<br>-             | 650.00           | 1,106.00                    | 11/2013<br>-          | 11/2013     | 0(O)<br>-                                  | 0/0                         |
| 679   | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu                        | 03/2005          | 941.00<br>-             | 941.00           | 1,901.00                    | 01/2011<br>-          | 12/2013     | 35(O)<br>-                                 | 0/0                         |
| 680   | SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat                                             | 09/2010          | 805.39<br>-             | 805.39           | 612.90                      | 03/2013<br>-          | 12/2013     | 9(O)<br>-                                  | 0/0                         |
| 681   | SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat                                               | 09/2010          | 805.39<br>-             | 805.39           | 543.70                      | 12/2013<br>-          | 12/2013     | 0(O)<br>-                                  | 0/0                         |
| 682   | SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha                          | 11/2011          | 909.00<br>-             | 909.00           | 941.90                      | 05/2014<br>-          | 05/2014     | 0(O)<br>-                                  | 0/0                         |
| 683   | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam                      | 12/2003          | 157.47<br>-             | 154.57           | 240.40                      | 09/2007<br>-          | 03/2014     | 78(O)<br>-                                 | 0/0                         |
| 684   | SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal                                     | 12/2003          | 225.00<br>-             | 225.00           | 191.30                      | 07/2008<br>-          | 03/2013     | -                                          | 0/0                         |
| 685   | SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu               | 06/2011          | 535.00<br>-             | 535.00           | -                           | 12/2013<br>-          | 12/2013     | 0(O)<br>-                                  | 0/0                         |
| 686   | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu               | 09/2011          | 1,250.00<br>-           | 1,250.00         | 16.15                       | 12/2013<br>-          | 12/2013     | 0(O)<br>-                                  | 0/0                         |
| 687   | SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh                         | 11/2011          | 1,535.00<br>-           | 1,535.00         | 1,182.00                    | 05/2014<br>-          | 05/2014     | 0(O)<br>-                                  | 0/0                         |
| 688   | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala                       | 02/2010          | 617.00<br>-             | 617.00           | 154.50                      | 08/2012<br>-          | 03/2015     | 31(O)<br>-                                 | 0/0                         |

## Sector Wise Details

(Aug,2013)

|       |                                                                                              |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 689   | SNG toBANL - [N24000189]NHAI,Jammu and Kashmir                                               | 06/2011          | 1,100.70 -              | 1,100.70         | -                           | 06/2014 -             | 06/2014     | 0(O) -                                     | 0/0                         |
| 690   | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam                                            | 12/2003          | 245.00 -                | 245.00           | 491.20                      | 03/2008 -             | 03/2014     | 72(O) -                                    | 0/0                         |
| 691   | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha                          | 04/2000          | 225.00 -                | 241.53           | 162.71                      | 04/2004 -             | 09/2013     | 113(O) -                                   | 0/0                         |
| 692   | Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State                      | 02/2009          | 1,693.75 -              | 1,693.75         | 2,707.00                    | 08/2011 -             | 12/2013     | 28(O) -                                    | 0/0                         |
| 693   | THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu                                     | 03/2005          | 280.00 -                | 280.00           | 581.50                      | 06/2009 -             | 09/2013     | 51(O) -                                    | 0/0                         |
| 694   | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                            | 03/2005          | 516.00 -                | 516.00           | 858.90                      | 07/2010 -             | 03/2014     | 44(O) -                                    | 0/0                         |
| 695   | Talegaon-amravati - [N24000140]NHAI,Maharashtra                                              | 11/2009          | 567.00 -                | 567.00           | 1,166.00                    | 11/2013 -             | 11/2013     | 0(O) -                                     | 0/0                         |
| 696   | Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu                                              | 04/2011          | 571.00 -                | 571.00           | -                           | 10/2013 -             | 10/2013     | 0(O) -                                     | 0/0                         |
| 697   | Trichy Bypass - [N24000176]NHAI,Tamil Nadu                                                   | 05/2010          | 374.00 -                | 374.00           | 117.60                      | 05/2013 -             | 12/2013     | 7(O) -                                     | 0/0                         |
| 698   | UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka                        | 11/2010          | 680.00 -                | 680.00           | -                           | -                     | 04/2013     | -                                          | 2/2                         |
| 699   | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State                        | 09/2011          | 2,848.00 -              | 2,848.00         | 915.90                      | 03/2014 -             | 03/2014     | 0(O) -                                     | 0/0                         |
| 700   | VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir  | 12/2003          | 166.27 -                | 193.10           | 198.50                      | 03/2008 -             | 02/2008     | -                                          | 0/0                         |
| 701   | WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra                        | 02/2011          | 193.45 -                | 193.45           | 54.59                       | 11/2012 -             | 03/2014     | 16(O) -                                    | 0/0                         |
| 702   | WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,Tamil Nadu                        | 06/2013          | 1,287.95 -              | 1,287.95         | -                           | 11/2015 -             | 11/2015     | 0(O) -                                     | 0/0                         |
| 703   | kandla - Mundra port - [N24000175]NHAI,Gujarat                                               | 01/2011          | 953.88 -                | 953.88           | 651.30                      | 07/2013 -             | 06/2014     | 11(O) -                                    | 0/0                         |
| 704   | six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State                  | 12/2011          | 1,047.00 -              | 1,047.00         | 202.40                      | 06/2014 -             | 06/2014     | 0(O) -                                     | 0/0                         |
|       | Total                                                                                        |                  | 105,203.54 -            | 107,142.16       | 83,521.87                   |                       |             |                                            | 10/14                       |
|       |                                                                                              |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Shipping And Ports</u>                                                                    |                  |                         |                  |                             |                       |             |                                            |                             |
| 705   | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra           | 10/2007          | 359.44 -                | 359.44           | 358.78                      | 04/2011 11/2011       | 11/2011     | -                                          | 0/0                         |
| 706   | ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State   | 07/2011          | 220.49 -                | 220.49           | 98.31                       | 01/2013 06/2013       | 06/2013     | -                                          | 0/0                         |
| 707   | ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State | 01/2012          | 511.87 -                | 511.87           | 106.72                      | 03/2014 08/2014       | 08/2014     | 5(O) 0(R)                                  | 0/0                         |
| 708   | Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra    | 08/2010          | 612.72 532.83           | 532.83           | 448.43                      | 12/2012 11/2013       | 11/2013     | 11(O) 0(R)                                 | 0/0                         |
| 709   | Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra                          | 04/2009          | 277.03 280.00           | 277.03           | 294.87                      | 12/2011 10/2012       | 10/2012     | -                                          | 0/0                         |
| 710   | Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra    | 10/2010          | 966.46 -                | 994.82           | 363.20                      | 02/2014 -             | 02/2014     | 0(O) -                                     | 0/0                         |



## Sector Wise Details

(Aug,2013)

|       |                                                                                              |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|----------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                      | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 711   | Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIP, Maharashtra     | 10/2010          | 1,028.10<br>1,012.23    | 1,012.23         | 554.60                      | 12/2013<br>11/2013    | 11/2013     | -1(O)<br>0(R)                              | 0/0                         |
| 712   | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra | 11/2007          | 1,228.00<br>1,460.00    | 1,460.00         | 965.23                      | 12/2010<br>09/2012    | 12/2014     | 48(O)<br>27(R)                             | 0/0                         |
| 713   | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat               | 12/2005          | 702.00<br>-             | 755.50           | 219.00                      | 03/2011<br>-          | 03/2013     | -                                          | 0/0                         |
| 714   | Construction of berthing and allied facilities off - [N25000037]PORT TRUST, Gujarat          | 04/2005          | 882.00<br>-             | 1,060.00         | 0.93                        | 02/2011<br>-          | 12/2012     | -                                          | 0/0                         |
| 715   | DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST, Maharashtra      | 10/2005          | 800.00<br>1,571.60      | 1,571.60         | 5.75                        | 10/2008<br>-          | -           | -                                          | 0/0                         |
| 716   | DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, Odisha                         | 12/2005          | 154.84<br>253.36        | 253.36           | 221.58                      | -<br>01/2009          | 12/2010     | -                                          | 0/1                         |
| 717   | ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu      | 10/2002          | 150.00<br>309.00        | 600.00           | 139.80                      | 03/2006<br>12/2013    | 12/2013     | 93(O)<br>0(R)                              | 0/0                         |
| 718   | Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh     | 02/2010          | 444.10<br>-             | 444.10           | -                           | 06/2010<br>-          | 11/2012     | -                                          | 0/0                         |
| 719   | Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat   | 06/2010          | 277.00<br>-             | 277.00           | 0.21                        | 03/2012<br>-          | 03/2012     | -                                          | 0/0                         |
| 720   | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala       | 03/2007          | 245.67<br>298.17        | 373.22           | 371.18                      | 04/2009<br>11/2009    | 02/2011     | -                                          | 0/0                         |
| 721   | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu                       | 06/2005          | 2,427.40<br>-           | 2,427.40         | 832.04                      | 10/2008<br>11/2010    | -           | -                                          | 0/0                         |
| 722   | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala           | 03/2009          | 3,500.00<br>4,150.00    | 4,150.00         | 3,661.95                    | 01/2012<br>09/2012    | 08/2013     | 19(O)<br>11(R)                             | 0/0                         |
| 723   | Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST, Gujarat          | 02/2011          | 830.00<br>-             | 621.53           | -                           | 05/2013<br>-          | 05/2013     | -                                          | 0/0                         |
|       | Total                                                                                        |                  | 15,617.12<br>-          | 17,902.42        | 8,642.58                    |                       |             |                                            | 0/1                         |
|       |                                                                                              |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Telecommunications</u>                                                                    |                  |                         |                  |                             |                       |             |                                            |                             |
| 724   | Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam                            | 06/2007          | 336.81<br>-             | 336.81           | 164.18                      | 01/2009<br>-          | 12/2013     | 59(O)<br>-                                 | 0/0                         |
| 725   | CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra                            | 01/2006          | 247.00<br>-             | 247.00           | 75.89                       | 02/2007<br>12/2010    | -           | -                                          | 0/0                         |
| 726   | CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi                              | 12/2005          | 249.00<br>-             | 229.41           | 67.21                       | 02/2007<br>03/2012    | 02/2013     | -                                          | 0/0                         |
| 727   | DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL, Delhi                            | 02/2006          | 229.41<br>-             | 229.41           | 67.21                       | 03/2012<br>02/2013    | -           | -                                          | 0/0                         |
| 728   | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State                   | 10/2009          | 384.00<br>-             | 384.00           | 29.45                       | 10/2010<br>03/2012    | 12/2013     | 38(O)<br>21(R)                             | 0/0                         |
| 729   | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL, Maharashtra             | 06/2006          | 231.38<br>-             | 176.00           | 86.11                       | 10/2007<br>-          | 12/2013     | 74(O)<br>-                                 | 0/0                         |
| 730   | GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttarakhand            | 01/2009          | 149.15<br>-             | 158.72           | 81.73                       | 06/2009<br>-          | 12/2013     | 54(O)<br>-                                 | 0/0                         |
| 731   | GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab                 | 02/2008          | 373.94<br>-             | 373.94           | 227.58                      | 12/2008<br>-          | 12/2012     | -                                          | 0/0                         |
| 732   | GSM equipment of 1625000Lines (2G) 325000 lines 3(-) [N26000090]BSNL, Madhya pradesh         | 11/2009          | 916.70<br>-             | 930.60           | 828.80                      | 11/2010<br>12/2012    | 09/2013     | 34(O)<br>9(R)                              | 0/0                         |



## Sector Wise Details

(Aug,2013)

|       |                                                                                            |                  |                         |                  |                             | Date of Commissioning |             |                                            |                             |
|-------|--------------------------------------------------------------------------------------------|------------------|-------------------------|------------------|-----------------------------|-----------------------|-------------|--------------------------------------------|-----------------------------|
| Sl.No | Project                                                                                    | Date of Approval | Original / Revised Cost | Anticipated Cost | Cumulative Expenditure Cost | Original / Revised    | Anticipated | Delay w.r.t. Original/ Revised (in months) | Miles tones Achieved/ Total |
| 1     | 2                                                                                          | 3                | 4                       | 5                | 6                           | 7                     | 8           | 9                                          | 10                          |
| 733   | GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand             | 03/2008          | 328.13 -                | 392.13           | 164.58                      | 03/2009 -             | 01/2013     | -                                          | 0/0                         |
| 734   | Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State           | 12/2007          | 152.65 -                | 152.65           | -                           | 03/2010 -             | -           | -                                          | 0/0                         |
| 735   | Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State | 12/2007          | 952.88 -                | 952.88           | -                           | 03/2010 -             | -           | -                                          | 0/0                         |
| 736   | Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State | 07/2010          | 1,148.19 -              | 964.37           | 178.11                      | 05/2011 -             | 09/2013     | 28(O) -                                    | 0/0                         |
|       | Total                                                                                      |                  | 5,699.24 -              | 5,527.92         | 1,970.85                    |                       |             |                                            | 0/0                         |
|       |                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Urban Development</u>                                                                   |                  |                         |                  |                             |                       |             |                                            |                             |
| 737   | BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka                                   | 05/2006          | 6,395.00 -              | 11,609.00        | 2,267.57                    | 06/2011 -             | 03/2013     | -                                          | 3/3                         |
| 738   | C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra           | 11/2006          | 114.18 173.08           | 173.08           | -                           | 04/2009 -             | -           | -                                          | 0/0                         |
| 739   | DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi                                               | 09/2011          | 35,242.00 -             | 35,242.00        | 3,853.30                    | 03/2016 -             | 03/2016     | 0(O) -                                     | 0/0                         |
| 740   | FARIDABAD EXTENSION - [N28000057]DMRC,Delhi                                                | 09/2011          | 2,494.00 -              | 2,494.00         | 300.76                      | 09/2014 -             | 05/2015     | 8(O) -                                     | 0/0                         |
|       | Total                                                                                      |                  | 44,245.18 -             | 49,518.08        | 6,421.63                    |                       |             |                                            | 3/3                         |
|       |                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|       | <u>Water Resources</u>                                                                     |                  |                         |                  |                             |                       |             |                                            |                             |
| 741   | PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam                                              | 01/2001          | 542.90 -                | 1,187.00         | 35.49                       | 12/2007 -             | 12/2012     | -                                          | 0/0                         |
|       | Total                                                                                      |                  | 542.90 -                | 1,187.00         | 35.49                       |                       |             |                                            | 0/0                         |
|       |                                                                                            |                  |                         |                  |                             |                       |             |                                            |                             |
|       | Grand Total                                                                                |                  | 912,567.98              | 1,087,065.02     | 503,192.40                  |                       |             |                                            | 1100/3786                   |

## Sector wise current status of projects on the Flash Report

### Urban Development


#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 4 |
| Number of Projects On Schedule | 1 |
| Number of Projects Delayed     | 1 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 2 |
|--------------------------------------------------|---|

#### Brief Analysis


**Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.**

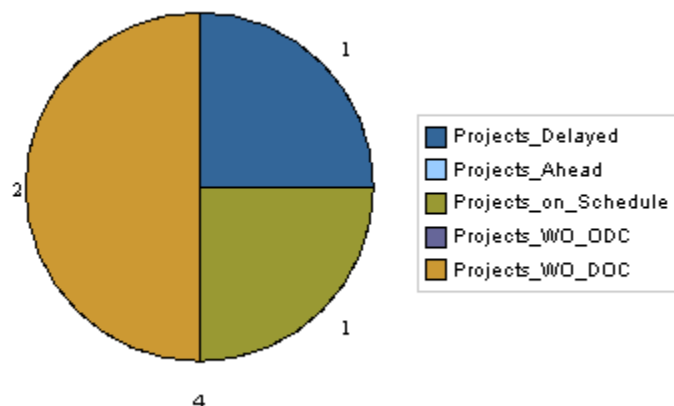

#### Investment Scenario

**The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till August, 2013 is Rs. 6421.63 crore, which is 13% of the revised cost of the projects.**

Figures are in Rs. Crore

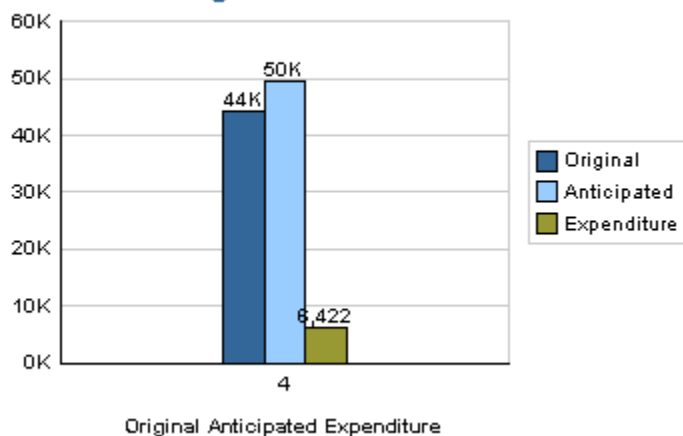

## Sector wise current status of projects on the Flash Report

### Telecommunications

#### Current Status:


Number of Projects **13**

Number of Projects Delayed **6**

Number of Projects Without Date Of Commissioning **7**

#### Brief Analysis


**Project Status with respect to Original Schedule: Out of 13 projects, 6 projects are delayed .7 projects do not have fixed dates of commissioning.**

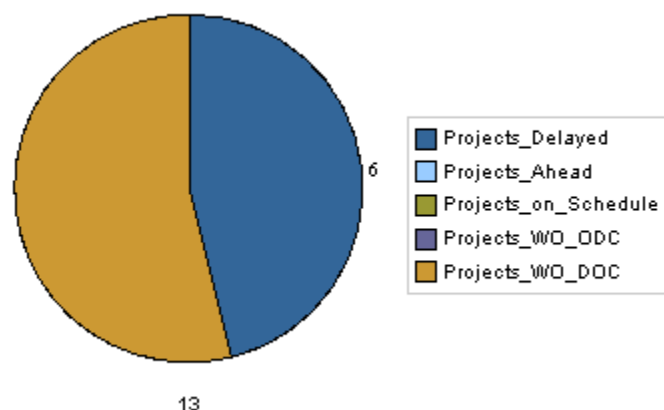

#### Investment Scenario

**The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5527.92 crore implying a cost overrun of -3%. The expenditure incurred on these projects till August, 2013 is Rs. 1970.85 crore, which is 35.7% of the revised cost of the projects.**

**Figures are in Rs. Crore**

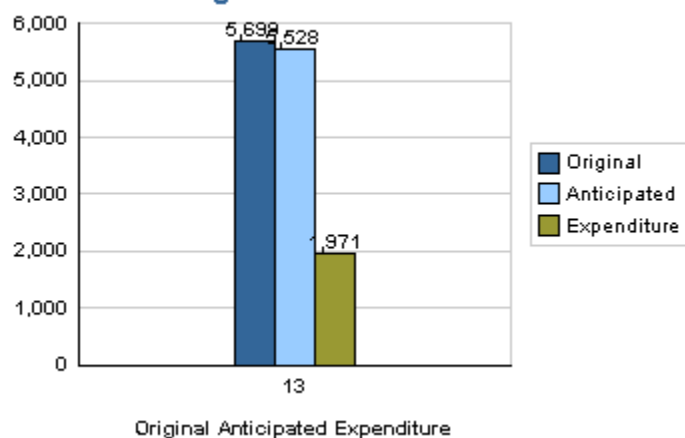

## Sector wise current status of projects on the Flash Report


### Shipping And Ports

#### Current Status:

|                                                  |    |
|--------------------------------------------------|----|
| Number of Projects                               | 19 |
| Number of Projects On Schedule                   | 1  |
| Number of Projects Delayed                       | 5  |
| Number of Projects Ahead                         | 1  |
| Number of Projects Without Date Of Commissioning | 12 |

#### Brief Analysis


**Project Status with respect to Original Schedule:** Out of 19 projects, 1 project are ahead of schedule, 1 project are on schedule and 5 projects are delayed .12 projects do not have fixed dates of commissioning.

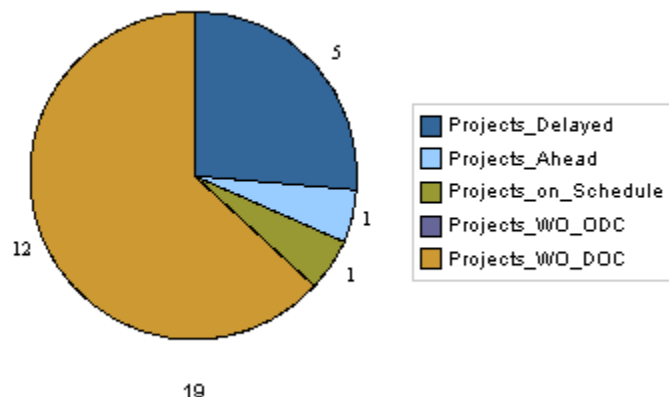

#### Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till August, 2013 is Rs. 8642.58 crore, which is 48.3% of the revised cost of the projects.

#### Figures are in Rs. Crore

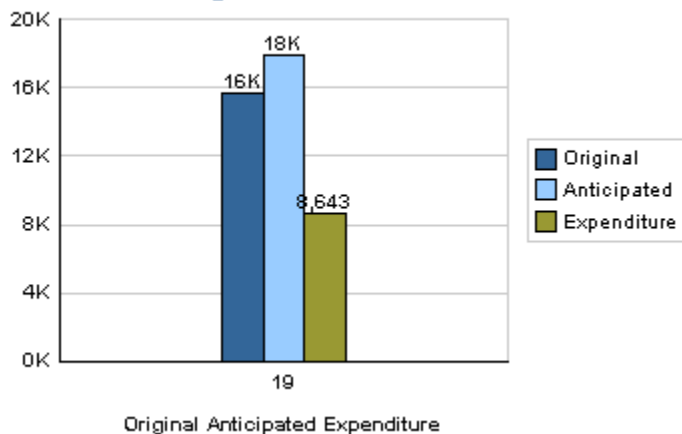

## Sector wise current status of projects on the Flash Report

### Road Transport And Highways


#### Current Status:

|                                |     |
|--------------------------------|-----|
| Number of Projects             | 152 |
| Number of Projects On Schedule | 42  |
| Number of Projects Delayed     | 100 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 5 |
| Number of Projects Without Date Of Commissioning          | 5 |

#### Brief Analysis


Project Status with respect to Original Schedule: Out of 152 projects, 42 projects are on schedule and 100 projects are delayed .5 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

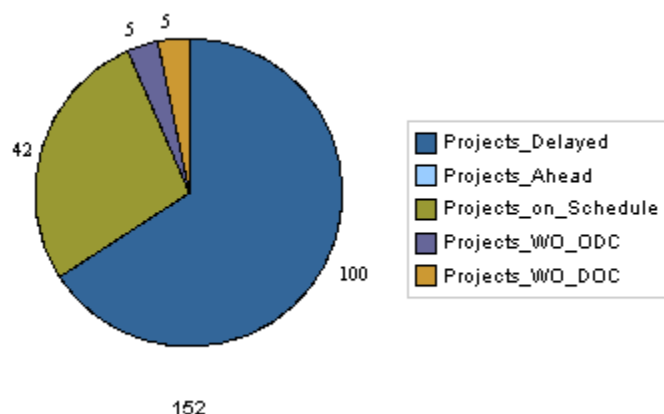

#### Investment Scenario

The Total Original cost of implementation of 152 projects when sanctioned, was of the order of Rs. 105203.54 crore but this was subsequently revised to Rs. 107142.16 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till August, 2013 is Rs. 83521.87 crore, which is 78% of the revised cost of the projects.

#### Figures are in Rs. Crore

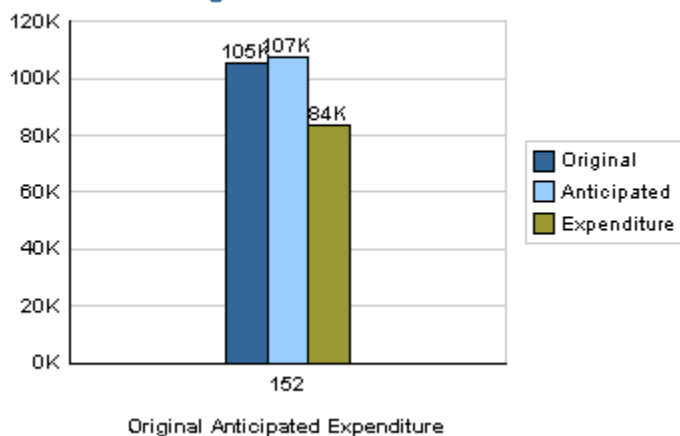

## Sector wise current status of projects on the Flash Report

### Railways


#### Current Status:

|                                |     |
|--------------------------------|-----|
| Number of Projects             | 283 |
| Number of Projects On Schedule | 16  |
| Number of Projects Delayed     | 36  |

|                                                           |     |
|-----------------------------------------------------------|-----|
| Number of Projects Without Original Date of Commissioning | 18  |
| Number of Projects Without Date Of Commissioning          | 213 |

#### Brief Analysis


**Project Status with respect to Original Schedule:** Out of 283 projects, 16 projects are on schedule and 36 projects are delayed .213 projects do not have fixed dates of commissioning.18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

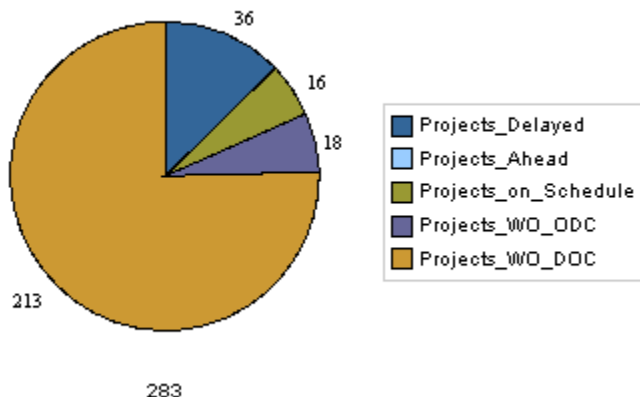

#### Investment Scenario

**The Total Original cost of implementation of 283 projects when sanctioned, was of the order of Rs. 147446.28 crore but this was subsequently revised to Rs. 258415.07 crore implying a cost overrun of 75.3%. The expenditure incurred on these projects till August, 2013 is Rs. 75004.75 crore, which is 29% of the revised cost of the projects.**

#### Figures are in Rs. Crore

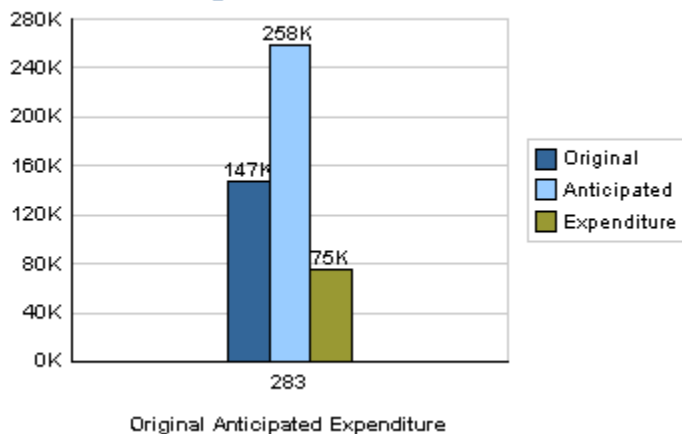

## Sector wise current status of projects on the Flash Report


### Power

#### Current Status:

|                                                           |    |
|-----------------------------------------------------------|----|
| Number of Projects                                        | 99 |
| Number of Projects On Schedule                            | 38 |
| Number of Projects Delayed                                | 51 |
| Number of Projects Ahead                                  | 3  |
| Number of Projects Without Original Date of Commissioning | 1  |
| Number of Projects Without Date Of Commissioning          | 6  |

#### Brief Analysis


**Project Status with respect to Original Schedule:** Out of 99 projects, 3 projects are ahead of schedule, 38 projects are on schedule and 51 projects are delayed .6 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

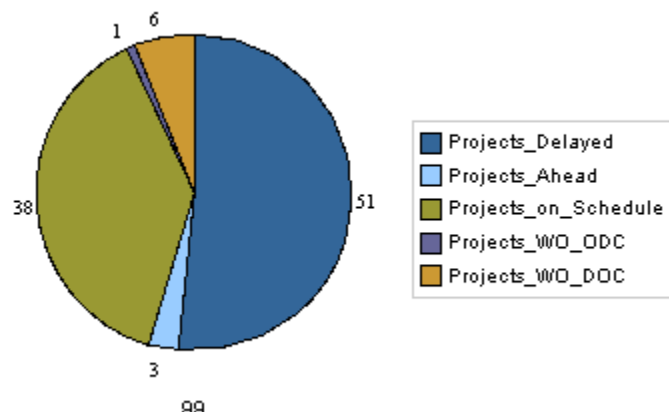

#### Investment Scenario

The Total Original cost of implementation of 99 projects when sanctioned, was of the order of Rs. 254014.6 crore but this was subsequently revised to Rs. 273611.01 crore implying a cost overrun of 7.7%. The expenditure incurred on these projects till August, 2013 is Rs. 128680.52 crore, which is 47% of the revised cost of the projects.

#### Figures are in Rs. Crore

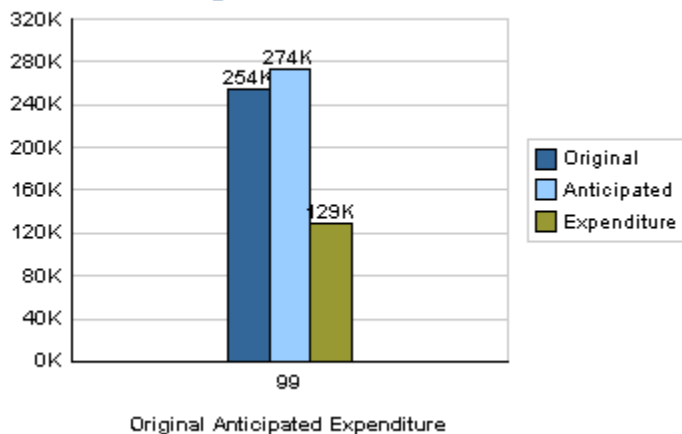

## Sector wise current status of projects on the Flash Report

### Petroleum


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 84 |
| Number of Projects On Schedule | 20 |
| Number of Projects Delayed     | 54 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 2 |
| Number of Projects Without Date Of Commissioning          | 8 |

#### Brief Analysis


**Project Status with respect to Original Schedule:** Out of 84 projects, 20 projects are on schedule and 54 projects are delayed .8 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

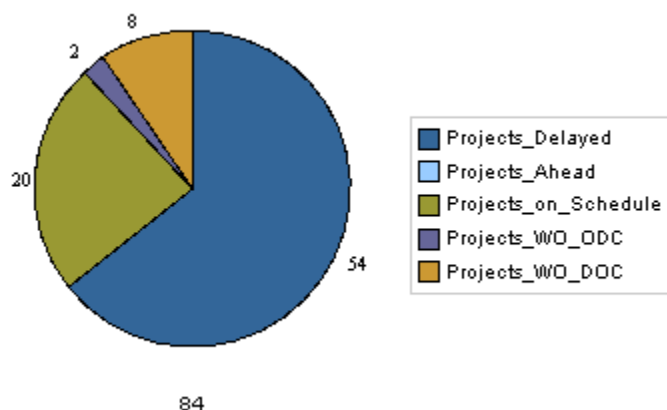

#### Investment Scenario

**The Total Original cost of implementation of 84 projects when sanctioned, was of the order of Rs. 184108.78 crore but this was subsequently revised to Rs. 198495.51 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till August, 2013 is Rs. 94028.32 crore, which is 47.4% of the revised cost of the projects.**

#### Figures are in Rs. Crore

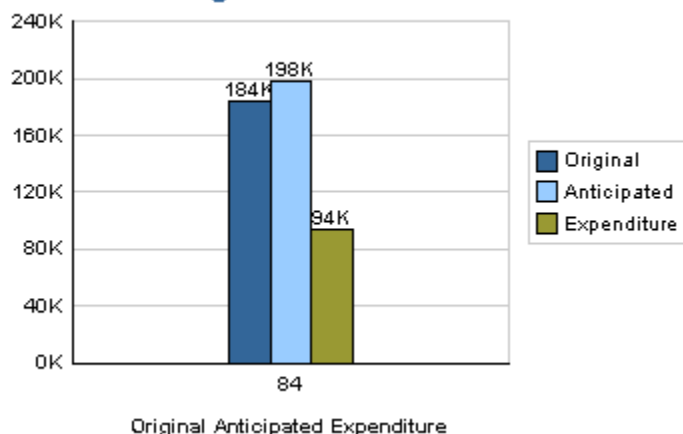



## Sector wise current status of projects on the Flash Report

### Steel


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 18 |
| Number of Projects On Schedule | 3  |
| Number of Projects Delayed     | 14 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 1 |
|--------------------------------------------------|---|

#### Brief Analysis


**Project Status with respect to Original Schedule:** Out of 18 projects, 3 projects are on schedule and 14 projects are delayed .1 project do not have fixed dates of commissioning.

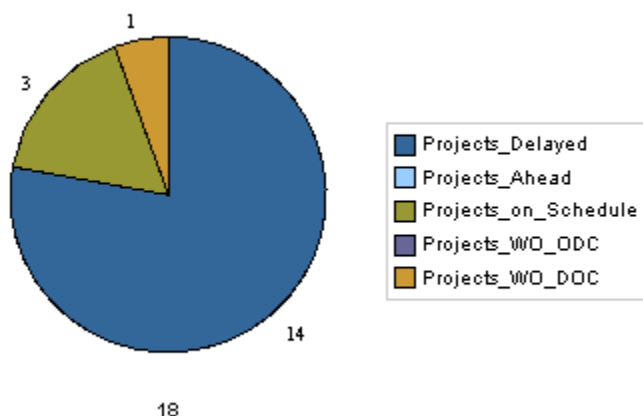

#### Investment Scenario

The Total Original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 65625.22 crore but this was subsequently revised to Rs. 71782.4 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till August, 2013 is Rs. 53178.98 crore, which is 74.1% of the revised cost of the projects.

#### Figures are in Rs. Crore

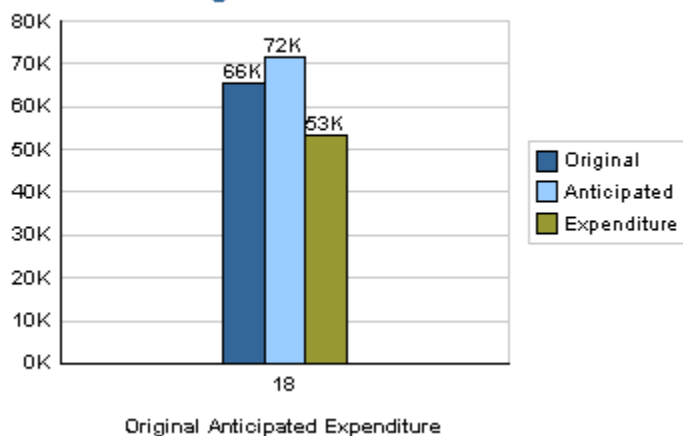

## Sector wise current status of projects on the Flash Report

### Coal


#### Current Status:

|                                |    |
|--------------------------------|----|
| Number of Projects             | 55 |
| Number of Projects On Schedule | 22 |
| Number of Projects Delayed     | 28 |

|                                                           |   |
|-----------------------------------------------------------|---|
| Number of Projects Without Original Date of Commissioning | 1 |
| Number of Projects Without Date Of Commissioning          | 4 |

#### Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 22 projects are on schedule and 28 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

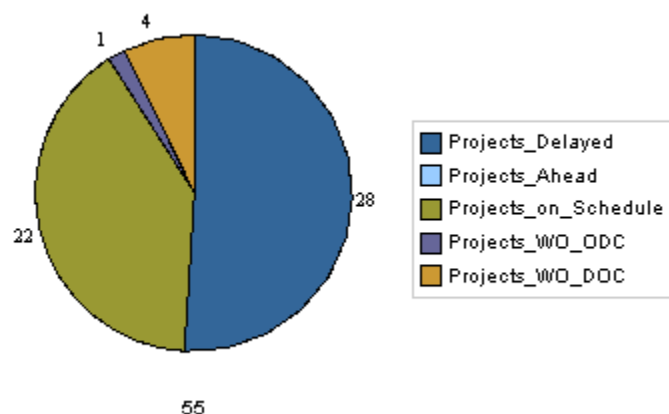

#### Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41212.5 crore implying a cost overrun of 8.1%. The expenditure incurred on these projects till August, 2013 is Rs. 15401.75 crore, which is 37.4% of the revised cost of the projects.

#### Figures are in Rs. Crore

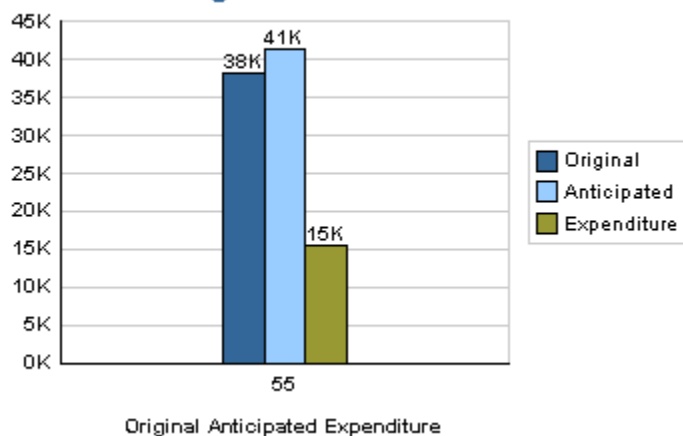

## Sector wise current status of projects on the Flash Report

### Civil Aviation


#### Current Status:

|                                |   |
|--------------------------------|---|
| Number of Projects             | 8 |
| Number of Projects On Schedule | 3 |
| Number of Projects Delayed     | 2 |

|                                                  |   |
|--------------------------------------------------|---|
| Number of Projects Without Date Of Commissioning | 3 |
|--------------------------------------------------|---|

#### Brief Analysis


**Project Status with respect to Original Schedule:** Out of 8 projects, 3 projects are on schedule and 2 projects are delayed .3 projects do not have fixed dates of commissioning.

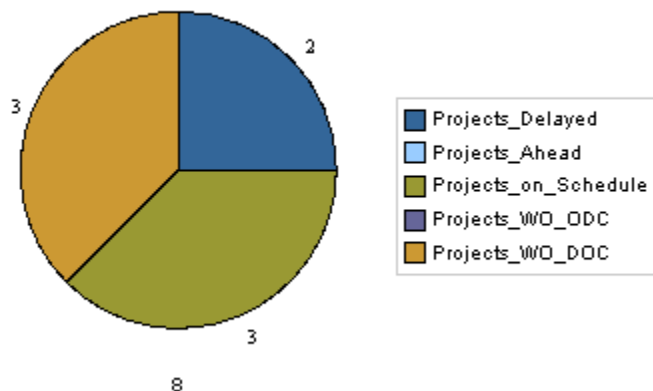

#### Investment Scenario

**The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6624.95 crore implying a cost overrun of 9.8%. The expenditure incurred on these projects till August, 2013 is Rs. 5421.55 crore, which is 81.8% of the revised cost of the projects.**

#### Figures are in Rs. Crore

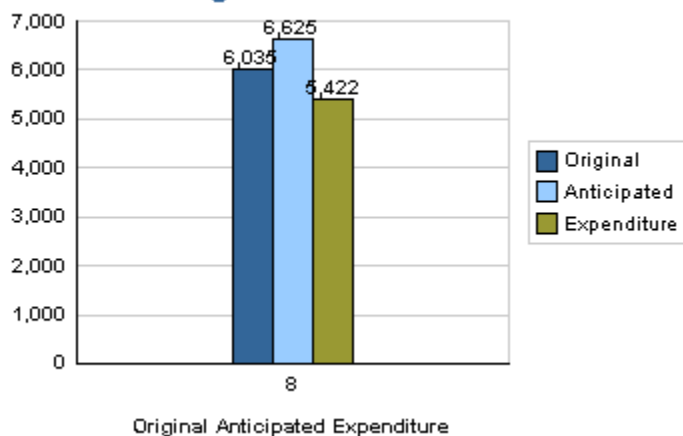

## Sector wise current status of projects on the Flash Report


### Atomic Energy

#### Current Status:

|                            |   |
|----------------------------|---|
| Number of Projects         | 4 |
| Number of Projects Delayed | 4 |

#### Brief Analysis


**Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .**



#### Investment Scenario

**The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till August, 2013 is Rs. 26373.6 crore, which is 56.4% of the revised cost of the projects.**

Figures are in Rs. Crore

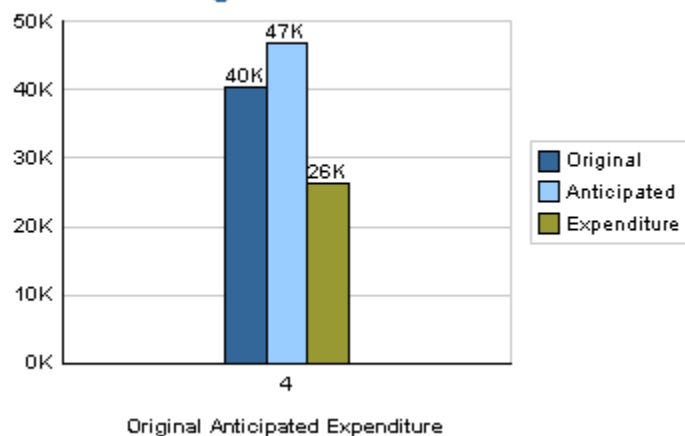

# *ANNEXURES*

### LIST OF CENTRAL SECTOR PROJECTS

| SN           | STATE             | NO OF<br>PROJECTS | COST<br>ORIGINAL | COST<br>ANTICIPATED | CUMULATIVE<br>EXPENDITURE |
|--------------|-------------------|-------------------|------------------|---------------------|---------------------------|
| 1            | Andhra Pradesh    | 46                | 37404.55         | 45444.29            | 23299.77                  |
| 2            | Arunachal Pradesh | 4                 | 9512.22          | 17330.32            | 9792.78                   |
| 3            | Assam             | 41                | 24155.49         | 38429.73            | 25401.30                  |
| 4            | Bihar             | 46                | 32579.04         | 41019.11            | 27996.46                  |
| 5            | Chandigarh        | 1                 | 452.00           | 452.00              | 127.08                    |
| 6            | Chhatisgarh       | 24                | 58278.32         | 59362.92            | 22097.89                  |
| 7            | Delhi             | 6                 | 38669.29         | 38649.70            | 4337.56                   |
| 8            | Goa               | 1                 | 335.61           | 335.61              | 233.69                    |
| 9            | Gujarat           | 34                | 38828.13         | 39875.20            | 14000.50                  |
| 10           | Haryana           | 10                | 4741.38          | 6423.96             | 7279.80                   |
| 11           | Himachal Pradesh  | 6                 | 14402.45         | 20285.83            | 14646.39                  |
| 12           | Jammu and Kashmir | 9                 | 14305.70         | 33912.56            | 15454.00                  |
| 13           | Jharkhand         | 26                | 15873.15         | 20137.52            | 9818.45                   |
| 14           | Karnataka         | 37                | 53868.01         | 63787.67            | 26493.23                  |
| 15           | Kerala            | 10                | 21010.59         | 22804.14            | 6171.54                   |
| 16           | Madhya pradesh    | 22                | 31749.13         | 32975.51            | 10121.18                  |
| 17           | Maharashtra       | 56                | 95785.33         | 109495.29           | 48642.01                  |
| 18           | Manipur           | 1                 | 727.56           | 4453.50             | 1595.53                   |
| 19           | Meghalaya         | 3                 | 4845.02          | 4845.02             | 805.20                    |
| 20           | Mizoram           | 2                 | 1532.97          | 3297.97             | 548.12                    |
| 21           | Multi State       | 174               | 188081.51        | 210851.88           | 85054.51                  |
| 22           | Nagaland          | 2                 | 5124.00          | 6715.48             | 8.94                      |
| 23           | Odisha            | 31                | 56321.53         | 63614.31            | 40980.46                  |
| 24           | Punjab            | 6                 | 2212.64          | 3154.41             | 3637.63                   |
| 25           | Rajasthan         | 25                | 25256.57         | 25682.57            | 10854.39                  |
| 26           | Sikkim            | 2                 | 1648.94          | 3690.04             | 291.20                    |
| 27           | Tamil Nadu        | 41                | 53242.79         | 68268.93            | 44437.34                  |
| 28           | Tripura           | 5                 | 2669.39          | 4358.45             | 2246.08                   |
| 29           | Uttar Pradesh     | 30                | 22605.71         | 27184.92            | 14422.34                  |
| 30           | Uttarakhand       | 6                 | 7844.04          | 10199.28            | 2705.93                   |
| 31           | West Bengal       | 34                | 48504.92         | 60026.90            | 29691.10                  |
| <b>TOTAL</b> |                   | <b>741</b>        | <b>912567.98</b> | <b>1087065.02</b>   | <b>503192.40</b>          |

**List of Projects in which Expenditure is more than cost**

| SN | PROJECT                                                                                              | SECTOR         | DOA     | COST ORIGINAL | COST REVISED | EXPENDITURE CUMM |
|----|------------------------------------------------------------------------------------------------------|----------------|---------|---------------|--------------|------------------|
| 1  | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)                                                    | Atomic Energy  | 09/2003 | 3492.00       | 0.00         | 4681.60          |
| 2  | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT                                                    | Civil Aviation | 08/2008 | 1942.51       | 0.00         | 2472.95          |
| 3  | KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I                                        | Petroleum      | 07/2009 | 238.68        | 0.00         | 293.12           |
| 4  | RESITMENT OF MARKETING INSTALATION AT VISAKH                                                         | Petroleum      | 01/2009 | 756.00        | 898.00       | 913.72           |
| 5  | IOR GELEKI (ONGCL)                                                                                   | Petroleum      | 09/2001 | 390.09        | 1674.11      | 1727.24          |
| 6  | IOR LAKWA - LAKHMANI (ONGCL)                                                                         | Petroleum      | 09/2001 | 345.10        | 663.69       | 729.07           |
| 7  | SUBANSIRI LOWER H.E.P (NHPC)                                                                         | Power          | 09/2003 | 6285.33       | 0.00         | 6332.94          |
| 8  | PARBATI HEP (NHPC) II                                                                                | Power          | 09/2002 | 3919.59       | 0.00         | 4027.33          |
| 9  | URI H.E.P STAGE -II (NHPC)                                                                           | Power          | 08/2005 | 1729.29       | 0.00         | 2035.18          |
| 10 | TEESTA LOW DAM HEP, STAGE-IV (NHPC)                                                                  | Power          | 09/2005 | 1061.38       | 0.00         | 1376.77          |
| 11 | NIMOO BAZGO HYDROELECTRIC PROJECT                                                                    | Power          | 08/2006 | 611.01        | 0.00         | 874.31           |
| 12 | KOLDAM HEP (NTPC)                                                                                    | Power          | 10/2002 | 4527.15       | 0.00         | 5095.00          |
| 13 | RAMPUR HEP(412 MW)                                                                                   | Power          | 01/2007 | 2047.03       | 0.00         | 2671.47          |
| 14 | PANVEL PEN DOUBLING                                                                                  | Railways       | 04/2006 | 191.00        | 0.00         | 195.08           |
| 15 | Sakri-Hasanpur Road (NL)                                                                             | Railways       | 04/1999 | 175.69        | 0.00         | 230.66           |
| 16 | LANJHIGARH-JUNAGARH NL(ECOR)                                                                         | Railways       | 04/1993 | 100.00        | 142.98       | 229.30           |
| 17 | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR                                                    | Railways       | 04/1996 | 114.01        | 332.92       | 438.36           |
| 18 | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR                                                            | Railways       | 04/1997 | 233.00        | 501.69       | 712.97           |
| 19 | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)                      | Railways       | 03/2000 | 907.69        | 3156.32      | 3451.00          |
| 20 | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR                                     | Railways       | 09/1996 | 156.00        | 156.00       | 350.63           |
| 21 | KATIHAR - JOGBANI (GC)(NEFR)                                                                         | Railways       | 09/2001 | 100.00        | 492.98       | 742.54           |
| 22 | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project                               | Railways       | 04/1996 | 1676.31       | 1676.31      | 3635.42          |
| 23 | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR                                                         | Railways       | 09/1997 | 1000.00       | 1500.00      | 2836.11          |
| 24 | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR                                               | Railways       | 04/2000 | 733.00        | 733.00       | 1477.35          |
| 25 | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR                                             | Railways       | 01/2004 | 915.70        | 915.70       | 2174.43          |
| 26 | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR                                                   | Railways       | 12/2006 | 170.00        | 170.00       | 411.28           |
| 27 | New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai | Railways       | 04/1999 | 523.17        | 0.00         | 1032.88          |

|    |                                                                                                       |                             |         |         |         |         |
|----|-------------------------------------------------------------------------------------------------------|-----------------------------|---------|---------|---------|---------|
| 28 | Construction of NL from Kumarghat-Agartala                                                            | Railways                    | 04/1999 | 895.00  | 0.00    | 944.78  |
| 29 | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)                                                                   | Railways                    | 04/2003 | 727.56  | 727.53  | 1595.53 |
| 30 | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)                                                               | Railways                    | 04/1999 | 323.40  | 323.40  | 513.75  |
| 31 | JIND-SONEPAT (NL),NR                                                                                  | Railways                    | 01/2004 | 190.81  | 238.56  | 472.03  |
| 32 | CHANDIGARH-LUDHIANA(NEW BG LINE),NR                                                                   | Railways                    | 07/1998 | 248.44  | 576.27  | 969.33  |
| 33 | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR                                                                | Railways                    | 03/2002 | 409.00  | 625.30  | 836.10  |
| 34 | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR                                                                   | Railways                    | 03/1995 | 2500.00 | 2500.00 | 8822.50 |
| 35 | Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC)                                | Railways                    | 04/2010 | 739.65  | 0.00    | 788.94  |
| 36 | Mavli Jn.-Bari Sadri, MM of Ajmer-Chittsurgarh-Udaipur                                                | Railways                    | 04/2013 | 456.00  | 0.00    | 557.35  |
| 37 | RAICHUR-GUNTAKAL(DL)(SCR)                                                                             | Railways                    | 04/2003 | 136.62  | 0.00    | 264.04  |
| 38 | BHOPAL BINA 3D LINE DOUBLING                                                                          | Railways                    | 09/2007 | 687.20  | 0.00    | 735.19  |
| 39 | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)                                                             | Railways                    | 04/2000 | 133.41  | 207.00  | 254.02  |
| 40 | RAJATGARH-BARANG(LD),ECOR                                                                             | Railways                    | 04/1999 | 166.16  | 0.00    | 281.73  |
| 41 | NANDYAL-YERRAGUNTALA(NL),SCR                                                                          | Railways                    | 03/1996 | 155.74  | 429.49  | 657.88  |
| 42 | GADWAL - RAICHUR (NL), SCR                                                                            | Railways                    | 04/1998 | 92.63   | 228.09  | 281.00  |
| 43 | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)                                                                | Railways                    | 12/1994 | 124.43  | 495.68  | 624.87  |
| 44 | RANCHI-LOHARDAGA(GC),SER                                                                              | Railways                    | 04/1997 | 194.07  | 194.07  | 347.58  |
| 45 | Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif | Railways                    | 04/2007 | 247.00  | 0.00    | 516.64  |
| 46 | KARUR-SALEM(NL),SR                                                                                    | Railways                    | 02/1997 | 155.55  | 155.00  | 754.44  |
| 47 | Chennai Beach-Tambaram-Chengalpattu Suburban GC                                                       | Railways                    | 04/1999 | 271.24  | 0.00    | 458.21  |
| 48 | Cuddalore-Salem via Vriddhachalam GC                                                                  | Railways                    | 04/1999 | 198.68  | 0.00    | 266.14  |
| 49 | CALICUT-MANGALORE (DL) (SR)                                                                           | Railways                    | 02/1996 | 240.00  | 0.00    | 599.40  |
| 50 | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)                                                               | Railways                    | 09/1995 | 100.00  | 100.00  | 546.50  |
| 51 | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE                                                     | Railways                    | 09/2006 | 343.17  | 343.17  | 664.99  |
| 52 | Kolar-Chickbalapur GC                                                                                 | Railways                    | 04/2006 | 287.99  | 0.00    | 421.25  |
| 53 | Munirabad (gingera) -Raichur NL                                                                       | Railways                    | 04/2007 | 179.65  | 0.00    | 248.11  |
| 54 | Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)                             | Railways                    | 04/2007 | 482.00  | 482.70  | 486.44  |
| 55 | KOTTUR-HARIHAR(NL),(SWR)                                                                              | Railways                    | 04/1995 | 65.94   | 302.23  | 354.49  |
| 56 | KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)                                                               | Railways                    | 04/1996 | 157.00  | 262.82  | 308.25  |
| 57 | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR                                                         | Railways                    | 02/1997 | 295.00  | 412.91  | 672.78  |
| 58 | Armur to kadloor yellareddy                                                                           | Road Transport And Highways | 02/2010 | 390.56  | 0.00    | 772.40  |



|    |                                                                |                                |         |        |      |        |
|----|----------------------------------------------------------------|--------------------------------|---------|--------|------|--------|
| 59 | BRAHMPUTRA BRIDGE,NH NO-31                                     | Road Transport<br>And Highways | 12/2003 | 217.61 | 0.00 | 290.00 |
| 60 | Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)           | Road Transport<br>And Highways | 05/2009 | 572.30 | 0.00 | 832.90 |
| 61 | DHARAMTUL TO SONAPUR (AS-19)                                   | Road Transport<br>And Highways | 12/2003 | 200.00 | 0.00 | 253.60 |
| 62 | NALBARI T BIJNI (AS-7)                                         | Road Transport<br>And Highways | 12/2003 | 208.00 | 0.00 | 303.90 |
| 63 | GUWAHATI TO NALBARI (AS-5)                                     | Road Transport<br>And Highways | 12/2003 | 198.16 | 0.00 | 272.30 |
| 64 | NAGAON TO DHARAMTUL (AS-2)                                     | Road Transport<br>And Highways | 12/2003 | 264.72 | 0.00 | 301.10 |
| 65 | SILCHAR-UDARBAND (PH.II) HN-54,<br>KM.309 TO KM.275            | Road Transport<br>And Highways | 12/2003 | 157.47 | 0.00 | 240.40 |
| 66 | BIJNI TO ASSAM/WB BORDER PH.II,<br>KM.30.00 TO 0.00, NH-31 C   | Road Transport<br>And Highways | 12/2003 | 230.00 | 0.00 | 239.20 |
| 67 | HARANGAJO TO MAIBANG (AS-23),<br>KM.126.450 TO KM.140.700      | Road Transport<br>And Highways | 12/2003 | 280.00 | 0.00 | 322.50 |
| 68 | BIJNI TO ASSAM WB BORDER (NH-<br>31.C)(1)(NHAI)                | Road Transport<br>And Highways | 12/2003 | 195.00 | 0.00 | 250.10 |
| 69 | BIJNI TO ASSAM /WB.BORDER (NH-<br>31.C)(NHAI)                  | Road Transport<br>And Highways | 12/2003 | 237.80 | 0.00 | 287.50 |
| 70 | NALBARI TO BIJNI (AS-8)                                        | Road Transport<br>And Highways | 12/2003 | 200.00 | 0.00 | 286.90 |
| 71 | GUWHATI TO NALBARI (AS-4)                                      | Road Transport<br>And Highways | 12/2003 | 175.96 | 0.00 | 211.60 |
| 72 | SONAPUR TO GUWAHTI (AS-3)                                      | Road Transport<br>And Highways | 12/2003 | 245.00 | 0.00 | 491.20 |
| 73 | DEVIHALLI-HASSAN                                               | Road Transport<br>And Highways | 12/2010 | 453.00 | 0.00 | 713.90 |
| 74 | BELGAUM-DHARWAD(NH-4)                                          | Road Transport<br>And Highways | 12/2010 | 480.00 | 0.00 | 563.30 |
| 75 | VIJAYAPUR TO PATHANKOT (NS-35/J AND<br>K) NH-1A KM.50 TO KM.80 | Road Transport<br>And Highways | 12/2003 | 166.27 | 0.00 | 198.50 |

|    |                                                             |                             |         |         |      |         |
|----|-------------------------------------------------------------|-----------------------------|---------|---------|------|---------|
| 76 | DELHI/ HARYANA BORDER TO ROHTAK                             | Road Transport And Highways | 04/2007 | 486.00  | 0.00 | 653.40  |
| 77 | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)                 | Road Transport And Highways | 05/2009 | 1108.00 | 0.00 | 3465.90 |
| 78 | PANIPAT-ROHTAK                                              | Road Transport And Highways | 04/2011 | 807.00  | 0.00 | 1318.00 |
| 79 | ROHTAK-BAWAL                                                | Road Transport And Highways | 05/2011 | 650.00  | 0.00 | 1106.00 |
| 80 | Gujarat/Maharashtra Border Surat-Hazira Port Section        | Road Transport And Highways | 03/2010 | 1509.10 | 0.00 | 2080.00 |
| 81 | 4 LANNING OF AHMEDABAD TO GODHARA                           | Road Transport And Highways | 12/2010 | 1008.50 | 0.00 | 1346.00 |
| 82 | Hungund-Surathkal and Mangalore-Knt/Kerala Border           | Road Transport And Highways | 09/2010 | 946.00  | 0.00 | 1790.00 |
| 83 | KUNDUPUR-SURATHKAL & MANGLORE                               | Road Transport And Highways | 09/2010 | 671.00  | 0.00 | 929.60  |
| 84 | 4 LANNING OF GODHARA TO GUJARAT/MP BORDER                   | Road Transport And Highways | 03/2011 | 785.50  | 0.00 | 839.30  |
| 85 | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 | Road Transport And Highways | 12/2003 | 240.00  | 0.00 | 295.00  |
| 86 | FORBESGANJ TO SIMRAHI (NH-57)(NHAI)                         | Road Transport And Highways | 12/2003 | 332.94  | 0.00 | 470.20  |
| 87 | 2 LANNING OF MOKAMA-MUNGER                                  | Road Transport And Highways | 05/2011 | 351.54  | 0.00 | 394.10  |
| 88 | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95                      | Road Transport And Highways | 09/2011 | 574.00  | 0.00 | 646.10  |
| 89 | 4-LANNING OF CHAPRA-HAJIPUR                                 | Road Transport And Highways | 01/2011 | 575.00  | 0.00 | 714.40  |
| 90 | 2 LANNING OF MUZAFFARPUR - SONBARSA                         | Road Transport And Highways | 05/2011 | 511.54  | 0.00 | 631.80  |
| 91 | NALBARI TO BIJNI (AS-6)                                     | Road Transport And Highways | 12/2003 | 225.00  | 0.00 | 264.70  |
| 92 | Kishangarh-Ajmer-Beawer                                     | Road Transport And Highways | 11/2009 | 795.00  | 0.00 | 1127.00 |

|     |                                                          |                             |         |         |      |         |
|-----|----------------------------------------------------------|-----------------------------|---------|---------|------|---------|
| 93  | Jaipur-Tonk-Deoli                                        | Road Transport And Highways | 06/2010 | 792.06  | 0.00 | 1972.00 |
| 94  | JAIPUR-REENGUS                                           | Road Transport And Highways | 08/2010 | 267.81  | 0.00 | 648.30  |
| 95  | PATHANKOT- BHOGPUR, KM.26-KM.70, NS 38 NH-1A             | Road Transport And Highways | 12/2003 | 284.00  | 0.00 | 315.50  |
| 96  | AMRITSAR-PATHANKOT                                       | Road Transport And Highways | 05/2010 | 705.00  | 0.00 | 2124.00 |
| 97  | GANJAM-ICCHAPURUM,NH-5(NHAI)                             | Road Transport And Highways | 04/2000 | 263.27  | 0.00 | 276.46  |
| 98  | BHUBANESWAR TO PURI                                      | Road Transport And Highways | 03/2011 | 500.29  | 0.00 | 509.00  |
| 99  | SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER              | Road Transport And Highways | 11/2011 | 909.00  | 0.00 | 941.90  |
| 100 | 2-LANNING OF SHILONG BYPASS                              | Road Transport And Highways | 02/2011 | 226.00  | 0.00 | 288.80  |
| 101 | Hazaribagh-Ranchi                                        | Road Transport And Highways | 08/2010 | 625.07  | 0.00 | 947.60  |
| 102 | 4-laning of Barhi-Hazaribagh                             | Road Transport And Highways | 02/2012 | 398.00  | 0.00 | 437.90  |
| 103 | AURANG-RAIPUR, NH-6, KM.232 TO KM.281                    | Road Transport And Highways | 03/2005 | 190.00  | 0.00 | 264.60  |
| 104 | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 | Road Transport And Highways | 12/2003 | 232.45  | 0.00 | 304.30  |
| 105 | Gurgaon-Kotputli Km 42.70 to 54.4 Km                     | Road Transport And Highways | 04/2009 | 1673.70 | 0.00 | 2839.00 |
| 106 | Surat- Dahisar(Six Lane) Km 263 to Km 502                | Road Transport And Highways | 02/2009 | 1693.75 | 0.00 | 2707.00 |
| 107 | 4-laning of Faraka-Raiganj                               | Road Transport And Highways | 02/2011 | 1078.84 | 0.00 | 1226.00 |
| 108 | 4-laning of Brahampore-Faraka                            | Road Transport And Highways | 02/2011 | 998.79  | 0.00 | 1202.00 |
| 109 | HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24             | Road Transport And Highways | 03/2005 | 220.00  | 0.00 | 284.20  |

|     |                                                              |                             |         |         |      |         |
|-----|--------------------------------------------------------------|-----------------------------|---------|---------|------|---------|
| 110 | JHANSI TO LALITPUR, NH-25,26                                 | Road Transport And Highways | 12/2003 | 355.06  | 0.00 | 507.30  |
| 111 | MURADABAD-BAREILY                                            | Road Transport And Highways | 04/2010 | 1267.00 | 0.00 | 1857.00 |
| 112 | GHAZIABAD-ALIGARH NH-91                                      | Road Transport And Highways | 02/2011 | 1141.00 | 0.00 | 1264.00 |
| 113 | THANJAUR-TRICHY,NH-67(NHAI)                                  | Road Transport And Highways | 03/2005 | 280.00  | 0.00 | 581.50  |
| 114 | TRICHY - KORUR NH-67                                         | Road Transport And Highways | 03/2005 | 516.00  | 0.00 | 858.90  |
| 115 | SALEM - U / UNDRUPET(BOT -1/TN-06) NH-68                     | Road Transport And Highways | 03/2005 | 941.00  | 0.00 | 1901.00 |
| 116 | Chennai-Tada(Six lane)                                       | Road Transport And Highways | 04/2009 | 353.37  | 0.00 | 417.20  |
| 117 | KOTA BYPASS,RJ-4, NH-76 (NHAI)                               | Road Transport And Highways | 12/2003 | 275.00  | 0.00 | 280.40  |
| 118 | NAGPUR-KONDHALI,NH-6(NHAI)                                   | Road Transport And Highways | 03/2005 | 168.00  | 0.00 | 457.30  |
| 119 | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)                | Road Transport And Highways | 03/2005 | 940.00  | 0.00 | 1325.00 |
| 120 | Pune-sholapur,pkg1                                           | Road Transport And Highways | 11/2009 | 1110.00 | 0.00 | 1802.00 |
| 121 | Talegaon-amravati                                            | Road Transport And Highways | 11/2009 | 567.00  | 0.00 | 1166.00 |
| 122 | RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) | Road Transport And Highways | 12/2003 | 251.03  | 0.00 | 337.80  |
| 123 | GWALIOR BYPSS, NH-75,3                                       | Road Transport And Highways | 12/2003 | 300.93  | 0.00 | 302.70  |
| 124 | INDORE-DEWAS(NH-3)                                           | Road Transport And Highways | 11/2010 | 325.00  | 0.00 | 518.70  |
| 125 | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH                | Road Transport And Highways | 03/2005 | 557.00  | 0.00 | 1128.00 |
| 126 | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)                      | Road Transport And Highways | 12/2003 | 160.00  | 0.00 | 207.20  |

|     |                                                               |                    |         |          |        |          |
|-----|---------------------------------------------------------------|--------------------|---------|----------|--------|----------|
| 127 | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST | Shipping And Ports | 03/2007 | 245.67   | 298.17 | 371.18   |
| 128 | Acquisition of Two nos. of 3060 DWT                           | Shipping And Ports | 04/2009 | 277.03   | 280.00 | 294.87   |
| 129 | EXPANSION OF IISCO STEEL PLANT                                | Steel              | 02/2008 | 14443.00 | 0.00   | 14967.69 |

## List of Projects Ahead of Schedule w.r.t. Original Schedule

|      |                                                                                                                   |                  |                                     |                              |                                         | (Aug,2013)            |             |
|------|-------------------------------------------------------------------------------------------------------------------|------------------|-------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|      |                                                                                                                   |                  |                                     |                              |                                         | Date of Commissioning |             |
| S.No | Project                                                                                                           | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                                                                 | 3                | 4                                   | 5                            | 6                                       | 7                     | 8           |
|      |                                                                                                                   |                  |                                     |                              |                                         |                       |             |
|      | <u>Power</u>                                                                                                      |                  |                                     |                              |                                         |                       |             |
| 1    | SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144                                                | 9/2012           | 1,508.74 -                          | 1,508.74                     | 75.99                                   | 06/2016 -             | 04/2015     |
| 2    | TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129                                        | 2/2012           | 3,201.44 -                          | 3,201.44                     | 912.30                                  | 10/2014 -             | 09/2014     |
| 3    | SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137                                                  | 9/2012           | 1,935.35 -                          | 1,935.35                     | 244.36                                  | 12/2014 -             | 11/2014     |
|      | Total                                                                                                             |                  | 6,645.53 -                          | 6,645.53                     | 1,232.65                                |                       |             |
|      |                                                                                                                   |                  |                                     |                              |                                         |                       |             |
|      | <u>Shipping And Ports</u>                                                                                         |                  |                                     |                              |                                         |                       |             |
| 4    | Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052 | 10/2010          | 1,028.10<br>1,012.23                | 1,012.23                     | 554.60                                  | 12/2013<br>11/2013    | 11/2013     |
|      | Total                                                                                                             |                  | 1,028.10 -                          | 1,012.23                     | 554.60                                  |                       |             |
|      |                                                                                                                   |                  |                                     |                              |                                         |                       |             |
|      | Grand Total                                                                                                       |                  | 7,673.63                            | 7,657.76                     | 1,787.25                                |                       |             |

## List of projects without Original Date of Commissioning

| (Aug,2013) |                                                                                              |                  |                                          |                                    |                                                  |                       |                 |                                         |                                  |
|------------|----------------------------------------------------------------------------------------------|------------------|------------------------------------------|------------------------------------|--------------------------------------------------|-----------------------|-----------------|-----------------------------------------|----------------------------------|
|            |                                                                                              |                  |                                          |                                    |                                                  | Date of Commissioning |                 |                                         |                                  |
| Sl.No      | Project                                                                                      | Date of Approval | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>Cost<br>(Rs. crore) | Original<br>/ Revised | Antici<br>pated | Delay w.r.t.<br>Original<br>(in months) | Milestones<br>Achieved/<br>Total |
| 1          | 2                                                                                            | 3                | 4                                        | 5                                  | 6                                                | 7                     | 8               | 9                                       | 10                               |
|            | <u>Coal</u>                                                                                  |                  |                                          |                                    |                                                  |                       |                 |                                         |                                  |
| 1          | RFR OF MANUGURU OC PROJECT -<br>[N06000102]SCCL,Andhra Pradesh                               | 11/2012          | 430.14<br>-                              | 430.14                             | 58.87                                            | -<br>-                | 03/2016         | -                                       | 4/48                             |
|            | Total                                                                                        |                  | 430.14<br>-                              | 430.14                             | 58.87                                            |                       |                 |                                         | 4/48                             |
|            | <u>Petroleum</u>                                                                             |                  |                                          |                                    |                                                  |                       |                 |                                         |                                  |
| 2          | RESITEMENT OF MARKETING INSTALATION<br>AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh       | 01/2009          | 756.00<br>898.00                         | 898.00                             | 913.72                                           | -<br>-                | 08/2013         | -                                       | 52/53                            |
| 3          | Surat Paradip Pipeline Project -<br>[N16000163]GAIL,Multi State                              | 10/2012          | 10,281.00<br>-                           | 10,281.00                          | 0.04                                             | -<br>-                | 04/2015         | -                                       | 0/0                              |
|            | Total                                                                                        |                  | 11,037.00<br>-                           | 11,179.00                          | 913.76                                           |                       |                 |                                         | 52/53                            |
|            | <u>Power</u>                                                                                 |                  |                                          |                                    |                                                  |                       |                 |                                         |                                  |
| 4          | TRIPURA GAS BASED POWER PROJECT -<br>[N18000071]NEEPCO,Tripura                               | 07/2009          | 421.01<br>623.44                         | 960.79                             | 618.62                                           | -<br>-                | 05/2014         | -                                       | 10/29                            |
|            | Total                                                                                        |                  | 421.01<br>-                              | 960.79                             | 618.62                                           |                       |                 |                                         | 10/29                            |
|            | <u>Railways</u>                                                                              |                  |                                          |                                    |                                                  |                       |                 |                                         |                                  |
| 5          | CHHINDWARA - NAGPUR (GC)(SECR) -<br>[220100324]SECR,Madhya pradesh                           | 04/2005          | 383.79<br>-                              | 585.93                             | 194.91                                           | -<br>-                | 12/2013         | -                                       | 0/0                              |
| 6          | CONSTRUCTION OF NEW LINE FROM<br>HARMATI-ITANAGAR/NAR -<br>[N22000083]NEFR,Arunachal Pradesh | 09/1996          | 156.00<br>156.00                         | 406.40                             | 350.63                                           | -<br>-                | 12/2013         | -                                       | 0/0                              |
| 7          | PANVEL PEN DOUBLING -<br>[N22000255]CR,Multi State                                           | 04/2006          | 191.00<br>-                              | 191.00                             | 195.08                                           | -<br>-                | 12/2013         | -                                       | 0/0                              |
| 8          | DAUSA-GANGAPUR CITY(NL),NWR -<br>[220100184]NWR,Rajasthan                                    | 02/1997          | 151.84<br>410.08                         | 410.08                             | 238.17                                           | -<br>-                | 03/2014         | -                                       | 0/0                              |
| 9          | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC<br>(NER) - [220100256]NER,Multi State                      | 04/1999          | 323.40<br>323.40                         | 744.71                             | 513.75                                           | -<br>-                | 03/2014         | -                                       | 0/1                              |
| 10         | KHURDA ROAD-BOLANGIR(NL)ECOR -<br>[220100284]ECOR,Odisha                                     | 04/1994          | 355.38<br>470.21                         | 1,995.25                           | 260.49                                           | -<br>-                | 03/2014         | -                                       | 0/0                              |
| 11         | RANGIA-MURKONGSELEK, (GC) ALONG<br>WITH LINKED FINGER -<br>[220100315]NEFR,Multi State       | 01/2004          | 915.70<br>915.70                         | 3,019.17                           | 2,174.43                                         | -<br>-                | 03/2014         | -                                       | 0/0                              |
| 12         | HATHUA-BHATNI (N L) (NER) -<br>[220100319]NER,Multi State                                    | 04/2005          | 230.03<br>230.03                         | 230.03                             | 149.24                                           | -<br>-                | 03/2014         | -                                       | 0/0                              |
| 13         | New BG line from Dudhnoi-Mendipatar -<br>[N22000192]NEFR,Multi State                         | 04/1999          | 175.43<br>-                              | 247.75                             | 145.43                                           | -<br>-                | 03/2014         | -                                       | 0/0                              |
| 14         | Viramgam-Surendranagar (DL) -<br>[N22000146]WR,Gujarat                                       | 04/2010          | 279.40<br>-                              | 264.06                             | 92.78                                            | -<br>-                | 04/2014         | -                                       | 0/0                              |

(Aug,2013)

|       |                                                                                  |                  |                                          |                                    |                                                  | Date of Commissioning    |                 |                                         |                                  |
|-------|----------------------------------------------------------------------------------|------------------|------------------------------------------|------------------------------------|--------------------------------------------------|--------------------------|-----------------|-----------------------------------------|----------------------------------|
| Sl.No | Project                                                                          | Date of Approval | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>Cost<br>(Rs. crore) | Original<br>/<br>Revised | Antici<br>pated | Delay w.r.t.<br>Original<br>(in months) | Milestones<br>Achieved/<br>Total |
| 1     | 2                                                                                | 3                | 4                                        | 5                                  | 6                                                | 7                        | 8               | 9                                       | 10                               |
| 15    | New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal | 04/1983          | 36.80<br>274.41                          | 703.17                             | 250.35                                           | -<br>-                   | 03/2015         | -                                       | 0/0                              |
| 16    | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam       | 09/2006          | 200.00<br>200.00                         | 385.20                             | 139.95                                           | -<br>-                   | 03/2015         | -                                       | 0/0                              |
| 17    | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                           | 04/2008          | 282.92<br>282.92                         | 359.86                             | 1.22                                             | -<br>-                   | 03/2015         | -                                       | 0/0                              |
| 18    | New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal                        | 04/2011          | 209.77<br>-                              | 209.77                             | 20.93                                            | -<br>-                   | 03/2015         | -                                       | 0/0                              |
| 19    | New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal    | 04/2012          | 283.55<br>-                              | 283.55                             | 0.40                                             | -<br>-                   | 03/2015         | -                                       | 0/0                              |
| 20    | Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam                         | 04/2011          | 312.12<br>-                              | 312.12                             | 29.93                                            | -<br>-                   | 03/2015         | -                                       | 0/0                              |
| 21    | Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand               | 04/2012          | 258.20<br>-                              | 258.20                             | -                                                | -<br>-                   | 03/2016         | -                                       | 0/0                              |
| 22    | Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra           | 04/2012          | 714.10<br>-                              | 714.10                             | 2.42                                             | -<br>12/2017             | 12/2017         | 0(R3)                                   | 0/0                              |
|       | Total                                                                            |                  | 5,459.43<br>-                            | 11,320.35                          | 4,760.11                                         |                          |                 |                                         | 0/1                              |
|       |                                                                                  |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
|       | <u>Road Transport And Highways</u>                                               |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
| 23    | DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka                                     | 12/2010          | 453.00<br>-                              | 453.00                             | 713.90                                           | -<br>-                   | 09/2013         | -                                       | 1/1                              |
| 24    | Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka    | 09/2010          | 946.00<br>-                              | 946.00                             | 1,790.00                                         | -<br>-                   | 10/2013         | -                                       | 3/3                              |
| 25    | BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka                                | 12/2010          | 480.00<br>-                              | 480.00                             | 563.30                                           | -<br>-                   | 10/2013         | -                                       | 2/2                              |
| 26    | CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka                             | 03/2011          | 839.00<br>-                              | 839.00                             | 665.60                                           | -<br>-                   | 12/2013         | -                                       | 0/1                              |
| 27    | KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka                        | 09/2010          | 671.00<br>-                              | 671.00                             | 929.60                                           | -<br>-                   | 06/2014         | -                                       | 2/3                              |
|       | Total                                                                            |                  | 3,389.00<br>-                            | 3,389.00                           | 4,662.40                                         |                          |                 |                                         | 8/10                             |
|       |                                                                                  |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
|       | Grand Total                                                                      |                  | 20,736.58                                | 27,279.28                          | 11,013.76                                        |                          |                 |                                         | 74/141                           |



## List of projects without Original Date of Commissioning

| (Aug,2013) |                                                                                              |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
|------------|----------------------------------------------------------------------------------------------|------------------|------------------------------------------|------------------------------------|--------------------------------------------------|--------------------------|-----------------|-----------------------------------------|----------------------------------|
|            |                                                                                              |                  |                                          |                                    |                                                  | Date of Commissioning    |                 |                                         |                                  |
| Sl.No      | Project                                                                                      | Date of Approval | Original/<br>Revised Cost<br>(Rs. crore) | Anticipated<br>Cost<br>(Rs. crore) | Cumulative<br>Expenditure<br>Cost<br>(Rs. crore) | Original<br>/<br>Revised | Antici<br>pated | Delay w.r.t.<br>Original<br>(in months) | Milestones<br>Achieved/<br>Total |
| 1          | 2                                                                                            | 3                | 4                                        | 5                                  | 6                                                | 7                        | 8               | 9                                       | 10                               |
|            | <u>Coal</u>                                                                                  |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
| 1          | RFR OF MANUGURU OC PROJECT -<br>[N06000102]SCCL,Andhra Pradesh                               | 11/2012          | 430.14<br>-                              | 430.14                             | 58.87                                            | -<br>-                   | 03/2016         | -                                       | 4/48                             |
|            | Total                                                                                        |                  | 430.14<br>-                              | 430.14                             | 58.87                                            |                          |                 |                                         | 4/48                             |
|            | <u>Petroleum</u>                                                                             |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
| 2          | RESITEMENT OF MARKETING INSTALATION<br>AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh       | 01/2009          | 756.00<br>898.00                         | 898.00                             | 913.72                                           | -<br>-                   | 08/2013         | -                                       | 52/53                            |
| 3          | Surat Paradip Pipeline Project -<br>[N16000163]GAIL,Multi State                              | 10/2012          | 10,281.00<br>-                           | 10,281.00                          | 0.04                                             | -<br>-                   | 04/2015         | -                                       | 0/0                              |
|            | Total                                                                                        |                  | 11,037.00<br>-                           | 11,179.00                          | 913.76                                           |                          |                 |                                         | 52/53                            |
|            | <u>Power</u>                                                                                 |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
| 4          | TRIPURA GAS BASED POWER PROJECT -<br>[N18000071]NEEPCO,Tripura                               | 07/2009          | 421.01<br>623.44                         | 960.79                             | 618.62                                           | -<br>-                   | 05/2014         | -                                       | 10/29                            |
|            | Total                                                                                        |                  | 421.01<br>-                              | 960.79                             | 618.62                                           |                          |                 |                                         | 10/29                            |
|            | <u>Railways</u>                                                                              |                  |                                          |                                    |                                                  |                          |                 |                                         |                                  |
| 5          | CHHINDWARA - NAGPUR (GC)(SECR) -<br>[220100324]SECR,Madhya pradesh                           | 04/2005          | 383.79<br>-                              | 585.93                             | 194.91                                           | -<br>-                   | 12/2013         | -                                       | 0/0                              |
| 6          | CONSTRUCTION OF NEW LINE FROM<br>HARMATI-ITANAGAR/NAR -<br>[N22000083]NEFR,Arunachal Pradesh | 09/1996          | 156.00<br>156.00                         | 406.40                             | 350.63                                           | -<br>-                   | 12/2013         | -                                       | 0/0                              |
| 7          | PANVEL PEN DOUBLING -<br>[N22000255]CR,Multi State                                           | 04/2006          | 191.00<br>-                              | 191.00                             | 195.08                                           | -<br>-                   | 12/2013         | -                                       | 0/0                              |
| 8          | DAUSA-GANGAPUR CITY(NL),NWR -<br>[220100184]NWR,Rajasthan                                    | 02/1997          | 151.84<br>410.08                         | 410.08                             | 238.17                                           | -<br>-                   | 03/2014         | -                                       | 0/0                              |
| 9          | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC<br>(NER) - [220100256]NER,Multi State                      | 04/1999          | 323.40<br>323.40                         | 744.71                             | 513.75                                           | -<br>-                   | 03/2014         | -                                       | 0/1                              |
| 10         | KHURDA ROAD-BOLANGIR(NL)ECOR -<br>[220100284]ECOR,Odisha                                     | 04/1994          | 355.38<br>470.21                         | 1,995.25                           | 260.49                                           | -<br>-                   | 03/2014         | -                                       | 0/0                              |
| 11         | RANGIA-MURKONGSELEK, (GC) ALONG<br>WITH LINKED FINGER -<br>[220100315]NEFR,Multi State       | 01/2004          | 915.70<br>915.70                         | 3,019.17                           | 2,174.43                                         | -<br>-                   | 03/2014         | -                                       | 0/0                              |
| 12         | HATHUA-BHATNI (N L) (NER) -<br>[220100319]NER,Multi State                                    | 04/2005          | 230.03<br>230.03                         | 230.03                             | 149.24                                           | -<br>-                   | 03/2014         | -                                       | 0/0                              |
| 13         | New BG line from Dudhnoi-Mendipatar -<br>[N22000192]NEFR,Multi State                         | 04/1999          | 175.43<br>-                              | 247.75                             | 145.43                                           | -<br>-                   | 03/2014         | -                                       | 0/0                              |
| 14         | Viramgam-Surendranagar (DL) -<br>[N22000146]WR,Gujarat                                       | 04/2010          | 279.40<br>-                              | 264.06                             | 92.78                                            | -<br>-                   | 04/2014         | -                                       | 0/0                              |

(Aug,2013)

|       |                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |                                   |                            |
|-------|----------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------|
| Sl.No | Project                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Milestones Achieved/ Total |
| 1     | 2                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           | 9                                 | 10                         |
| 15    | New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal | 04/1983          | 36.80<br>274.41                    | 703.17                       | 250.35                                  | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 16    | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam       | 09/2006          | 200.00<br>200.00                   | 385.20                       | 139.95                                  | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 17    | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                           | 04/2008          | 282.92<br>282.92                   | 359.86                       | 1.22                                    | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 18    | New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal                        | 04/2011          | 209.77<br>-                        | 209.77                       | 20.93                                   | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 19    | New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal    | 04/2012          | 283.55<br>-                        | 283.55                       | 0.40                                    | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 20    | Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam                         | 04/2011          | 312.12<br>-                        | 312.12                       | 29.93                                   | -<br>-                | 03/2015     | -                                 | 0/0                        |
| 21    | Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand               | 04/2012          | 258.20<br>-                        | 258.20                       | -                                       | -<br>-                | 03/2016     | -                                 | 0/0                        |
| 22    | Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra           | 04/2012          | 714.10<br>-                        | 714.10                       | 2.42                                    | -<br>12/2017          | 12/2017     | 0(R3)                             | 0/0                        |
|       | Total                                                                            |                  | 5,459.43<br>-                      | 11,320.35                    | 4,760.11                                |                       |             |                                   | 0/1                        |
|       |                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                            |
|       | <u>Road Transport And Highways</u>                                               |                  |                                    |                              |                                         |                       |             |                                   |                            |
| 23    | DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka                                     | 12/2010          | 453.00<br>-                        | 453.00                       | 713.90                                  | -<br>-                | 09/2013     | -                                 | 1/1                        |
| 24    | Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka    | 09/2010          | 946.00<br>-                        | 946.00                       | 1,790.00                                | -<br>-                | 10/2013     | -                                 | 3/3                        |
| 25    | BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka                                | 12/2010          | 480.00<br>-                        | 480.00                       | 563.30                                  | -<br>-                | 10/2013     | -                                 | 2/2                        |
| 26    | CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka                             | 03/2011          | 839.00<br>-                        | 839.00                       | 665.60                                  | -<br>-                | 12/2013     | -                                 | 0/1                        |
| 27    | KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka                        | 09/2010          | 671.00<br>-                        | 671.00                       | 929.60                                  | -<br>-                | 06/2014     | -                                 | 2/3                        |
|       | Total                                                                            |                  | 3,389.00<br>-                      | 3,389.00                     | 4,662.40                                |                       |             |                                   | 8/10                       |
|       |                                                                                  |                  |                                    |                              |                                         |                       |             |                                   |                            |
|       | Grand Total                                                                      |                  | 20,736.58                          | 27,279.28                    | 11,013.76                               |                       |             |                                   | 74/141                     |

## List of on schedule Projects w.r.t. Original Schedule

| (Aug,2013) |                                                                                     |                  |                                    |                              |                                         |                       |             |
|------------|-------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
|            |                                                                                     |                  |                                    |                              |                                         | Date of Commissioning |             |
| S.No       | Project                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1          | 2                                                                                   | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
|            | <u>Civil Aviation</u>                                                               |                  |                                    |                              |                                         |                       |             |
| 1          | DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II<br>- [N04000070]    | 2/2011           | 452.00<br>-                        | 452.00                       | 127.08                                  | 03/2015<br>-          | 03/2015     |
| 2          | SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS<br>- [N04000071]         | 10/2012          | 217.60<br>-                        | 217.60                       | 0.02                                    | 03/2015<br>-          | 03/2015     |
| 3          | ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS<br>- [N04000072] | 2/2010           | 344.28<br>-                        | 344.28                       | -                                       | 03/2014<br>-          | 03/2014     |
|            | Total                                                                               |                  | 1,013.88<br>-                      | 1,013.88                     | 127.10                                  |                       |             |
|            | <u>Coal</u>                                                                         |                  |                                    |                              |                                         |                       |             |
| 4          | BLOCK-B OCP NCL (3.5 MTY)<br>- [N06000009]                                          | 6/2011           | 746.04<br>-                        | 535.10                       | 161.09                                  | 03/2015<br>-          | 03/2015     |
| 5          | BHUBANESWARI OCP, MCL (20.0 Mty)<br>- [N06000034]                                   | 12/2007          | 490.00<br>-                        | 490.10                       | 150.13                                  | 03/2017<br>-          | 03/2017     |
| 6          | TALABIRA OCP<br>- [N06000043]                                                       | 3/2008           | 447.72<br>-                        | 447.72                       | 44.33                                   | 03/2016<br>-          | 03/2016     |
| 7          | Batura OCP (2.0 MTY)<br>- [N06000049]                                               | 9/2008           | 203.82<br>-                        | 203.82                       | -                                       | 03/2015<br>-          | 03/2015     |
| 8          | AMLAI OC EXPANSION SECTOR B (1.50 MTY)<br>- [N06000082]                             | 11/2009          | 150.59<br>-                        | 198.59                       | 89.13                                   | 03/2016<br>-          | 03/2016     |
| 9          | KARMA OCP (1.0MTY)<br>- [N06000088]                                                 | 6/2009           | 162.46<br>-                        | 162.46                       | 40.64                                   | 03/2014<br>-          | 03/2014     |
| 10         | KALYANIKHANI OPENCAST PROJECT<br>- [N06000101]                                      | 7/2012           | 417.33<br>-                        | 417.33                       | 0.06                                    | 07/2016<br>-          | 07/2016     |
| 11         | RAMAGUNDUM OC -III EXTENSION (PHASE -II) PROJECT<br>- [N06000100]                   | 6/2012           | 365.01<br>-                        | 365.01                       | -                                       | 06/2015<br>-          | 06/2015     |
| 12         | BAROUD OC EXPANSION (RCE)- 3MTY<br>- [N06000099]                                    | 4/2012           | 258.56<br>-                        | 258.56                       | 52.44                                   | 03/2016<br>-          | 03/2016     |
| 13         | Moonidih XV Seam UG<br>- [N06000098]                                                | 8/2011           | 1,230.27<br>-                      | 1,230.27                     | -                                       | 04/2015<br>-          | 04/2015     |
| 14         | Muraidih UG Turn-key Project<br>- [N06000096]                                       | 2/2011           | 339.88<br>-                        | 339.88                       | -                                       | 04/2014<br>-          | 04/2014     |
| 15         | JALAGAM VENGALA RAO OCP-II<br>- [N06000094]                                         | 7/2011           | 447.06<br>-                        | 447.06                       | 14.02                                   | 03/2015<br>-          | 03/2015     |
| 16         | RCE OF INDARAM OCP(1.20 MTPA)<br>- [N06000093]                                      | 7/2011           | 162.76<br>-                        | 162.76                       | 3.25                                    | 03/2015<br>-          | 03/2015     |
| 17         | KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)<br>- [N06000091]  | 6/2011           | 1,131.28<br>-                      | 1,131.28                     | 4.88                                    | 03/2018<br>-          | 03/2018     |
| 18         | Kistaram OCP<br>- [N06000089]                                                       | 11/2010          | 242.29<br>-                        | 242.29                       | -                                       | 03/2015<br>-          | 03/2015     |
| 19         | AMRAPALI OC(12MTY)<br>- [N06000103]                                                 | 2/2012           | 858.11<br>-                        | 858.11                       | 49.33                                   | 03/2020<br>-          | 03/2020     |
| 20         | Rajrappa RCE OCP ( 3.0 MTY)<br>- [N06000087]                                        | 12/2009          | 510.85<br>-                        | 510.85                       | 265.46                                  | 03/2016<br>-          | 03/2016     |

(Aug,2013)

|      |                                                                       |                  |                                    |                              |                                         | Date of Commissioning |             |
|------|-----------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| S.No | Project                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                     | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 21   | RKP OCP PHASE-I<br>- [N06000079]                                      | 3/2010           | 209.78<br>-                        | 209.78                       | 50.71                                   | 03/2015<br>-          | 03/2015     |
| 22   | PELMA OCP(10.00MTY)<br>- [N06000045]                                  | 7/2008           | 448.32<br>-                        | 448.32                       | -                                       | 03/2015<br>-          | 03/2015     |
| 23   | GOPAL PRASAD OCP (15MTY)<br>- [N06000042]                             | 2/2008           | 395.87<br>-                        | 395.87                       | 72.34                                   | 03/2015<br>-          | 03/2015     |
| 24   | BINA EXTN. PROJ(6.0 Mtpa)<br>- [N06000019]                            | 11/2006          | 168.97<br>-                        | 168.97                       | 45.02                                   | 03/2014<br>-          | 03/2014     |
| 25   | AMLOHRI EPR (NCL) (6 MTY , INCR.)<br>- [N06000010]                    | 12/2009          | 1,352.04<br>-                      | 1,143.54                     | 470.53                                  | 03/2016<br>03/2016    | 03/2016     |
|      | Total                                                                 |                  | 10,739.01<br>-                     | 10,367.67                    | 1,513.36                                |                       |             |
|      |                                                                       |                  |                                    |                              |                                         |                       |             |
|      | <u>Petroleum</u>                                                      |                  |                                    |                              |                                         |                       |             |
| 26   | Wax Project<br>- [N16000101]                                          | 6/2010           | 576.60<br>-                        | 576.60                       | 289.40                                  | 12/2013<br>-          | 12/2013     |
| 27   | Purchase of 2 Nos. of 2000 HP Drilling Rig<br>- [N16000165]           | 4/2010           | 270.00<br>-                        | 270.00                       | -                                       | 12/2014<br>-          | 12/2014     |
| 28   | Reconstruction of BPA and BPB Platforms<br>- [N16000161]              | 3/2013           | 1,138.50<br>-                      | 1,138.50                     | -                                       | 04/2015<br>-          | 04/2015     |
| 29   | Integrated Development of Bassein Field<br>- [N16000160]              | 12/2012          | 3,513.07<br>-                      | 3,513.07                     | -                                       | 02/2016<br>-          | 02/2016     |
| 30   | Pipeline Replacement Project, Ahmedabad<br>- [N16000159]              | 9/2011           | 202.25<br>-                        | 160.16                       | -                                       | 07/2016<br>-          | 07/2016     |
| 31   | Mounded Bullet Project at CPCL<br>- [N16000154]                       | 12/2012          | 279.00<br>-                        | 279.00                       | 279.00                                  | 12/2014<br>-          | 12/2014     |
| 32   | PARADIP HALDIA DURGAPUR LPG PIPELINE<br>- [N16000148]                 | 2/2011           | 913.00<br>-                        | 913.00                       | 35.31                                   | 07/2015<br>-          | 07/2015     |
| 33   | DABHOL BANGALORE PIPELINE PROJECT PHASE-II<br>- [N16000147]           | 6/2009           | 486.00<br>-                        | 486.00                       | 57.56                                   | 09/2013<br>-          | 09/2013     |
| 34   | MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)<br>- [N16000146] | 11/2012          | 666.00<br>-                        | 701.00                       | 16.56                                   | 11/2015<br>-          | 11/2015     |
| 35   | REWARI KANPUR PIPELINE PROJECT<br>- [N16000145]                       | 2/2012           | 1,210.64<br>-                      | 1,210.64                     | 169.14                                  | 11/2015<br>-          | 11/2015     |
| 36   | Replacement of CDU/VDU at Mumbai Refinery<br>- [N16000142]            | 1/1999           | 1,419.00<br>-                      | 1,419.00                     | 134.21                                  | 12/2014<br>-          | 12/2014     |
| 37   | BUTENE-1 PROJECT AT PANIPAT<br>- [N16000139]                          | 2/2012           | 190.00<br>-                        | 190.00                       | 67.27                                   | 03/2014<br>-          | 03/2014     |
| 38   | Pipeline Replacement Project-3<br>- [N16000137]                       | 4/2012           | 2,547.26<br>-                      | 1,417.00                     | 485.99                                  | 05/2014<br>-          | 05/2014     |
| 39   | Development of Western Periphery of MH South Field<br>- [N16000136]   | 4/2012           | 600.17<br>-                        | 600.17                       | 80.56                                   | 12/2014<br>-          | 12/2014     |
| 40   | Construction of three ETPs, Mehsana<br>- [N16000135]                  | 3/2012           | 260.74<br>-                        | 260.74                       | 0.52                                    | 11/2014<br>-          | 11/2014     |
| 41   | Construction of one ETP at GGS-NADA, Ankleshwar<br>- [N16000134]      | 10/2011          | 200.69<br>-                        | 200.69                       | 3.03                                    | 07/2014<br>-          | 07/2014     |
| 42   | Development of C-26 Cluster Fields<br>- [N16000133]                   | 3/2012           | 2,592.17<br>-                      | 2,592.17                     | 11.90                                   | 05/2014<br>-          | 05/2014     |
| 43   | PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA<br>- [N16000112]        | 8/2010           | 8,140.00<br>-                      | 8,140.00                     | 5,177.12                                | 02/2014<br>-          | 02/2014     |

(Aug,2013)

|      |                                                                                                                      |                  |                                    |                              |                                         | Date of Commissioning |             |
|------|----------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| S.No | Project                                                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                                                                    | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 44   | Heera and South Heera Redevelopment Ph-II<br>- [N16000132]                                                           | 3/2012           | 5,608.40<br>-                      | 5,608.40                     | 1,178.55                                | 05/2015<br>-          | 05/2015     |
| 45   | Integrated Development of B-127 fields<br>- [N16000131]                                                              | 12/2011          | 2,059.63<br>-                      | 2,665.65                     | 246.35                                  | 03/2015<br>-          | 03/2015     |
|      | Total                                                                                                                |                  | 32,873.12<br>-                     | 32,341.79                    | 8,232.47                                |                       |             |
|      |                                                                                                                      |                  |                                    |                              |                                         |                       |             |
|      | <u>Power</u>                                                                                                         |                  |                                    |                              |                                         |                       |             |
| 46   | Transm System for development of Pooling stn. in NR part of West Bengal And Transfer of power from B - [N18000077]   | 4/2010           | 4,404.57<br>-                      | 4,404.57                     | 388.61                                  | 01/2015<br>-          | 01/2015     |
| 47   | ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH<br>- [N18000101]  | 5/2011           | 1,961.87<br>-                      | 1,961.87                     | 1,101.84                                | 05/2014<br>-          | 05/2014     |
| 48   | INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]   | 8/2011           | 1,391.97<br>-                      | 1,391.97                     | 1,041.70                                | 12/2013<br>-          | 12/2013     |
| 49   | COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL)<br>- [N18000111]               | 8/2011           | 1,637.34<br>-                      | 1,637.34                     | 882.14                                  | 08/2014<br>-          | 08/2014     |
| 50   | TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2<br>[N18000113]                        | 12/2011          | 2,422.66<br>-                      | 2,422.66                     | 470.84                                  | 08/2014<br>-          | 08/2014     |
| 51   | Transmission System associated with Mauda Stage-II<br>- [N18000153]                                                  | 9/2013           | 1,575.30<br>-                      | 1,575.30                     | -                                       | 05/2016<br>-          | 05/2016     |
| 52   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV<br>- [N18000152]                                                     | 9/2013           | 680.69<br>-                        | 680.69                       | -                                       | 03/2016<br>-          | 03/2016     |
| 53   | Gadarwara Super Thermal Power Project Stage-I<br>- [N18000151]                                                       | 2/2013           | 11,638.55<br>-                     | 11,638.55                    | 681.00                                  | 09/2017<br>-          | 09/2017     |
| 54   | COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION<br>- [N18000145] | 6/2012           | 1,909.24<br>-                      | 1,909.24                     | 174.43                                  | 06/2015<br>-          | 06/2015     |
| 55   | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION<br>- [N18000123]                                | 3/2012           | 198.63<br>-                        | 198.63                       | -                                       | 09/2014<br>-          | 09/2014     |
| 56   | TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B<br>[N18000122]                                         | 2/2012           | 1,927.16<br>-                      | 1,927.16                     | 401.94                                  | 10/2014<br>-          | 10/2014     |
| 57   | TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1<br>- [N18000121]                                         | 2/2012           | 324.33<br>-                        | 324.33                       | 40.34                                   | 08/2014<br>-          | 08/2014     |
| 58   | SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH<br>[N18000120]                    | 2/2012           | 1,310.85<br>-                      | 1,310.85                     | 427.43                                  | 02/2015<br>-          | 02/2015     |
| 59   | TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD<br>[N18000118]                        | 1/2012           | 259.28<br>-                        | 259.28                       | 108.70                                  | 01/2014<br>-          | 01/2014     |
| 60   | SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH<br>[N18000117]                       | 1/2012           | 1,422.85<br>-                      | 1,422.85                     | 393.32                                  | 01/2015<br>-          | 01/2015     |
| 61   | SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH<br>- [N18000116]                       | 12/2011          | 1,746.65<br>-                      | 1,746.65                     | 157.92                                  | 08/2014<br>-          | 08/2014     |
| 62   | SYTEM STRENGTHENING OF SOUTHERN REGION - XIV<br>[N18000115]                                                          | 12/2011          | 297.33<br>-                        | 297.33                       | 132.02                                  | 08/2014<br>-          | 08/2014     |

(Aug,2013)

|      |                                                                                                                   |                  |                                    |                              |                                         | Date of Commissioning |             |
|------|-------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| S.No | Project                                                                                                           | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                                                                 | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 63   | TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114                                  | 12/2011          | 552.44 -                           | 552.44                       | 323.50                                  | 02/2014 -             | 02/2014     |
| 64   | COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144    | 3/2013           | 2,514.88 -                         | 2,514.88                     | -                                       | 12/2015 -             | 12/2015     |
| 65   | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143    | 3/2013           | 514.20 -                           | 514.20                       | -                                       | 06/2015 -             | 06/2015     |
| 66   | Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142                                                    | 7/2012           | 1,527.00 -                         | 1,527.00                     | 113.03                                  | 08/2017 -             | 08/2017     |
| 67   | LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140                                                | 11/2012          | 11,846.00 -                        | 11,846.00                    | 1,096.00                                | 05/2017 -             | 05/2017     |
| 68   | COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139       | 1/2013           | 182.80 -                           | 182.80                       | 3.60                                    | 10/2014 -             | 10/2014     |
| 69   | AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138                                               | 12/2012          | 156.04 -                           | 156.04                       | -                                       | 10/2014 -             | 10/2014     |
| 70   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136                                                     | 9/2012           | 803.34 -                           | 803.34                       | 98.44                                   | 03/2015 -             | 03/2015     |
| 71   | VINDHYACHAL STPP STAGE-V - [N18000134                                                                             | 12/2011          | 3,180.40 -                         | 3,180.40                     | 438.00                                  | 08/2015 -             | 08/2015     |
| 72   | SOLAPUR STPP - [N18000133                                                                                         | 3/2012           | 9,395.18 -                         | 9,395.18                     | 1,608.00                                | 11/2016 -             | 11/2016     |
| 73   | MOUDA STPP STAGE 2 - [N18000132                                                                                   | 3/2012           | 7,921.47 -                         | 7,921.47                     | 1,139.00                                | 09/2016 -             | 09/2016     |
| 74   | KUDGI STPP STAGE 1 - [N18000131                                                                                   | 12/2011          | 15,166.19 -                        | 15,166.19                    | 1,775.00                                | 12/2016 -             | 12/2016     |
| 75   | SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130                                                   | 6/2012           | 1,263.26 -                         | 1,263.26                     | 243.28                                  | 11/2014 -             | 11/2014     |
| 76   | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128                                                     | 11/2011          | 723.63 -                           | 723.63                       | 188.04                                  | 11/2014 -             | 11/2014     |
| 77   | IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127                                                         | 12/2011          | 901.77 -                           | 901.77                       | 345.53                                  | 08/2014 -             | 08/2014     |
| 78   | COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126               | 3/2012           | 206.44 -                           | 206.44                       | 40.67                                   | 06/2014 -             | 06/2014     |
| 79   | WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125                                           | 3/2012           | 9,569.76 -                         | 9,569.76                     | 829.02                                  | 06/2015 -             | 06/2015     |
| 80   | SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124                          | 3/2012           | 213.78 -                           | 213.78                       | -                                       | 03/2014 -             | 03/2014     |
| 81   | TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112  | 11/2011          | 2,127.51 -                         | 2,127.51                     | 1,081.67                                | 07/2014 -             | 07/2014     |
| 82   | SYTEM STRENGTHENING XIII OF SR GRID - [N18000109                                                                  | 10/2011          | 487.49 -                           | 487.49                       | 181.51                                  | 06/2014 -             | 06/2014     |
| 83   | Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103 | 9/2011           | 1,940.13 -                         | 1,940.13                     | 1,000.05                                | 09/2014 -             | 09/2014     |
|      | Total                                                                                                             |                  | 106,302.98 -                       | 106,302.98                   | 16,906.57                               |                       |             |
|      |                                                                                                                   |                  |                                    |                              |                                         |                       |             |
|      | <u>Railways</u>                                                                                                   |                  |                                    |                              |                                         |                       |             |

(Aug,2013)

|      |                                                                                                              |                  |                                    |                              |                                         | Date of Commissioning |             |
|------|--------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| S.No | Project                                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                                                            | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 84   | SUKINDA ROAD - ANGUL (NL)(ECOR)<br>- [N220100325                                                             | 4/1998           | 183.23<br>-                        | 818.29                       | 103.44                                  | 02/2015<br>-          | 02/2015     |
| 85   | New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110    | 4/2010           | 3,951.98<br>-                      | 3,951.98                     | -                                       | 03/2016<br>-          | 03/2016     |
| 86   | Himmatnagar - Udaipur Gauge Conversion (NWR)<br>- [N22000112                                                 | 4/2008           | 829.74<br>-                        | 829.74                       | 30.04                                   | 03/2015<br>-          | 03/2015     |
| 87   | Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR)<br>- [N22000114                               | 4/2008           | 516.23<br>-                        | 516.23                       | 401.08                                  | 03/2014<br>-          | 03/2014     |
| 88   | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE<br>- [N22000135                                     | 3/2013           | 4,874.58<br>-                      | 4,874.58                     | -                                       | 03/2016<br>-          | 03/2016     |
| 89   | Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC<br>- [N22000245                                      | 4/2010           | 423.66<br>-                        | 423.66                       | 132.84                                  | 03/2017<br>-          | 03/2017     |
| 90   | Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura Sharif NL<br>- [N22000244                         | 4/2009           | 257.42<br>-                        | 257.42                       | 32.87                                   | 03/2014<br>-          | 03/2014     |
| 91   | Princepghat-Majerhat Doubling of Circular Railway<br>- [N22000239                                            | 4/2011           | 299.60<br>-                        | 299.60                       | 1.09                                    | 03/2017<br>-          | 03/2017     |
| 92   | Plassey-Jiaganj Doubling<br>- [N22000220                                                                     | 4/2011           | 248.07<br>-                        | 248.07                       | 8.91                                    | 03/2015<br>-          | 03/2015     |
| 93   | Dangoaposi-Rajkharwan 3rd line Doubling<br>- [N22000164                                                      | 4/2010           | 309.44<br>-                        | 388.67                       | 42.01                                   | 12/2015<br>-          | 12/2015     |
| 94   | Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158     | 4/2010           | 622.41<br>-                        | 2,030.50                     | 1.22                                    | 02/2019<br>-          | 02/2019     |
| 95   | Gwalior-Seopurkala with extension to Kota (GC)<br>- [N22000148                                               | 4/2011           | 1,176.09<br>-                      | 3,845.60                     | 1.52                                    | 02/2020<br>-          | 02/2020     |
| 96   | Udhna-Jalgaon with electrification(doubling) (WR)<br>- [N22000122                                            | 4/2008           | 1,389.62<br>-                      | 1,389.62                     | 655.55                                  | 03/2014<br>-          | 03/2014     |
| 97   | Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR)<br>- [N22000113                            | 4/2008           | 653.19<br>-                        | 653.47                       | 246.16                                  | 03/2014<br>-          | 03/2014     |
| 98   | New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111                | 4/2010           | 2,619.02<br>-                      | 2,913.51                     | 324.72                                  | 03/2016<br>-          | 03/2016     |
| 99   | New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109 | 4/2010           | 2,069.60<br>-                      | 2,298.42                     | 58.94                                   | 03/2014<br>-          | 03/2014     |
|      | Total                                                                                                        |                  | 20,423.88<br>-                     | 25,739.36                    | 2,040.39                                |                       |             |
|      |                                                                                                              |                  |                                    |                              |                                         |                       |             |
|      | <b>Road Transport And Highways</b>                                                                           |                  |                                    |                              |                                         |                       |             |
| 100  | New 4 Lane elevated road from chennai airport-maduravoyal NH no.4<br>- [N24000139                            | 9/2010           | 1,655.00<br>-                      | 1,655.00                     | 393.70                                  | 09/2013<br>-          | 09/2013     |
| 101  | PANIPAT-ROHTAK<br>- [N24000151                                                                               | 4/2011           | 807.00<br>-                        | 807.00                       | 1,318.00                                | 10/2014<br>-          | 10/2014     |
| 102  | SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00<br>- [N24000171                                  | 6/2011           | 535.00<br>-                        | 535.00                       | -                                       | 12/2013<br>-          | 12/2013     |
| 103  | 2 Laning of Muzaffarpur - Sonbarsa<br>- [N24000174                                                           | 5/2011           | 511.54<br>-                        | 511.54                       | 65.78                                   | 11/2013<br>-          | 11/2013     |
| 104  | JORBAT - BARAPANI<br>- [N24000180                                                                            | 1/2011           | 536.00<br>-                        | 536.00                       | 513.80                                  | 01/2014<br>-          | 01/2014     |
| 105  | 2 LANING WITH PS KANPUR KABRAI<br>- [N24000221                                                               | 1/2013           | 373.47<br>-                        | 373.47                       | 38.90                                   | 07/2014<br>-          | 07/2014     |
| 106  | 2 LANING WITH PS AGRA ALIGARH<br>- [N24000220                                                                | 10/2012          | 250.50<br>-                        | 250.50                       | 131.40                                  | 10/2014<br>-          | 10/2014     |

(Aug,2013)

|      |                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
|------|----------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| S.No | Project                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 107  | ETAWAH CHAKERI<br>- [N24000219]                                                  | 3/2013           | 1,573.00<br>-                      | 1,573.00                     | 15.05                                   | 09/2015<br>-          | 09/2015     |
| 108  | FOUR LANING OF ORISSA CHATTISHGARH BORDER<br>- [N24000218]                       | 2/2013           | 1,232.00<br>-                      | 1,232.00                     | 150.70                                  | 08/2015<br>-          | 08/2015     |
| 109  | PANVEL-INDAPUR<br>- [N24000216]                                                  | 12/2011          | 942.69<br>-                        | 942.69                       | 196.20                                  | 06/2014<br>-          | 06/2014     |
| 110  | RANCHI-RARGA-JAMSETHPUR<br>- [N24000215]                                         | 12/2012          | 1,479.00<br>-                      | 1,479.00                     | 190.40                                  | 06/2015<br>-          | 06/2015     |
| 111  | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)<br>- [N24000213]     | 4/2012           | 624.00<br>-                        | 624.00                       | 296.40                                  | 04/2014<br>-          | 04/2014     |
| 112  | 2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI<br>- [N24000211]             | 7/2012           | 356.40<br>-                        | 356.40                       | -                                       | 07/2014<br>-          | 07/2014     |
| 113  | 4-laning of Barhi-Hazaribagh<br>- [N24000191]                                    | 2/2012           | 398.00<br>-                        | 398.00                       | 437.90                                  | 02/2014<br>-          | 02/2014     |
| 114  | WALAJAPET POONAMALEE KM 106.8 TO KM 13.8<br>- [N24000228]                        | 6/2013           | 1,287.95<br>-                      | 1,287.95                     | -                                       | 11/2015<br>-          | 11/2015     |
| 115  | REENGUS SIKAR<br>- [N24000227]                                                   | 3/2012           | 333.51<br>-                        | 333.51                       | 227.90                                  | 09/2014<br>-          | 09/2014     |
| 116  | 2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC<br>- [N24000226]    | 10/2011          | 1,565.00<br>-                      | 1,565.00                     | 648.30                                  | 10/2014<br>-          | 10/2014     |
| 117  | 4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6<br>- [N24000225]     | 3/2012           | 828.00<br>-                        | 828.00                       | 470.50                                  | 09/2014<br>-          | 09/2014     |
| 118  | DELHI AGRA APPROVED LENGTH 180.0 KM<br>- [N24000224]                             | 10/2012          | 1,928.22<br>-                      | 1,928.22                     | 302.60                                  | 04/2015<br>-          | 04/2015     |
| 119  | SAMAIKHIALI GANDHIDHAM<br>- [N24000223]                                          | 9/2010           | 805.39<br>-                        | 805.39                       | 543.70                                  | 12/2013<br>-          | 12/2013     |
| 120  | AHMEDABAD TO VADODARA SECTION<br>- [N24000222]                                   | 1/2013           | 2,125.24<br>-                      | 2,125.24                     | 30.80                                   | 12/2015<br>-          | 12/2015     |
| 121  | 2laning with PS Gopalganj-Chappra<br>- [N24000190]                               | 12/2011          | 325.00<br>-                        | 325.00                       | 161.20                                  | 05/2014<br>-          | 05/2014     |
| 122  | SRINAGAR TO BANIHAL<br>- [N24000189]                                             | 6/2011           | 1,100.70<br>-                      | 1,100.70                     | -                                       | 06/2014<br>-          | 06/2014     |
| 123  | 2 LANNING OF MUZAFFARPUR - SONBARSA<br>- [N24000188]                             | 5/2011           | 511.54<br>-                        | 511.54                       | 631.80                                  | 11/2013<br>-          | 11/2013     |
| 124  | 2-LANNING WITH PS MOTIHARI-RAXAUL<br>- [N24000186]                               | 10/2011          | 375.09<br>-                        | 375.09                       | 174.40                                  | 04/2014<br>-          | 04/2014     |
| 125  | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95<br>- [N24000185]                          | 9/2011           | 574.00<br>-                        | 574.00                       | 646.10                                  | 03/2014<br>-          | 03/2014     |
| 126  | SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547<br>- [N24000183] | 11/2011          | 1,535.00<br>-                      | 1,535.00                     | 1,182.00                                | 05/2014<br>-          | 05/2014     |
| 127  | VARANASI-AURANGABAD KM.786 TO KM.978.40<br>- [N24000182]                         | 9/2011           | 2,848.00<br>-                      | 2,848.00                     | 915.90                                  | 03/2014<br>-          | 03/2014     |
| 128  | 2-LANNING OF SHILONG BYPASS<br>- [N24000181]                                     | 2/2011           | 226.00<br>-                        | 226.00                       | 288.80                                  | 02/2014<br>-          | 02/2014     |
| 129  | NAGPUR-WAINGANGA BRIDGE<br>- [N24000210]                                         | 4/2012           | 484.19<br>-                        | 484.19                       | 282.80                                  | 10/2014<br>-          | 10/2014     |
| 130  | KRISHNANAGAR-BERHAMPUR<br>- [N24000209]                                          | 2/2012           | 702.16<br>-                        | 702.16                       | 463.54                                  | 07/2014<br>-          | 07/2014     |
| 131  | 2-LANING WITH PS RAIBAREILI TO ALLAHABAD<br>- [N24000208]                        | 7/2012           | 291.36<br>-                        | 291.36                       | 86.37                                   | 01/2014<br>-          | 01/2014     |



(Aug,2013)

|      |                                                                                                                  |                  |                                    |                              |                                         | Date of Commissioning |             |
|------|------------------------------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|-----------------------------------------|-----------------------|-------------|
| S.No | Project                                                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure Cost (Rs. crore) | Original/ Revised     | Anticipated |
| 1    | 2                                                                                                                | 3                | 4                                  | 5                            | 6                                       | 7                     | 8           |
| 132  | 6-LANING OF DHANKUNI-KHARAGPUR SECTION<br>- [N24000206                                                           | 4/2012           | 1,396.18<br>-                      | 1,396.18                     | 1,027.00                                | 09/2014<br>-          | 09/2014     |
| 133  | six laning of Chandikhol-Jagatpur-Bhubaneswar<br>- [N24000205                                                    | 12/2011          | 1,047.00<br>-                      | 1,047.00                     | 202.40                                  | 06/2014<br>-          | 06/2014     |
| 134  | BAREILY-SITAPUR<br>- [N24000200                                                                                  | 3/2011           | 1,046.00<br>-                      | 1,046.00                     | 352.90                                  | 09/2013<br>-          | 09/2013     |
| 135  | BEAWAR-PALI-PINDWARA<br>- [N24000199                                                                             | 12/2011          | 2,388.00<br>-                      | 2,388.00                     | 1,306.00                                | 06/2014<br>-          | 06/2014     |
| 136  | SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER<br>- [N24000196                                                      | 11/2011          | 909.00<br>-                        | 909.00                       | 941.90                                  | 05/2014<br>-          | 05/2014     |
| 137  | PUNE-SHOLAPUR,Pkg-II<br>- [N24000193                                                                             | 9/2011           | 835.00<br>-                        | 835.00                       | 388.20                                  | 01/2014<br>-          | 01/2014     |
| 138  | Tirupati - Tiruthani - Chennai<br>- [N24000178                                                                   | 4/2011           | 571.00<br>-                        | 571.00                       | -                                       | 10/2013<br>-          | 10/2013     |
| 139  | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION<br>KM.0.00 TO KM.148.3 NH-46 - [N24000172                         | 9/2011           | 1,250.00<br>-                      | 1,250.00                     | 16.15                                   | 12/2013<br>-          | 12/2013     |
| 140  | ROHTAK-BAWAL<br>- [N24000169                                                                                     | 5/2011           | 650.00<br>-                        | 650.00                       | 1,106.00                                | 11/2013<br>-          | 11/2013     |
| 141  | Talegaon-amravati<br>- [N24000140                                                                                | 11/2009          | 567.00<br>-                        | 567.00                       | 1,166.00                                | 11/2013<br>-          | 11/2013     |
|      | Total                                                                                                            |                  | 39,779.13<br>-                     | 39,779.13                    | 17,311.49                               |                       |             |
|      |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|      | <u>Shipping And Ports</u>                                                                                        |                  |                                    |                              |                                         |                       |             |
| 142  | Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053 | 10/2010          | 966.46<br>-                        | 994.82                       | 363.20                                  | 02/2014<br>-          | 02/2014     |
|      | Total                                                                                                            |                  | 966.46<br>-                        | 994.82                       | 363.20                                  |                       |             |
|      |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|      | <u>Steel</u>                                                                                                     |                  |                                    |                              |                                         |                       |             |
| 143  | Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh<br>- [N12000078                                   | 7/2012           | 332.65<br>-                        | 332.65                       | 68.92                                   | 08/2014<br>-          | 08/2014     |
| 144  | Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha<br>- [N12000079                                      | 1/2012           | 254.90<br>-                        | 254.90                       | 3.46                                    | 12/2014<br>-          | 12/2014     |
| 145  | Rebuilding of Battery Block 5A and Re-construction of Battery Block 5B<br>- [N12000080                           | 3/2012           | 339.35<br>-                        | 339.35                       | 12.07                                   | 06/2015<br>-          | 06/2015     |
|      | Total                                                                                                            |                  | 926.90<br>-                        | 926.90                       | 84.45                                   |                       |             |
|      |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|      | <u>Urban Development</u>                                                                                         |                  |                                    |                              |                                         |                       |             |
| 146  | DELHI MRTS PHASE-III<br>- [N28000056                                                                             | 9/2011           | 35,242.00<br>-                     | 35,242.00                    | 3,853.30                                | 03/2016<br>-          | 03/2016     |
|      | Total                                                                                                            |                  | 35,242.00<br>-                     | 35,242.00                    | 3,853.30                                |                       |             |
|      |                                                                                                                  |                  |                                    |                              |                                         |                       |             |
|      | Grand Total                                                                                                      |                  | 248,267.36                         | 252,708.53                   | 50,432.33                               |                       |             |

## List of Delayed Projects w.r.t. Original and Revised Schedule

| (Aug,2013) |                                                                                          |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|------------|------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
|            |                                                                                          |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
| S.No       | Project                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1          | 2                                                                                        | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
|            | <u>Atomic Energy</u>                                                                     |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 1          | KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu                                     | 12/2001          | 13,171.00<br>17,270.00             | 17,270.00                    | 16,485.00                          | 12/2008<br>-          | 06/2014     | 66                                | -                                |
| 2          | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu        | 09/2003          | 3,492.00<br>-                      | 5,677.00                     | 4,681.60                           | 09/2010<br>-          | 03/2015     | 54                                | -                                |
| 3          | KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat                       | 10/2009          | 11,459.00<br>-                     | 11,459.00                    | 3,088.00                           | 12/2015<br>-          | 11/2016     | 11                                | -                                |
| 4          | RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan          | 10/2009          | 12,320.00<br>-                     | 12,320.00                    | 2,119.00                           | 12/2016<br>-          | 03/2017     | 3                                 | -                                |
|            | <b>Total</b>                                                                             |                  | 40,442.00<br>-                     | 46,726.00                    | 26,373.60                          |                       |             |                                   |                                  |
|            |                                                                                          |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|            | <u>Civil Aviation</u>                                                                    |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 5          | Construction of New International Terminal Building - [N04000069]AAI,Goa                 | 05/2010          | 335.61<br>-                        | 335.61                       | 233.69                             | 05/2012<br>-          | 09/2013     | 16                                | -                                |
| 6          | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim                       | 01/2009          | 309.46<br>-                        | 309.46                       | 231.80                             | 01/2011<br>04/2013    | 12/2014     | 47                                | 20                               |
|            | <b>Total</b>                                                                             |                  | 645.07<br>-                        | 645.07                       | 465.49                             |                       |             |                                   |                                  |
|            |                                                                                          |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|            | <u>Coal</u>                                                                              |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 7          | TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu                    | 10/2004          | 2,030.78<br>3,027.59               | 3,027.59                     | 2,772.41                           | 06/2009<br>-          | 01/2014     | 55                                | -                                |
| 8          | KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha                              | 01/2005          | 302.96<br>-                        | 302.96                       | 115.27                             | 03/2010<br>-          | 03/2014     | 48                                | -                                |
| 9          | ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand                                  | 12/2007          | 471.66<br>341.63                   | 341.63                       | 108.85                             | 03/2011<br>-          | 03/2014     | 36                                | -                                |
| 10         | KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh                                 | 06/2011          | 789.88<br>-                        | 741.62                       | 372.96                             | 03/2013<br>-          | 03/2014     | 12                                | -                                |
| 11         | TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu                    | 05/2008          | 4,904.54<br>6,540.93               | 6,540.93                     | 4,539.00                           | 03/2012<br>-          | 03/2014     | 24                                | -                                |
| 12         | ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha                              | 08/2008          | 207.28<br>-                        | 207.28                       | 114.09                             | 03/2012<br>-          | 03/2014     | 24                                | -                                |
| 13         | ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh                                  | 12/2009          | 212.34<br>779.26                   | 977.53                       | 722.85                             | 03/2013<br>09/2012    | 10/2014     | 19                                | 25                               |
| 14         | NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh | 10/2007          | 259.40<br>-                        | 259.40                       | 6.66                               | 03/2012<br>-          | 03/2015     | 36                                | -                                |
| 15         | KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha                                      | 12/2007          | 457.77<br>-                        | 457.77                       | 112.72                             | 03/2013<br>-          | 03/2015     | 24                                | -                                |
| 16         | BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha                              | 12/2007          | 172.08<br>-                        | 172.08                       | 124.54                             | 03/2010<br>-          | 03/2015     | 60                                | -                                |
| 17         | HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha                                | 11/2008          | 479.63<br>-                        | 479.63                       | 114.88                             | 03/2013<br>-          | 03/2015     | 24                                | -                                |
| 18         | MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh                       | 03/2010          | 181.19<br>-                        | 181.19                       | 34.58                              | 03/2012<br>-          | 03/2015     | 36                                | -                                |

(Aug,2013)

|      |                                                                                             |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|---------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                     | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                           | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 19   | Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand                                           | 07/2008          | 210.98 -                           | 210.98                       | 89.24                              | 03/2013 -             | 03/2015     | 24                                | -                                |
| 20   | GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh                        | 06/2010          | 2,675.67 -                         | 2,675.67                     | 1,419.31                           | 03/2014 -             | 03/2016     | 24                                | -                                |
| 21   | DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh                        | 12/2009          | 1,943.66 -                         | 1,943.66                     | 1,259.22                           | 03/2014 -             | 03/2016     | 24                                | -                                |
| 22   | MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand                                           | 08/2008          | 469.78 -                           | 706.40                       | 27.60                              | 07/2012 -             | 03/2016     | 44                                | -                                |
| 23   | CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh                                         | 06/2008          | 462.35 -                           | 462.35                       | 266.91                             | 03/2014 -             | 03/2016     | 24                                | -                                |
| 24   | KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh                                          | 12/2008          | 453.63 -                           | 453.63                       | 87.53                              | 12/2012 -             | 03/2016     | 39                                | -                                |
| 25   | RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand                                                 | 09/2009          | 153.82 -                           | 153.82                       | 24.89                              | 03/2014 -             | 03/2016     | 24                                | -                                |
| 26   | PENGANGA OC - [N06000066]WCL,Maharashtra                                                    | 10/2008          | 339.77 -                           | 339.77                       | 1.20                               | 03/2014 -             | 03/2016     | 24                                | -                                |
| 27   | KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh                                 | 07/2008          | 178.44 -                           | 178.44                       | -                                  | 03/2014 -             | 03/2016     | 24                                | -                                |
| 28   | MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh                               | 12/2009          | 321.42 -                           | 321.50                       | 209.96                             | 03/2014 -             | 03/2016     | 24                                | -                                |
| 29   | Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand                                        | 08/2007          | 163.51 -                           | 163.51                       | 35.12                              | 03/2011 -             | 03/2016     | 60                                | -                                |
| 30   | Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand                                              | 08/2008          | 264.68 -                           | 264.68                       | 138.03                             | 03/2012 -             | 03/2016     | 48                                | -                                |
| 31   | JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal                                         | 11/2006          | 287.18 -                           | 287.17                       | 0.92                               | 03/2011 -             | 03/2017     | 72                                | -                                |
| 32   | JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh                                    | 09/2008          | 152.43 -                           | 152.43                       | -                                  | 03/2015 -             | 03/2017     | 24                                | -                                |
| 33   | North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand                                      | 12/2007          | 179.87 -                           | 179.87                       | 56.12                              | 03/2012 -             | 03/2017     | 60                                | -                                |
| 34   | NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu                     | 06/2011          | 5,907.11 -                         | 5,907.11                     | 33.10                              | 12/2015 -             | 02/2018     | 26                                | -                                |
|      | Total                                                                                       |                  | 24,633.81 -                        | 28,090.60                    | 12,787.96                          |                       |             |                                   |                                  |
|      |                                                                                             |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Steel</u>                                                                                |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 35   | EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh | 10/2005          | 8,692.00<br>12,291.00              | 12,291.00                    | 10,522.68                          | 10/2009<br>10/2012    | 09/2013     | 47                                | 11                               |
| 36   | 67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh            | 07/2007          | 230.00<br>343.58                   | 343.58                       | 278.77                             | 02/2011<br>02/2011    | 09/2013     | 31                                | 31                               |
| 37   | Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh                | 01/2007          | 295.89<br>607.17                   | 607.17                       | 353.13                             | 12/2011<br>03/2012    | 12/2013     | 24                                | 21                               |
| 38   | COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh                           | 08/2007          | 108.00<br>216.68                   | 216.68                       | 152.10                             | 10/2012<br>10/2012    | 12/2013     | 14                                | 14                               |
| 39   | EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal                                | 02/2008          | 14,443.00 -                        | 16,408.00                    | 14,967.69                          | 12/2011 -             | 12/2013     | 24                                | -                                |
| 40   | Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State                      | 05/2008          | 480.00 -                           | 450.00                       | 278.90                             | 05/2012<br>05/2012    | 12/2013     | 19                                | 19                               |
| 41   | EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand                                 | 01/2008          | 6,325.00 -                         | 6,325.00                     | 3,727.01                           | 12/2011 -             | 12/2013     | 24                                | -                                |

(Aug,2013)

|      |                                                                                      |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|--------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                    | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 42   | Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha                           | 09/2008          | 11,812.00 -                        | 11,812.00                    | 9,817.02                           | 03/2013 -             | 12/2013     | 9                                 | -                                |
| 43   | 1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka          | 04/2011          | 572.00 -                           | 572.00                       | 321.92                             | 04/2013 12/2013       | 12/2013     | 8                                 | 0                                |
| 44   | 7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka        | 02/2011          | 898.55 -                           | 898.55                       | 213.94                             | 05/2013 03/2014       | 03/2014     | 10                                | 0                                |
| 45   | EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal                      | 06/2009          | 2,875.00 -                         | 2,875.00                     | 1,772.53                           | 12/2012 -             | 03/2014     | 15                                | -                                |
| 46   | INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra      | 12/2011          | 187.33 -                           | 187.33                       | 80.31                              | 10/2013 -             | 06/2014     | 8                                 | -                                |
| 47   | EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh                        | 09/2008          | 17,265.00 -                        | 17,265.00                    | 10,284.01                          | 03/2013 -             | 09/2014     | 18                                | -                                |
| 48   | ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha           | 11/2011          | 254.55 -                           | 254.55                       | 69.12                              | 11/2013 -             | 06/2015     | 19                                | -                                |
|      | Total                                                                                |                  | 64,438.32 -                        | 70,505.86                    | 52,839.13                          |                       |             |                                   |                                  |
|      |                                                                                      |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Petrochemicals</u>                                                                |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 49   | ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam                                    | 04/2006          | 5,460.61 8,920.00                  | 8,920.00                     | 4,510.51                           | 04/2012 12/2013       | 12/2013     | 20                                | 0                                |
|      | Total                                                                                |                  | 5,460.61 -                         | 8,920.00                     | 4,510.51                           |                       |             |                                   |                                  |
|      |                                                                                      |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Petroleum</u>                                                                     |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 50   | DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh      | 03/2009          | 3,597.00 2,730.00                  | 2,730.00                     | 1,697.33                           | 09/2011 03/2012       | 08/2013     | 23                                | 17                               |
| 51   | DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra         | 03/2009          | 3,284.00 2,174.00                  | 2,174.00                     | 1,459.18                           | 09/2011 05/2012       | 09/2013     | 24                                | 16                               |
| 52   | HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra     | 04/2008          | 825.00 -                           | 1,827.00                     | -                                  | 04/2013 -             | 09/2013     | 5                                 | -                                |
| 53   | Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat         | 03/2009          | 234.78 234.78                      | 317.64                       | 96.88                              | 09/2012 -             | 09/2013     | 12                                | -                                |
| 54   | BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana                | 11/2009          | 341.50 -                           | 341.50                       | 192.74                             | 02/2013 -             | 09/2013     | 7                                 | -                                |
| 55   | MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka                      | 08/2008          | 12,412.00 -                        | 12,160.26                    | 10,486.51                          | 01/2012 -             | 10/2013     | 21                                | -                                |
| 56   | Development of SB-14 field - [N16000116]ONGC,Multi State                             | 01/2011          | 410.44 -                           | 410.44                       | 228.26                             | 11/2012 -             | 10/2013     | 11                                | -                                |
| 57   | ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra                | 10/2008          | 1,797.35 -                         | 977.00                       | 773.81                             | 12/2011 -             | 11/2013     | 23                                | -                                |
| 58   | Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh       | 07/2010          | 1,000.00 -                         | 1,000.00                     | 649.76                             | 01/2013 -             | 11/2013     | 10                                | -                                |
| 59   | IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam                                 | 09/2001          | 345.10 663.69                      | 750.00                       | 729.07                             | 03/2007 03/2014       | 12/2013     | 81                                | -3                               |
| 60   | IOR GELEKI (ONGCL) - [160100216]ONGC,Assam                                           | 09/2001          | 390.09 1,674.11                    | 1,674.11                     | 1,727.24                           | 03/2007 03/2017       | 12/2013     | 81                                | -39                              |
| 61   | IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam                                      | 09/2001          | 113.90 438.85                      | 438.85                       | 432.22                             | 03/2006 03/2013       | 12/2013     | 93                                | 9                                |
| 62   | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra | 01/2007          | 740.02 -                           | 740.02                       | 730.48                             | 03/2010 03/2012       | 12/2013     | 45                                | 21                               |

(Aug,2013)

|      |                                                                                            |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|--------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                          | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 63   | VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State | 12/2009          | 463.32<br>-                        | 330.47                       | 261.51                             | 03/2012<br>-          | 12/2013     | 21                                | -                                |
| 64   | Polypropylene unit - [N16000113]Mangalore Refin,Karnataka                                  | 05/2009          | 1,803.78<br>-                      | 1,803.78                     | 732.72                             | 07/2012<br>-          | 12/2013     | 17                                | -                                |
| 65   | Construction of 6 ETPs - [N16000117]ONGC,Gujarat                                           | 03/2009          | 302.26<br>-                        | 240.95                       | 98.72                              | 09/2012<br>-          | 12/2013     | 15                                | -                                |
| 66   | Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State                           | 08/2010          | 372.11<br>-                        | 372.11                       | 234.31                             | 03/2013<br>-          | 12/2013     | 9                                 | -                                |
| 67   | PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra | 08/2009          | 246.81<br>276.83                   | 276.83                       | 238.10                             | 04/2012<br>06/2013    | 12/2013     | 20                                | 6                                |
| 68   | SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka          | 07/2010          | 1,043.57<br>-                      | 957.10                       | 655.84                             | 04/2012<br>-          | 12/2013     | 20                                | -                                |
| 69   | STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka              | 01/2006          | 732.00<br>1,227.00                 | 1,227.00                     | 722.53                             | 10/2011<br>-          | 12/2013     | 26                                | -                                |
| 70   | GAS TURBINE GENERATION SET - [N18000146]OIL,Assam                                          | 07/2009          | 216.88<br>-                        | 216.88                       | 160.36                             | 10/2011<br>-          | 12/2013     | 26                                | -                                |
| 71   | CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam                     | 08/2008          | 144.02<br>-                        | 204.29                       | 130.26                             | 06/2012<br>-          | 12/2013     | 18                                | -                                |
| 72   | STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh             | 01/2006          | 672.00<br>1,038.00                 | 1,038.00                     | 904.74                             | 10/2011<br>-          | 01/2014     | 27                                | -                                |
| 73   | DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State                                  | 04/2003          | 429.82<br>2,735.65                 | 2,735.65                     | 2,184.00                           | 04/2006<br>06/2012    | 02/2014     | 94                                | 20                               |
| 74   | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                               | 08/2006          | 3,195.16<br>3,690.37               | 3,690.37                     | 2,520.91                           | 12/2008<br>04/2013    | 03/2014     | 63                                | 11                               |
| 75   | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra                         | 10/2007          | 5,713.03<br>8,813.41               | 8,813.41                     | 7,204.61                           | 05/2010<br>03/2013    | 03/2014     | 46                                | 12                               |
| 76   | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                            | 06/2007          | 1,436.21<br>1,456.96               | 1,436.21                     | 1,100.32                           | 07/2010<br>05/2012    | 03/2014     | 44                                | 22                               |
| 77   | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra                       | 01/2009          | 7,133.39<br>-                      | 6,855.93                     | 5,308.52                           | 09/2012<br>-          | 03/2014     | 18                                | -                                |
| 78   | ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam                                  | 03/2009          | 2,465.15<br>-                      | 2,378.86                     | 1,494.55                           | 03/2013<br>-          | 03/2014     | 12                                | -                                |
| 79   | Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura            | 07/2008          | 288.04<br>288.04                   | 253.66                       | 199.40                             | 08/2012<br>-          | 03/2014     | 19                                | -                                |
| 80   | 102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan                                      | 07/2010          | 1,106.00<br>-                      | 678.02                       | 28.10                              | 06/2012<br>-          | 03/2014     | 21                                | -                                |
| 81   | Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State            | 11/2010          | 331.20<br>-                        | 269.10                       | 78.89                              | 08/2013<br>-          | 03/2014     | 7                                 | -                                |
| 82   | CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam                           | 08/2008          | 126.18<br>-                        | 159.54                       | 59.52                              | 06/2012<br>-          | 03/2014     | 21                                | -                                |
| 83   | PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha                                          | 02/2009          | 29,777.00<br>-                     | 32,710.00                    | 22,957.00                          | 11/2012<br>-          | 04/2014     | 17                                | -                                |
| 84   | DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra                          | 06/2007          | 3,248.78<br>5,633.44               | 5,633.44                     | 5,116.25                           | 08/2010<br>03/2012    | 05/2014     | 45                                | 26                               |
| 85   | ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State                                 | 01/2010          | 2,163.64<br>2,331.62               | 2,331.62                     | 1,557.08                           | 06/2012<br>-          | 05/2014     | 23                                | -                                |
| 86   | Development of WD-16 Cluster Fields - [N16000105]ONGC,Multi State                          | 06/2010          | 2,523.00<br>-                      | 2,523.00                     | 957.44                             | 01/2014<br>-          | 05/2014     | 4                                 | -                                |
| 87   | CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra            | 03/2011          | 861.79<br>-                        | 761.68                       | 281.53                             | 05/2013<br>-          | 05/2014     | 12                                | -                                |

(Aug,2013)

|      |                                                                                        |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|----------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                      | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 88   | IOR of B-173A Field - [N16000140]ONGC,Multi State                                      | 01/2012          | 352.49 -                           | 352.49                       | 4.19                               | 03/2014 -             | 05/2014     | 2                                 | -                                |
| 89   | URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State                       | 11/2012          | 309.81 -                           | 309.82                       | 48.71                              | 08/2014 -             | 10/2014     | 2                                 | -                                |
| 90   | Development of Cluster-7 Fields - [N16000104]ONGC,Multi State                          | 03/2010          | 3,241.03<br>6,638.94               | 6,638.94                     | 1,451.42                           | 03/2013<br>11/2014    | 11/2014     | 20                                | 0                                |
| 91   | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana                             | 11/2007          | 281.07 -                           | 281.07                       | 4.42                               | 10/2010 -             | 12/2014     | 50                                | -                                |
| 92   | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State          | 06/2007          | 736.65 -                           | 736.65                       | 360.32                             | 09/2011 -             | 12/2014     | 39                                | -                                |
| 93   | CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam               | 06/2010          | 202.94 -                           | 202.94                       | 4.12                               | 01/2014 -             | 01/2015     | 12                                | -                                |
| 94   | UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam    | 09/2012          | 871.35 -                           | 871.35                       | 2.26                               | 03/2015 -             | 06/2015     | 3                                 | -                                |
| 95   | AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,Multi State           | 08/2011          | 586.00 -                           | 586.00                       | 56.49                              | 07/2015 -             | 08/2015     | 1                                 | -                                |
| 96   | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                       | 01/2007          | 2,323.40<br>2,920.82               | 2,920.82                     | 1,902.72                           | 09/2010<br>03/2012    | 12/2015     | 63                                | 45                               |
| 97   | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State               | 07/2009          | 7,596.18 -                         | 7,596.18                     | 13.30                              | 01/2013 -             | 12/2015     | 35                                | -                                |
| 98   | IREP - [N16000143]BPCL,Kerala                                                          | 01/1999          | 14,225.00 -                        | 14,225.00                    | 508.63                             | 12/2015 -             | 05/2016     | 5                                 | -                                |
| 99   | Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State          | 01/2010          | 723.64 -                           | 723.64                       | -                                  | 03/2013 -             | 06/2016     | 39                                | -                                |
| 100  | CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY - [N16000167]OIL,Multi State | 08/2006          | 374.56 -                           | 374.56                       | -                                  | 09/2012 -             | 10/2016     | 49                                | -                                |
| 101  | Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat                                      | 11/2010          | 1,916.10 -                         | 1,916.10                     | 783.72                             | 12/2014 -             | 12/2016     | 24                                | -                                |
| 102  | Ankleswar Redevelopment - [N16000122]ONGC,Gujarat                                      | 11/2010          | 2,189.63 -                         | 2,189.63                     | 1,039.14                           | 12/2014 -             | 12/2016     | 24                                | -                                |
| 103  | Mehesana Redevelopment - [N16000121]ONGC,Gujarat                                       | 11/2010          | 3,823.00 -                         | 3,823.00                     | 701.81                             | 04/2015 -             | 03/2017     | 23                                | -                                |
|      | Total                                                                                  |                  | 132,039.17 -                       | 147,186.91                   | 81,271.94                          |                       |             |                                   |                                  |
|      |                                                                                        |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Power</u>                                                                           |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 104  | TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State      | 12/2008          | 7,031.88 -                         | 7,031.88                     | 4,572.72                           | 12/2012 -             | 09/2013     | 9                                 | -                                |
| 105  | TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State          | 02/2009          | 184.19 -                           | 184.19                       | 157.27                             | 11/2011 -             | 09/2013     | 22                                | -                                |
| 106  | System Strengthening -XII of SR - [N18000085]PGCIL,Multi State                         | 02/2010          | 232.34 -                           | 232.34                       | 153.02                             | 06/2012 -             | 09/2013     | 15                                | -                                |
| 107  | URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir                         | 08/2005          | 1,729.29 -                         | 2,081.00                     | 2,035.18                           | 11/2009<br>02/2013    | 10/2013     | 47                                | 8                                |
| 108  | NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir                  | 08/2006          | 611.01 -                           | 936.00                       | 874.31                             | 08/2010<br>01/2013    | 10/2013     | 38                                | 9                                |
| 109  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State          | 10/2010          | 182.68 -                           | 182.68                       | 134.05                             | 01/2013 -             | 10/2013     | 9                                 | -                                |
| 110  | RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh                 | 01/2009          | 6,230.81 -                         | 6,230.81                     | 4,468.00                           | 10/2012 -             | 11/2013     | 13                                | -                                |

(Aug,2013)

|      |                                                                                            |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|--------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                          | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 111  | EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State                       | 10/2006          | 975.96 -                           | 975.96                       | 885.07                             | 10/2009 -             | 12/2013     | 50                                | -                                |
| 112  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State           | 02/2009          | 509.66 -                           | 509.66                       | 380.93                             | 11/2011 -             | 12/2013     | 25                                | -                                |
| 113  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State             | 02/2009          | 410.29 -                           | 410.29                       | 266.57                             | 02/2012 -             | 12/2013     | 22                                | -                                |
| 114  | 765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State          | 11/2009          | 1,075.12 -                         | 1,075.12                     | 838.25                             | 05/2012 -             | 12/2013     | 19                                | -                                |
| 115  | Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh                | 12/2010          | 1,719.52 -                         | 1,719.52                     | 1,259.49                           | 08/2013 -             | 12/2013     | 4                                 | -                                |
| 116  | SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State          | 08/2010          | 170.36 -                           | 170.36                       | 90.67                              | 04/2013 -             | 12/2013     | 8                                 | -                                |
| 117  | TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra          | 07/2011          | 181.93 -                           | 181.93                       | 136.41                             | 07/2013 -             | 12/2013     | 5                                 | -                                |
| 118  | TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh | 08/2011          | 425.51 -                           | 425.51                       | 322.97                             | 10/2013 -             | 12/2013     | 2                                 | -                                |
| 119  | PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh                        | 10/2005          | 2,304.56 -                         | 2,716.00                     | 2,169.15                           | 10/2010 01/2013       | 03/2014     | 41                                | 14                               |
| 120  | RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pradesh                                    | 01/2007          | 2,047.03 -                         | 2,047.03                     | 2,671.47                           | 01/2012 -             | 03/2014     | 26                                | -                                |
| 121  | SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State          | 08/2008          | 2,360.95 2,580.90                  | 2,580.90                     | 2,059.77                           | 08/2012 -             | 03/2014     | 19                                | -                                |
| 122  | 765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State          | 08/2008          | 7,075.33 -                         | 7,075.33                     | 5,883.09                           | 08/2012 -             | 03/2014     | 19                                | -                                |
| 123  | NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State           | 03/2010          | 965.58 -                           | 965.58                       | 601.58                             | 11/2012 -             | 03/2014     | 16                                | -                                |
| 124  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State             | 07/2010          | 752.64 -                           | 752.64                       | 313.52                             | 07/2013 -             | 03/2014     | 8                                 | -                                |
| 125  | TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha               | 09/2010          | 2,074.86 -                         | 2,074.86                     | 1,202.80                           | 03/2013 -             | 05/2014     | 14                                | -                                |
| 126  | TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha               | 12/2010          | 2,743.19 -                         | 2,743.19                     | 1,670.12                           | 12/2013 -             | 05/2014     | 5                                 | -                                |
| 127  | TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State            | 03/2011          | 2,569.25 -                         | 2,569.25                     | 1,813.91                           | 03/2014 -             | 05/2014     | 2                                 | -                                |
| 128  | TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State  | 10/2008          | 4,824.12 -                         | 4,824.12                     | 3,504.41                           | 10/2012 -             | 06/2014     | 20                                | -                                |
| 129  | Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State          | 02/2010          | 2,144.00 -                         | 2,144.00                     | 1,371.71                           | 12/2012 -             | 06/2014     | 18                                | -                                |
| 130  | System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State        | 12/2009          | 1,216.83 -                         | 1,216.83                     | 900.28                             | 08/2012 -             | 06/2014     | 22                                | -                                |
| 131  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State              | 02/2009          | 520.48 -                           | 520.48                       | 363.00                             | 11/2011 -             | 07/2014     | 32                                | -                                |
| 132  | KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh                                       | 10/2002          | 4,527.15 -                         | 6,414.56                     | 5,095.00                           | 04/2009 -             | 09/2014     | 65                                | -                                |
| 133  | PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh                  | 12/2008          | 573.99 1,117.92                    | 1,117.92                     | 660.88                             | 08/2012 08/2013       | 09/2014     | 25                                | 13                               |
| 134  | BARH STPP STAGE -II - [N18000047]NTPC,Bihar                                                | 02/2008          | 7,341.04 -                         | 7,341.04                     | 6,307.00                           | 08/2013 -             | 09/2014     | 13                                | -                                |
| 135  | EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State                      | 07/2010          | 1,272.80 -                         | 1,272.80                     | 709.36                             | 11/2012 -             | 09/2014     | 22                                | -                                |



(Aug,2013)

|      |                                                                                             |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|---------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                     | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                           | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 136  | TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand             | 10/2011          | 558.26 -                           | 558.26                       | 166.39                             | 11/2013 -             | 09/2014     | 10                                | -                                |
| 137  | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal                           | 09/2005          | 1,061.38 -                         | 1,501.75                     | 1,376.77                           | 09/2009 06/2013       | 11/2014     | 62                                | 17                               |
| 138  | Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State          | 05/2010          | 250.03 -                           | 250.03                       | 63.41                              | 01/2013 -             | 12/2014     | 23                                | -                                |
| 139  | Transmission system for transfer of power from Gen- PART B - [N18000099]PGCIL,Multi State   | 03/2011          | 1,585.12 -                         | 1,585.12                     | 1,014.35                           | 11/2013 -             | 12/2014     | 13                                | -                                |
| 140  | TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State | 09/2011          | 1,366.34 -                         | 1,366.34                     | 768.46                             | 12/2013 -             | 12/2014     | 12                                | -                                |
| 141  | TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram                           | 01/2011          | 913.63 -                           | 913.63                       | 451.94                             | 07/2014 -             | 02/2015     | 7                                 | -                                |
| 142  | Transmission System of Vindhuchal -IV And Rihand - [N18000076]PGCIL,Multi State             | 03/2010          | 4,672.99 -                         | 4,672.99                     | 2,650.25                           | 11/2012 -             | 03/2015     | 28                                | -                                |
| 143  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State             | 08/2010          | 1,677.57 -                         | 1,677.57                     | 882.14                             | 04/2013 -             | 03/2015     | 23                                | -                                |
| 144  | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State           | 09/2012          | 524.40 -                           | 524.40                       | 40.78                              | 04/2015 -             | 05/2015     | 1                                 | -                                |
| 145  | NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State           | 02/2009          | 11,130.19 -                        | 11,130.19                    | 6,539.65                           | 08/2013 -             | 06/2015     | 22                                | -                                |
| 146  | BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam                                    | 01/2008          | 4,375.35 -                         | 4,375.35                     | 4,002.00                           | 07/2011 -             | 10/2015     | 51                                | -                                |
| 147  | TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand                        | 11/2006          | 2,978.48 -                         | 3,846.30                     | 1,880.00                           | 03/2013 -             | 03/2016     | 36                                | -                                |
| 148  | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand                   | 08/2008          | 2,491.58 -                         | 3,745.08                     | 360.37                             | 07/2014 -             | 05/2016     | 22                                | -                                |
| 149  | KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir                                         | 07/2007          | 2,238.67 3,642.04                  | 3,642.00                     | 2,579.51                           | 01/2016 01/2016       | 11/2016     | 10                                | 10                               |
| 150  | BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar                                    | 12/2003          | 8,692.97 -                         | 8,693.00                     | 8,627.00                           | 12/2009 -             | 02/2017     | 86                                | -                                |
| 151  | TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh                         | 07/2006          | 1,657.00 2,978.86                  | 2,978.86                     | 509.53                             | 07/2010 02/2016       | 02/2017     | 79                                | 12                               |
| 152  | KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh                 | 12/2004          | 2,496.90 -                         | 5,139.00                     | 2,448.33                           | 05/2013 05/2013       | 03/2017     | 46                                | 46                               |
| 153  | SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh                            | 09/2003          | 6,285.33 -                         | 10,667.00                    | 6,332.94                           | 09/2010 08/2014       | 12/2017     | 87                                | 40                               |
| 154  | PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh                                    | 09/2002          | 3,919.59 -                         | 5,366.00                     | 4,027.33                           | 09/2009 07/2014       | 07/2018     | 106                               | 48                               |
|      | Total                                                                                       |                  | 125,860.13 -                       | 143,356.65                   | 98,593.11                          |                       |             |                                   |                                  |
|      |                                                                                             |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Railways</u>                                                                             |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 155  | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha                                       | 04/1993          | 100.00 142.98                      | 227.94                       | 229.30                             | 03/2002 -             | 09/2013     | 138                               | -                                |
| 156  | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State              | 04/1986          | 158.77 580.83                      | 580.83                       | 579.43                             | 03/1994 -             | 10/2013     | 235                               | -                                |
| 157  | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh                   | 04/1999          | 108.00 427.21                      | 432.72                       | 394.63                             | 12/2009 03/2011       | 10/2013     | 46                                | 31                               |



(Aug,2013)

|      |                                                                                  |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|----------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                          | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 158  | Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal                            | 04/2009          | 189.97<br>611.03                   | 611.03                       | 130.61                             | 12/2011<br>11/2013    | 11/2013     | 23                                | 0                                |
| 159  | Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal   | 04/1999          | 207.52<br>207.52                   | 207.52                       | 177.60                             | 12/2012<br>-          | 12/2013     | 12                                | -                                |
| 160  | Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka                                 | 04/2006          | 287.99<br>-                        | 287.99                       | 421.25                             | 01/1999<br>-          | 12/2013     | 179                               | -                                |
| 161  | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G' - [N22000094]RE,Uttar Pradesh | 02/2008          | 171.10<br>224.89                   | 246.44                       | 141.55                             | 03/2012<br>12/2013    | 03/2014     | 24                                | 3                                |
| 162  | Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka    | 04/2007          | 482.00<br>482.70                   | 482.70                       | 486.44                             | 03/2013<br>-          | 03/2014     | 12                                | -                                |
| 163  | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha                               | 04/1999          | 166.16<br>-                        | 288.00                       | 281.73                             | 02/2009<br>02/2009    | 08/2014     | 66                                | 66                               |
| 164  | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha               | 04/2000          | 133.41<br>207.00                   | 276.00                       | 254.02                             | 03/2009<br>03/2009    | 08/2014     | 65                                | 65                               |
| 165  | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh                          | 09/2001          | 129.70<br>245.39                   | 245.39                       | 230.40                             | 12/2008<br>-          | 09/2014     | 69                                | -                                |
| 166  | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra  | 03/1996          | 401.81<br>495.44                   | 1,814.48                     | 250.13                             | 03/2004<br>12/2010    | 12/2014     | 129                               | 48                               |
| 167  | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar                  | 04/2002          | 921.00<br>2,363.00                 | 2,363.00                     | 1,146.14                           | 03/2009<br>12/2012    | 12/2014     | 69                                | 24                               |
| 168  | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu     | 04/2006          | 495.74<br>-                        | 495.74                       | 250.82                             | 06/2013<br>06/2013    | 12/2014     | 18                                | 18                               |
| 169  | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam       | 04/1996          | 1,676.31<br>1,676.31               | 5,000.00                     | 3,635.42                           | 03/2009<br>-          | 12/2014     | 69                                | -                                |
| 170  | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State       | 03/1984          | 520.00<br>835.04                   | 835.04                       | 602.18                             | 03/1995<br>-          | 03/2015     | 240                               | -                                |
| 171  | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal                    | 04/1974          | 31.42<br>393.46                    | 535.40                       | 177.85                             | 03/2007<br>03/2007    | 03/2015     | 96                                | 96                               |
| 172  | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar                             | 09/2001          | 100.00<br>492.98                   | 1,041.79                     | 742.54                             | 12/2010<br>12/2010    | 03/2015     | 51                                | 51                               |
| 173  | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State | 04/2000          | 733.00<br>733.00                   | 2,350.00                     | 1,477.35                           | 12/2008<br>-          | 03/2015     | 75                                | -                                |
| 174  | Katakhal to Bhairabi - [N22000126]NEFR,Assam                                     | 04/1998          | 227.90<br>227.90                   | 223.01                       | 125.93                             | 12/2012<br>-          | 03/2015     | 27                                | -                                |
| 175  | Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura             | 04/1999          | 895.00<br>-                        | 1,151.00                     | 944.78                             | 03/2007<br>-          | 03/2015     | 96                                | -                                |
| 176  | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam             | 09/1997          | 1,000.00<br>1,500.00               | 4,996.19                     | 2,836.11                           | 04/2008<br>03/2014    | 12/2015     | 92                                | 21                               |
| 177  | PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar                              | 04/2001          | 624.47<br>2,921.00                 | 2,921.00                     | 1,854.28                           | 10/2007<br>12/2012    | 12/2015     | 98                                | 36                               |
| 178  | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh                    | 09/2007          | 687.20<br>-                        | 800.00                       | 735.19                             | 03/2010<br>-          | 12/2015     | 69                                | -                                |
| 179  | AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura                             | 04/2008          | 813.34<br>813.34                   | 1,741.00                     | 483.28                             | 03/2014<br>-          | 12/2015     | 21                                | -                                |
| 180  | Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha                | 04/2010          | 149.90<br>-                        | 177.38                       | 41.41                              | 03/2015<br>-          | 12/2015     | 9                                 | -                                |
| 181  | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal                    | 03/1984          | 293.97<br>1,025.39                 | 1,074.47                     | 447.00                             | 06/2005<br>07/2011    | 06/2016     | 132                               | 59                               |
| 182  | New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal | 04/2010          | 2,397.72<br>-                      | 2,397.72                     | 56.63                              | 03/2016<br>-          | 06/2016     | 3                                 | -                                |

(Aug,2013)

|      |                                                                                 |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|---------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                         | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                               | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 183  | BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal                       | 03/1998          | 111.90<br>1,028.05                 | 1,423.98                     | 482.24                             | 03/2005<br>12/2008    | 12/2016     | 141                               | 96                               |
| 184  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra           | 04/2008          | 5,300.00<br>5,300.00               | 6,220.15                     | 1,294.74                           | 03/2014<br>03/2016    | 12/2016     | 33                                | 9                                |
| 185  | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur                   | 04/2003          | 727.56<br>727.53                   | 4,453.50                     | 1,595.53                           | 03/2011<br>03/2014    | 03/2017     | 72                                | 36                               |
| 186  | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh              | 04/2006          | 325.00<br>325.00                   | 1,116.53                     | 225.51                             | 03/2010<br>03/2017    | 03/2017     | 84                                | 0                                |
| 187  | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram                            | 04/2008          | 619.34<br>-                        | 2,384.34                     | 96.18                              | 04/2014<br>-          | 03/2017     | 35                                | -                                |
| 188  | SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim                                     | 04/2008          | 1,339.48<br>-                      | 3,380.58                     | 59.40                              | 12/2015<br>-          | 03/2017     | 15                                | -                                |
| 189  | New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland   | 04/2006          | 850.00<br>850.00                   | 2,441.48                     | 8.94                               | 03/2015<br>-          | 03/2017     | 24                                | -                                |
| 190  | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir           | 03/1995          | 2,500.00<br>2,500.00               | 20,000.00                    | 8,822.50                           | 11/2002<br>-          | 12/2017     | 181                               | -                                |
|      | Total                                                                           |                  | 25,876.68<br>-                     | 75,224.34                    | 31,719.04                          |                       |             |                                   |                                  |
|      |                                                                                 |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Road Transport And Highways</u>                                              |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 191  | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha             | 04/2000          | 225.00<br>-                        | 241.53                       | 162.71                             | 04/2004<br>-          | 09/2013     | 113                               | -                                |
| 192  | PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab           | 12/2003          | 284.00<br>-                        | 359.00                       | 315.50                             | 05/2008<br>-          | 09/2013     | 64                                | -                                |
| 193  | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam                                 | 12/2003          | 225.00<br>-                        | 225.00                       | 264.70                             | 06/2008<br>-          | 09/2013     | 63                                | -                                |
| 194  | THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu                        | 03/2005          | 280.00<br>-                        | 280.00                       | 581.50                             | 06/2009<br>-          | 09/2013     | 51                                | -                                |
| 195  | GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha                           | 04/2000          | 263.27<br>-                        | 263.27                       | 276.46                             | 02/2004<br>-          | 09/2013     | 115                               | -                                |
| 196  | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha      | 04/2000          | 228.70<br>-                        | 228.70                       | 194.51                             | 02/2004<br>-          | 09/2013     | 115                               | -                                |
| 197  | Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan                             | 11/2009          | 795.00<br>-                        | 795.00                       | 1,127.00                           | 05/2012<br>-          | 09/2013     | 16                                | -                                |
| 198  | Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan                                   | 06/2010          | 792.06<br>-                        | 792.06                       | 1,972.00                           | 12/2012<br>-          | 09/2013     | 9                                 | -                                |
| 199  | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh | 11/2010          | 1,585.00<br>-                      | 1,585.00                     | 957.80                             | 05/2013<br>-          | 09/2013     | 4                                 | -                                |
| 200  | JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan                                      | 08/2010          | 267.81<br>-                        | 267.81                       | 648.30                             | 02/2013<br>-          | 09/2013     | 7                                 | -                                |
| 201  | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka            | 04/2000          | 241.00<br>-                        | 196.65                       | 203.44                             | 08/2004<br>07/2010    | 10/2013     | 110                               | 39                               |
| 202  | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka       | 04/2000          | 318.00<br>-                        | 207.56                       | 196.42                             | 08/2004<br>-          | 10/2013     | 110                               | -                                |
| 203  | NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka                     | 04/2000          | 196.50<br>363.00                   | 196.50                       | 284.40                             | 06/2011<br>06/2011    | 10/2013     | 28                                | 28                               |
| 204  | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana                       | 04/2007          | 486.00<br>-                        | 486.00                       | 653.40                             | 05/2010<br>-          | 10/2013     | 41                                | -                                |
| 205  | Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra                               | 11/2009          | 1,110.00<br>-                      | 1,110.00                     | 1,802.00                           | 05/2012<br>-          | 10/2013     | 17                                | -                                |

(Aug,2013)

|      |                                                                                               |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                             | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 206  | Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand                                                 | 08/2010          | 625.07 -                           | 625.07                       | 947.60                             | 01/2013 -             | 10/2013     | 9                                 | -                                |
| 207  | DEOLI-KOTA - [N24000148]NHAI,Rajasthan                                                        | 01/2011          | 593.00 -                           | 593.00                       | 566.40                             | 07/2013 -             | 10/2013     | 3                                 | -                                |
| 208  | PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar                                                    | 08/2010          | 671.30 -                           | 671.30                       | 625.90                             | 02/2013 -             | 10/2013     | 8                                 | -                                |
| 209  | BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh                                                | 10/2011          | 209.00 -                           | 209.00                       | 34.38                              | 01/2013 -             | 10/2013     | 9                                 | -                                |
| 210  | HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh                  | 03/2005          | 220.00 -                           | 220.00                       | 284.20                             | 09/2007 -             | 11/2013     | 74                                | -                                |
| 211  | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar           | 12/2003          | 240.00 -                           | 240.00                       | 295.00                             | 10/2008 -             | 12/2013     | 62                                | -                                |
| 212  | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh                           | 03/2005          | 190.00 -                           | 190.00                       | 264.60                             | 01/2009 -             | 12/2013     | 59                                | -                                |
| 213  | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar                                   | 12/2003          | 332.94 -                           | 332.94                       | 470.20                             | 09/2008 -             | 12/2013     | 63                                | -                                |
| 214  | KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan                                    | 12/2003          | 275.00 -                           | 250.39                       | 280.40                             | 10/2008 -             | 12/2013     | 62                                | -                                |
| 215  | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam                                               | 12/2003          | 200.00 -                           | 200.00                       | 286.90                             | 06/2008 -             | 12/2013     | 66                                | -                                |
| 216  | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam                                            | 12/2003          | 264.72 -                           | 264.72                       | 301.10                             | 06/2008 -             | 12/2013     | 66                                | -                                |
| 217  | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam                               | 12/2003          | 160.00 -                           | 160.00                       | 207.20                             | 05/2008 -             | 12/2013     | 67                                | -                                |
| 218  | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                          | 12/2003          | 200.00 -                           | 200.00                       | 253.60                             | 06/2008 -             | 12/2013     | 66                                | -                                |
| 219  | LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh | 12/2003          | 407.60 -                           | 407.60                       | 186.50                             | 06/2010 -             | 12/2013     | 42                                | -                                |
| 220  | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh                                  | 12/2003          | 355.06 -                           | 355.06                       | 507.30                             | 09/2009 -             | 12/2013     | 51                                | -                                |
| 221  | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu                        | 03/2005          | 941.00 -                           | 941.00                       | 1,901.00                           | 01/2011 -             | 12/2013     | 35                                | -                                |
| 222  | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra                   | 03/2005          | 940.00 -                           | 940.00                       | 1,325.00                           | 07/2012 -             | 12/2013     | 17                                | -                                |
| 223  | Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra               | 04/2010          | 1,170.52 -                         | 1,170.52                     | 4.41                               | 06/2011 -             | 12/2013     | 30                                | -                                |
| 224  | Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat                 | 03/2010          | 1,509.10 -                         | 1,509.10                     | 2,080.00                           | 09/2012 -             | 12/2013     | 15                                | -                                |
| 225  | Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State                            | 04/2009          | 1,673.70 -                         | 1,673.70                     | 2,839.00                           | 10/2011 -             | 12/2013     | 26                                | -                                |
| 226  | Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State                       | 02/2009          | 1,693.75 -                         | 1,693.75                     | 2,707.00                           | 08/2011 -             | 12/2013     | 28                                | -                                |
| 227  | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana                         | 05/2009          | 1,108.00 -                         | 2,288.00                     | 3,465.90                           | 11/2011 -             | 12/2013     | 25                                | -                                |
| 228  | Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh                                      | 10/2010          | 1,175.00 -                         | 1,175.00                     | 138.67                             | 04/2013 -             | 12/2013     | 8                                 | -                                |
| 229  | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu           | 09/2010          | 852.00 -                           | 852.00                       | 834.00                             | 03/2013 -             | 12/2013     | 9                                 | -                                |
| 230  | AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab                                                   | 05/2010          | 705.00 -                           | 705.00                       | 2,124.00                           | 11/2012 -             | 12/2013     | 13                                | -                                |

(Aug,2013)

|      |                                                                                               |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                             | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 231  | 4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat                                   | 12/2010          | 1,008.50 -                         | 1,008.50                     | 1,346.00                           | 06/2013 -             | 12/2013     | 6                                 | -                                |
| 232  | 4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat                           | 03/2011          | 785.50 -                           | 785.50                       | 839.30                             | 08/2013 -             | 12/2013     | 4                                 | -                                |
| 233  | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI,Tamil Nadu             | 06/2011          | 600.00 -                           | 600.00                       | 75.85                              | 06/2013 -             | 12/2013     | 6                                 | -                                |
| 234  | Trichy Bypass - [N24000176]NHAI,Tamil Nadu                                                    | 05/2010          | 374.00 -                           | 374.00                       | 117.60                             | 05/2013 -             | 12/2013     | 7                                 | -                                |
| 235  | SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat                                            | 09/2010          | 805.39 -                           | 805.39                       | 612.90                             | 03/2013 -             | 12/2013     | 9                                 | -                                |
| 236  | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar                                           | 01/2011          | 575.00 -                           | 575.00                       | 714.40                             | 07/2013 -             | 12/2013     | 5                                 | -                                |
| 237  | BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha                                                  | 03/2011          | 500.29 -                           | 500.29                       | 509.00                             | 08/2013 -             | 12/2013     | 4                                 | -                                |
| 238  | INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh                                           | 11/2010          | 325.00 -                           | 325.00                       | 518.70                             | 05/2013 -             | 02/2014     | 9                                 | -                                |
| 239  | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam                      | 12/2003          | 157.47 -                           | 154.57                       | 240.40                             | 09/2007 -             | 03/2014     | 78                                | -                                |
| 240  | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh     | 12/2003          | 155.00 -                           | 201.66                       | 143.60                             | 09/2008 -             | 03/2014     | 66                                | -                                |
| 241  | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam             | 12/2003          | 230.00 -                           | 230.00                       | 239.20                             | 06/2005 -             | 03/2014     | 105                               | -                                |
| 242  | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam                           | 12/2003          | 195.00 -                           | 195.00                       | 250.10                             | 06/2008 -             | 03/2014     | 69                                | -                                |
| 243  | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                          | 12/2003          | 237.80 -                           | 237.80                       | 287.50                             | 06/2008 -             | 03/2014     | 69                                | -                                |
| 244  | RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh | 12/2003          | 251.03 -                           | 251.03                       | 337.80                             | 10/2008 -             | 03/2014     | 65                                | -                                |
| 245  | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam                                             | 12/2003          | 175.96 -                           | 175.96                       | 211.60                             | 04/2008 -             | 03/2014     | 71                                | -                                |
| 246  | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam                                             | 12/2003          | 245.00 -                           | 245.00                       | 491.20                             | 03/2008 -             | 03/2014     | 72                                | -                                |
| 247  | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam                                            | 12/2003          | 198.16 -                           | 198.16                       | 272.30                             | 04/2008 -             | 03/2014     | 71                                | -                                |
| 248  | NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra                                      | 03/2005          | 168.00 -                           | 168.00                       | 457.30                             | 12/2008 -             | 03/2014     | 63                                | -                                |
| 249  | AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh                  | 12/2003          | 348.16 -                           | 465.50                       | 237.20                             | 09/2007 -             | 03/2014     | 78                                | -                                |
| 250  | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                             | 03/2005          | 516.00 -                           | 516.00                       | 858.90                             | 07/2010 -             | 03/2014     | 44                                | -                                |
| 251  | Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu                                           | 04/2009          | 353.37 -                           | 353.37                       | 417.20                             | 10/2011 -             | 03/2014     | 29                                | -                                |
| 252  | WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra                         | 02/2011          | 193.45 -                           | 193.45                       | 54.59                              | 11/2012 -             | 03/2014     | 16                                | -                                |
| 253  | MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh                                            | 04/2010          | 1,267.00 -                         | 1,267.00                     | 1,857.00                           | 06/2013 -             | 03/2014     | 9                                 | -                                |
| 254  | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar                                            | 05/2011          | 351.54 -                           | 351.54                       | 394.10                             | 05/2013 -             | 03/2014     | 10                                | -                                |
| 255  | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State                                          | 09/2011          | 754.00 -                           | 754.00                       | 515.60                             | 03/2013 -             | 03/2014     | 12                                | -                                |

(Aug,2013)

|      |                                                                                      |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|--------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                              | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                    | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 256  | HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand                 | 11/2011          | 478.00 -                           | 478.00                       | 270.80                             | 10/2013 -             | 03/2014     | 5                                 | -                                |
| 257  | HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam                | 12/2003          | 212.00 -                           | 386.10                       | 68.94                              | 09/2007 -             | 04/2014     | 79                                | -                                |
| 258  | PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra                                      | 10/2010          | 1,724.55 -                         | 1,724.55                     | 1,193.00                           | 03/2013 -             | 04/2014     | 13                                | -                                |
| 259  | 2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar                            | 05/2011          | 664.00 -                           | 664.00                       | 550.00                             | 02/2014 -             | 04/2014     | 2                                 | -                                |
| 260  | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam       | 12/2003          | 280.00 -                           | 280.00                       | 322.50                             | 02/2009 03/2014       | 05/2014     | 63                                | 2                                |
| 261  | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam                                       | 12/2003          | 208.00 -                           | 208.00                       | 303.90                             | 04/2008 -             | 05/2014     | 73                                | -                                |
| 262  | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam                                  | 12/2003          | 196.00 -                           | 363.74                       | 155.90                             | 07/2009 -             | 05/2014     | 58                                | -                                |
| 263  | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar  | 12/2003          | 300.00 -                           | 300.00                       | 176.80                             | 10/2008 -             | 06/2014     | 68                                | -                                |
| 264  | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam         | 12/2003          | 155.04 -                           | 280.13                       | 123.00                             | 11/2008 -             | 06/2014     | 67                                | -                                |
| 265  | Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh | 05/2009          | 572.30 -                           | 572.30                       | 832.90                             | 10/2011 -             | 06/2014     | 32                                | -                                |
| 266  | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir               | 07/2010          | 1,813.76 -                         | 1,813.76                     | -                                  | 07/2013 -             | 06/2014     | 11                                | -                                |
| 267  | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh                              | 02/2011          | 1,141.00 -                         | 1,141.00                     | 1,264.00                           | 08/2013 -             | 06/2014     | 10                                | -                                |
| 268  | kandla - Mundra port - [N24000175]NHAI,Gujarat                                       | 01/2011          | 953.88 -                           | 953.88                       | 651.30                             | 07/2013 -             | 06/2014     | 11                                | -                                |
| 269  | 4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING - [N24000153]NHAI,Karnataka        | 03/2011          | 359.00 -                           | 359.00                       | 39.27                              | 09/2013 -             | 07/2014     | 10                                | -                                |
| 270  | LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh                                   | 07/1999          | 635.90 -                           | 635.90                       | 214.20                             | 07/2012 -             | 07/2014     | 24                                | -                                |
| 271  | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State     | 12/2003          | 232.45 -                           | 232.45                       | 304.30                             | 09/2010 -             | 08/2014     | 47                                | -                                |
| 272  | LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh     | 12/2003          | 263.17 -                           | 263.17                       | 233.80                             | 09/2009 -             | 09/2014     | 60                                | -                                |
| 273  | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam                                   | 12/2003          | 217.61 -                           | 217.61                       | 290.00                             | 04/2010 -             | 11/2014     | 55                                | -                                |
| 274  | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam          | 12/2003          | 199.81 -                           | 385.13                       | 91.97                              | 04/2009 -             | 12/2014     | 68                                | -                                |
| 275  | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam    | 12/2003          | 167.64 -                           | 167.64                       | 66.16                              | 11/2008 -             | 12/2014     | 73                                | -                                |
| 276  | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam           | 12/2003          | 200.00 -                           | 200.00                       | 164.50                             | 04/2009 -             | 12/2014     | 68                                | -                                |
| 277  | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State                                  | 12/2003          | 604.00 -                           | 604.00                       | 495.40                             | 12/2009 -             | 12/2014     | 60                                | -                                |
| 278  | NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,Kerala               | 03/2005          | 557.00 -                           | 557.00                       | 1,128.00                           | 02/2010 -             | 12/2014     | 58                                | -                                |
| 279  | NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha                                       | 07/2011          | 586.00 -                           | 586.00                       | 237.60                             | 01/2014 -             | 12/2014     | 11                                | -                                |
| 280  | 4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State                             | 02/2011          | 1,078.84 -                         | 1,078.84                     | 1,226.00                           | 08/2013 -             | 12/2014     | 16                                | -                                |

(Aug,2013)

|      |                                                                                              |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|----------------------------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                                            | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 281  | 4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State                                  | 02/2011          | 998.79 -                           | 998.79                       | 1,202.00                           | 08/2013 -             | 12/2014     | 16                                | -                                |
| 282  | Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu                                                | 09/2011          | 485.00 -                           | 485.00                       | 317.00                             | 08/2013 -             | 02/2015     | 18                                | -                                |
| 283  | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala                      | 02/2010          | 617.00 -                           | 617.00                       | 154.50                             | 08/2012 -             | 03/2015     | 31                                | -                                |
| 284  | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                                     | 12/2003          | 275.00 -                           | 281.31                       | 180.10                             | 02/2010 -             | 06/2015     | 64                                | -                                |
| 285  | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State                                       | 02/2011          | 2,498.76 -                         | 2,498.76                     | 1,734.00                           | 08/2014 -             | 07/2015     | 11                                | -                                |
| 286  | PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha                                                    | 03/2012          | 1,410.00 -                         | 1,410.00                     | 153.80                             | 09/2014 -             | 10/2015     | 13                                | -                                |
| 287  | FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala                      | 04/2011          | 682.00 -                           | 682.00                       | 143.60                             | 10/2013 -             | 11/2015     | 25                                | -                                |
| 288  | 4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State                                    | 02/2011          | 580.43 -                           | 580.43                       | 280.10                             | 08/2013 -             | 12/2015     | 28                                | -                                |
| 289  | NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir                                           | 06/2010          | 2,159.00 -                         | 2,159.00                     | -                                  | 06/2015 -             | 05/2016     | 11                                | -                                |
| 290  | QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir                 | 07/2010          | 1,987.00 -                         | 1,987.00                     | 944.00                             | 07/2015 -             | 06/2016     | 11                                | -                                |
|      | Total                                                                                        |                  | 60,272.65 -                        | 62,184.44                    | 60,083.08                          |                       |             |                                   |                                  |
|      |                                                                                              |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Shipping And Ports</u>                                                                    |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 291  | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala            | 03/2009          | 3,500.00 4,150.00                  | 4,150.00                     | 3,661.95                           | 01/2012 09/2012       | 08/2013     | 19                                | 11                               |
| 292  | Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra    | 08/2010          | 612.72 532.83                      | 532.83                       | 448.43                             | 12/2012 11/2013       | 11/2013     | 11                                | 0                                |
| 293  | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu        | 10/2002          | 150.00 309.00                      | 600.00                       | 139.80                             | 03/2006 12/2013       | 12/2013     | 93                                | 0                                |
| 294  | ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State | 01/2012          | 511.87 -                           | 511.87                       | 106.72                             | 03/2014 08/2014       | 08/2014     | 5                                 | 0                                |
| 295  | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra  | 11/2007          | 1,228.00 1,460.00                  | 1,460.00                     | 965.23                             | 12/2010 09/2012       | 12/2014     | 48                                | 27                               |
|      | Total                                                                                        |                  | 6,002.59 -                         | 7,254.70                     | 5,322.13                           |                       |             |                                   |                                  |
|      |                                                                                              |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Telecommunications</u>                                                                    |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 296  | GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh           | 11/2009          | 916.70 -                           | 930.60                       | 828.80                             | 11/2010 12/2012       | 09/2013     | 34                                | 9                                |
| 297  | Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State   | 07/2010          | 1,148.19 -                         | 964.37                       | 178.11                             | 05/2011 -             | 09/2013     | 28                                | -                                |
| 298  | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra              | 06/2006          | 231.38 -                           | 176.00                       | 86.11                              | 10/2007 -             | 12/2013     | 74                                | -                                |
| 299  | GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand             | 01/2009          | 149.15 -                           | 158.72                       | 81.73                              | 06/2009 -             | 12/2013     | 54                                | -                                |
| 300  | Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam                            | 06/2007          | 336.81 -                           | 336.81                       | 164.18                             | 01/2009 -             | 12/2013     | 59                                | -                                |

(Aug,2013)

|      |                                                                           |                  |                                    |                              |                                    | Date of Commissioning |             |                                   |                                  |
|------|---------------------------------------------------------------------------|------------------|------------------------------------|------------------------------|------------------------------------|-----------------------|-------------|-----------------------------------|----------------------------------|
| S.No | Project                                                                   | Date of Approval | Original/ Revised Cost (Rs. crore) | Anticipated Cost (Rs. crore) | Cumulative Expenditure (Rs. crore) | Original / Revised    | Anticipated | Delay w.r.t. Original (in months) | Delay w.r.t. Revised (in months) |
| 1    | 2                                                                         | 3                | 4                                  | 5                            | 6                                  | 7                     | 8           | 9                                 | 10                               |
| 301  | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State | 10/2009          | 384.00 -                           | 384.00                       | 29.45                              | 10/2010<br>03/2012    | 12/2013     | 38                                | 21                               |
|      | Total                                                                     |                  | 3,166.23 -                         | 2,950.50                     | 1,368.38                           |                       |             |                                   |                                  |
|      |                                                                           |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | <u>Urban Development</u>                                                  |                  |                                    |                              |                                    |                       |             |                                   |                                  |
| 302  | FARIDABAD EXTENSION - [N28000057]DMRC,Delhi                               | 09/2011          | 2,494.00 -                         | 2,494.00                     | 300.76                             | 09/2014<br>-          | 05/2015     | 8                                 | -                                |
|      | Total                                                                     |                  | 2,494.00 -                         | 2,494.00                     | 300.76                             |                       |             |                                   |                                  |
|      |                                                                           |                  |                                    |                              |                                    |                       |             |                                   |                                  |
|      | Grand Total                                                               |                  | 491,331.26                         | 595,539.07                   | 375,635.13                         |                       |             |                                   |                                  |

## List of ongoing projects having cost overrun w.r.t. to original schedule

| (Aug,2013) |                                                                                 |                  |                                   |                             |                       |             |                  |
|------------|---------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
|            |                                                                                 |                  |                                   |                             | Date of Commissioning |             |                  |
| S.No       | Project                                                                         | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1          | 2                                                                               | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|            |                                                                                 |                  |                                   |                             |                       |             |                  |
|            | <u>Atomic Energy</u>                                                            |                  |                                   |                             |                       |             |                  |
| 1          | KUDANKULAM APP (NPCIL)<br>- [020100040]                                         | 12/2001          | 13,171.00<br>-                    | 17,270.00                   | 12/2008<br>-          | 06/2014     | 31.12            |
| 2          | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]              | 09/2003          | 3,492.00<br>-                     | 5,677.00                    | 09/2010<br>-          | 03/2015     | 62.57            |
|            | Total                                                                           |                  | 16,663.00<br>-                    | 22,947.00                   |                       |             |                  |
|            |                                                                                 |                  |                                   |                             |                       |             |                  |
|            | <u>Civil Aviation</u>                                                           |                  |                                   |                             |                       |             |                  |
| 3          | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT<br>- [N04000037]              | 08/2008          | 1,942.51<br>-                     | 2,325.00                    | 05/2011<br>-          | 03/2013     | 19.69            |
| 4          | D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1)<br>- [N04000038] | 08/2008          | 1,808.00<br>-                     | 2,015.00                    | 01/2011<br>-          | 02/2012     | 11.45            |
|            | Total                                                                           |                  | 3,750.51<br>-                     | 27,287.00                   |                       |             |                  |
|            |                                                                                 |                  |                                   |                             |                       |             |                  |
|            | <u>Coal</u>                                                                     |                  |                                   |                             |                       |             |                  |
| 5          | TPS-II EXPANSION (1470MW TO 1970MW) (NLC)<br>- [060100087]                      | 10/2004          | 2,030.78<br>-                     | 3,027.59                    | 06/2009<br>-          | 01/2014     | 49.09            |
| 6          | MAGADH OC 20 MTY (CCL)<br>- [N06000015]                                         | 08/2008          | 469.78<br>-                       | 706.40                      | 07/2012<br>-          | 03/2016     | 50.37            |
| 7          | ADRIYALA SHAFT PROJECT<br>- [N06000016]                                         | 12/2009          | 212.34<br>-                       | 977.53                      | 03/2013<br>-          | 10/2014     | 360.36           |
| 8          | BHUBANESWARI OCP, MCL (20.0 Mty)<br>- [N06000034]                               | 12/2007          | 490.00<br>-                       | 490.10                      | 03/2017<br>-          | 03/2017     | 0.02             |
| 9          | TUTICORIN THERMAL POWER PROJECT- 2X500 MW<br>- [N06000047]                      | 05/2008          | 4,904.54<br>-                     | 6,540.93                    | 03/2012<br>-          | 03/2014     | 33.36            |
| 10         | MANIKPUR OC EXPANSION (3.5 MTY)<br>- [N06000081]                                | 12/2009          | 321.42<br>-                       | 321.50                      | 03/2014<br>-          | 03/2016     | 0.02             |
| 11         | AMLAI OC EXPANSION SECTOR B (1.50 MTY)<br>- [N06000082]                         | 11/2009          | 150.59<br>-                       | 198.59                      | 03/2016<br>-          | 03/2016     | 31.87            |
|            | Total                                                                           |                  | 8,579.45<br>-                     | 39,549.64                   |                       |             |                  |
|            |                                                                                 |                  |                                   |                             |                       |             |                  |
|            | <u>Petrochemicals</u>                                                           |                  |                                   |                             |                       |             |                  |
| 12         | Assam gas Cracker project<br>- [N16000106]                                      | 04/2006          | 5,460.61<br>-                     | 8,920.00                    | 04/2012<br>-          | 12/2013     | 63.35            |
|            | Total                                                                           |                  | 5,460.61<br>-                     | 48,469.64                   |                       |             |                  |
|            |                                                                                 |                  |                                   |                             |                       |             |                  |
|            | <u>Petroleum</u>                                                                |                  |                                   |                             |                       |             |                  |



(Aug,2013)

|      |                                                                                              |                  |                                   |                             | Date of Commissioning |             |                  |
|------|----------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                                      | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                            | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 13   | IOR LAKWA - LAKHMANI (ONGCL)<br>- [160100215                                                 | 09/2001          | 345.10<br>-                       | 750.00                      | 03/2007<br>-          | 12/2013     | 117.33           |
| 14   | IOR GELEKI (ONGCL)<br>- [160100216                                                           | 09/2001          | 390.09<br>-                       | 1,674.11                    | 03/2007<br>-          | 12/2013     | 329.16           |
| 15   | IOR, RUDRASAGAR (ONGCL)<br>- [160100217                                                      | 09/2001          | 113.90<br>-                       | 438.85                      | 03/2006<br>-          | 12/2013     | 285.29           |
| 16   | DEV OF G1 AND GS-15 (ONGCL)<br>- [160100231                                                  | 04/2003          | 429.82<br>-                       | 2,735.65                    | 04/2006<br>-          | 02/2014     | 536.46           |
| 17   | DEVELOPMENT OF C-SERIES FIELDS<br>- [N16000023                                               | 08/2006          | 3,195.16<br>-                     | 3,690.37                    | 12/2008<br>-          | 03/2014     | 15.50            |
| 18   | DEVELOPMENT OF B-22 CLUSTER FIELDS<br>- [N16000032                                           | 01/2007          | 2,323.40<br>-                     | 2,920.82                    | 09/2010<br>03/2012    | 12/2015     | 25.71            |
| 19   | DEVELOPMENT OF B-193 CLUSTER FIELDS<br>- [N16000033                                          | 06/2007          | 3,248.78<br>-                     | 5,633.44                    | 08/2010<br>03/2012    | 05/2014     | 73.40            |
| 20   | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2<br>- [N16000039                                         | 10/2007          | 5,713.03<br>-                     | 8,813.41                    | 05/2010<br>-          | 03/2014     | 54.27            |
| 21   | RESITMENT OF MARKETING INSTALATION AT VISAKH<br>- [N16000057                                 | 01/2009          | 756.00<br>-                       | 898.00                      | -<br>-                | 08/2013     | 18.78            |
| 22   | PARADIP REFINERY PROJECT<br>- [N16000058                                                     | 02/2009          | 29,777.00<br>-                    | 32,710.00                   | 11/2012<br>-          | 04/2014     | 9.85             |
| 23   | CONSTRUCTION OF NEW TERMINAL AT ENNORE<br>CHENNAI - [N16000066                               | 01/2008          | 224.00<br>-                       | 394.00                      | -<br>-                | 03/2013     | 75.89            |
| 24   | KARANPUR MORADABAD-KASHIPUR-RUDRAPUR<br>PIPELINE PROJECT PHASE-I<br>[N16000070               | 07/2009          | 238.68<br>-                       | 312.00                      | 01/2012<br>-          | 07/2013     | 30.72            |
| 25   | HYDROCRACKER REVAMP AND SETTING UP A NEW CCR<br>AT MUMBAI REFINERY - [N16000081              | 04/2008          | 825.00<br>-                       | 1,827.00                    | 04/2013<br>-          | 09/2013     | 121.45           |
| 26   | ADDITIONAL DEV. OF D-1 FIELD<br>- [N16000086                                                 | 01/2010          | 2,163.64<br>-                     | 2,331.62                    | 06/2012<br>-          | 05/2014     | 7.76             |
| 27   | Construction of six Effluent Treatment Plants (ETP),<br>Ahmedabad And Ankleswar - [N16000099 | 03/2009          | 234.78<br>234.78                  | 317.64                      | 09/2012<br>-          | 09/2013     | 35.29            |
| 28   | Development of Cluster-7 Fields<br>- [N16000104                                              | 03/2010          | 3,241.03<br>-                     | 6,638.94                    | 03/2013<br>-          | 11/2014     | 104.84           |
| 29   | Integrated Development of B-127 fields<br>- [N16000131                                       | 12/2011          | 2,059.63<br>-                     | 2,665.65                    | 03/2015<br>-          | 03/2015     | 29.42            |
| 30   | PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO<br>URAN LPG PLANT - [N16000138                | 08/2009          | 246.81<br>-                       | 276.83                      | 04/2012<br>-          | 12/2013     | 12.16            |
| 31   | MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE<br>(MHMSLPL) - [N16000146                         | 11/2012          | 666.00<br>-                       | 701.00                      | 11/2015<br>-          | 11/2015     | 5.26             |
| 32   | URAN CHAKAN/SHIKRAPUR LPG PIPELINE<br>- [N16000155                                           | 11/2012          | 309.81<br>-                       | 309.82                      | 08/2014<br>-          | 10/2014     | 0.00             |
| 33   | STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG<br>- [N16000156                                 | 01/2006          | 672.00<br>-                       | 1,038.00                    | 10/2011<br>-          | 01/2014     | 54.46            |
| 34   | STRATEGIC CRUDE OIL STORAGE PROJECT AT<br>MANGALORE - [N16000157                             | 01/2006          | 732.00<br>-                       | 1,227.00                    | 10/2011<br>-          | 12/2013     | 67.62            |
| 35   | CENTRAL GAS GATHERING STATION AND OFFTAKE<br>POINT - [N18000149                              | 08/2008          | 144.02<br>-                       | 204.29                      | 06/2012<br>-          | 12/2013     | 41.85            |

(Aug,2013)

|      |                                                                                  |                  |                                   |                             | Date of Commissioning |             |                  |
|------|----------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                          | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 36   | CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN<br>- [N18000150]                       | 08/2008          | 126.18<br>-                       | 159.54                      | 06/2012<br>-          | 03/2014     | 26.44            |
|      | Total                                                                            |                  | 58,175.86<br>-                    | 127,137.62                  |                       |             |                  |
|      |                                                                                  |                  |                                   |                             |                       |             |                  |
|      | <u>Power</u>                                                                     |                  |                                   |                             |                       |             |                  |
| 37   | PARBATI HEP (NHPC) II<br>- [180100210]                                           | 09/2002          | 3,919.59<br>-                     | 5,366.00                    | 09/2009<br>-          | 07/2018     | 36.90            |
| 38   | KOLDAM HEP (NTPC)<br>- [180100211]                                               | 10/2002          | 4,527.15<br>-                     | 6,414.56                    | 04/2009<br>-          | 09/2014     | 41.69            |
| 39   | SUBANSIRI LOWER H.E.P (NHPC)<br>- [180100221]                                    | 09/2003          | 6,285.33<br>-                     | 10,667.00                   | 09/2010<br>-          | 12/2017     | 69.71            |
| 40   | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239]                           | 12/2004          | 2,496.90<br>-                     | 5,139.00                    | 05/2013<br>05/2013    | 03/2017     | 105.82           |
| 41   | BARH STPP(3X660MW) NTPC<br>- [180100242]                                         | 12/2003          | 8,692.97<br>-                     | 8,693.00                    | 12/2009<br>-          | 02/2017     | 0.00             |
| 42   | TEESTA LOW DAM HEP, STAGE-IV (NHPC)<br>- [180100243]                             | 09/2005          | 1,061.38<br>-                     | 1,501.75                    | 09/2009<br>-          | 11/2014     | 41.49            |
| 43   | KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL)<br>- [180100246]                       | 03/2005          | 596.45<br>-                       | 1,007.16                    | 12/2007<br>-          | -           | 68.86            |
| 44   | PARBATI H.E.P. STAGE -III (NHPC)<br>- [180100250]                                | 10/2005          | 2,304.56<br>-                     | 2,716.00                    | 10/2010<br>-          | 03/2014     | 17.85            |
| 45   | URI H.E.P STAGE -II (NHPC)<br>- [180100251]                                      | 08/2005          | 1,729.29<br>-                     | 2,081.00                    | 11/2009<br>-          | 10/2013     | 20.34            |
| 46   | KUNADANKULAM APP TRANS SYSTEM (PGCIL)<br>- [180100258]                           | 05/2005          | 1,779.29<br>-                     | 2,159.07                    | 09/2008<br>-          | 03/2013     | 21.34            |
| 47   | NIMOO BAZGO HYDROELECTRIC PROJECT<br>- [N18000006]                               | 08/2006          | 611.01<br>-                       | 936.00                      | 08/2010<br>-          | 10/2013     | 53.19            |
| 48   | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N180000010]                             | 07/2006          | 1,657.00<br>-                     | 2,978.86                    | 07/2010<br>-          | 02/2017     | 79.77            |
| 49   | Tapovan-Vishnugad HEP (4x130MW)<br>- [N180000014]                                | 11/2006          | 2,978.48<br>-                     | 3,846.30                    | 03/2013<br>-          | 03/2016     | 29.14            |
| 50   | TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III<br>HEP - [N180000018]            | 07/2006          | 557.24<br>-                       | 775.25                      | 01/2010<br>-          | 07/2013     | 39.12            |
| 51   | KISHANGANGA HEP<br>- [N180000031]                                                | 07/2007          | 2,238.67<br>-                     | 3,642.00                    | 01/2016<br>-          | 11/2016     | 62.69            |
| 52   | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT<br>- [N180000042]                     | 08/2008          | 2,491.58<br>-                     | 3,745.08                    | 07/2014<br>-          | 05/2016     | 50.31            |
| 53   | PARE HYDRO ELECTRIC PROJECT<br>- [N180000045]                                    | 12/2008          | 573.99<br>-                       | 1,117.92                    | 08/2012<br>-          | 09/2014     | 94.76            |
| 54   | MOUDA STPP<br>- [N180000048]                                                     | 11/2008          | 5,459.28<br>-                     | 6,010.89                    | 08/2012<br>-          | 03/2013     | 10.10            |
| 55   | SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH<br>DVC AND MAITHON RBC - [N180000065] | 08/2008          | 2,360.95<br>-                     | 2,580.90                    | 08/2012<br>-          | 03/2014     | 9.32             |
| 56   | TRIPURA GAS BASED POWER PROJECT<br>- [N180000071]                                | 07/2009          | 421.01<br>-                       | 960.79                      | -<br>-                | 05/2014     | 128.21           |

(Aug,2013)

|      |                                                                                         |                  |                                   |                             | Date of Commissioning |             |                  |
|------|-----------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                                 | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                       | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|      | Total                                                                                   |                  | 52,742.12<br>-                    | 199,476.15                  |                       |             |                  |
|      |                                                                                         |                  |                                   |                             |                       |             |                  |
|      | <u>Railways</u>                                                                         |                  |                                   |                             |                       |             |                  |
| 57   | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)<br>- [220100007                       | 04/1986          | 158.77<br>274.56                  | 580.83                      | 03/1994<br>-          | 10/2013     | 265.83           |
| 58   | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)<br>- [220100009                            | 03/1984          | 520.00<br>422.79                  | 835.04                      | 03/1995<br>-          | 03/2015     | 60.58            |
| 59   | VIRAMGAM-BHILDI(WR),GC<br>- [220100062                                                  | 04/1990          | 155.66<br>-                       | 548.01                      | -<br>03/2010          | -           | 252.06           |
| 60   | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)<br>- [220100106                                  | 12/1994          | 124.43<br>-                       | 925.30                      | -<br>-                | 03/2012     | 643.63           |
| 61   | AMRAVATI-NARKHER NL(CR)<br>- [220100118                                                 | 06/1994          | 120.90<br>175.30                  | 725.00                      | 06/1999<br>-          | 03/2011     | 499.67           |
| 62   | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR<br>- [220100133                                     | 03/1995          | 2,500.00<br>-                     | 20,000.00                   | 11/2002<br>-          | 12/2017     | 700.00           |
| 63   | New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR<br>- [220100135 | 04/1983          | 36.80<br>274.41                   | 703.17                      | -<br>-                | 03/2015     | 1,810.79         |
| 64   | LANJHIGARH-JUNAGARH NL(ECOR)<br>- [220100148                                            | 04/1993          | 100.00<br>119.29                  | 227.94                      | 03/2002<br>-          | 09/2013     | 127.94           |
| 65   | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL<br>- [220100149        | 04/1995          | 304.00<br>-                       | 968.60                      | 12/2012<br>-          | -           | 218.62           |
| 66   | CALICUT-MANGALORE (DL) (SR)<br>- [220100151                                             | 02/1996          | 240.00<br>-                       | 579.37                      | -<br>-                | 02/2012     | 141.40           |
| 67   | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)<br>- [220100164                       | 03/1996          | 401.81<br>-                       | 1,814.48                    | 03/2004<br>-          | 12/2014     | 351.58           |
| 68   | MANDARHILL-DUMKA-RAMPURHAT (NL),ER<br>- [220100168                                      | 04/1995          | 184.00<br>-                       | 900.05                      | 12/2011<br>12/2010    | 03/2013     | 389.16           |
| 69   | AHMEDNAGAR-PARLI VAIJNATH(NL) CR<br>- [220100181                                        | 02/1997          | 353.08<br>-                       | 2,820.00                    | -<br>-                | -           | 698.69           |
| 70   | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR<br>[220100183                             | 02/1997          | 295.00<br>-                       | 412.91                      | -<br>-                | 01/2013     | 39.97            |
| 71   | DAUSA-GANGAPUR CITY(NL),NWR<br>- [220100184                                             | 02/1997          | 151.84<br>-                       | 410.08                      | -<br>-                | 03/2014     | 170.07           |
| 72   | GONDIA-JABALPUR(GC),(SECR)<br>- [220100186                                              | 02/1997          | 386.30<br>-                       | 1,038.00                    | 03/1998<br>-          | -           | 168.70           |
| 73   | NANGALDAM-TALWARA(NL),NR<br>- [220100188                                                | 03/1981          | 37.68<br>-                        | 1,036.78                    | 07/2012<br>-          | -           | 2,651.54         |
| 74   | KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)<br>- [220100190                                 | 04/1996          | 157.00<br>-                       | 333.50                      | 03/2012<br>-          | 03/2013     | 112.42           |
| 75   | KARUR-SALEM(NL),SR<br>- [220100191                                                      | 02/1997          | 155.55<br>-                       | 775.36                      | -<br>-                | 10/2012     | 398.46           |
| 76   | NANDYAL-YERRAGUNTALA(NL),SCR<br>- [220100192                                            | 03/1996          | 155.74<br>164.36                  | 883.00                      | 02/2009<br>-          | 03/2012     | 466.97           |
| 77   | HUBLI-ANKOLA(NL),SWR<br>- [220100193                                                    | 04/1997          | 227.00<br>-                       | 2,135.00                    | -<br>-                | -           | 840.53           |

(Aug,2013)

|      |                                                                           |                  |                                   |                             | Date of Commissioning |             |                  |
|------|---------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                   | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                         | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 78   | KANPUR-KASGANJ-MATHURA(GC),NER<br>- [220100197                            | 03/1997          | 395.00<br>598.98                  | 1,708.41                    | -<br>-                | 03/2013     | 332.51           |
| 79   | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR<br>- [220100201              | 09/1997          | 1,000.00<br>-                     | 4,996.19                    | 04/2008<br>12/2011    | 12/2015     | 399.62           |
| 80   | MUNEERABAD-MAHABOBNAGAR(NL),SCR<br>- [220100205                           | 04/1997          | 218.24<br>236.41                  | 645.00                      | -<br>-                | 03/2012     | 195.55           |
| 81   | HOWRAH-AMTA-CHAMPADANGA NL (SER)<br>- [220100208                          | 04/1974          | 31.42<br>154.30                   | 535.40                      | 03/2007<br>03/2007    | 03/2015     | 1,604.01         |
| 82   | KOTTUR-HARIHAR(NL),(SWR)<br>- [220100212                                  | 04/1995          | 65.94<br>-                        | 302.23                      | -<br>-                | 12/2012     | 358.34           |
| 83   | RANCHI-LOHARDAGA(GC),SER<br>- [220100214                                  | 04/1997          | 194.07<br>-                       | 596.00                      | 06/2004<br>-          | 12/2012     | 207.11           |
| 84   | MACHERLA-NALGONDA(NL)(SCR)<br>- [220100220                                | 07/1998          | 125.00<br>-                       | 480.00                      | 07/2008<br>-          | 07/2008     | 284.00           |
| 85   | KODERMA-RANCHI VIA BARKAKANA (NL),ECR<br>- [220100222                     | 03/1999          | 491.19<br>-                       | 2,957.21                    | 07/2005<br>-          | -           | 502.05           |
| 86   | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)<br>- [220100232                    | 09/1998          | 925.00<br>-                       | 1,630.97                    | 05/2008<br>-          | -           | 76.32            |
| 87   | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR<br>- [220100240                 | 04/1997          | 233.00<br>335.77                  | 1,043.56                    | 03/2012<br>-          | -           | 347.88           |
| 88   | CHANDIGARH-LUDHIANA(NEW BG LINE),NR<br>- [220100241                       | 07/1998          | 248.44<br>-                       | 1,115.21                    | 12/2012<br>-          | 04/2013     | 348.89           |
| 89   | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR<br>- [220100243                | 04/1999          | 108.00<br>-                       | 432.72                      | 12/2009<br>-          | 10/2013     | 300.67           |
| 90   | KATIHAR - JOGBANI (GC)(NEFR)<br>- [220100247                              | 09/2001          | 100.00<br>-                       | 1,041.79                    | 12/2010<br>-          | 03/2015     | 941.79           |
| 91   | ANGAMALI-SABARIMALA (N.L.)(SR)<br>- [220100252                            | 10/1998          | 550.00<br>-                       | 1,566.00                    | -<br>-                | -           | 184.73           |
| 92   | GULBARGA-BIDAR,SCR(NL)<br>- [220100254                                    | 02/1998          | 242.42<br>369.70                  | 832.00                      | -<br>05/2009          | 05/2009     | 243.21           |
| 93   | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-<br>NAUTANWA GC (NER)<br>[220100255 | 03/2002          | 381.17<br>-                       | 863.23                      | -<br>-                | 03/2012     | 126.47           |
| 94   | KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)<br>- [220100256                   | 04/1999          | 323.40<br>-                       | 744.71                      | -<br>-                | 03/2014     | 130.28           |
| 95   | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)<br>- [220100257                     | 04/1997          | 78.23<br>-                        | 162.87                      | -<br>-                | -           | 108.19           |
| 96   | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR<br>- [220100258                    | 03/2002          | 409.00<br>408.76                  | 847.75                      | 06/2007<br>-          | 06/2007     | 107.27           |
| 97   | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)<br>- [220100262                   | 09/1995          | 100.00<br>-                       | 800.00                      | -<br>-                | -           | 700.00           |
| 98   | QUILON-TIRUNELVELI-TENKASI-<br>VIRUDHUNAGAR(SR)(GC)<br>[220100263         | 03/1998          | 280.00<br>-                       | 1,029.92                    | -<br>-                | 03/2013     | 267.83           |
| 99   | KOTLPALLI-NARASAPUR (NL) (SCR)<br>- [220100265                            | 12/2001          | 330.00<br>-                       | 1,045.20                    | -<br>-                | -           | 216.73           |
| 100  | NEW MAYNAGURI TO JOGIGHOPA VIA<br>CHANGRABANDHA (NL),NEFR<br>- [220100266 | 04/2000          | 733.00<br>-                       | 2,350.00                    | 12/2008<br>-          | 03/2015     | 220.60           |

(Aug,2013)

|      |                                                                                              |                  |                                   |                             | Date of Commissioning |             |                  |
|------|----------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                                      | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                            | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 101  | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268 | 03/2000          | 907.69                            | 3,176.10                    | 12/2006               | 08/2010     | 249.91           |
| 102  | GADWAL - RAICHUR (NL), SCR - [220100270                                                      | 04/1998          | 92.63                             | 270.00                      | 02/2011               | 03/2013     | 191.48           |
| 103  | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272                                     | 04/2000          | 157.96                            | 1,188.91                    | -<br>12/2009          | 02/2012     | 652.67           |
| 104  | DEOGHAR - SULTANGANJ (INL), ER - [220100273                                                  | 04/2000          | 138.00<br>240.59                  | 607.09                      | 12/2012<br>12/2012    | 02/2013     | 339.92           |
| 105  | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274                                              | 02/1999          | 138.00                            | 901.62                      | -<br>-                | -           | 553.35           |
| 106  | BANKURA - DAMODAR (GC) (SER) - [220100277                                                    | 03/1998          | 111.90                            | 1,423.98                    | 03/2005<br>12/2008    | 12/2016     | 1,172.55         |
| 107  | JIND-SONEPAT (NL),NR - [220100280                                                            | 01/2004          | 190.81                            | 693.39                      | 03/2012               | 12/2012     | 263.39           |
| 108  | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284                                                    | 04/1994          | 355.38                            | 1,995.25                    | -<br>-                | 03/2014     | 461.44           |
| 109  | HARIDASPUR-PARADEEP(NL) - [220100285                                                         | 04/1996          | 301.64                            | 1,185.64                    | -<br>09/2009          | -           | 293.06           |
| 110  | RAJATGARH-BARANG(LD),ECOR - [220100286                                                       | 04/1999          | 166.16                            | 288.00                      | 02/2009<br>02/2009    | 08/2014     | 73.33            |
| 111  | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288                                             | 04/2003          | 727.56                            | 4,453.50                    | 03/2011               | 03/2017     | 512.11           |
| 112  | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303                                          | 04/2003          | 324.66                            | 528.65                      | -<br>-                | -           | 62.83            |
| 113  | KOSI BRIDGE (NL), ECR - [220100304                                                           | 04/2002          | 323.41                            | 341.41                      | 03/2012               | 03/2013     | 5.57             |
| 114  | KODERMA GIRIDH (NL), ECR - [220100306                                                        | 04/1996          | 371.36                            | 768.87                      | -<br>-                | 03/2010     | 107.04           |
| 115  | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307                                        | 04/2002          | 921.00                            | 2,363.00                    | 03/2009               | 12/2014     | 156.57           |
| 116  | PATNA GANGA BRIDGE (NL), ECR - [220100308                                                    | 04/2001          | 624.47                            | 2,921.00                    | 10/2007               | 12/2015     | 367.76           |
| 117  | DANIWAN-BIHARSARIF (NL), ECR - [220100311                                                    | 04/2001          | 104.79                            | 406.92                      | -<br>-                | -           | 288.32           |
| 118  | RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314                                                    | 04/2001          | 727.13<br>727.13                  | 1,225.90                    | -<br>-                | -           | 68.59            |
| 119  | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315                        | 01/2004          | 915.70                            | 3,019.17                    | -<br>-                | 03/2014     | 229.71           |
| 120  | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316                                                  | 04/2003          | 218.19                            | 472.00                      | -<br>-                | 02/2013     | 116.33           |
| 121  | ETAWAH-MAINPURI (NL),NCR - [220100318                                                        | 09/2001          | 129.70                            | 245.39                      | 12/2008               | 09/2014     | 89.20            |
| 122  | RUPSA-BANGRIPOSI (GC)(SER) - [220100323                                                      | 02/1996          | 57.94                             | 639.97                      | 03/1998<br>08/2005    | 08/2005     | 1,004.54         |
| 123  | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324                                                  | 04/2005          | 383.79                            | 585.93                      | -<br>-                | 12/2013     | 52.67            |
| 124  | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325                                                 | 04/1998          | 183.23                            | 818.29                      | 02/2015               | 02/2015     | 346.59           |

(Aug,2013)

|      |                                                                                     |                  |                                   |                             | Date of Commissioning |             |                  |
|------|-------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                             | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                   | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 125  | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [N220100327                          | 04/2000          | 133.41<br>207.00                  | 276.00                      | 03/2009<br>03/2009    | 08/2014     | 106.88           |
| 126  | TALCHER-BIMALAGARH(NL)(ECOR)<br>- [N220100328                                       | 04/2005          | 726.96<br>-                       | 810.78                      | -<br>-                | -           | 11.53            |
| 127  | RAICHUR-GUNTAKAL(DL)(SCR)<br>- [N220100329                                          | 04/2003          | 136.62<br>-                       | 289.93                      | 12/2007<br>03/2010    | -           | 112.22           |
| 128  | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN<br>ECR<br>- [N220000002               | 04/1996          | 114.01<br>283.95                  | 477.88                      | 03/2012<br>-          | 03/2013     | 319.16           |
| 129  | MANOHARABAD-KOTHPALL NEW LINE(SCR)<br>- [N220000032                                 | 04/2006          | 378.56<br>-                       | 791.59                      | -<br>-                | -           | 109.11           |
| 130  | GOELKERA-MANOHARPUR,(LD)(SER)<br>- [N220000045                                      | 03/1997          | 186.92<br>-                       | 261.70                      | 02/2006<br>-          | -           | 40.01            |
| 131  | OBULAVARIPALLE-KRISHNAPATNAM(RVNL)<br>- [N220000049                                 | 07/2006          | 743.00<br>-                       | 1,117.11                    | 03/2008<br>06/2008    | -           | 50.35            |
| 132  | HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50<br>COAC. WS and PU<br>- [N220000052   | 04/2003          | 98.74<br>-                        | 337.30                      | -<br>-                | 03/2012     | 241.60           |
| 133  | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING<br>PLANT<br>- [N220000053                 | 03/2005          | 470.09<br>-                       | 1,417.97                    | -<br>-                | 03/2012     | 201.64           |
| 134  | SALKA ROAD -ANUPNAGAR LINE DOUBLING<br>- [N220000075                                | 09/2006          | 324.90<br>-                       | 385.54                      | 03/2010<br>-          | -           | 18.66            |
| 135  | BHOPAL BINA 3D LINE DOUBLING<br>- [N220000077                                       | 09/2007          | 687.20<br>-                       | 800.00                      | 03/2010<br>-          | 12/2015     | 16.41            |
| 136  | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU<br>'PONDI'-AGASTIYAMPALLI<br>[N220000079   | 09/2007          | 404.19<br>-                       | 1,383.45                    | -<br>-                | -           | 242.28           |
| 137  | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND<br>COIMBATORE<br>- [N220000080               | 09/2006          | 343.17<br>-                       | 914.98                      | -<br>-                | 12/2012     | 166.63           |
| 138  | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA,<br>NEFR<br>- [N220000082              | 12/2006          | 170.00<br>-                       | 435.87                      | 03/2011<br>-          | 03/2011     | 156.39           |
| 139  | CONSTRUCTION OF NEW LINE FROM HARMATI-<br>ITANAGAR/NARHARIAGUN, NEFR<br>[N220000083 | 09/1996          | 156.00<br>-                       | 406.40                      | -<br>-                | 12/2013     | 160.51           |
| 140  | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)<br>- [N220000084                              | 09/2006          | 125.00<br>-                       | 227.40                      | -<br>-                | -           | 81.92            |
| 141  | TIDIVANAM-NAGARI (NL)<br>- [N220000085                                              | 09/2006          | 456.00<br>-                       | 582.83                      | -<br>-                | -           | 27.81            |
| 142  | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL<br>PROJECT), NEFR<br>- [N220000086 | 09/2006          | 200.00<br>-                       | 385.20                      | -<br>-                | 03/2015     | 92.60            |
| 143  | NEW B.G. LINE FROM ARARIA TO GALGALIA<br>(THAKURGUNG), NEFR<br>[N220000087          | 09/2006          | 300.00<br>-                       | 532.87                      | -<br>-                | -           | 77.62            |
| 144  | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)<br>- [N220000088                               | 04/2006          | 325.00<br>-                       | 1,116.53                    | 03/2010<br>-          | 03/2017     | 243.55           |
| 145  | BARDHAMAN-KATWA (GC)<br>- [N220000091                                               | 04/2007          | 245.15<br>-                       | 1,106.62                    | 12/2010<br>-          | 03/2011     | 351.41           |
| 146  | MUMBAI URBAN TRANSPORT PROJECT PHASE-II<br>- [N220000092                            | 04/2008          | 5,300.00<br>-                     | 6,220.15                    | 03/2014<br>-          | 12/2016     | 17.36            |
| 147  | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR<br>AND G'BAD-MEERUT<br>- [N220000094    | 02/2008          | 171.10<br>-                       | 246.44                      | 03/2012<br>-          | 03/2014     | 44.03            |

(Aug,2013)

|      |                                                                                                                  |                  |                                   |                             | Date of Commissioning |             |                  |
|------|------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                                                          | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                                                | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 148  | TAMLUK DIGHA,LINE DOUBLING (SER)<br>- [N22000097]                                                                | 03/1984          | 293.97<br>-                       | 1,074.47                    | 06/2005<br>-          | 06/2016     | 265.50           |
| 149  | AGARTALA SABROOM, NL, NEFR<br>- [N22000099]                                                                      | 04/2008          | 813.34<br>-                       | 1,741.00                    | 03/2014<br>-          | 12/2015     | 114.06           |
| 150  | BHAIRABI SAIRONG, NL, NEFR<br>- [N22000100]                                                                      | 04/2008          | 619.34<br>-                       | 2,384.34                    | 04/2014<br>-          | 03/2017     | 284.98           |
| 151  | KISHANGANJ JALALGARH, NL, NEFR<br>- [N22000101]                                                                  | 04/2008          | 282.92<br>-                       | 359.86                      | -<br>-                | 03/2015     | 27.20            |
| 152  | SEVOK RANGPO, NEFR<br>- [N22000102]                                                                              | 04/2008          | 1,339.48<br>-                     | 3,380.58                    | 12/2015<br>-          | 03/2017     | 152.38           |
| 153  | Ramanagram-Mysore doubling with electrification of Kengesil-Musore (SWR)<br>- [N22000107]                        | 04/2007          | 482.00<br>-                       | 482.70                      | 03/2013<br>-          | 03/2014     | 0.15             |
| 154  | New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP)<br>- [N22000109] | 04/2010          | 2,069.60<br>-                     | 2,298.42                    | 03/2014<br>-          | 03/2014     | 11.06            |
| 155  | New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.<br>- [N22000111]                | 04/2010          | 2,619.02<br>-                     | 2,913.51                    | 03/2016<br>-          | 03/2016     | 11.24            |
| 156  | Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR)<br>- [N22000113]                               | 04/2008          | 653.19<br>-                       | 653.47                      | 03/2014<br>-          | 03/2014     | 0.04             |
| 157  | Dakshin-barasal-lakshmikantapur<br>- [N22000116]                                                                 | 04/2009          | 259.51<br>-                       | 533.38                      | 12/2011<br>-          | 02/2012     | 105.53           |
| 158  | Ghutiasharif-Canning (ER)<br>- [N22000117]                                                                       | 04/2009          | 189.97<br>-                       | 611.03                      | 12/2011<br>-          | 11/2013     | 221.65           |
| 159  | Pandabeswar-Chinpai doubling (ER)<br>- [N22000118]                                                               | 04/2004          | 225.68<br>-                       | 293.74                      | 12/2010<br>-          | 12/2010     | 30.16            |
| 160  | Ratlam-Mhow-Khandwa-Akola (GC)<br>- [N22000120]                                                                  | 04/2008          | 603.04<br>-                       | 1,421.25                    | 03/2012<br>-          | -           | 135.68           |
| 161  | Ahmedabad-Himmatnagar-Udaipur (WR)<br>- [N22000121]                                                              | 04/2008          | 394.14<br>-                       | 1,215.30                    | 03/2013<br>-          | 03/2013     | 208.34           |
| 162  | New Line from Dimapur to Zubza(Kohima) national project (NEFR)<br>- [N22000124]                                  | 04/2006          | 850.00<br>-                       | 2,441.48                    | 03/2015<br>-          | 03/2017     | 187.23           |
| 163  | Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR)<br>- [N22000125]                              | 04/2006          | 117.36<br>196.95                  | 196.95                      | 03/2011<br>-          | -           | 67.82            |
| 164  | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project<br>- [N22000127]                          | 04/1996          | 1,676.31<br>-                     | 5,000.00                    | 03/2009<br>-          | 12/2014     | 198.27           |
| 165  | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP<br>- [N22000133]                                                          | 03/2012          | 160.89<br>-                       | 199.75                      | -<br>-                | -           | 24.15            |
| 166  | Virangam-Samakhiali (DL)<br>- [N22000145]                                                                        | 04/2011          | 446.00<br>-                       | 685.17                      | -<br>-                | -           | 53.63            |
| 167  | Gwalior-Seopurkala with extension to Kota (GC)<br>- [N22000148]                                                  | 04/2011          | 1,176.09<br>-                     | 3,845.60                    | 02/2020<br>-          | 02/2020     | 226.98           |
| 168  | Thiyat Hamira-Sanu<br>- [N22000149]                                                                              | 04/2013          | 236.39<br>-                       | 236.93                      | -<br>-                | -           | 0.23             |
| 169  | Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur<br>- [N22000152]                                         | 04/2013          | 456.00<br>-                       | 965.16                      | -<br>-                | -           | 111.66           |
| 170  | Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC)<br>- [N22000153]                          | 04/2010          | 739.65<br>-                       | 872.22                      | -<br>-                | -           | 17.92            |
| 171  | Ajmer-Bangurgram<br>- [N22000155]                                                                                | 04/2011          | 213.39<br>-                       | 218.39                      | -<br>-                | -           | 2.34             |

(Aug,2013)

|      |                                                                                                                     |                  |                                   |                             | Date of Commissioning |             |                  |
|------|---------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                                                             | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                                                   | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 172  | Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]           | 04/2010          | 622.41<br>-                       | 2,030.50                    | 02/2019<br>-          | 02/2019     | 226.23           |
| 173  | Digha-Jaleswar including MM for Digha-Egra - [N22000160]                                                            | 04/2010          | 553.63<br>-                       | 651.17                      | -<br>-                | -           | 17.62            |
| 174  | Champajharan-Bimalgarh Doubling extension - [N22000162]                                                             | 04/2010          | 149.90<br>-                       | 177.38                      | 03/2015<br>-          | 12/2015     | 18.33            |
| 175  | Tamluk-Basulya-Sutahata Doubling - [N22000163]                                                                      | 04/2010          | 146.95<br>-                       | 171.02                      | 06/2013<br>-          | -           | 16.38            |
| 176  | Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]                                                              | 04/2010          | 309.44<br>-                       | 388.67                      | 12/2015<br>-          | 12/2015     | 25.60            |
| 177  | Sakri-Hasanpur Road (NL) - [N22000171]                                                                              | 04/1999          | 175.69<br>-                       | 325.00                      | -<br>-                | -           | 84.98            |
| 178  | Chhapra-Muzaffarpur (NL) - [N22000172]                                                                              | 04/2006          | 285.07<br>-                       | 378.56                      | -<br>-                | -           | 32.80            |
| 179  | Attippattu-Puttur - [N22000184]                                                                                     | 04/2008          | 446.87<br>-                       | 527.00                      | -<br>-                | -           | 17.93            |
| 180  | Chennai-Cuddalore via Mamallapuram - [N22000185]                                                                    | 04/2008          | 523.52<br>-                       | 1,200.00                    | -<br>-                | -           | 129.22           |
| 181  | Cuddalore-Salem via Vriddhachalam GC - [N22000187]                                                                  | 04/1999          | 198.68<br>-                       | 556.64                      | -<br>-                | -           | 180.17           |
| 182  | Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]                                                       | 04/1999          | 271.24<br>-                       | 520.00                      | -<br>-                | -           | 91.71            |
| 183  | Villupuram-Dindigul with Electrification - [N22000189]                                                              | 04/2008          | 822.39<br>-                       | 1,280.83                    | -<br>-                | -           | 55.74            |
| 184  | New BG line from Dudhnoi-Mendipatar - [N22000192]                                                                   | 04/1999          | 175.43<br>-                       | 247.75                      | -<br>-                | 03/2014     | 41.22            |
| 185  | Construction of NL from Kumarghat-Agartala - [N22000194]                                                            | 04/1999          | 895.00<br>-                       | 1,151.00                    | 03/2007<br>-          | 03/2015     | 28.60            |
| 186  | Erode-Palani - [N22000199]                                                                                          | 04/2008          | 288.57<br>-                       | 603.22                      | -<br>-                | -           | 109.04           |
| 187  | Madurai-Bodinayakanur - [N22000201]                                                                                 | 04/2008          | 164.41<br>-                       | 260.72                      | -<br>-                | -           | 58.58            |
| 188  | Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif - [N22000202] | 04/2007          | 247.00<br>-                       | 951.24                      | -<br>-                | -           | 285.12           |
| 189  | New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai - [N22000209]  | 04/1999          | 523.17<br>-                       | 1,393.44                    | -<br>-                | -           | 166.35           |
| 190  | Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Phase-II - [N22000213]                                     | 04/2012          | 632.68<br>-                       | 816.55                      | 04/2012<br>-          | -           | 29.06            |
| 191  | Madurai-Tuticorin via Aruppukkottai - [N22000215]                                                                   | 04/2011          | 601.43<br>-                       | 800.00                      | -<br>-                | -           | 33.02            |
| 192  | Wardha-Nanded Maharashtra - [N22000231]                                                                             | 04/2008          | 697.00<br>-                       | 1,604.00                    | -<br>-                | -           | 130.13           |
| 193  | Munirabad (gingera) -Raichur NL - [N22000257]                                                                       | 04/2007          | 179.65<br>-                       | 645.00                      | -<br>-                | -           | 259.03           |
| 194  | Akola-Khandwa GC Akola-Akot - [N22000263]                                                                           | 04/2008          | 184.26<br>-                       | 2,000.00                    | -<br>-                | -           | 985.42           |



(Aug,2013)

|      |                                                                                                         |                  |                                   |                             | Date of Commissioning |              |                  |
|------|---------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|--------------|------------------|
| S.No | Project                                                                                                 | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated  | Cost Overrun (%) |
| 1    | 2                                                                                                       | 3                | 4                                 | 5                           | 6                     | 7            | 8                |
| 195  | Bhanupali-Bilaspur Beri NL<br>- [N22000273                                                              | 04/2008          | 1,046.88<br>-                     | 2,966.99<br>-               | -<br>-                | -<br>-       | 183.41           |
| 196  | Haridwar-Laksar<br>- [N22000289                                                                         | 04/2012          | 219.83<br>-                       | 444.18<br>-                 | -<br>-                | -<br>-       | 102.06           |
|      | Total                                                                                                   |                  | 62,375.58<br>-                    | 373,015.02<br>-             |                       |              |                  |
|      |                                                                                                         |                  |                                   |                             |                       |              |                  |
|      | <u>Road Transport And Highways</u>                                                                      |                  |                                   |                             |                       |              |                  |
| 197  | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)<br>- [240101153                                              | 04/2000          | 225.00<br>-                       | 241.53<br>-                 | 04/2004<br>-          | 09/2013<br>- | 7.35             |
| 198  | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25,<br>KM.75-80.06<br>- [240106221                            | 12/2003          | 155.00<br>-                       | 201.66<br>-                 | 09/2008<br>-          | 03/2014<br>- | 30.10            |
| 199  | VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A<br>KM.50 TO KM.80<br>- [240106236                          | 12/2003          | 166.27<br>-                       | 193.10<br>-                 | 03/2008<br>-          | 02/2008<br>- | 16.14            |
| 200  | PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A<br>- [240106237                                            | 12/2003          | 284.00<br>-                       | 359.00<br>-                 | 05/2008<br>-          | 09/2013<br>- | 26.41            |
| 201  | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000<br>- [240106278                                     | 12/2003          | 199.81<br>-                       | 385.13<br>-                 | 04/2009<br>-          | 12/2014<br>- | 92.75            |
| 202  | MAIBANG TO LUNDING (AS-24), KM.111.000 TO<br>KM.126.450<br>- [240106280                                 | 12/2003          | 155.04<br>-                       | 280.13<br>-                 | 11/2008<br>-          | 06/2014<br>- | 80.68            |
| 203  | HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54<br>- [N24000061                                           | 12/2003          | 212.00<br>-                       | 386.10<br>-                 | 09/2007<br>-          | 04/2014<br>- | 82.12            |
| 204  | HARANGAJO TO MAIBANG, NH-54<br>- [N24000062                                                             | 12/2003          | 196.00<br>-                       | 363.74<br>-                 | 07/2009<br>-          | 05/2014<br>- | 85.58            |
| 205  | CHAMBAL BRIDGE, NH-76 (RJ-5)<br>- [N24000068                                                            | 12/2003          | 275.00<br>-                       | 281.31<br>-                 | 02/2010<br>-          | 06/2015<br>- | 2.29             |
| 206  | AGRA-BYPASS(NS-1/UP-1), NH-2,3<br>- [N24000098                                                          | 12/2003          | 348.16<br>-                       | 465.50<br>-                 | 09/2007<br>-          | 03/2014<br>- | 33.70            |
| 207  | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)<br>- [N24000133                                             | 05/2009          | 1,108.00<br>-                     | 2,288.00<br>-               | 11/2011<br>-          | 12/2013<br>- | 106.50           |
|      | Total                                                                                                   |                  | 3,324.28<br>-                     | 378,460.22<br>-             |                       |              |                  |
|      |                                                                                                         |                  |                                   |                             |                       |              |                  |
|      | <u>Shipping And Ports</u>                                                                               |                  |                                   |                             |                       |              |                  |
| 208  | DEEPENING AND WIDENING OF MUMBAI HARBOUR<br>CHANNEL AND JNPT CHANNEL<br>- [N25000003                    | 10/2005          | 800.00<br>-                       | 1,571.60<br>-               | 10/2008<br>-          | -<br>-       | 96.45            |
| 209  | DEEPENING OF CHANNEL AT PARADIP PORT<br>- [N25000004                                                    | 12/2005          | 154.84<br>-                       | 253.36<br>-                 | -<br>01/2009          | 12/2010<br>- | 63.63            |
| 210  | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS &<br>TERMINAL<br>- [N25000016                              | 11/2007          | 1,228.00<br>-                     | 1,460.00<br>-               | 12/2010<br>-          | 12/2014<br>- | 18.89            |
| 211  | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE<br>VEHICLE (SPV)<br>- [N25000035                          | 10/2002          | 150.00<br>-                       | 600.00<br>-                 | 03/2006<br>-          | 12/2013<br>- | 300.00           |
| 212  | Construction of berthing and allied facilities off Tekra near<br>Tuna,Kandla Port Trust<br>- [N25000037 | 04/2005          | 882.00<br>-                       | 1,060.00<br>-               | 02/2011<br>-          | 12/2012<br>- | 20.18            |
| 213  | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA<br>- [N25000039                                           | 12/2005          | 702.00<br>-                       | 755.50<br>-                 | 03/2011<br>-          | 03/2013<br>- | 7.62             |

(Aug,2013)

|      |                                                                                                                   |                  |                                   |                             | Date of Commissioning |             |                  |
|------|-------------------------------------------------------------------------------------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                                                                                                           | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                                                                                                 | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
| 214  | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]                                     | 03/2009          | 3,500.00 -                        | 4,150.00                    | 01/2012 -             | 08/2013     | 18.57            |
| 215  | Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053] | 10/2010          | 966.46 -                          | 994.82                      | 02/2014 -             | 02/2014     | 2.93             |
| 216  | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]                                       | 03/2007          | 245.67 -                          | 373.22                      | 04/2009 -             | 02/2011     | 51.92            |
|      | Total                                                                                                             |                  | 8,628.97 -                        | 389,678.72                  |                       |             |                  |
|      |                                                                                                                   |                  |                                   |                             |                       |             |                  |
|      | <u>Steel</u>                                                                                                      |                  |                                   |                             |                       |             |                  |
| 217  | EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]                                         | 10/2005          | 8,692.00 -                        | 12,291.00                   | 10/2009 -             | 09/2013     | 41.41            |
| 218  | Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]                                                      | 01/2007          | 295.89 -                          | 607.17                      | 12/2011 06/2010       | 12/2013     | 105.20           |
| 219  | COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]                                                                    | 08/2007          | 108.00 -                          | 216.68                      | 10/2012 -             | 12/2013     | 100.63           |
| 220  | EXPANSION OF IISCO STEEL PLANT - [N12000051]                                                                      | 02/2008          | 14,443.00 -                       | 16,408.00                   | 12/2011 -             | 12/2013     | 13.61            |
| 221  | 67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]                                       | 07/2007          | 230.00 -                          | 343.58                      | 02/2011 -             | 09/2013     | 49.38            |
| 222  | 330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]                                                               | 07/2007          | 260.00 -                          | 349.64                      | 08/2010 -             | 06/2013     | 34.48            |
|      | Total                                                                                                             |                  | 24,028.89 -                       | 419,894.79                  |                       |             |                  |
|      |                                                                                                                   |                  |                                   |                             |                       |             |                  |
|      | <u>Telecommunications</u>                                                                                         |                  |                                   |                             |                       |             |                  |
| 223  | GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]                               | 01/2009          | 149.15 -                          | 158.72                      | 06/2009 -             | 12/2013     | 6.42             |
| 224  | GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]               | 03/2008          | 328.13 -                          | 392.13                      | 03/2009 -             | 01/2013     | 19.50            |
| 225  | GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]                    | 11/2009          | 916.70 -                          | 930.60                      | 11/2010 -             | 09/2013     | 1.52             |
|      | Total                                                                                                             |                  | 1,393.98 -                        | 421,376.24                  |                       |             |                  |
|      |                                                                                                                   |                  |                                   |                             |                       |             |                  |
|      | <u>Urban Development</u>                                                                                          |                  |                                   |                             |                       |             |                  |
| 226  | BANGALORE METRO RAIL PROJECT - [N28000008]                                                                        | 05/2006          | 6,395.00 -                        | 11,609.00                   | 06/2011 -             | 03/2013     | 81.53            |
| 227  | C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048]                                         | 11/2006          | 114.18 173.08                     | 173.08                      | 04/2009 -             | -           | 51.59            |
|      | Total                                                                                                             |                  | 6,509.18 -                        | 433,158.32                  |                       |             |                  |
|      |                                                                                                                   |                  |                                   |                             |                       |             |                  |

(Aug,2013)

|      |                                       |                  |                                   |                             | Date of Commissioning |             |                  |
|------|---------------------------------------|------------------|-----------------------------------|-----------------------------|-----------------------|-------------|------------------|
| S.No | Project                               | Date of Approval | Original / Revised Cost(Rs crore) | Anticipated Cost (Rs.crore) | Original/ Revised     | Anticipated | Cost Overrun (%) |
| 1    | 2                                     | 3                | 4                                 | 5                           | 6                     | 7           | 8                |
|      | <u>Water Resources</u>                |                  |                                   |                             |                       |             |                  |
| 228  | PAGLADIYA DAM PROJECT<br>- [300100001 | 01/2001          | 542.90<br>-                       | 1,187.00                    | 12/2007<br>-          | 12/2012     | 118.64           |
|      | Total                                 |                  | 542.90<br>-                       | 434,345.32                  |                       |             |                  |
|      |                                       |                  |                                   |                             |                       |             |                  |
|      | Grand Total                           |                  | 252,175.33                        | 3,314,795.68                |                       |             |                  |

## List of ongoing projects having time and cost overrun w.r.t original schedule

| (Aug,2013) |                                                                                               |                  |                                     |                             |                       |             |                  |                            |
|------------|-----------------------------------------------------------------------------------------------|------------------|-------------------------------------|-----------------------------|-----------------------|-------------|------------------|----------------------------|
|            |                                                                                               |                  |                                     |                             | Date of Commissioning |             |                  |                            |
| Sl.No      | Project                                                                                       | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised    | Anticipated | Cost Overrun (%) | Range of T.O.R (in months) |
| 1          | 2                                                                                             | 3                | 4                                   | 5                           | 6                     | 7           | 8                | 9                          |
|            |                                                                                               |                  |                                     |                             |                       |             |                  |                            |
|            | <u>Atomic Energy</u>                                                                          |                  |                                     |                             |                       |             |                  |                            |
| 1          | PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)<br>- [020100044]                            | 09/2003          | 3,492.00<br>-                       | 5,677.00                    | 09/2010<br>-          | 03/2015     | 62.57            | 54- 54                     |
| 2          | KUDANKULAM APP (NPCIL)<br>- [020100040]                                                       | 12/2001          | 13,171.00<br>-                      | 17,270.00                   | 12/2008<br>-          | 06/2014     | 31.12            | 66- 66                     |
|            | Total                                                                                         |                  | 16,663.00<br>-                      | 22,947.00                   |                       |             |                  |                            |
|            |                                                                                               |                  |                                     |                             |                       |             |                  |                            |
|            | <u>Coal</u>                                                                                   |                  |                                     |                             |                       |             |                  |                            |
| 3          | ADRIYALA SHAFT PROJECT<br>- [N06000016]                                                       | 12/2009          | 212.34<br>-                         | 977.53                      | 03/2013<br>-          | 10/2014     | 360.36           | 19- 19                     |
| 4          | MANIKPUR OC EXPANSION (3.5 MTY)<br>- [N06000081]                                              | 12/2009          | 321.42<br>-                         | 321.50                      | 03/2014<br>-          | 03/2016     | 0.02             | 24- 24                     |
| 5          | MAGADH OC 20 MTY (CCL)<br>- [N06000015]                                                       | 08/2008          | 469.78<br>-                         | 706.40                      | 07/2012<br>-          | 03/2016     | 50.37            | 44- 44                     |
| 6          | TPS-II EXPANSION (1470MW TO 1970MW) (NLC)<br>- [060100087]                                    | 10/2004          | 2,030.78<br>-                       | 3,027.59                    | 06/2009<br>-          | 01/2014     | 49.09            | 55- 55                     |
| 7          | TUTICORIN THERMAL POWER PROJECT- 2X500 MW<br>- [N06000047]                                    | 05/2008          | 4,904.54<br>-                       | 6,540.93                    | 03/2012<br>-          | 03/2014     | 33.36            | 24- 24                     |
|            | Total                                                                                         |                  | 7,938.86<br>-                       | 34,520.95                   |                       |             |                  |                            |
|            |                                                                                               |                  |                                     |                             |                       |             |                  |                            |
|            | <u>Petrochemicals</u>                                                                         |                  |                                     |                             |                       |             |                  |                            |
| 8          | Assam gas Cracker project<br>- [N16000106]                                                    | 04/2006          | 5,460.61<br>-                       | 8,920.00                    | 04/2012<br>-          | 12/2013     | 63.35            | 20- 20                     |
|            | Total                                                                                         |                  | 5,460.61<br>-                       | 43,440.95                   |                       |             |                  |                            |
|            |                                                                                               |                  |                                     |                             |                       |             |                  |                            |
|            | <u>Petroleum</u>                                                                              |                  |                                     |                             |                       |             |                  |                            |
| 9          | IOR, RUDRASAGAR (ONGCL)<br>- [160100217]                                                      | 09/2001          | 113.90<br>-                         | 438.85                      | 03/2006<br>-          | 12/2013     | 285.29           | 93- 93                     |
| 10         | CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN<br>- [N18000150]                                    | 08/2008          | 126.18<br>-                         | 159.54                      | 06/2012<br>-          | 03/2014     | 26.44            | 21- 21                     |
| 11         | CENTRAL GAS GATHERING STATION AND OFFTAKE POINT<br>- [N18000149]                              | 08/2008          | 144.02<br>-                         | 204.29                      | 06/2012<br>-          | 12/2013     | 41.85            | 18- 18                     |
| 12         | Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar<br>- [N16000099] | 03/2009          | 234.78<br>234.78                    | 317.64                      | 09/2012<br>-          | 09/2013     | 35.29            | 12- 12                     |
| 13         | PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT<br>- [N16000138]                | 08/2009          | 246.81<br>-                         | 276.83                      | 04/2012<br>-          | 12/2013     | 12.16            | 20- 20                     |
| 14         | URAN CHAKAN/SHIKRAPUR LPG PIPELINE<br>- [N16000155]                                           | 11/2012          | 309.81<br>-                         | 309.82                      | 08/2014<br>-          | 10/2014     | 0.00             | 2- 2                       |
| 15         | IOR LAKWA - LAKHMANI (ONGCL)<br>- [160100215]                                                 | 09/2001          | 345.10<br>-                         | 750.00                      | 03/2007<br>-          | 12/2013     | 117.33           | 81- 81                     |

(Aug,2013)

|       |                                                                                |                  |                                     |                             | Date of Commissioning |             |                  |                            |
|-------|--------------------------------------------------------------------------------|------------------|-------------------------------------|-----------------------------|-----------------------|-------------|------------------|----------------------------|
| Sl.No | Project                                                                        | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised    | Anticipated | Cost Overrun (%) | Range of T.O.R (in months) |
| 1     | 2                                                                              | 3                | 4                                   | 5                           | 6                     | 7           | 8                | 9                          |
| 16    | IOR GELEKI (ONGCL)<br>- [160100216                                             | 09/2001          | 390.09<br>-                         | 1,674.11                    | 03/2007<br>-          | 12/2013     | 329.16           | 81- 81                     |
| 17    | DEV OF G1 AND GS-15 (ONGCL)<br>- [160100231                                    | 04/2003          | 429.82<br>-                         | 2,735.65                    | 04/2006<br>-          | 02/2014     | 536.46           | 94- 94                     |
| 18    | STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG<br>- [N16000156                   | 01/2006          | 672.00<br>-                         | 1,038.00                    | 10/2011<br>-          | 01/2014     | 54.46            | 27- 27                     |
| 19    | STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE<br>[N16000157                 | 01/2006          | 732.00<br>-                         | 1,227.00                    | 10/2011<br>-          | 12/2013     | 67.62            | 26- 26                     |
| 20    | HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY<br>[N16000081  | 04/2008          | 825.00<br>-                         | 1,827.00                    | 04/2013<br>-          | 09/2013     | 121.45           | 5- 5                       |
| 21    | ADDITIONAL DEV. OF D-1 FIELD<br>- [N16000086                                   | 01/2010          | 2,163.64<br>-                       | 2,331.62                    | 06/2012<br>-          | 05/2014     | 7.76             | 23- 23                     |
| 22    | DEVELOPMENT OF B-22 CLUSTER FIELDS<br>- [N16000032                             | 01/2007          | 2,323.40<br>-                       | 2,920.82                    | 09/2010<br>03/2012    | 12/2015     | 25.71            | 63- 63                     |
| 23    | DEVELOPMENT OF C-SERIES FIELDS<br>- [N16000023                                 | 08/2006          | 3,195.16<br>-                       | 3,690.37                    | 12/2008<br>-          | 03/2014     | 15.50            | 63- 63                     |
| 24    | Development of Cluster-7 Fields<br>- [N16000104                                | 03/2010          | 3,241.03<br>-                       | 6,638.94                    | 03/2013<br>-          | 11/2014     | 104.84           | 20- 20                     |
| 25    | DEVELOPMENT OF B-193 CLUSTER FIELDS<br>- [N16000033                            | 06/2007          | 3,248.78<br>-                       | 5,633.44                    | 08/2010<br>03/2012    | 05/2014     | 73.40            | 45- 45                     |
| 26    | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2<br>- [N16000039                           | 10/2007          | 5,713.03<br>-                       | 8,813.41                    | 05/2010<br>-          | 03/2014     | 54.27            | 46- 46                     |
| 27    | PARADIP REFINERY PROJECT<br>- [N16000058                                       | 02/2009          | 29,777.00<br>-                      | 32,710.00                   | 11/2012<br>-          | 04/2014     | 9.85             | 17- 17                     |
|       | Total                                                                          |                  | 54,231.55<br>-                      | 117,138.28                  |                       |             |                  |                            |
|       |                                                                                |                  |                                     |                             |                       |             |                  |                            |
|       | Power                                                                          |                  |                                     |                             |                       |             |                  |                            |
| 28    | PARE HYDRO ELECTRIC PROJECT<br>- [N18000045                                    | 12/2008          | 573.99<br>-                         | 1,117.92                    | 08/2012<br>-          | 09/2014     | 94.76            | 25- 25                     |
| 29    | NIMOO BAZGO HYDROELECTRIC PROJECT<br>- [N18000006                              | 08/2006          | 611.01<br>-                         | 936.00                      | 08/2010<br>-          | 10/2013     | 53.19            | 38- 38                     |
| 30    | TEESTA LOW DAM HEP, STAGE-IV (NHPC)<br>- [180100243                            | 09/2005          | 1,061.38<br>-                       | 1,501.75                    | 09/2009<br>-          | 11/2014     | 41.49            | 62- 62                     |
| 31    | TEHRI PUMPED STORAGE PLANT(1000MW)<br>- [N18000010                             | 07/2006          | 1,657.00<br>-                       | 2,978.86                    | 07/2010<br>-          | 02/2017     | 79.77            | 79- 79                     |
| 32    | URI H.E.P STAGE -II (NHPC)<br>- [180100251                                     | 08/2005          | 1,729.29<br>-                       | 2,081.00                    | 11/2009<br>-          | 10/2013     | 20.34            | 47- 47                     |
| 33    | KISHANGANGA HEP<br>- [N18000031                                                | 07/2007          | 2,238.67<br>-                       | 3,642.00                    | 01/2016<br>-          | 11/2016     | 62.69            | 10- 10                     |
| 34    | PARBATI H.E.P. STAGE -III (NHPC)<br>- [180100250                               | 10/2005          | 2,304.56<br>-                       | 2,716.00                    | 10/2010<br>-          | 03/2014     | 17.85            | 41- 41                     |
| 35    | SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC<br>- [N18000065 | 08/2008          | 2,360.95<br>-                       | 2,580.90                    | 08/2012<br>-          | 03/2014     | 9.32             | 19- 19                     |
| 36    | VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT<br>[N18000042                       | 08/2008          | 2,491.58<br>-                       | 3,745.08                    | 07/2014<br>-          | 05/2016     | 50.31            | 22- 22                     |

(Aug,2013)

|       |                                                                                           |                  |                                     |                             | Date of Commissioning |             |                  |                            |
|-------|-------------------------------------------------------------------------------------------|------------------|-------------------------------------|-----------------------------|-----------------------|-------------|------------------|----------------------------|
| Sl.No | Project                                                                                   | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised    | Anticipated | Cost Overrun (%) | Range of T.O.R (in months) |
| 1     | 2                                                                                         | 3                | 4                                   | 5                           | 6                     | 7           | 8                | 9                          |
| 37    | KAMENG HYDROELECTRIC PROJECT (NEEPCO)<br>- [180100239                                     | 12/2004          | 2,496.90<br>-                       | 5,139.00                    | 05/2013<br>05/2013    | 03/2017     | 105.82           | 46- 46                     |
| 38    | Tapovan-Vishnugad HEP (4x130MW)<br>- [N18000014                                           | 11/2006          | 2,978.48<br>-                       | 3,846.30                    | 03/2013<br>-          | 03/2016     | 29.14            | 36- 36                     |
| 39    | PARBATI HEP (NHPC) II<br>- [180100210                                                     | 09/2002          | 3,919.59<br>-                       | 5,366.00                    | 09/2009<br>-          | 07/2018     | 36.90            | 106- 106                   |
| 40    | KOLDAM HEP (NTPC)<br>- [180100211                                                         | 10/2002          | 4,527.15<br>-                       | 6,414.56                    | 04/2009<br>-          | 09/2014     | 41.69            | 65- 65                     |
| 41    | SUBANSIRI LOWER H.E.P (NHPC)<br>- [180100221                                              | 09/2003          | 6,285.33<br>-                       | 10,667.00                   | 09/2010<br>-          | 12/2017     | 69.71            | 87- 87                     |
| 42    | BARH STPP(3X660MW) NTPC<br>- [180100242                                                   | 12/2003          | 8,692.97<br>-                       | 8,693.00                    | 12/2009<br>-          | 02/2017     | 0.00             | 86- 86                     |
|       | Total                                                                                     |                  | 43,928.85<br>-                      | 178,563.65                  |                       |             |                  |                            |
|       |                                                                                           |                  |                                     |                             |                       |             |                  |                            |
|       | <u>Railways</u>                                                                           |                  |                                     |                             |                       |             |                  |                            |
| 43    | HOWRAH-AMTA-CHAMPADANGA NL (SER)<br>- [220100208                                          | 04/1974          | 31.42<br>154.30                     | 535.40                      | 03/2007<br>03/2007    | 03/2015     | 1,604.01         | 96- 96                     |
| 44    | LANJHIGARH-JUNAGARH NL(ECOR)<br>- [220100148                                              | 04/1993          | 100.00<br>119.29                    | 227.94                      | 03/2002<br>-          | 09/2013     | 127.94           | 138- 138                   |
| 45    | KATIHAR - JOGBANI (GC)(NEFR)<br>- [220100247                                              | 09/2001          | 100.00<br>-                         | 1,041.79                    | 12/2010<br>-          | 03/2015     | 941.79           | 51- 51                     |
| 46    | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR<br>- [220100243                                | 04/1999          | 108.00<br>-                         | 432.72                      | 12/2009<br>-          | 10/2013     | 300.67           | 46- 46                     |
| 47    | BANKURA - DAMODAR (GC) (SER)<br>- [220100277                                              | 03/1998          | 111.90<br>-                         | 1,423.98                    | 03/2005<br>12/2008    | 12/2016     | 1,172.55         | 141- 141                   |
| 48    | ETAWAH-MAINPURI (NL),NCR<br>- [220100318                                                  | 09/2001          | 129.70<br>-                         | 245.39                      | 12/2008<br>-          | 09/2014     | 89.20            | 69- 69                     |
| 49    | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)<br>- [220100327                                 | 04/2000          | 133.41<br>207.00                    | 276.00                      | 03/2009<br>03/2009    | 08/2014     | 106.88           | 65- 65                     |
| 50    | Champajharan-Bimalgarh Doubling extension<br>- [N22000162                                 | 04/2010          | 149.90<br>-                         | 177.38                      | 03/2015<br>-          | 12/2015     | 18.33            | 9- 9                       |
| 51    | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL,<br>(NCR) - [220100007                         | 04/1986          | 158.77<br>274.56                    | 580.83                      | 03/1994<br>-          | 10/2013     | 265.83           | 235- 235                   |
| 52    | RAJATGARH-BARANG(LD),ECOR<br>- [220100286                                                 | 04/1999          | 166.16<br>-                         | 288.00                      | 02/2009<br>02/2009    | 08/2014     | 73.33            | 66- 66                     |
| 53    | ELECTRIFICATION OF KHURJA-MEERUT-<br>SAHARANPUR AND G'BAD-MEERUT<br>- [N22000094          | 02/2008          | 171.10<br>-                         | 246.44                      | 03/2012<br>-          | 03/2014     | 44.03            | 24- 24                     |
| 54    | Ghutiasharif-Canning (ER)<br>- [N22000117                                                 | 04/2009          | 189.97<br>-                         | 611.03                      | 12/2011<br>-          | 11/2013     | 221.65           | 23- 23                     |
| 55    | TAMLUK DIGHA,LINE DOUBLING (SER)<br>- [N22000097                                          | 03/1984          | 293.97<br>-                         | 1,074.47                    | 06/2005<br>-          | 06/2016     | 265.50           | 132- 132                   |
| 56    | UTRATIA-ZAFRABAD, NR (LINE DOUBLING)<br>- [N22000088                                      | 04/2006          | 325.00<br>-                         | 1,116.53                    | 03/2010<br>-          | 03/2017     | 243.55           | 84- 84                     |
| 57    | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE<br>LINE(MTP) - [220100164                         | 03/1996          | 401.81<br>-                         | 1,814.48                    | 03/2004<br>-          | 12/2014     | 351.58           | 129- 129                   |
| 58    | Ramanagram-Mysore doubling with electrification of<br>Kengesii- Musore (SWR) - [N22000107 | 04/2007          | 482.00<br>-                         | 482.70                      | 03/2013<br>-          | 03/2014     | 0.15             | 12- 12                     |

(Aug,2013)

|       |                                                                                      |                  |                                     |                             | Date of Commissioning |             |                  |                            |
|-------|--------------------------------------------------------------------------------------|------------------|-------------------------------------|-----------------------------|-----------------------|-------------|------------------|----------------------------|
| Sl.No | Project                                                                              | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised    | Anticipated | Cost Overrun (%) | Range of T.O.R (in months) |
| 1     | 2                                                                                    | 3                | 4                                   | 5                           | 6                     | 7           | 8                | 9                          |
| 59    | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]                           | 03/1984          | 520.00<br>422.79                    | 835.04                      | 03/1995<br>-          | 03/2015     | 60.58            | 240- 240                   |
| 60    | BHAIRABI SAIRONG, NL, NEFR - [N22000100]                                             | 04/2008          | 619.34<br>-                         | 2,384.34                    | 04/2014<br>-          | 03/2017     | 284.98           | 35- 35                     |
| 61    | PATNA GANGA BRIDGE (NL), ECR - [220100308]                                           | 04/2001          | 624.47<br>-                         | 2,921.00                    | 10/2007<br>-          | 12/2015     | 367.76           | 98- 98                     |
| 62    | BHOPAL BINA 3D LINE DOUBLING - [N22000077]                                           | 09/2007          | 687.20<br>-                         | 800.00                      | 03/2010<br>-          | 12/2015     | 16.41            | 69- 69                     |
| 63    | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]                                    | 04/2003          | 727.56<br>-                         | 4,453.50                    | 03/2011<br>-          | 03/2017     | 512.11           | 72- 72                     |
| 64    | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]                 | 04/2000          | 733.00<br>-                         | 2,350.00                    | 12/2008<br>-          | 03/2015     | 220.60           | 75- 75                     |
| 65    | AGARTALA SABROOM, NL, NEFR - [N22000099]                                             | 04/2008          | 813.34<br>-                         | 1,741.00                    | 03/2014<br>-          | 12/2015     | 114.06           | 21- 21                     |
| 66    | New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]         | 04/2006          | 850.00<br>-                         | 2,441.48                    | 03/2015<br>-          | 03/2017     | 187.23           | 24- 24                     |
| 67    | Construction of NL from Kumarghat-Agartala - [N22000194]                             | 04/1999          | 895.00<br>-                         | 1,151.00                    | 03/2007<br>-          | 03/2015     | 28.60            | 96- 96                     |
| 68    | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]                               | 04/2002          | 921.00<br>-                         | 2,363.00                    | 03/2009<br>-          | 12/2014     | 156.57           | 69- 69                     |
| 69    | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]                           | 09/1997          | 1,000.00<br>-                       | 4,996.19                    | 04/2008<br>12/2011    | 12/2015     | 399.62           | 92- 92                     |
| 70    | SEVOK RANGPO, NEFR - [N22000102]                                                     | 04/2008          | 1,339.48<br>-                       | 3,380.58                    | 12/2015<br>-          | 03/2017     | 152.38           | 15- 15                     |
| 71    | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127] | 04/1996          | 1,676.31<br>-                       | 5,000.00                    | 03/2009<br>-          | 12/2014     | 198.27           | 69- 69                     |
| 72    | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]                                    | 03/1995          | 2,500.00<br>-                       | 20,000.00                   | 11/2002<br>-          | 12/2017     | 700.00           | 181- 181                   |
| 73    | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]                                | 04/2008          | 5,300.00<br>-                       | 6,220.15                    | 03/2014<br>-          | 12/2016     | 17.36            | 33- 33                     |
|       | Total                                                                                |                  | 22,259.81<br>-                      | 250,176.01                  |                       |             |                  |                            |
|       |                                                                                      |                  |                                     |                             |                       |             |                  |                            |
|       | <u>Road Transport And Highways</u>                                                   |                  |                                     |                             |                       |             |                  |                            |
| 74    | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]              | 12/2003          | 155.00<br>-                         | 201.66                      | 09/2008<br>-          | 03/2014     | 30.10            | 66- 66                     |
| 75    | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]                   | 12/2003          | 155.04<br>-                         | 280.13                      | 11/2008<br>-          | 06/2014     | 80.68            | 67- 67                     |
| 76    | HARANGAJO TO MAIBANG, NH-54 - [N24000062]                                            | 12/2003          | 196.00<br>-                         | 363.74                      | 07/2009<br>-          | 05/2014     | 85.58            | 58- 58                     |
| 77    | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]                    | 12/2003          | 199.81<br>-                         | 385.13                      | 04/2009<br>-          | 12/2014     | 92.75            | 68- 68                     |
| 78    | HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]                          | 12/2003          | 212.00<br>-                         | 386.10                      | 09/2007<br>-          | 04/2014     | 82.12            | 79- 79                     |
| 79    | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]                             | 04/2000          | 225.00<br>-                         | 241.53                      | 04/2004<br>-          | 09/2013     | 7.35             | 113- 113                   |

(Aug,2013)

|       |                                                                                                |                  |                                     |                             | Date of Commissioning |             |                  |                            |
|-------|------------------------------------------------------------------------------------------------|------------------|-------------------------------------|-----------------------------|-----------------------|-------------|------------------|----------------------------|
| Sl.No | Project                                                                                        | Date of Approval | Original / Revised Cost (Rs. crore) | Anticipated Cost (Rs.crore) | Original / Revised    | Anticipated | Cost Overrun (%) | Range of T.O.R (in months) |
| 1     | 2                                                                                              | 3                | 4                                   | 5                           | 6                     | 7           | 8                | 9                          |
| 80    | CHAMBAL BRIDGE, NH-76 (RJ-5)<br>- [N24000068                                                   | 12/2003          | 275.00<br>-                         | 281.31                      | 02/2010<br>-          | 06/2015     | 2.29             | 64- 64                     |
| 81    | PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A<br>- [240106237                                   | 12/2003          | 284.00<br>-                         | 359.00                      | 05/2008<br>-          | 09/2013     | 26.41            | 64- 64                     |
| 82    | AGRA-BYPASS(NS-1/UP-1), NH-2,3<br>- [N24000098                                                 | 12/2003          | 348.16<br>-                         | 465.50                      | 09/2007<br>-          | 03/2014     | 33.70            | 78- 78                     |
| 83    | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)<br>- [N24000133                                    | 05/2009          | 1,108.00<br>-                       | 2,288.00                    | 11/2011<br>-          | 12/2013     | 106.50           | 25- 25                     |
|       | Total                                                                                          |                  | 3,158.01<br>-                       | 255,428.11                  |                       |             |                  |                            |
|       |                                                                                                |                  |                                     |                             |                       |             |                  |                            |
|       | <u>Shipping And Ports</u>                                                                      |                  |                                     |                             |                       |             |                  |                            |
| 84    | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)<br>[N25000035                      | 10/2002          | 150.00<br>-                         | 600.00                      | 03/2006<br>-          | 12/2013     | 300.00           | 93- 93                     |
| 85    | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL<br>[N25000016                          | 11/2007          | 1,228.00<br>-                       | 1,460.00                    | 12/2010<br>-          | 12/2014     | 18.89            | 48- 48                     |
| 86    | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN<br>[N25000048                  | 03/2009          | 3,500.00<br>-                       | 4,150.00                    | 01/2012<br>-          | 08/2013     | 18.57            | 19- 19                     |
|       | Total                                                                                          |                  | 4,878.00<br>-                       | 261,638.11                  |                       |             |                  |                            |
|       |                                                                                                |                  |                                     |                             |                       |             |                  |                            |
|       | <u>Steel</u>                                                                                   |                  |                                     |                             |                       |             |                  |                            |
| 87    | COKE OVEN BATTERY NO. 4 PHASE-II<br>- [N12000038                                               | 08/2007          | 108.00<br>-                         | 216.68                      | 10/2012<br>-          | 12/2013     | 100.63           | 14- 14                     |
| 88    | 67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT<br>[N12000068                    | 07/2007          | 230.00<br>-                         | 343.58                      | 02/2011<br>-          | 09/2013     | 49.38            | 31- 31                     |
| 89    | Bailadila Iron Ore Project Deposit- 11B (NMDC)<br>- [N12000018                                 | 01/2007          | 295.89<br>-                         | 607.17                      | 12/2011<br>06/2010    | 12/2013     | 105.20           | 24- 24                     |
| 90    | EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)<br>- [120100067                    | 10/2005          | 8,692.00<br>-                       | 12,291.00                   | 10/2009<br>-          | 09/2013     | 41.41            | 47- 47                     |
| 91    | EXPANSION OF IISCO STEEL PLANT<br>- [N12000051                                                 | 02/2008          | 14,443.00<br>-                      | 16,408.00                   | 12/2011<br>-          | 12/2013     | 13.61            | 24- 24                     |
|       | Total                                                                                          |                  | 23,768.89<br>-                      | 291,504.54                  |                       |             |                  |                            |
|       |                                                                                                |                  |                                     |                             |                       |             |                  |                            |
|       | <u>Telecommunications</u>                                                                      |                  |                                     |                             |                       |             |                  |                            |
| 92    | GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL<br>[N26000058            | 01/2009          | 149.15<br>-                         | 158.72                      | 06/2009<br>-          | 12/2013     | 6.42             | 54- 54                     |
| 93    | GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle<br>[N26000090 | 11/2009          | 916.70<br>-                         | 930.60                      | 11/2010<br>-          | 09/2013     | 1.52             | 34- 34                     |
|       | Total                                                                                          |                  | 1,065.85<br>-                       | 292,593.86                  |                       |             |                  |                            |
|       |                                                                                                |                  |                                     |                             |                       |             |                  |                            |
|       | Grand Total                                                                                    |                  | 183,353.43                          | 1,747,951.46                |                       |             |                  |                            |



## List of Projects without Milestones w.r.t. Original Schedule

|       |                                                                                           |                  |                                    | (Aug,2013)            |             |                            |
|-------|-------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                           |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                   | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                         | 3                | 4                                  | 5                     | 6           | 7                          |
|       | <u>Civil Aviation</u>                                                                     |                  |                                    |                       |             |                            |
| 1     | D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu             | 08/2008          | 1,808.00<br>2,015.00               | 01/2011<br>02/2012    | 02/2012     | 0/0                        |
| 2     | C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal            | 08/2008          | 1,942.51<br>-                      | 05/2011<br>-          | 03/2013     | 0/0                        |
| 3     | GAGAN PROJECT - [N04000065]AAI,Multi State                                                | 09/2008          | 626.00<br>-                        | 06/2013<br>-          | 06/2013     | 0/0                        |
| 4     | Construction of New International Terminal Building - [N04000069]AAI,Goa                  | 05/2010          | 335.61<br>-                        | 05/2012<br>-          | 09/2013     | 0/0                        |
| 5     | ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI - [N04000072]AAI,Multi State | 02/2010          | 344.28<br>-                        | 03/2014<br>-          | 03/2014     | 0/0                        |
| 6     | C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim                        | 01/2009          | 309.46<br>-                        | 01/2011<br>04/2013    | 12/2014     | 0/0                        |
| 7     | DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Chandigarh            | 02/2011          | 452.00<br>-                        | 03/2015<br>-          | 03/2015     | 0/0                        |
| 8     | SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State   | 10/2012          | 217.60<br>-                        | 03/2015<br>-          | 03/2015     | 0/0                        |
|       | Total                                                                                     |                  | 6,035.46<br>-                      |                       |             | 0/0                        |
|       | <u>Coal</u>                                                                               |                  |                                    |                       |             |                            |
| 9     | Muraidih UG - [N06000096]BCCL,Jharkhand                                                   | 02/2011          | 339.88<br>-                        | 04/2014<br>-          | 04/2014     | 0/0                        |
| 10    | Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand                                           | 08/2011          | 1,230.27<br>-                      | 04/2015<br>-          | 04/2015     | 0/0                        |
|       | Total                                                                                     |                  | 1,570.15<br>-                      |                       |             | 0/0                        |
|       | <u>Steel</u>                                                                              |                  |                                    |                       |             |                            |
| 11    | Coke Oven Battery-5 - [N12000080]SAIL,West Bengal                                         | 03/2012          | 339.35<br>-                        | 06/2015<br>-          | 06/2015     | 0/0                        |
|       | Total                                                                                     |                  | 339.35<br>-                        |                       |             | 0/0                        |
|       | <u>Petroleum</u>                                                                          |                  |                                    |                       |             |                            |
| 12    | Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan  | 04/2011          | 152.89<br>-                        | 06/2013<br>-          | 06/2013     | 0/0                        |
| 13    | DBPL-II - [N16000147]GAIL,Multi State                                                     | 06/2009          | 486.00<br>-                        | 09/2013<br>-          | 09/2013     | 0/0                        |
| 14    | OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra      | 01/2007          | 740.02<br>-                        | 03/2010<br>03/2012    | 12/2013     | 0/0                        |

|       |                                                                                            |                  | (Aug,2013)                         |                       |             |                            |
|-------|--------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                            |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                          | 3                | 4                                  | 5                     | 6           | 7                          |
| 15    | Wax Project - [N16000101]NRL,Assam                                                         | 06/2010          | 576.60                             | 12/2013               | 12/2013     | 0/0                        |
| 16    | Construction of 6 ETPs - [N16000117]ONGC,Gujarat                                           | 03/2009          | 302.26                             | 09/2012               | 12/2013     | 0/0                        |
| 17    | PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra | 08/2009          | 246.81<br>276.83                   | 04/2012<br>06/2013    | 12/2013     | 0/0                        |
| 18    | SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka          | 07/2010          | 1,043.57                           | 04/2012               | 12/2013     | 0/0                        |
| 19    | STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,Karnataka               | 01/2006          | 732.00<br>1,227.00                 | 10/2011               | 12/2013     | 0/0                        |
| 20    | CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam                     | 08/2008          | 144.02                             | 06/2012               | 12/2013     | 0/0                        |
| 21    | STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR,Andhra Pradesh              | 01/2006          | 672.00<br>1,038.00                 | 10/2011               | 01/2014     | 0/0                        |
| 22    | DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State                                  | 04/2003          | 429.82<br>2,735.65                 | 04/2006<br>06/2012    | 02/2014     | 0/0                        |
| 23    | PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State                | 08/2010          | 8,140.00                           | 02/2014               | 02/2014     | 0/0                        |
| 24    | DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra                               | 08/2006          | 3,195.16<br>3,690.37               | 12/2008<br>04/2013    | 03/2014     | 0/0                        |
| 25    | MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra                         | 10/2007          | 5,713.03<br>8,813.41               | 05/2010<br>03/2013    | 03/2014     | 0/0                        |
| 26    | DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra                            | 06/2007          | 1,436.21<br>1,456.96               | 07/2010<br>05/2012    | 03/2014     | 0/0                        |
| 27    | MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra                       | 01/2009          | 7,133.39                           | 09/2012               | 03/2014     | 0/0                        |
| 28    | CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam                           | 08/2008          | 126.18                             | 06/2012               | 03/2014     | 0/0                        |
| 29    | ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State                                 | 01/2010          | 2,163.64<br>2,331.62               | 06/2012               | 05/2014     | 0/0                        |
| 30    | URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State                           | 11/2012          | 309.81                             | 08/2014               | 10/2014     | 0/0                        |
| 31    | JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana                                 | 11/2007          | 281.07                             | 10/2010               | 12/2014     | 0/0                        |
| 32    | CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State              | 06/2007          | 736.65                             | 09/2011               | 12/2014     | 0/0                        |
| 33    | Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra                    | 01/1999          | 1,419.00                           | 12/2014               | 12/2014     | 0/0                        |
| 34    | Mounded Bullet - [N16000154]CPCL,Tamil Nadu                                                | 12/2012          | 279.00                             | 12/2014               | 12/2014     | 0/0                        |
| 35    | Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]OIL,Multi State                    | 04/2010          | 270.00                             | 12/2014               | 12/2014     | 0/0                        |
| 36    | Reconstruction of BPA and BPB Platforms - [N16000161]ONGC,Maharashtra                      | 03/2013          | 1,138.50                           | 04/2015               | 04/2015     | 0/0                        |
| 37    | Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State                               | 10/2012          | 10,281.00                          | -                     | 04/2015     | 0/0                        |
| 38    | PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State                         | 02/2011          | 913.00                             | 07/2015               | 07/2015     | 0/0                        |
| 39    | AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State              | 08/2011          | 586.00                             | 07/2015               | 08/2015     | 0/0                        |

|       |                                                                                               |                  | (Aug,2013)                         |                       |             |                            |
|-------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                               |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                             | 3                | 4                                  | 5                     | 6           | 7                          |
| 40    | MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka              | 11/2012          | 666.00<br>-                        | 11/2015<br>-          | 11/2015     | 0/0                        |
| 41    | DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra                              | 01/2007          | 2,323.40<br>2,920.82               | 09/2010<br>03/2012    | 12/2015     | 0/0                        |
| 42    | JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State                      | 07/2009          | 7,596.18<br>-                      | 01/2013<br>-          | 12/2015     | 0/0                        |
| 43    | Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra                         | 12/2012          | 3,513.07<br>-                      | 02/2016<br>-          | 02/2016     | 0/0                        |
| 44    | IREP - [N16000143]BPCL,Kerala                                                                 | 01/1999          | 14,225.00<br>-                     | 12/2015<br>-          | 05/2016     | 0/0                        |
| 45    | Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State                 | 01/2010          | 723.64<br>-                        | 03/2013<br>-          | 06/2016     | 0/0                        |
| 46    | CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY - [N16000167]OIL,Multi State        | 08/2006          | 374.56<br>-                        | 09/2012<br>-          | 10/2016     | 0/0                        |
| 47    | Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat                                             | 11/2010          | 1,916.10<br>-                      | 12/2014<br>-          | 12/2016     | 0/0                        |
| 48    | Ankleswar Redevelopment - [N16000122]ONGC,Gujarat                                             | 11/2010          | 2,189.63<br>-                      | 12/2014<br>-          | 12/2016     | 0/0                        |
| 49    | Mehesana Redevelopment - [N16000121]ONGC,Gujarat                                              | 11/2010          | 3,823.00<br>-                      | 04/2015<br>-          | 03/2017     | 0/0                        |
| 50    | DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra              | 12/2009          | 1,584.00<br>-                      | -<br>-                | -           | 0/0                        |
| 51    | Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu                               | 05/2013          | 711.00<br>-                        | -<br>-                | -           | 0/0                        |
|       | Total                                                                                         |                  | 89,293.21<br>-                     |                       |             | 0/0                        |
|       |                                                                                               |                  |                                    |                       |             |                            |
|       | <u>Power</u>                                                                                  |                  |                                    |                       |             |                            |
| 52    | ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State   | 03/2012          | 198.63<br>-                        | 09/2014<br>-          | 09/2014     | 0/0                        |
| 53    | COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu                            | 01/2013          | 182.80<br>-                        | 10/2014<br>-          | 10/2014     | 0/0                        |
| 54    | TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal                             | 09/2005          | 1,061.38<br>-                      | 09/2009<br>06/2013    | 11/2014     | 0/0                        |
| 55    | SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State            | 09/2012          | 1,935.35<br>-                      | 12/2014<br>-          | 11/2014     | 0/0                        |
| 56    | COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC - [N18000143]PGCIL,Multi State             | 03/2013          | 514.20<br>-                        | 06/2015<br>-          | 06/2015     | 0/0                        |
| 57    | COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh | 06/2012          | 1,909.24<br>-                      | 06/2015<br>-          | 06/2015     | 0/0                        |
| 58    | NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,Multi State                | 09/2013          | 680.69<br>-                        | 03/2016<br>-          | 03/2016     | 0/0                        |
| 59    | Transmission System associated with Mauda Stage-II - [N18000153]PGCIL,Multi State             | 09/2013          | 1,575.30<br>-                      | 05/2016<br>-          | 05/2016     | 0/0                        |
|       | Total                                                                                         |                  | 8,057.59<br>-                      |                       |             | 0/0                        |
|       |                                                                                               |                  |                                    |                       |             |                            |
|       | <u>Railways</u>                                                                               |                  |                                    |                       |             |                            |

|       |                                                                                        |                  | (Aug,2013)                         |                       |             |                            |
|-------|----------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                        |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                      | 3                | 4                                  | 5                     | 6           | 7                          |
| 60    | RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha                                     | 02/1996          | 57.94<br>604.04                    | 03/1998<br>08/2005    | 08/2005     | 0/0                        |
| 61    | JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State                     | 03/2002          | 409.00<br>625.30                   | 06/2007<br>-          | 06/2007     | 0/0                        |
| 62    | MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh                             | 07/1998          | 125.00<br>363.26                   | 07/2008<br>-          | 07/2008     | 0/0                        |
| 63    | GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka                                      | 02/1998          | 242.42<br>369.70                   | -<br>05/2009          | 05/2009     | 0/0                        |
| 64    | KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand                                    | 04/1996          | 371.36<br>768.87                   | -<br>03/2010          | 03/2010     | 0/0                        |
| 65    | TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal        | 03/2000          | 907.69<br>3,156.32                 | 12/2006<br>08/2010    | 08/2010     | 0/0                        |
| 66    | Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal                          | 04/2004          | 225.68<br>293.74                   | 12/2010<br>12/2010    | 12/2010     | 0/0                        |
| 67    | AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra                                    | 06/1994          | 120.90<br>663.10                   | 06/1999<br>03/2011    | 03/2011     | 0/0                        |
| 68    | ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State       | 12/2006          | 170.00<br>170.00                   | 03/2011<br>03/2011    | 03/2011     | 0/0                        |
| 69    | BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal                                       | 04/2007          | 245.15<br>1,106.62                 | 12/2010<br>03/2011    | 03/2011     | 0/0                        |
| 70    | CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State                                | 02/1996          | 240.00<br>-                        | -<br>-                | 02/2012     | 0/0                        |
| 71    | TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal                | 04/2000          | 157.96<br>1,188.91                 | -<br>12/2009          | 02/2012     | 0/0                        |
| 72    | Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal                            | 04/2009          | 259.51<br>533.38                   | 12/2011<br>02/2012    | 02/2012     | 0/0                        |
| 73    | PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh                 | 12/1994          | 124.43<br>495.68                   | -<br>-                | 03/2012     | 0/0                        |
| 74    | NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh                            | 03/1996          | 155.74<br>429.49                   | 02/2009<br>-          | 03/2012     | 0/0                        |
| 75    | MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State                           | 04/1997          | 218.24<br>377.32                   | -<br>-                | 03/2012     | 0/0                        |
| 76    | GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh | 03/2002          | 381.17<br>863.23                   | -<br>-                | 03/2012     | 0/0                        |
| 77    | HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar            | 04/2003          | 98.74<br>224.51                    | -<br>-                | 03/2012     | 0/0                        |
| 78    | CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar               | 03/2005          | 470.09<br>1,417.97                 | -<br>-                | 03/2012     | 0/0                        |
| 79    | KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu                                          | 02/1997          | 155.55<br>155.00                   | -<br>-                | 10/2012     | 0/0                        |
| 80    | KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka                                    | 04/1995          | 65.94<br>302.23                    | -<br>-                | 12/2012     | 0/0                        |
| 81    | RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand                                    | 04/1997          | 194.07<br>194.07                   | 06/2004<br>-          | 12/2012     | 0/0                        |
| 82    | JIND-SONEPAT (NL),NR - [220100280]NR,Haryana                                           | 01/2004          | 190.81<br>238.56                   | 03/2012<br>03/2012    | 12/2012     | 0/0                        |
| 83    | DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu           | 09/2006          | 343.17<br>343.17                   | -<br>-                | 12/2012     | 0/0                        |
| 84    | HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka               | 02/1997          | 295.00<br>412.91                   | -<br>-                | 01/2013     | 0/0                        |

|       |                                                                                              |                  | (Aug,2013)                         |                       |             |                            |
|-------|----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                              |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                                  | 5                     | 6           | 7                          |
| 85    | DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State                                   | 04/2000          | 138.00<br>607.09                   | 12/2012<br>12/2012    | 02/2013     | 0/0                        |
| 86    | MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar                                        | 04/2003          | 218.19<br>218.19                   | -<br>-                | 02/2013     | 0/0                        |
| 87    | Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand                                          | 04/2008          | 167.73<br>167.73                   | 03/2012<br>-          | 02/2013     | 0/0                        |
| 88    | MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand                                 | 04/1995          | 184.00<br>900.05                   | 12/2011<br>12/2011    | 03/2013     | 0/0                        |
| 89    | KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka                           | 04/1996          | 157.00<br>262.82                   | 03/2012<br>03/2012    | 03/2013     | 0/0                        |
| 90    | KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh                                | 03/1997          | 395.00<br>1,577.45                 | -<br>-                | 03/2013     | 0/0                        |
| 91    | GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State                                      | 04/1998          | 92.63<br>228.09                    | 02/2011<br>02/2011    | 03/2013     | 0/0                        |
| 92    | KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar                                                 | 04/2002          | 323.41<br>322.95                   | 03/2012<br>03/2013    | 03/2013     | 0/0                        |
| 93    | MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar                     | 04/1996          | 114.01<br>332.92                   | 03/2012<br>03/2013    | 03/2013     | 0/0                        |
| 94    | Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat                                   | 04/2008          | 394.14<br>385.60                   | 03/2013<br>-          | 03/2013     | 0/0                        |
| 95    | CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab                                   | 07/1998          | 248.44<br>576.27                   | 12/2012<br>01/2013    | 04/2013     | 0/0                        |
| 96    | LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha                                        | 04/1993          | 100.00<br>142.98                   | 03/2002<br>-          | 09/2013     | 0/0                        |
| 97    | GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State               | 04/1986          | 158.77<br>580.83                   | 03/1994<br>-          | 10/2013     | 0/0                        |
| 98    | AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh                    | 04/1999          | 108.00<br>427.21                   | 12/2009<br>03/2011    | 10/2013     | 0/0                        |
| 99    | Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal                                        | 04/2009          | 189.97<br>611.03                   | 12/2011<br>11/2013    | 11/2013     | 0/0                        |
| 100   | CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh                              | 04/2005          | 383.79<br>-                        | -<br>-                | 12/2013     | 0/0                        |
| 101   | CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh       | 09/1996          | 156.00<br>156.00                   | -<br>-                | 12/2013     | 0/0                        |
| 102   | Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal               | 04/1999          | 207.52<br>207.52                   | 12/2012<br>-          | 12/2013     | 0/0                        |
| 103   | PANVEL PEN DOUBLING - [N22000255]CR,Multi State                                              | 04/2006          | 191.00<br>-                        | -<br>-                | 12/2013     | 0/0                        |
| 104   | Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka                                             | 04/2006          | 287.99<br>-                        | 01/1999<br>-          | 12/2013     | 0/0                        |
| 105   | DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan                                       | 02/1997          | 151.84<br>410.08                   | -<br>-                | 03/2014     | 0/0                        |
| 106   | KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha                                        | 04/1994          | 355.38<br>470.21                   | -<br>-                | 03/2014     | 0/0                        |
| 107   | RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State             | 01/2004          | 915.70<br>915.70                   | -<br>-                | 03/2014     | 0/0                        |
| 108   | HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State                                       | 04/2005          | 230.03<br>230.03                   | -<br>-                | 03/2014     | 0/0                        |
| 109   | ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G <sup>1</sup> - [N22000094]RE,Uttar Pradesh | 02/2008          | 171.10<br>224.89                   | 03/2012<br>12/2013    | 03/2014     | 0/0                        |

|       |                                                                                          |                  | (Aug,2013)                         |                       |             |                            |
|-------|------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                          |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                                  | 5                     | 6           | 7                          |
| 110   | Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka            | 04/2007          | 482.00<br>482.70                   | 03/2013<br>-          | 03/2014     | 0/0                        |
| 111   | New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal         | 04/2010          | 2,069.60<br>-                      | 03/2014<br>-          | 03/2014     | 0/0                        |
| 112   | Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan            | 04/2008          | 653.19<br>653.19                   | 03/2014<br>-          | 03/2014     | 0/0                        |
| 113   | Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan            | 04/2008          | 516.23<br>516.23                   | 03/2014<br>-          | 03/2014     | 0/0                        |
| 114   | Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat                | 04/2008          | 1,389.62<br>-                      | 03/2014<br>-          | 03/2014     | 0/0                        |
| 115   | New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State                        | 04/1999          | 175.43<br>-                        | -<br>-                | 03/2014     | 0/0                        |
| 116   | Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244]ER,Multi State | 04/2009          | 257.42<br>-                        | 03/2014<br>-          | 03/2014     | 0/0                        |
| 117   | Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat                                      | 04/2010          | 279.40<br>-                        | -<br>-                | 04/2014     | 0/0                        |
| 118   | RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha                                       | 04/1999          | 166.16<br>-                        | 02/2009<br>02/2009    | 08/2014     | 0/0                        |
| 119   | KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha                       | 04/2000          | 133.41<br>207.00                   | 03/2009<br>03/2009    | 08/2014     | 0/0                        |
| 120   | ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh                                  | 09/2001          | 129.70<br>245.39                   | 12/2008<br>-          | 09/2014     | 0/0                        |
| 121   | BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra          | 03/1996          | 401.81<br>495.44                   | 03/2004<br>12/2010    | 12/2014     | 0/0                        |
| 122   | RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar                          | 04/2002          | 921.00<br>2,363.00                 | 03/2009<br>12/2012    | 12/2014     | 0/0                        |
| 123   | EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu             | 04/2006          | 495.74<br>-                        | 06/2013<br>06/2013    | 12/2014     | 0/0                        |
| 124   | Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam               | 04/1996          | 1,676.31<br>1,676.31               | 03/2009<br>-          | 12/2014     | 0/0                        |
| 125   | SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha                                 | 04/1998          | 183.23<br>-                        | 02/2015<br>-          | 02/2015     | 0/0                        |
| 126   | FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State               | 03/1984          | 520.00<br>835.04                   | 03/1995<br>-          | 03/2015     | 0/0                        |
| 127   | New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal         | 04/1983          | 36.80<br>274.41                    | -<br>-                | 03/2015     | 0/0                        |
| 128   | HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal                            | 04/1974          | 31.42<br>393.46                    | 03/2007<br>03/2007    | 03/2015     | 0/0                        |
| 129   | KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar                                     | 09/2001          | 100.00<br>492.98                   | 12/2010<br>12/2010    | 03/2015     | 0/0                        |
| 130   | NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State         | 04/2000          | 733.00<br>733.00                   | 12/2008<br>-          | 03/2015     | 0/0                        |
| 131   | NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam               | 09/2006          | 200.00<br>200.00                   | -<br>-                | 03/2015     | 0/0                        |
| 132   | KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar                                   | 04/2008          | 282.92<br>282.92                   | -<br>-                | 03/2015     | 0/0                        |
| 133   | Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan                  | 04/2008          | 829.74<br>829.74                   | 03/2015<br>-          | 03/2015     | 0/0                        |
| 134   | Katakhal to Bhairabi - [N22000126]NEFR,Assam                                             | 04/1998          | 227.90<br>227.90                   | 12/2012<br>-          | 03/2015     | 0/0                        |

|       |                                                                                        |                  | (Aug,2013)                         |                       |             |                            |
|-------|----------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                        |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                      | 3                | 4                                  | 5                     | 6           | 7                          |
| 135   | Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura                   | 04/1999          | 895.00<br>-                        | 03/2007<br>-          | 03/2015     | 0/0                        |
| 136   | New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal                              | 04/2011          | 209.77<br>-                        | -<br>-                | 03/2015     | 0/0                        |
| 137   | New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal          | 04/2012          | 283.55<br>-                        | -<br>-                | 03/2015     | 0/0                        |
| 138   | Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam                               | 04/2011          | 312.12<br>-                        | -<br>-                | 03/2015     | 0/0                        |
| 139   | Plassey-Jiaganj Doubling - [N22000220]ER,Multi State                                   | 04/2011          | 248.07<br>-                        | 03/2015<br>-          | 03/2015     | 0/0                        |
| 140   | BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam                   | 09/1997          | 1,000.00<br>1,500.00               | 04/2008<br>03/2014    | 12/2015     | 0/0                        |
| 141   | PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar                                    | 04/2001          | 624.47<br>2,921.00                 | 10/2007<br>12/2012    | 12/2015     | 0/0                        |
| 142   | BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh                          | 09/2007          | 687.20<br>-                        | 03/2010<br>-          | 12/2015     | 0/0                        |
| 143   | AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura                                   | 04/2008          | 813.34<br>813.34                   | 03/2014<br>-          | 12/2015     | 0/0                        |
| 144   | Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha                      | 04/2010          | 149.90<br>-                        | 03/2015<br>-          | 12/2015     | 0/0                        |
| 145   | Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164]SER,Jharkhand                     | 04/2010          | 309.44<br>-                        | 12/2015<br>-          | 12/2015     | 0/0                        |
| 146   | New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal       | 04/2010          | 3,951.98<br>-                      | 03/2016<br>-          | 03/2016     | 0/0                        |
| 147   | New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal               | 04/2010          | 2,619.02<br>-                      | 03/2016<br>-          | 03/2016     | 0/0                        |
| 148   | EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal | 03/2013          | 4,874.58<br>-                      | 03/2016<br>-          | 03/2016     | 0/0                        |
| 149   | Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand                     | 04/2012          | 258.20<br>-                        | -<br>-                | 03/2016     | 0/0                        |
| 150   | TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal                          | 03/1984          | 293.97<br>1,025.39                 | 06/2005<br>07/2011    | 06/2016     | 0/0                        |
| 151   | New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal       | 04/2010          | 2,397.72<br>-                      | 03/2016<br>-          | 06/2016     | 0/0                        |
| 152   | BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal                              | 03/1998          | 111.90<br>1,028.05                 | 03/2005<br>12/2008    | 12/2016     | 0/0                        |
| 153   | MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra                  | 04/2008          | 5,300.00<br>5,300.00               | 03/2014<br>03/2016    | 12/2016     | 0/0                        |
| 154   | JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur                          | 04/2003          | 727.56<br>727.53                   | 03/2011<br>03/2014    | 03/2017     | 0/0                        |
| 155   | UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh                     | 04/2006          | 325.00<br>325.00                   | 03/2010<br>03/2017    | 03/2017     | 0/0                        |
| 156   | BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram                                   | 04/2008          | 619.34<br>-                        | 04/2014<br>-          | 03/2017     | 0/0                        |
| 157   | SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim                                            | 04/2008          | 1,339.48<br>-                      | 12/2015<br>-          | 03/2017     | 0/0                        |
| 158   | New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland          | 04/2006          | 850.00<br>850.00                   | 03/2015<br>-          | 03/2017     | 0/0                        |
| 159   | Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State          | 04/2011          | 299.60<br>-                        | 03/2017<br>-          | 03/2017     | 0/0                        |

|       |                                                                                           |                  | (Aug,2013)                         |                       |             |                            |
|-------|-------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                           |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                   | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                         | 3                | 4                                  | 5                     | 6           | 7                          |
| 160   | Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State       | 04/2010          | 423.66<br>-                        | 03/2017<br>-          | 03/2017     | 0/0                        |
| 161   | UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir                     | 03/1995          | 2,500.00<br>2,500.00               | 11/2002<br>-          | 12/2017     | 0/0                        |
| 162   | Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra                    | 04/2012          | 714.10<br>-                        | -<br>12/2017          | 12/2017     | 0/0                        |
| 163   | Dholpur-Sirmuttra with extension to Gangapucity A - [N22000158]NCR,Multi State            | 04/2010          | 622.41<br>2,030.50                 | 02/2019<br>-          | 02/2019     | 0/0                        |
| 164   | Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State               | 04/2011          | 1,176.09<br>3,845.60               | 02/2020<br>-          | 02/2020     | 0/0                        |
| 165   | DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh          | 04/1995          | 304.00<br>-                        | 12/2012<br>-          | -           | 0/0                        |
| 166   | GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State                                  | 02/1997          | 386.30<br>1,038.00                 | 03/1998<br>-          | -           | 0/0                        |
| 167   | ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala                                     | 10/1998          | 550.00<br>517.70                   | -<br>-                | -           | 0/0                        |
| 168   | HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha                                          | 04/1996          | 301.64<br>-                        | -<br>09/2009          | -           | 0/0                        |
| 169   | KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand                                      | 04/2002          | 459.91<br>418.17                   | -<br>-                | -           | 0/0                        |
| 170   | RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh                                | 04/2003          | 136.62<br>-                        | 12/2007<br>03/2010    | -           | 0/0                        |
| 171   | GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand                                  | 03/1997          | 186.92<br>261.70                   | 02/2006<br>-          | -           | 0/0                        |
| 172   | OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh                       | 07/2006          | 743.00<br>-                        | 03/2008<br>06/2008    | -           | 0/0                        |
| 173   | SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh                         | 09/2006          | 324.90<br>-                        | 03/2010<br>-          | -           | 0/0                        |
| 174   | ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh                      | 03/2013          | 307.00<br>-                        | -<br>-                | -           | 0/0                        |
| 175   | CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State               | 03/2007          | 243.78<br>-                        | -<br>-                | -           | 0/0                        |
| 176   | BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh                             | 03/2008          | 195.64<br>-                        | -<br>-                | -           | 0/0                        |
| 177   | AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh                     | 03/2012          | 160.89<br>-                        | -<br>-                | -           | 0/0                        |
| 178   | CHHAPRA-BALLIA UP - [N22000134]NER,Multi State                                            | 03/2013          | 295.00<br>-                        | -<br>-                | -           | 0/0                        |
| 179   | KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh | 03/2013          | 643.00<br>-                        | -<br>-                | -           | 0/0                        |
| 180   | Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan                               | 04/2012          | 246.08<br>-                        | -<br>-                | -           | 0/0                        |
| 181   | Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State                                         | 04/2007          | 1,347.26<br>-                      | -<br>-                | -           | 0/0                        |
| 182   | Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State              | 04/2007          | 1,640.04<br>-                      | -<br>-                | -           | 0/0                        |
| 183   | Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat                                              | 04/2012          | 567.18<br>-                        | -<br>-                | -           | 0/0                        |
| 184   | Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat                                               | 04/2012          | 376.59<br>-                        | -<br>-                | -           | 0/0                        |



|       |                                                                                    |                  | (Aug,2013)                         |                       |             |                            |
|-------|------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                    |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                            | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                  | 3                | 4                                  | 5                     | 6           | 7                          |
| 185   | Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat                         | 04/2011          | 439.88<br>-                        | -<br>-                | -           | 0/0                        |
| 186   | Rajkot-Veraval,Wansjalai to Jataisar with new MM f - [N22000143]WR,Gujarat         | 04/1994          | 320.66<br>-                        | -<br>-                | -           | 0/0                        |
| 187   | Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat                                  | 04/2013          | 1,266.89<br>-                      | -<br>-                | -           | 0/0                        |
| 188   | Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat                                   | 04/2011          | 446.00<br>-                        | -<br>-                | -           | 0/0                        |
| 189   | Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State                    | 04/2012          | 2,082.75<br>-                      | -<br>-                | -           | 0/0                        |
| 190   | Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan                                      | 04/2013          | 236.39<br>-                        | -<br>-                | -           | 0/0                        |
| 191   | Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan                          | 04/2013          | 822.00<br>-                        | -<br>-                | -           | 0/0                        |
| 192   | Pushkar-Merta - [N22000151]NWR,Rajasthan                                           | 04/2013          | 323.00<br>-                        | -<br>-                | -           | 0/0                        |
| 193   | Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur - [N22000152]NWR,Rajasthan | 04/2013          | 456.00<br>-                        | -<br>-                | -           | 0/0                        |
| 194   | Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And - [N22000153]NWR,Rajasthan       | 04/2010          | 739.65<br>-                        | -<br>-                | -           | 0/0                        |
| 195   | Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan                      | 04/2011          | 239.73<br>-                        | -<br>-                | -           | 0/0                        |
| 196   | Ajmer-Bangurgram - [N22000155]NWR,Rajasthan                                        | 04/2011          | 213.39<br>-                        | -<br>-                | -           | 0/0                        |
| 197   | Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan                          | 04/2012          | 288.97<br>-                        | -<br>-                | -           | 0/0                        |
| 198   | Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan                                 | 04/2013          | 242.09<br>-                        | -<br>-                | -           | 0/0                        |
| 199   | Bowaichandi-Arambagh - [N22000159]SER,West Bengal                                  | 04/2010          | 267.37<br>-                        | -<br>-                | -           | 0/0                        |
| 200   | Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State            | 04/2010          | 553.63<br>-                        | -<br>-                | -           | 0/0                        |
| 201   | Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal                    | 04/2011          | 289.64<br>-                        | -<br>-                | -           | 0/0                        |
| 202   | Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal                      | 04/2010          | 146.95<br>-                        | 06/2013<br>-          | -           | 0/0                        |
| 203   | Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar                                       | 04/2008          | 490.80<br>-                        | -<br>-                | -           | 0/0                        |
| 204   | Nawada-Laxmipur (NL) - [N22000167]SER,Bihar                                        | 04/2008          | 620.57<br>-                        | -<br>-                | -           | 0/0                        |
| 205   | Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar                          | 04/2008          | 445.25<br>-                        | -<br>-                | -           | 0/0                        |
| 206   | Gaya-Chatra (NL) - [N22000169]ECOR,Multi State                                     | 04/2008          | 415.67<br>-                        | -<br>-                | -           | 0/0                        |
| 207   | Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar                                      | 04/2008          | 326.20<br>-                        | -<br>-                | -           | 0/0                        |
| 208   | Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar                                   | 04/1999          | 175.69<br>-                        | -<br>-                | -           | 0/0                        |
| 209   | Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar                                   | 04/2006          | 285.07<br>-                        | -<br>-                | -           | 0/0                        |

|       |                                                                                         |                  | (Aug,2013)                         |                       |             |                            |
|-------|-----------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                         |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                 | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                       | 3                | 4                                  | 5                     | 6           | 7                          |
| 210   | Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar                                   | 04/2005          | 366.73<br>-                        | -<br>-                | -           | 0/0                        |
| 211   | Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar                                          | 04/2006          | 211.00<br>-                        | -<br>-                | -           | 0/0                        |
| 212   | Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar                      | 04/2008          | 678.62<br>-                        | -<br>-                | -           | 0/0                        |
| 213   | Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar                        | 04/2008          | 228.05<br>-                        | -<br>-                | -           | 0/0                        |
| 214   | Araria-Supaul (NL) - [N22000177]ECR,Bihar                                               | 04/2008          | 304.41<br>-                        | -<br>-                | -           | 0/0                        |
| 215   | Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar                                          | 04/2008          | 192.56<br>-                        | -<br>-                | -           | 0/0                        |
| 216   | Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar                                       | 04/2008          | 281.30<br>-                        | -<br>-                | -           | 0/0                        |
| 217   | Sakri-Nirmali and Jhanjharpur-Laukahabazar and Sah - [N22000180]ECR,Bihar               | 04/2004          | 372.14<br>-                        | -<br>-                | -           | 0/0                        |
| 218   | Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar     | 04/2009          | 470.00<br>-                        | -<br>-                | -           | 0/0                        |
| 219   | Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar                                  | 04/2013          | 213.01<br>-                        | -<br>-                | -           | 0/0                        |
| 220   | New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State                  | 04/2013          | 1,798.00<br>-                      | -<br>-                | -           | 0/0                        |
| 221   | Attippattu-Puttur - [N22000184]SR,Tamil Nadu                                            | 04/2008          | 446.87<br>-                        | -<br>-                | -           | 0/0                        |
| 222   | Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State                          | 04/2008          | 523.52<br>-                        | -<br>-                | -           | 0/0                        |
| 223   | Sriperumbudur-Guduvanchery with spur to Irungattukottai-Ava - [N22000186]SR,Tamil Nadu  | 04/2013          | 839.00<br>-                        | -<br>-                | -           | 0/0                        |
| 224   | Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu                         | 04/1999          | 198.68<br>-                        | -<br>-                | -           | 0/0                        |
| 225   | Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu              | 04/1999          | 271.24<br>-                        | -<br>-                | -           | 0/0                        |
| 226   | Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State                    | 04/2008          | 822.39<br>-                        | -<br>-                | -           | 0/0                        |
| 227   | Kuruppanthara-Chingavanam - [N22000190]SR,Multi State                                   | 04/2007          | 270.14<br>-                        | -<br>-                | -           | 0/0                        |
| 228   | Kumbalam-Turavur - [N22000191]SR,Kerala                                                 | 04/2011          | 252.96<br>-                        | -<br>-                | -           | 0/0                        |
| 229   | New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal                  | 04/2010          | 221.42<br>-                        | -<br>-                | -           | 0/0                        |
| 230   | Agartala-Akhaura NL - [N22000195]NEFR,Tripura                                           | 04/2012          | 252.00<br>-                        | -<br>-                | -           | 0/0                        |
| 231   | Dimapur-Tizit NL - [N22000196]NEFR,Nagaland                                             | 04/2013          | 4,274.00<br>-                      | -<br>-                | -           | 0/0                        |
| 232   | Erode-Palani - [N22000199]SR,Tamil Nadu                                                 | 04/2008          | 288.57<br>-                        | -<br>-                | -           | 0/0                        |
| 233   | Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu                                        | 04/2008          | 164.41<br>-                        | -<br>-                | -           | 0/0                        |
| 234   | Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu | 04/2007          | 247.00<br>-                        | -<br>-                | -           | 0/0                        |

|       |                                                                                               |                  | (Aug,2013)                         |                       |             |                            |
|-------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                               |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                             | 3                | 4                                  | 5                     | 6           | 7                          |
| 235   | Chengannur-Chingavanam - [N22000203]SR,Kerala                                                 | 04/2006          | 191.72<br>-                        | -<br>-                | -           | 0/0                        |
| 236   | Ernakulam-Kumbalam - [N22000204]SR,Kerala                                                     | 04/2010          | 189.24<br>-                        | -<br>-                | -           | 0/0                        |
| 237   | New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya                             | 04/2010          | 4,083.02<br>-                      | -<br>-                | -           | 0/0                        |
| 238   | New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State                         | 04/2010          | 242.22<br>-                        | -<br>-                | -           | 0/0                        |
| 239   | New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State                          | 04/2010          | 241.52<br>-                        | -<br>-                | -           | 0/0                        |
| 240   | Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State                                        | 04/2011          | 165.82<br>-                        | -<br>-                | -           | 0/0                        |
| 241   | New Jalpaiguri-Siliguri-New Bongaigaon including B - [N22000209]NEFR,Multi State              | 04/1999          | 523.17<br>-                        | -<br>-                | -           | 0/0                        |
| 242   | Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam                                  | 04/2012          | 246.07<br>-                        | -<br>-                | -           | 0/0                        |
| 243   | Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal           | 04/2009          | 573.78<br>-                        | -<br>-                | -           | 0/0                        |
| 244   | Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP,Andhra Pradesh | 04/2012          | 632.68<br>-                        | 04/2012<br>-          | -           | 0/0                        |
| 245   | Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State                               | 04/2011          | 601.43<br>-                        | -<br>-                | -           | 0/0                        |
| 246   | Lakshmikantapur-Namkhana subsequently MM for Namkh - [N22000216]ER,Multi State                | 04/1999          | 406.99<br>-                        | -<br>-                | -           | 0/0                        |
| 247   | Sultanganj-Katuria via Asarganj, Tarapur And Belha - [N22000217]ER,Multi State                | 04/2007          | 450.00<br>-                        | -<br>-                | -           | 0/0                        |
| 248   | Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State                                  | 04/2010          | 172.03<br>-                        | -<br>-                | -           | 0/0                        |
| 249   | Pirpainti-Jasidih - [N22000219]ER,Multi State                                                 | 04/2013          | 915.98<br>-                        | -<br>-                | -           | 0/0                        |
| 250   | Bandel-Boinchi 3rd line - [N22000221]ER,Multi State                                           | 04/2011          | 288.35<br>-                        | -<br>-                | -           | 0/0                        |
| 251   | Pirpainti-Bhagalpur - [N22000222]ER,Multi State                                               | 04/2011          | 261.38<br>-                        | -<br>-                | -           | 0/0                        |
| 252   | Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State               | 04/2000          | 157.17<br>-                        | -<br>-                | -           | 0/0                        |
| 253   | Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER,Multi State       | 04/2001          | 923.52<br>-                        | -<br>-                | -           | 0/0                        |
| 254   | Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER,Multi State      | 04/2005          | 595.91<br>-                        | -<br>-                | -           | 0/0                        |
| 255   | Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER,Multi State      | 04/2010          | 174.56<br>-                        | -<br>-                | -           | 0/0                        |
| 256   | Sondalia-Champapur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State        | 04/2010          | 277.28<br>-                        | -<br>-                | -           | 0/0                        |
| 257   | Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER,Multi State      | 04/2010          | 296.44<br>-                        | -<br>-                | -           | 0/0                        |
| 258   | Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State        | 04/2010          | 157.94<br>-                        | -<br>-                | -           | 0/0                        |
| 259   | Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra                                         | 04/2008          | 697.00<br>-                        | -<br>-                | -           | 0/0                        |

|       |                                                                                          |                  | (Aug,2013)                         |                       |             |                            |
|-------|------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                          |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                  | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                        | 3                | 4                                  | 5                     | 6           | 7                          |
| 260   | Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra                                       | 04/2011          | 277.70<br>-                        | -<br>-                | -           | 0/0                        |
| 261   | Bariarpur-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State           | 04/2007          | 450.55<br>-                        | -<br>-                | -           | 0/0                        |
| 262   | Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State                                | 04/2010          | 365.17<br>-                        | -<br>-                | -           | 0/0                        |
| 263   | Hansdiha-Godda NL - [N22000236]ER,Multi State                                            | 04/2011          | 267.09<br>-                        | -<br>-                | -           | 0/0                        |
| 264   | Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State                                   | 04/2011          | 193.44<br>-                        | -<br>-                | -           | 0/0                        |
| 265   | Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State                                  | 04/2011          | 175.80<br>-                        | -<br>-                | -           | 0/0                        |
| 266   | New Alipur to Akra, MM for Budge Budge-Pujali NL, - [N22000240]ER,Multi State            | 04/2010          | 494.54<br>-                        | -<br>-                | -           | 0/0                        |
| 267   | Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State | 04/2000          | 297.47<br>-                        | -<br>-                | -           | 0/0                        |
| 268   | Chandpara-Bangaon doubling with extension to Chandb - [N22000242]ER,Multi State          | 04/2003          | 337.96<br>-                        | -<br>-                | -           | 0/0                        |
| 269   | Magrahat-Diamond Harbour with MM Sangrampur-Krishna - [N22000243]ER,Multi State          | 04/2009          | 493.96<br>-                        | -<br>-                | -           | 0/0                        |
| 270   | Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State                                 | 04/2010          | 169.82<br>-                        | -<br>-                | -           | 0/0                        |
| 271   | 3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra                            | 04/2011          | 182.06<br>-                        | -<br>-                | -           | 0/0                        |
| 272   | Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State         | 04/2010          | 268.52<br>-                        | -<br>-                | -           | 0/0                        |
| 273   | Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State | 04/2011          | 166.89<br>-                        | -<br>-                | -           | 0/0                        |
| 274   | Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra                                 | 04/2012          | 297.85<br>-                        | -<br>-                | -           | 0/0                        |
| 275   | PEN ROHA DOUBLING - [N22000254]CR,Multi State                                            | 04/2007          | 203.00<br>-                        | -<br>-                | -           | 0/0                        |
| 276   | Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka                               | 04/2011          | 913.00<br>-                        | -<br>-                | -           | 0/0                        |
| 277   | Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka                               | 04/2007          | 179.65<br>-                        | -<br>-                | -           | 0/0                        |
| 278   | Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka                                           | 04/2010          | 377.93<br>-                        | -<br>-                | -           | 0/0                        |
| 279   | Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh                                    | 04/2013          | 1,112.00<br>-                      | -<br>-                | -           | 0/0                        |
| 280   | Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh                                  | 04/2013          | 723.00<br>-                        | -<br>-                | -           | 0/0                        |
| 281   | Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State          | 04/2012          | 1,054.35<br>-                      | -<br>-                | -           | 0/0                        |
| 282   | Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State                               | 04/2008          | 184.26<br>-                        | -<br>-                | -           | 0/0                        |
| 283   | Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh                                    | 04/2012          | 923.23<br>-                        | -<br>-                | -           | 0/0                        |
| 284   | Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh                                  | 04/2011          | 283.54<br>-                        | -<br>-                | -           | 0/0                        |

|       |                                                                                         |                  | (Aug,2013)                         |                       |             |                            |
|-------|-----------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                         |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                 | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                       | 3                | 4                                  | 5                     | 6           | 7                          |
| 285   | Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh                              | 04/2012          | 289.79<br>-                        | -<br>-                | -           | 0/0                        |
| 286   | ansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur M - [N22000268]NR,Punjab     | 04/2009          | 396.04<br>-                        | -<br>-                | -           | 0/0                        |
| 287   | Grade Seperator at Dayabasti - [N22000269]NR,Delhi                                      | 04/1999          | 159.20<br>-                        | -<br>-                | -           | 0/0                        |
| 288   | Faizabad-Lalgarj via Akbarganj, Maharajganj and Raebareli - [N22000270]NR,Uttar Pradesh | 04/2013          | 654.00<br>-                        | -<br>-                | -           | 0/0                        |
| 289   | Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State                       | 04/2013          | 1,239.00<br>-                      | -<br>-                | -           | 0/0                        |
| 290   | Rohtak-Meham Hansi - [N22000272]NR,Haryana                                              | 04/2012          | 287.00<br>-                        | -<br>-                | -           | 0/0                        |
| 291   | Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh                             | 04/2008          | 1,046.88<br>-                      | -<br>-                | -           | 0/0                        |
| 292   | Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State                         | 04/2007          | 336.91<br>-                        | -<br>-                | -           | 0/0                        |
| 293   | Chikballa-pur-Puttaparthry-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka          | 04/2013          | 558.00<br>-                        | -<br>-                | -           | 0/0                        |
| 294   | Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State                              | 04/2013          | 296.00<br>-                        | -<br>-                | -           | 0/0                        |
| 295   | Shimoga-Harihar NL - [N22000278]SWR,Karnataka                                           | 04/2011          | 562.74<br>-                        | -<br>-                | -           | 0/0                        |
| 296   | Rayadurga-Tumkur NL - [N22000279]SWR,Multi State                                        | 04/2007          | 970.34<br>-                        | -<br>-                | -           | 0/0                        |
| 297   | White Field-Kolar NL - [N22000280]SWR,Karnataka                                         | 04/2011          | 341.05<br>-                        | -<br>-                | -           | 0/0                        |
| 298   | Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi                         | 04/2012          | 295.68<br>-                        | -<br>-                | -           | 0/0                        |
| 299   | Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh                                      | 04/2013          | 829.00<br>-                        | -<br>-                | -           | 0/0                        |
| 300   | Mudkhed-Parbhani - [N22000283](SCR),Maharashtra                                         | 04/2011          | 390.60<br>-                        | -<br>-                | -           | 0/0                        |
| 301   | Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh                                      | 04/2012          | 153.00<br>-                        | -<br>-                | -           | 0/0                        |
| 302   | Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh                                | 04/2011          | 1,313.48<br>-                      | -<br>-                | -           | 0/0                        |
| 303   | Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh                          | 04/2010          | 337.49<br>-                        | -<br>-                | -           | 0/0                        |
| 304   | Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State           | 04/2008          | 2,050.00<br>-                      | -<br>-                | -           | 0/0                        |
| 305   | Haridwar-Laksar - [N22000289]NR,Uttarakhand                                             | 04/2012          | 219.83<br>-                        | -<br>-                | -           | 0/0                        |
| 306   | Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State | 04/2010          | 338.54<br>-                        | -<br>-                | -           | 0/0                        |
| 307   | Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State                        | 04/2008          | 165.65<br>-                        | -<br>-                | -           | 0/0                        |
| 308   | Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana                           | 04/2013          | 400.00<br>-                        | -<br>-                | -           | 0/0                        |
| 309   | Yamunanagar-Chandigarh via Sadhaura Narayargarh - [N22000293]NR,Multi State             | 04/2013          | 876.00<br>-                        | -<br>-                | -           | 0/0                        |

|       |                                                                                |                  | (Aug,2013)                         |                       |             |                            |
|-------|--------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                        | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                              | 3                | 4                                  | 5                     | 6           | 7                          |
| 310   | Unchahar-Amethi - [N22000294]NR,Uttar Pradesh                                  | 04/2012          | 380.00<br>-                        | -<br>-                | -           | 0/0                        |
| 311   | Qadian-Beas - [N22000295]NR,Punjab                                             | 04/2011          | 205.22<br>-                        | -<br>-                | -           | 0/0                        |
| 312   | Chandigarh-Baddi NL - [N22000296]NR,Multi State                                | 04/2007          | 328.14<br>-                        | -<br>-                | -           | 0/0                        |
| 313   | Hospet-Hubli-Londa-Vascodagama DL - [N22000297]SWR,Karnataka                   | 04/2010          | 2,127.00<br>-                      | -<br>-                | -           | 0/0                        |
| 314   | Gadag-Wadi NL - [N22000299]SWR,Karnataka                                       | 04/2013          | 1,117.00<br>-                      | -<br>-                | -           | 0/0                        |
| 315   | Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka                       | 04/2013          | 327.25<br>-                        | -<br>-                | -           | 0/0                        |
| 316   | Monigram- Nimtita - [N22000301]ER,Multi State                                  | 04/2012          | 250.93<br>-                        | -<br>-                | -           | 0/0                        |
| 317   | Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal                   | 04/2012          | 255.64<br>-                        | -<br>-                | -           | 0/0                        |
| 318   | VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State                              | 04/1990          | 155.66<br>356.87                   | -<br>03/2010          | -           | 0/0                        |
| 319   | AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra                   | 02/1997          | 353.08<br>514.68                   | -<br>-                | -           | 0/0                        |
| 320   | NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State                           | 03/1981          | 37.68<br>450.00                    | 07/2012<br>-          | -           | 0/0                        |
| 321   | HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka                                | 04/1997          | 227.00<br>997.58                   | -<br>-                | -           | 0/0                        |
| 322   | KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand               | 03/1999          | 491.19<br>2,957.21                 | 07/2005<br>-          | -           | 0/0                        |
| 323   | LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State            | 09/1998          | 925.00<br>-                        | 05/2008<br>03/2011    | -           | 0/0                        |
| 324   | JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar               | 04/1997          | 233.00<br>501.69                   | 03/2012<br>08/2012    | -           | 0/0                        |
| 325   | KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar                   | 04/1997          | 78.23<br>162.87                    | -<br>-                | -           | 0/0                        |
| 326   | TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu             | 09/1995          | 100.00<br>100.00                   | -<br>-                | -           | 0/0                        |
| 327   | KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh                 | 12/2001          | 330.00<br>1,047.00                 | -<br>-                | -           | 0/0                        |
| 328   | BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka                  | 02/1999          | 138.00<br>901.62                   | -<br>-                | -           | 0/0                        |
| 329   | HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar                  | 04/2003          | 324.66<br>528.65                   | -<br>-                | -           | 0/0                        |
| 330   | DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar                           | 04/2001          | 104.79<br>-                        | -<br>-                | -           | 0/0                        |
| 331   | RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh                   | 04/2001          | 727.13<br>727.13                   | -<br>-                | -           | 0/0                        |
| 332   | TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha                          | 04/2005          | 726.96<br>810.78                   | -<br>-                | -           | 0/0                        |
| 333   | MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh             | 04/2006          | 378.56<br>671.82                   | -<br>-                | -           | 0/0                        |
| 334   | MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDIL'-A - [N22000079]SR,Tamil Nadu | 09/2007          | 404.19<br>404.19                   | -<br>-                | -           | 0/0                        |

|       |                                                                                             |                  | (Aug,2013)                         |                       |             |                            |
|-------|---------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                             |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                     | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                           | 3                | 4                                  | 5                     | 6           | 7                          |
| 335   | TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu                            | 09/2006          | 125.00<br>125.00                   | -<br>-                | -           | 0/0                        |
| 336   | TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu                                            | 09/2006          | 456.00<br>456.00                   | -<br>-                | -           | 0/0                        |
| 337   | NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar                  | 09/2006          | 300.00<br>300.00                   | -<br>-                | -           | 0/0                        |
| 338   | Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh                               | 04/2008          | 603.04<br>603.04                   | 03/2012<br>-          | -           | 0/0                        |
| 339   | Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat                  | 04/2008          | 318.24<br>-                        | 03/2012<br>-          | -           | 0/0                        |
| 340   | Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat                  | 04/2006          | 117.36<br>196.95                   | 03/2011<br>-          | -           | 0/0                        |
|       | Total                                                                                       |                  | 146,842.88<br>-                    |                       |             | 0/0                        |
|       |                                                                                             |                  |                                    |                       |             |                            |
|       | <u>Road Transport And Highways</u>                                                          |                  |                                    |                       |             |                            |
| 341   | VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir | 12/2003          | 166.27<br>-                        | 03/2008<br>-          | 02/2008     | 0/0                        |
| 342   | SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal                                   | 12/2003          | 225.00<br>-                        | 07/2008<br>-          | 03/2013     | 0/0                        |
| 343   | GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh                                    | 12/2003          | 300.93<br>-                        | 10/2009<br>-          | 06/2013     | 0/0                        |
| 344   | Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh                                | 02/2010          | 390.56<br>-                        | 02/2012<br>-          | 06/2013     | 0/0                        |
| 345   | SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha                         | 04/2000          | 225.00<br>-                        | 04/2004<br>-          | 09/2013     | 0/0                        |
| 346   | PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab                       | 12/2003          | 284.00<br>-                        | 05/2008<br>-          | 09/2013     | 0/0                        |
| 347   | NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam                                             | 12/2003          | 225.00<br>-                        | 06/2008<br>-          | 09/2013     | 0/0                        |
| 348   | THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu                                    | 03/2005          | 280.00<br>-                        | 06/2009<br>-          | 09/2013     | 0/0                        |
| 349   | GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha                                       | 04/2000          | 263.27<br>-                        | 02/2004<br>-          | 09/2013     | 0/0                        |
| 350   | BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha                  | 04/2000          | 228.70<br>-                        | 02/2004<br>-          | 09/2013     | 0/0                        |
| 351   | Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan                                         | 11/2009          | 795.00<br>-                        | 05/2012<br>-          | 09/2013     | 0/0                        |
| 352   | Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan                                               | 06/2010          | 792.06<br>-                        | 12/2012<br>-          | 09/2013     | 0/0                        |
| 353   | New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu                  | 09/2010          | 1,655.00<br>-                      | 09/2013<br>-          | 09/2013     | 0/0                        |
| 354   | CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh             | 11/2010          | 1,585.00<br>-                      | 05/2013<br>-          | 09/2013     | 0/0                        |
| 355   | JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan                                                  | 08/2010          | 267.81<br>-                        | 02/2013<br>-          | 09/2013     | 0/0                        |
| 356   | BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh                                             | 03/2011          | 1,046.00<br>-                      | 09/2013<br>-          | 09/2013     | 0/0                        |

|       |                                                                                               |                  | (Aug,2013)                         |                       |             |                            |
|-------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                               |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                             | 3                | 4                                  | 5                     | 6           | 7                          |
| 357   | HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka                          | 04/2000          | 241.00 -                           | 08/2004 07/2010       | 10/2013     | 0/0                        |
| 358   | HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka                     | 04/2000          | 318.00 -                           | 08/2004 -             | 10/2013     | 0/0                        |
| 359   | DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana                                     | 04/2007          | 486.00 -                           | 05/2010 -             | 10/2013     | 0/0                        |
| 360   | Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra                                             | 11/2009          | 1,110.00 -                         | 05/2012 -             | 10/2013     | 0/0                        |
| 361   | Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand                                                 | 08/2010          | 625.07 -                           | 01/2013 -             | 10/2013     | 0/0                        |
| 362   | DEOLI-KOTA - [N24000148]NHAI,Rajasthan                                                        | 01/2011          | 593.00 -                           | 07/2013 -             | 10/2013     | 0/0                        |
| 363   | PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar                                                    | 08/2010          | 671.30 -                           | 02/2013 -             | 10/2013     | 0/0                        |
| 364   | Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu                                               | 04/2011          | 571.00 -                           | 10/2013 -             | 10/2013     | 0/0                        |
| 365   | BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh                                                | 10/2011          | 209.00 -                           | 01/2013 -             | 10/2013     | 0/0                        |
| 366   | HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh                  | 03/2005          | 220.00 -                           | 09/2007 -             | 11/2013     | 0/0                        |
| 367   | Talegaon-amravati - [N24000140]NHAI,Maharashtra                                               | 11/2009          | 567.00 -                           | 11/2013 -             | 11/2013     | 0/0                        |
| 368   | ROHTAK-BAWAL - [N24000169]NHAI,Haryana                                                        | 05/2011          | 650.00 -                           | 11/2013 -             | 11/2013     | 0/0                        |
| 369   | Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar                                                 | 05/2011          | 511.54 -                           | 11/2013 -             | 11/2013     | 0/0                        |
| 370   | 2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar                                  | 05/2011          | 511.54 -                           | 11/2013 -             | 11/2013     | 0/0                        |
| 371   | KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar           | 12/2003          | 240.00 -                           | 10/2008 -             | 12/2013     | 0/0                        |
| 372   | AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh                           | 03/2005          | 190.00 -                           | 01/2009 -             | 12/2013     | 0/0                        |
| 373   | FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar                                   | 12/2003          | 332.94 -                           | 09/2008 -             | 12/2013     | 0/0                        |
| 374   | KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan                                    | 12/2003          | 275.00 -                           | 10/2008 -             | 12/2013     | 0/0                        |
| 375   | NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam                                               | 12/2003          | 200.00 -                           | 06/2008 -             | 12/2013     | 0/0                        |
| 376   | NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam                                            | 12/2003          | 264.72 -                           | 06/2008 -             | 12/2013     | 0/0                        |
| 377   | DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam                               | 12/2003          | 160.00 -                           | 05/2008 -             | 12/2013     | 0/0                        |
| 378   | DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam                                          | 12/2003          | 200.00 -                           | 06/2008 -             | 12/2013     | 0/0                        |
| 379   | LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh | 12/2003          | 407.60 -                           | 06/2010 -             | 12/2013     | 0/0                        |
| 380   | JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh                                  | 12/2003          | 355.06 -                           | 09/2009 -             | 12/2013     | 0/0                        |
| 381   | SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu                        | 03/2005          | 941.00 -                           | 01/2011 -             | 12/2013     | 0/0                        |



|       |                                                                                     |                  | (Aug,2013)                         |                       |             |                            |
|-------|-------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                     |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                             | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                   | 3                | 4                                  | 5                     | 6           | 7                          |
| 382   | PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra         | 03/2005          | 940.00                             | 07/2012               | 12/2013     | 0/0                        |
| 383   | Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra     | 04/2010          | 1,170.52                           | 06/2011               | 12/2013     | 0/0                        |
| 384   | Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat      | 03/2010          | 1,509.10                           | 09/2012               | 12/2013     | 0/0                        |
| 385   | Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State                  | 04/2009          | 1,673.70                           | 10/2011               | 12/2013     | 0/0                        |
| 386   | Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State             | 02/2009          | 1,693.75                           | 08/2011               | 12/2013     | 0/0                        |
| 387   | Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana               | 05/2009          | 1,108.00                           | 11/2011               | 12/2013     | 0/0                        |
| 388   | Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh                            | 10/2010          | 1,175.00                           | 04/2013               | 12/2013     | 0/0                        |
| 389   | CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu | 09/2010          | 852.00                             | 03/2013               | 12/2013     | 0/0                        |
| 390   | AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab                                         | 05/2010          | 705.00                             | 11/2012               | 12/2013     | 0/0                        |
| 391   | 4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat                         | 12/2010          | 1,008.50                           | 06/2013               | 12/2013     | 0/0                        |
| 392   | 4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat                 | 03/2011          | 785.50                             | 08/2013               | 12/2013     | 0/0                        |
| 393   | SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu     | 06/2011          | 535.00                             | 12/2013               | 12/2013     | 0/0                        |
| 394   | SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu     | 09/2011          | 1,250.00                           | 12/2013               | 12/2013     | 0/0                        |
| 395   | DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu     | 06/2011          | 600.00                             | 06/2013               | 12/2013     | 0/0                        |
| 396   | Trichy Bypass - [N24000176]NHAI,Tamil Nadu                                          | 05/2010          | 374.00                             | 05/2013               | 12/2013     | 0/0                        |
| 397   | SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat                                   | 09/2010          | 805.39                             | 03/2013               | 12/2013     | 0/0                        |
| 398   | 4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar                                 | 01/2011          | 575.00                             | 07/2013               | 12/2013     | 0/0                        |
| 399   | BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha                                        | 03/2011          | 500.29                             | 08/2013               | 12/2013     | 0/0                        |
| 400   | SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat                                     | 09/2010          | 805.39                             | 12/2013               | 12/2013     | 0/0                        |
| 401   | JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya                                       | 01/2011          | 536.00                             | 01/2014               | 01/2014     | 0/0                        |
| 402   | PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra                                  | 09/2011          | 835.00                             | 01/2014               | 01/2014     | 0/0                        |
| 403   | 2-LANNING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh           | 07/2012          | 291.36                             | 01/2014               | 01/2014     | 0/0                        |
| 404   | INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh                                 | 11/2010          | 325.00                             | 05/2013               | 02/2014     | 0/0                        |
| 405   | 2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya                             | 02/2011          | 226.00                             | 02/2014               | 02/2014     | 0/0                        |
| 406   | 4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand                            | 02/2012          | 398.00                             | 02/2014               | 02/2014     | 0/0                        |

|       |                                                                                               |                  | (Aug,2013)                         |                       |             |                            |
|-------|-----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                               |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                       | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                             | 3                | 4                                  | 5                     | 6           | 7                          |
| 407   | SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam                      | 12/2003          | 157.47 -                           | 09/2007 -             | 03/2014     | 0/0                        |
| 408   | GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh     | 12/2003          | 155.00 -                           | 09/2008 -             | 03/2014     | 0/0                        |
| 409   | BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam             | 12/2003          | 230.00 -                           | 06/2005 -             | 03/2014     | 0/0                        |
| 410   | BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam                           | 12/2003          | 195.00 -                           | 06/2008 -             | 03/2014     | 0/0                        |
| 411   | BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam                          | 12/2003          | 237.80 -                           | 06/2008 -             | 03/2014     | 0/0                        |
| 412   | RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh | 12/2003          | 251.03 -                           | 10/2008 -             | 03/2014     | 0/0                        |
| 413   | GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam                                             | 12/2003          | 175.96 -                           | 04/2008 -             | 03/2014     | 0/0                        |
| 414   | SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam                                             | 12/2003          | 245.00 -                           | 03/2008 -             | 03/2014     | 0/0                        |
| 415   | GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam                                            | 12/2003          | 198.16 -                           | 04/2008 -             | 03/2014     | 0/0                        |
| 416   | NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra                                      | 03/2005          | 168.00 -                           | 12/2008 -             | 03/2014     | 0/0                        |
| 417   | AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh                  | 12/2003          | 348.16 -                           | 09/2007 -             | 03/2014     | 0/0                        |
| 418   | TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu                                             | 03/2005          | 516.00 -                           | 07/2010 -             | 03/2014     | 0/0                        |
| 419   | Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu                                           | 04/2009          | 353.37 -                           | 10/2011 -             | 03/2014     | 0/0                        |
| 420   | WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra                         | 02/2011          | 193.45 -                           | 11/2012 -             | 03/2014     | 0/0                        |
| 421   | MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh                                             | 04/2010          | 1,267.00 -                         | 06/2013 -             | 03/2014     | 0/0                        |
| 422   | 2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar                                            | 05/2011          | 351.54 -                           | 05/2013 -             | 03/2014     | 0/0                        |
| 423   | VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State                         | 09/2011          | 2,848.00 -                         | 03/2014 -             | 03/2014     | 0/0                        |
| 424   | PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar                                | 09/2011          | 574.00 -                           | 03/2014 -             | 03/2014     | 0/0                        |
| 425   | MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State                                          | 09/2011          | 754.00 -                           | 03/2013 -             | 03/2014     | 0/0                        |
| 426   | HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand                          | 11/2011          | 478.00 -                           | 10/2013 -             | 03/2014     | 0/0                        |
| 427   | HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam                          | 12/2003          | 212.00 -                           | 09/2007 -             | 04/2014     | 0/0                        |
| 428   | PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra                                               | 10/2010          | 1,724.55 -                         | 03/2013 -             | 04/2014     | 0/0                        |
| 429   | 2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar                                     | 05/2011          | 664.00 -                           | 02/2014 -             | 04/2014     | 0/0                        |
| 430   | 2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar                                     | 10/2011          | 375.09 -                           | 04/2014 -             | 04/2014     | 0/0                        |
| 431   | 2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State       | 04/2012          | 624.00 -                           | 04/2014 -             | 04/2014     | 0/0                        |

|       |                                                                                       |                  | (Aug,2013)                         |                       |             |                            |
|-------|---------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                       |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                               | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                     | 3                | 4                                  | 5                     | 6           | 7                          |
| 432   | HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam        | 12/2003          | 280.00 -                           | 02/2009<br>03/2014    | 05/2014     | 0/0                        |
| 433   | NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam                                        | 12/2003          | 208.00 -                           | 04/2008 -             | 05/2014     | 0/0                        |
| 434   | HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam                                   | 12/2003          | 196.00 -                           | 07/2009 -             | 05/2014     | 0/0                        |
| 435   | SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh                 | 11/2011          | 1,535.00 -                         | 05/2014 -             | 05/2014     | 0/0                        |
| 436   | 2laning with PS Gopalganj-Chhapra - [N24000190]NHAI,Bihar                             | 12/2011          | 325.00 -                           | 05/2014 -             | 05/2014     | 0/0                        |
| 437   | SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha                  | 11/2011          | 909.00 -                           | 05/2014 -             | 05/2014     | 0/0                        |
| 438   | DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar   | 12/2003          | 300.00 -                           | 10/2008 -             | 06/2014     | 0/0                        |
| 439   | MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam          | 12/2003          | 155.04 -                           | 11/2008 -             | 06/2014     | 0/0                        |
| 440   | Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh  | 05/2009          | 572.30 -                           | 10/2011 -             | 06/2014     | 0/0                        |
| 441   | JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir                | 07/2010          | 1,813.76 -                         | 07/2013 -             | 06/2014     | 0/0                        |
| 442   | GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh                               | 02/2011          | 1,141.00 -                         | 08/2013 -             | 06/2014     | 0/0                        |
| 443   | kandla - Mundra port - [N24000175]NHAI,Gujarat                                        | 01/2011          | 953.88 -                           | 07/2013 -             | 06/2014     | 0/0                        |
| 444   | SNG toBANL - [N24000189]NHAI,Jammu and Kashmir                                        | 06/2011          | 1,100.70 -                         | 06/2014 -             | 06/2014     | 0/0                        |
| 445   | BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan                                      | 12/2011          | 2,388.00 -                         | 06/2014 -             | 06/2014     | 0/0                        |
| 446   | six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State           | 12/2011          | 1,047.00 -                         | 06/2014 -             | 06/2014     | 0/0                        |
| 447   | PANVEL-INDAPUR - [N24000216]NHAI,Multi State                                          | 12/2011          | 942.69 -                           | 06/2014 -             | 06/2014     | 0/0                        |
| 448   | 4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka          | 03/2011          | 359.00 -                           | 09/2013 -             | 07/2014     | 0/0                        |
| 449   | LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh                                    | 07/1999          | 635.90 -                           | 07/2012 -             | 07/2014     | 0/0                        |
| 450   | KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal                                  | 02/2012          | 702.16 -                           | 07/2014 -             | 07/2014     | 0/0                        |
| 451   | 2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar           | 07/2012          | 356.40 -                           | 07/2014 -             | 07/2014     | 0/0                        |
| 452   | 2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh                        | 01/2013          | 373.47 -                           | 07/2014 -             | 07/2014     | 0/0                        |
| 453   | DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State      | 12/2003          | 232.45 -                           | 09/2010 -             | 08/2014     | 0/0                        |
| 454   | LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh      | 12/2003          | 263.17 -                           | 09/2009 -             | 09/2014     | 0/0                        |
| 455   | 6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal                  | 04/2012          | 1,396.18 -                         | 09/2014 -             | 09/2014     | 0/0                        |
| 456   | 4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat | 03/2012          | 828.00 -                           | 09/2014 -             | 09/2014     | 0/0                        |

|       |                                                                                              |                  | (Aug,2013)                         |                       |             |                            |
|-------|----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                              |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                                  | 5                     | 6           | 7                          |
| 457   | REENGUS SIKAR - [N24000227]NHAI,Rajasthan                                                    | 03/2012          | 333.51<br>-                        | 09/2014<br>-          | 09/2014     | 0/0                        |
| 458   | PANIPAT-ROHTAK - [N24000151]NHAI,Haryana                                                     | 04/2011          | 807.00<br>-                        | 10/2014<br>-          | 10/2014     | 0/0                        |
| 459   | NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra                                        | 04/2012          | 484.19<br>-                        | 10/2014<br>-          | 10/2014     | 0/0                        |
| 460   | 2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh                                | 10/2012          | 250.50<br>-                        | 10/2014<br>-          | 10/2014     | 0/0                        |
| 461   | 2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh | 10/2011          | 1,565.00<br>-                      | 10/2014<br>-          | 10/2014     | 0/0                        |
| 462   | BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam                                           | 12/2003          | 217.61<br>-                        | 04/2010<br>-          | 11/2014     | 0/0                        |
| 463   | MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam                  | 12/2003          | 199.81<br>-                        | 04/2009<br>-          | 12/2014     | 0/0                        |
| 464   | MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam            | 12/2003          | 167.64<br>-                        | 11/2008<br>-          | 12/2014     | 0/0                        |
| 465   | MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam                   | 12/2003          | 200.00<br>-                        | 04/2009<br>-          | 12/2014     | 0/0                        |
| 466   | GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State                                          | 12/2003          | 604.00<br>-                        | 12/2009<br>-          | 12/2014     | 0/0                        |
| 467   | NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala                       | 03/2005          | 557.00<br>-                        | 02/2010<br>-          | 12/2014     | 0/0                        |
| 468   | NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha                                               | 07/2011          | 586.00<br>-                        | 01/2014<br>-          | 12/2014     | 0/0                        |
| 469   | 4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State                                     | 02/2011          | 1,078.84<br>-                      | 08/2013<br>-          | 12/2014     | 0/0                        |
| 470   | 4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State                                  | 02/2011          | 998.79<br>-                        | 08/2013<br>-          | 12/2014     | 0/0                        |
| 471   | Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu                                                | 09/2011          | 485.00<br>-                        | 08/2013<br>-          | 02/2015     | 0/0                        |
| 472   | SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala                      | 02/2010          | 617.00<br>-                        | 08/2012<br>-          | 03/2015     | 0/0                        |
| 473   | DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State                            | 10/2012          | 1,928.22<br>-                      | 04/2015<br>-          | 04/2015     | 0/0                        |
| 474   | CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan                                     | 12/2003          | 275.00<br>-                        | 02/2010<br>-          | 06/2015     | 0/0                        |
| 475   | RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State                                        | 12/2012          | 1,479.00<br>-                      | 06/2015<br>-          | 06/2015     | 0/0                        |
| 476   | 4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State                                       | 02/2011          | 2,498.76<br>-                      | 08/2014<br>-          | 07/2015     | 0/0                        |
| 477   | FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State                      | 02/2013          | 1,232.00<br>-                      | 08/2015<br>-          | 08/2015     | 0/0                        |
| 478   | ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh                                               | 03/2013          | 1,573.00<br>-                      | 09/2015<br>-          | 09/2015     | 0/0                        |
| 479   | PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha                                                    | 03/2012          | 1,410.00<br>-                      | 09/2014<br>-          | 10/2015     | 0/0                        |
| 480   | FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala                      | 04/2011          | 682.00<br>-                        | 10/2013<br>-          | 11/2015     | 0/0                        |
| 481   | WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,Tamil Nadu                        | 06/2013          | 1,287.95<br>-                      | 11/2015<br>-          | 11/2015     | 0/0                        |

|       |                                                                                              |                  | (Aug,2013)                         |                       |             |                            |
|-------|----------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                              |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                      | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                            | 3                | 4                                  | 5                     | 6           | 7                          |
| 482   | 4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State                                    | 02/2011          | 580.43<br>-                        | 08/2013<br>-          | 12/2015     | 0/0                        |
| 483   | AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat                                      | 01/2013          | 2,125.24<br>-                      | 12/2015<br>-          | 12/2015     | 0/0                        |
| 484   | NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir                                           | 06/2010          | 2,159.00<br>-                      | 06/2015<br>-          | 05/2016     | 0/0                        |
| 485   | QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir                 | 07/2010          | 1,987.00<br>-                      | 07/2015<br>-          | 06/2016     | 0/0                        |
|       | Total                                                                                        |                  | 100,938.04<br>-                    |                       |             | 0/0                        |
|       |                                                                                              |                  |                                    |                       |             |                            |
|       | <u>Shipping And Ports</u>                                                                    |                  |                                    |                       |             |                            |
| 486   | RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala        | 03/2007          | 245.67<br>298.17                   | 04/2009<br>11/2009    | 02/2011     | 0/0                        |
| 487   | ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra           | 10/2007          | 359.44<br>-                        | 04/2011<br>11/2011    | 11/2011     | 0/0                        |
| 488   | Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat    | 06/2010          | 277.00<br>-                        | 03/2012<br>-          | 03/2012     | 0/0                        |
| 489   | Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra                          | 04/2009          | 277.03<br>280.00                   | 12/2011<br>10/2012    | 10/2012     | 0/0                        |
| 490   | Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh      | 02/2010          | 444.10<br>-                        | 06/2010<br>-          | 11/2012     | 0/0                        |
| 491   | Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat           | 04/2005          | 882.00<br>-                        | 02/2011<br>-          | 12/2012     | 0/0                        |
| 492   | CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat                | 12/2005          | 702.00<br>-                        | 03/2011<br>-          | 03/2013     | 0/0                        |
| 493   | Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat           | 02/2011          | 830.00<br>-                        | 05/2013<br>-          | 05/2013     | 0/0                        |
| 494   | ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State   | 07/2011          | 220.49<br>-                        | 01/2013<br>06/2013    | 06/2013     | 0/0                        |
| 495   | SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala            | 03/2009          | 3,500.00<br>4,150.00               | 01/2012<br>09/2012    | 08/2013     | 0/0                        |
| 496   | Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra    | 08/2010          | 612.72<br>532.83                   | 12/2012<br>11/2013    | 11/2013     | 0/0                        |
| 497   | Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra    | 10/2010          | 1,028.10<br>1,012.23               | 12/2013<br>11/2013    | 11/2013     | 0/0                        |
| 498   | ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu        | 10/2002          | 150.00<br>309.00                   | 03/2006<br>12/2013    | 12/2013     | 0/0                        |
| 499   | Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra    | 10/2010          | 966.46<br>-                        | 02/2014<br>-          | 02/2014     | 0/0                        |
| 500   | ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State | 01/2012          | 511.87<br>-                        | 03/2014<br>08/2014    | 08/2014     | 0/0                        |
| 501   | CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra  | 11/2007          | 1,228.00<br>1,460.00               | 12/2010<br>09/2012    | 12/2014     | 0/0                        |
| 502   | SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu                        | 06/2005          | 2,427.40<br>-                      | 10/2008<br>11/2010    | -           | 0/0                        |
| 503   | DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra       | 10/2005          | 800.00<br>1,571.60                 | 10/2008<br>-          | -           | 0/0                        |

|       |                                                                                            |                  | (Aug,2013)                         |                       |             |                            |
|-------|--------------------------------------------------------------------------------------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |                                                                                            |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project                                                                                    | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2                                                                                          | 3                | 4                                  | 5                     | 6           | 7                          |
|       | Total                                                                                      |                  | 15,462.28 -                        |                       |             | 0/0                        |
|       |                                                                                            |                  |                                    |                       |             |                            |
|       | <u>Telecommunications</u>                                                                  |                  |                                    |                       |             |                            |
| 504   | GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab                | 02/2008          | 373.94 -                           | 12/2008 -             | 12/2012     | 0/0                        |
| 505   | GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand            | 03/2008          | 328.13 -                           | 03/2009 -             | 01/2013     | 0/0                        |
| 506   | CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi                             | 12/2005          | 249.00 -                           | 02/2007 03/2012       | 02/2013     | 0/0                        |
| 507   | GSM equipment of 1625000Lines (2G) 325000 lines 3( - [N26000090]BSNL,Madhya pradesh        | 11/2009          | 916.70 -                           | 11/2010 12/2012       | 09/2013     | 0/0                        |
| 508   | Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State | 07/2010          | 1,148.19 -                         | 05/2011 -             | 09/2013     | 0/0                        |
| 509   | EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra            | 06/2006          | 231.38 -                           | 10/2007 -             | 12/2013     | 0/0                        |
| 510   | GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand           | 01/2009          | 149.15 -                           | 06/2009 -             | 12/2013     | 0/0                        |
| 511   | Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam                           | 06/2007          | 336.81 -                           | 01/2009 -             | 12/2013     | 0/0                        |
| 512   | ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State                  | 10/2009          | 384.00 -                           | 10/2010 03/2012       | 12/2013     | 0/0                        |
| 513   | CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra                           | 01/2006          | 247.00 -                           | 02/2007 12/2010       | -           | 0/0                        |
| 514   | Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State | 12/2007          | 952.88 -                           | 03/2010 -             | -           | 0/0                        |
| 515   | Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State           | 12/2007          | 152.65 -                           | 03/2010 -             | -           | 0/0                        |
| 516   | DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi                           | 02/2006          | 229.41 -                           | 03/2012 02/2013       | -           | 0/0                        |
|       | Total                                                                                      |                  | 5,699.24 -                         |                       |             | 0/0                        |
|       |                                                                                            |                  |                                    |                       |             |                            |
|       | <u>Urban Development</u>                                                                   |                  |                                    |                       |             |                            |
| 517   | FARIDABAD EXTENSION - [N28000057]DMRC,Delhi                                                | 09/2011          | 2,494.00 -                         | 09/2014 -             | 05/2015     | 0/0                        |
| 518   | DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi                                               | 09/2011          | 35,242.00 -                        | 03/2016 -             | 03/2016     | 0/0                        |
| 519   | C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra           | 11/2006          | 114.18 173.08                      | 04/2009 -             | -           | 0/0                        |
|       | Total                                                                                      |                  | 37,850.18 -                        |                       |             | 0/0                        |
|       |                                                                                            |                  |                                    |                       |             |                            |
|       | <u>Water Resources</u>                                                                     |                  |                                    |                       |             |                            |
| 520   | PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam                                              | 01/2001          | 542.90 -                           | 12/2007 -             | 12/2012     | 0/0                        |
|       | Total                                                                                      |                  | 542.90 -                           |                       |             | 0/0                        |

|       |             |                  | (Aug,2013)                         |                       |             |                            |
|-------|-------------|------------------|------------------------------------|-----------------------|-------------|----------------------------|
|       |             |                  |                                    | Date of Commissioning |             |                            |
| Sl.No | Project     | Date of Approval | Original/ Revised Cost (Rs. crore) | Original / Revised    | Anticipated | Milestones Achieved/ Total |
| 1     | 2           | 3                | 4                                  | 5                     | 6           | 7                          |
|       |             |                  |                                    |                       |             |                            |
|       | Grand Total |                  | 412,631.28                         |                       |             | 0/0                        |
